

Daily Coordination Meeting



14:00 Sign In



Daily Coordination Meeting

General Topics:

- **Cranes**
 - **10 hrs/day – 06:00-16:00**
 - **No night shift for mobiles**
 - **Friday crane work only by approval of Craig**

[illegible]


ELRAM

Ars Vac room
PCD Bathtub
PCD Staggering
TTNW WC's
5W Studs WC's

HEATCOIL REPL.


Taper Tech Ongoing
Finish 2/3
Pipe contractors In 2/3

UTILITY LEVEL MOD2

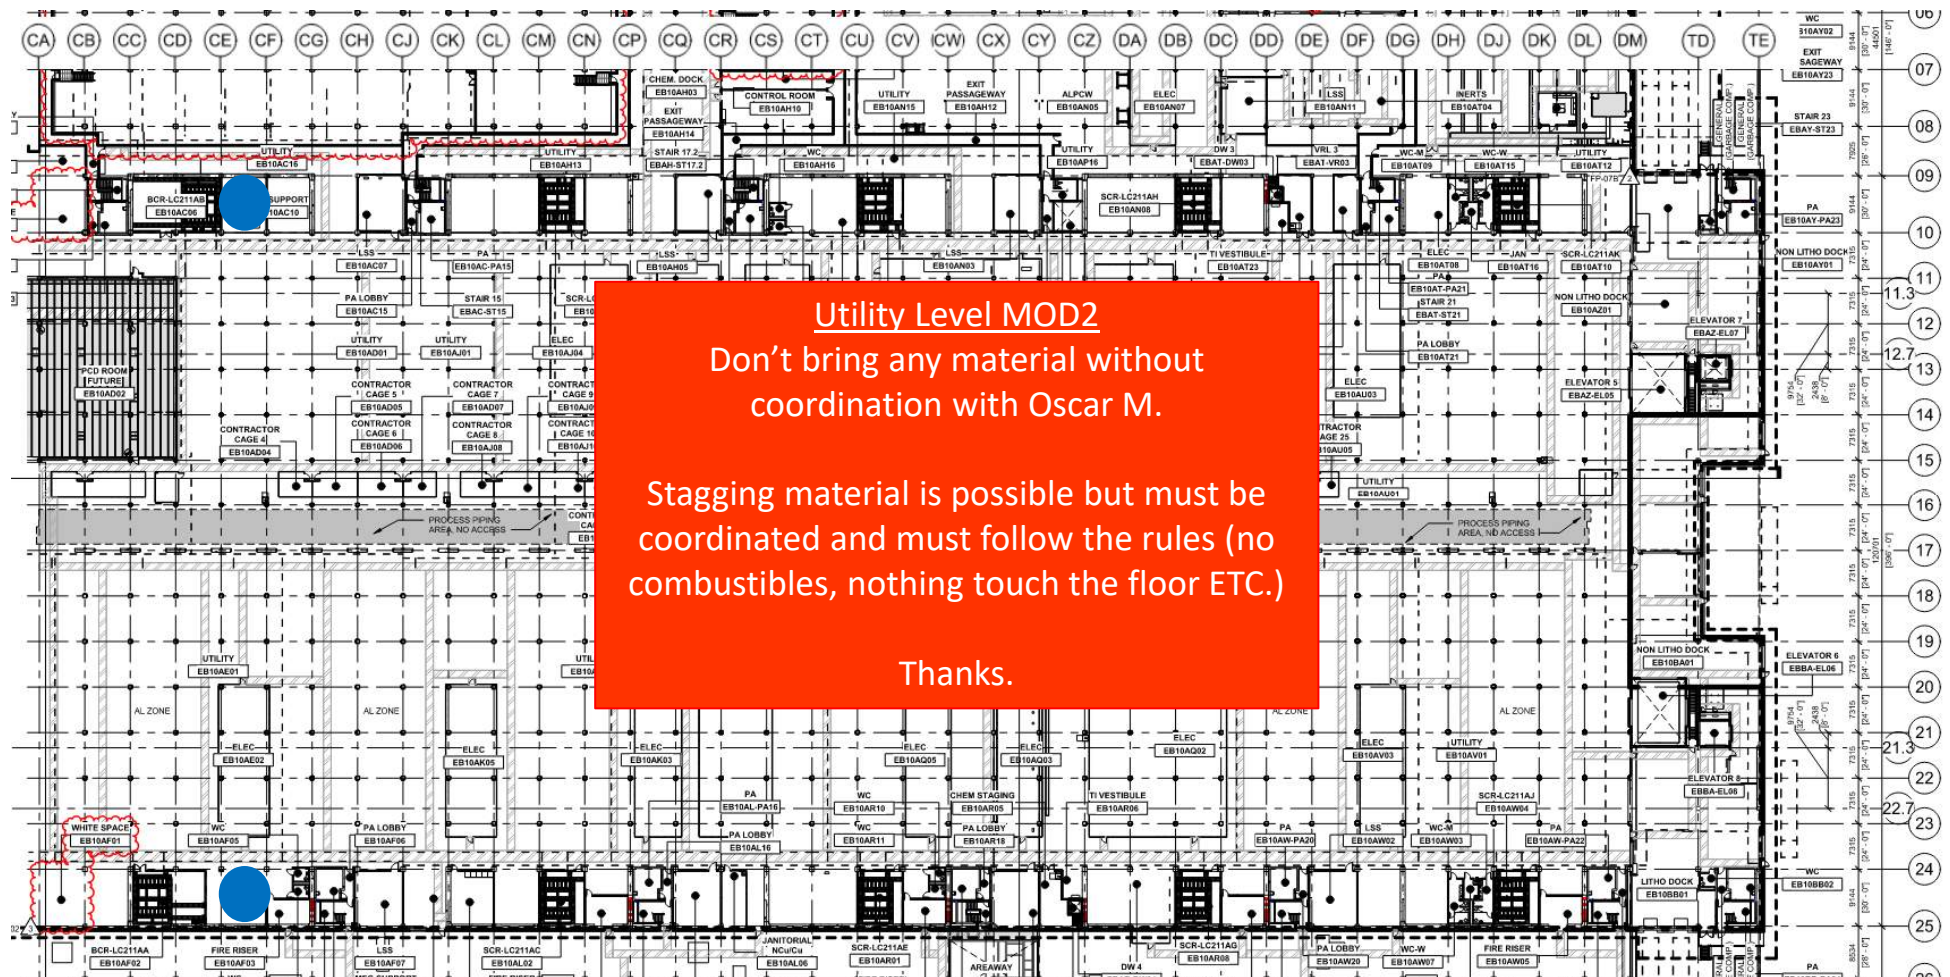



SUT 38.1 LEVEL

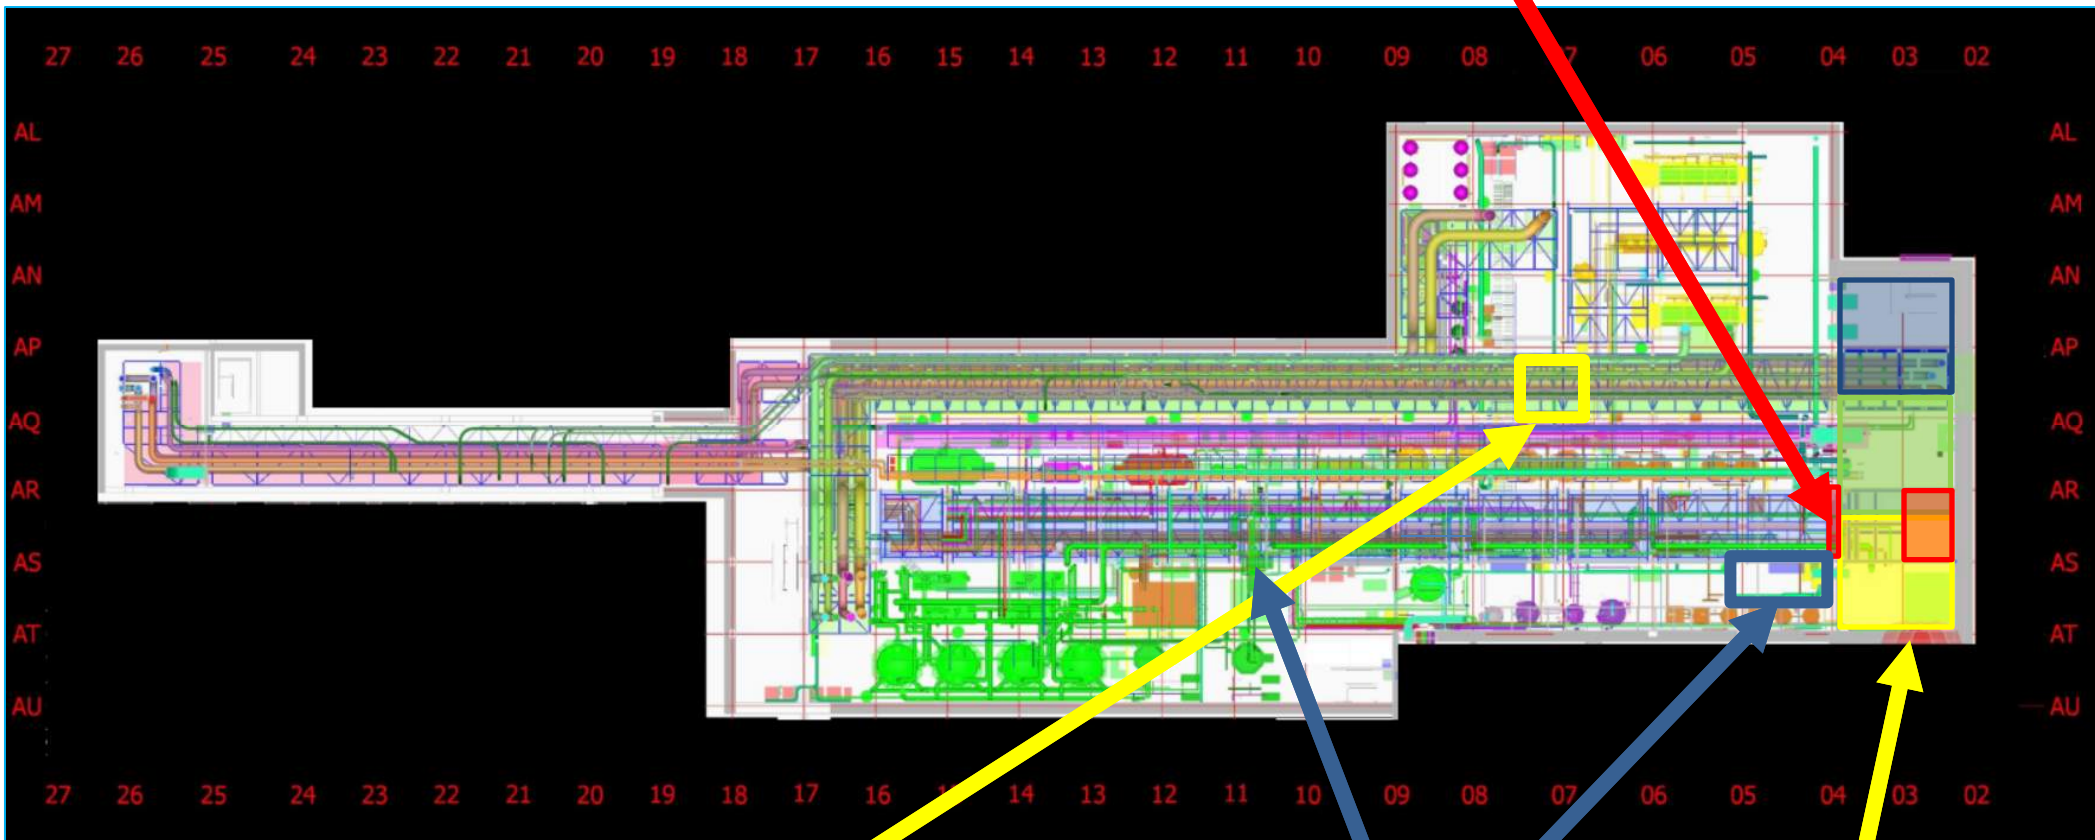

OH roll-up door
Install 30/1

CRC

HYG
Need to install SOG platform +
Bodice Grating ASAP

Topping slab Schedule


- Pour 1 – 1/9 – 1/15 V
- Pour 2 – 1/15 – 1/22 V
- Pour 3 -1/22-1/27 V
- Pour 4 – 1/28-2/4



HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

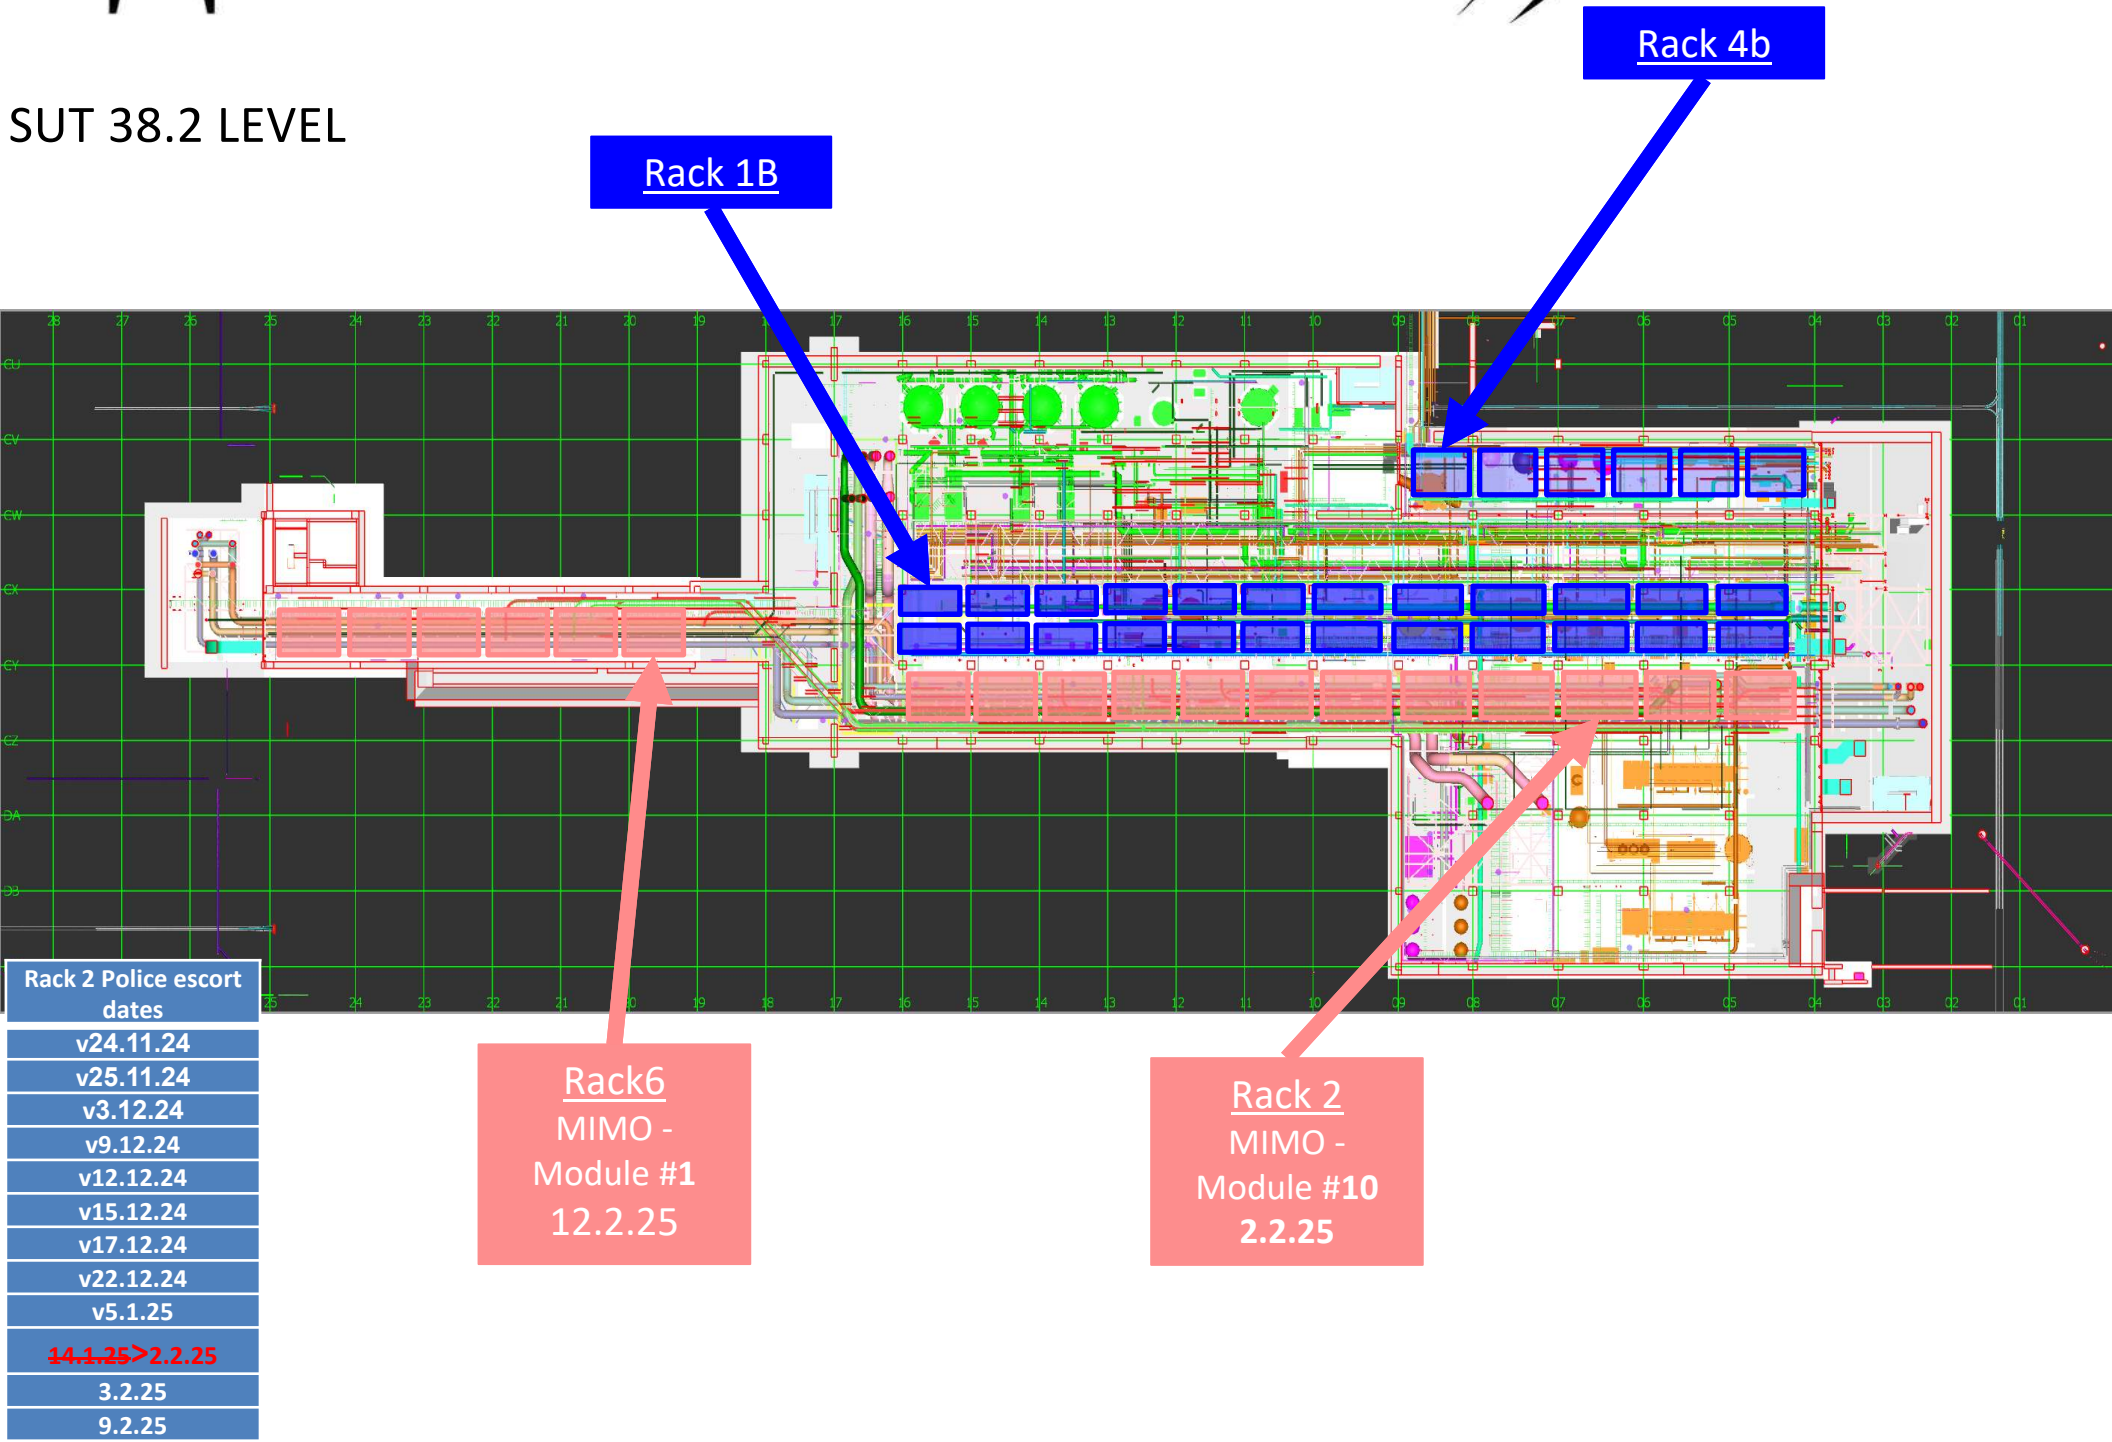


Rack 1B

Rack 4b


Rack 6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25


SUBFAB BUILDOUT MOD 1

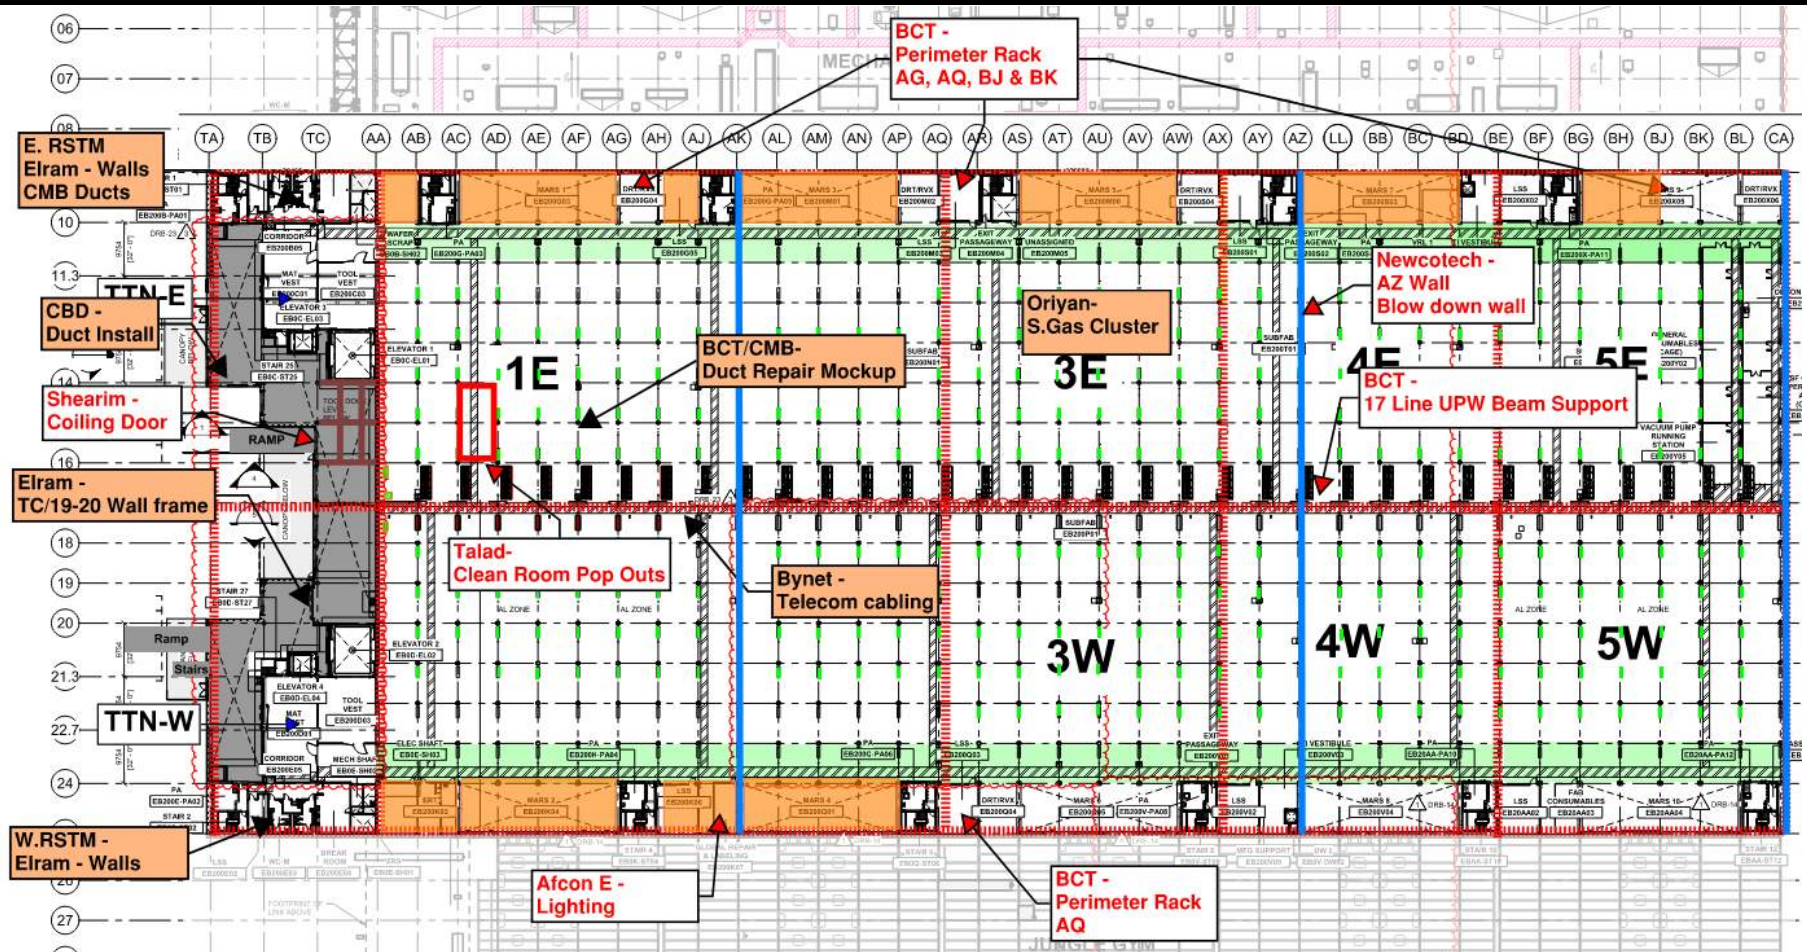


SUBFAB CRC TOPCOAT

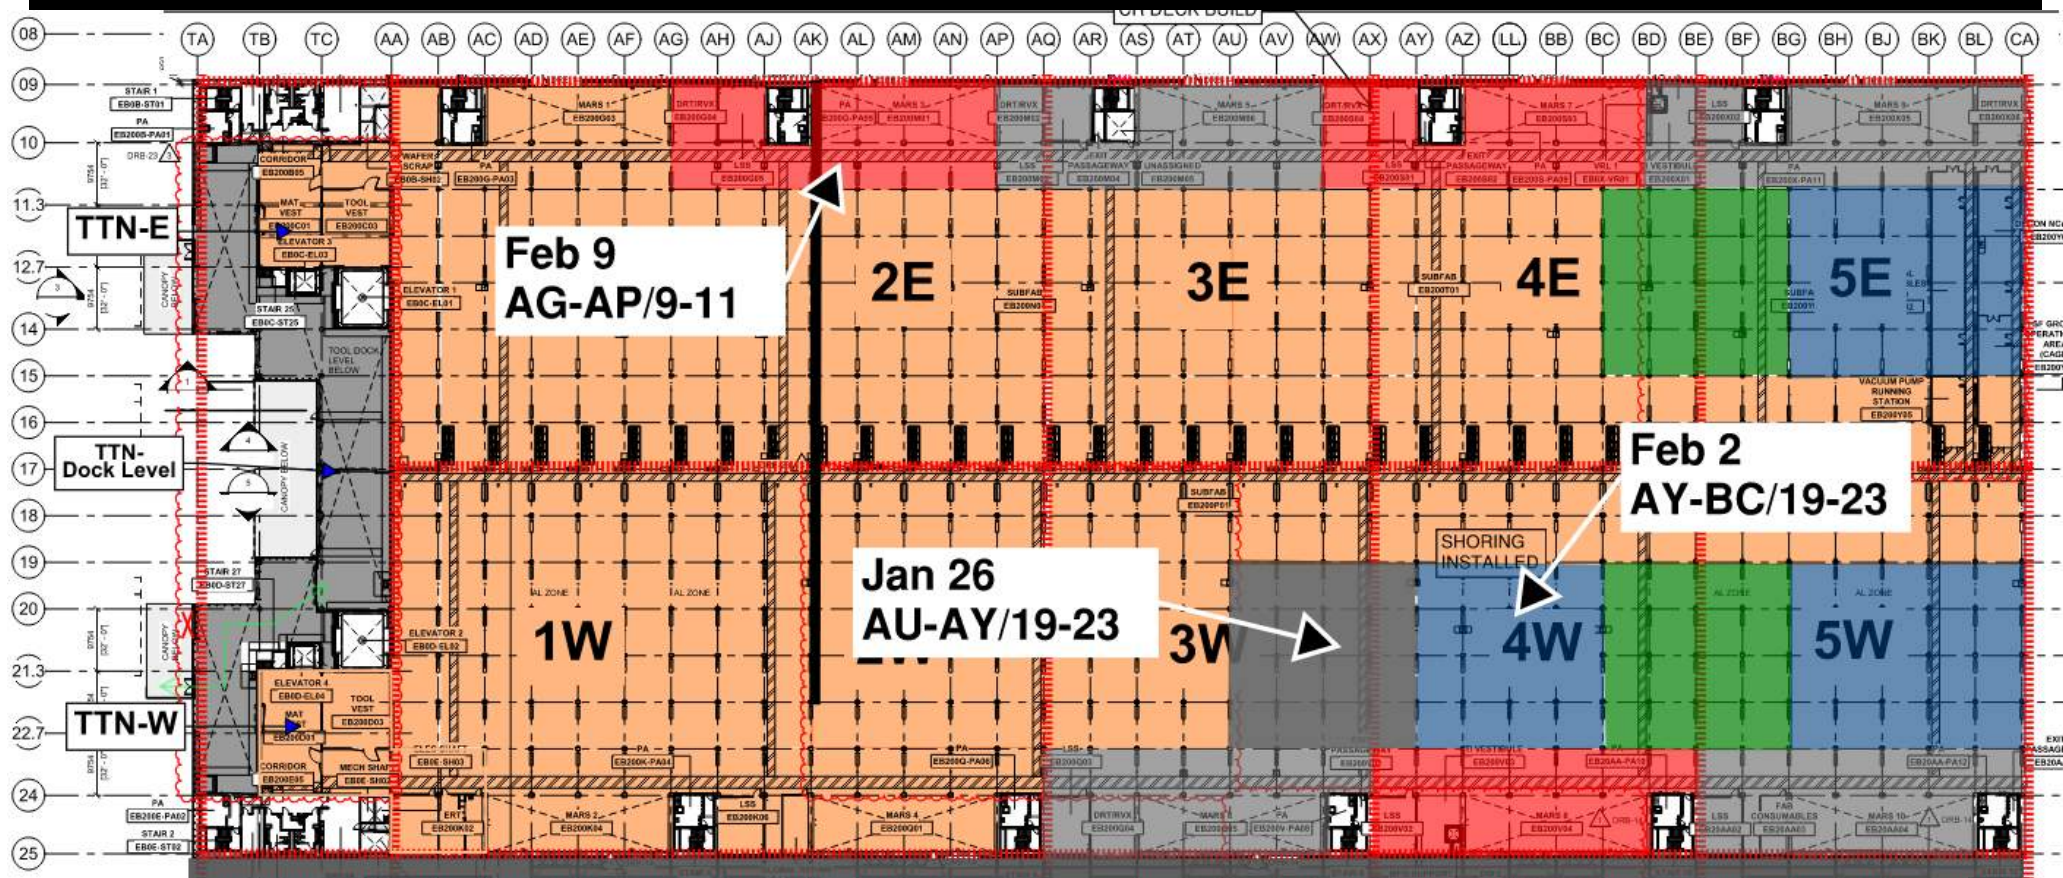

BCT Pressure Test Tomorrow

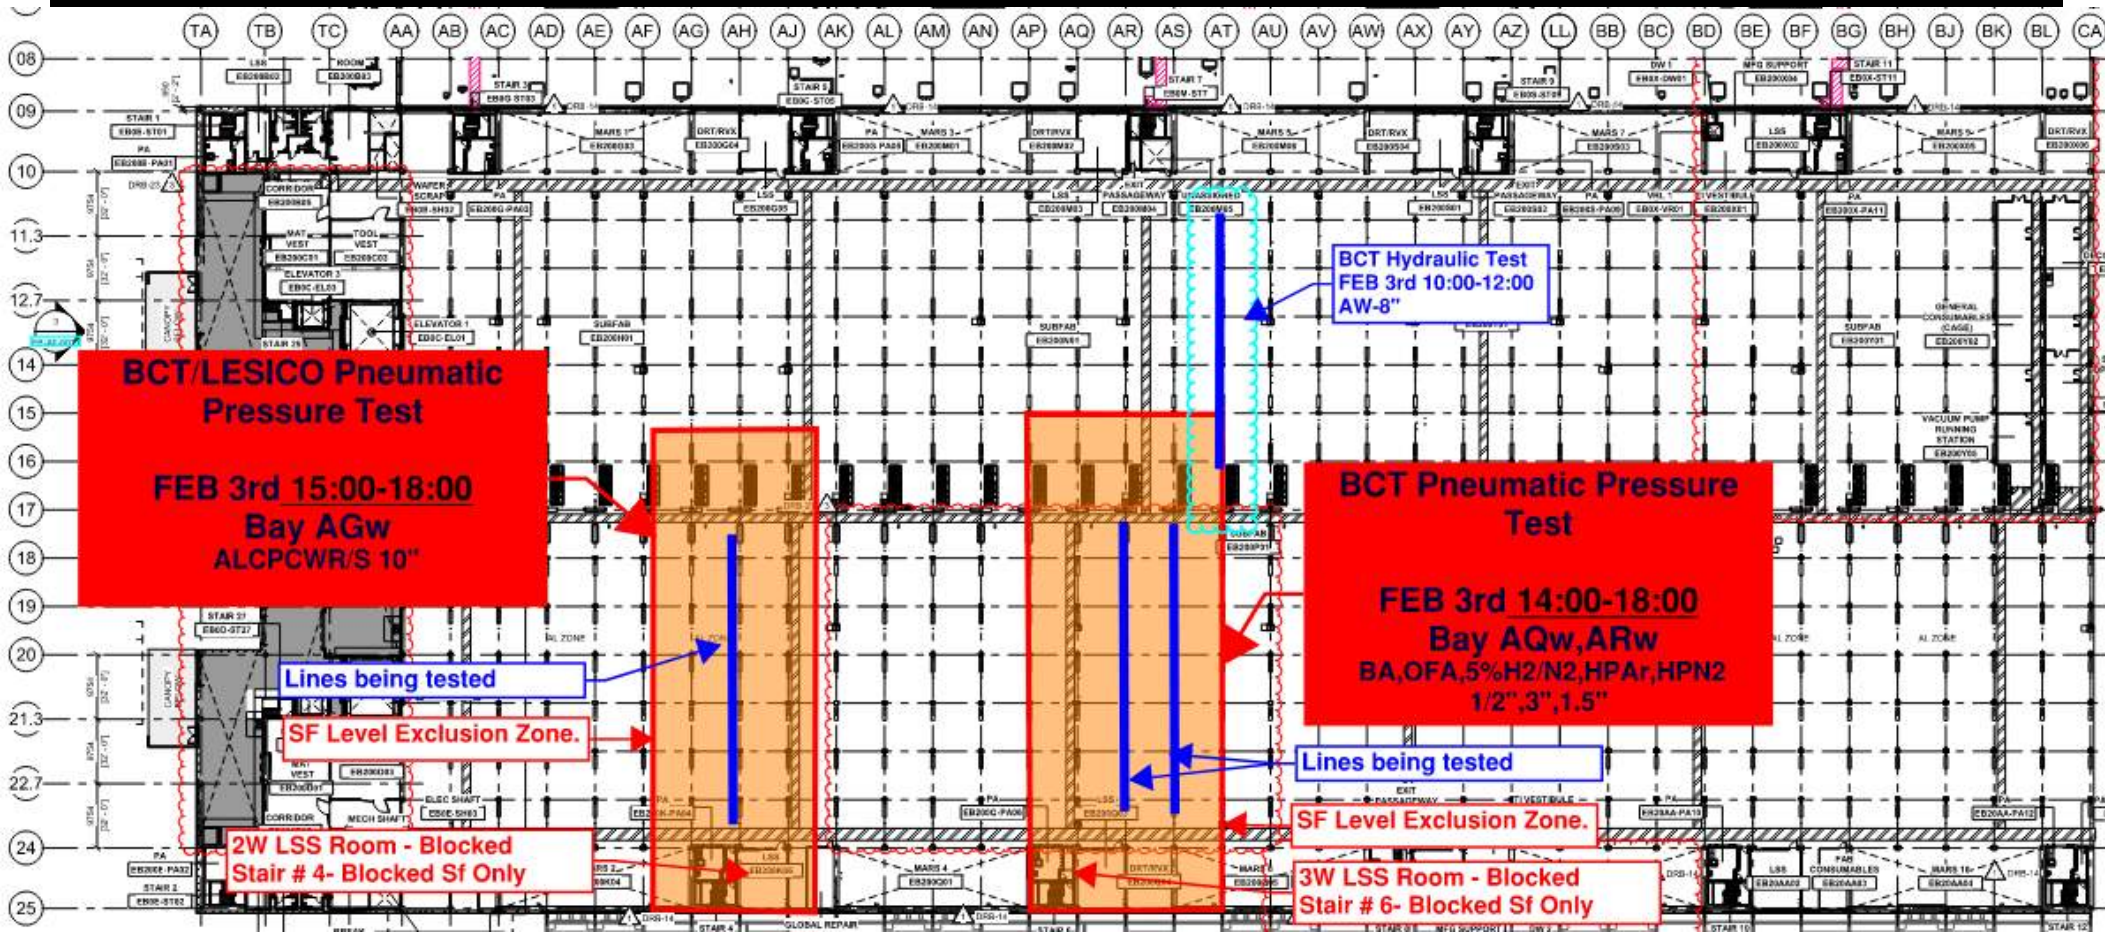

SUBFAB BUILDOUT MOD 2

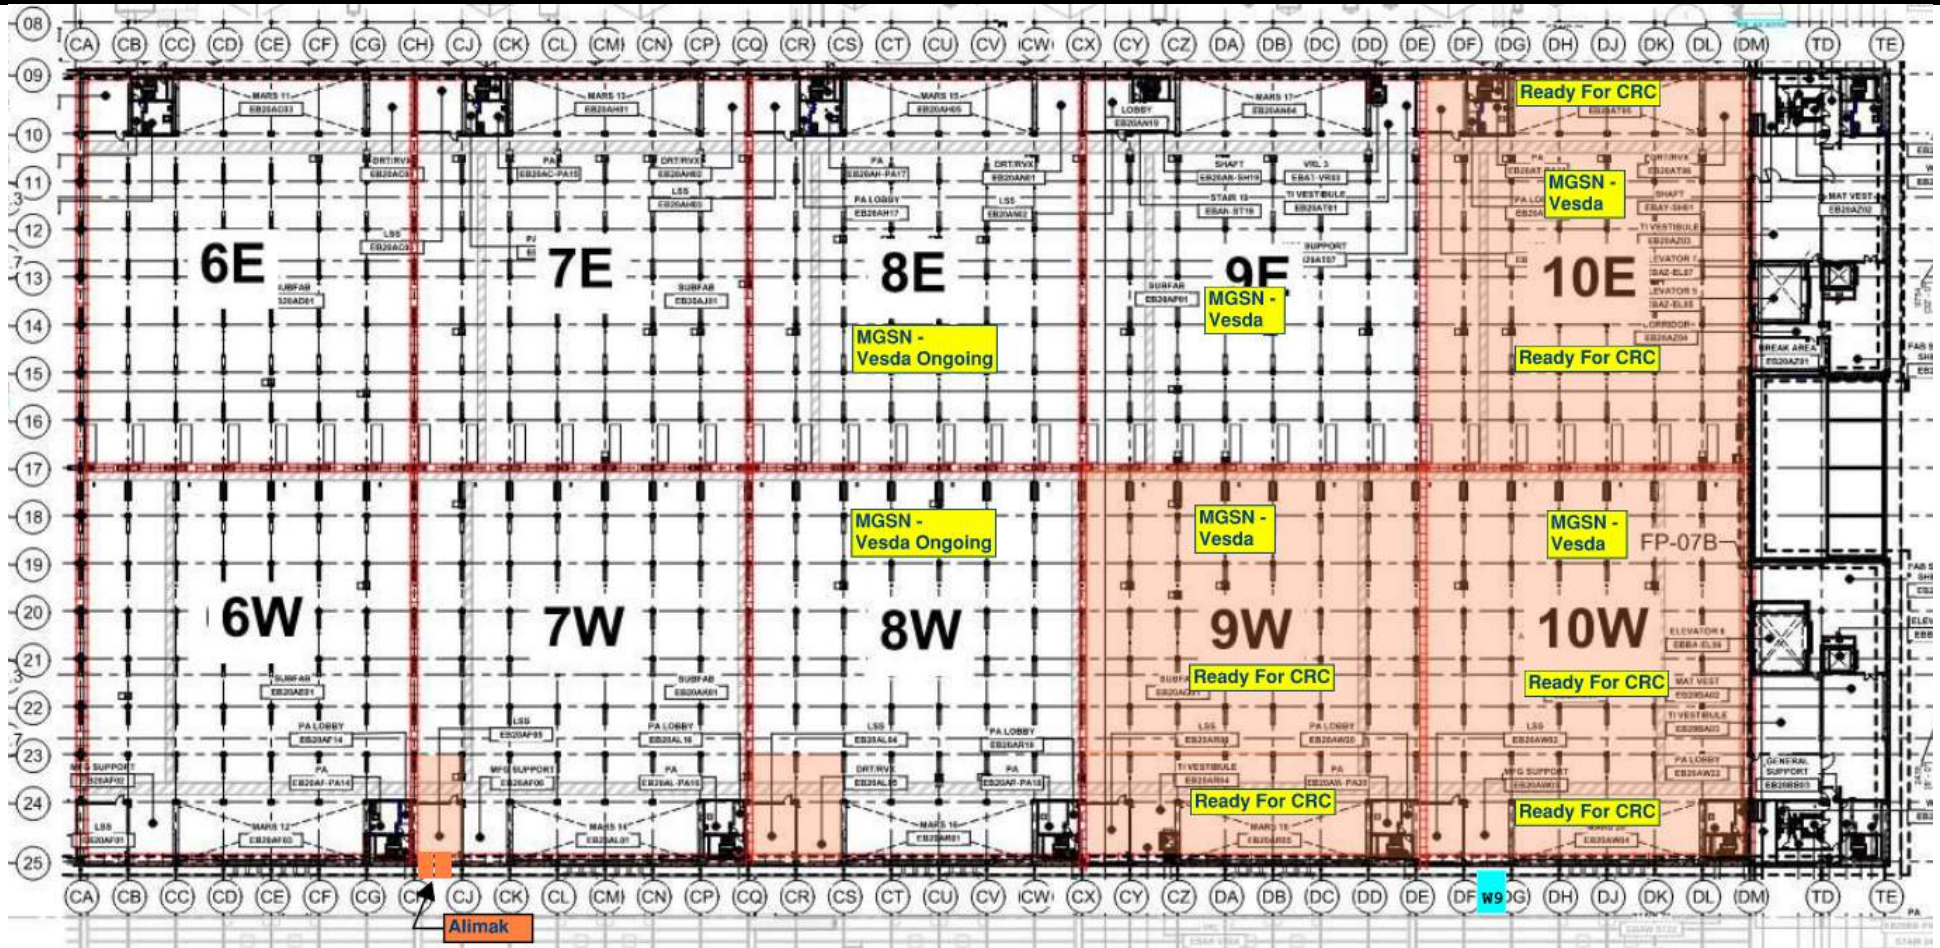




Talad- Lids
clean/paint/install Air flow
lids
Taper-Tech- RMF install
1W Mars 3FA
scaffold green tagged

HYG -
Stairs 7.3 working
from CR level

30%


60%


NTT
Meptagone-
EMT
Pipes+devices
C-B- Duct install
Chemo - Pipe
install

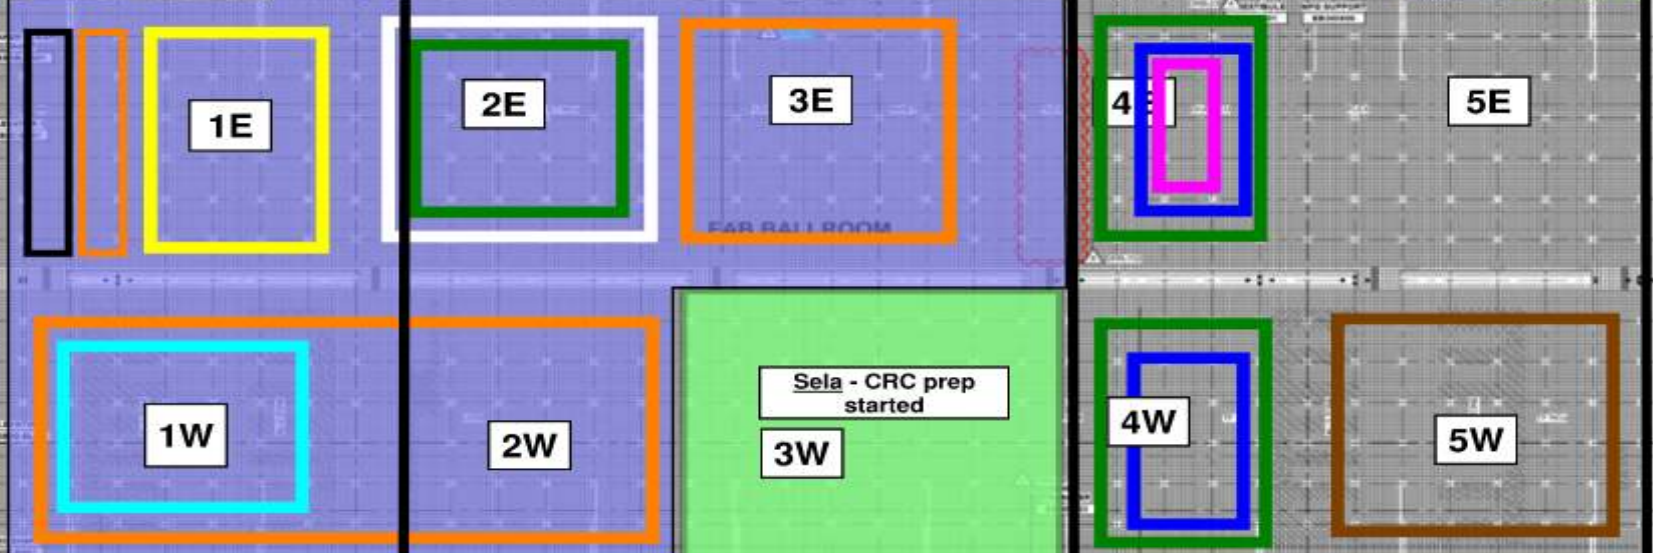


Link-mobile scaffold moved
to seq.#8
Next movement on feb 10th
to seq#6,5,4,3 for d&p
blades drilling.
Crc ddfd to be covered
tomorrow.


Afcon - Cable trays, modules and
stickers
MB- Pipes and drops
Eiram - Columns/shaft walls/G1 wall
Meptagon - I&C+ Zero ref. pipes
D&P - Stick build+ separation
walls+FFU
Tzur-esh - 1W blade paint
HYG - Stairs 7.3 starts WW04
Talad - UPN install, ceiling grid, lids
removal
Talent - Super clean
Taper-Tech - RMF
Talent - Super clean

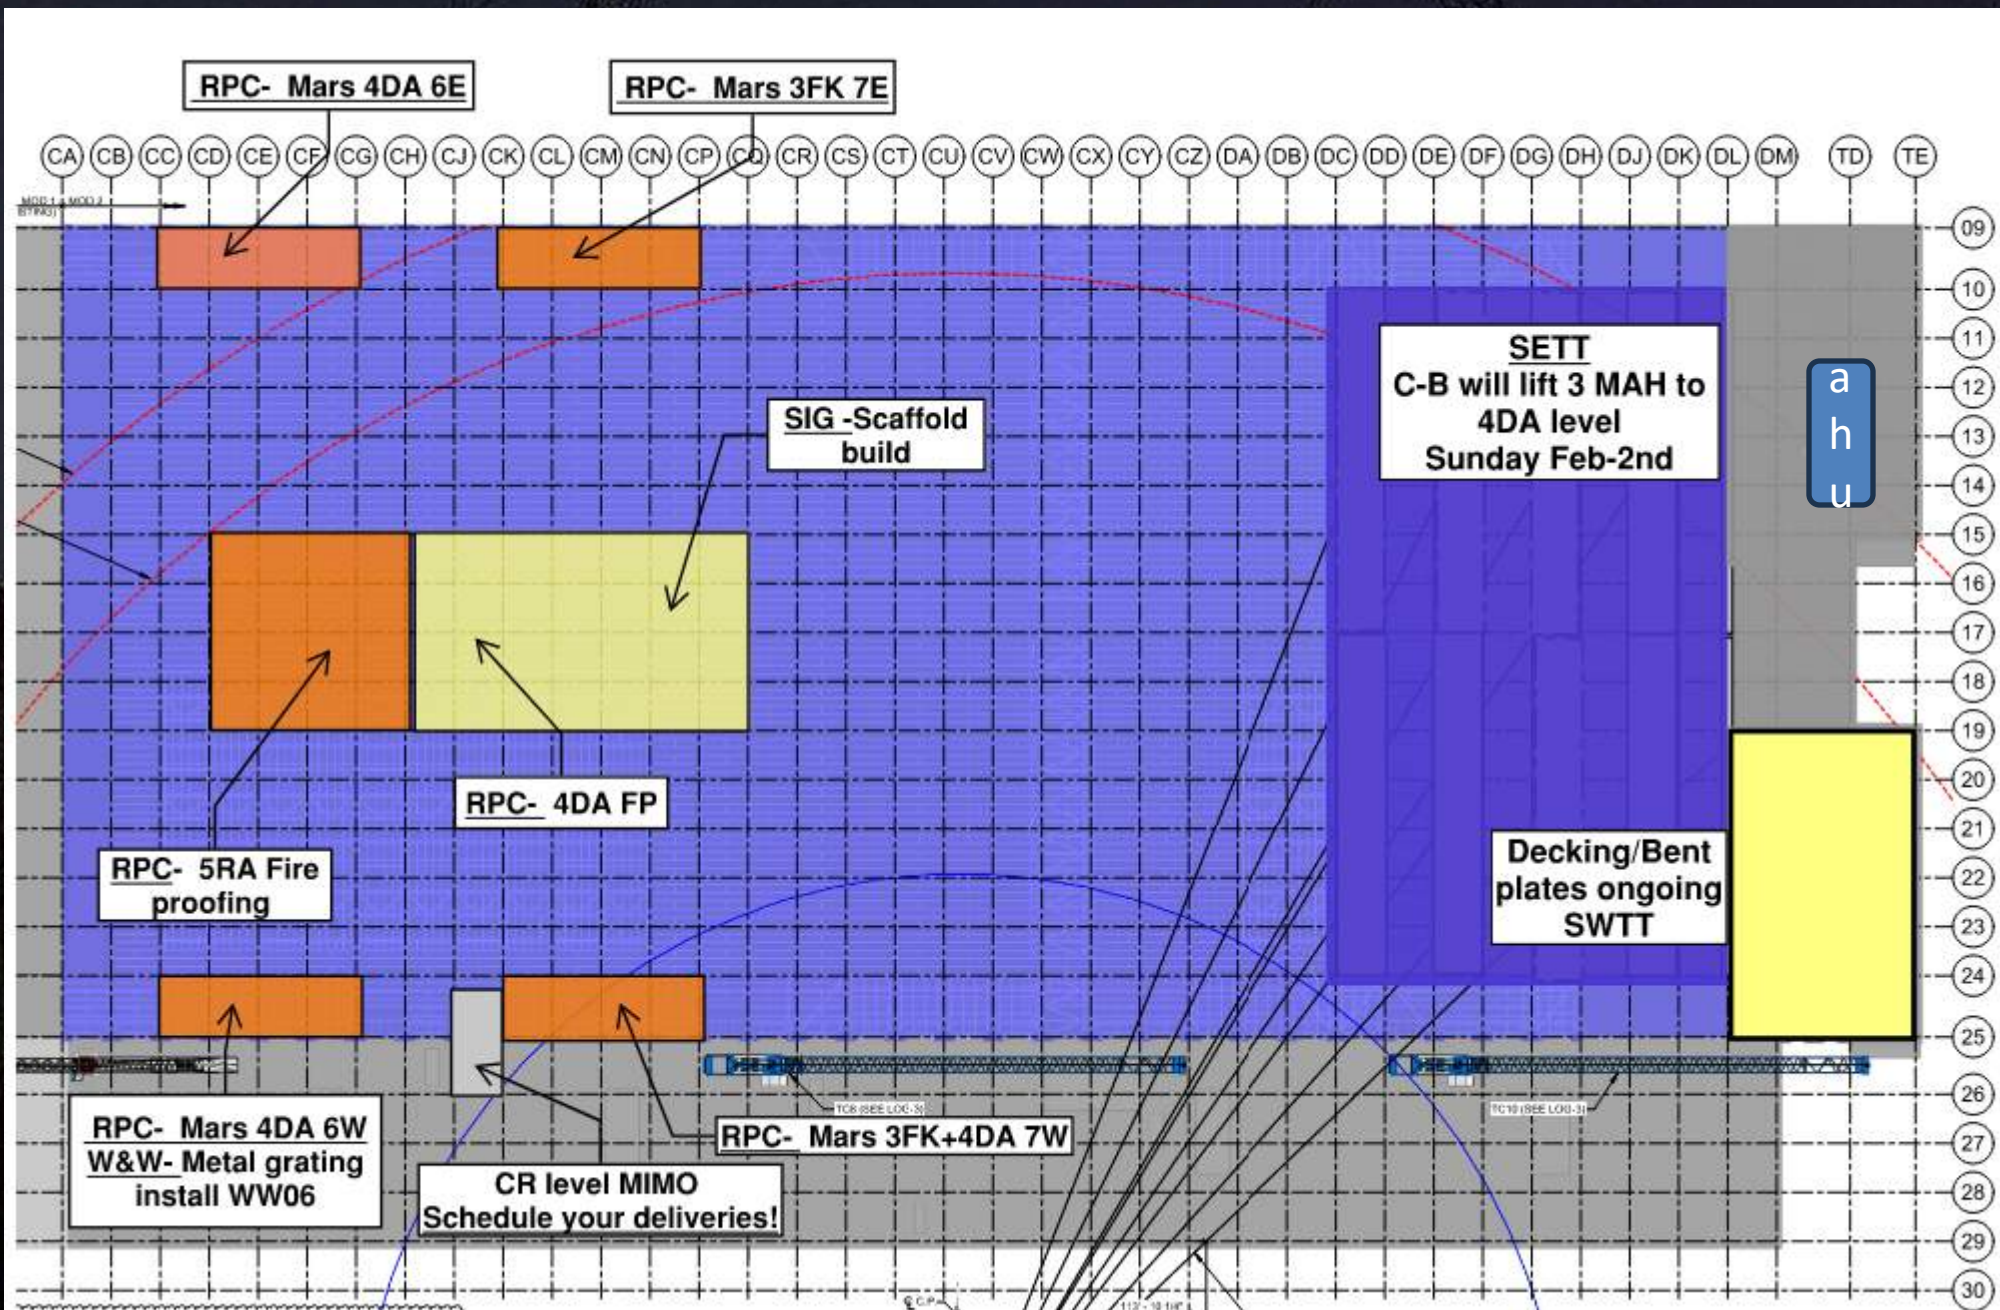




HOFFMAN CONSTRUCTION COMPANY

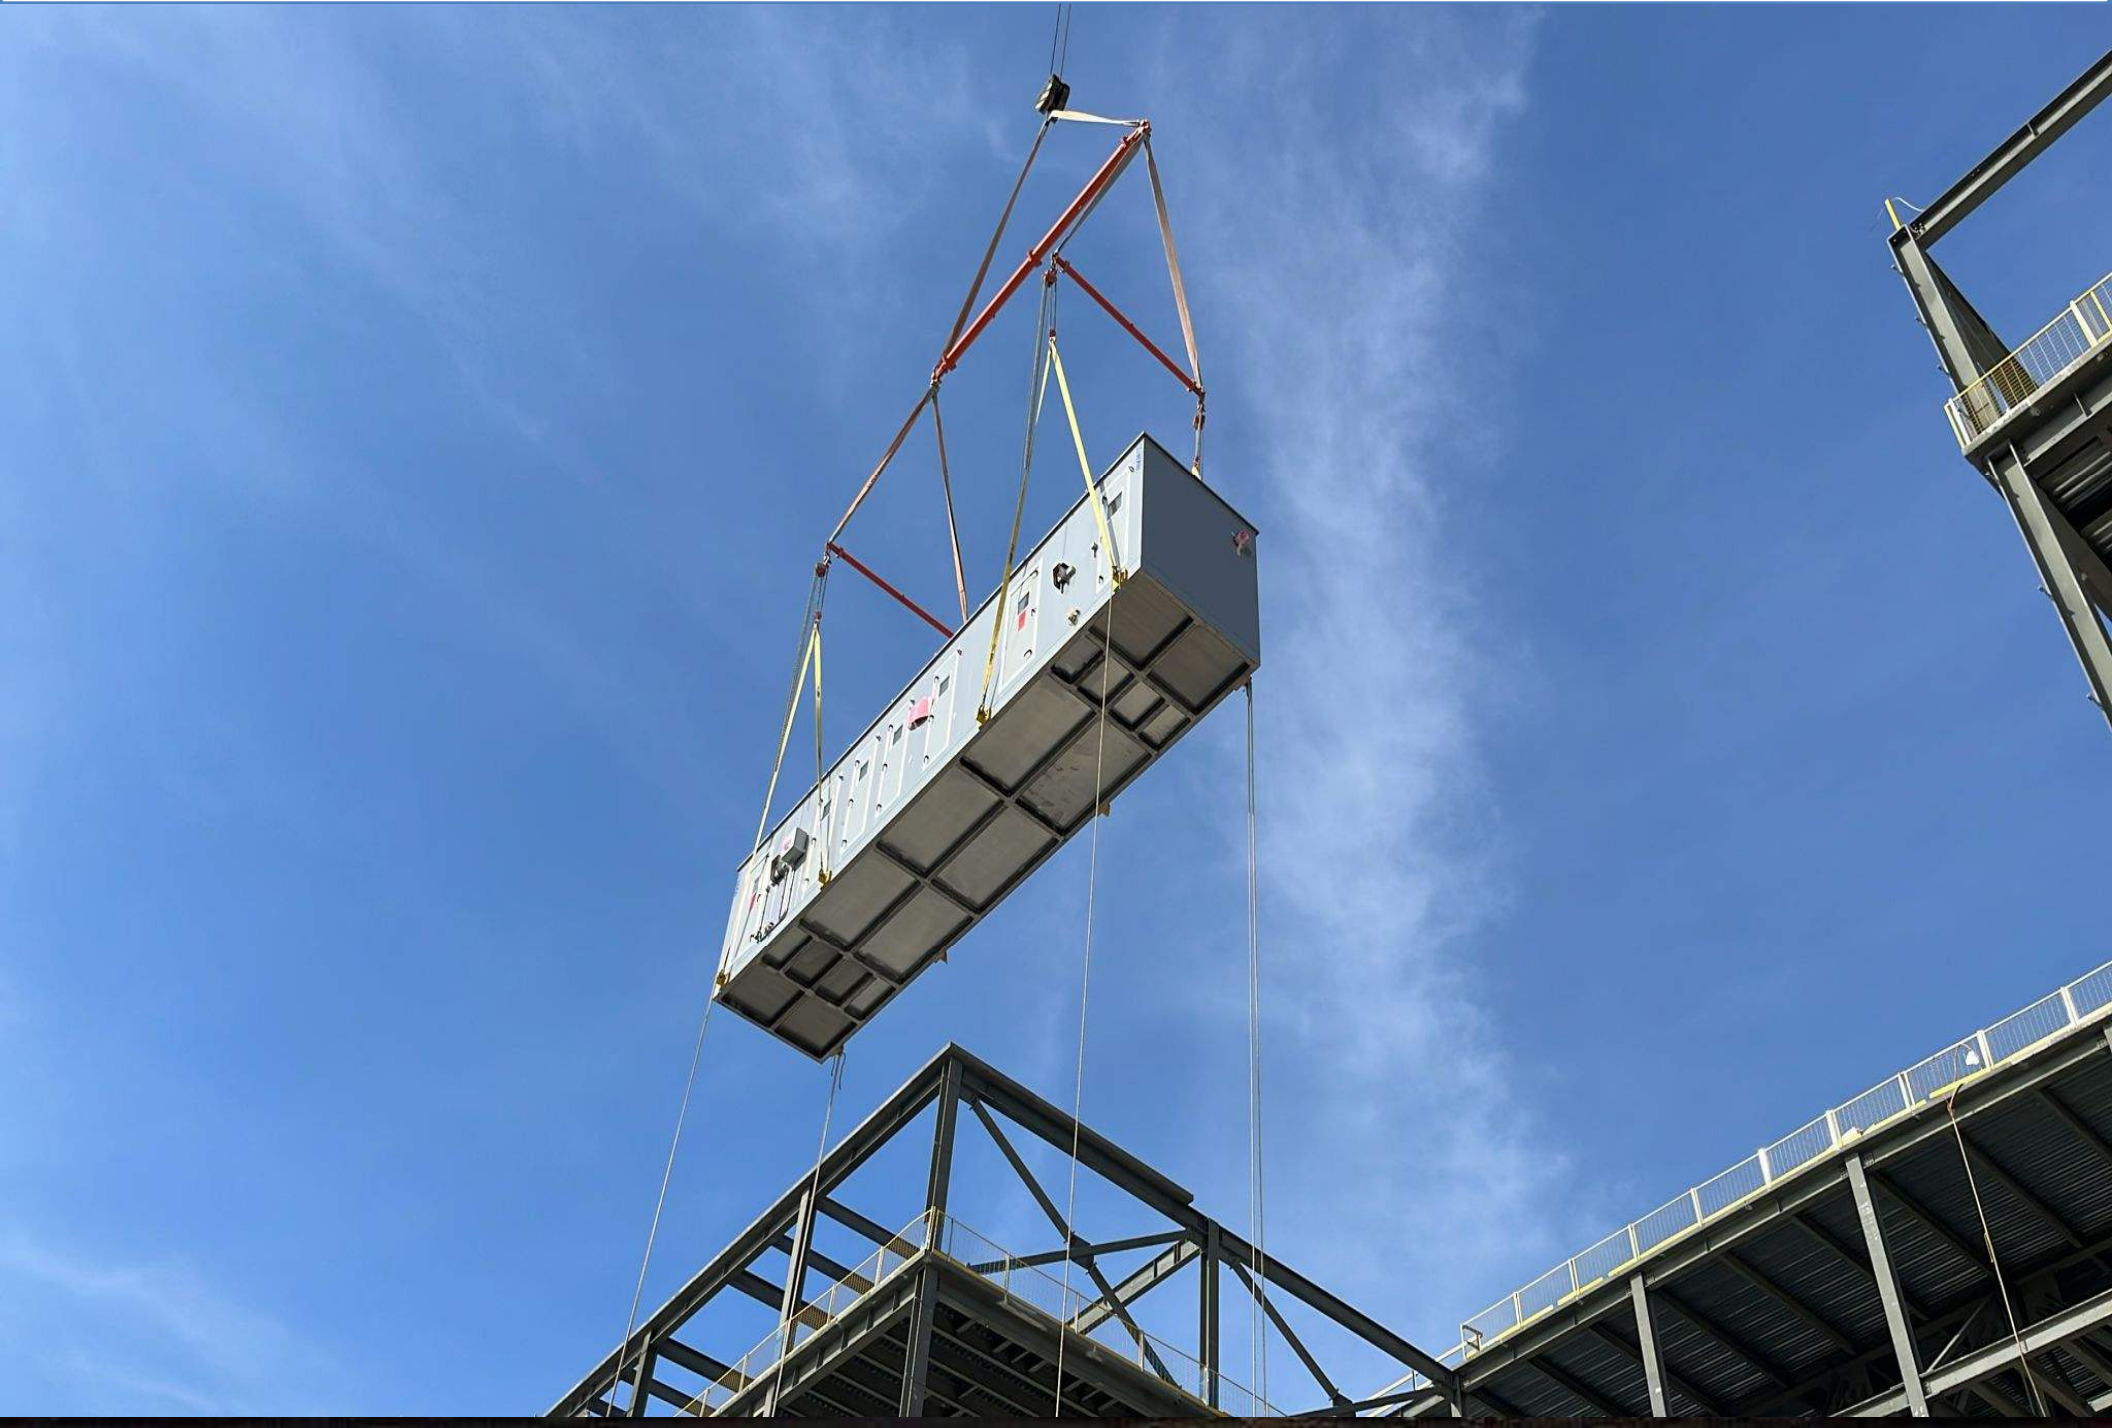

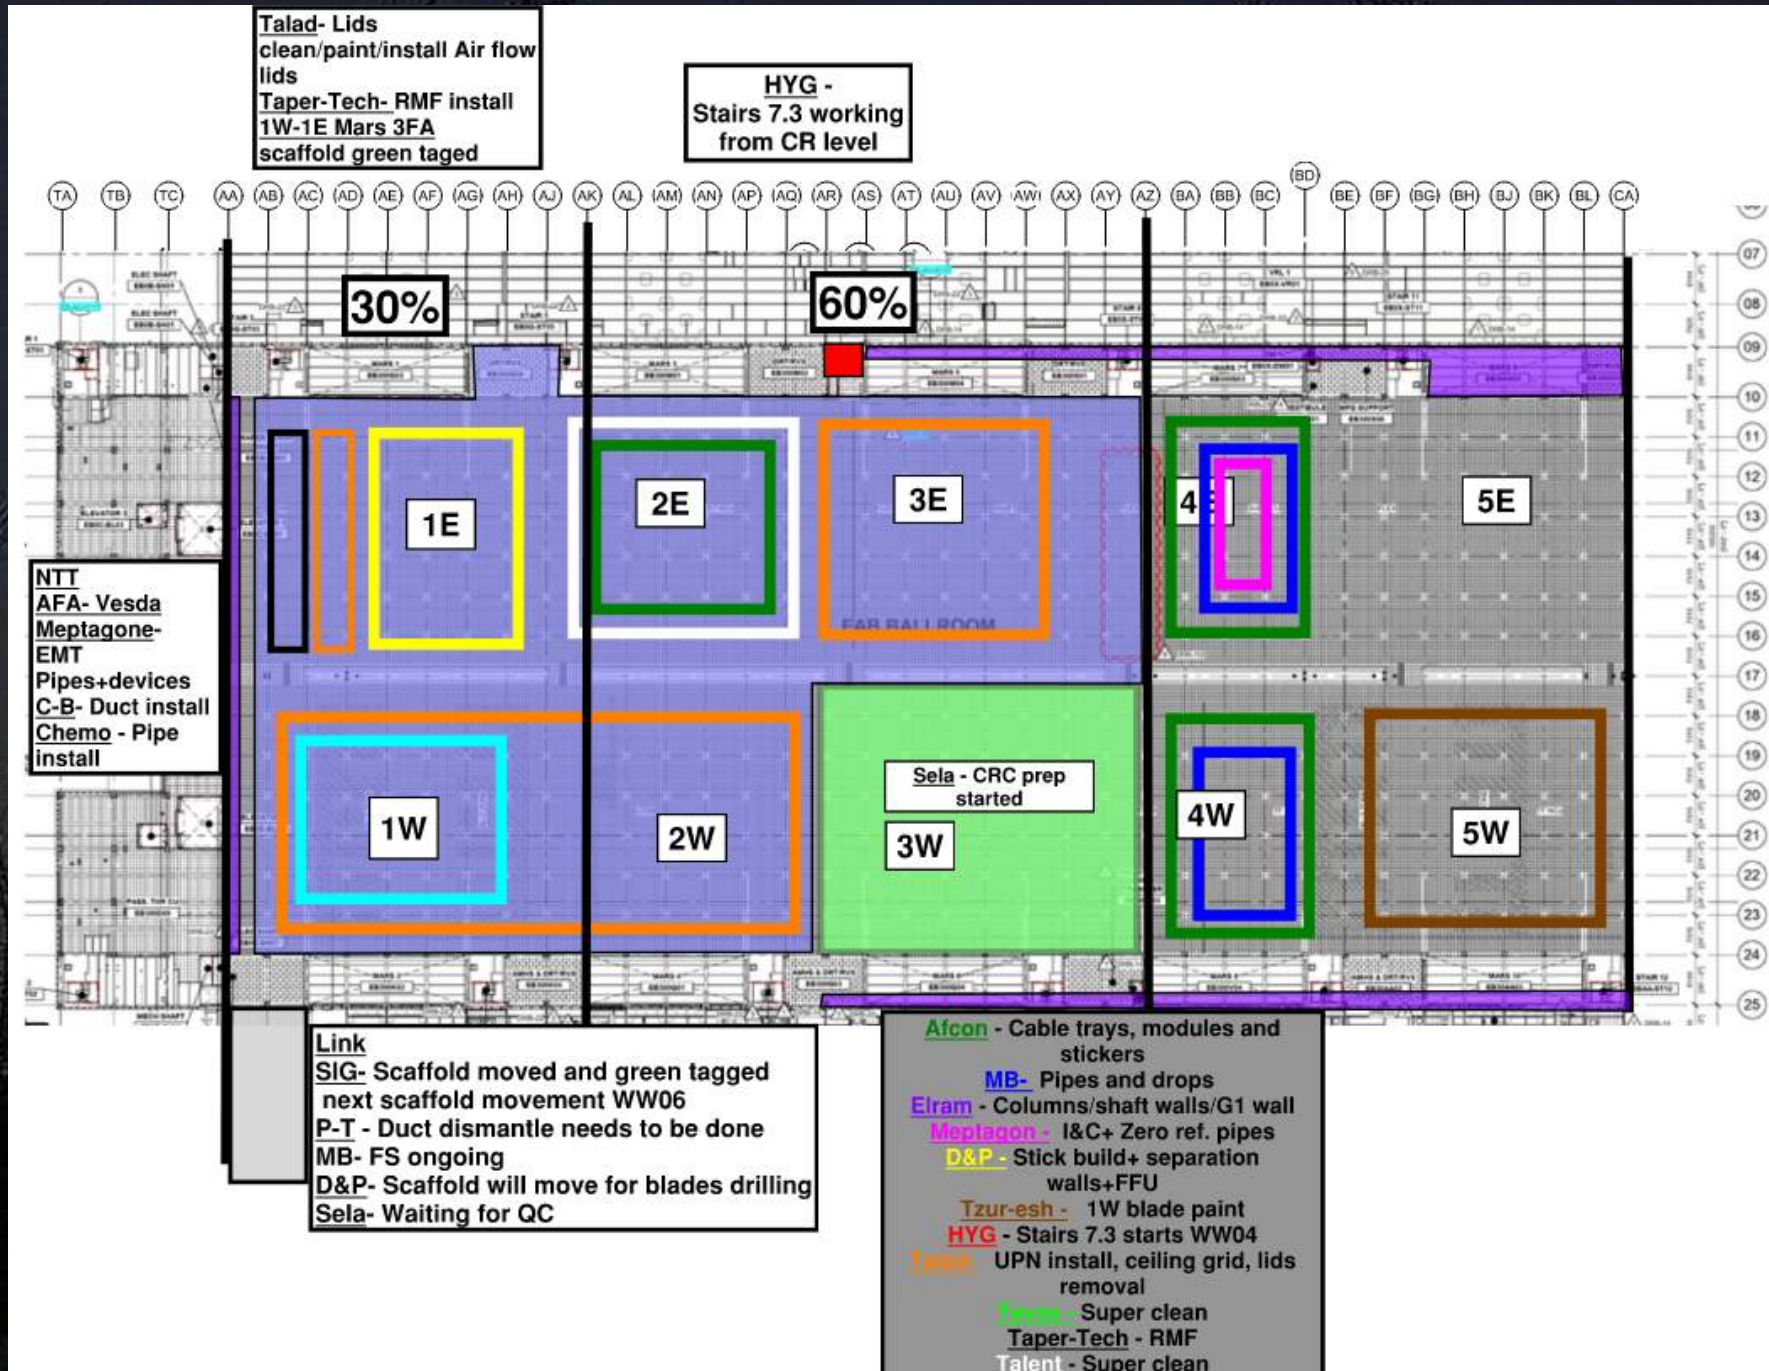

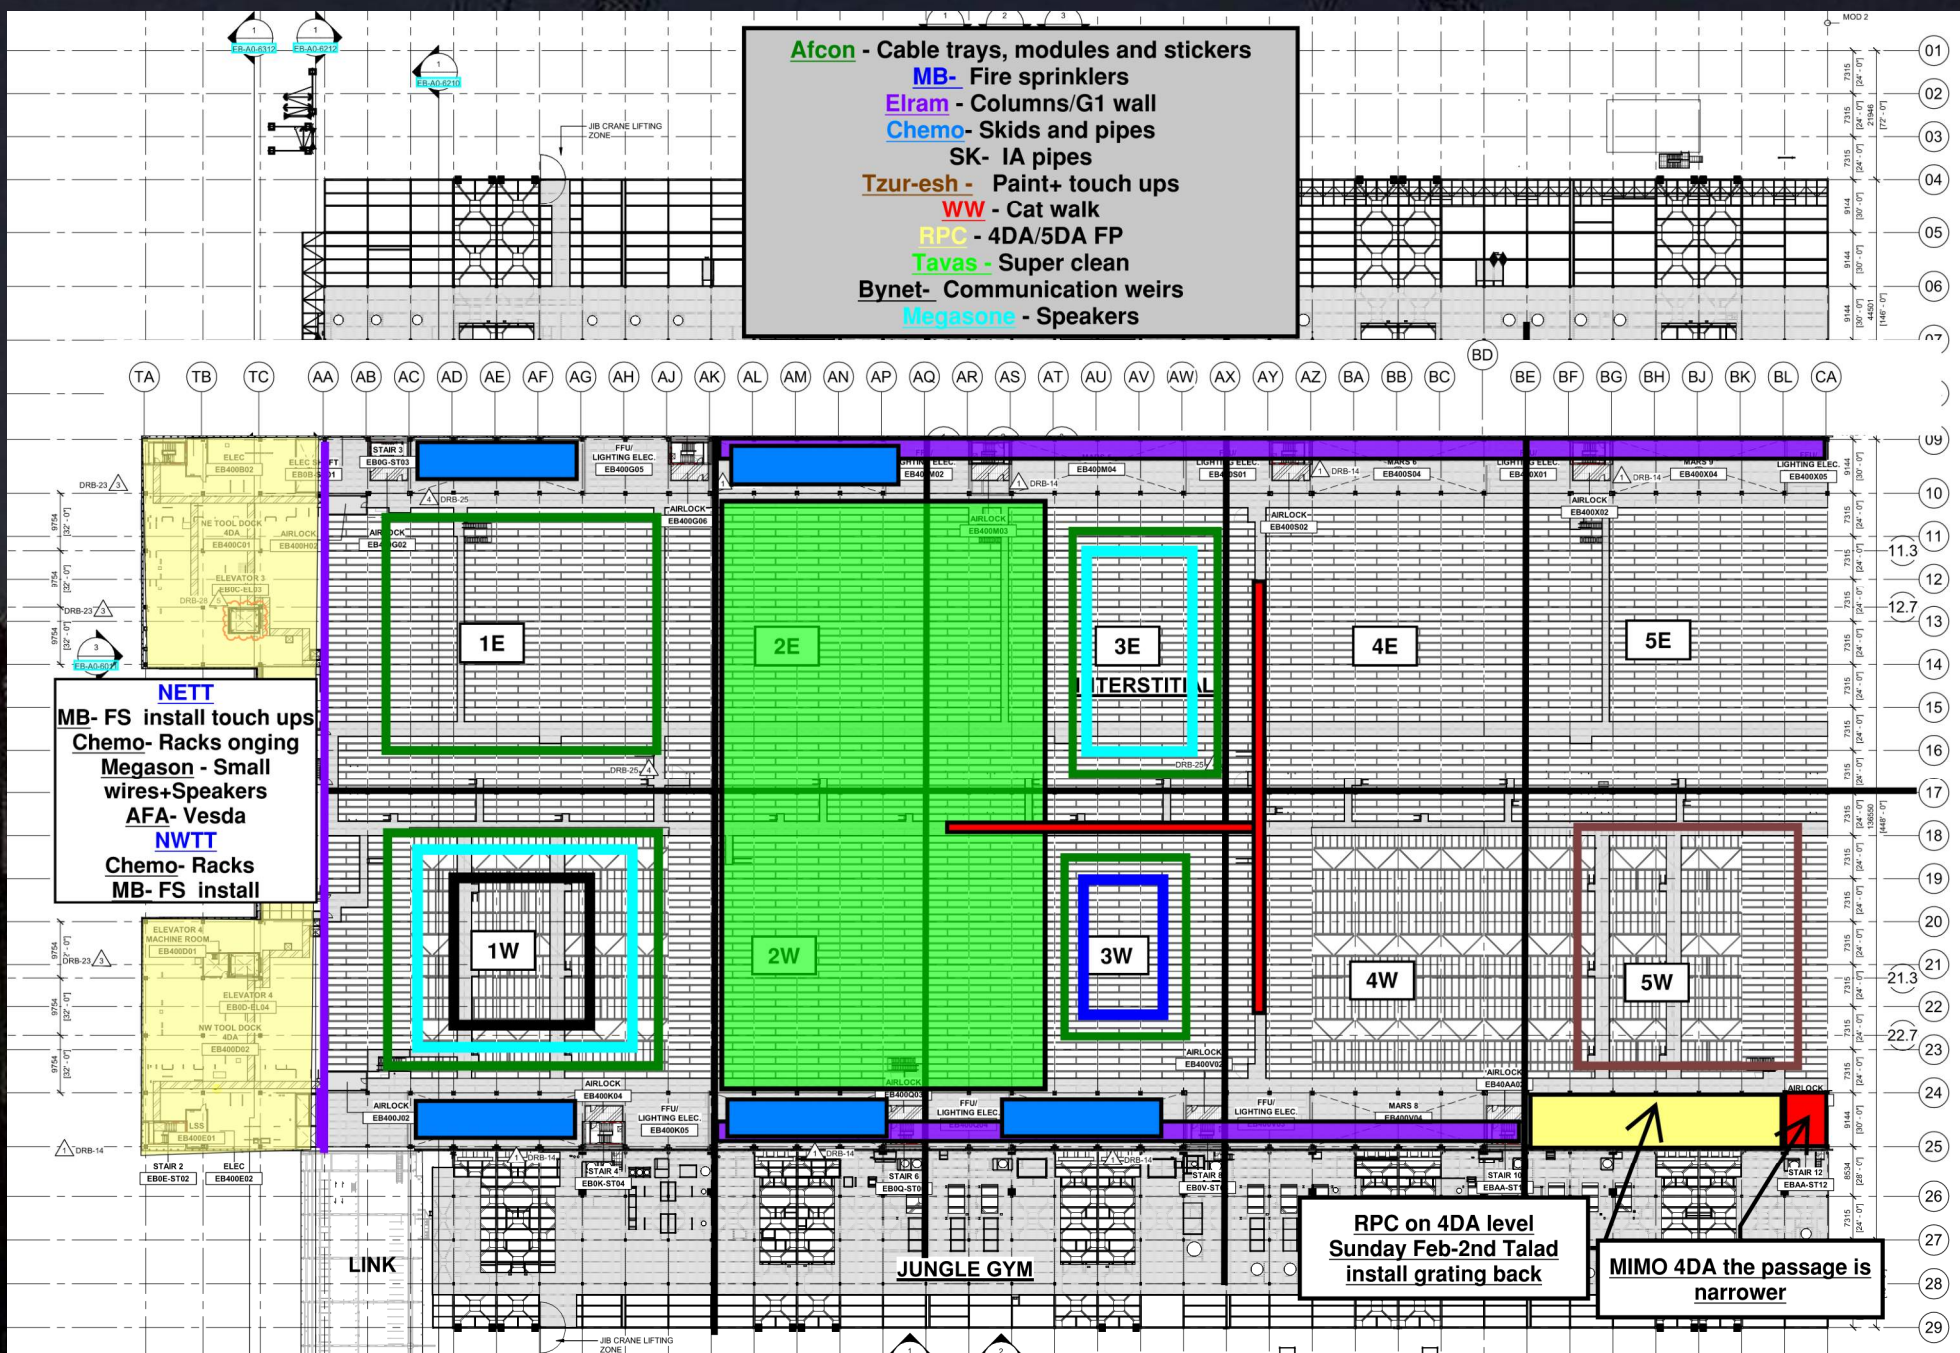



Main boom 44 m

Radius (m)	Jib length in (m)							
	20	29	41	53	62	71	83	95
14.2	64.2	1	1	1	1	1	1	1
17	52.3	50.4						
22	38.0	37.7	34.1					
24	34.1	33.9	33.1	24.5				
26	30.9	30.7	30.3	24.3				
28		28.1	27.7	23.8	18.5			
30		25.8	25.4	23.3	18.2	14.3		
34		22.1	21.8	21.3	17.5	13.8	9.8	
36		12.1	20.3	19.9	17.2	13.7	9.6	
38			19.0	18.5	17.0	13.4	9.4	6.2
46			14.9	14.5	14.2	12.6	8.6	5.6
55				11.4	11.2	10.8	7.9	5.0
65					8.8	8.4	7.3	4.5
75						6.7	6.3	3.9
85							4.9	n.c.
100								

South Tool Tower AHU's - Tapertech - Set Date 2/2/2025

AHU's = 10 Tons Maximum

LR1250

83 degree main Boom at 36 meter Radius = 20.3 Ton Capacity
49% of Capacity



Personal protocol violations

Personal protocol violations are documented and addressed in the following order:

*Employees name and number will be taken.

- **First violation:** team leader\champion will be informed.
- **Second violation:** team leader\champion will be informed + requires additional protocol training
- **Third violation:** Escalated to the HCC project manager.

Please note that violations will be based on the protocol spec as instructed during the trainings:

PL3 Dress code:



Put on Hair-net



Put on Beard cover



Put on shoe cover



Wear Latex Gloves



Siding - West FAB - JYG

BLOWDOWN 30%

[illegible]

LM BL BT BO BW BX BY BZ CA CB CC CD CE CF CG CH CI CJ CK CL CM CN CO CP CQ CR CS CT CU CV CW CX CY CZ DA DB DC DD DE DF DG DH DI DJ DK DL DM DN DO DP DQ DR DS DT DU DV DW DX DY DZ EA EB EC ED EE EF EG EH EI EJ EK EL EM EN EO EP EQ ER ES ET EU EV EW EX EY EZ FA FB FC FD FE FF FG FH FI FJ FK FL FM FN FO FP FQ FR FS FT FU FV FW FX FY FZ GA GB GC GD GE GF GH GI GJ GK GL GM GN GO GP GQ GR GS GT GU GV GW GX GY GZ HA HB HC HD HE HF HG HH HI HJ HK HL HM HN HO HP HQ HR HS HT HU HV HW HX HY HZ IA IB IC ID IE IF IG IH II IJ IK IL IM IN IO IP IQ IR IS IT IU IV IW IX IY IZ JA JB JC JD JE JF JG JH JI JJ JK JL JM JN JO JP JQ JR JS JT JU JV JW JX JY JZ KA KB KC KD KE KF KG KH KI KJ KL KM KN KO KP KQ KR KS KT KU KV KW KX KY KZ LA LB LC LD LE LF LG LH LI LJ LK LL LM LN LO LP LQ LR LS LT LU LV LW LX LY LZ MA MB MC MD ME MF MG MH MI MJ MK ML MN MO MP MQ MR MS MT MU MV MW MX MY MZ NA NB NC ND NE NF NG NH NI NJ NK NL NM NO NP NQ NR NS NT NU NV NW NX NY NZ OA OB OC OD OE OF OG OH OI OJ OK OL OM ON OP OQ OR OS OT OU OV OW OX OY OZ PA PB PC PD PE PF PG PH PI PJ PK PL PM PN PO PP PQ PR PS PT PU PV PW PX PY PZ QA QB QC QD QE QF QG QH QI QJ QK QL QM QN QO QP QQ QR QS QT QU QV QW QX QY QZ RA RB RC RD RE RF RG RH RI RJ RK RL RM RN RO RP RQ RR RS RT RU RV RW RX RY RZ SA SB SC SD SE SF SG SH SI SJ SK SL SM SN SO SP SQ SR SS ST SU SV SW SX SY SZ TA TB TC TD TE TF TG TH TI TJ TK TL TM TN TO TP TQ TR TS TT TU TV TW TX TY TZ UA UB UC UD UE UF UG UH UI UJ UK UL UM UN UO UP UQ UR US UT UY UZ VA VB VC VD VE VF VG VH VI VJ VK VL VM VN VO VP VQ VR VS VT VY VZ WA WB WC WD WE WF WG WH WI WJ WK WL WM WN WO WP WQ WR WS WT WY WZ XA XB XC XD XE XF XG XH XI XJ XK XL XM XN XO XP XQ XR XS XT XU XV XW XX XY XZ YA YB YC YD YE YF YG YH YI YJ YK YL YM YN YO YP YQ YR YS YT YU YV YW YX YY YZ ZA ZB ZC ZD ZE ZF ZG ZH ZI ZJ ZK ZL ZM ZN ZO ZP ZQ ZR ZS ZT ZU ZV ZW ZX ZY ZZ

Siding - East FAB - PSSS

BLOWDOWN 30%

OF - 172166.0

CK - 167798.0

Q 16'-1" - 162,037.0

1 - 156,825.2


150,349.064

143,433.6

CK - 147,700.0

1 - 145,647.2

DEMO

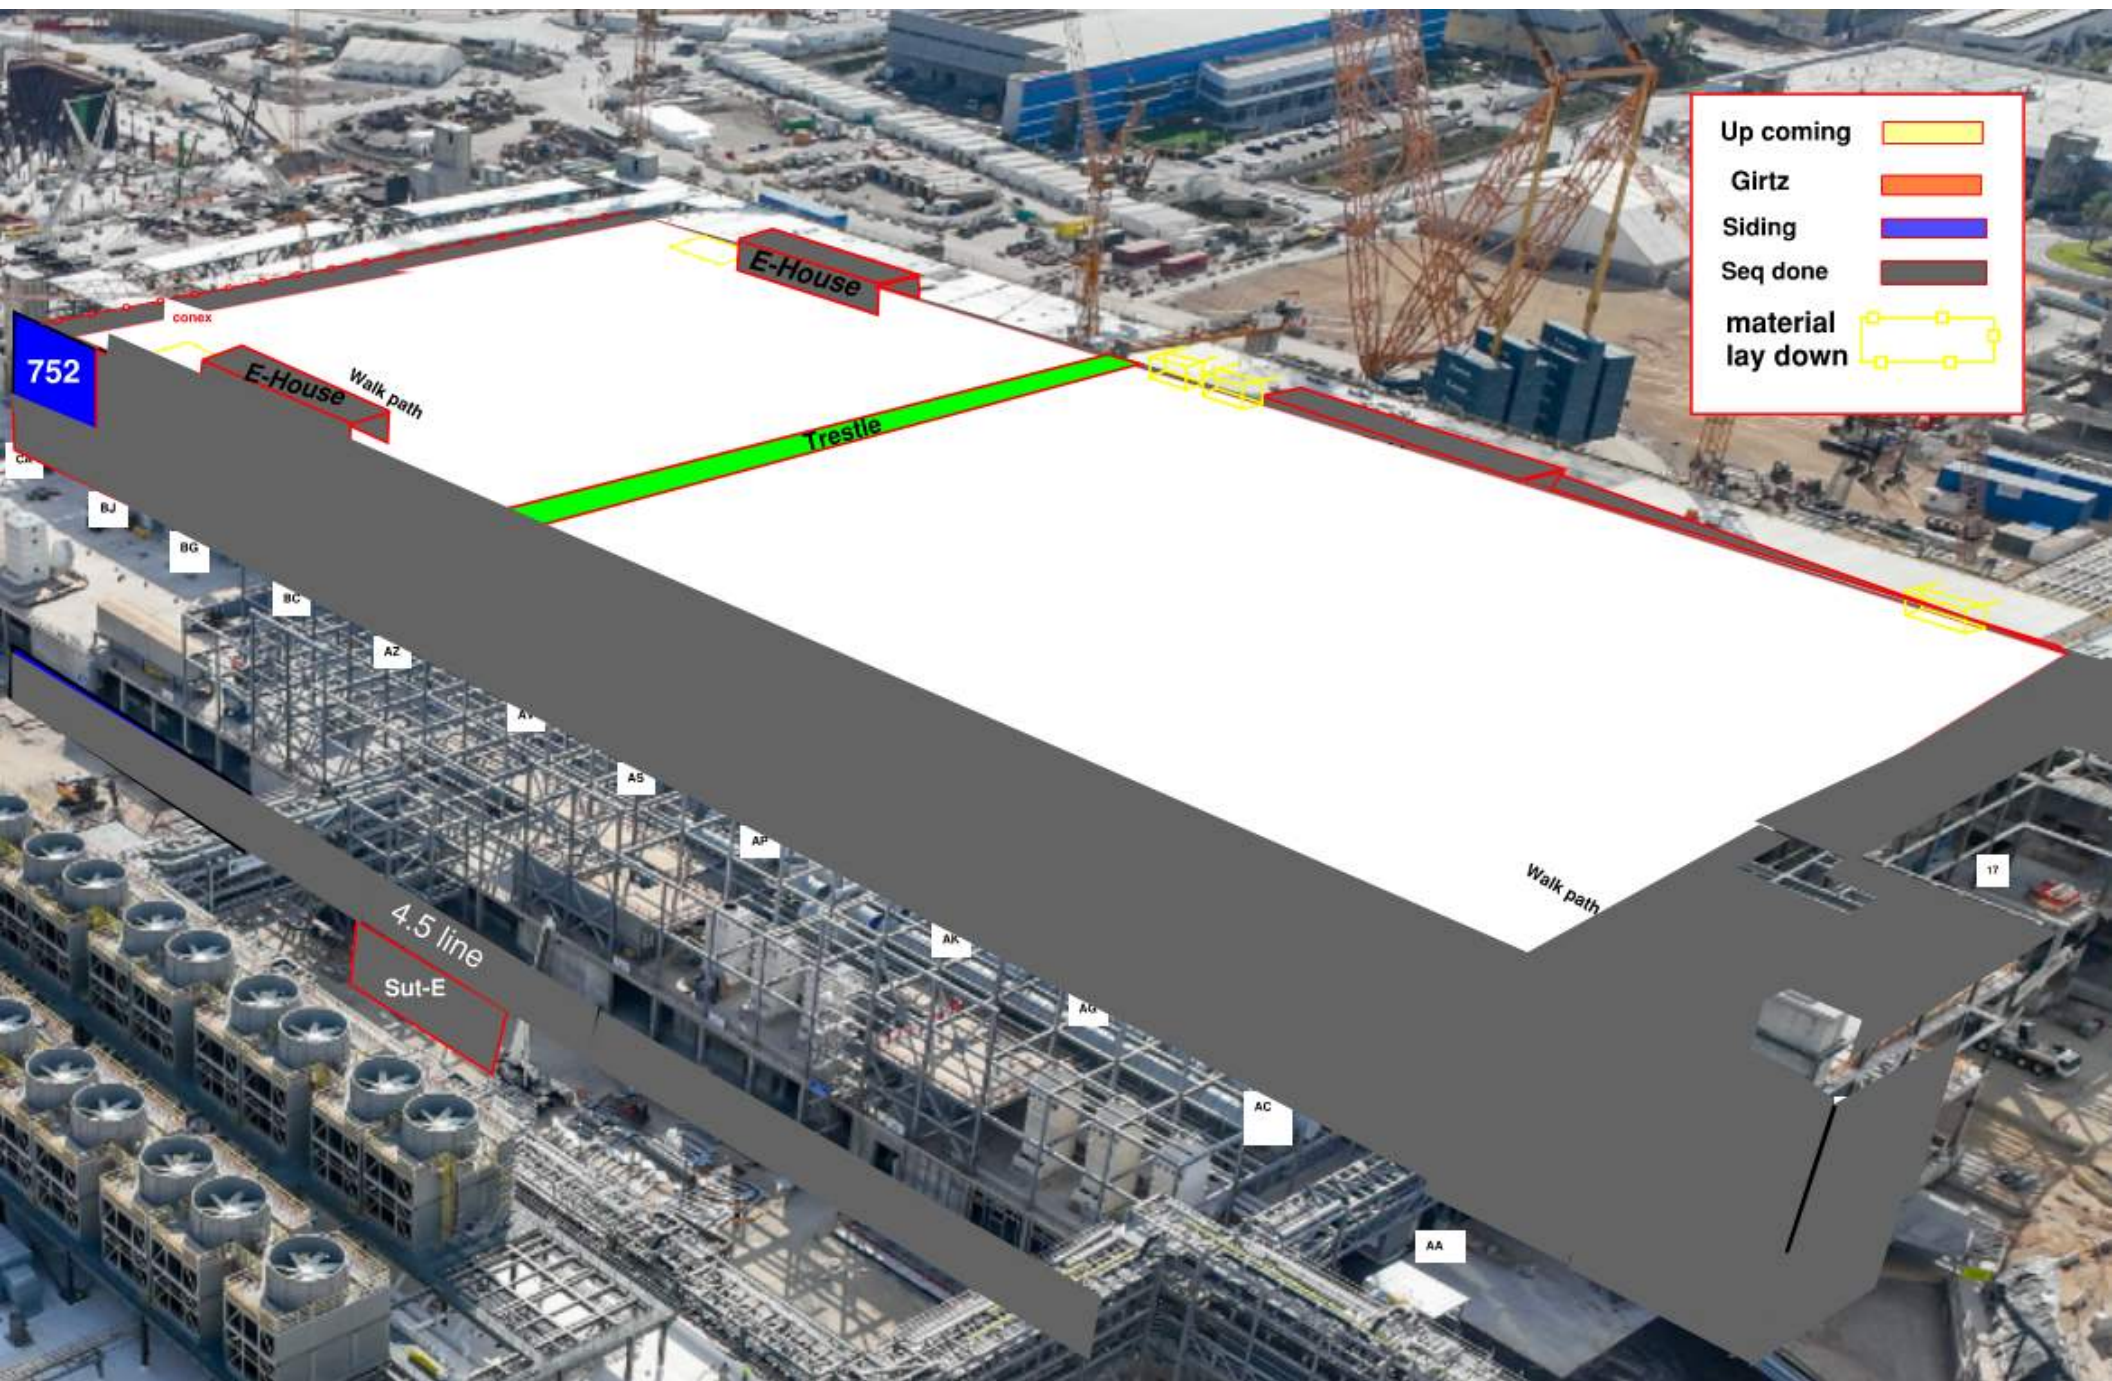

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

752

E-House

E-House

Walk path

Trestle

Walk path

4.5 line
Sut-E

BJ

BG

BC

AZ

AV

AS

AP


AK

AG

AC

AA

17

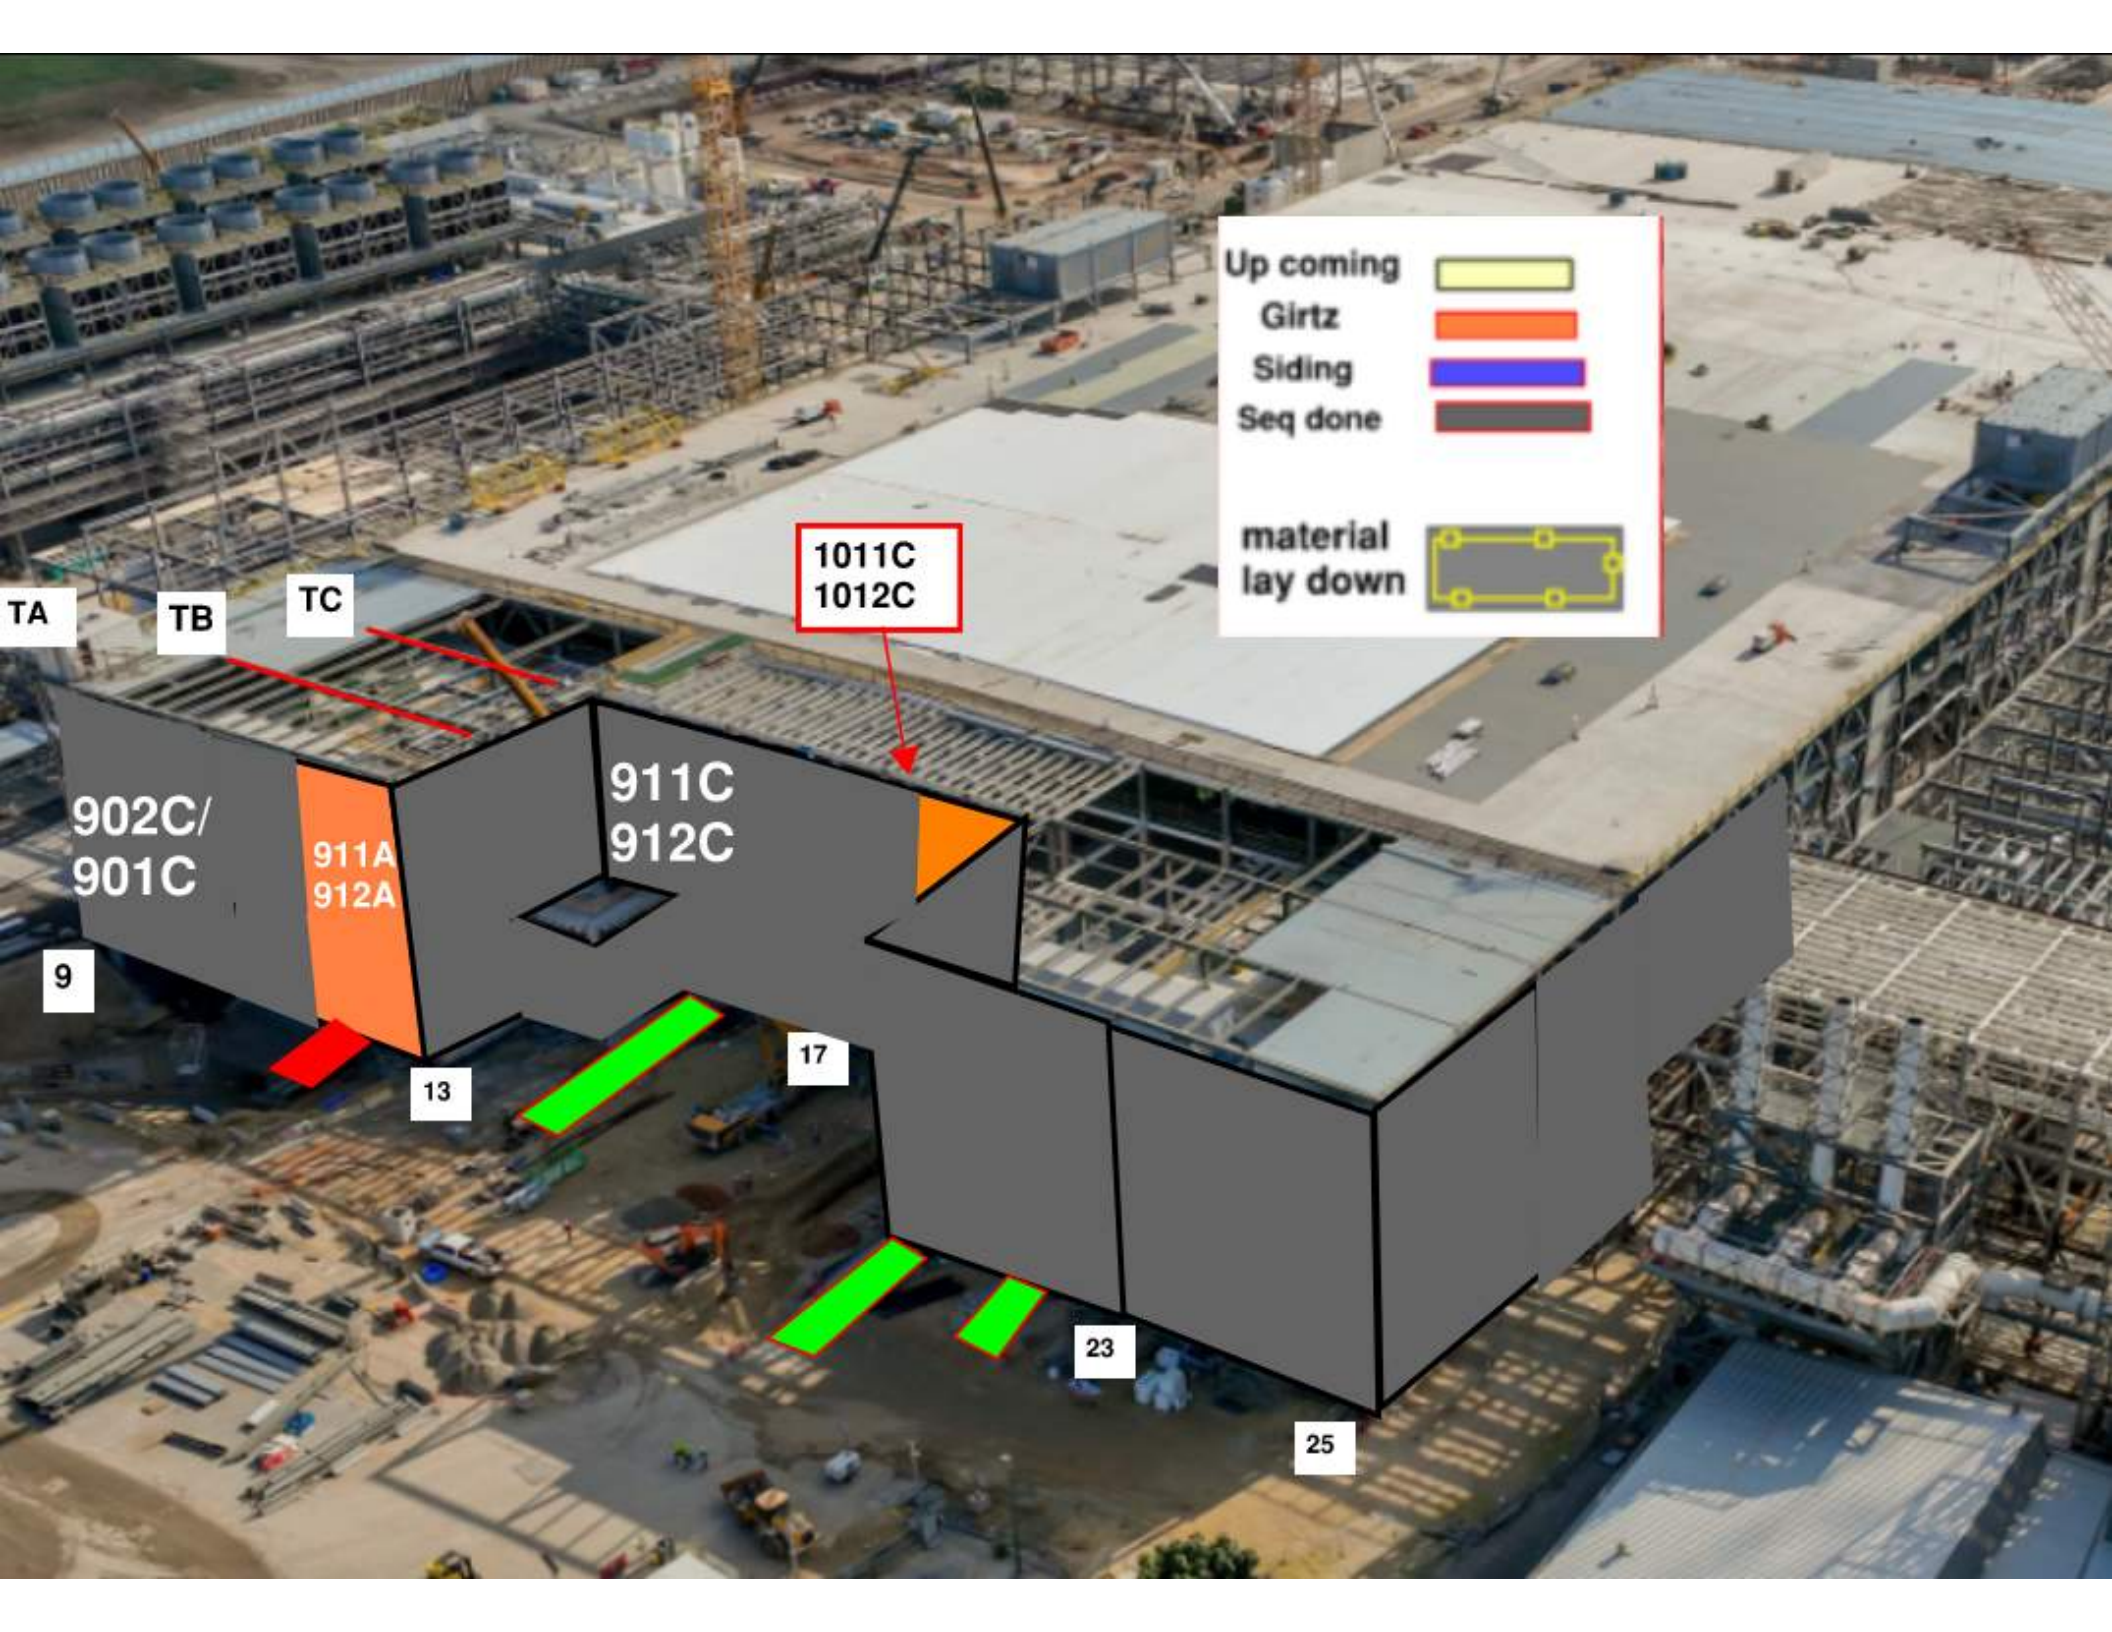

Up coming



Girtz



Siding



Seq done



material
lay down



TA

TB

TC

1011C
1012C

902C/
901C

911A
912A

911C
912C


9

13

17

23

25

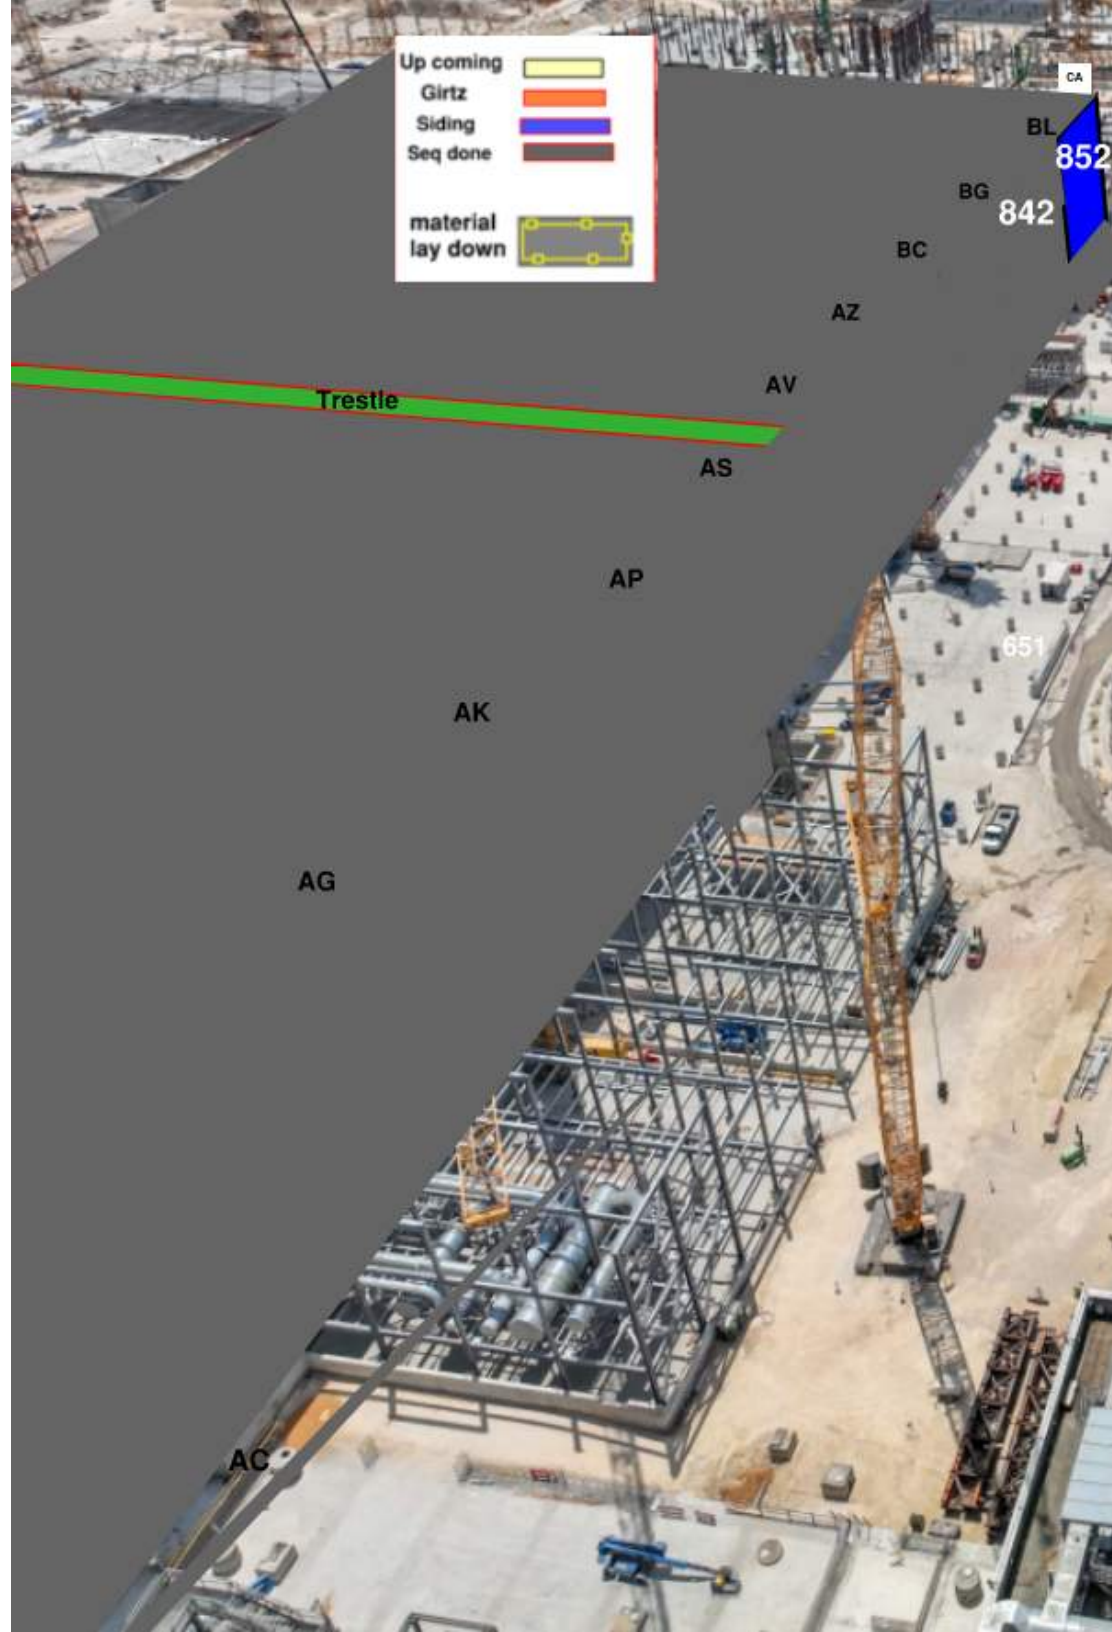

Up coming

Girtz

Siding

Seq done

material lay down

CA

BL

852

BG

842

BC

AZ

AV

AS

AP

AK

AG


AC

651

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

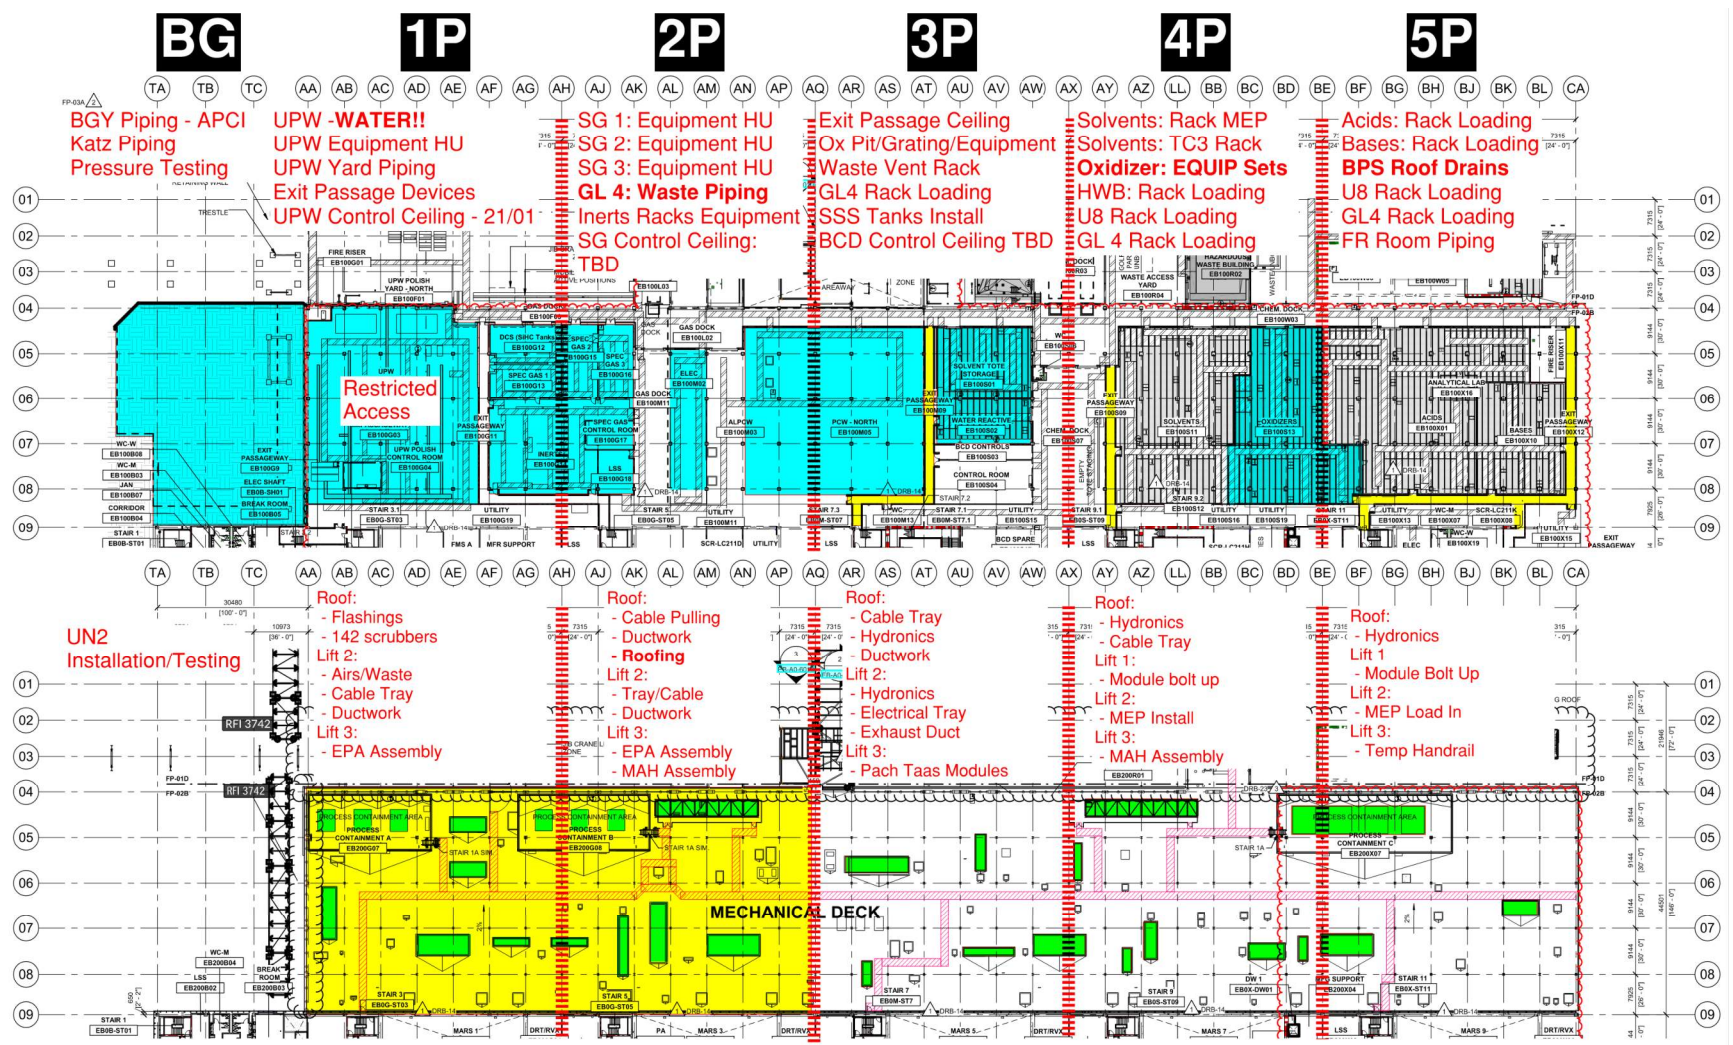


PSSS.2

Utility Level

1YA

PSSS Roof 2SA

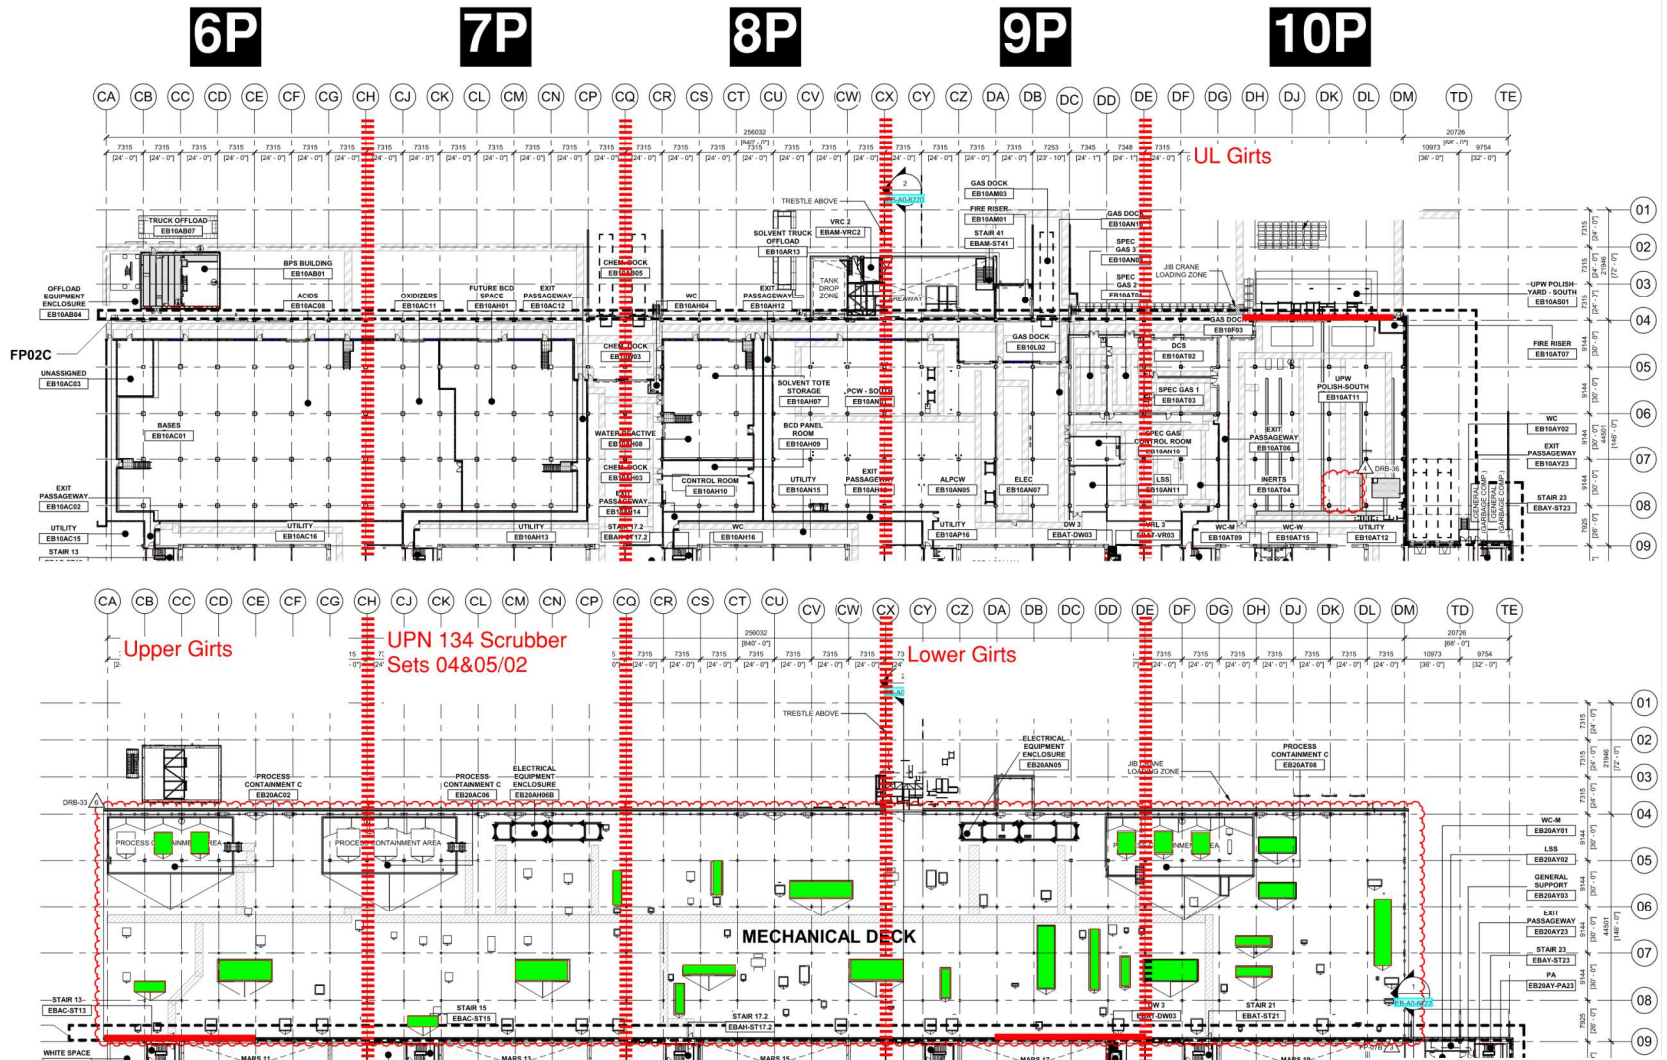

GN2


Analytical

BGY Closed


30/01 @12:00

to 02/02 @

23:59

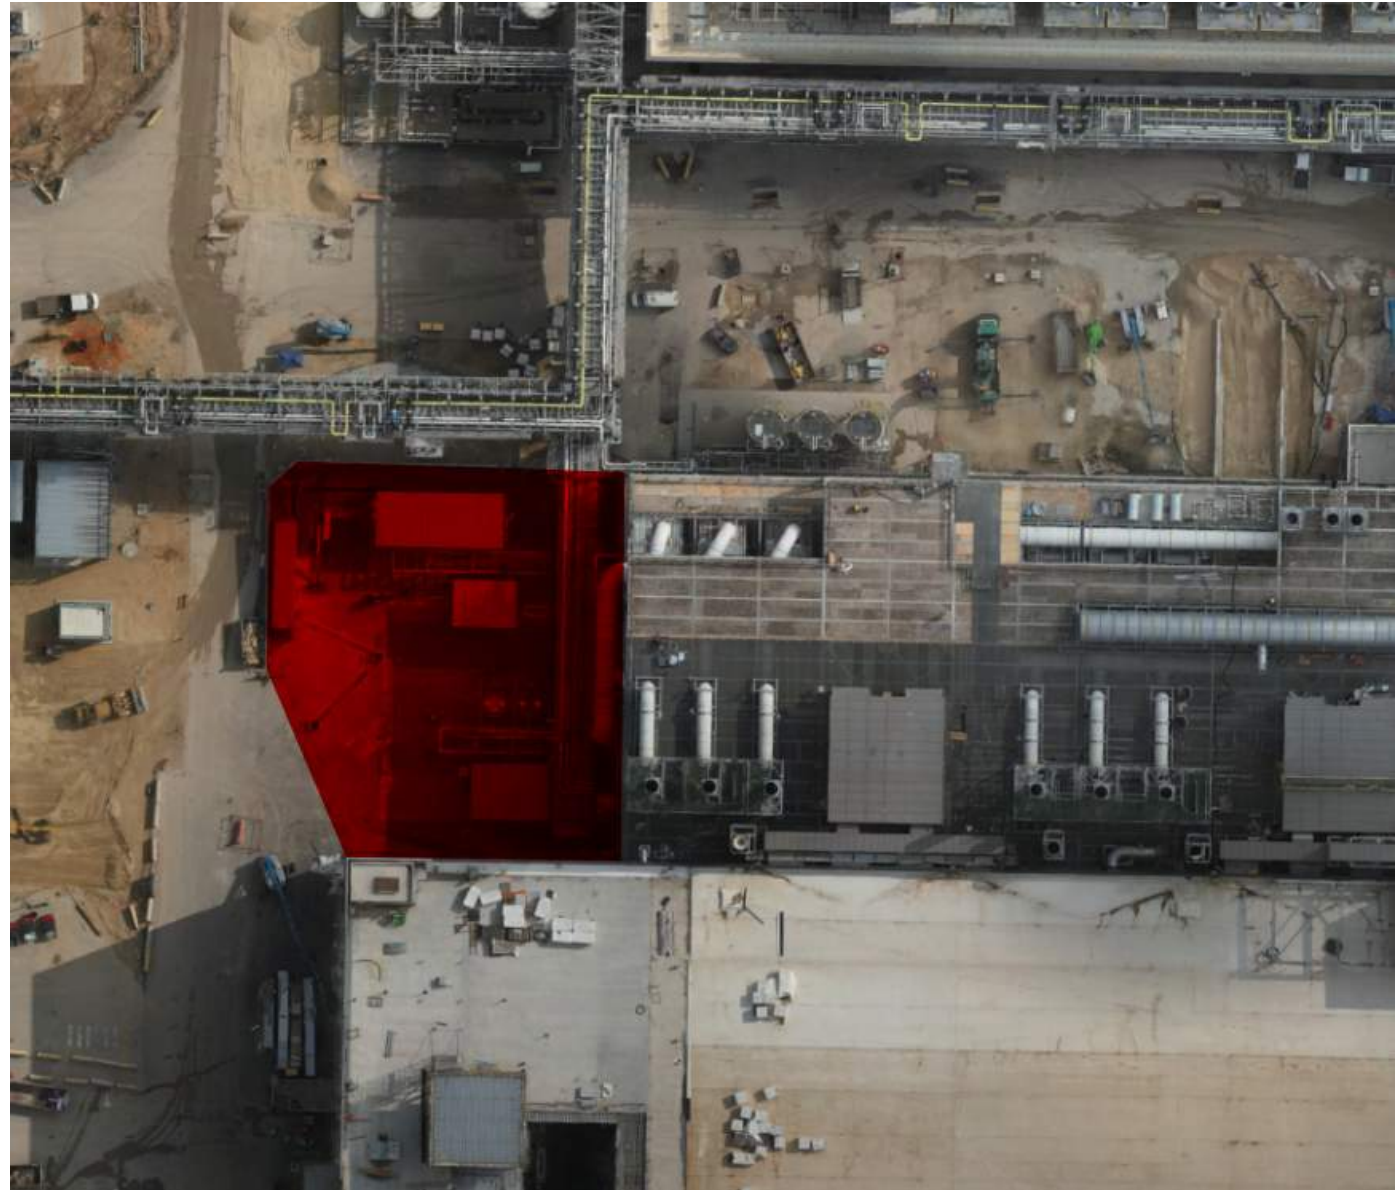


PSSS 02/02 Pressure Tests

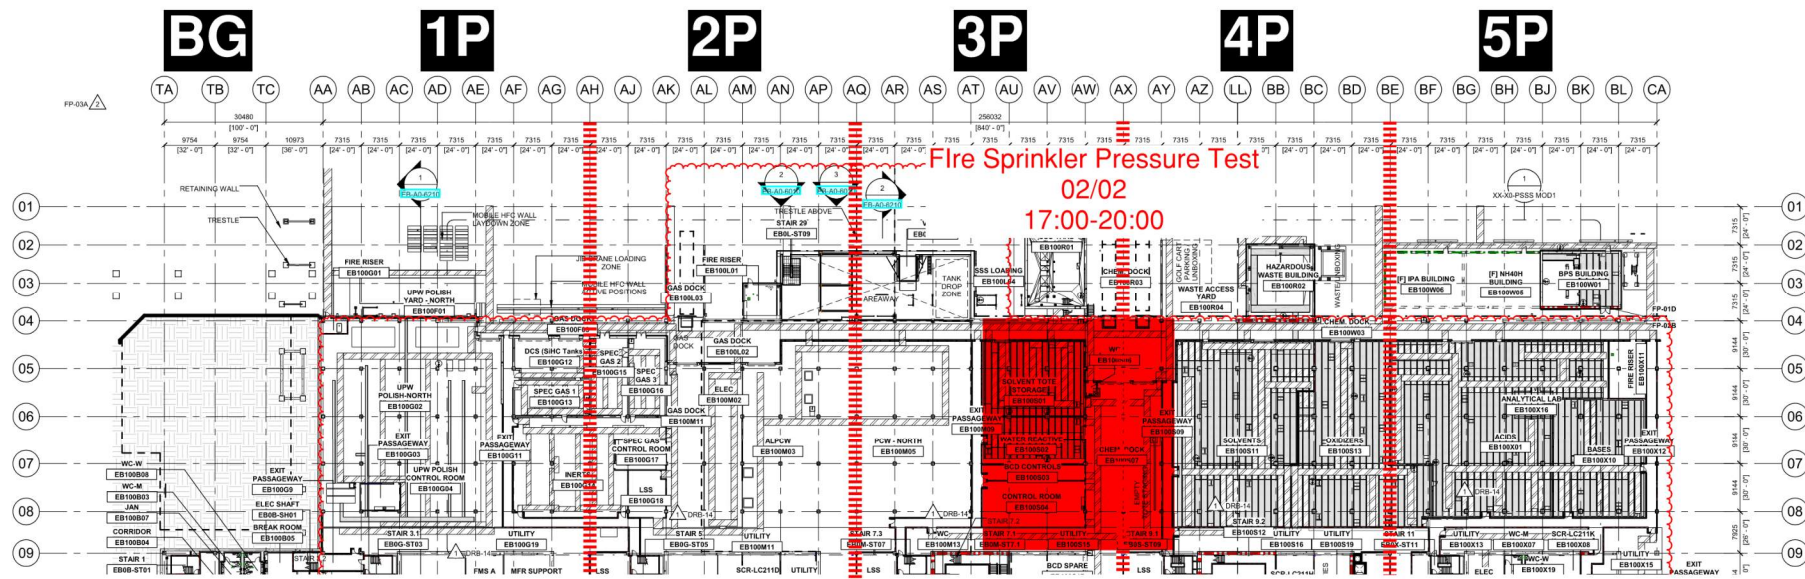

Utility Level 1YA

WJG 01J, 02J LIFT 2 & 3

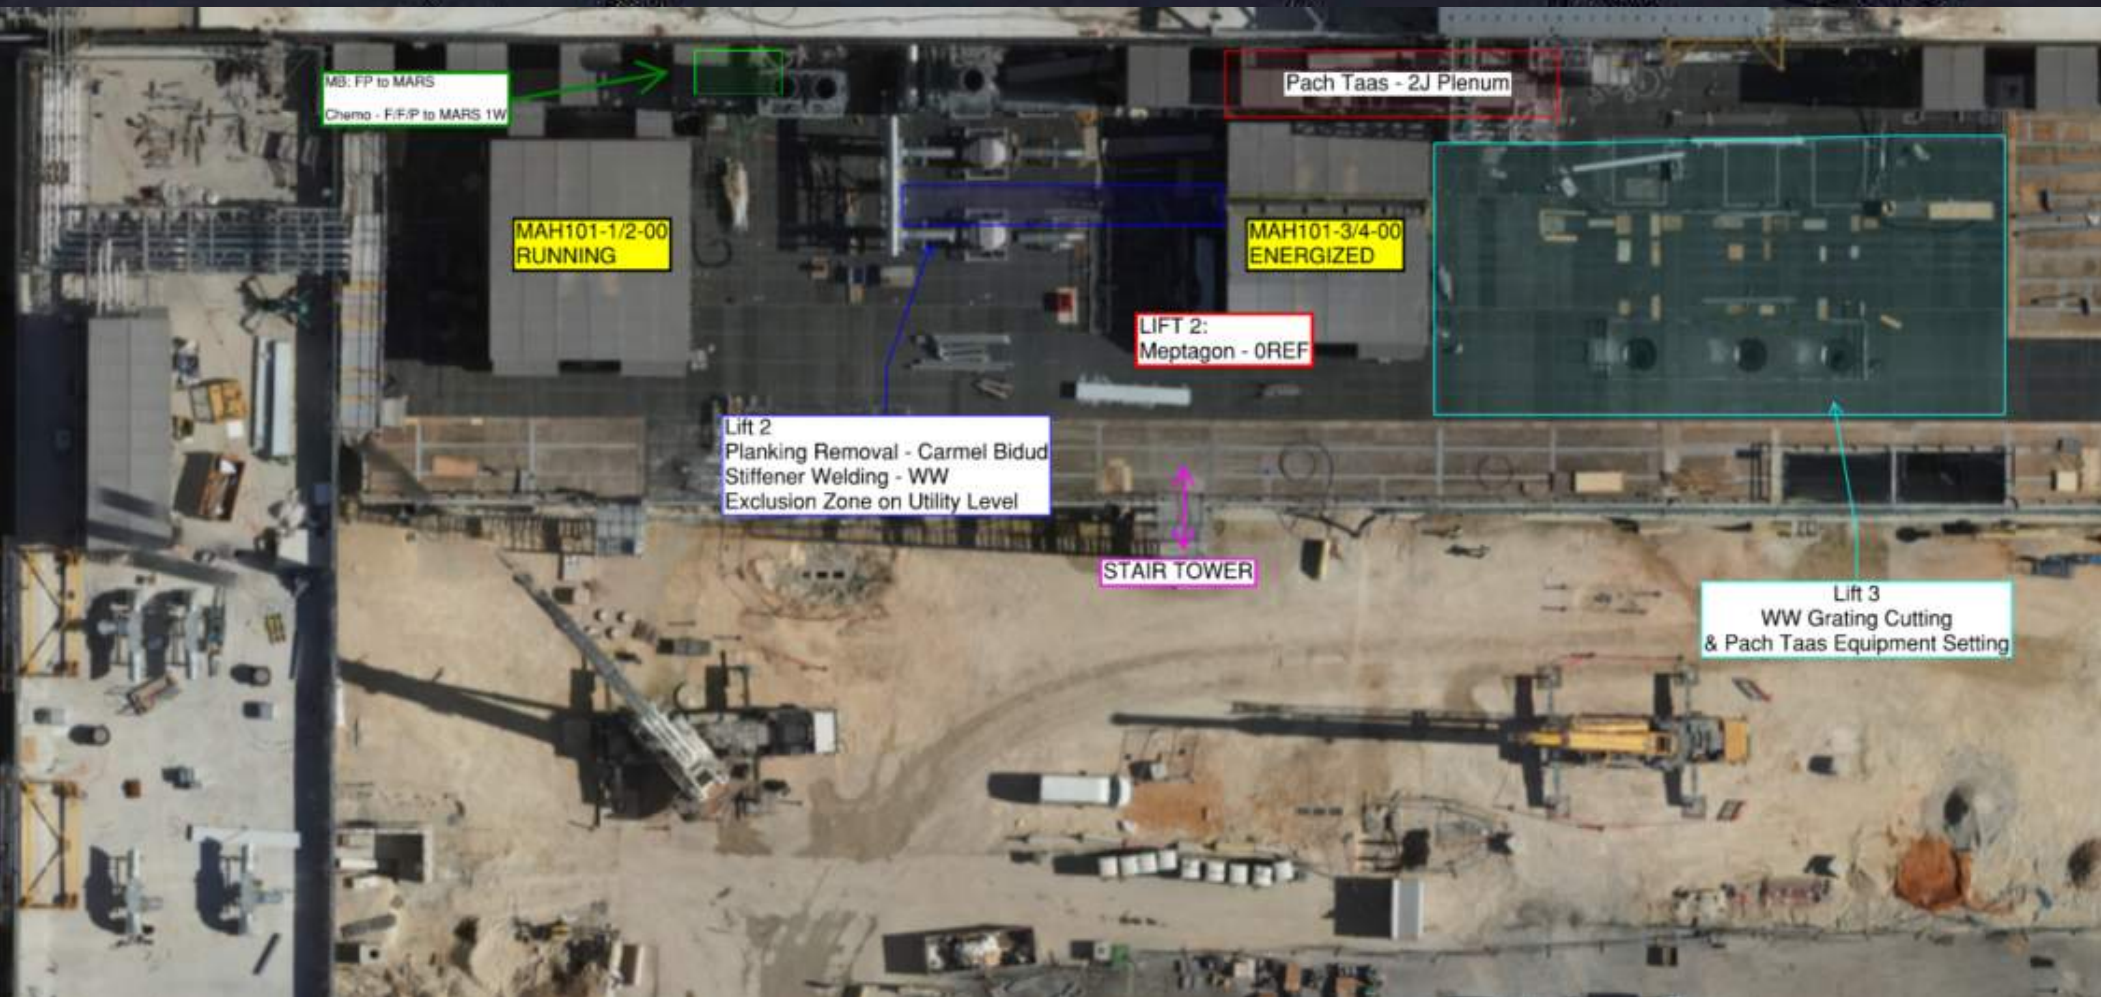


WJG 03J, 04J, 05J LIFT 2 & 3





WJG UTILITY LEVEL BUILD OUT

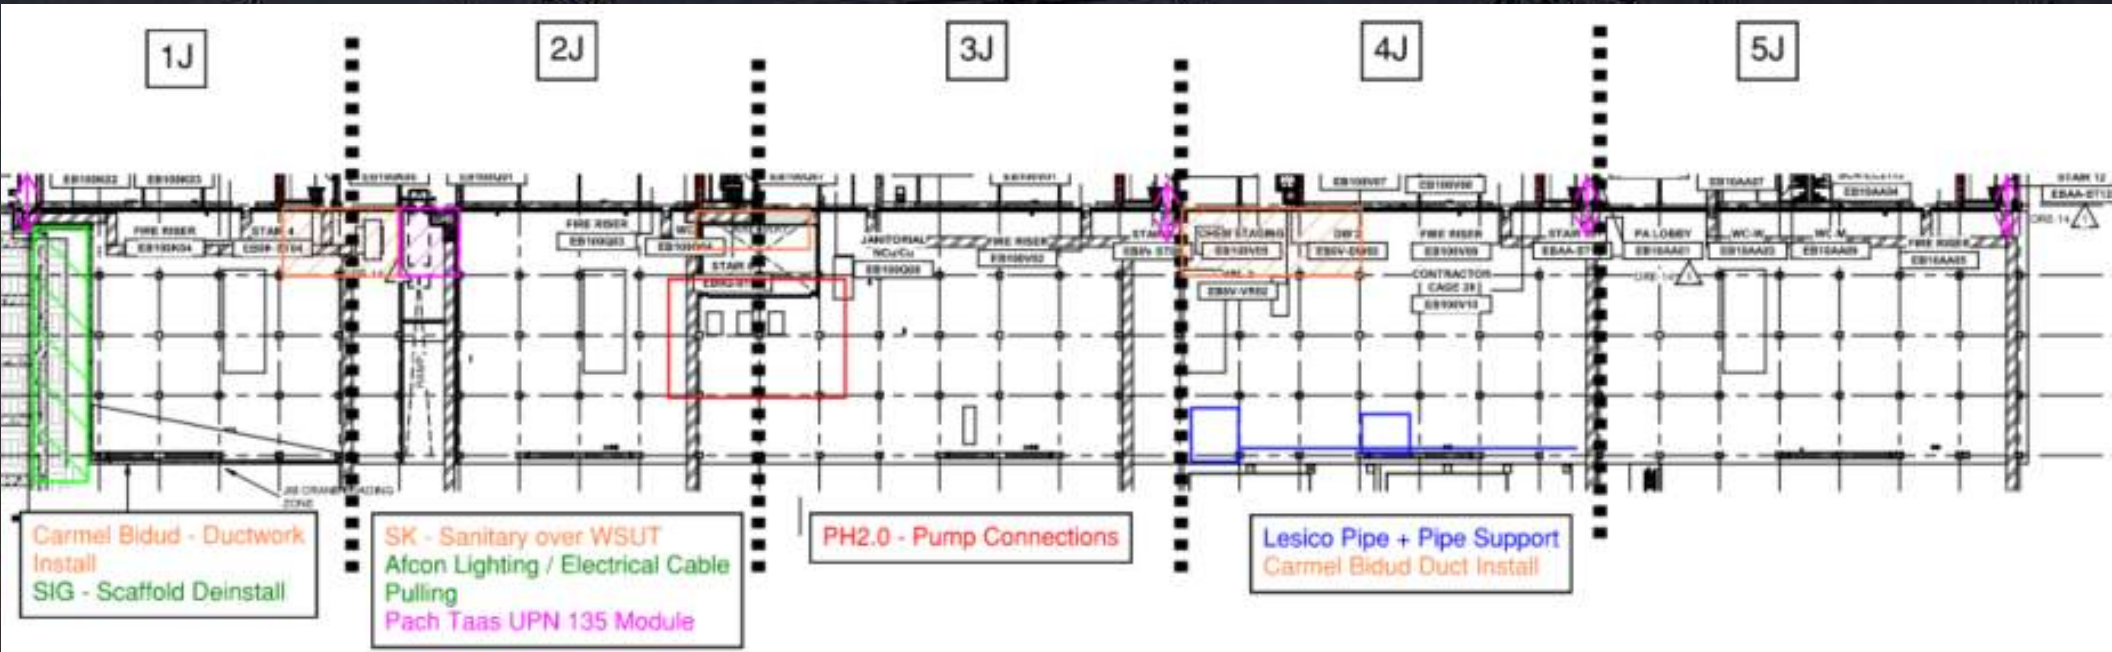

EAST YARD

BCS/BSA-JEA Pressure Test Jan.27

CUB 1 Evacuation Muster area North Yard

Paving North Yard WW 8

DRB 40 Scaffolding Meptagon Brand Roxtec Firestopping ongoing

ELECTRICAL

WWT OPS READY / PUNCHLIST RESTRICTED ACCESS SEE RED AREAS

TMWX to Roof Trestle Pressure Tests Inner pipe Jan 26 Outer pipe Jan 27

Insulation, Labeling Feb 5 QC walk DV Feb 10

Insulation, Labeling Feb 12 QC walk DV Feb 17

Insulation, Labeling Feb 5 QC walk DV Feb 10

NH4W 283

NH4W to Roof Trestle Pressure Tests Inner pipe Jan 23 Outer pipe Jan 27

Complete Chiller room lighting Jan 26- 30 Pending Scaffold removal

Trane/Rockwell Cx AFDs Chiller start dates: 126-1-10 Jan 23-29 111-1-10 Jan 30- Feb 2 126-3-10 Feb.6-12

Gas Detection OAT Feb.2

BOILERS

Natural Gas to Boiler Feb.16

Oil Fuel Tank

Revised Access

FUEL OFF LOADING INTEL ACCESS ONLY

Scaffold Removal dates Needed

NATURAL GAS EXCLUSION ZONE

WATER TREATMENT

IW Blend Station Pipe support adjustments Feb. 2-6

CTB 114

SWS 237

ROP 242

URW 262

UN2 / IA Tie-in Feb.2

CHILLERS

SAND FILTERS

CHILLERS

BOILERS

NH4W 283

Analyzer Room

MECH. CONTROL ROOM

MECH. WORKSHOP

LIWS LAB

FMS CONTROL ROOM I&C LAB

ELECTRICAL SHOP

WWT

TRUCK OFFLOAD 1

TRUCK OFFLOAD 2

TRUCK OFFLOAD 3

TRUCK OFFLOAD 4

TRUCK OFFLOAD 5

TRUCK OFFLOAD 6

TRUCK OFFLOAD 7

TRUCK OFFLOAD 8

TRUCK OFFLOAD 9

TRUCK OFFLOAD 10

TRUCK OFFLOAD 11

TRUCK OFFLOAD 12

TRUCK OFFLOAD 13

TRUCK OFFLOAD 14

TRUCK OFFLOAD 15

TRUCK OFFLOAD 16

TRUCK OFFLOAD 17

TRUCK OFFLOAD 18

TRUCK OFFLOAD 19

TRUCK OFFLOAD 20

TRUCK OFFLOAD 21

TRUCK OFFLOAD 22

TRUCK OFFLOAD 23

TRUCK OFFLOAD 24

TRUCK OFFLOAD 25

TRUCK OFFLOAD 26

TRUCK OFFLOAD 27

TRUCK OFFLOAD 28

TRUCK OFFLOAD 29

TRUCK OFFLOAD 30

TRUCK OFFLOAD 31

TRUCK OFFLOAD 32

TRUCK OFFLOAD 33

TRUCK OFFLOAD 34

TRUCK OFFLOAD 35

TRUCK OFFLOAD 36

TRUCK OFFLOAD 37

TRUCK OFFLOAD 38

TRUCK OFFLOAD 39

TRUCK OFFLOAD 40

TRUCK OFFLOAD 41

TRUCK OFFLOAD 42

TRUCK OFFLOAD 43

TRUCK OFFLOAD 44

TRUCK OFFLOAD 45

TRUCK OFFLOAD 46

TRUCK OFFLOAD 47

TRUCK OFFLOAD 48

TRUCK OFFLOAD 49

TRUCK OFFLOAD 50

TRUCK OFFLOAD 51

TRUCK OFFLOAD 52

TRUCK OFFLOAD 53

TRUCK OFFLOAD 54

TRUCK OFFLOAD 55

TRUCK OFFLOAD 56

TRUCK OFFLOAD 57

TRUCK OFFLOAD 58

TRUCK OFFLOAD 59

TRUCK OFFLOAD 60

TRUCK OFFLOAD 61

TRUCK OFFLOAD 62

TRUCK OFFLOAD 63

TRUCK OFFLOAD 64

TRUCK OFFLOAD 65

TRUCK OFFLOAD 66

TRUCK OFFLOAD 67

TRUCK OFFLOAD 68

TRUCK OFFLOAD 69

TRUCK OFFLOAD 70

TRUCK OFFLOAD 71

TRUCK OFFLOAD 72

TRUCK OFFLOAD 73

TRUCK OFFLOAD 74

TRUCK OFFLOAD 75

TRUCK OFFLOAD 76

TRUCK OFFLOAD 77

TRUCK OFFLOAD 78

TRUCK OFFLOAD 79

TRUCK OFFLOAD 80

TRUCK OFFLOAD 81

TRUCK OFFLOAD 82

TRUCK OFFLOAD 83

TRUCK OFFLOAD 84

TRUCK OFFLOAD 85

TRUCK OFFLOAD 86

TRUCK OFFLOAD 87

TRUCK OFFLOAD 88

TRUCK OFFLOAD 89

TRUCK OFFLOAD 90

TRUCK OFFLOAD 91

TRUCK OFFLOAD 92

TRUCK OFFLOAD 93

TRUCK OFFLOAD 94

TRUCK OFFLOAD 95

TRUCK OFFLOAD 96

TRUCK OFFLOAD 97

TRUCK OFFLOAD 98

TRUCK OFFLOAD 99

TRUCK OFFLOAD 100

TRUCK OFFLOAD 101

TRUCK OFFLOAD 102

TRUCK OFFLOAD 103

TRUCK OFFLOAD 104

TRUCK OFFLOAD 105

TRUCK OFFLOAD 106

TRUCK OFFLOAD 107

TRUCK OFFLOAD 108

TRUCK OFFLOAD 109

TRUCK OFFLOAD 110

TRUCK OFFLOAD 111

TRUCK OFFLOAD 112

TRUCK OFFLOAD 113

TRUCK OFFLOAD 114

TRUCK OFFLOAD 115

TRUCK OFFLOAD 116

TRUCK OFFLOAD 117

TRUCK OFFLOAD 118

TRUCK OFFLOAD 119

TRUCK OFFLOAD 120

TRUCK OFFLOAD 121

TRUCK OFFLOAD 122

TRUCK OFFLOAD 123

TRUCK OFFLOAD 124

TRUCK OFFLOAD 125

TRUCK OFFLOAD 126

TRUCK OFFLOAD 127

TRUCK OFFLOAD 128

TRUCK OFFLOAD 129

TRUCK OFFLOAD 130

TRUCK OFFLOAD 131

TRUCK OFFLOAD 132

TRUCK OFFLOAD 133

TRUCK OFFLOAD 134

TRUCK OFFLOAD 135

TRUCK OFFLOAD 136

TRUCK OFFLOAD 137

TRUCK OFFLOAD 138

TRUCK OFFLOAD 139

TRUCK OFFLOAD 140

TRUCK OFFLOAD 141

TRUCK OFFLOAD 142

TRUCK OFFLOAD 143

TRUCK OFFLOAD 144

TRUCK OFFLOAD 145

TRUCK OFFLOAD 146

TRUCK OFFLOAD 147

TRUCK OFFLOAD 148

TRUCK OFFLOAD 149

TRUCK OFFLOAD 150

TRUCK OFFLOAD 151

TRUCK OFFLOAD 152

TRUCK OFFLOAD 153

TRUCK OFFLOAD 154

TRUCK OFFLOAD 155

TRUCK OFFLOAD 156

TRUCK OFFLOAD 157

TRUCK OFFLOAD 158

TRUCK OFFLOAD 159

TRUCK OFFLOAD 160

TRUCK OFFLOAD 161

TRUCK OFFLOAD 162

TRUCK OFFLOAD 163

TRUCK OFFLOAD 164

TRUCK OFFLOAD 165

TRUCK OFFLOAD 166

TRUCK OFFLOAD 167

TRUCK OFFLOAD 168

TRUCK OFFLOAD 169

TRUCK OFFLOAD 170

TRUCK OFFLOAD 171

TRUCK OFFLOAD 172

TRUCK OFFLOAD 173

TRUCK OFFLOAD 174

TRUCK OFFLOAD 175

TRUCK OFFLOAD 176

TRUCK OFFLOAD 177

TRUCK OFFLOAD 178

TRUCK OFFLOAD 179


TRUCK OFFLOAD 180

TRUCK OFFLOAD 181

TRUCK OFFLOAD 182


TRUCK

CUB 1 – EXTERIOR/ROOF

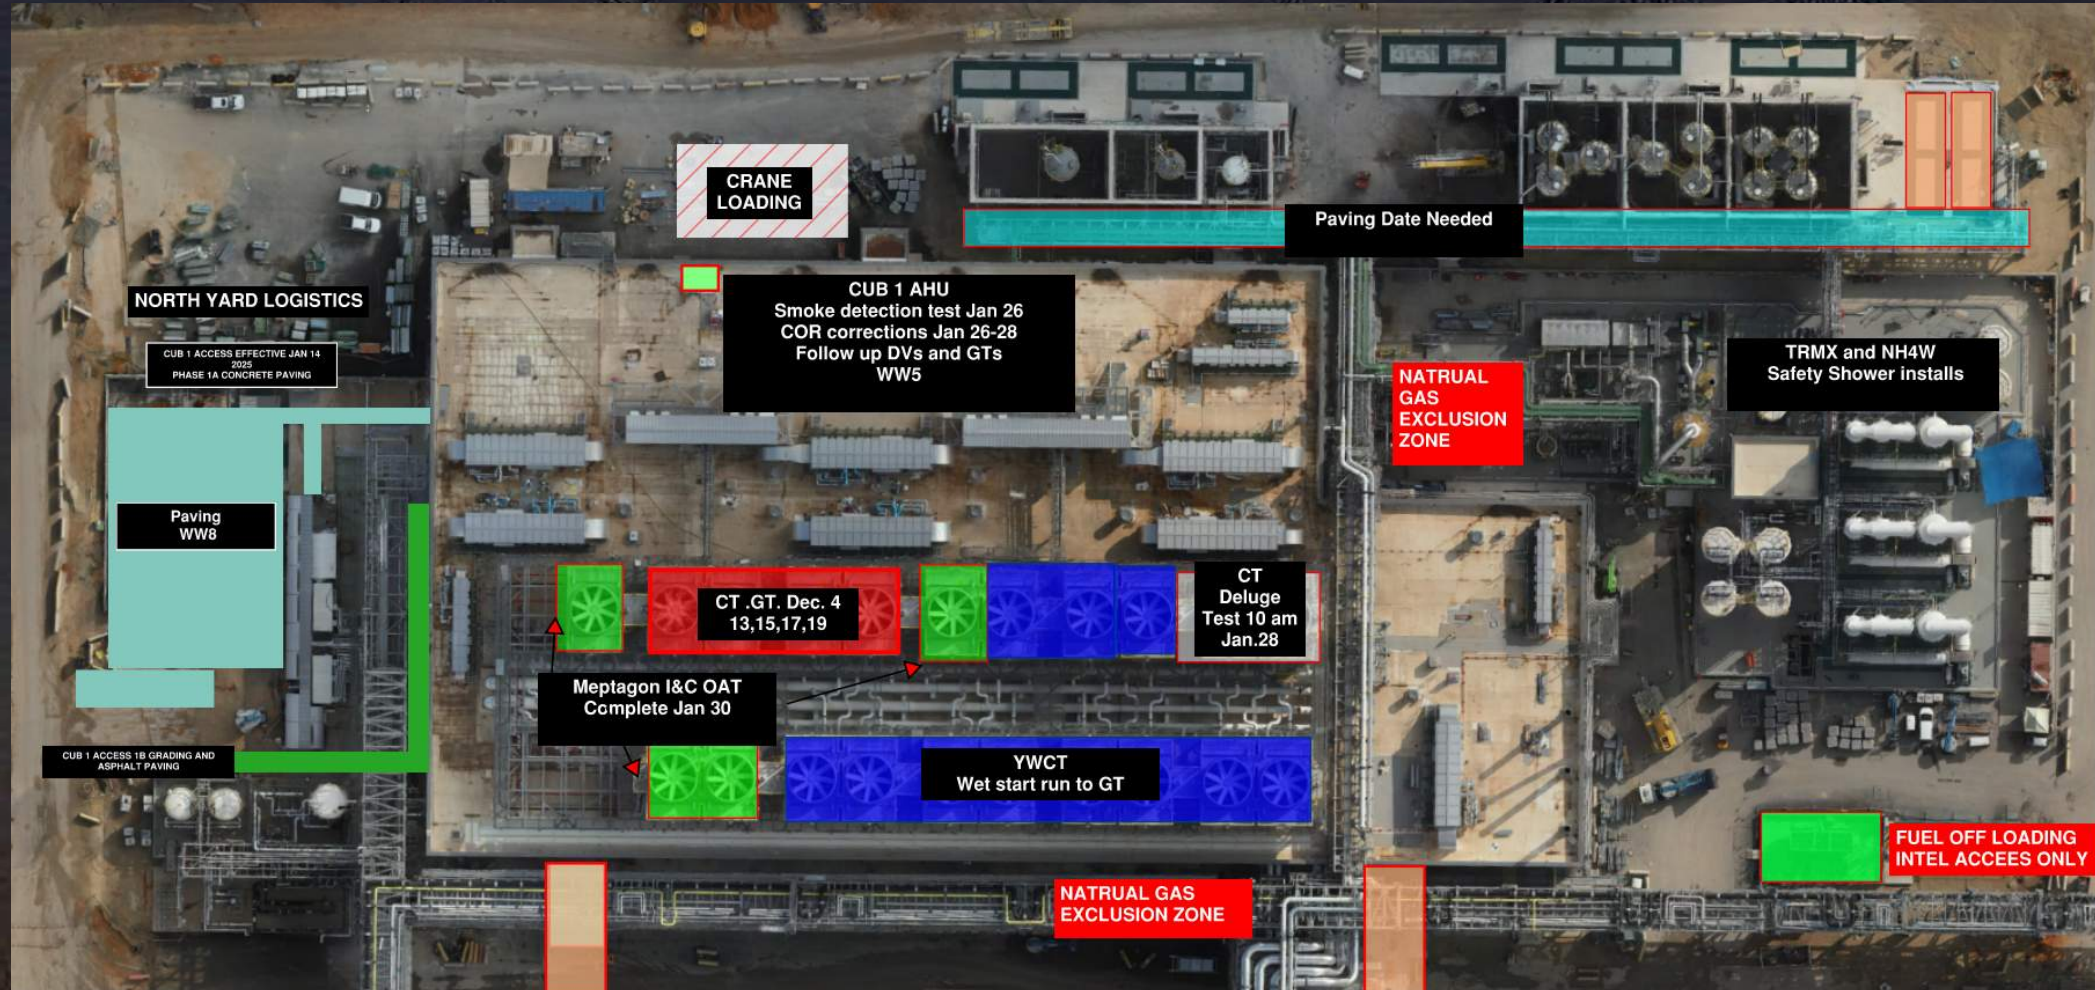



CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

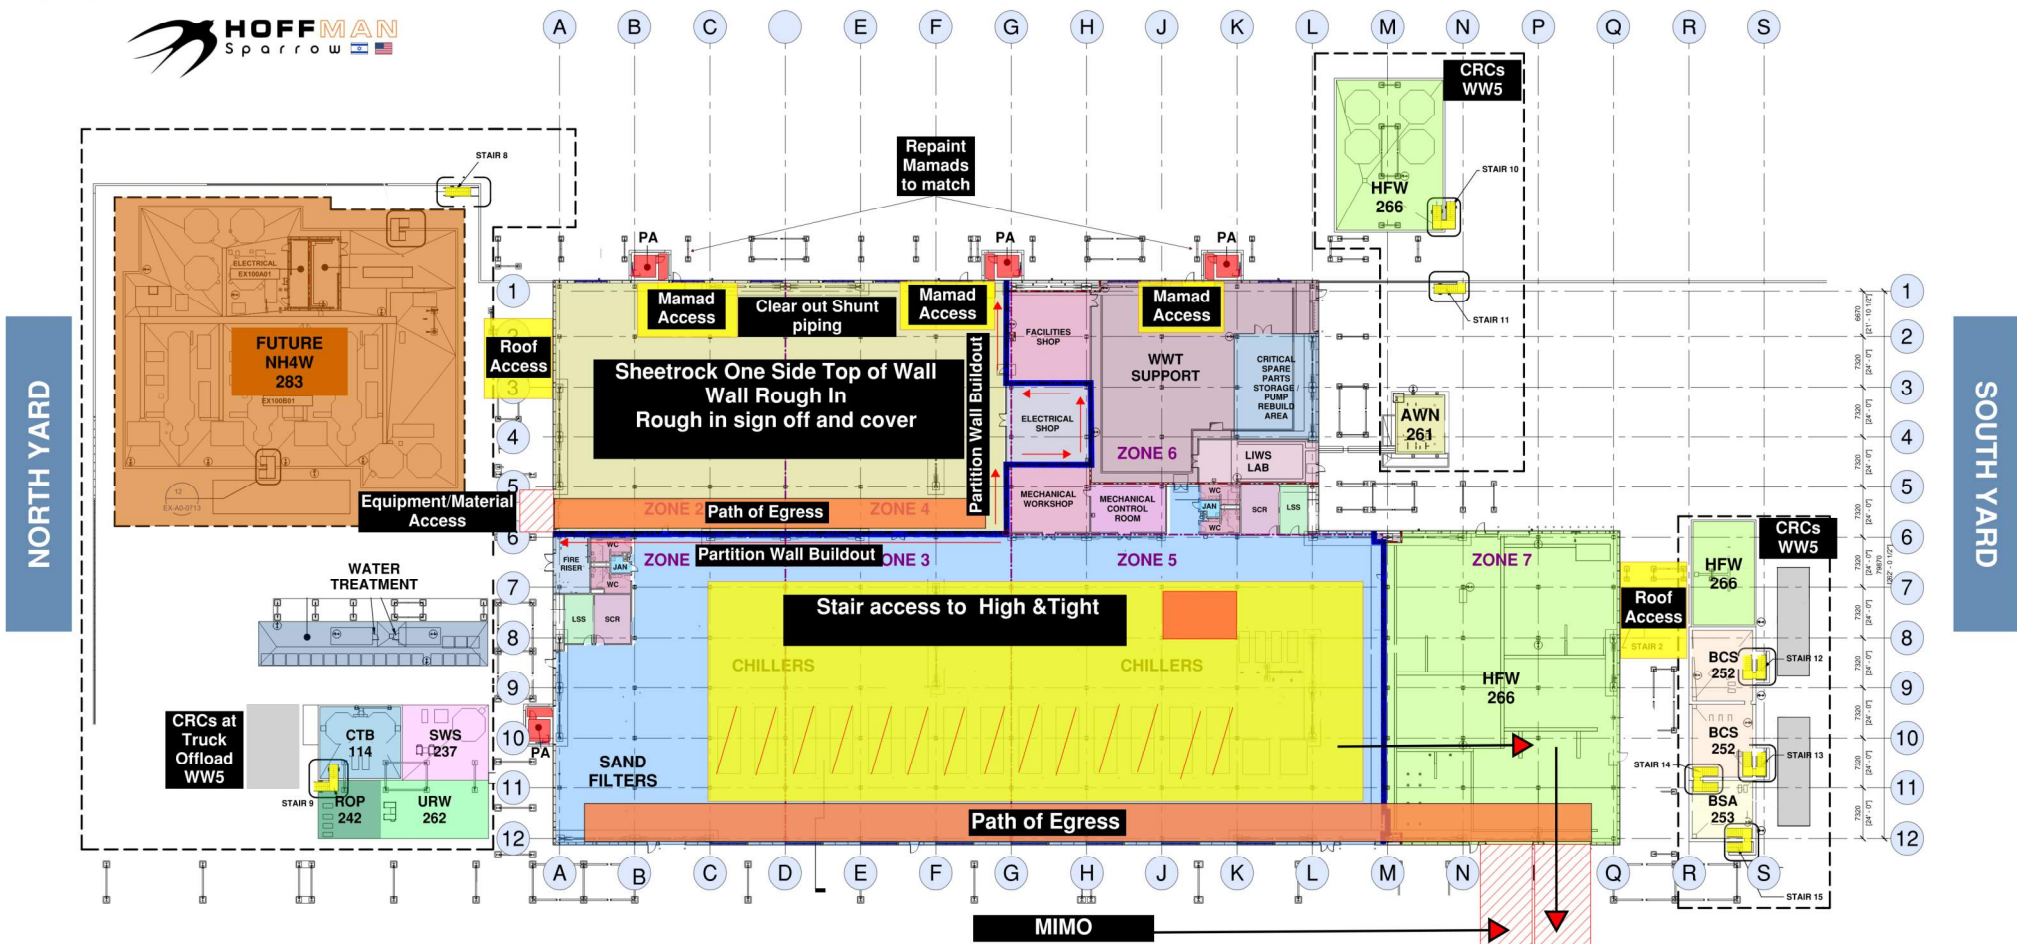


CUB 2 – EXTERIOR/ROOF

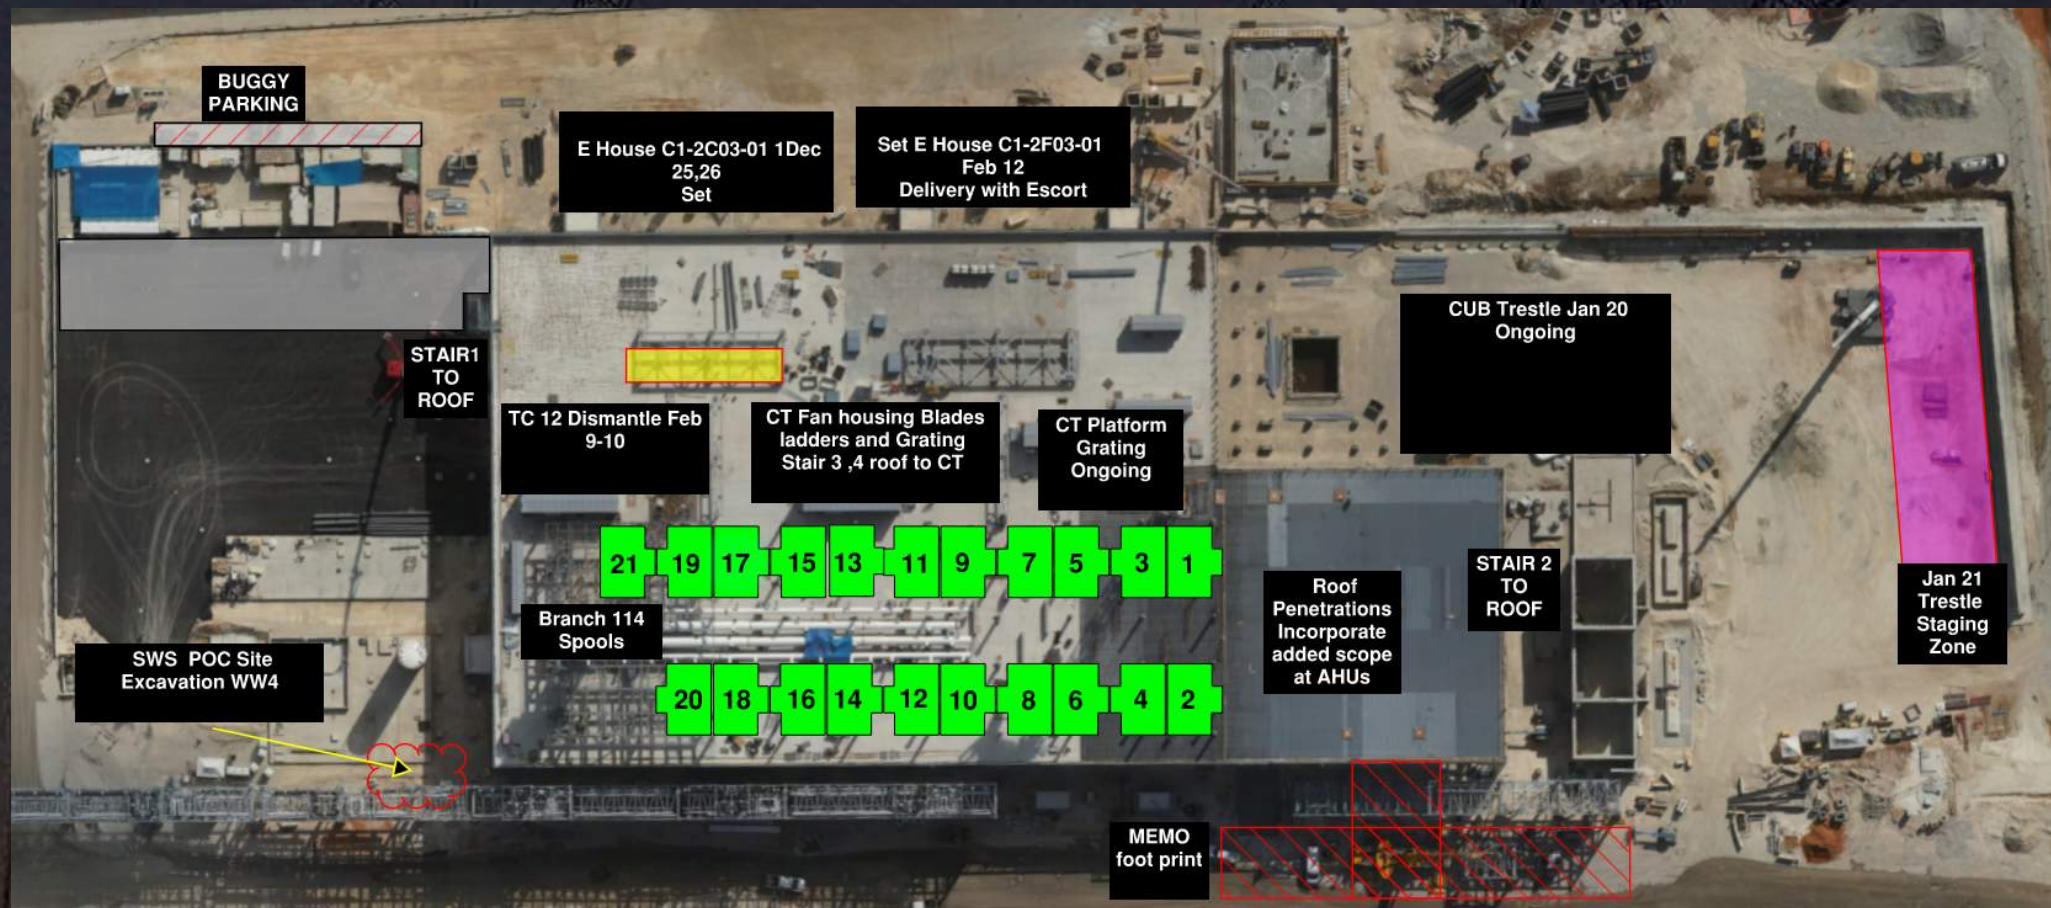



HOFFMAN CONSTRUCTION COMPANY

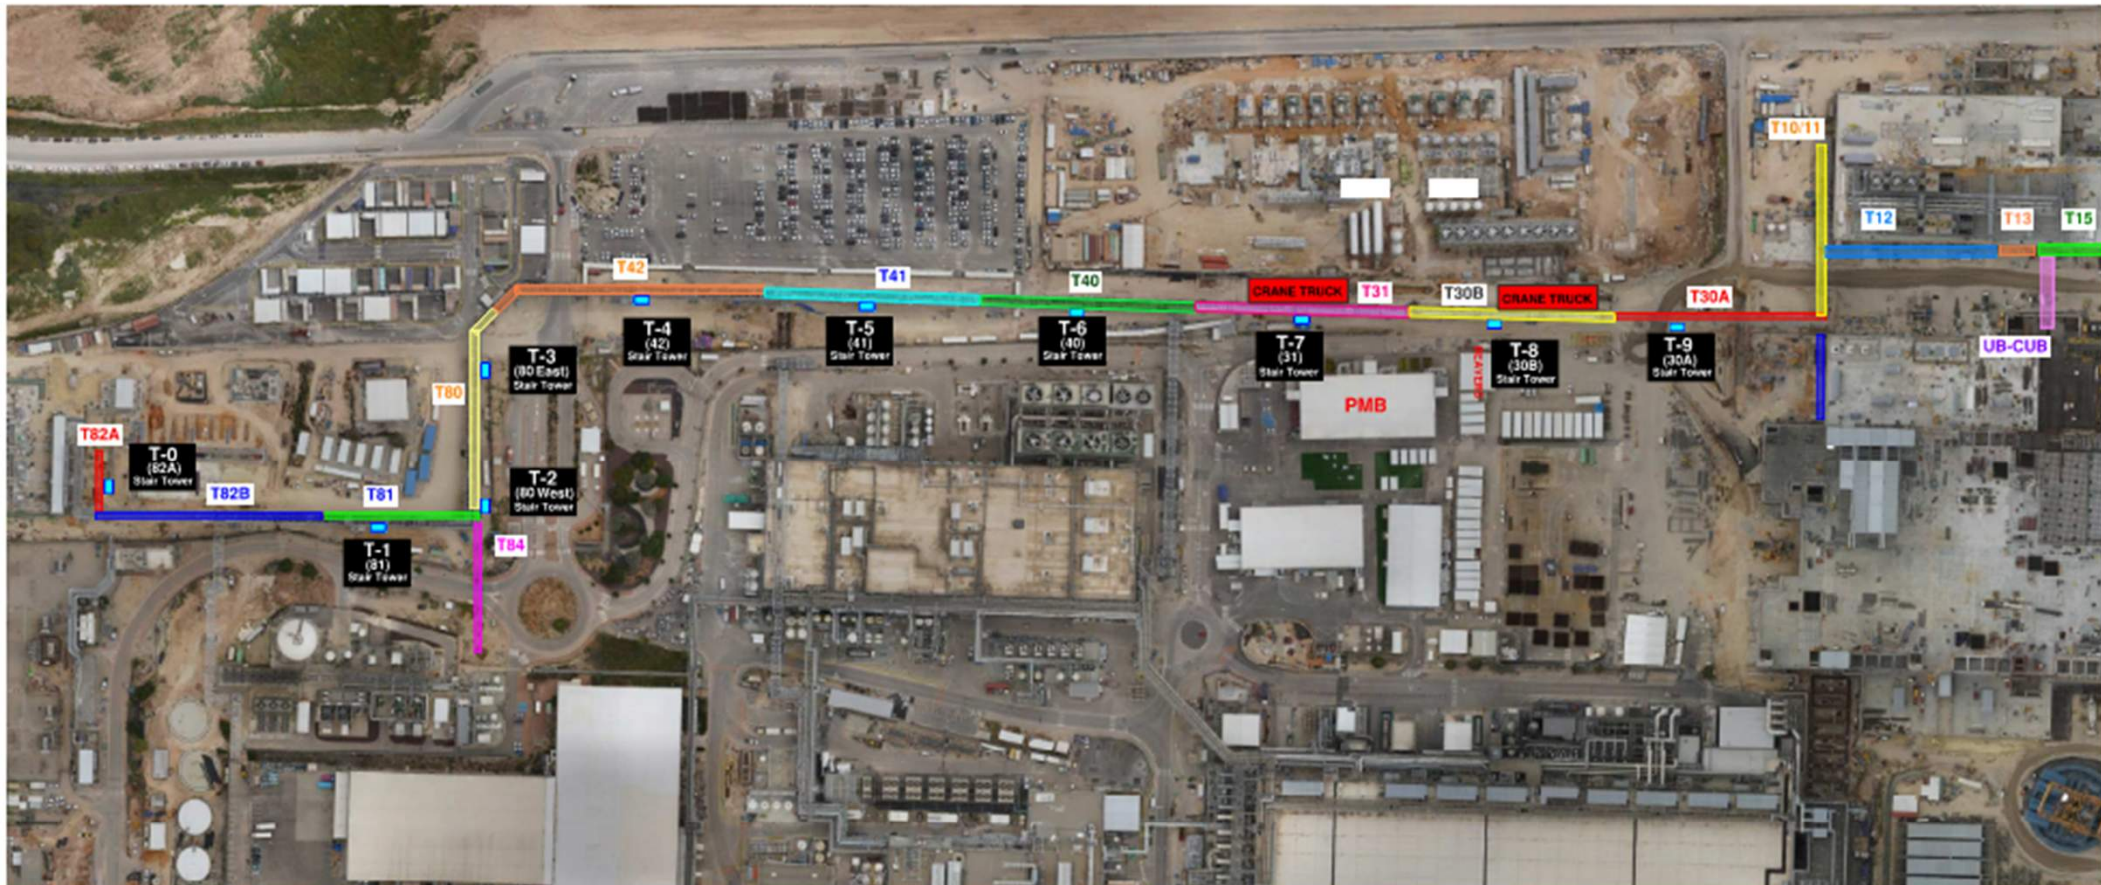



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Entry





Daily Coordination Meeting

Site Logistics North



Site Logistics

This aerial photograph shows a large industrial complex with several buildings and parking lots. Various areas are highlighted with colored overlays and labeled with red text boxes and arrows:

- Sarens Dismantle Area NO ENTRY (starting 2-Feb):** A large blue shaded area on the left side of the image.
- LSS Underground:** A yellow cloud-like shape with an arrow pointing to a small orange rectangular area near the top center.
- Blast Wall Excavation & Concrete:** An arrow pointing to a small orange rectangular area below the LSS Underground area.
- Shotcrete:** An arrow pointing to a large orange L-shaped area on the right side of the image.
- Concrete Flatwork:** An arrow pointing to a small orange rectangular area below the Shotcrete area.
- Gas Dock Pile Chipping:** An arrow pointing to a small orange rectangular area in the center of the image.
- Loading Dock Concrete:** An arrow pointing to a small orange rectangular area at the bottom center.
- Loading Dock Storm Repair:** A green cloud-like shape with an arrow pointing to a small orange rectangular area at the bottom left.

The facility is surrounded by a purple scalloped border on the right and bottom edges. The image is a high-resolution aerial view showing details of the buildings, roofs, and surrounding infrastructure.

Ladders Last

- Ladders should be our last choice of accessing our work at heights. And should only be used for small tasks that do not require pushing or pulling.
- Ladders must be inspected before use.
- Ensure the ladder is set up correctly, with a 4:1 ratio.
 - Extension ladders must be secured at the top and bottom and A-frame ladders must be completely open.
- Utilize 3 points of contact when climbing a ladder.
- Never carry anything in your hands while climbing a ladder.
- Use the belt buckle rule and ensure you are not leaning over the side of the ladder, reposition it instead.
- Always face the ladder.

HCC/EHS Weekend Work- 31.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

John Scott - 052-3291705

Ziv Srur - 053-2712258

Tsurriel Evgi - 052-3718851

Ken Power - 052-2531428

Kevin O'Hanlon - 052-3239625

CSA CM

Brandon Britton - 052-6042828

Nitzan Mulay - 052-3257365

Andy Jollands - 052-9659290

Dan Stanley - 052-6215642

Tareq Nairoukh - 052-6636782

Kevin O'Hanlon - 052-3239625

MEP

Cx

Cranes

Maksym Panov - 055-9181086

Safety

- Safety Foreman- Hay Halfon- 052-8049342 Hay-Halfon@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 31.01.2025

FAB

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Clean Room

- **Talad** – 20 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Mati 0504887477, Super Igor 0544509386)
- **Afcon** – 5 guys CR – cable trays, INT Level cable pulling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- **Chemo** – 35 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- **Sela** – 10 1E, 3W CRC (Supervisor Yoav 0548076339, EHS Sergey 0526650046)
- Protocol 2 guys (Roni 0542496363, Lidia 05072148)
- **Talent solution** 11 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Yosi 0526557130)
- **W&W** 10 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- **Megason** 6 guys 4DA 4W-4E FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Subfab

- **Pach Taas**
 - Perimeter Racks AQe, BJe
 - Safety: Offek Ben Harush - 0507838486
 - Team leader: Itamar - 0509301917
- **Afcon E**
 - All over the SF
 - Team leader: Raz - 0546838626
- **Combe UPW**
 - TTNE/W
 - Team leader: Dani - 0526527883

Subcontractor Weekend Work- 31.01.2025

PSSS

- **Pach Taas** – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **SK Engineering** – GL4 UL Piping, 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe Waste** – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe UPW** – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- **Lesico** – UN2 Pressure Test
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109

WJG

WW – 2J/3J Lift 3 Grating Install (with 500T & 220T)
Foreman: Chris 052 588 3215

Afcon – Lift 2 Cable Tray and Utility Level Lighting
Foreman: Montu 055 911 6973
Safety: Pradeep 055 274 2935

Chemo 1J/4J/5J Lift 2 Piping / Insulation
Foreman: Maor 050 988 9071
Safety: Erez 054 971 6840

Pach Taas: All over (HRA)
Foreman: Ilya 050 577 1907
Safety: Eran 054 770 6233

Lesico: Natural Gas Piping Utility Level
Foreman: Anoop 058 691 1748

Subcontractor Weekend Work- 31.01.2025

CUB

D&P:

Constantin - 0545501602

David - 0548894447

Chemo:

Dudu - 0509808846

Alberto - 0508573970

SK:

Reynato - 0548991623

Marzuk - 0548830263

Sami Najami:

Hussein - 0526917461

Average - 0509059920

Pach Taas:

Itamar - 0509301917

Ofek - 0507838486

Megason:

Israel - 0526869393

Guy - 0544915407

HSI:

Sergey - 0552728807

Haim - 0548038554

Trestle

SNJ:

PIPES –T40 - UB CUB - 20 workers (4 teams)

STEEL –Galvanized paint + T30 A+B -T41 8 workers (2 teams)

Steel adjustment - 12 workers (3 teams).

FORMAN-

Mucles- 0526017477

SAFETY TRESTLE-

Aviram shrike - 0509059920

Siding

Site

- Derech Afar – Shotcrete wall
 - Supervision = Raed: 054-244203
 - EHS = Alex: 054-5403849

Daily Coordination Meeting



14:00 Sign In
