

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:

- Area Assessments

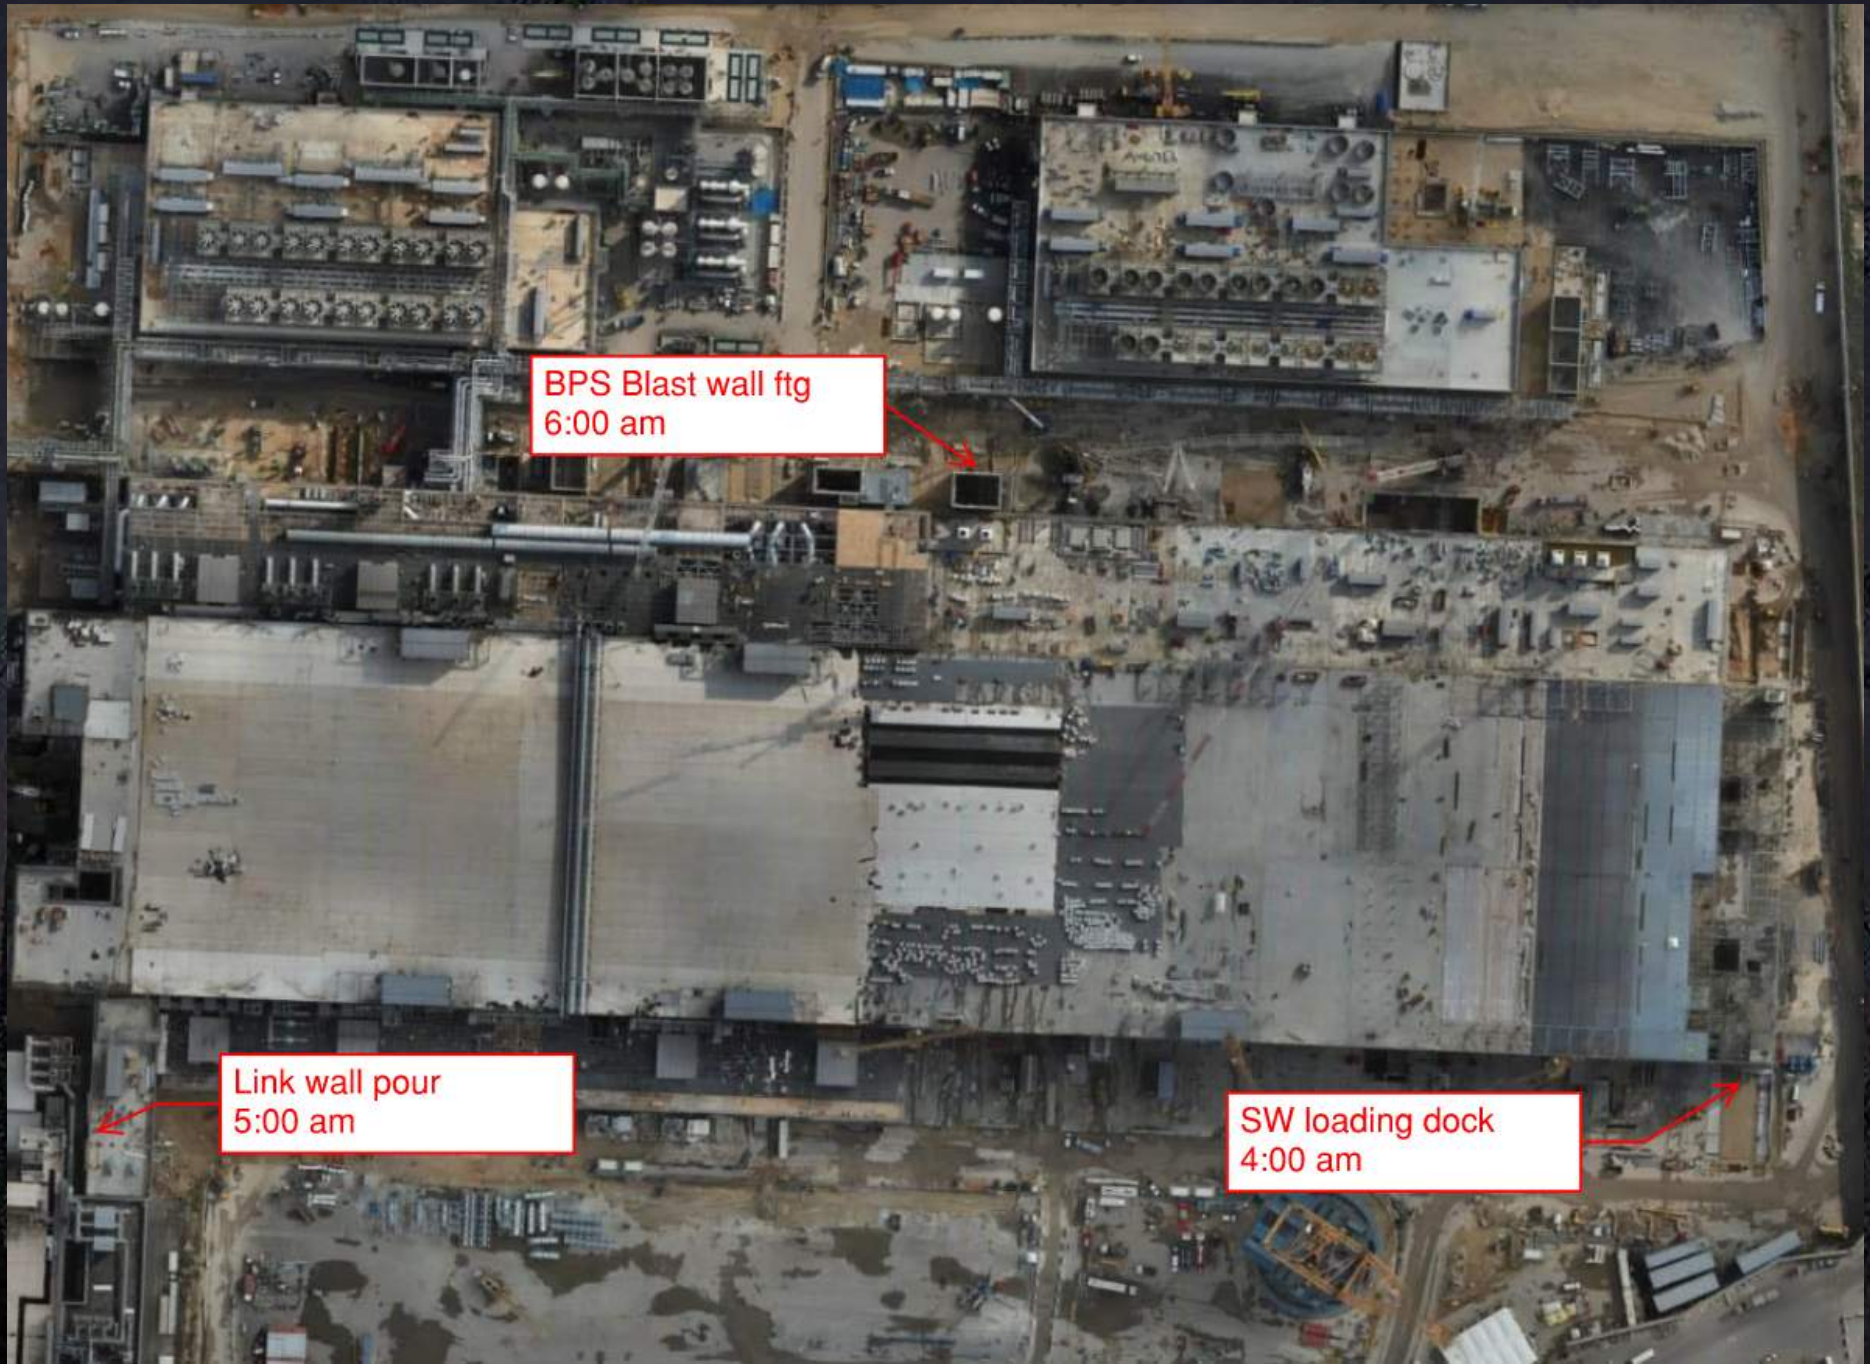


BPS Blast wall ftg
6:00 am


Link wall pour
5:00 am

SW loading dock
4:00 am

UTILITY LEVEL MOD1

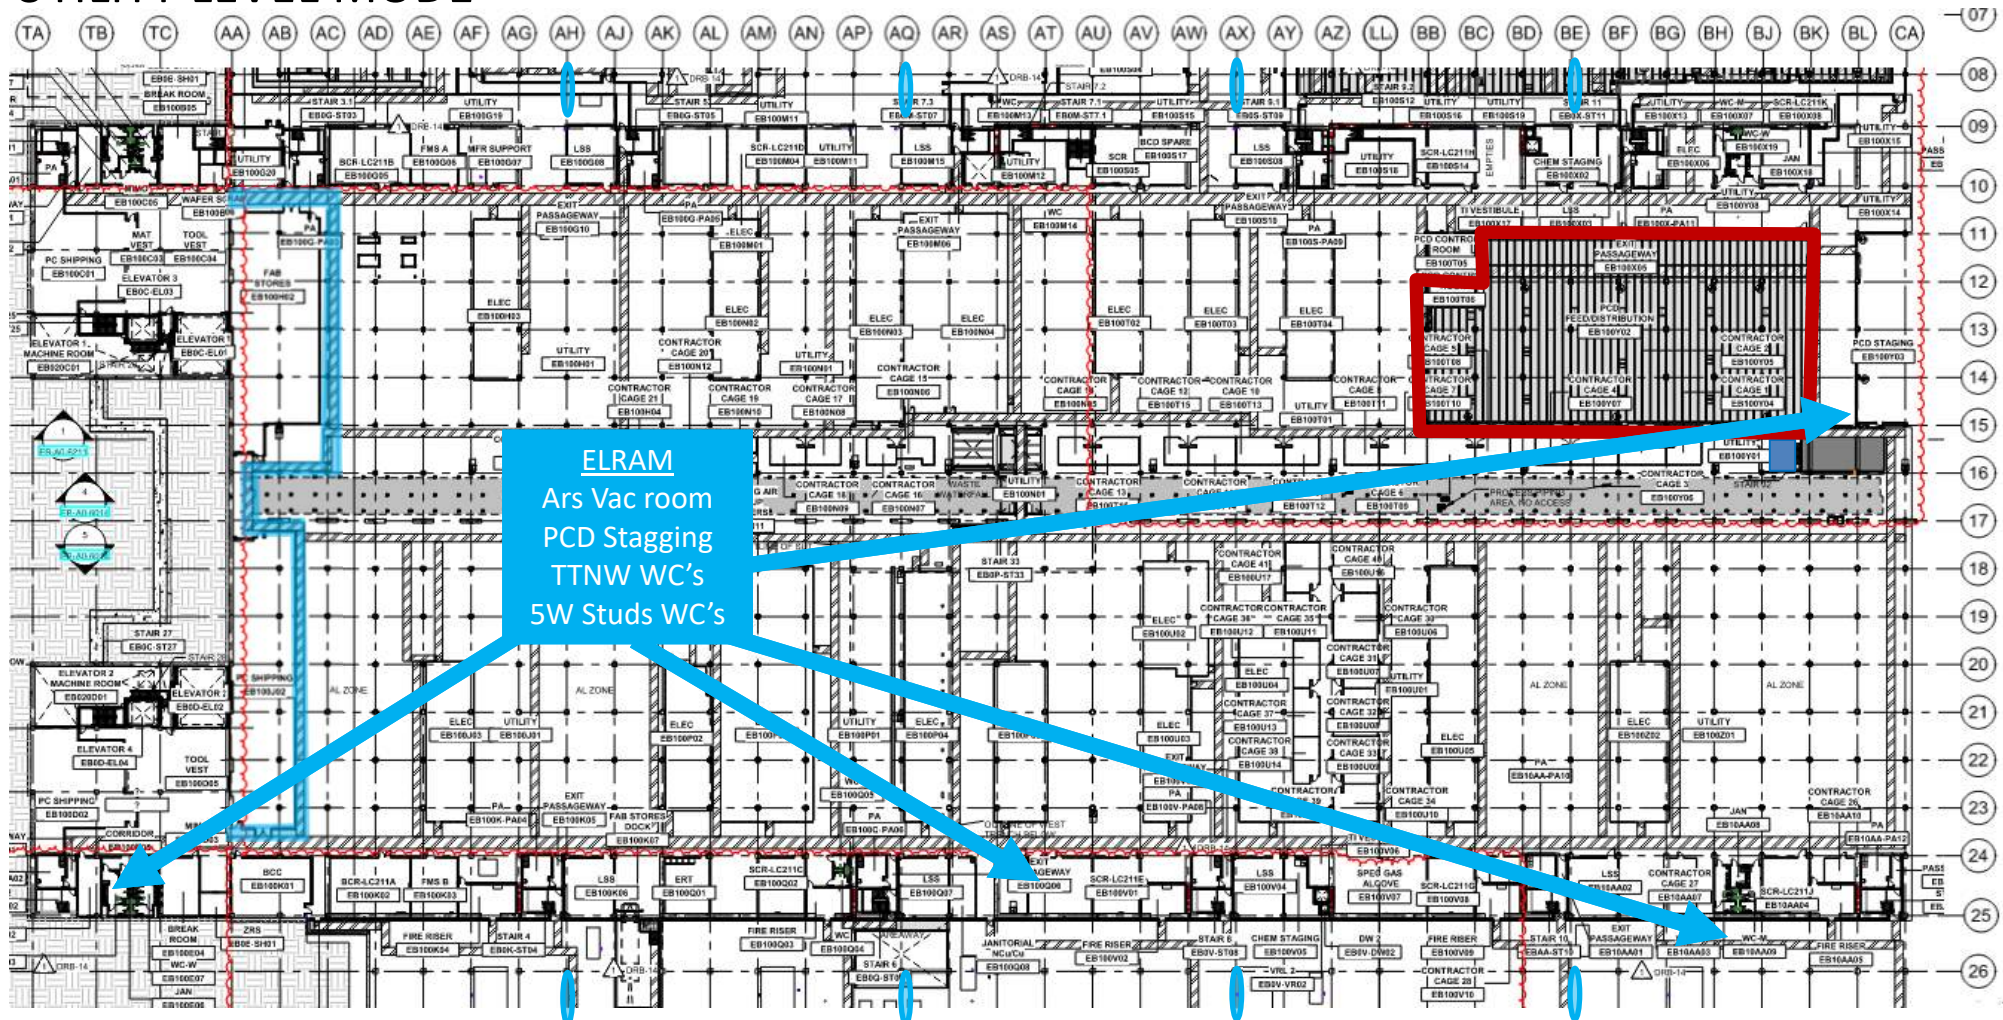

SUT 38.1 LEVEL

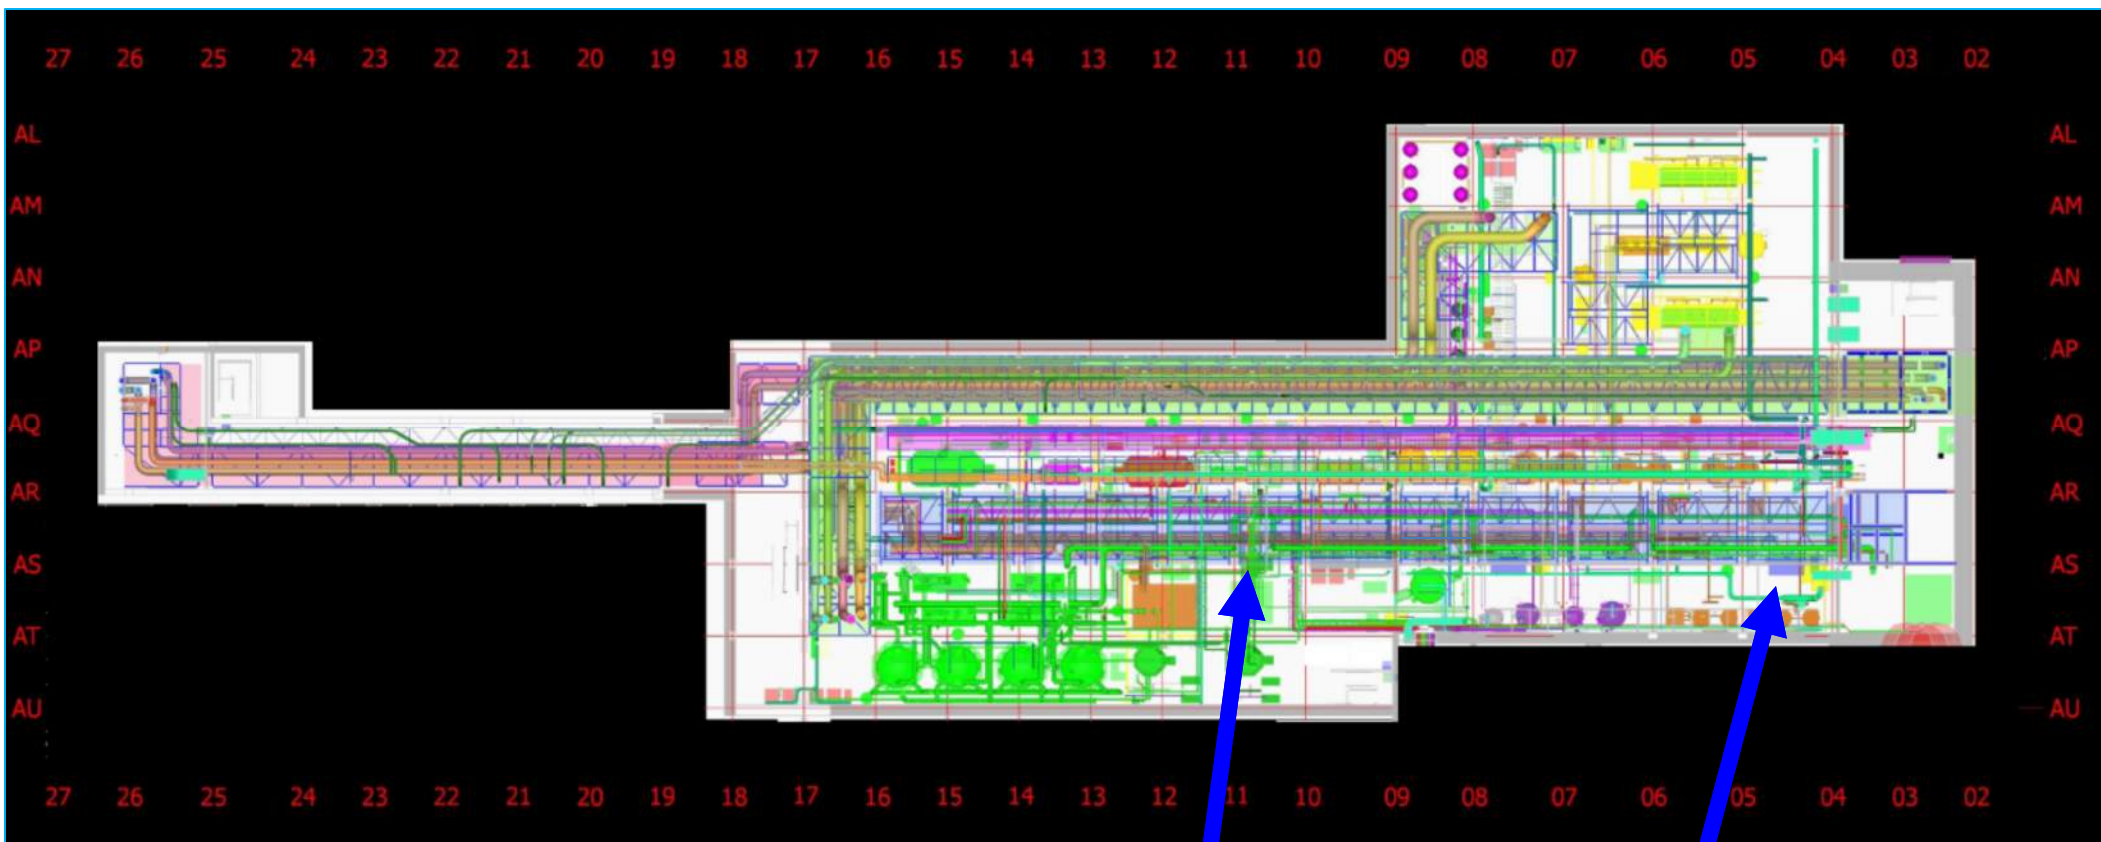


Biocide
Totes Set
18/2

SOG
Ready for
Totes set.

SUT 38.2 LEVEL


Rack 4b
Inter
Connection's

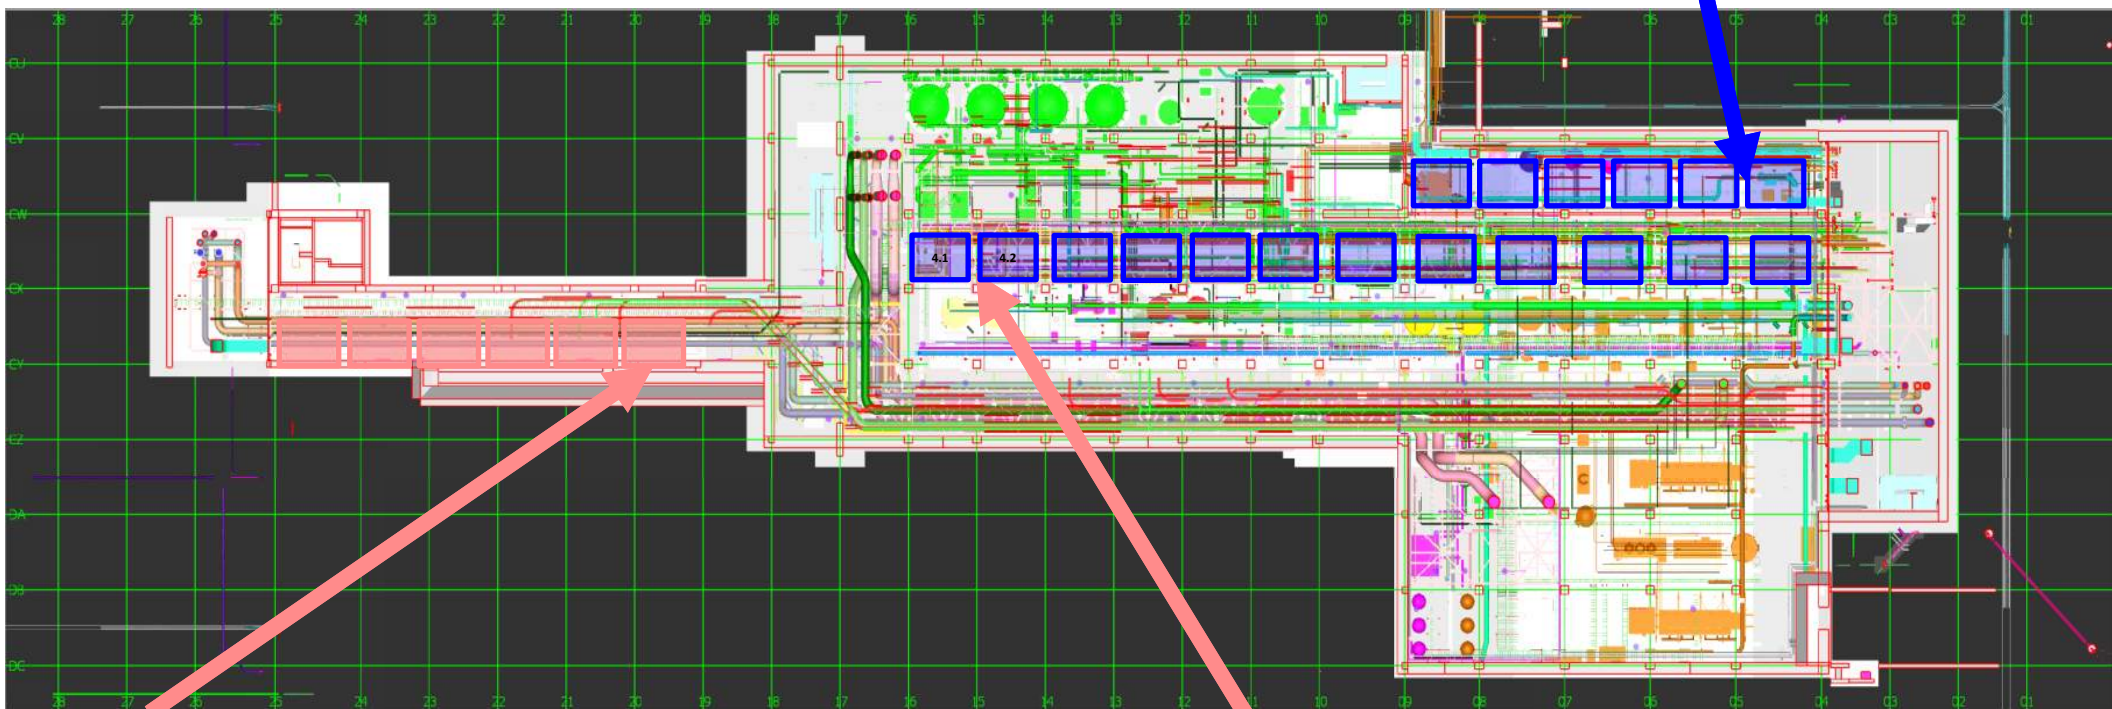


16/02/2025	Module 1
20/02/2025	Module 2
23/02/2025	Module 3
26/02/2025	Module 4
02/03/2025	Module 5
04/03/2025	Module 6

Temp stairs
relocation


SUBFAB BUILDOUT MOD 1

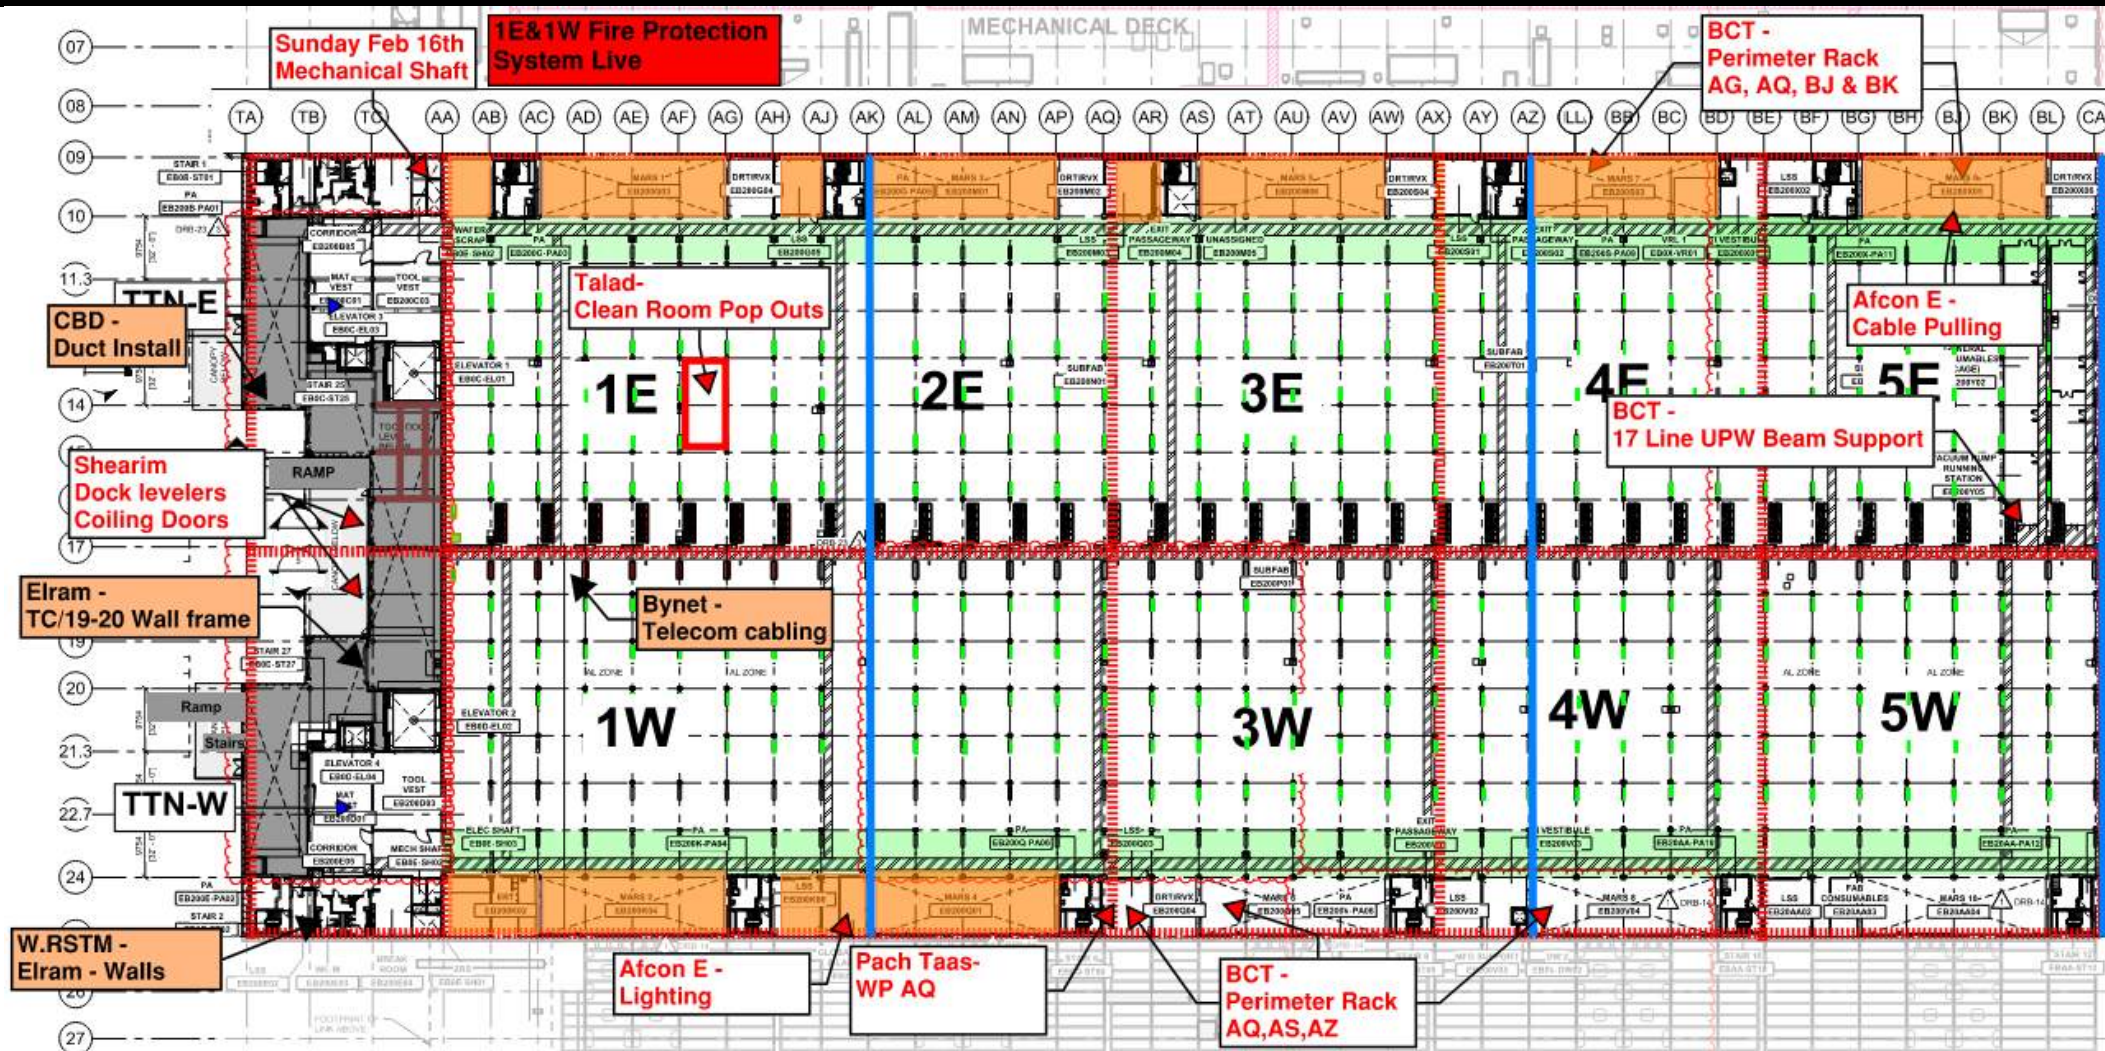


SUBFAB CRC TOPCOAT

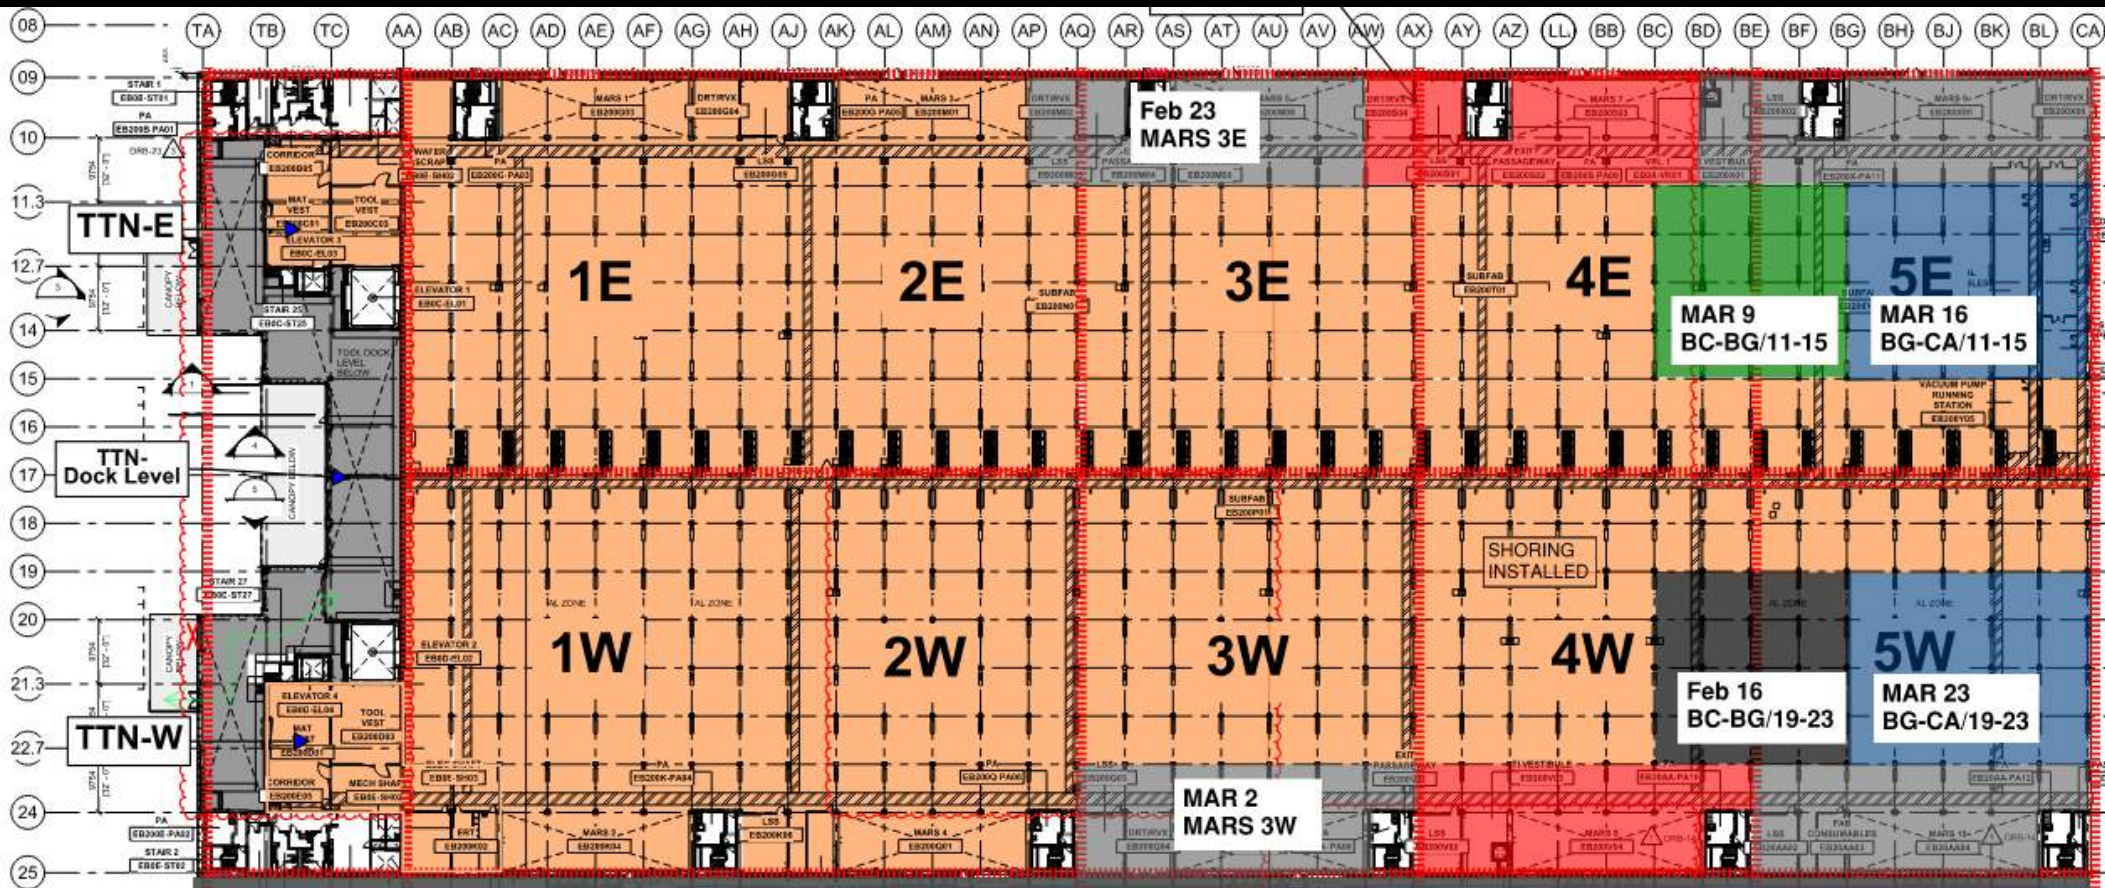



BCT Pressure Tests Tomorrow

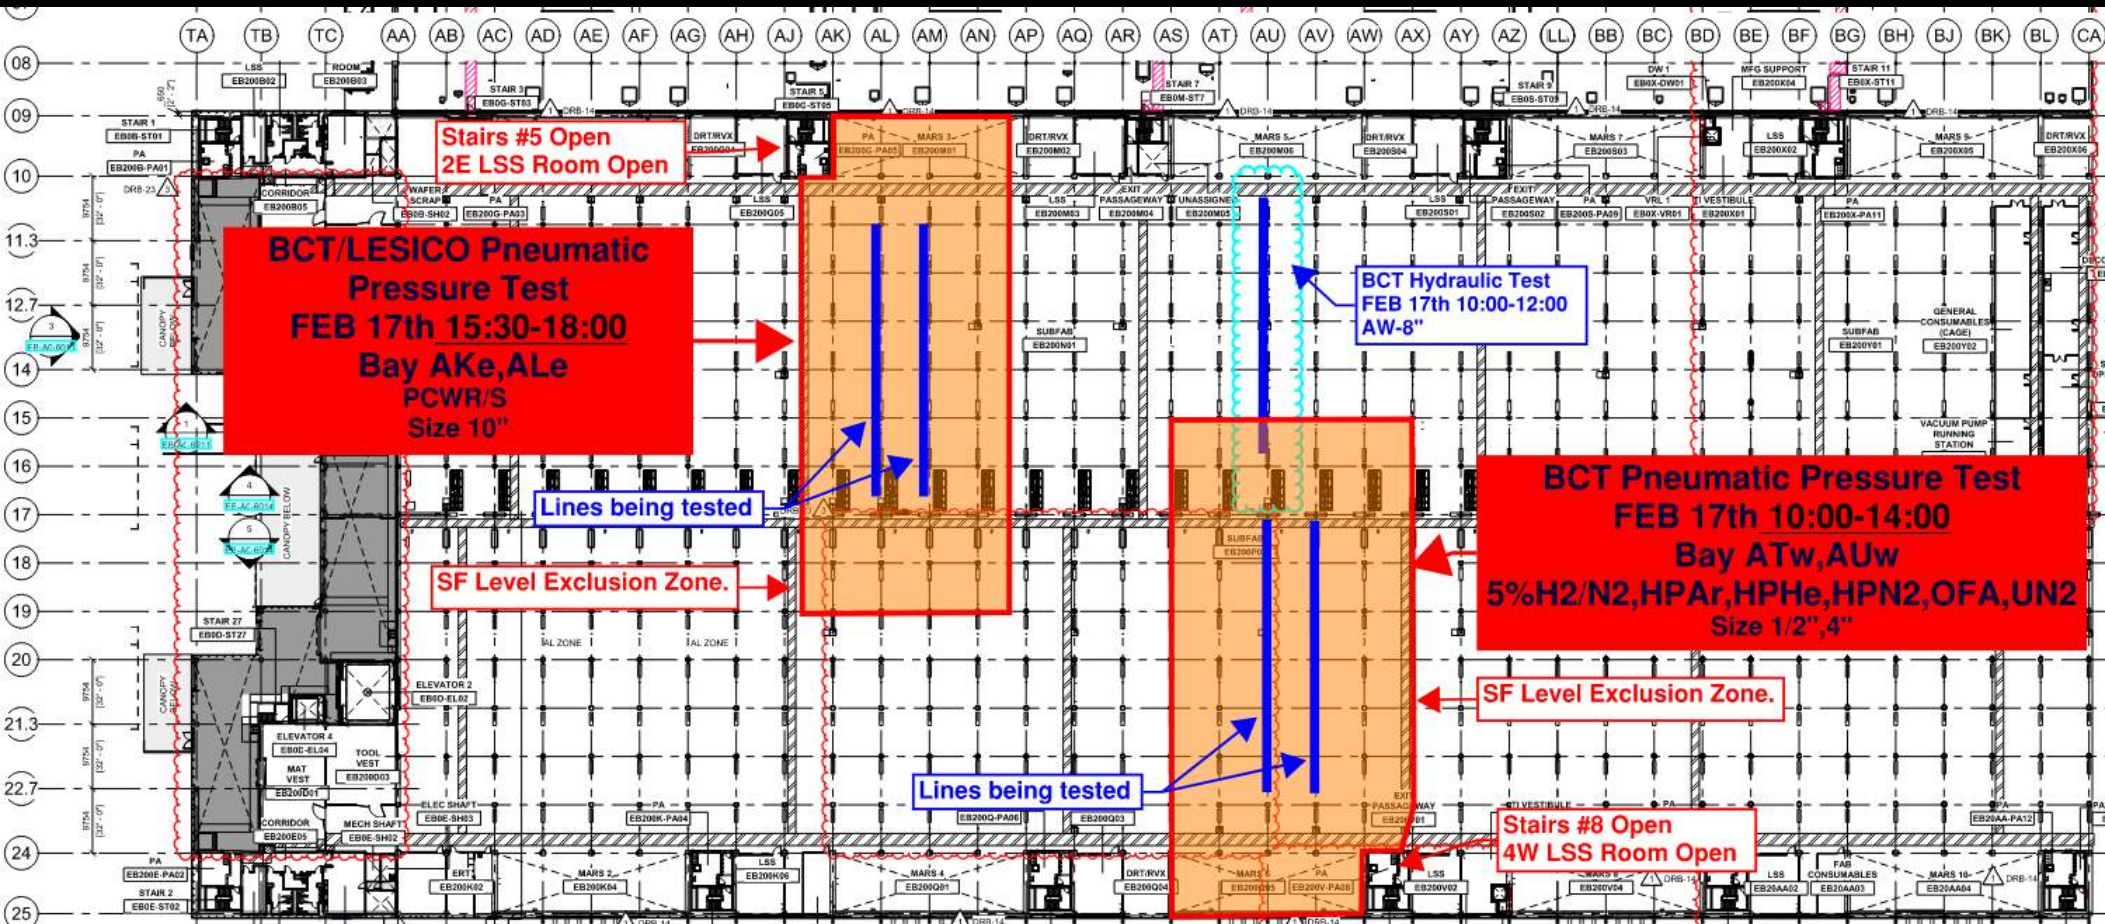



SUBFAB BUILDOUT MOD 2

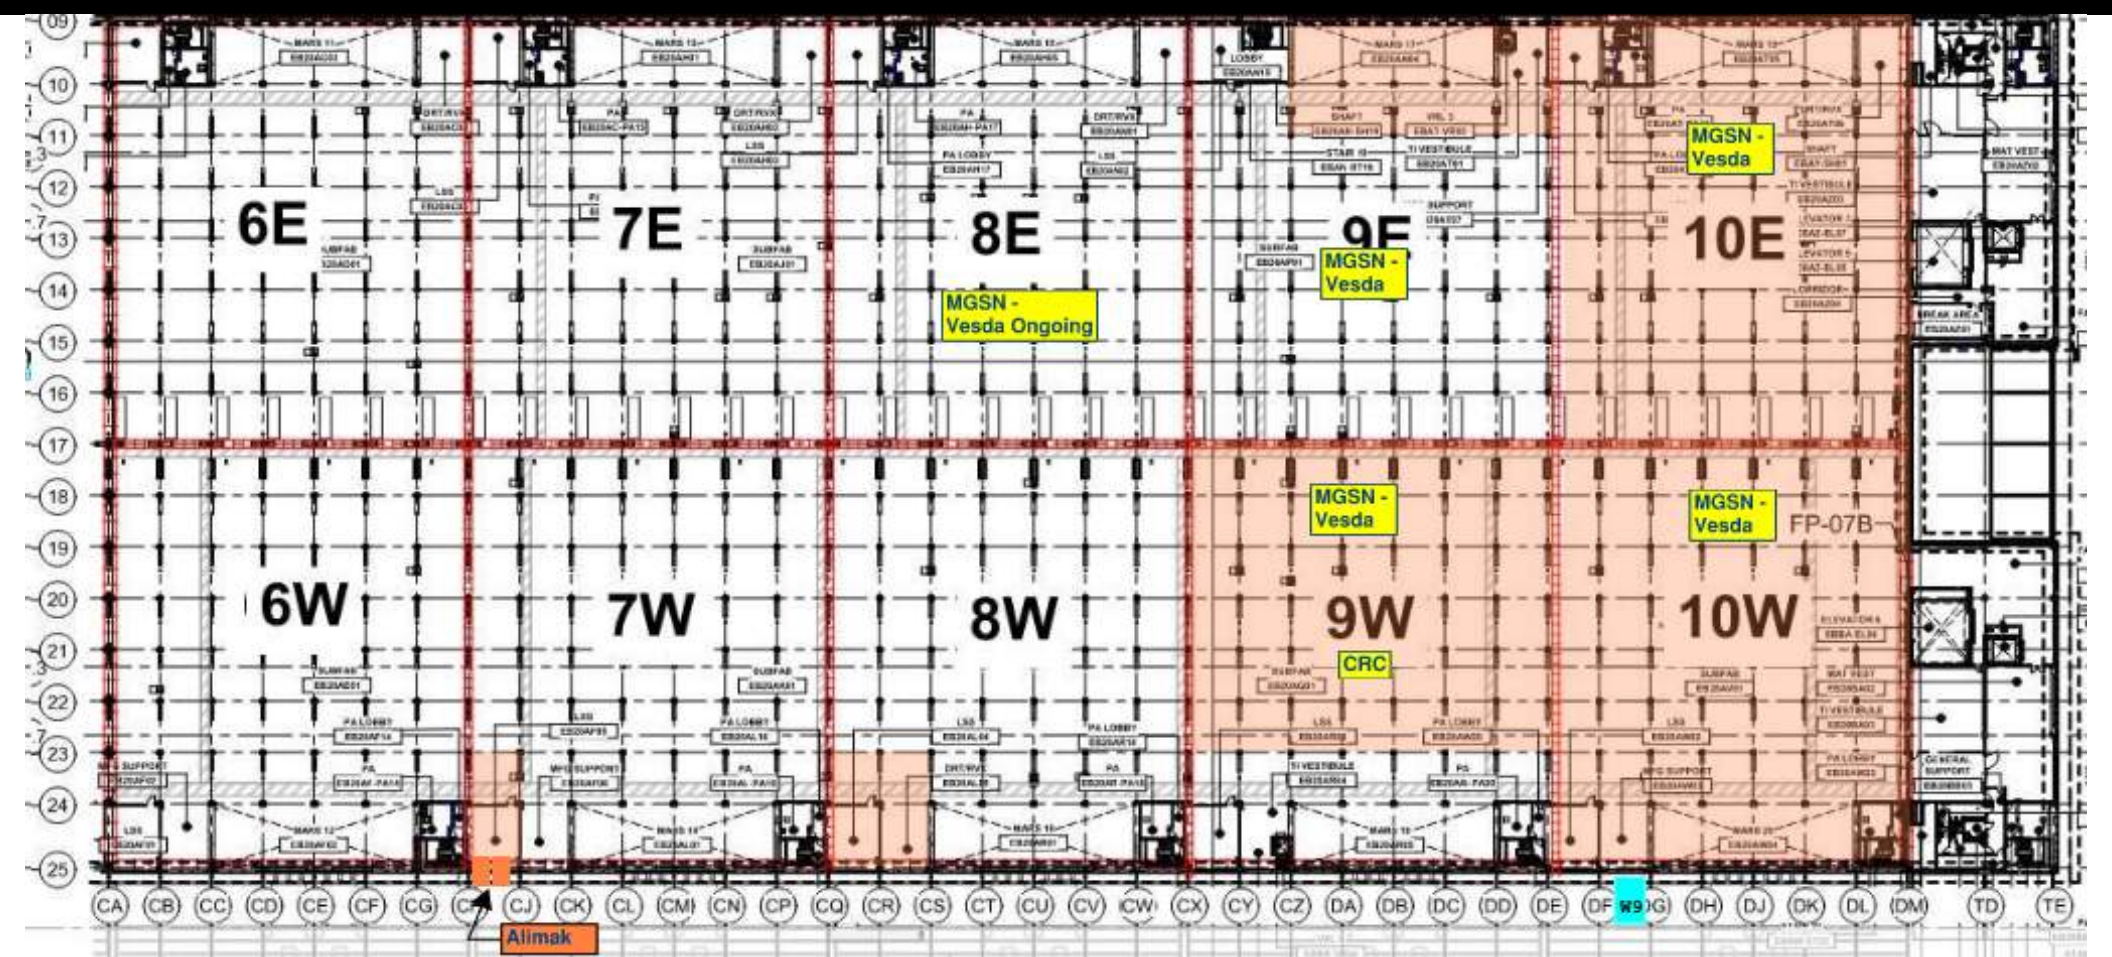

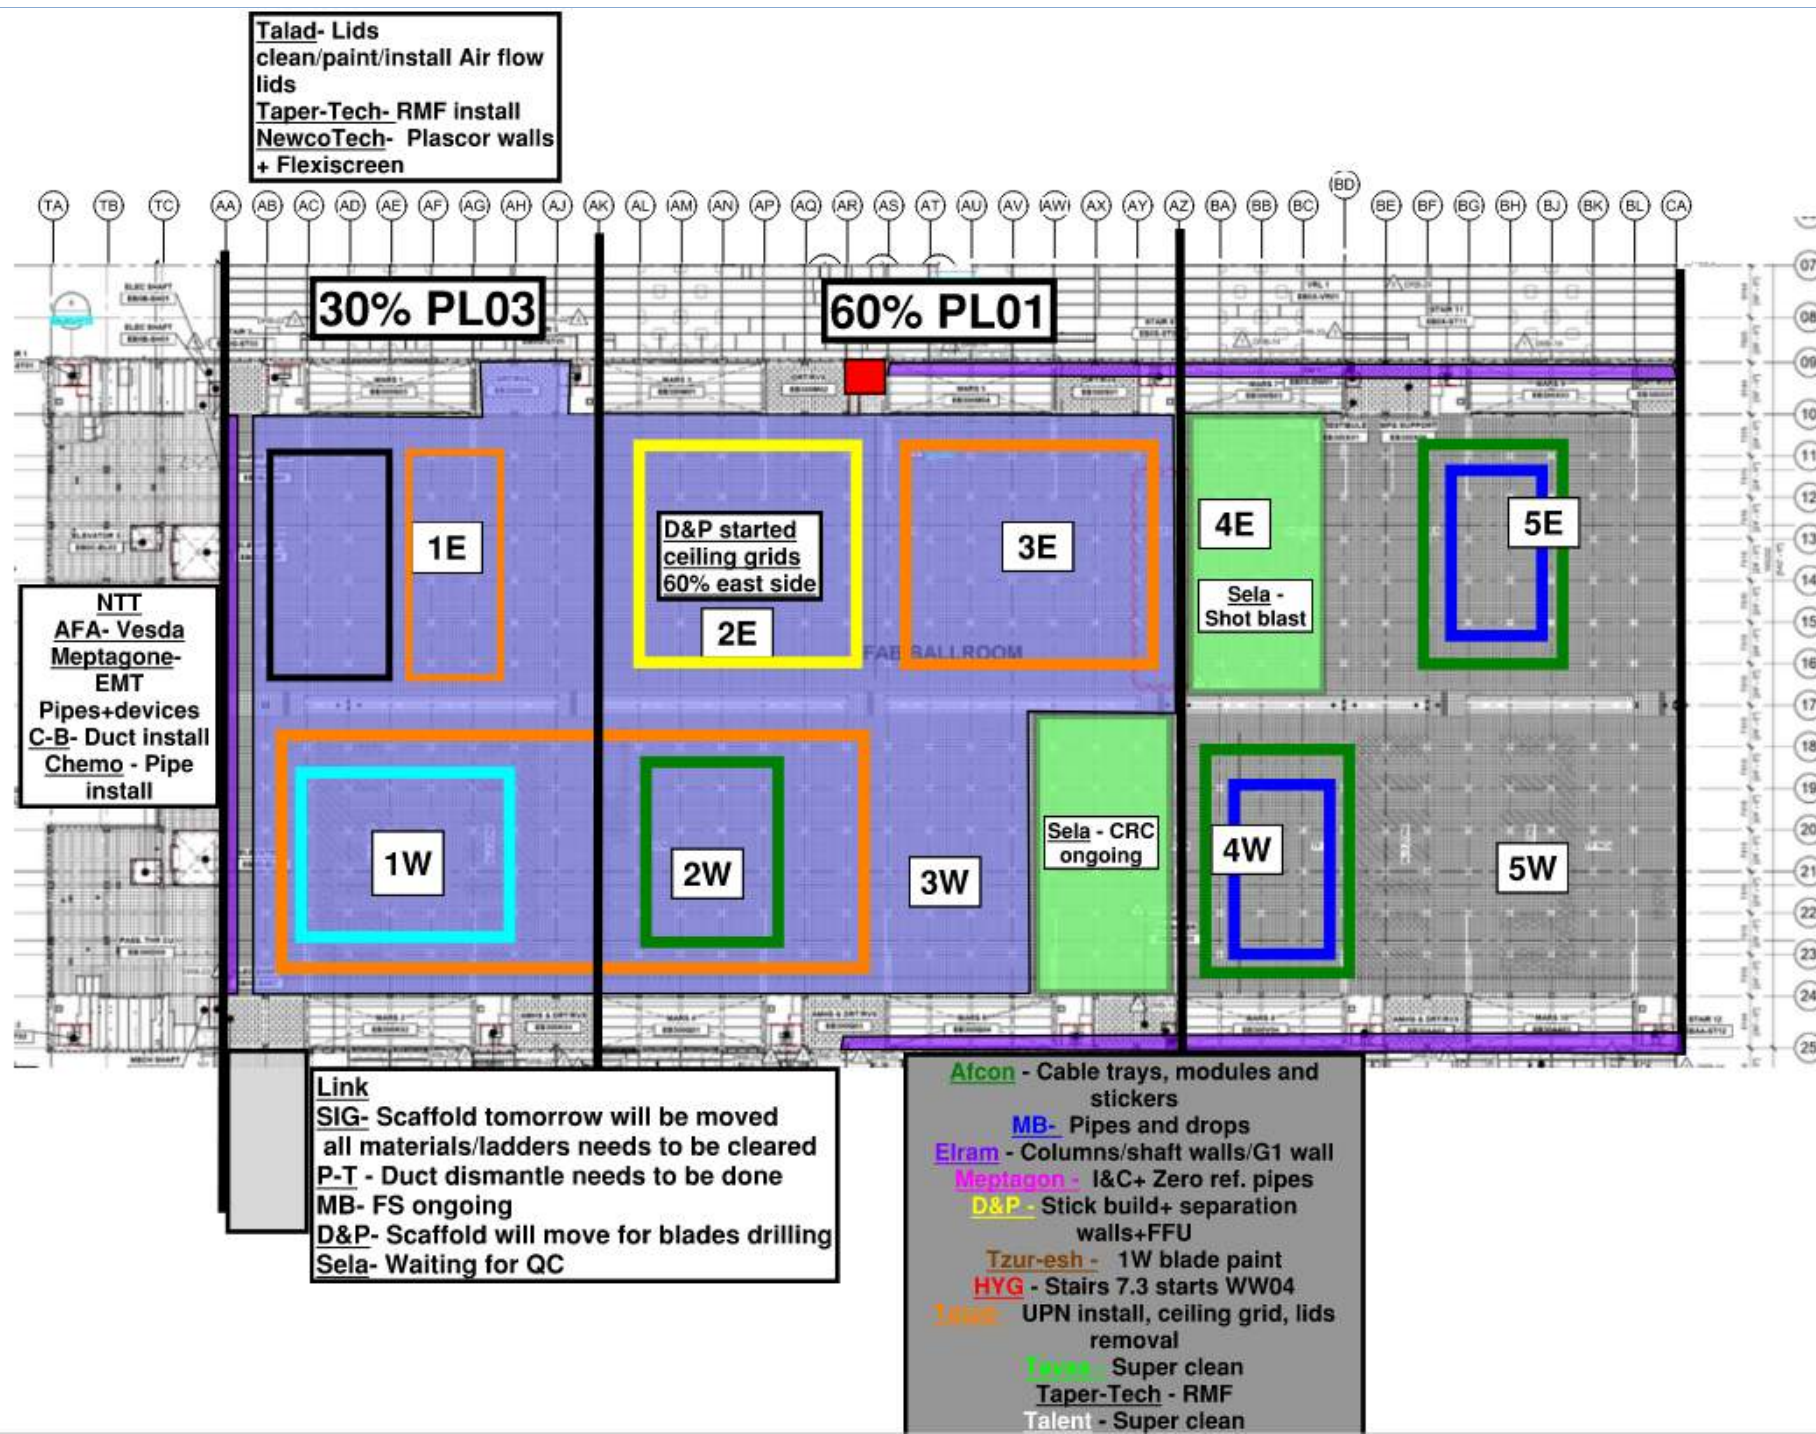


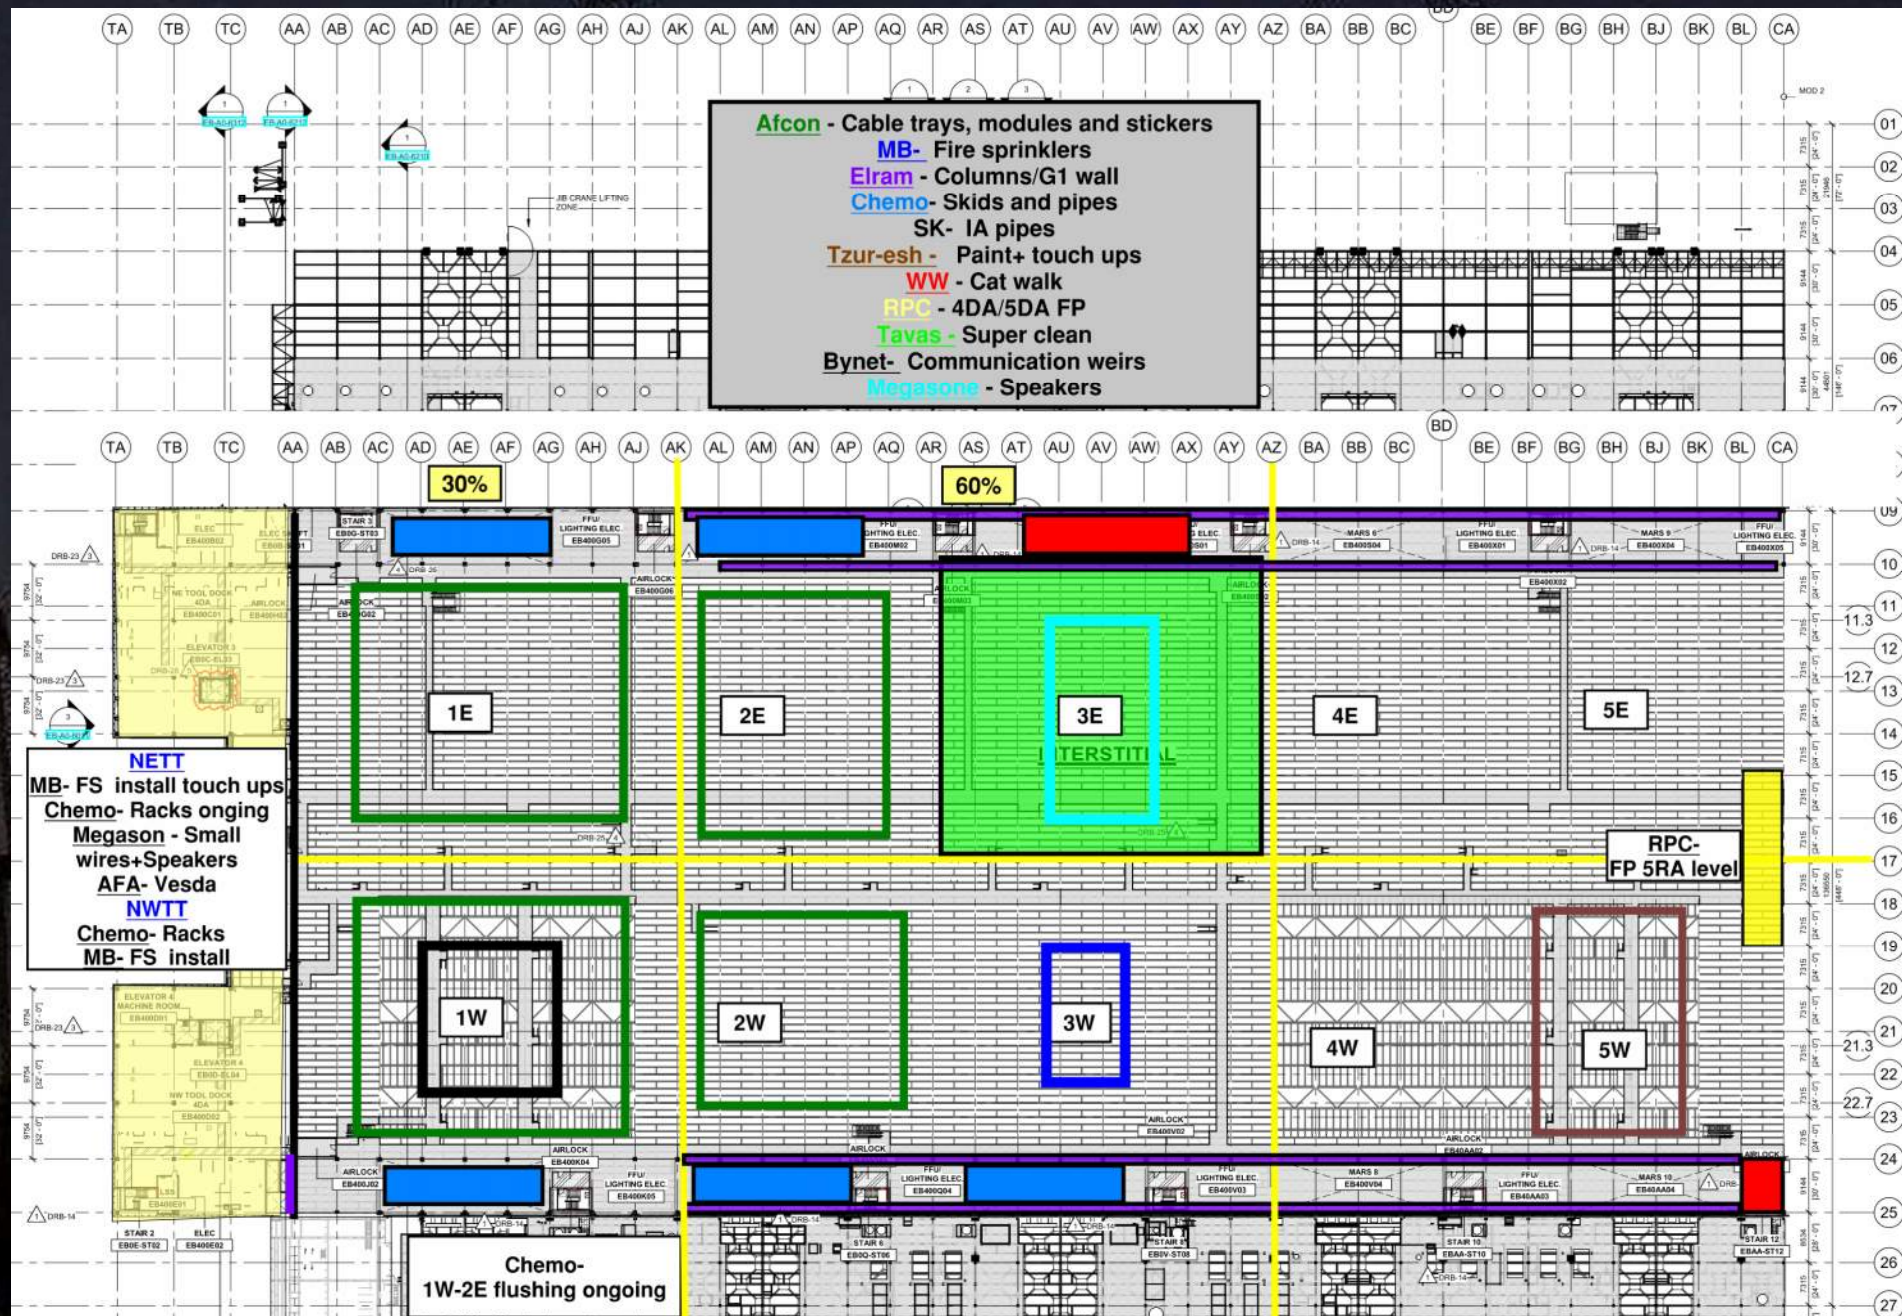

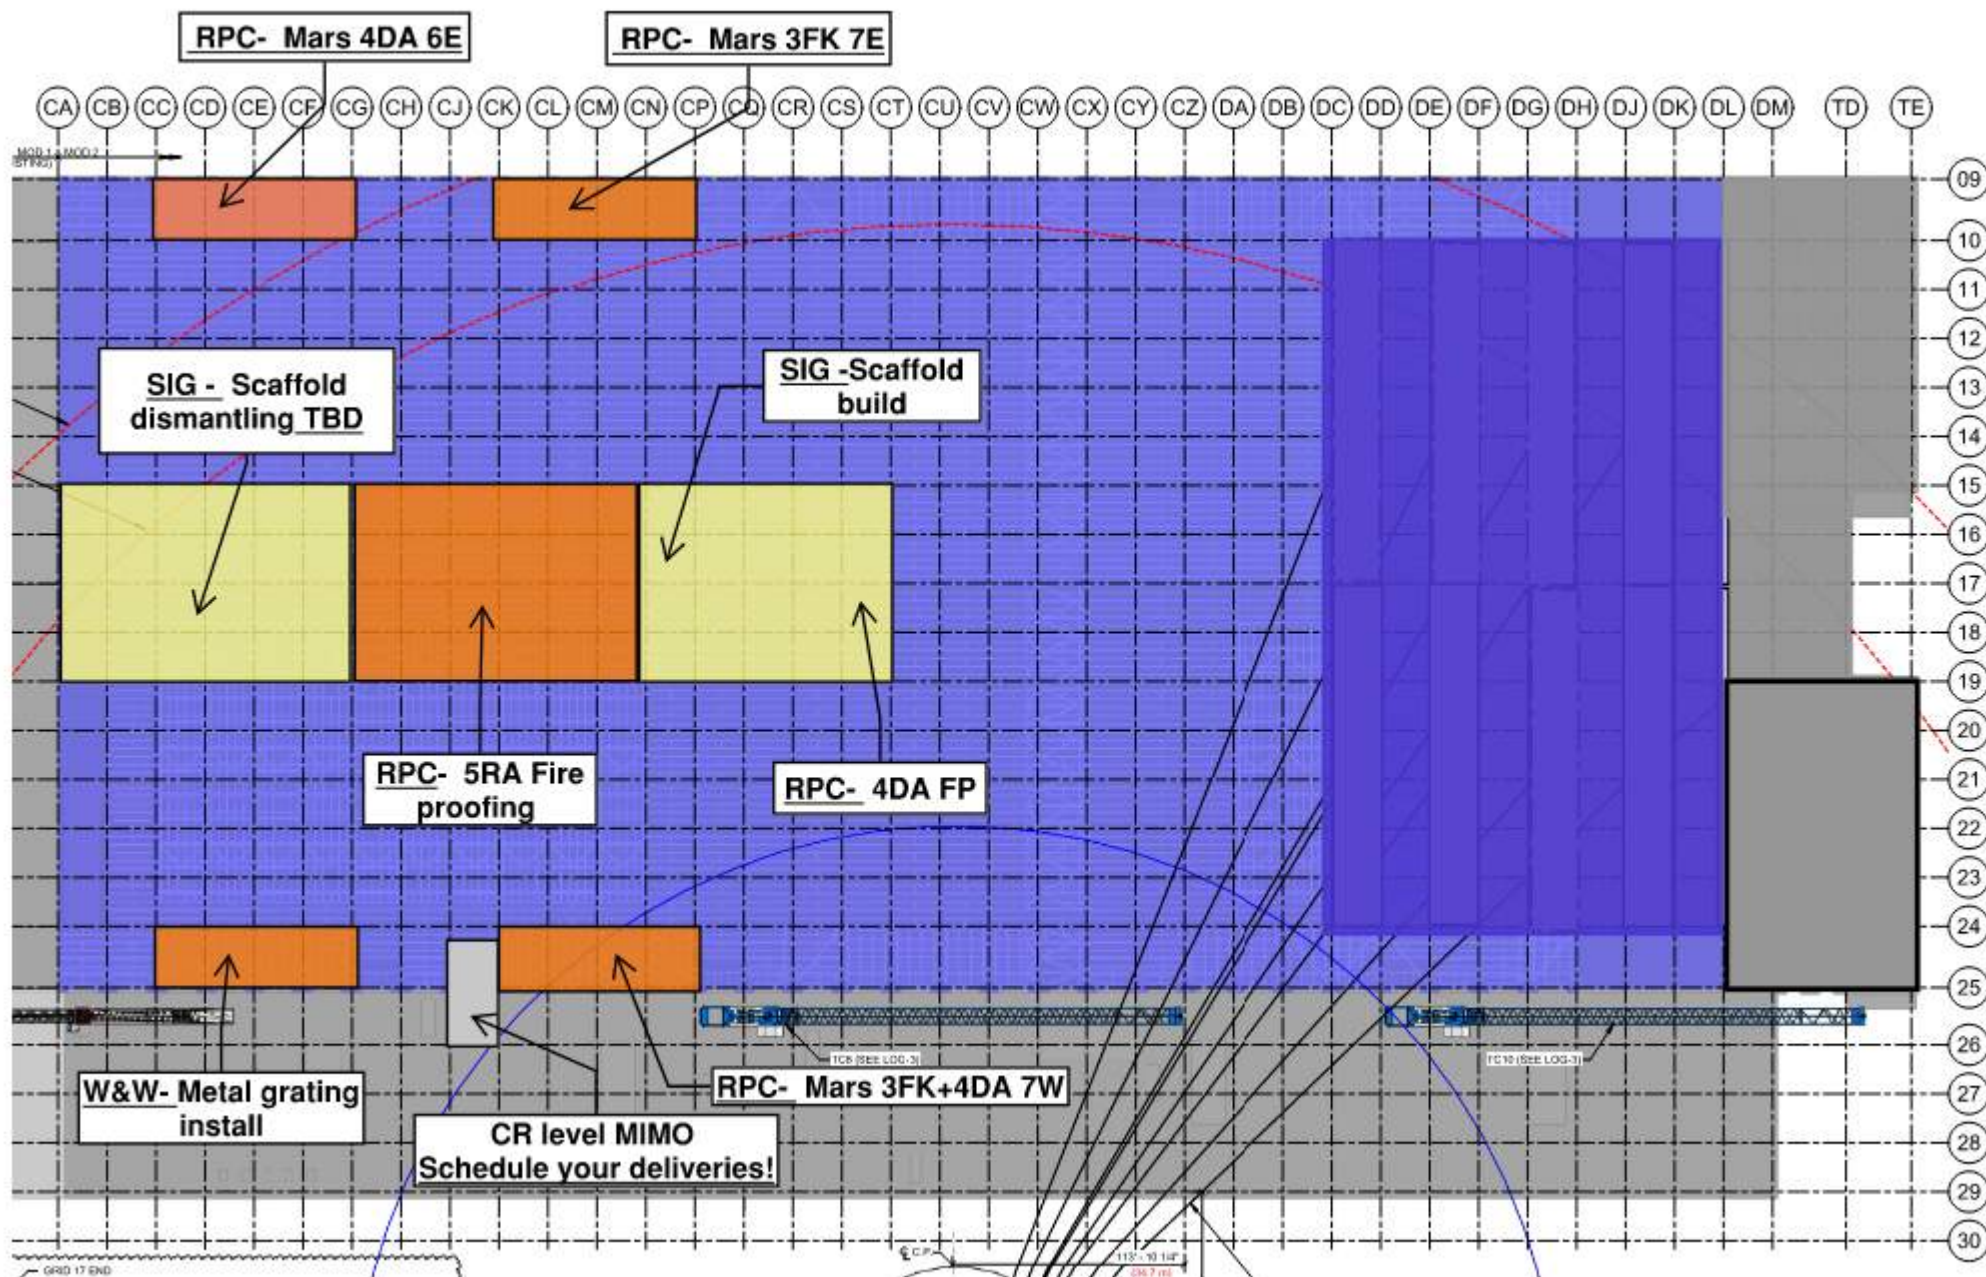


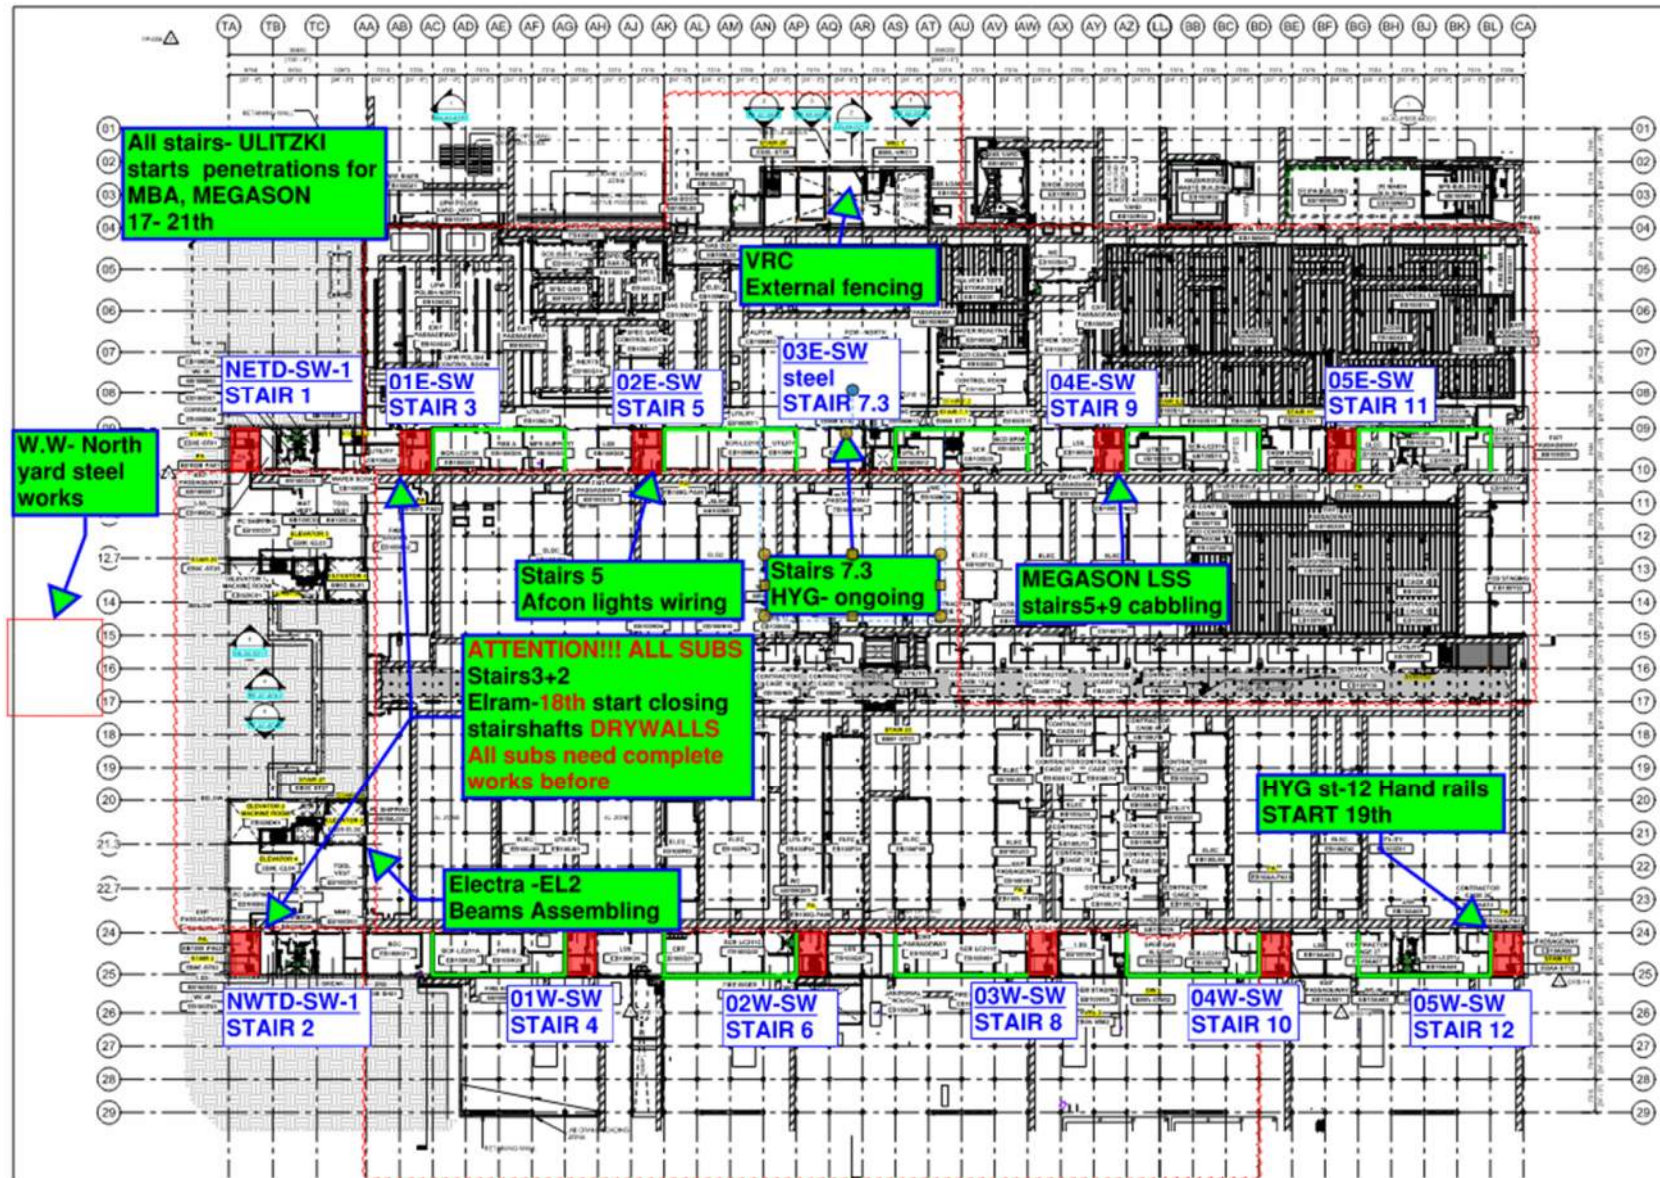


Siding Penetration Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

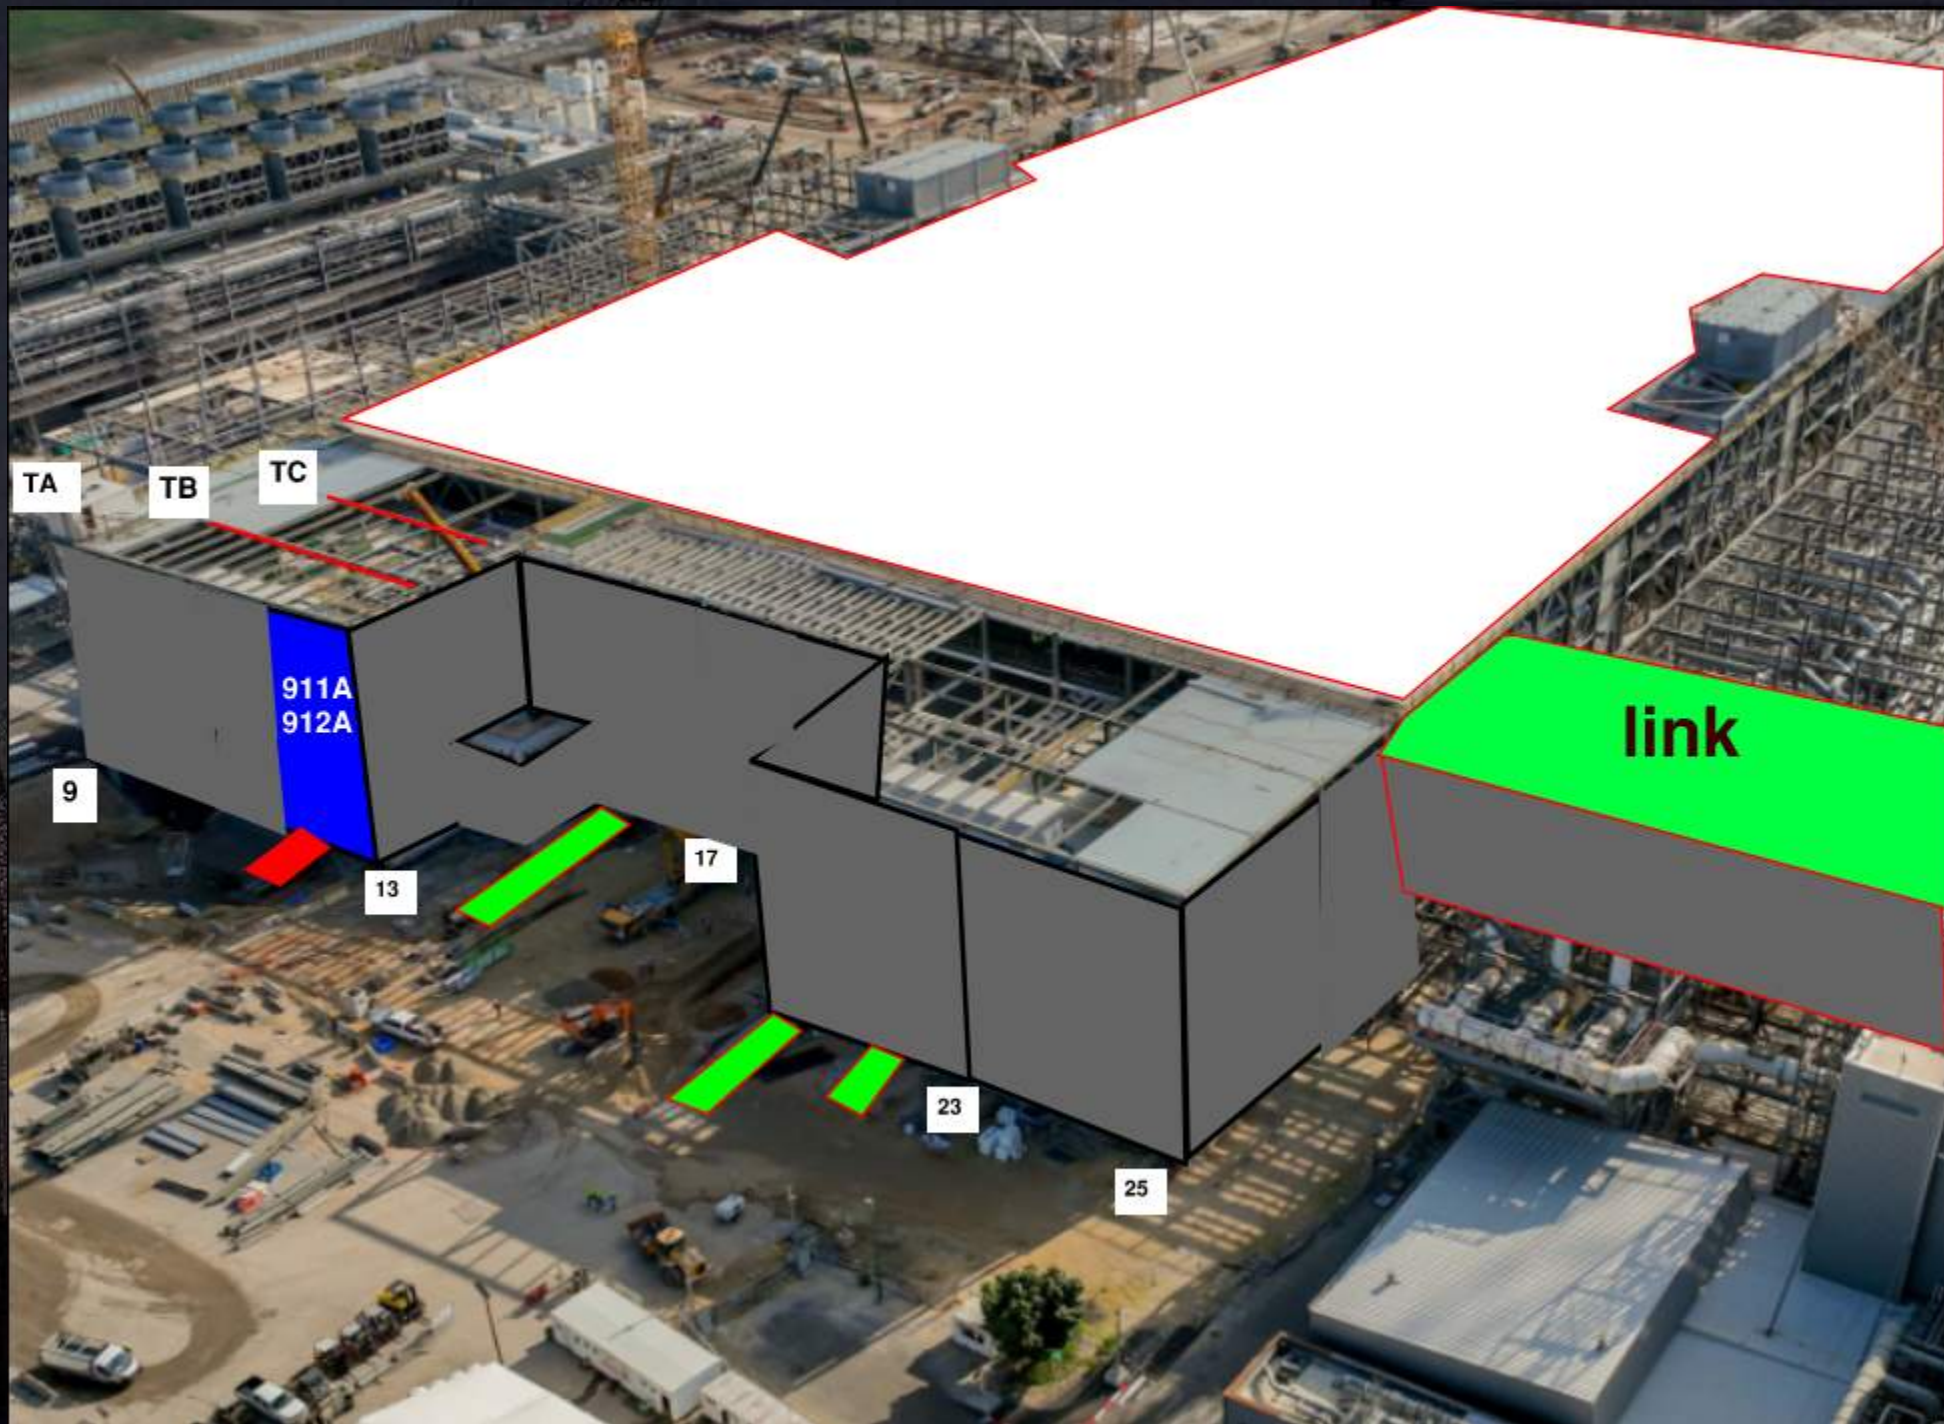


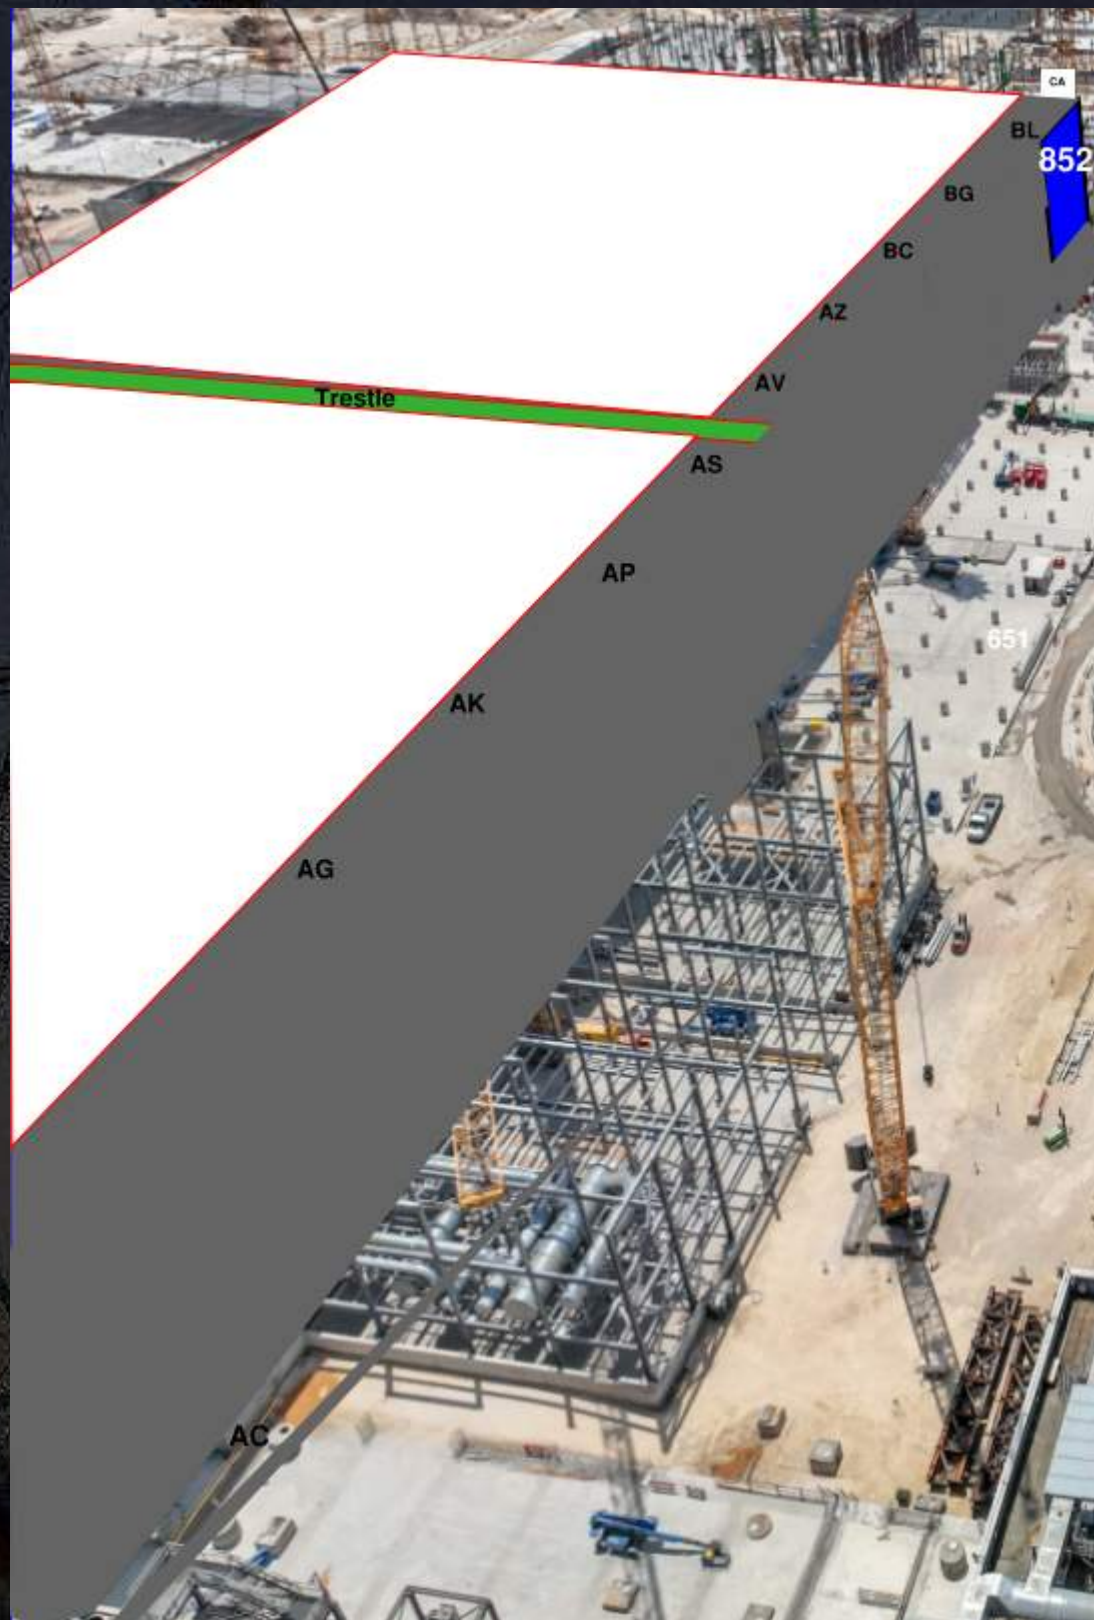



MOBILE EAST SIDE CITY SIDING



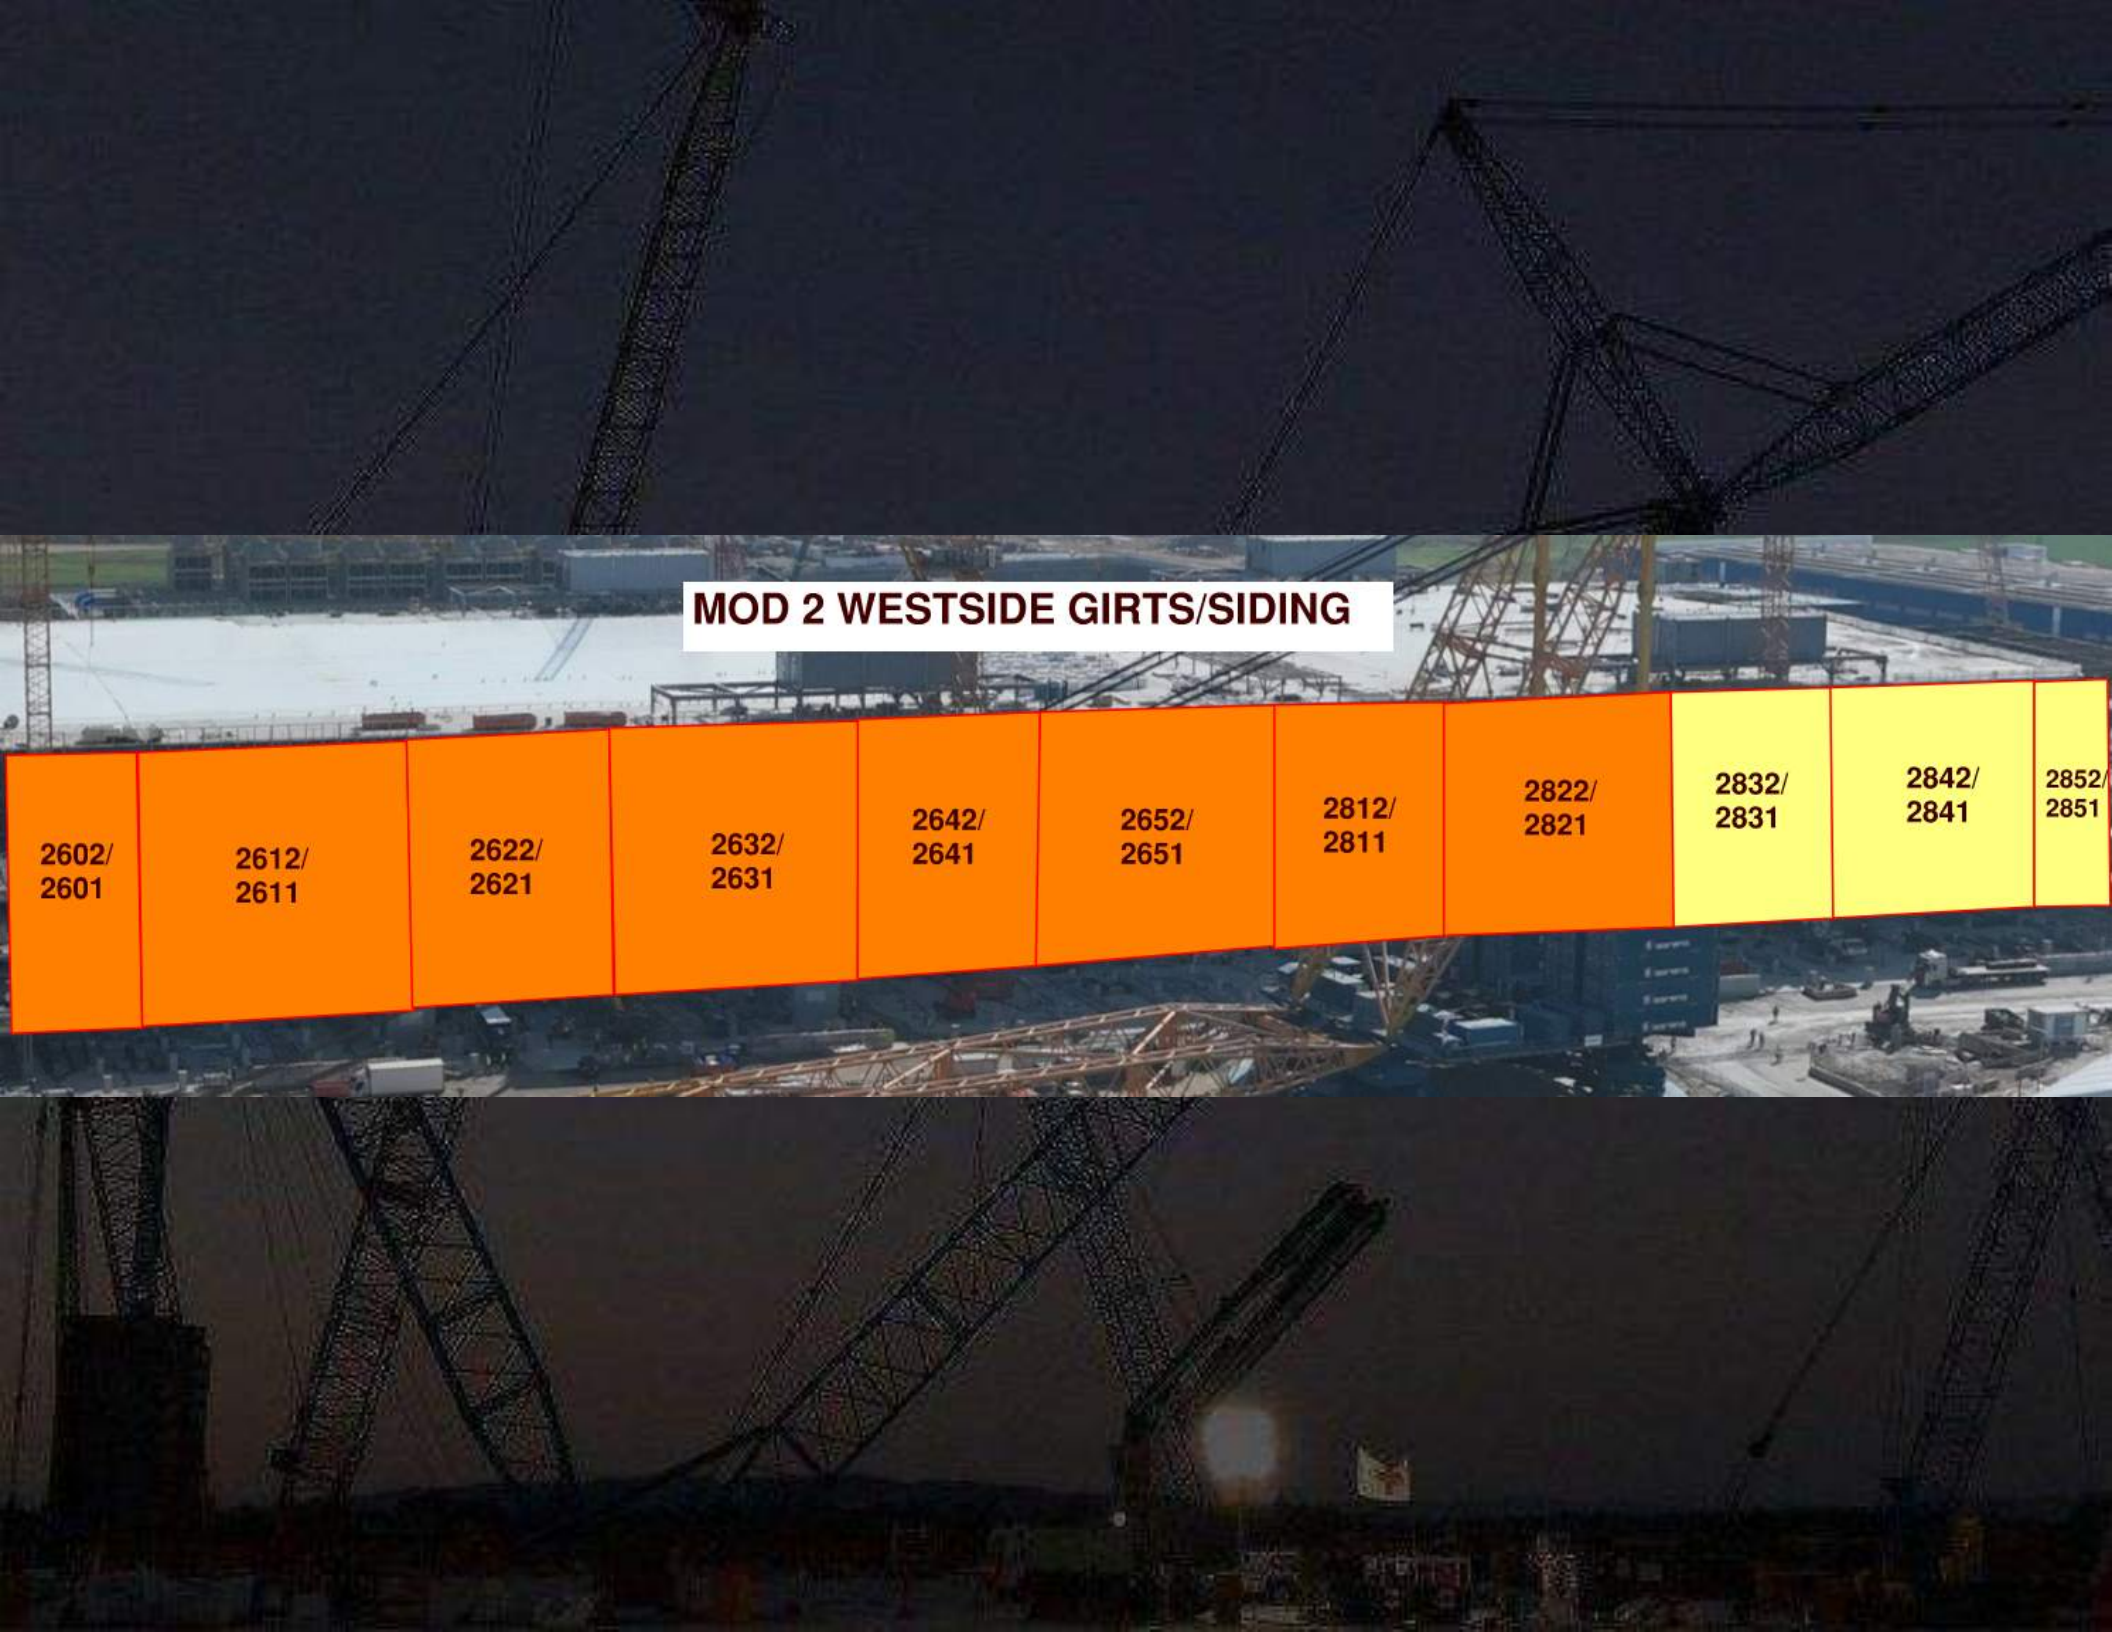

MOD 2 WESTSIDE GIRTS/SIDING

2602/
2601

2612/
2611

2622/
2621

2632/
2631

2642/
2641

2652/
2651

2812/
2811

2822/
2821

2832/
2831


2842/
2841

2852/
2851

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

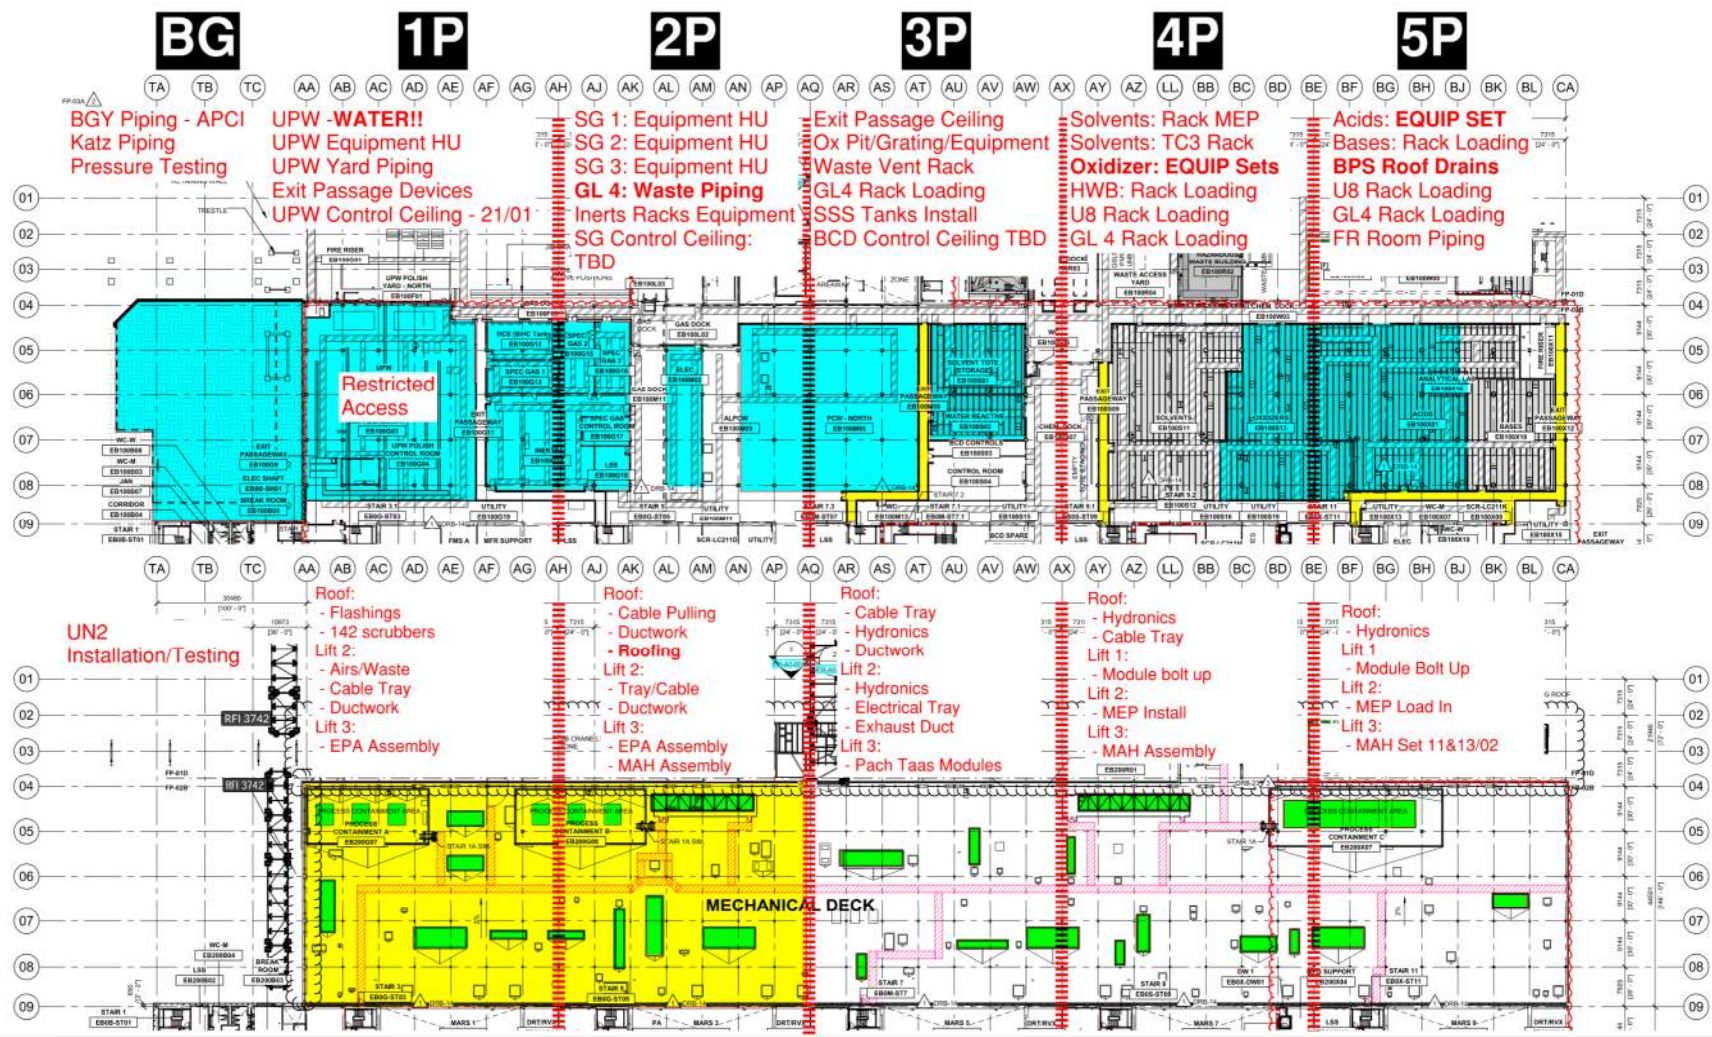

PSSS.2


Utility Level 1YA

PSSS Roof
2SA

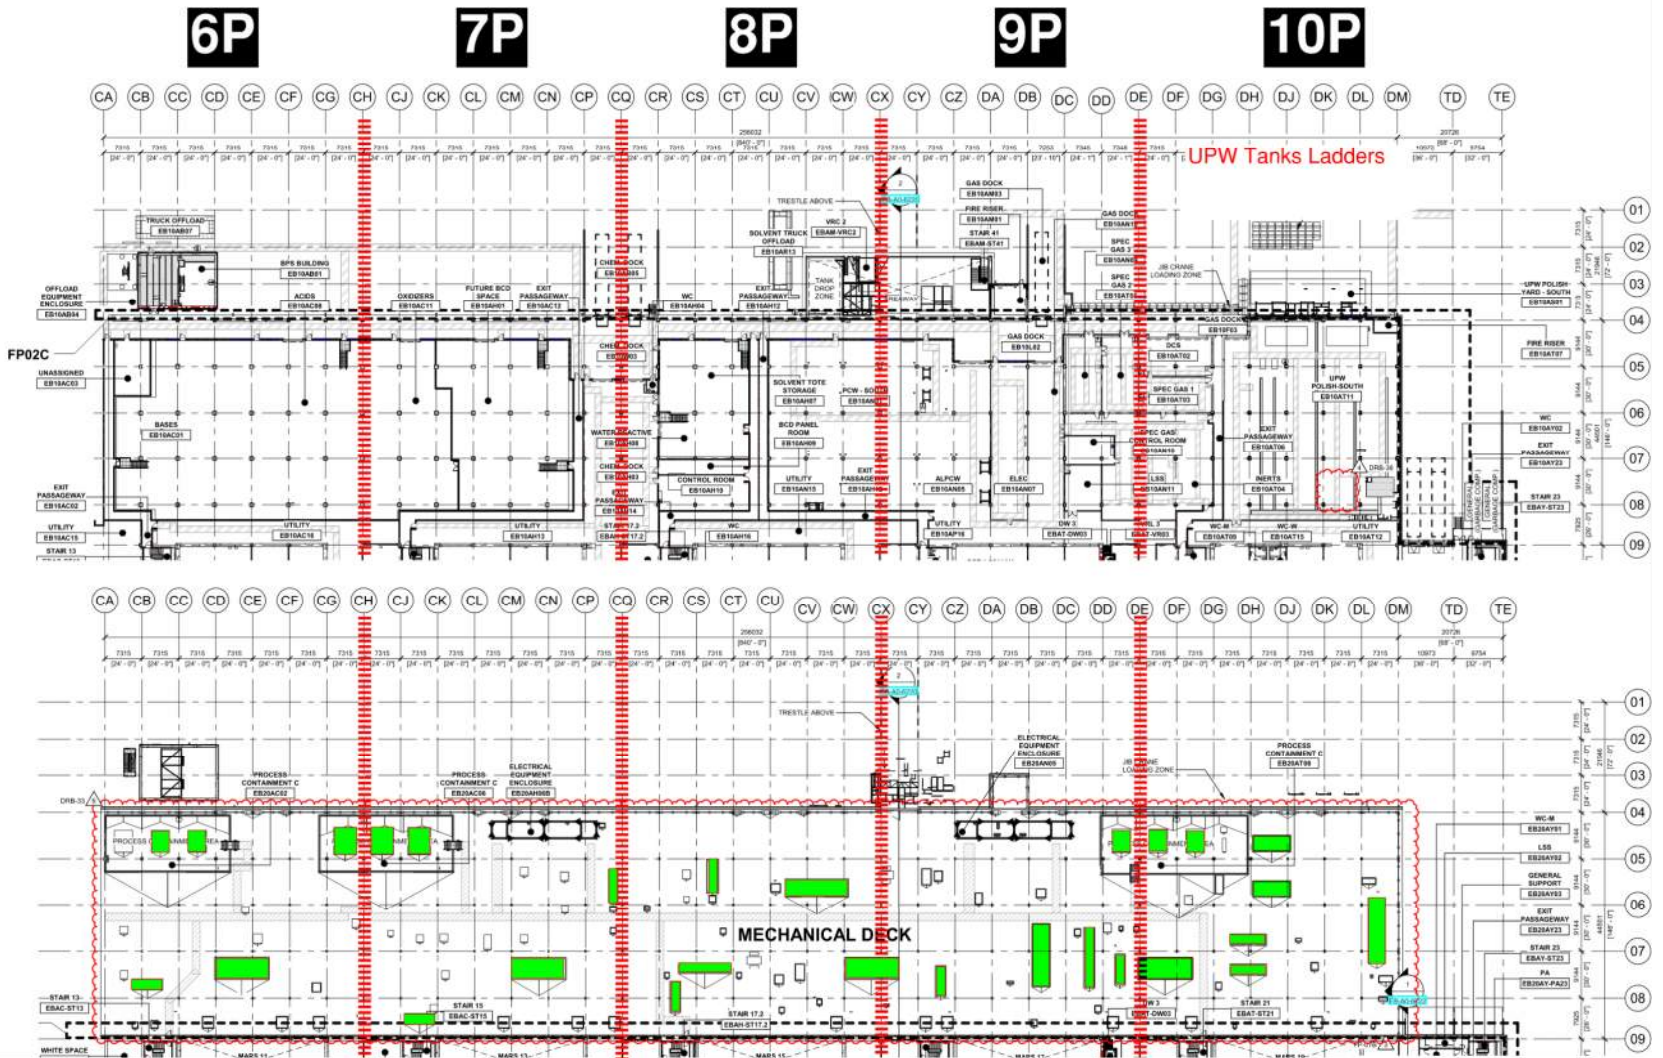

PSSS Pressure Tests

Utility Level
1YA

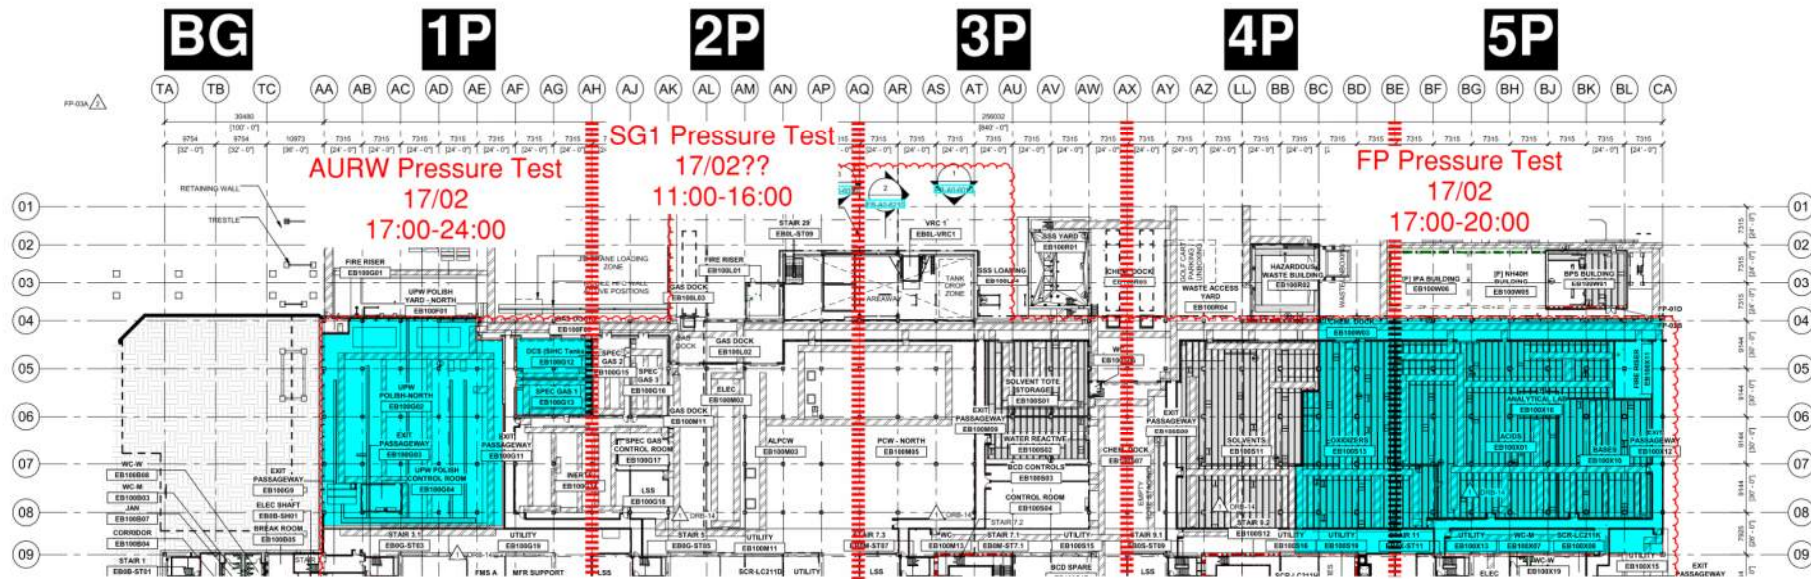

500T Dismantle 17th-19th




WJG – UL

*Carmel Bidud - installation of air ducts to small AH.
 * Megason - working on fire detection and alarm
 * SIG - erecting a scaffold for SN gutter pipes works

*Afcon - installation of permanent lighting and cable pulling.
 *Pach Taas - installation of modules in UL of west SUT.

*Afcon - installation of permanent lighting and cable pulling to the fixtures.
 * Pach Taas - installation of wall panels

* SK - installation of 3" cooper pipe

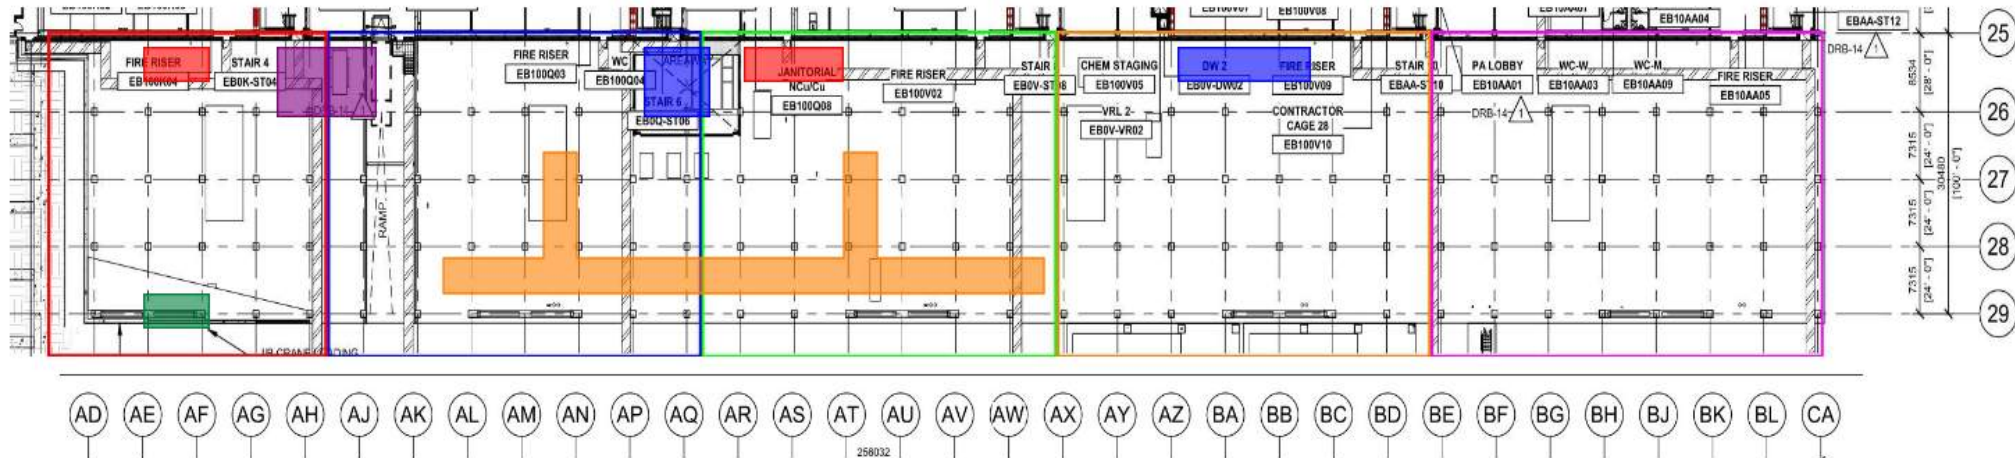

WJG – Lift 3

Afcon - installation of electrical trays.
*SK - installatyon of supports for MAH pipes

* Sami Najami - cutting grating penetrations.
* W&W -welding supports for Jib crane.

Sami Najami - cutting grating penetrations.



WJG UTILITY LEVEL BUILD OUT

Crane logistics


Crane: 220 ton
location: AF on west
road

Crane: 500 ton
location: AQ on west
road







CUB 1

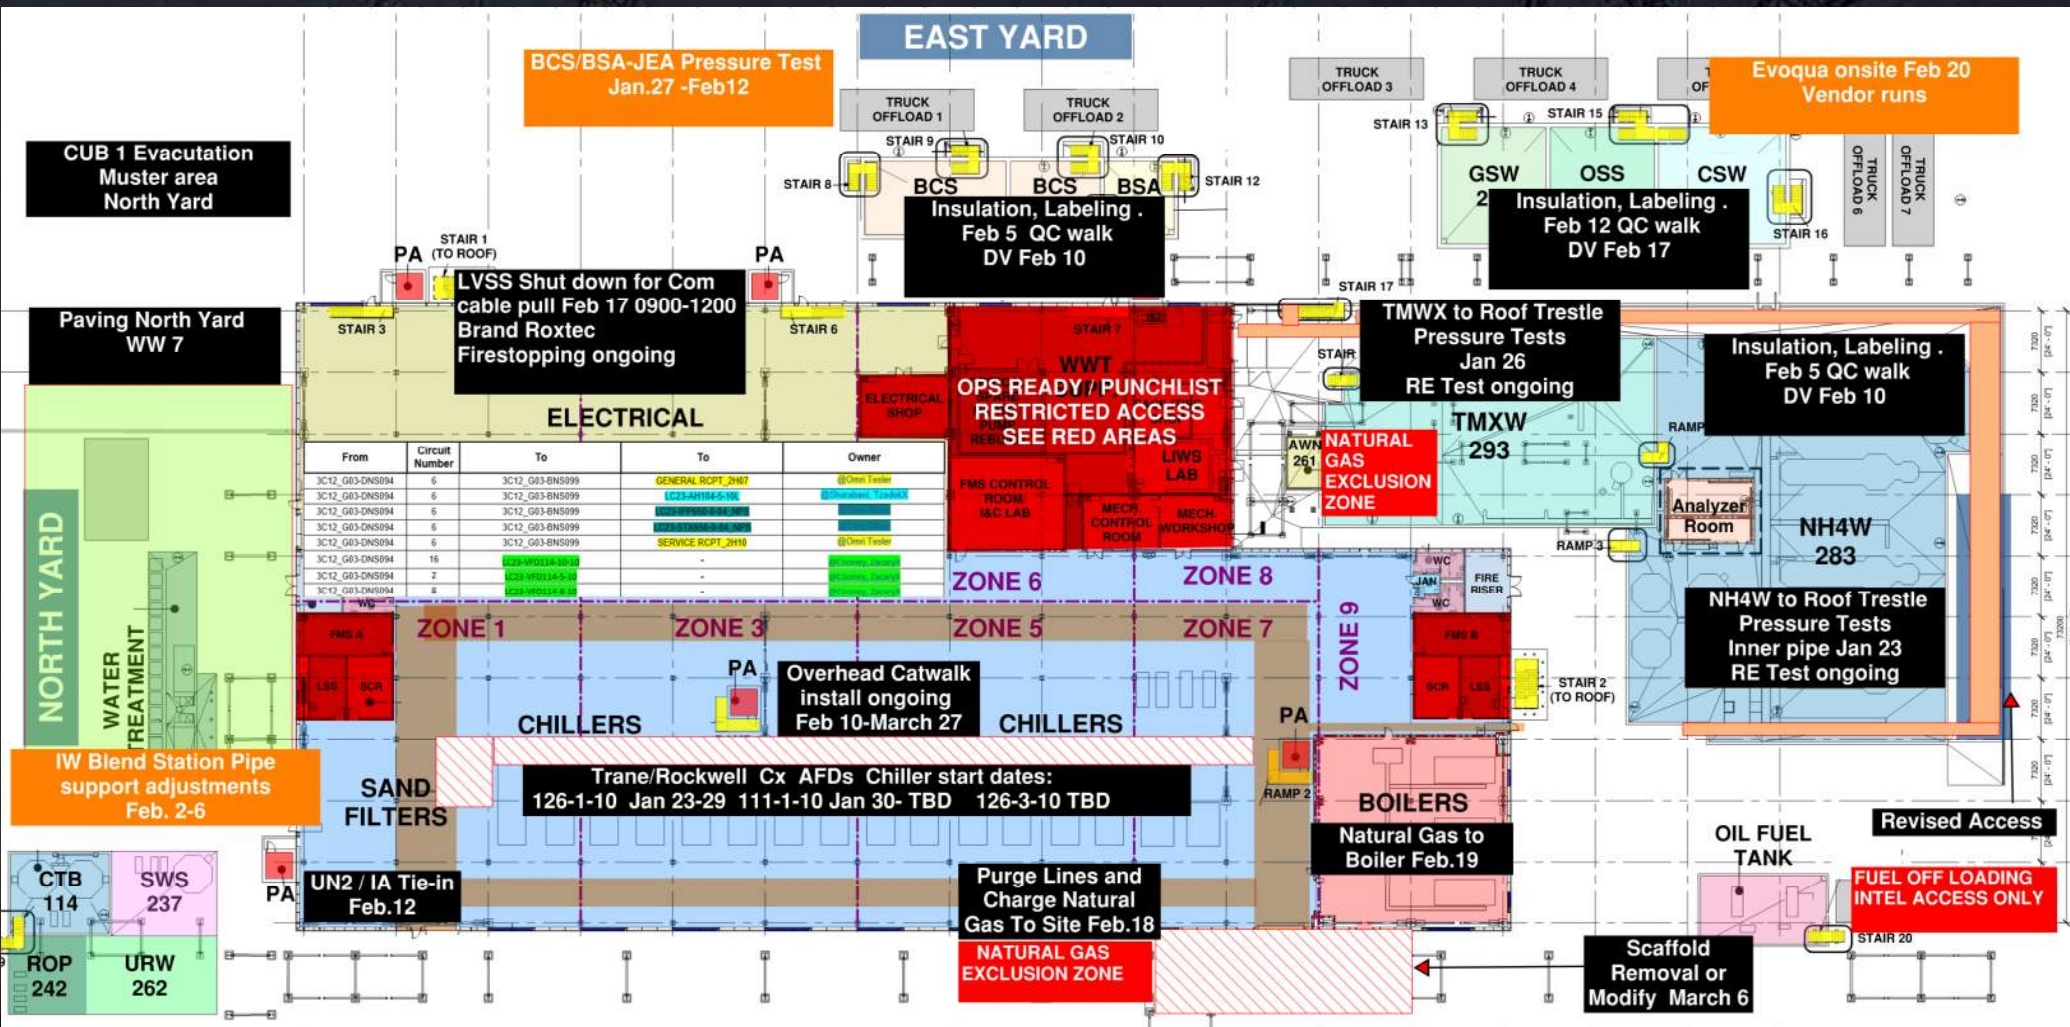


CUB 1 Exterior Pre-Punch Status

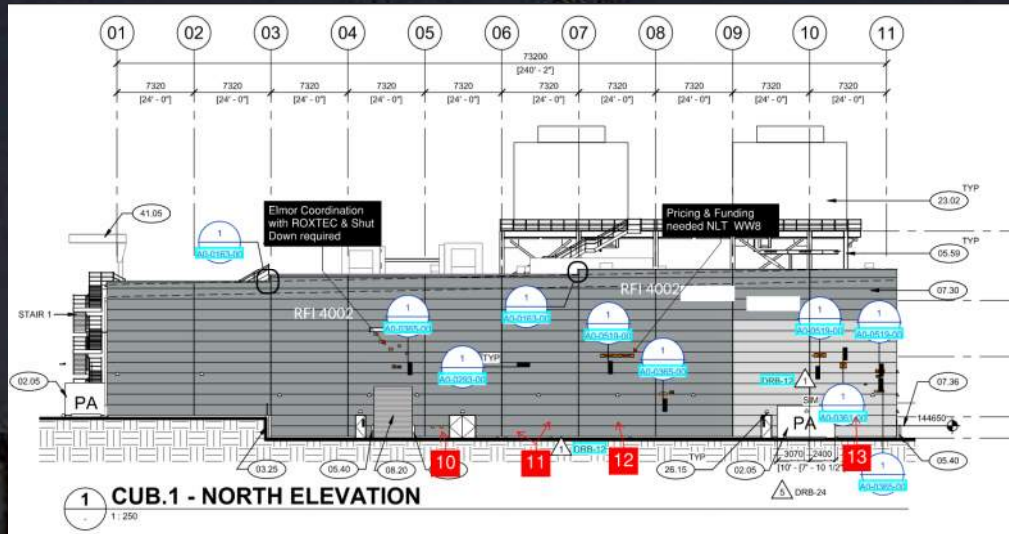

1. North Elevation ROXTEC Electrical in Coordination with Elmor WW 8
2. West Elevation pending UN2 tie in, Blank out Conditioned water to CUB 2
3. Set Final Man door complete Access Controls March 6- 20

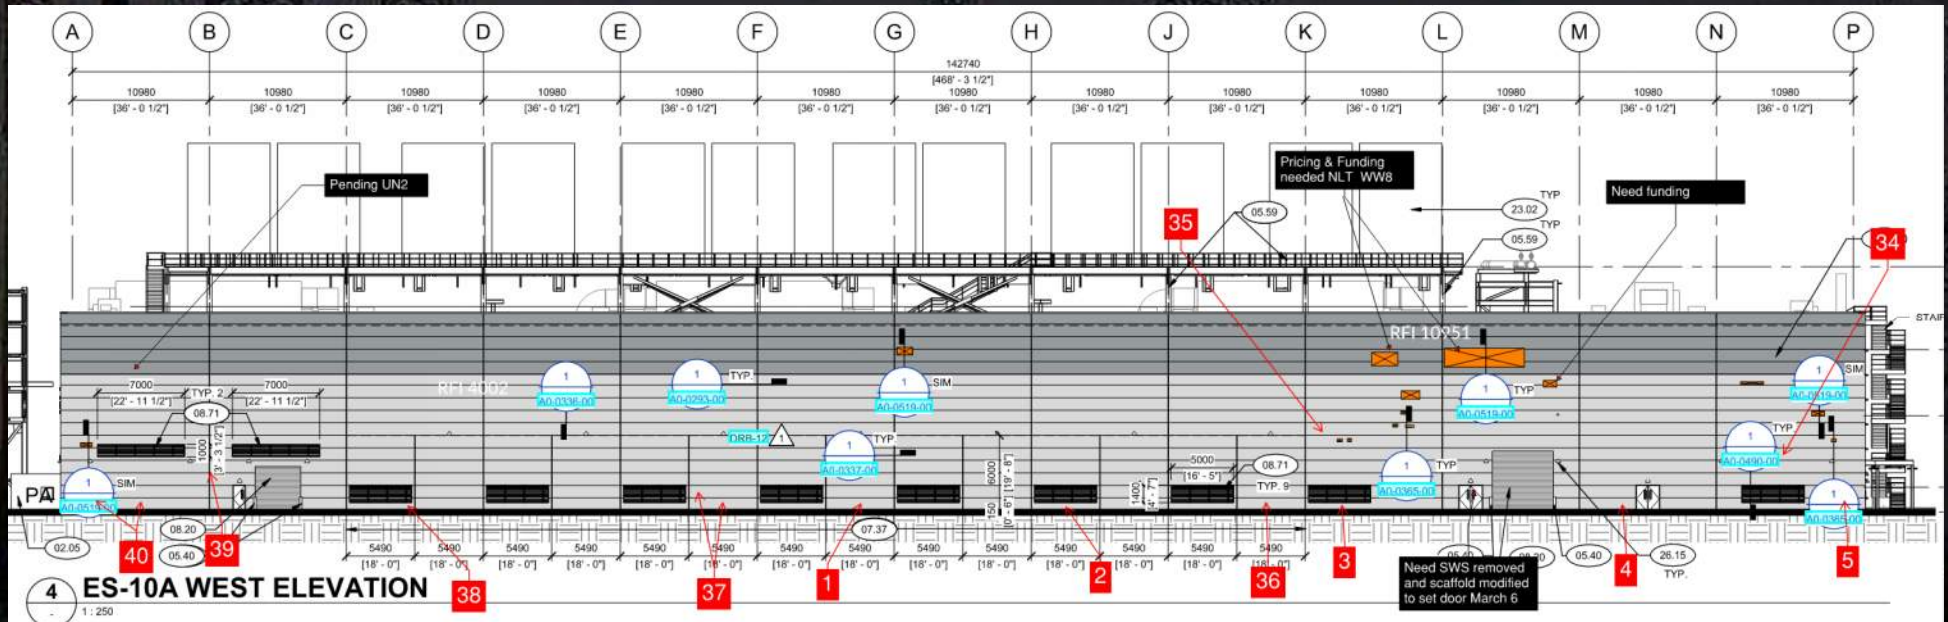


CUB 1 – EXTERIOR/ROOF

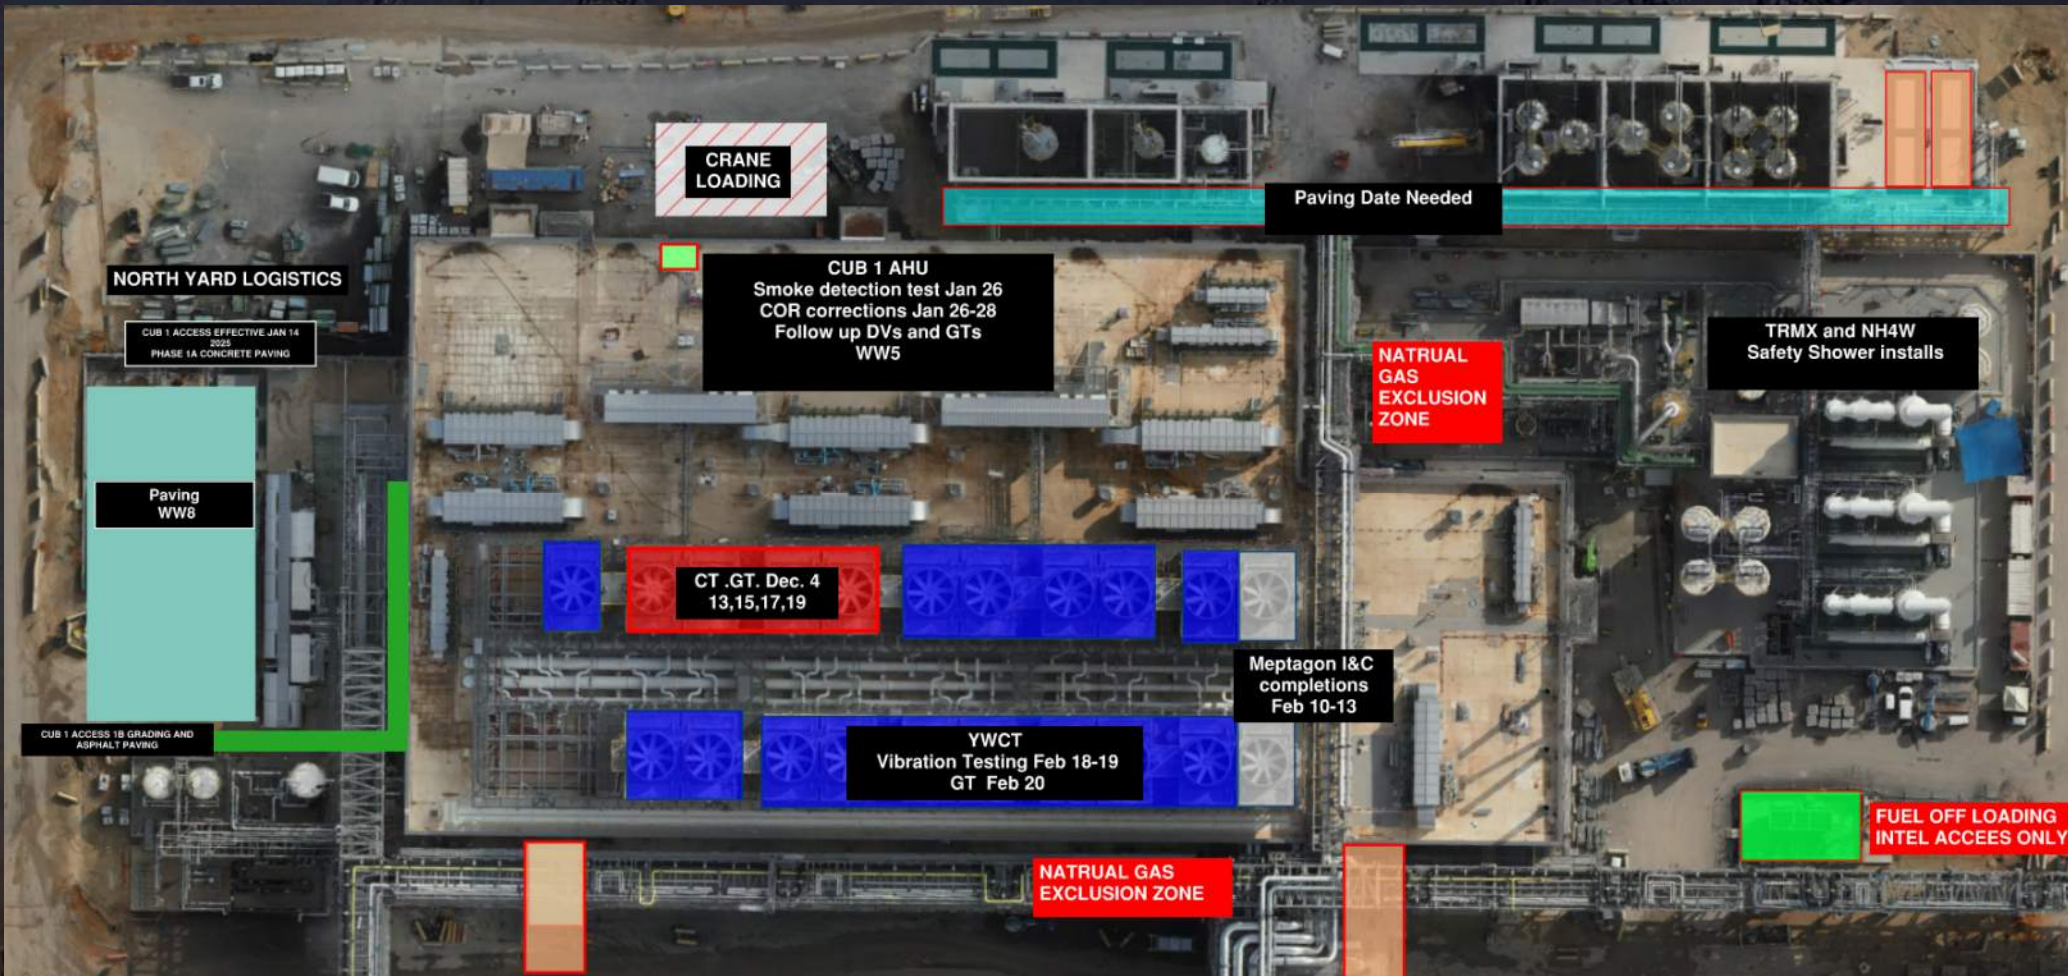


CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

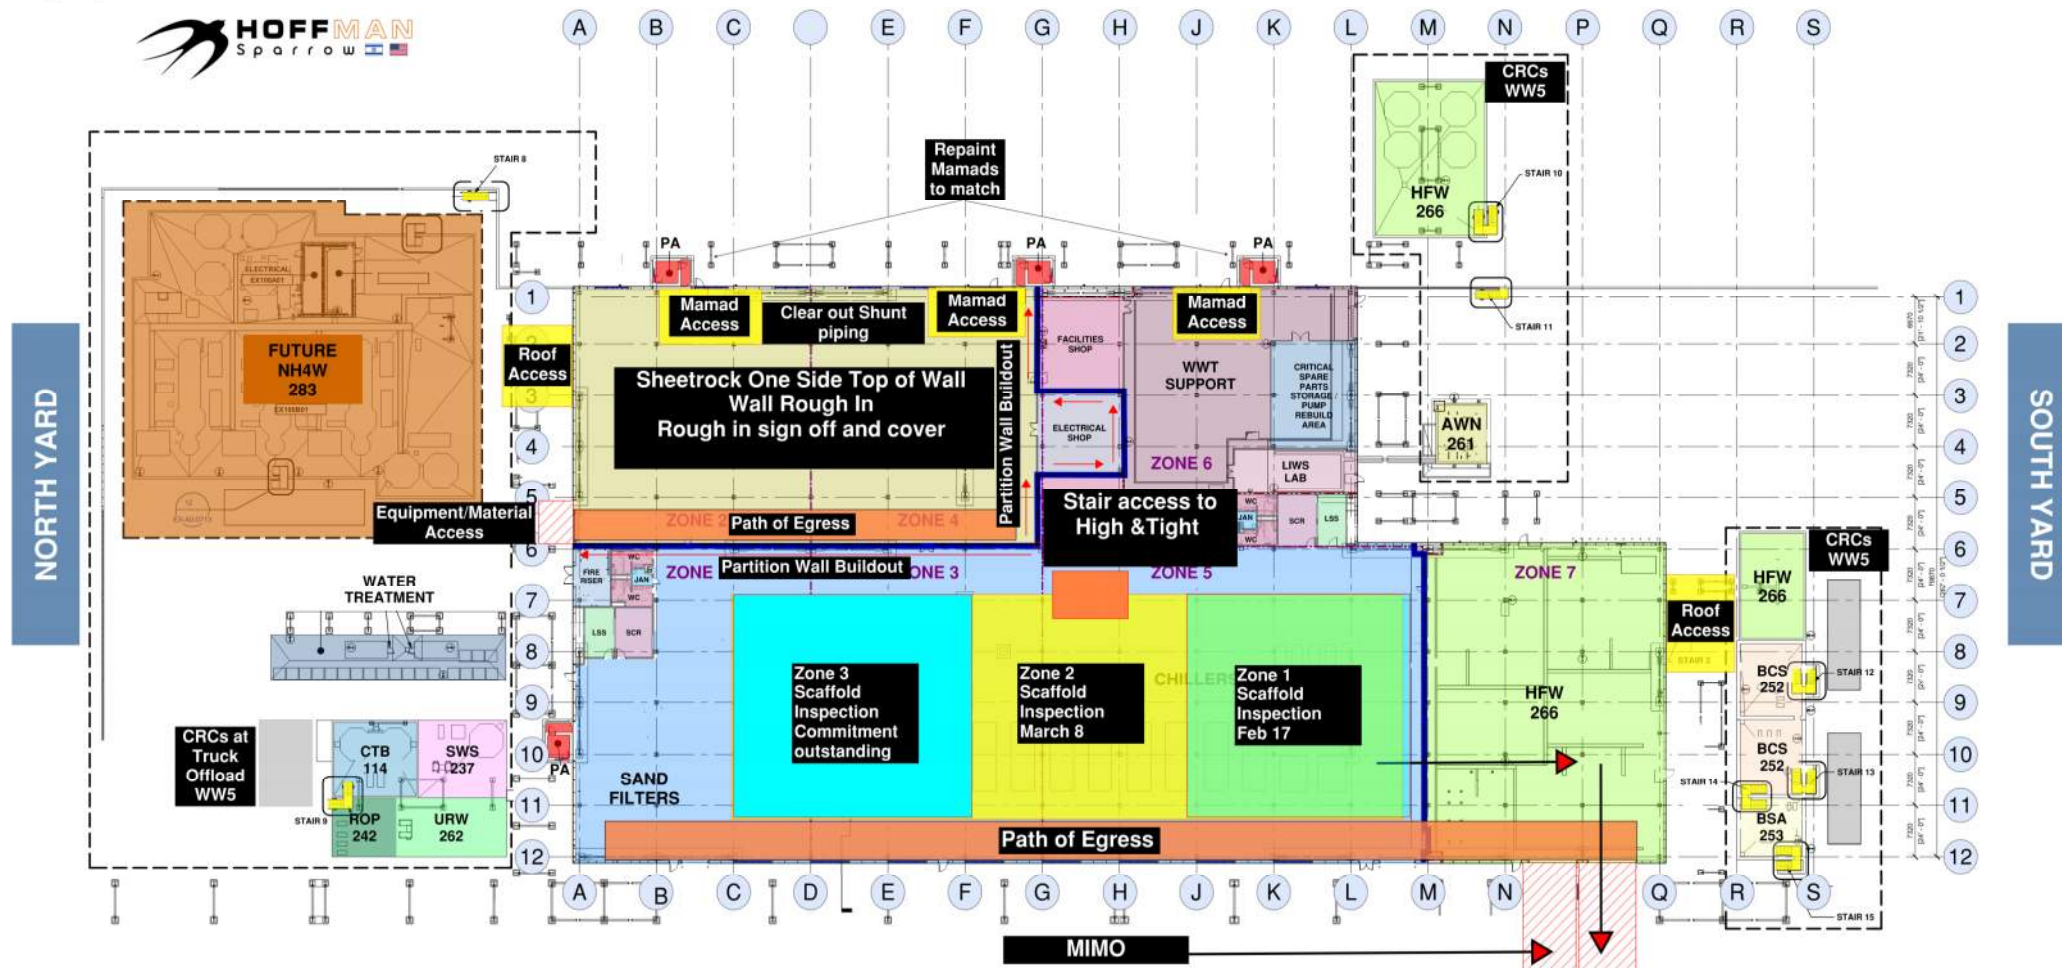

CUB 2 – EXTERIOR/ROOF

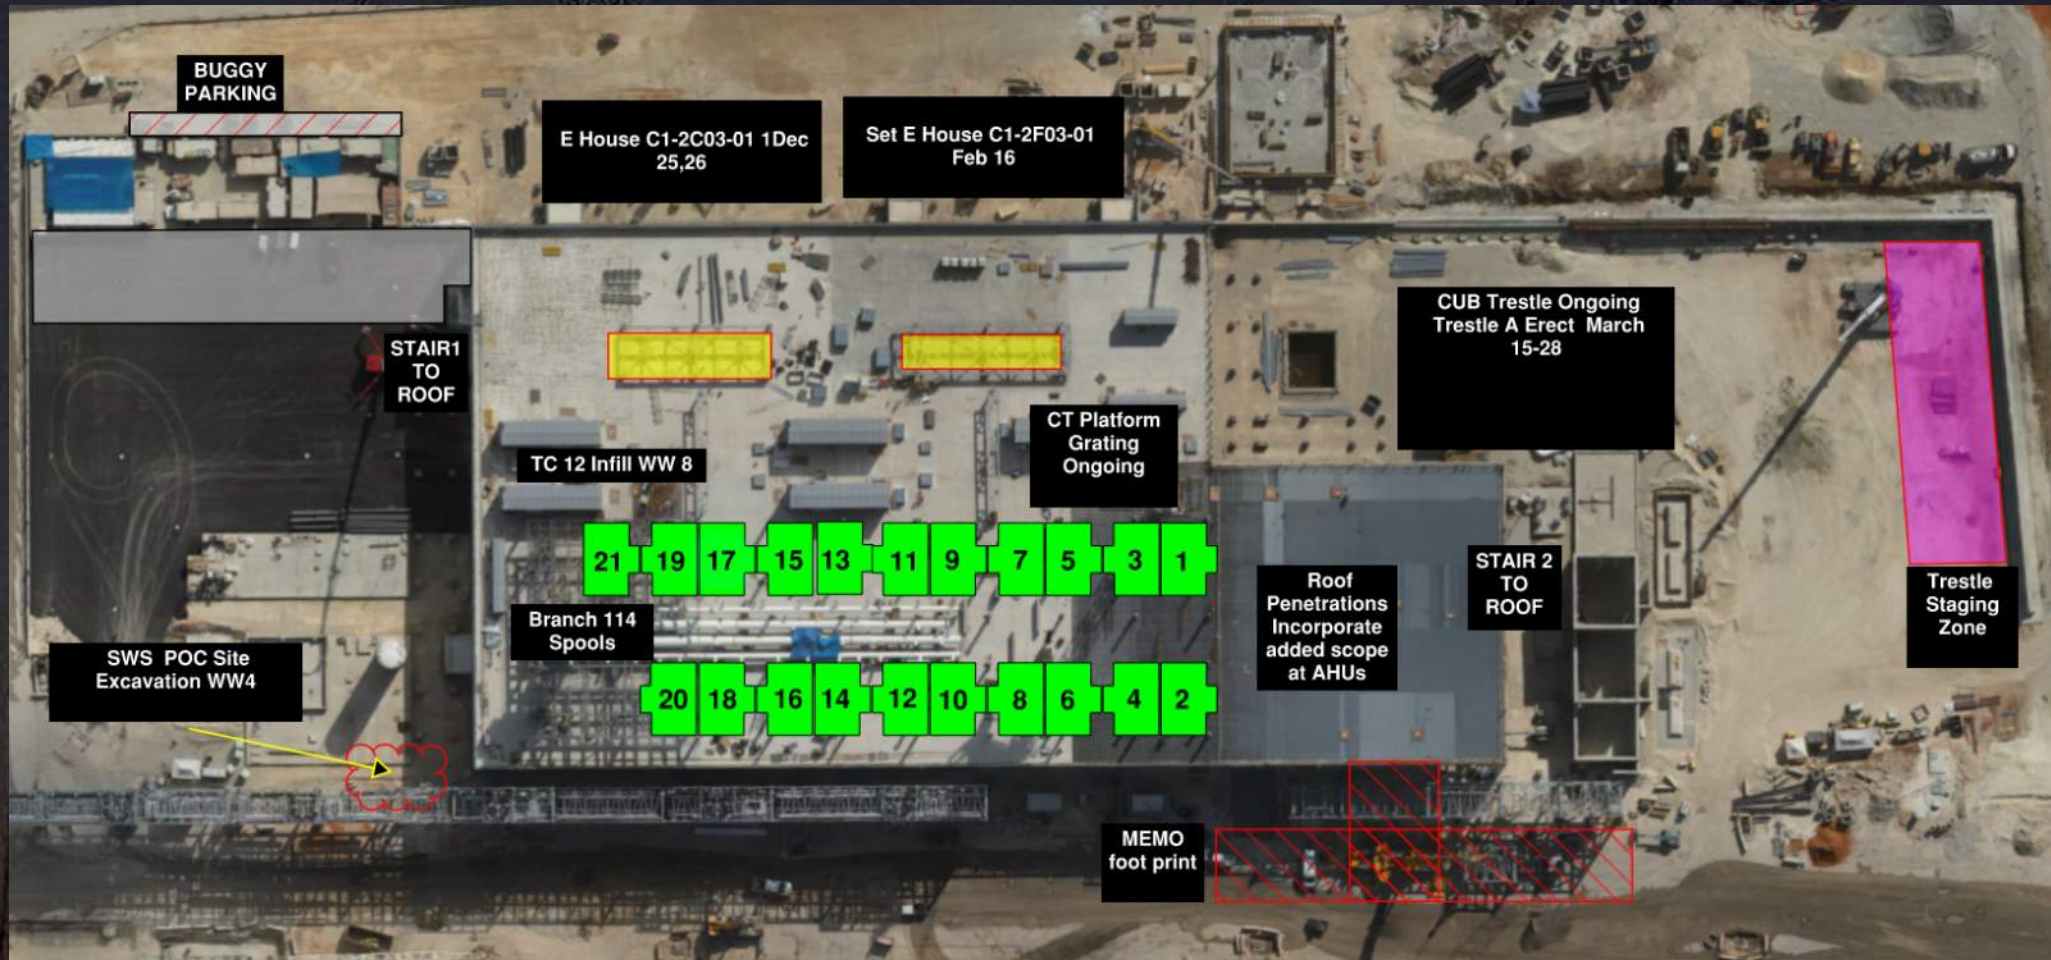



HOFFMAN CONSTRUCTION COMPANY



From main kiosk

Site temporary power

Legend :

— 22KV Line

— 400V Line

109 - Kiosk

● - Lift Station

Temp power shutdown
Start: 16-Feb- 18:00 PM
End: 16-Feb- 20:00 PM
From AW to CC Grid line
All the floors + JG
SB, lights, elevator
+TC-6

Fab 38.2

Fab 38.1

North

Cub 2

TC-12
Done

Cub 1

630A
SW

TC-9

630A
SE

TC-7

630A
NW

630A
NE

TC-5

630A
SE

630A
NW

630A
NE

TC-10

TC-8

To 115

From main

117

115

116

114

113

112

111

108

109

107

106

105




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

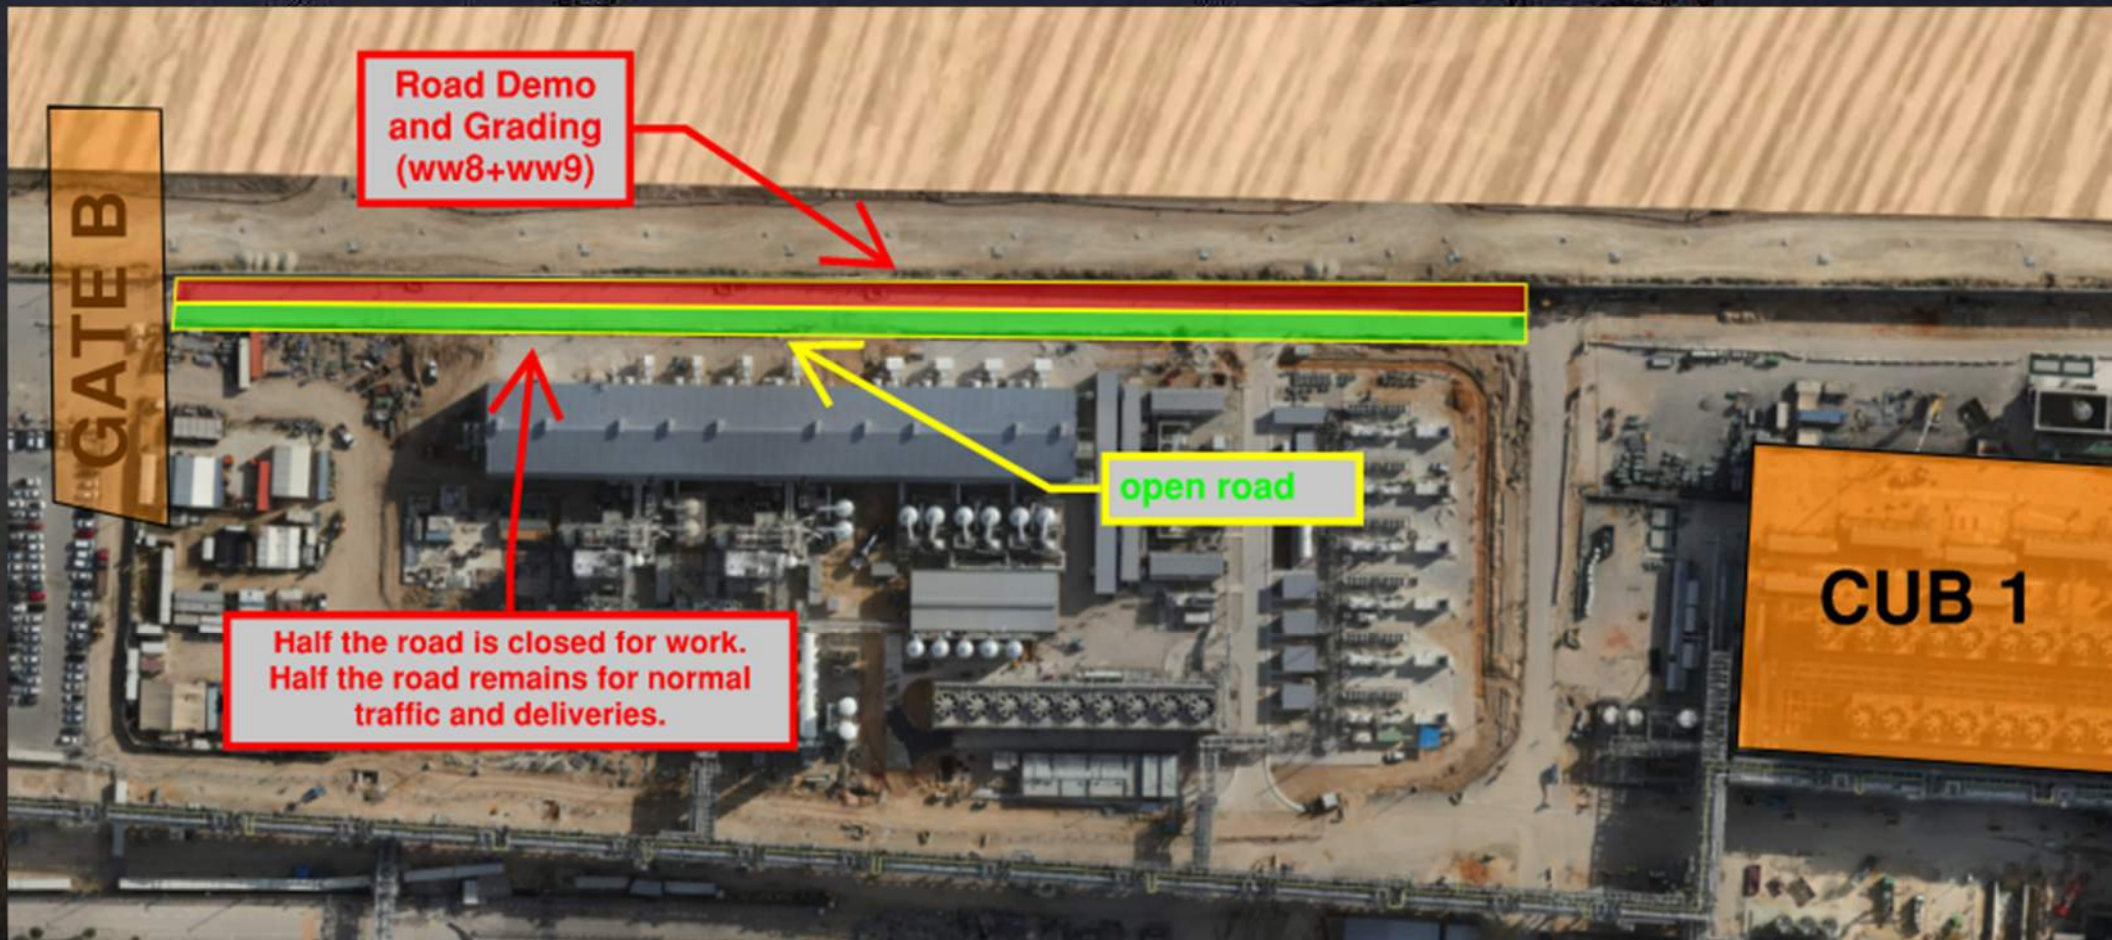



Daily Coordination Meeting

Site Logistics North






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South

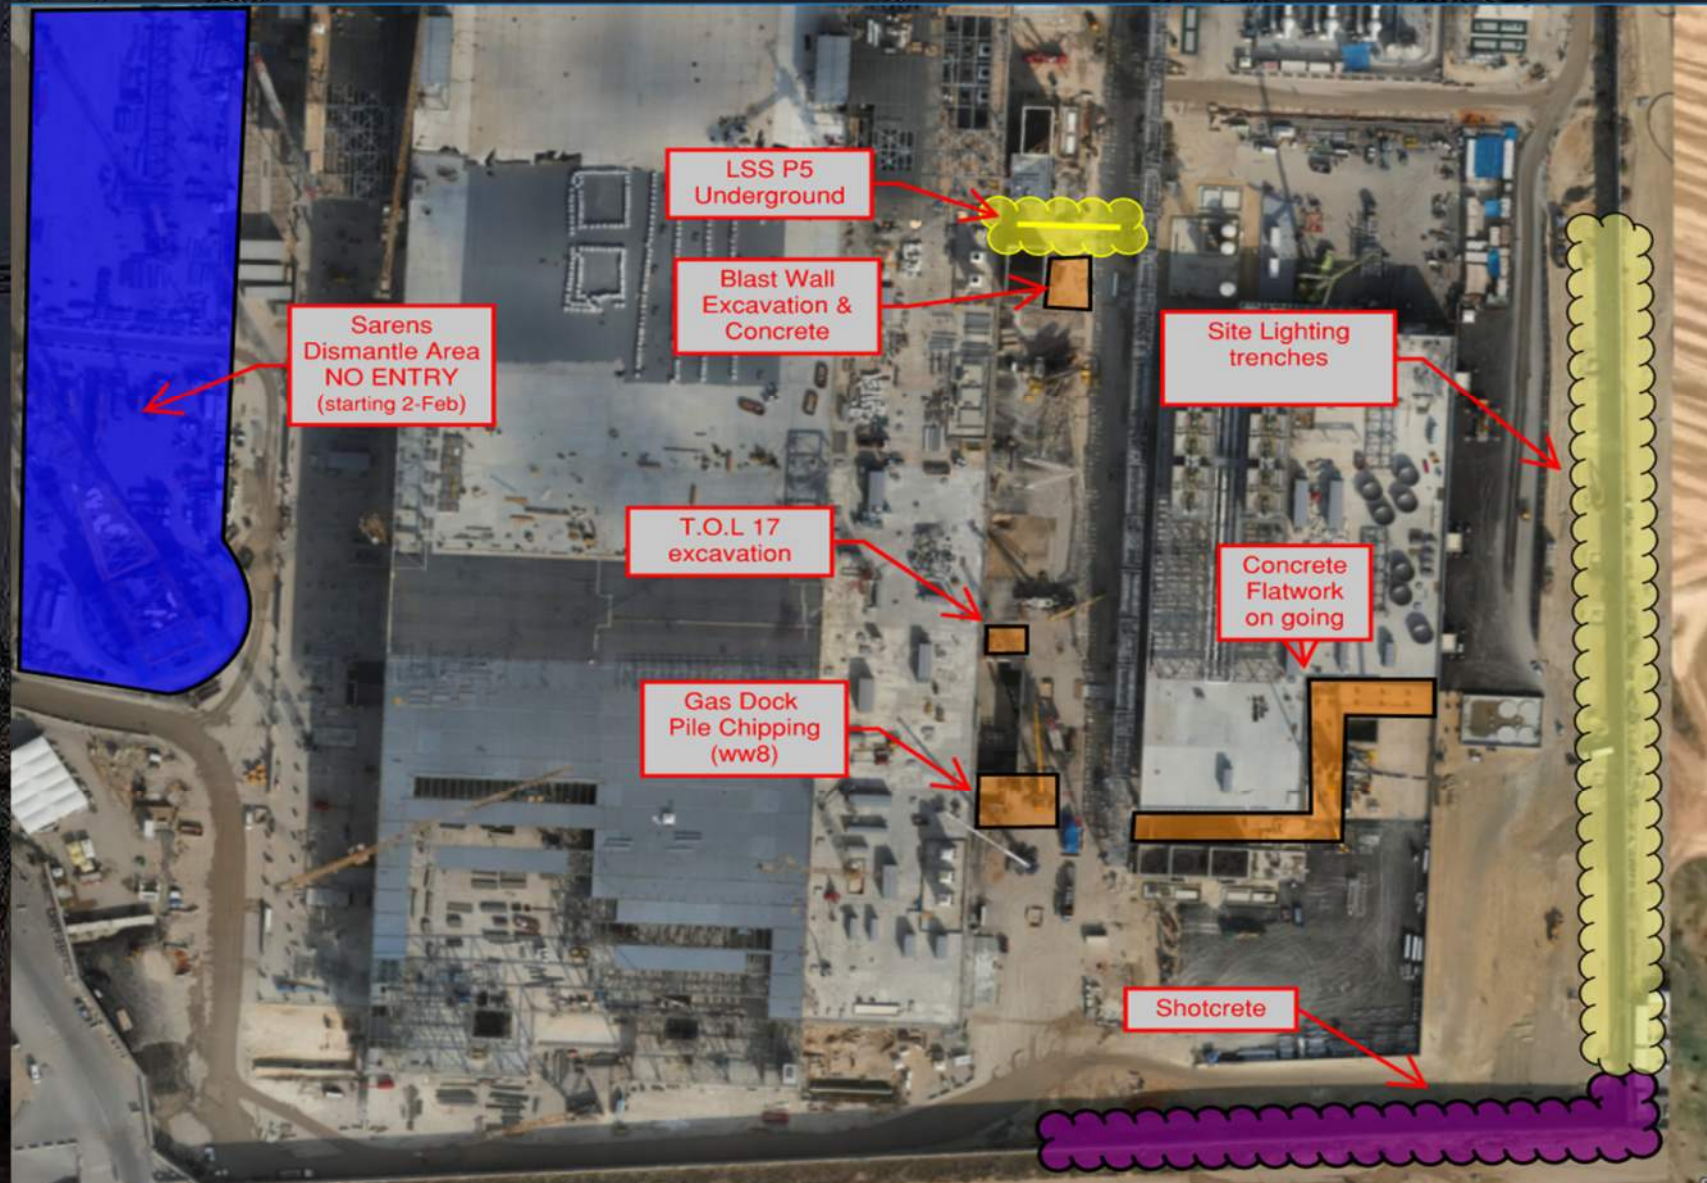

Spotters & Operators

- Operators are responsible for the safe operation of their equipment/vehicle.
- When there is a spotter used to assist them with navigating through areas, they are also responsible for that person.
- This means, before they move their vehicle or equipment they need to verify the location of their spotter, make sure they are out of the moving path of the vehicle, and they need to communicate where they are moving.
- It can be deadly to not know where the spotter is, as they could be struck by the vehicle. Yes, spotters should not stand in the line of fire, but the added layer of defense here is for the operator to not move until they know exactly where their spotter is.
- This also allows the spotter to make sure that the operator can/should be moving in the planned direction.

HCC/EHS Weekend Work- 14.02.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jeff Bowen – 052-3787746
Gad Yaacov - 052-3784838
Pini Kahlon - 052-7343004
Brian Smith - 052-2181361
Asher Amar - 052-8801316
David Jollands - 052-3961675

CSA CM

Nikol – Loboda - 052-3124965
Ben Tauar - 052-3173040
David McBride - 052-5379828
Shir A
Hadar S

MEP

Cx

Cranes

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 14.02.2025

FAB

Utility level/ SUT

Subfab

- Pach Taas
 - Wall Penetration
 - Tomer: 0507670585
 - Ofik: 0507838486
- Afcon E
 - All over SF
 - Raz: 0546838626
- MEGASON
 - MOD 2,LSS Rooms
 - Israel: 0526869393
- SELA
 - 2E MARS
 - Yuvel: 0502649246
- Afcon-Telecom
 - 5E,5W
 - Anish: 0559537332
- Elram
 - TTNE
 - Eliezer: 0544236899
- Lesico
 - 17 Line
 - Gabriel 0549892929

Clean Room

- Talad – 25 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Elad 0546654473)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Roni 0542496363, Elisha 0587963704)
- Talent solution 8 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Super Yosi 0526557130)
- W&W 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Sig – 17 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Codrin 0546594273, EHS Ovidiu 0546993648)

Subcontractor Weekend Work- 14.02.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- Lesico – H2 Vent/SUT East Area Way Rack
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109
- Combe UPW – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- HSAI – Chem Dock Retaining Wall
 - Foreman – Dave – 052-4121028
 - Safety – Hiam
- SK Engineering – 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112

WJG

Pach Taas

Foreman: Tomer Sasi – 0507670585

Safety: Eran Tzadok - 0547706233

Afcon

Foreman: Montu - 0559116973

Safety: Stiven – 0552742935

Chemo Aharon

Foreman: Shai Adi – 0524801180

Safety: Erez Megidish - 0549716840

Subcontractor Weekend Work- 14.02.2025

CUB

Chemo Aharon CUB 2:
Dudu - 0509808846
Alberto - 0508573970

SKE CUB 2:
Mario - 0548991051
Marzuk - 0548830263

Sami Najami CUB 2:
Husein - 052-6917461
Aviram - 050-9059920

HSAI CUB 1&2:
Sergey - 0552728807
Haim - 054-8038554

Meptagon I&C CUB 1:
Sergey - 0537981592
Itzik - 0587441140

Pach Taas CUB 1 Roof:
Tomer - 050-767-0585
Eran - 054-7706233

Trestle

SNJ:

Piping:
17 People
Steal:
15 People

Superintendent
Mahmoud Ayub 054-4915889

Safety:
Aviram Shriki / 050-9059920

Site

- D.A. - shotcrete south wall
- Olizki - Cub 1 east, north,
- Afkon - BGY

Daily Coordination Meeting



14:00 Sign In
