

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:




[illegible]


TRUSS SET
7W
Tomorrow
Start 4:00am



UTILITY LEVEL MOD1

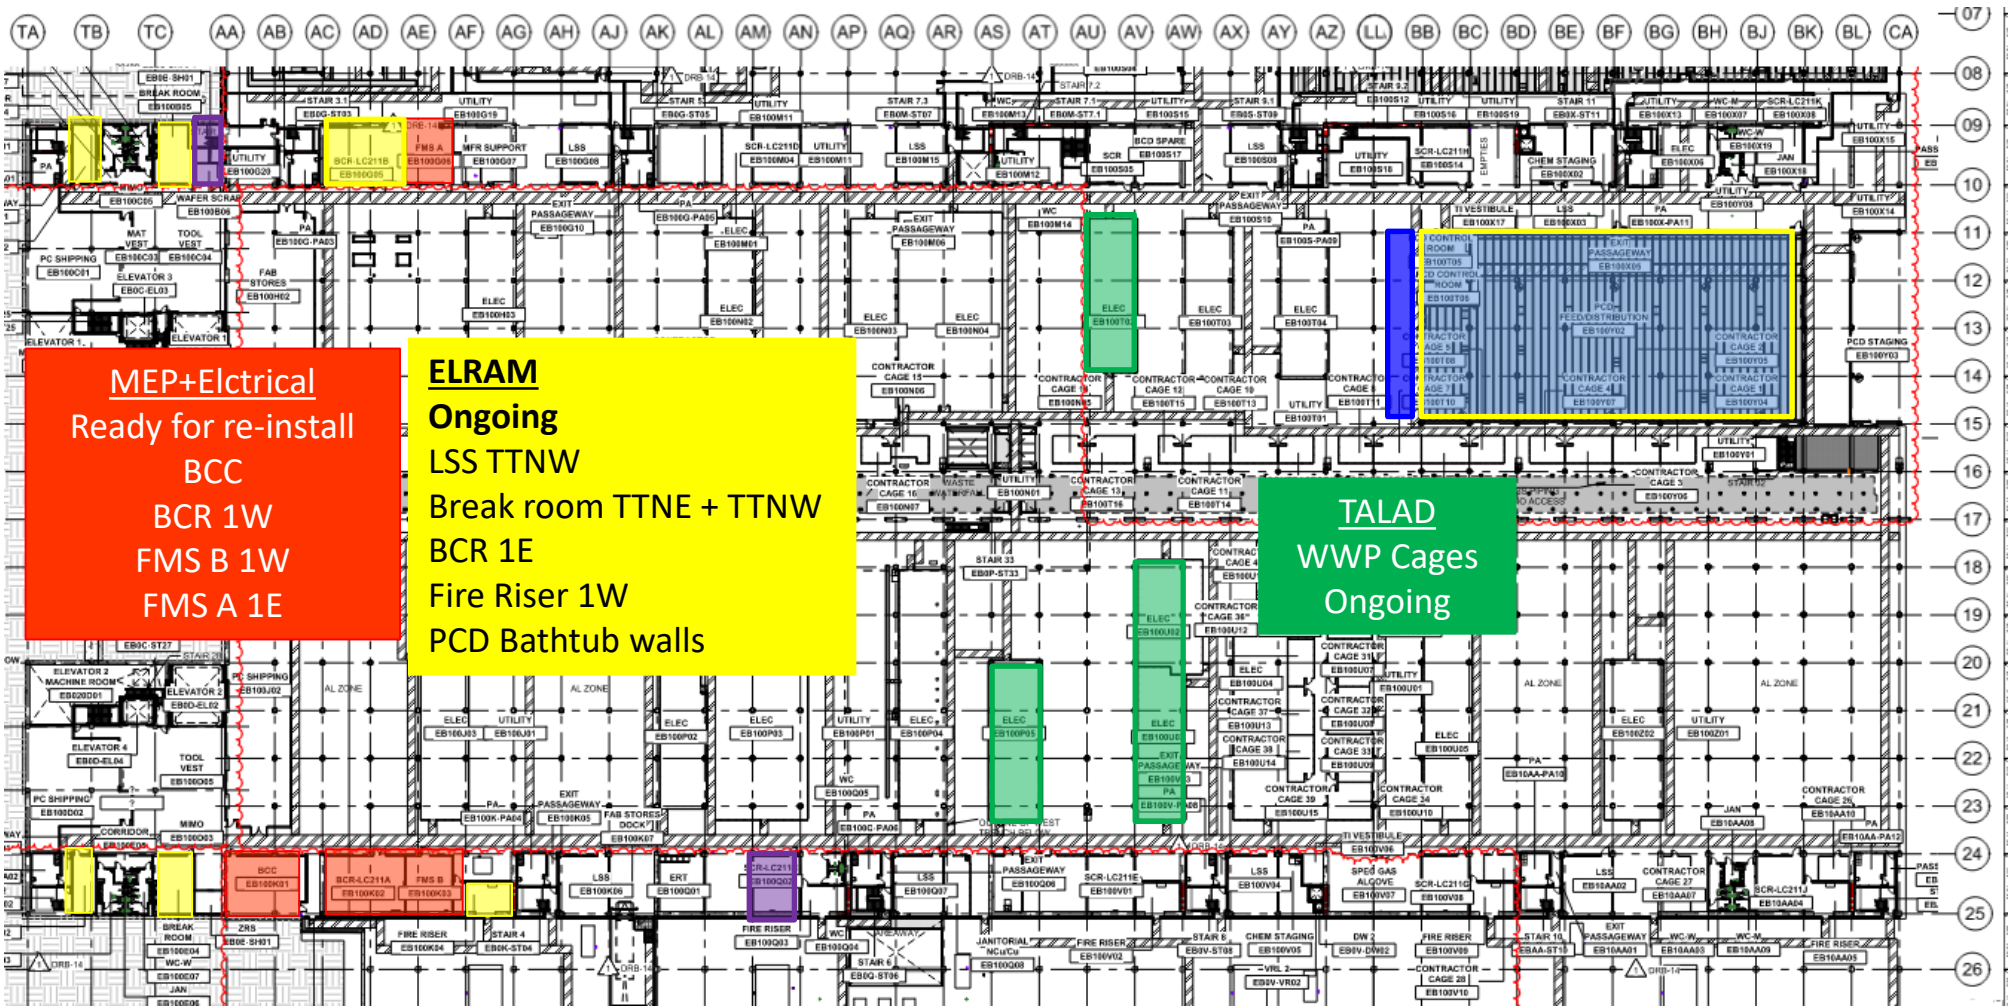

UTILITY LEVEL MOD2

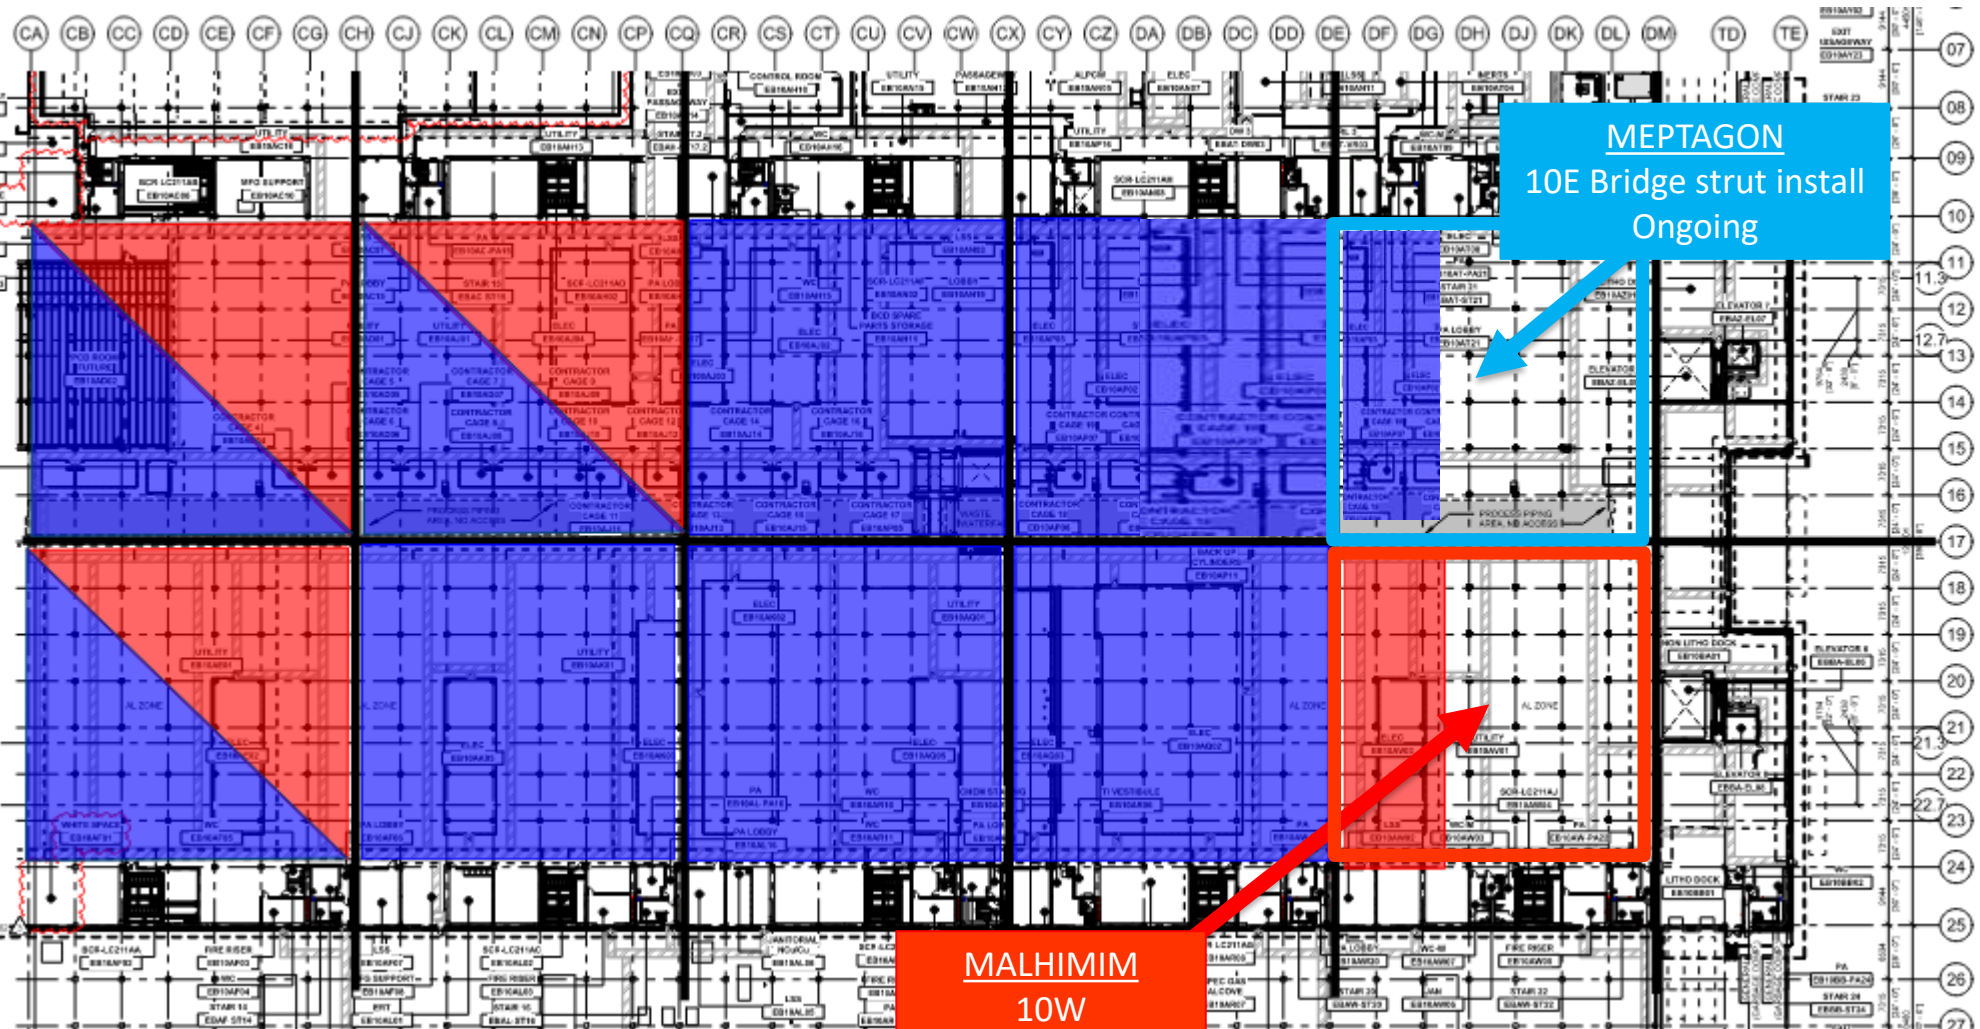


MEPTAGON
10E Bridge strut install
Ongoing

MALHIMIM
10W
Sprinklers install




SUT 38.1 LEVEL

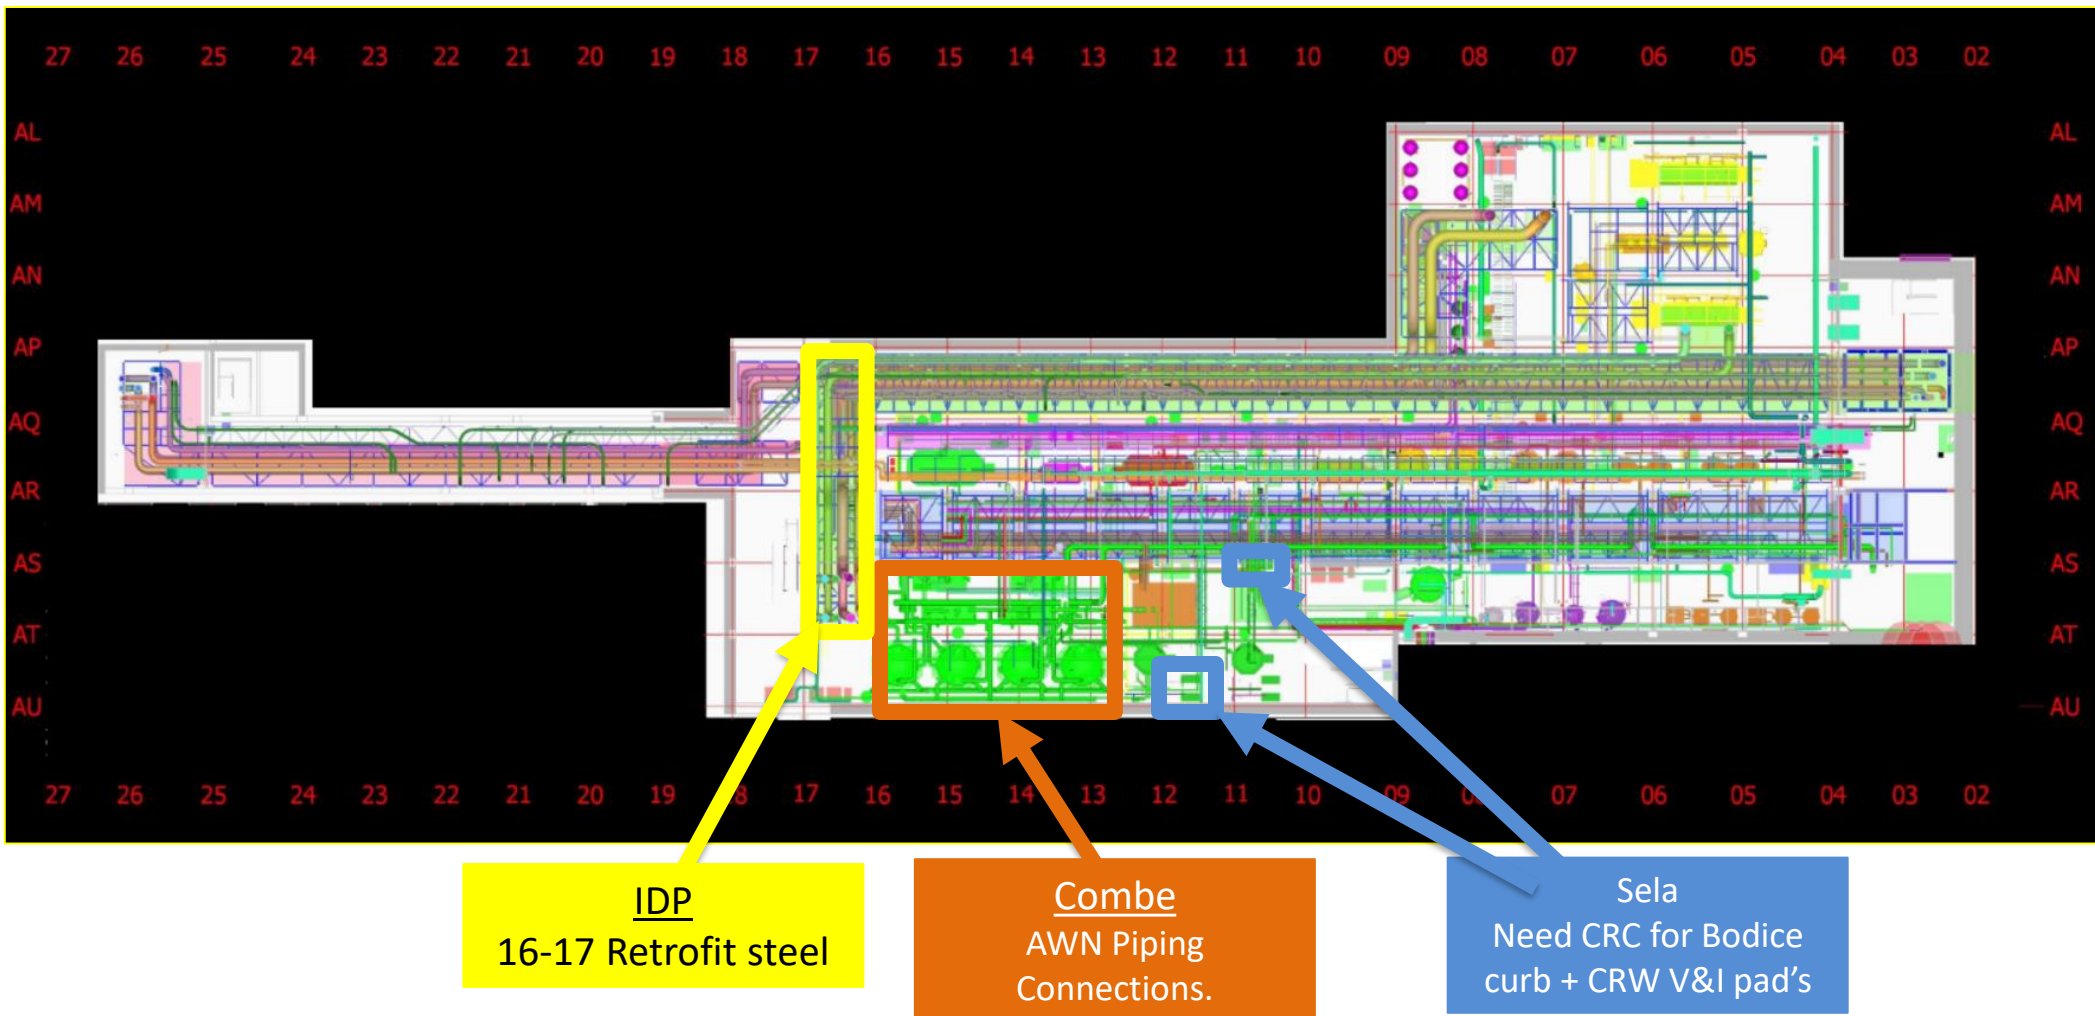



SUT 38.2 LEVEL

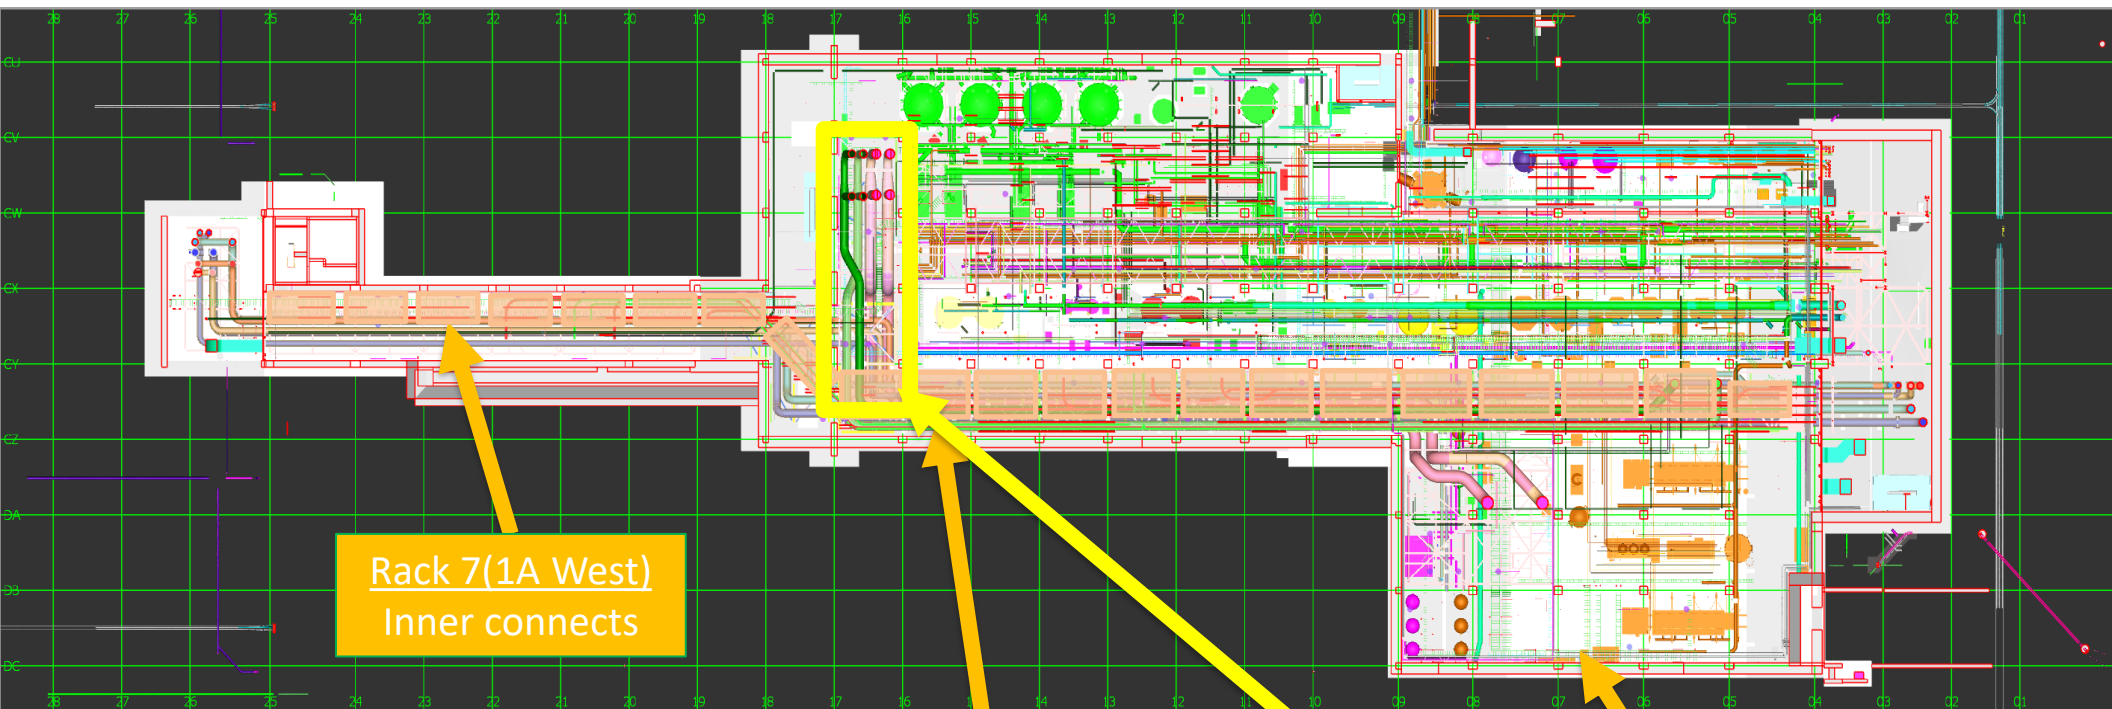

Rack 7(1A West)
Inner connects

1A Rack
Inner connects


16-17 line
Upper Steel Bed
build

8 Rack
Lifting


CRW
H&T
Installing supports

Vesda
H&T
Not actively installing


SUBFAB BUILDOUT MOD 1

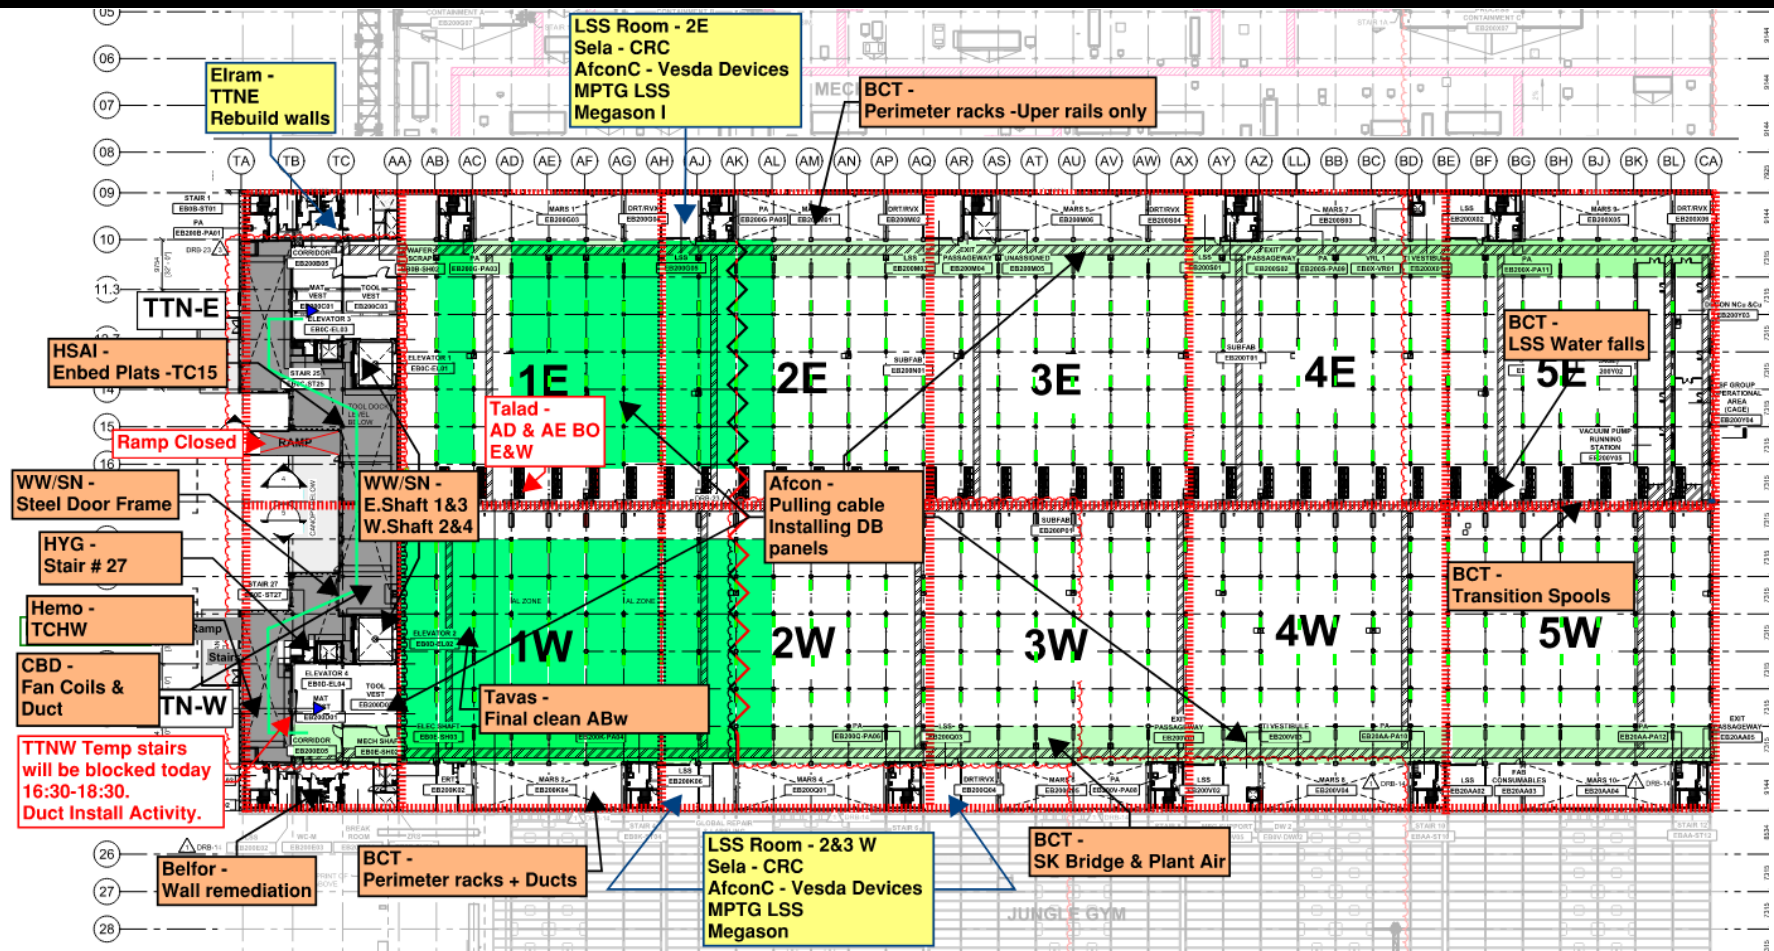

SUBFAB BUILDOUT MOD 2

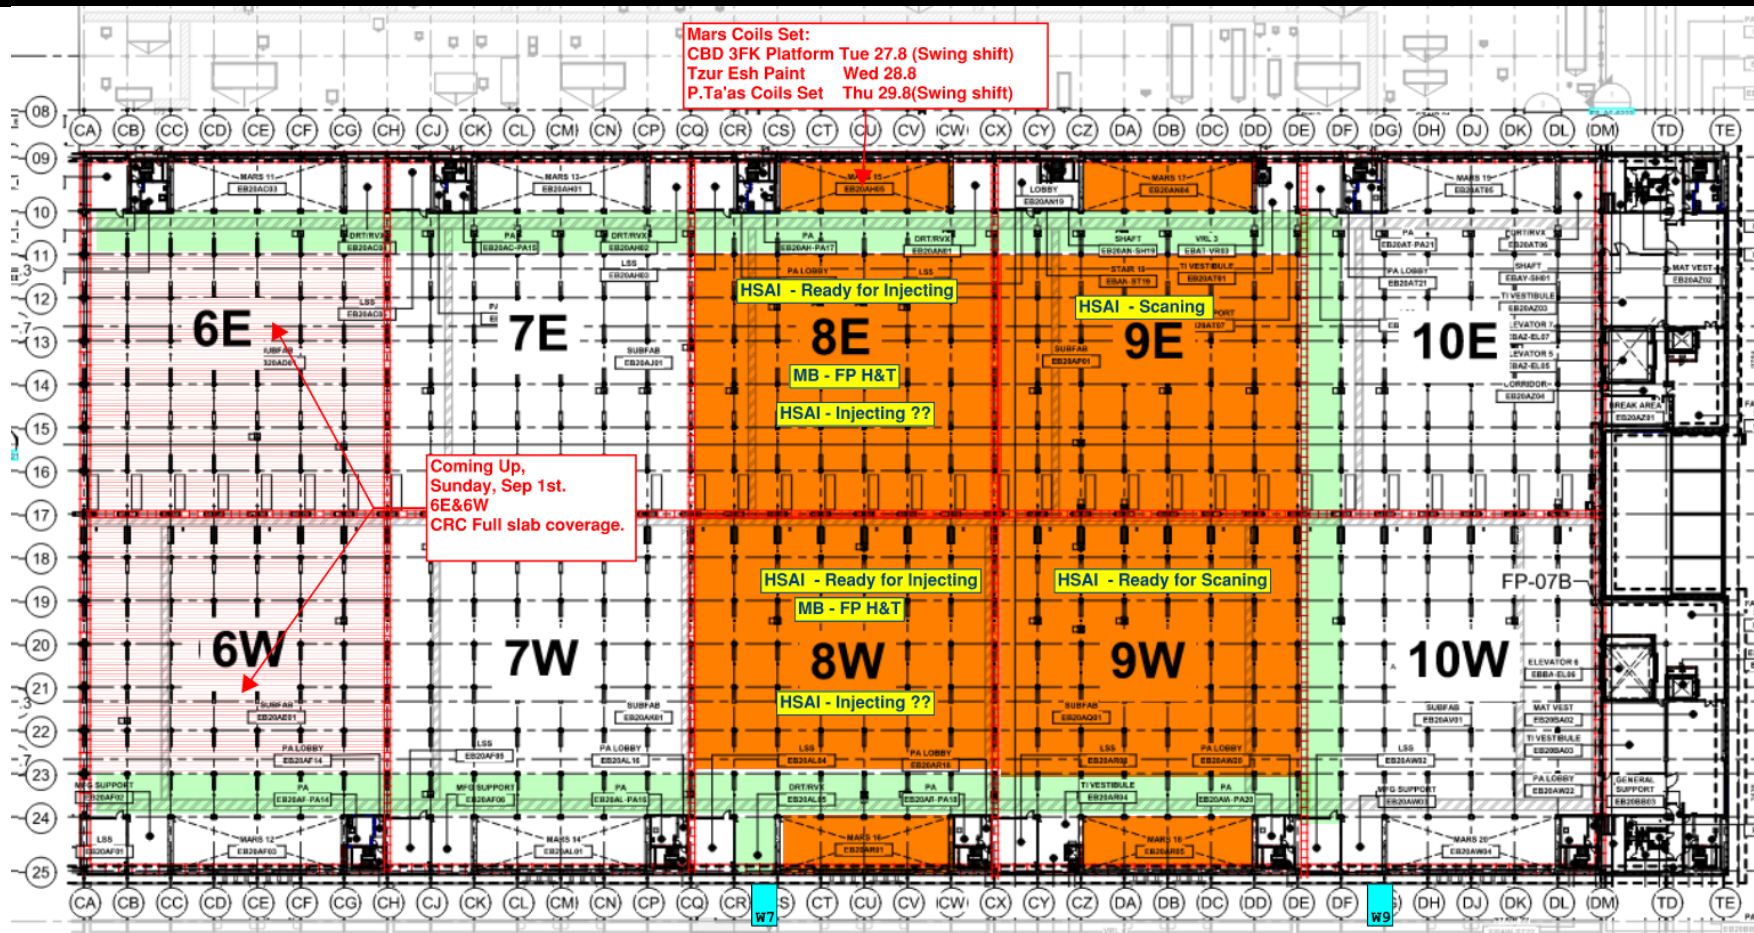

SUBFAB CRC TOPCOAT

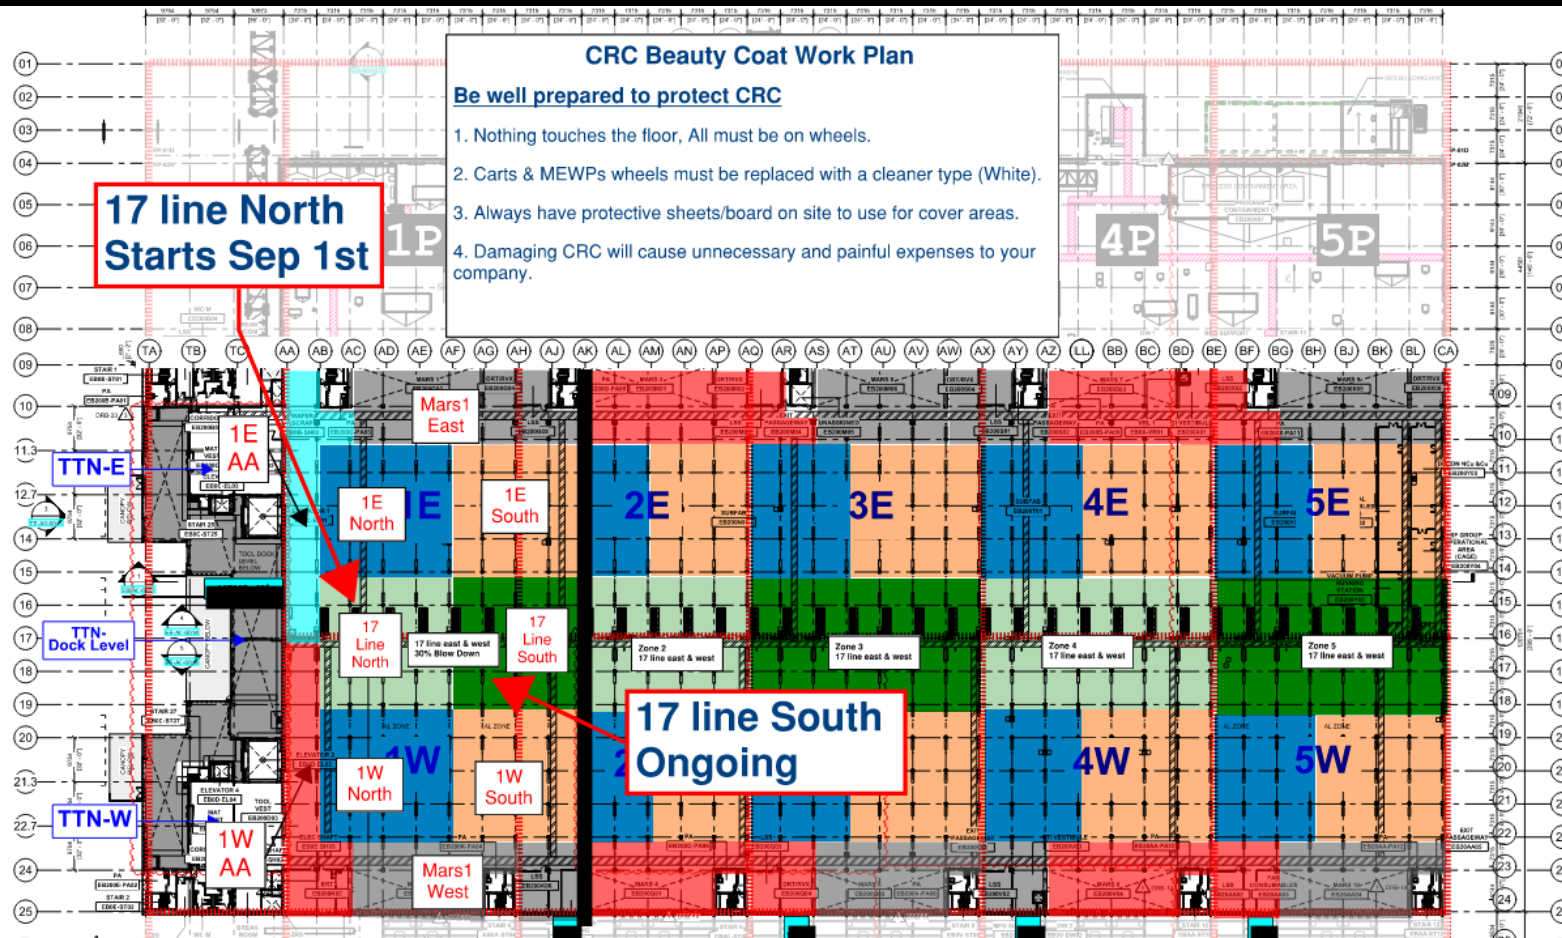



NTTE/W

WW/SN - west side welding tabs and replacing beams
Elram - East/West floor done QA/QC
SK - east side pipes needs to be completed
HYG - East to finish steel.
West receiving material

Belfor TA-TC line

CR level:

Afcon - Cable trays, modules and stickers 1W,2E, 2W,3E,3W
MB- 1E drops, 1W drops. 2E- drops
Elram - 10, 24 columns/shaft walls. AA line column wraps
WW/JS - 17-18 line added beams+ AS south stocker beams
Meptagon - I&C 1E
D&P - Ceiling rods 1E, 5E blades install.
Tzur-esh - 24-25 lines. 4E-4W blades
HYG- 5W Litho crane steel
PT - Duct prep for test AA-AH east
Talat- 1W holes drilling

CRC AA-AK/12-17 ongoing

Sela: Shot blast

WW36 moving to 1W

2E

3E

4E

5E

F B BALLROOM

1W

2W

3W


4W


5W


Link


RP - FP 5RA level

MB - Upper level fire protection piping
Pach taas - exhaust duct install and tie in

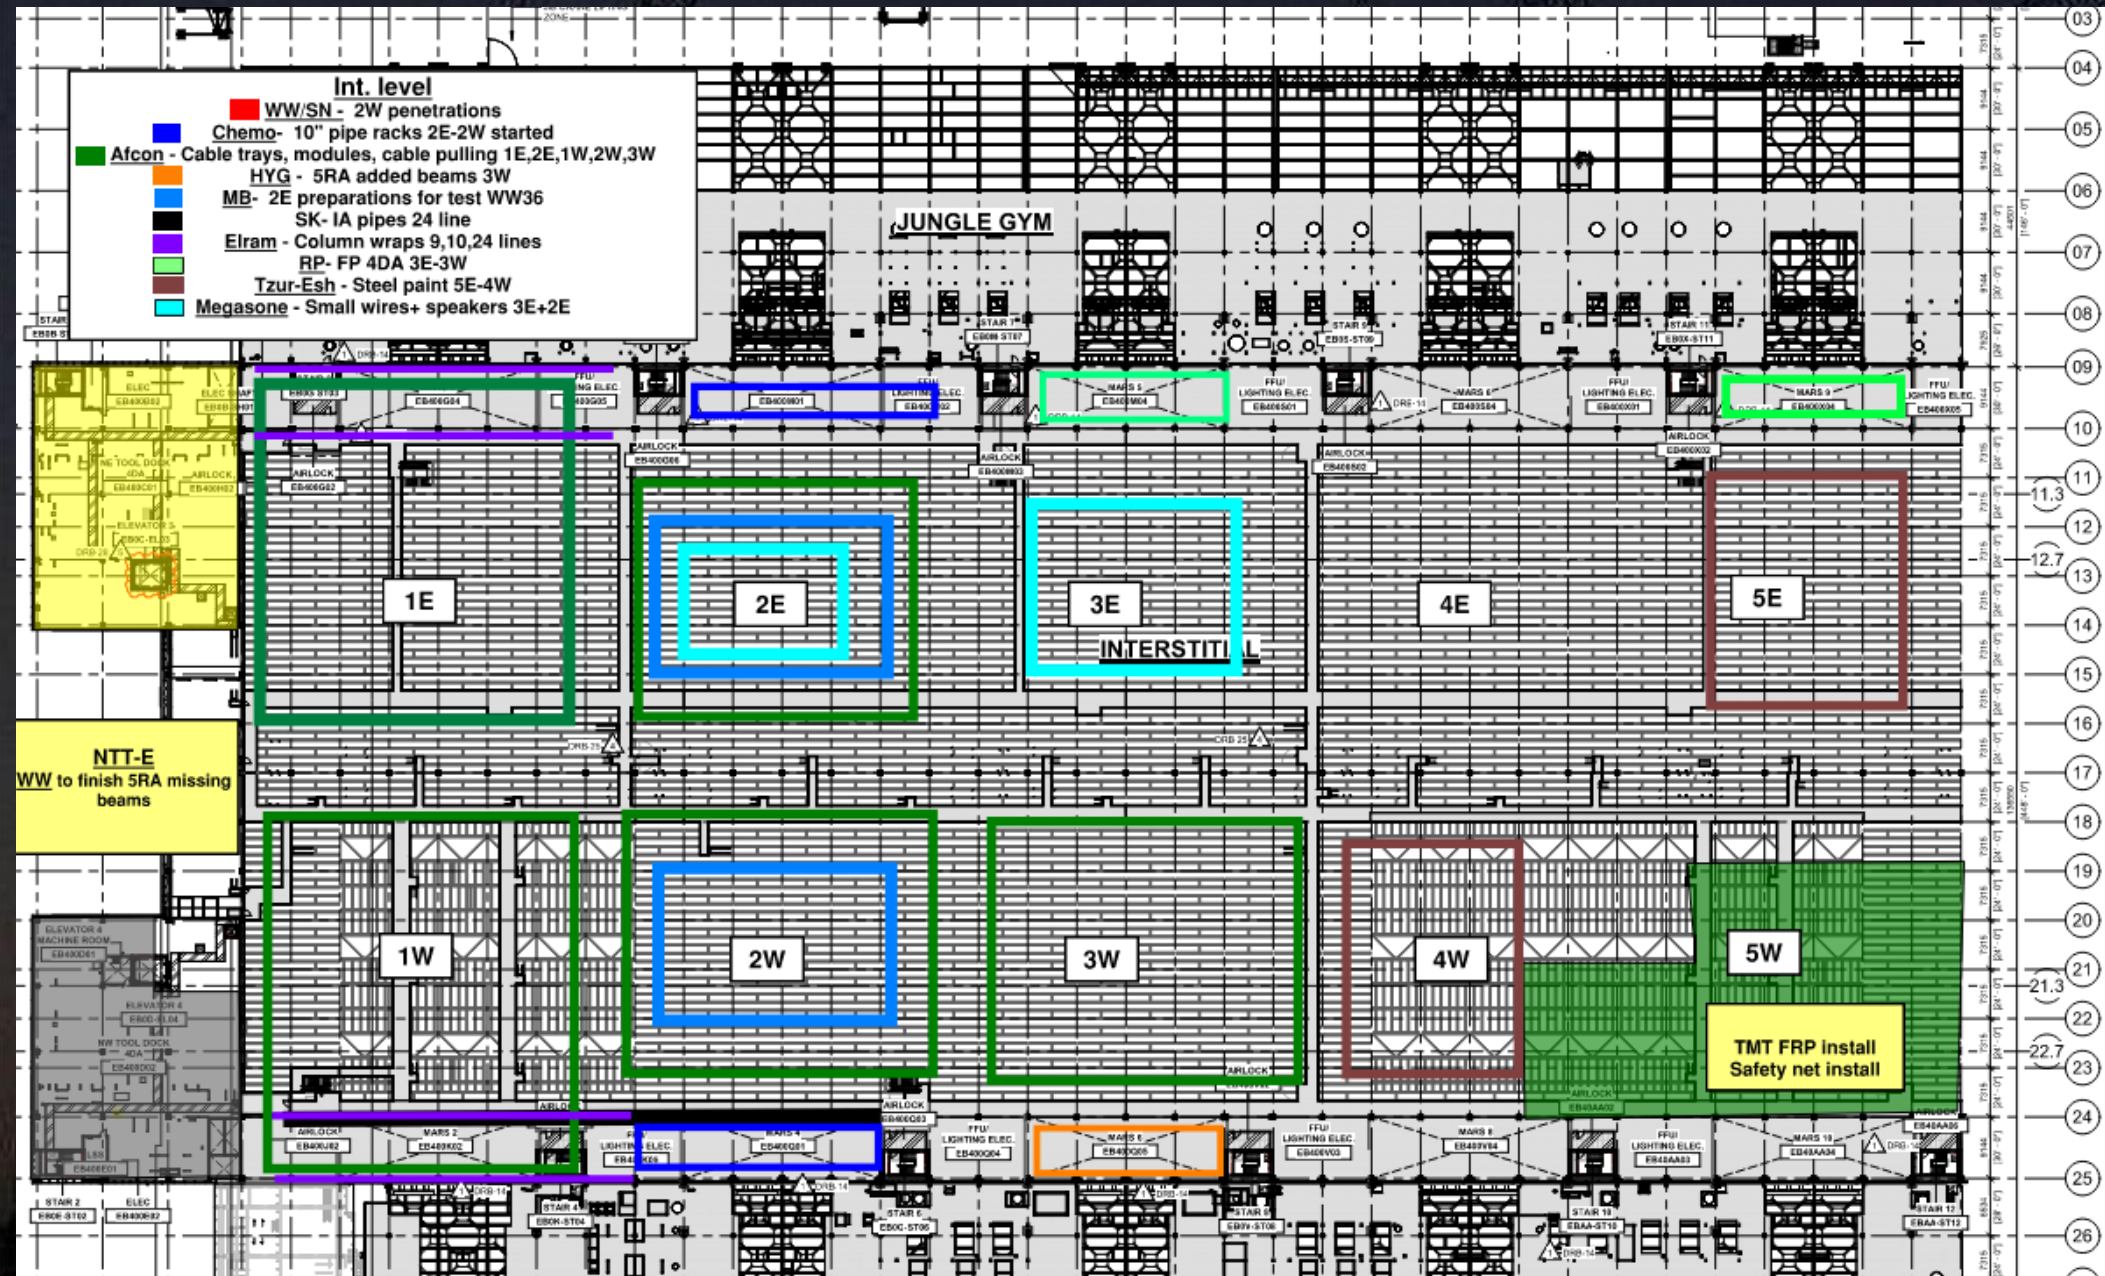


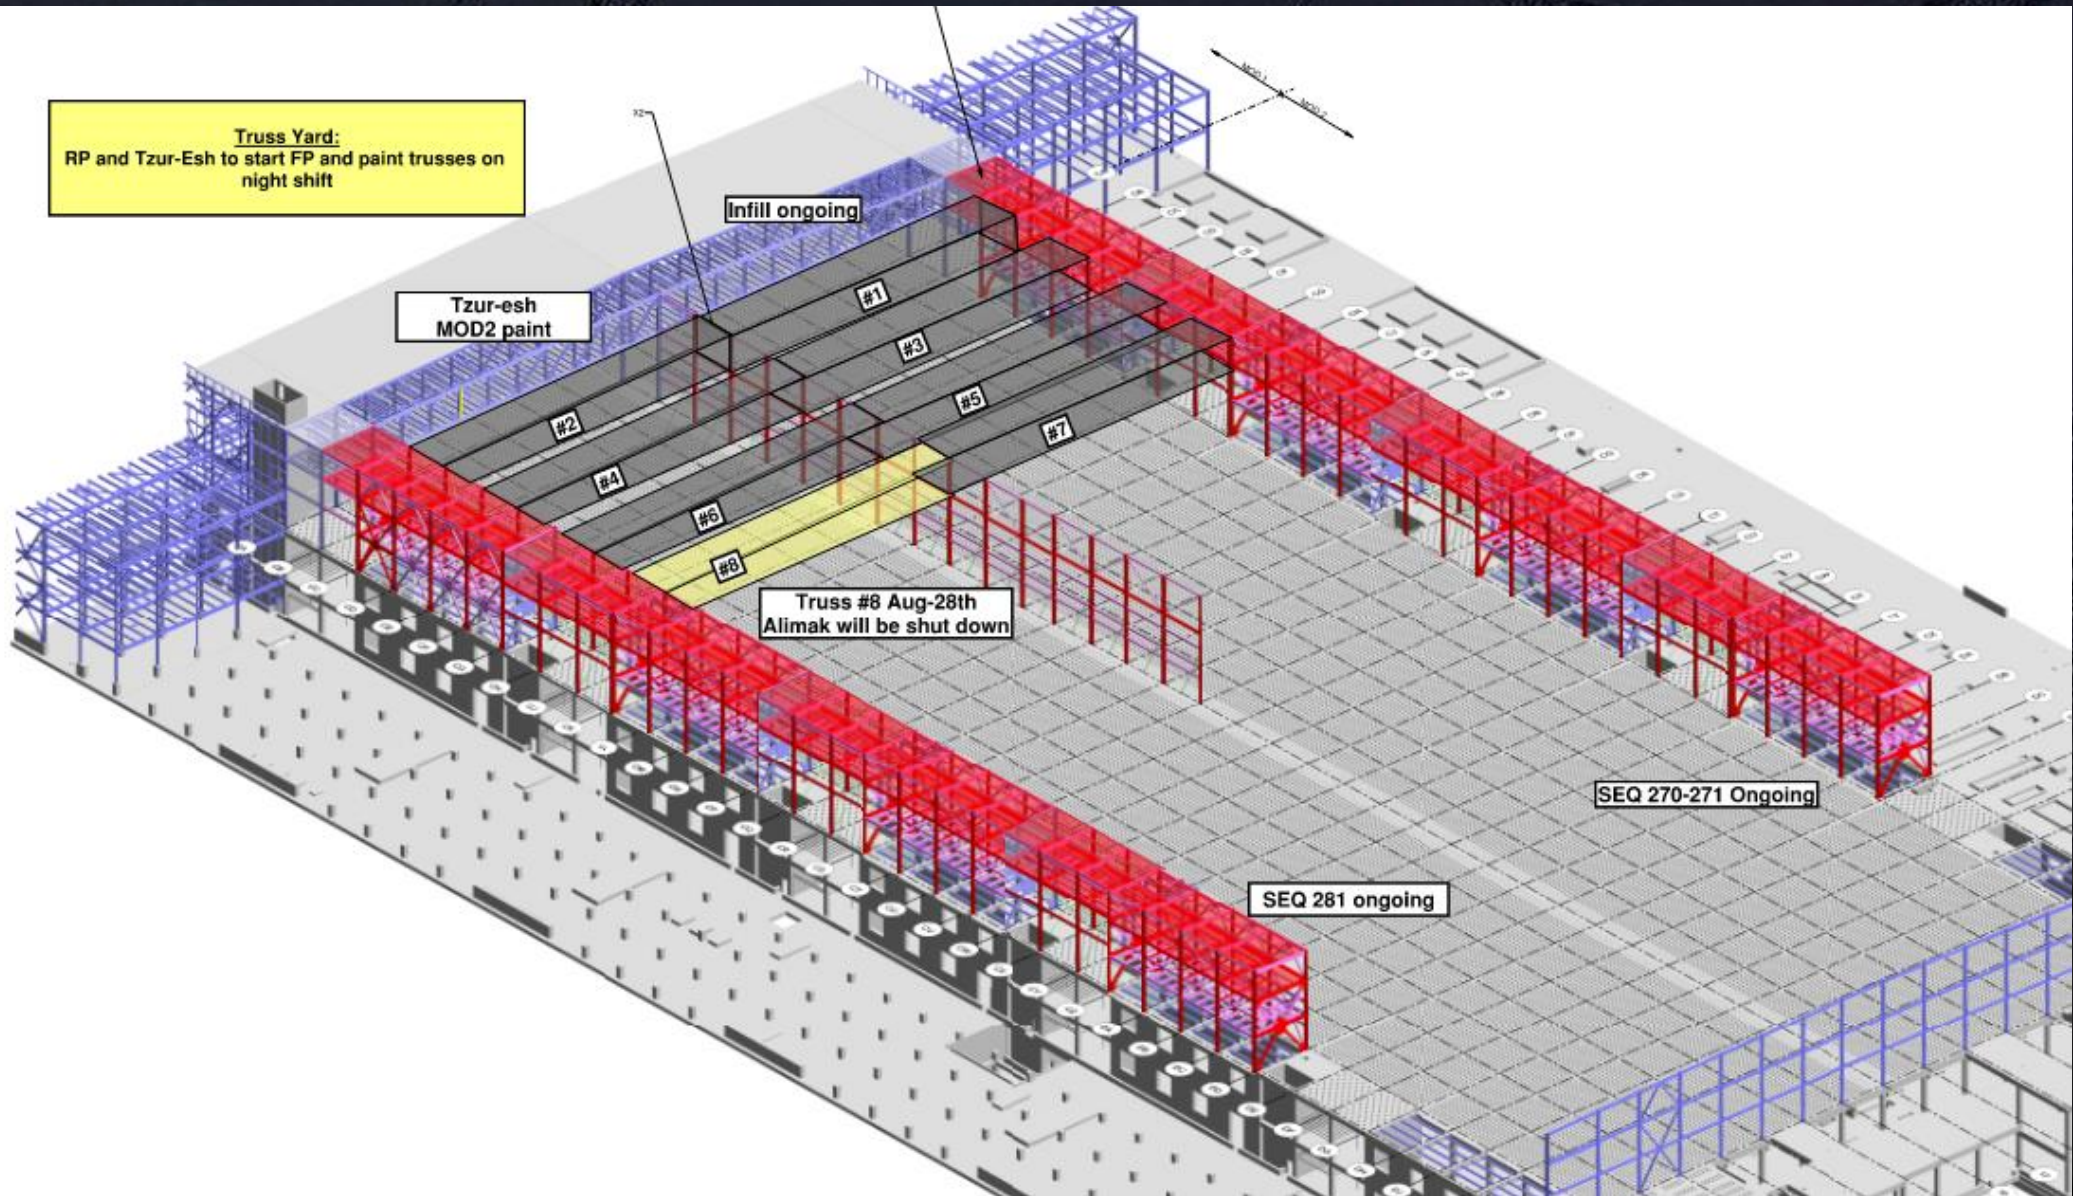


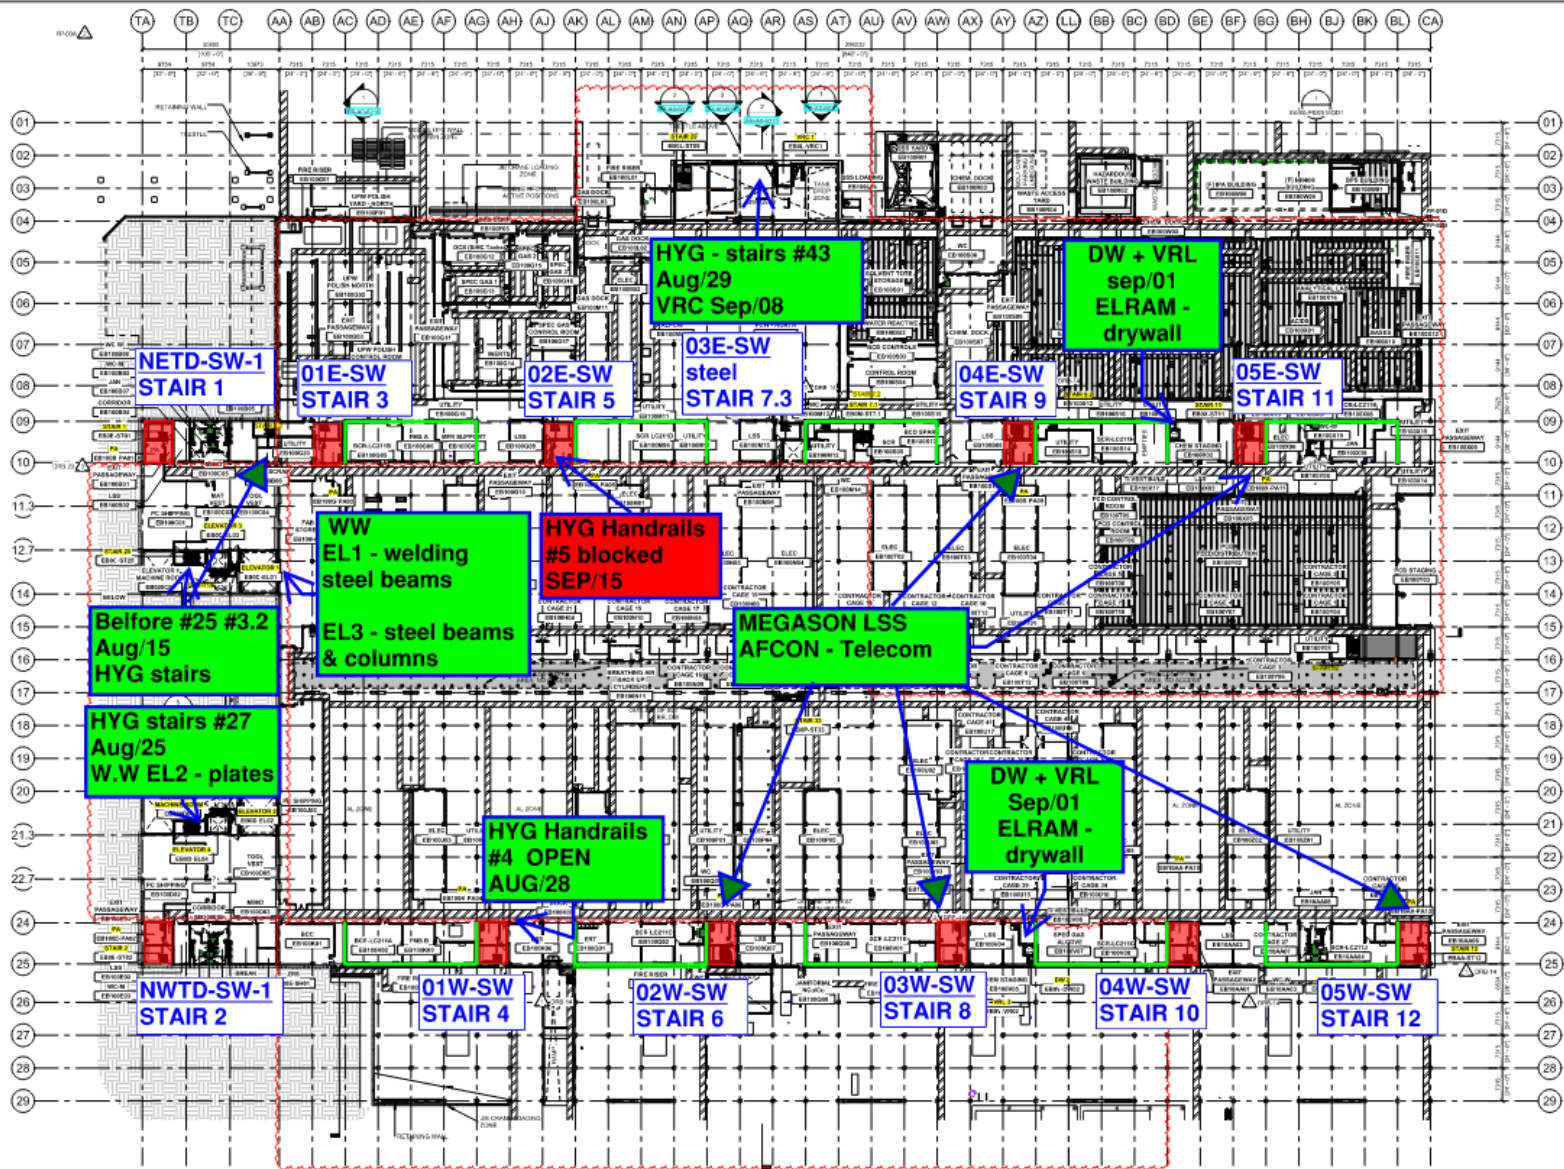

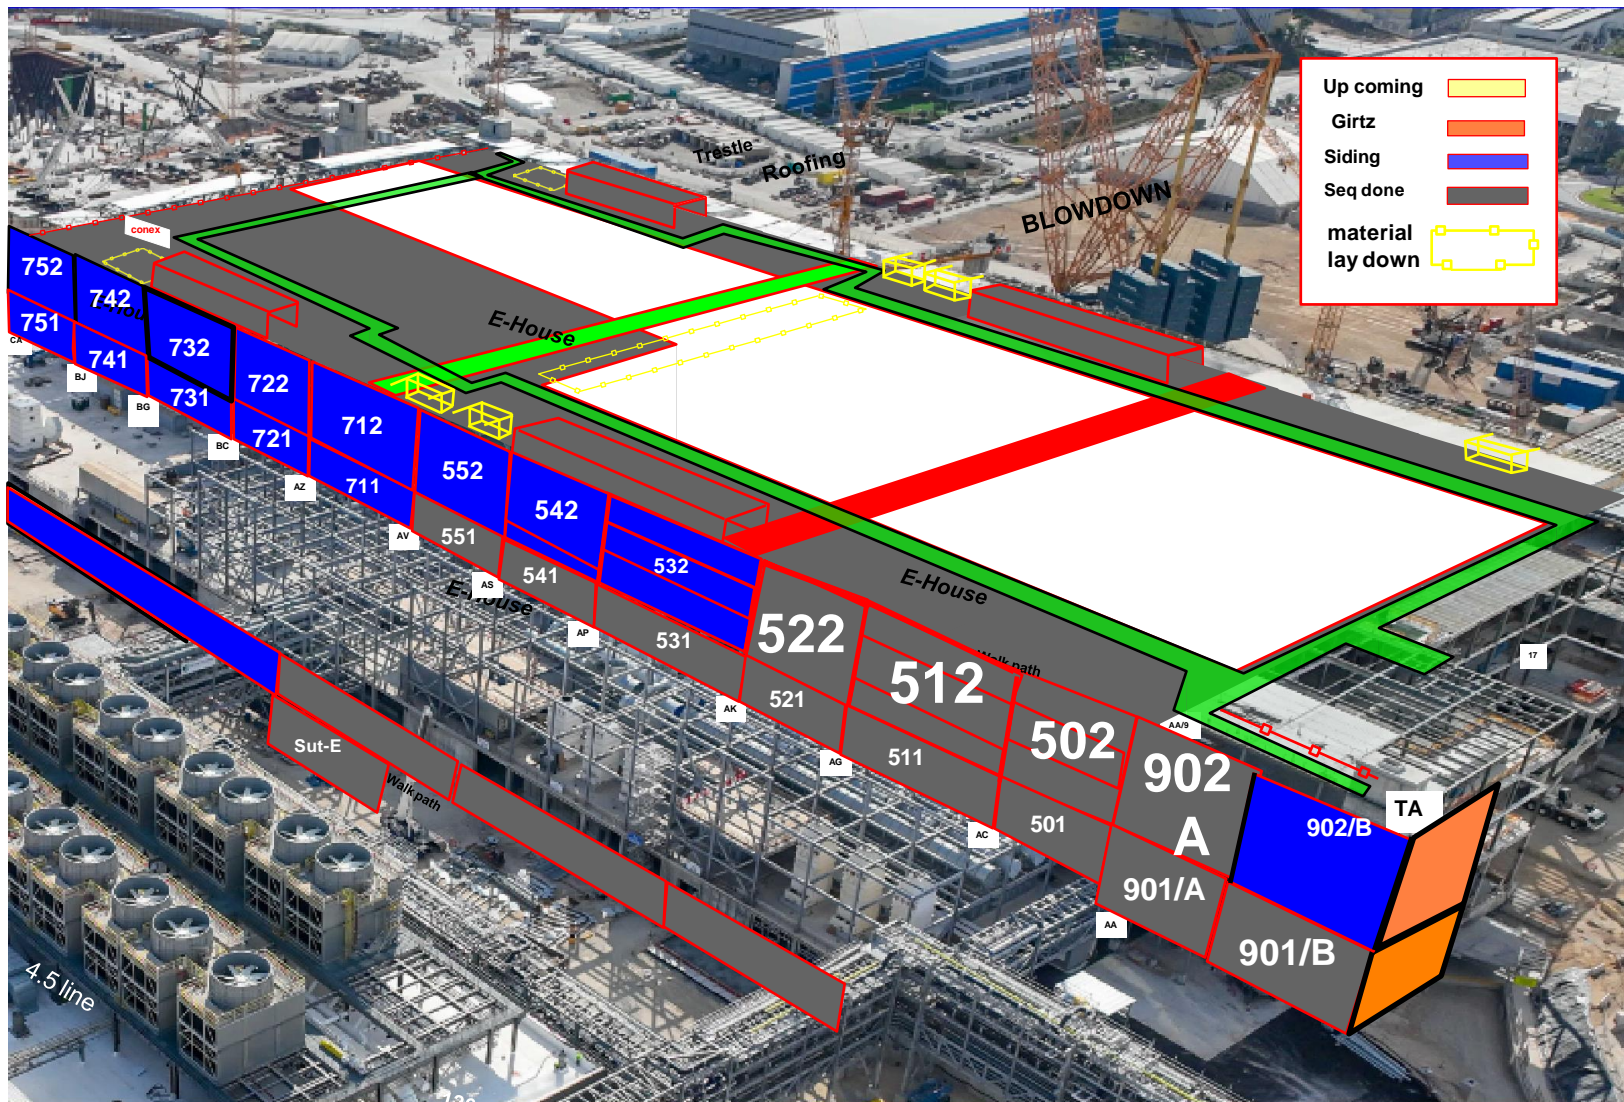

Walk path

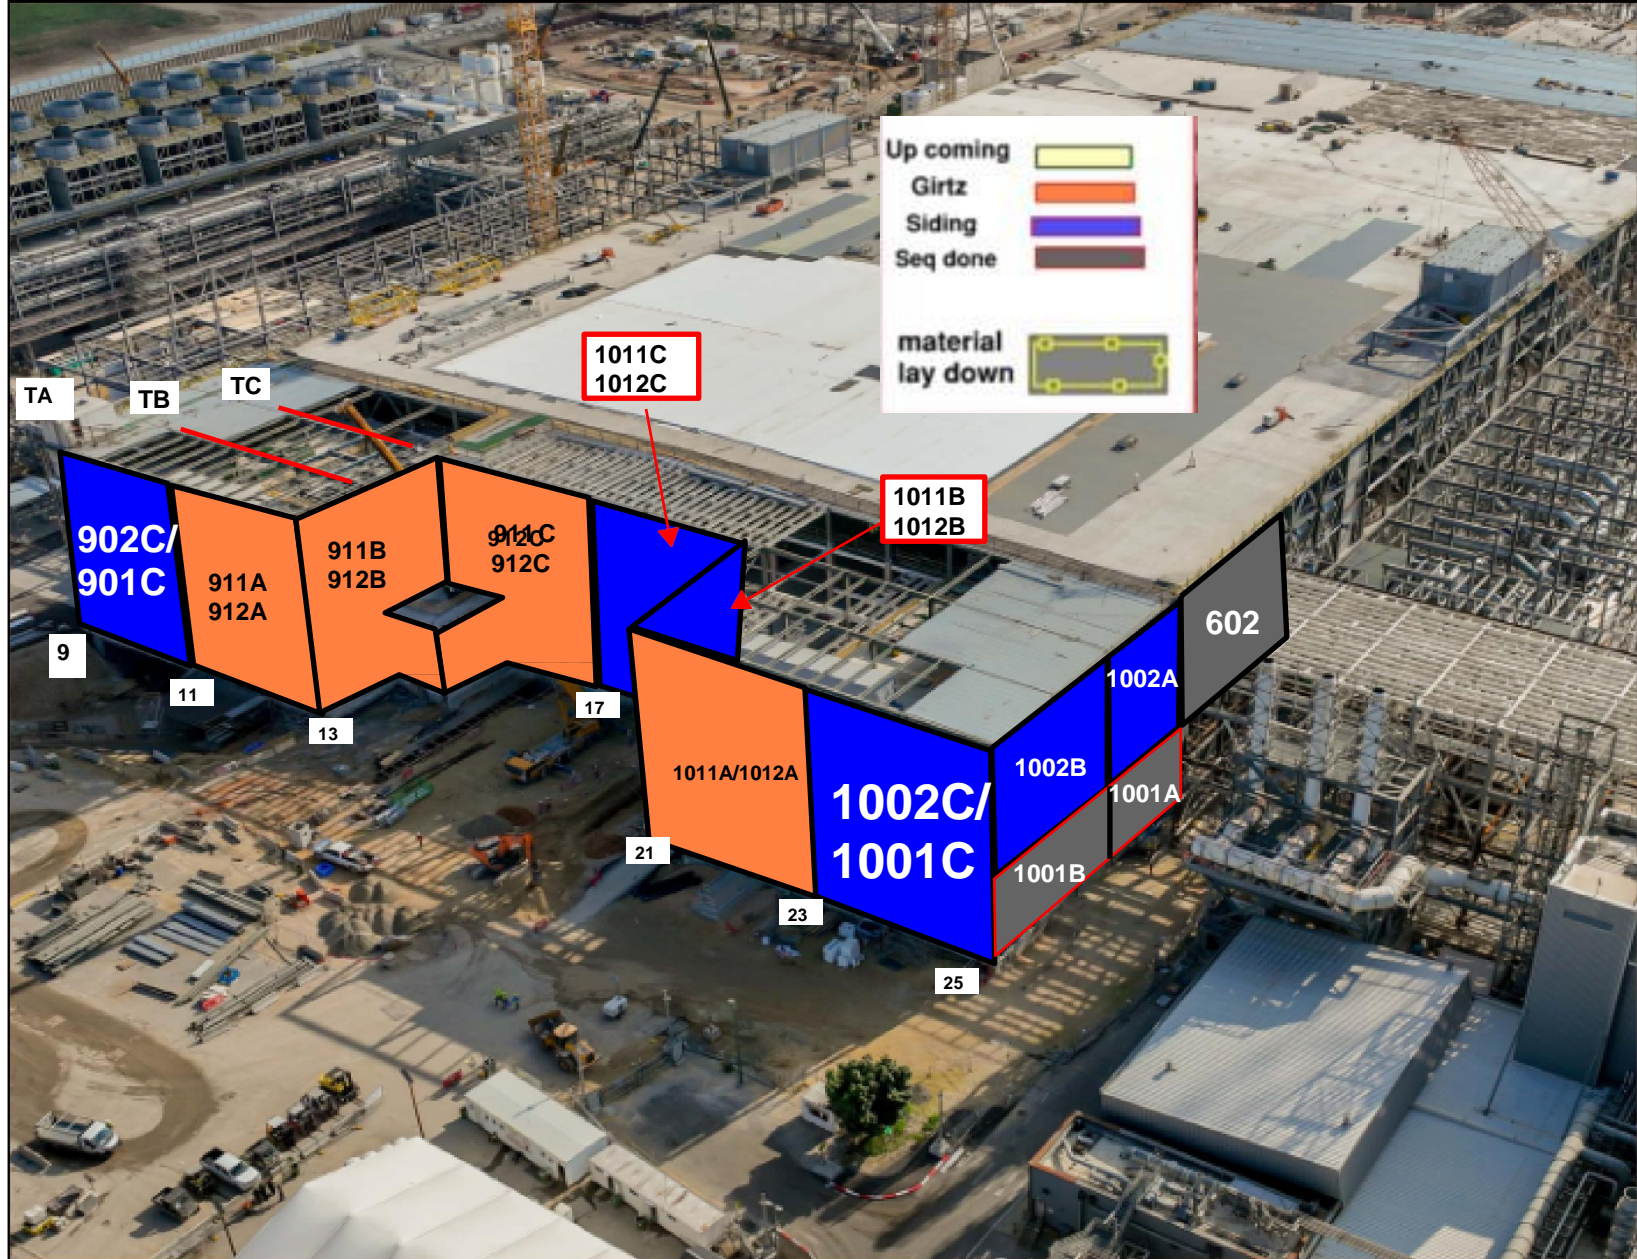

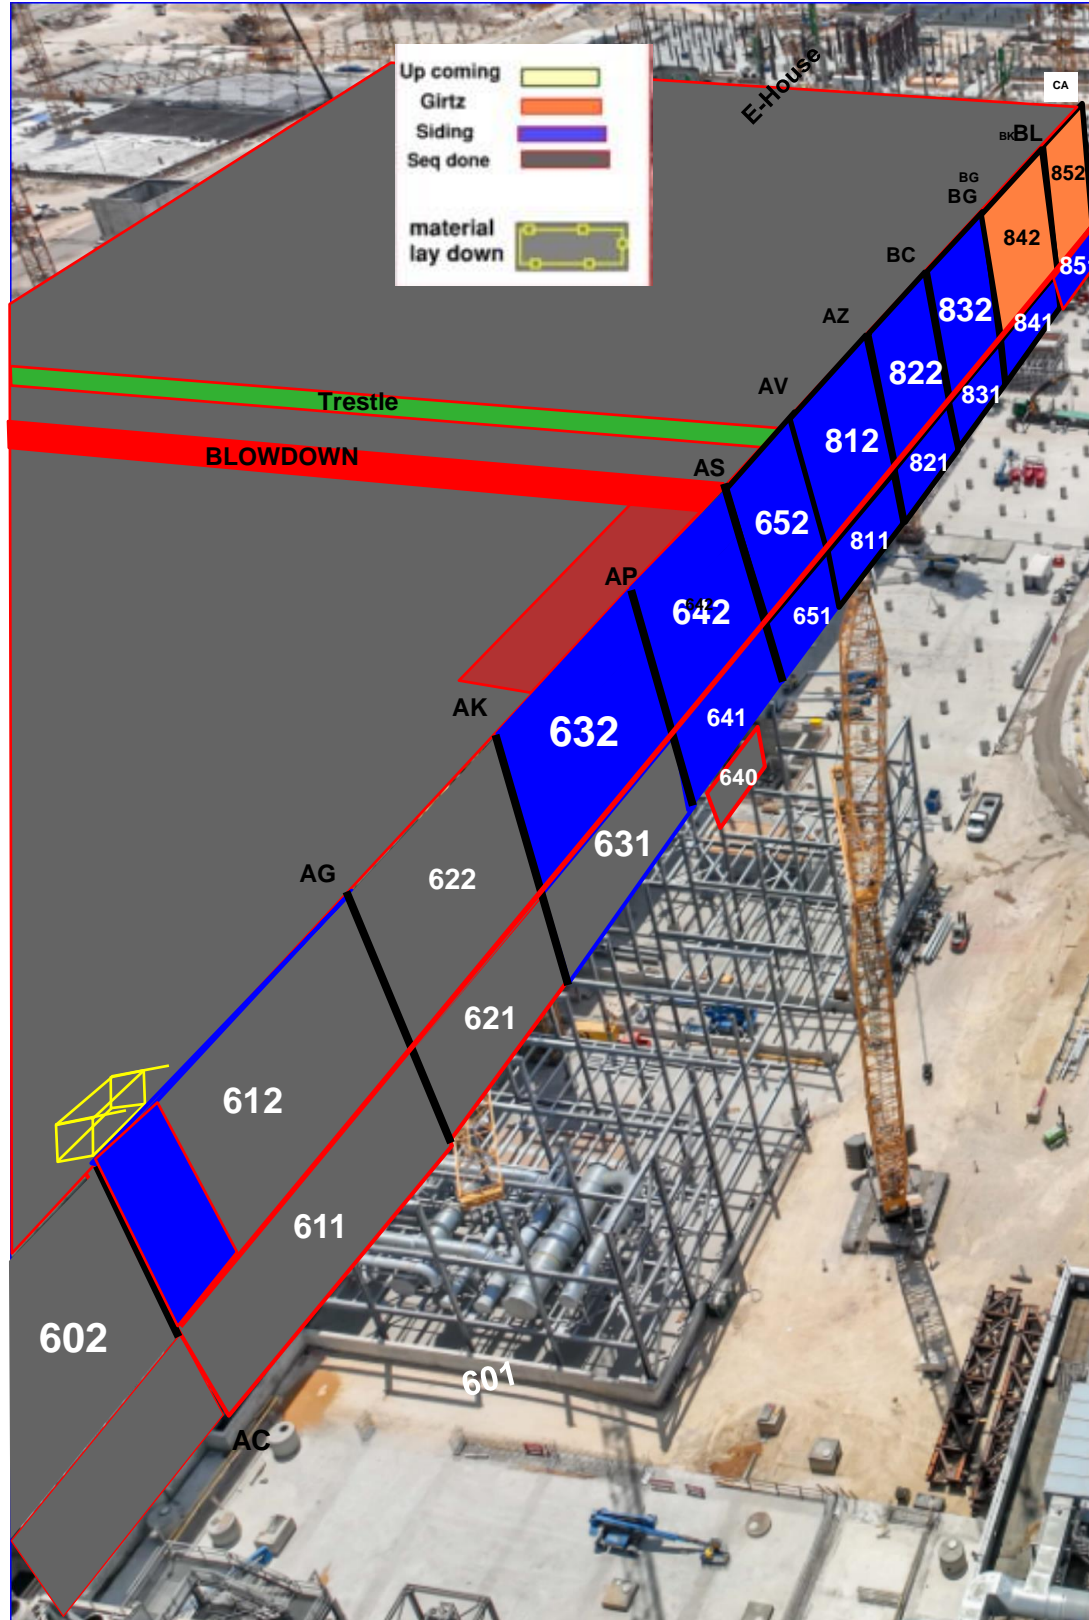

Siding - West FAB - JYG

BLOWDOWN 30%

	TA	TB	TC	RA	RB	RC	RD	RE	RF	RG	RH	RI	RJ	RK	RL	RM	RN	RO	RP	RQ	RR	RS	RT	RU	RV
	1001/1002			601/602		611/612				621/622			631/632				641/642			651/652					
Total	28	28	28	15	18	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	
Installed	8	14	18	15	18	14	31	31	31	31	31	31	38	21	24	24	13	5	5	14	5	5	5	8	
X	25X	58X	55X	100X	100X	45X	100X	100X	100X	100X	100X	100X	97X	68X	77X	77X	42X	19X	19X	45X	19X	19X	19X	8X	
SRA																									
KDA																									
SPK																									
SPR																									
25A SP																									
UL																									


Link

Siding - East FAB - PSSS


BLOWDOWN 30

[illegible]

PSSS-UL

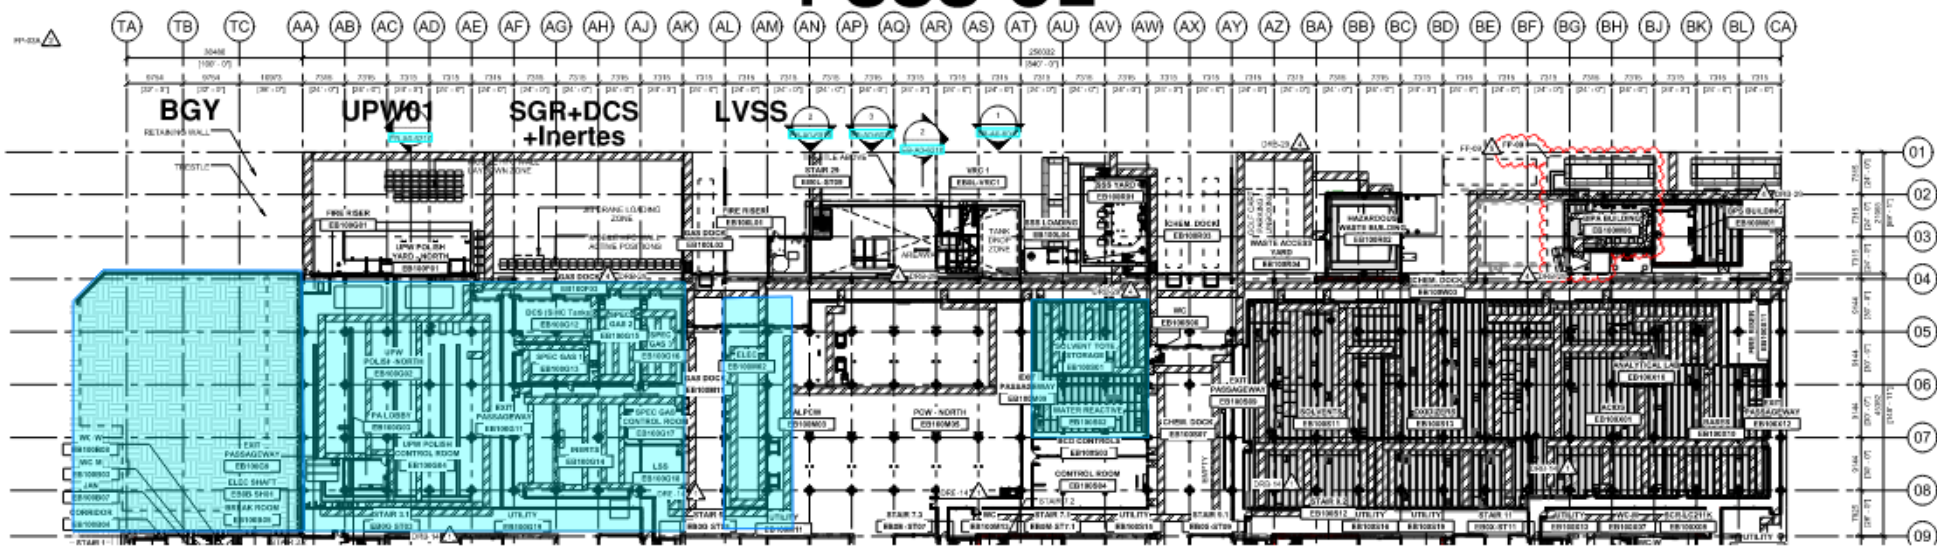


PSSS-Roof(MOD01)

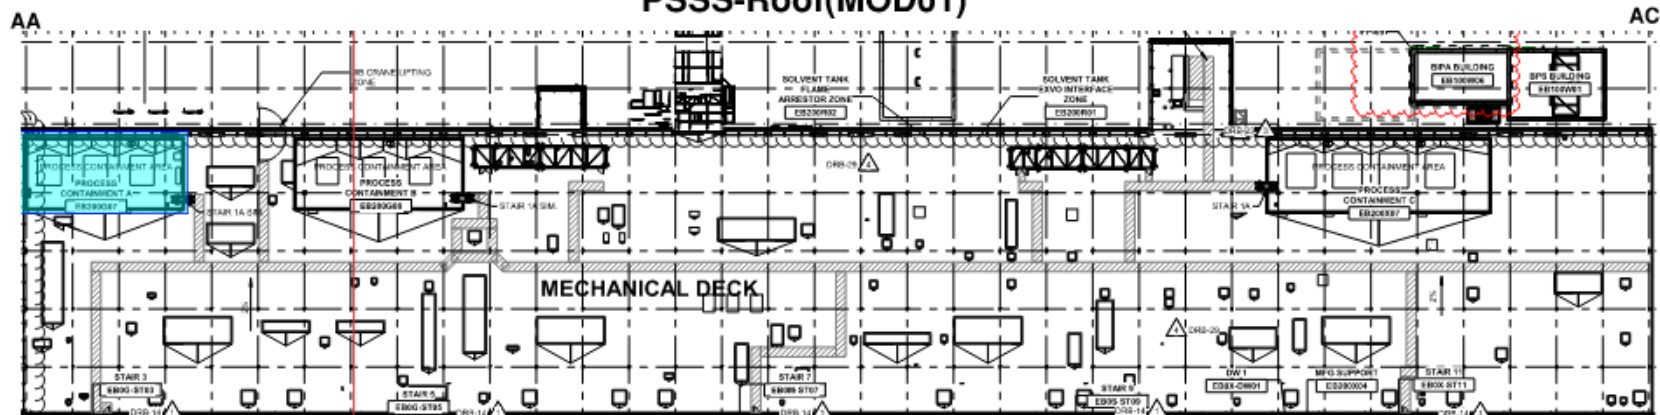

PSSS.2


10P

Utility Level 1YA

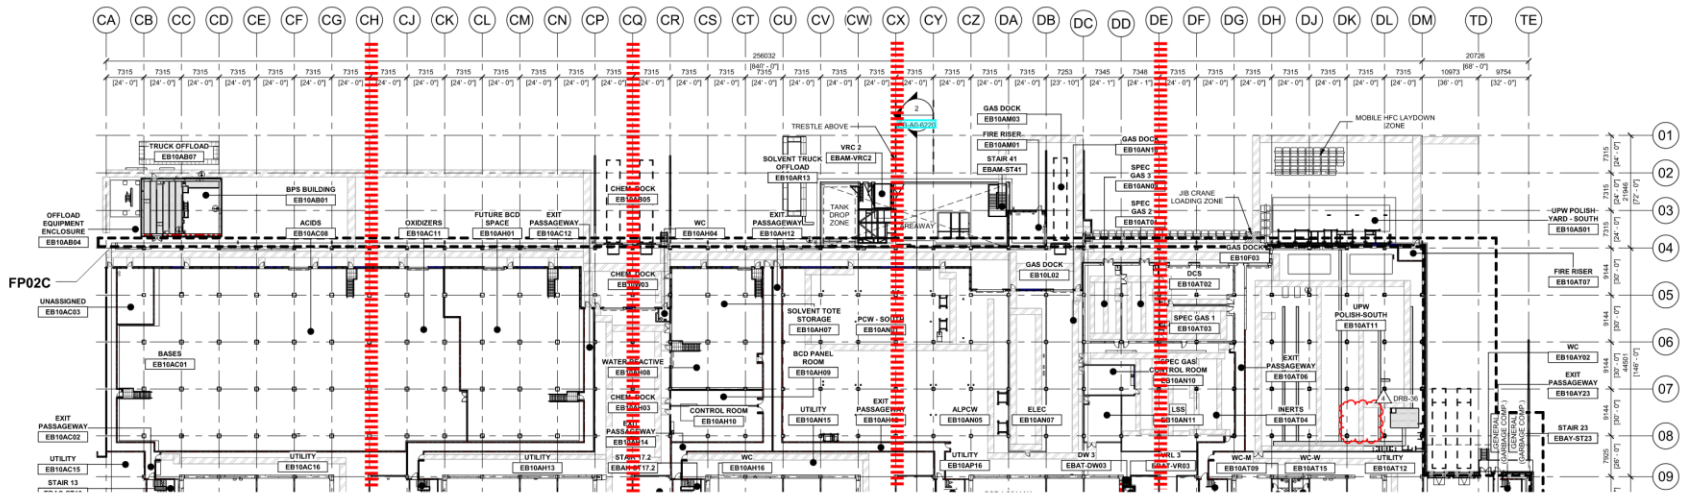


PSSS Roof 2SA

AHU Delivery 08/06

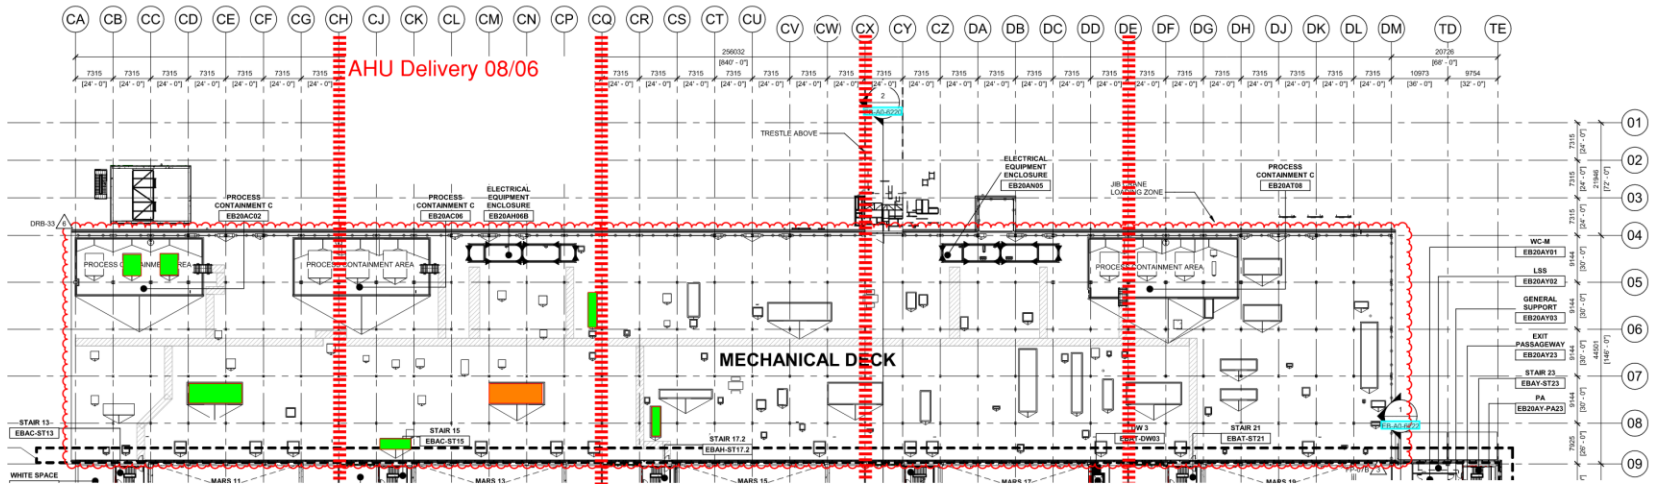



WJG 01J, 02J LIFT 2 & 3

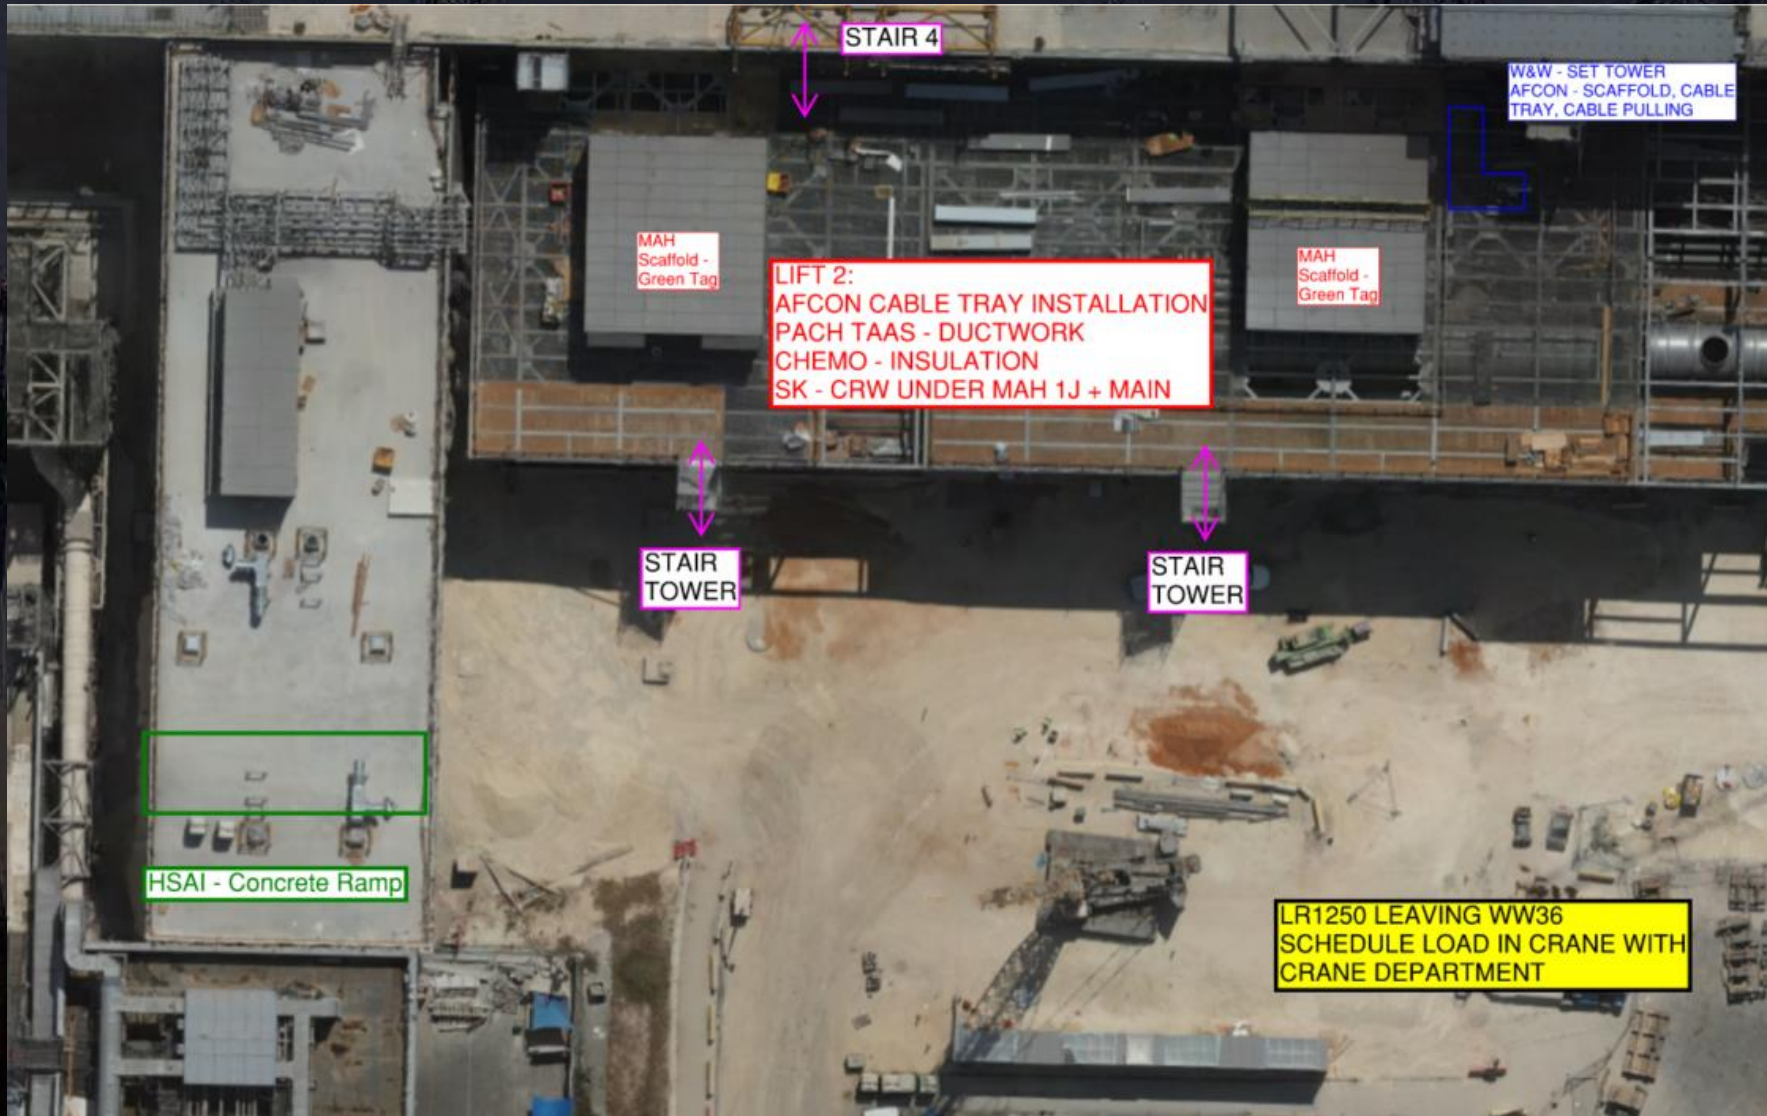






WJG 03J, 04J, 05J LIFT 2 & 3





[illegible]

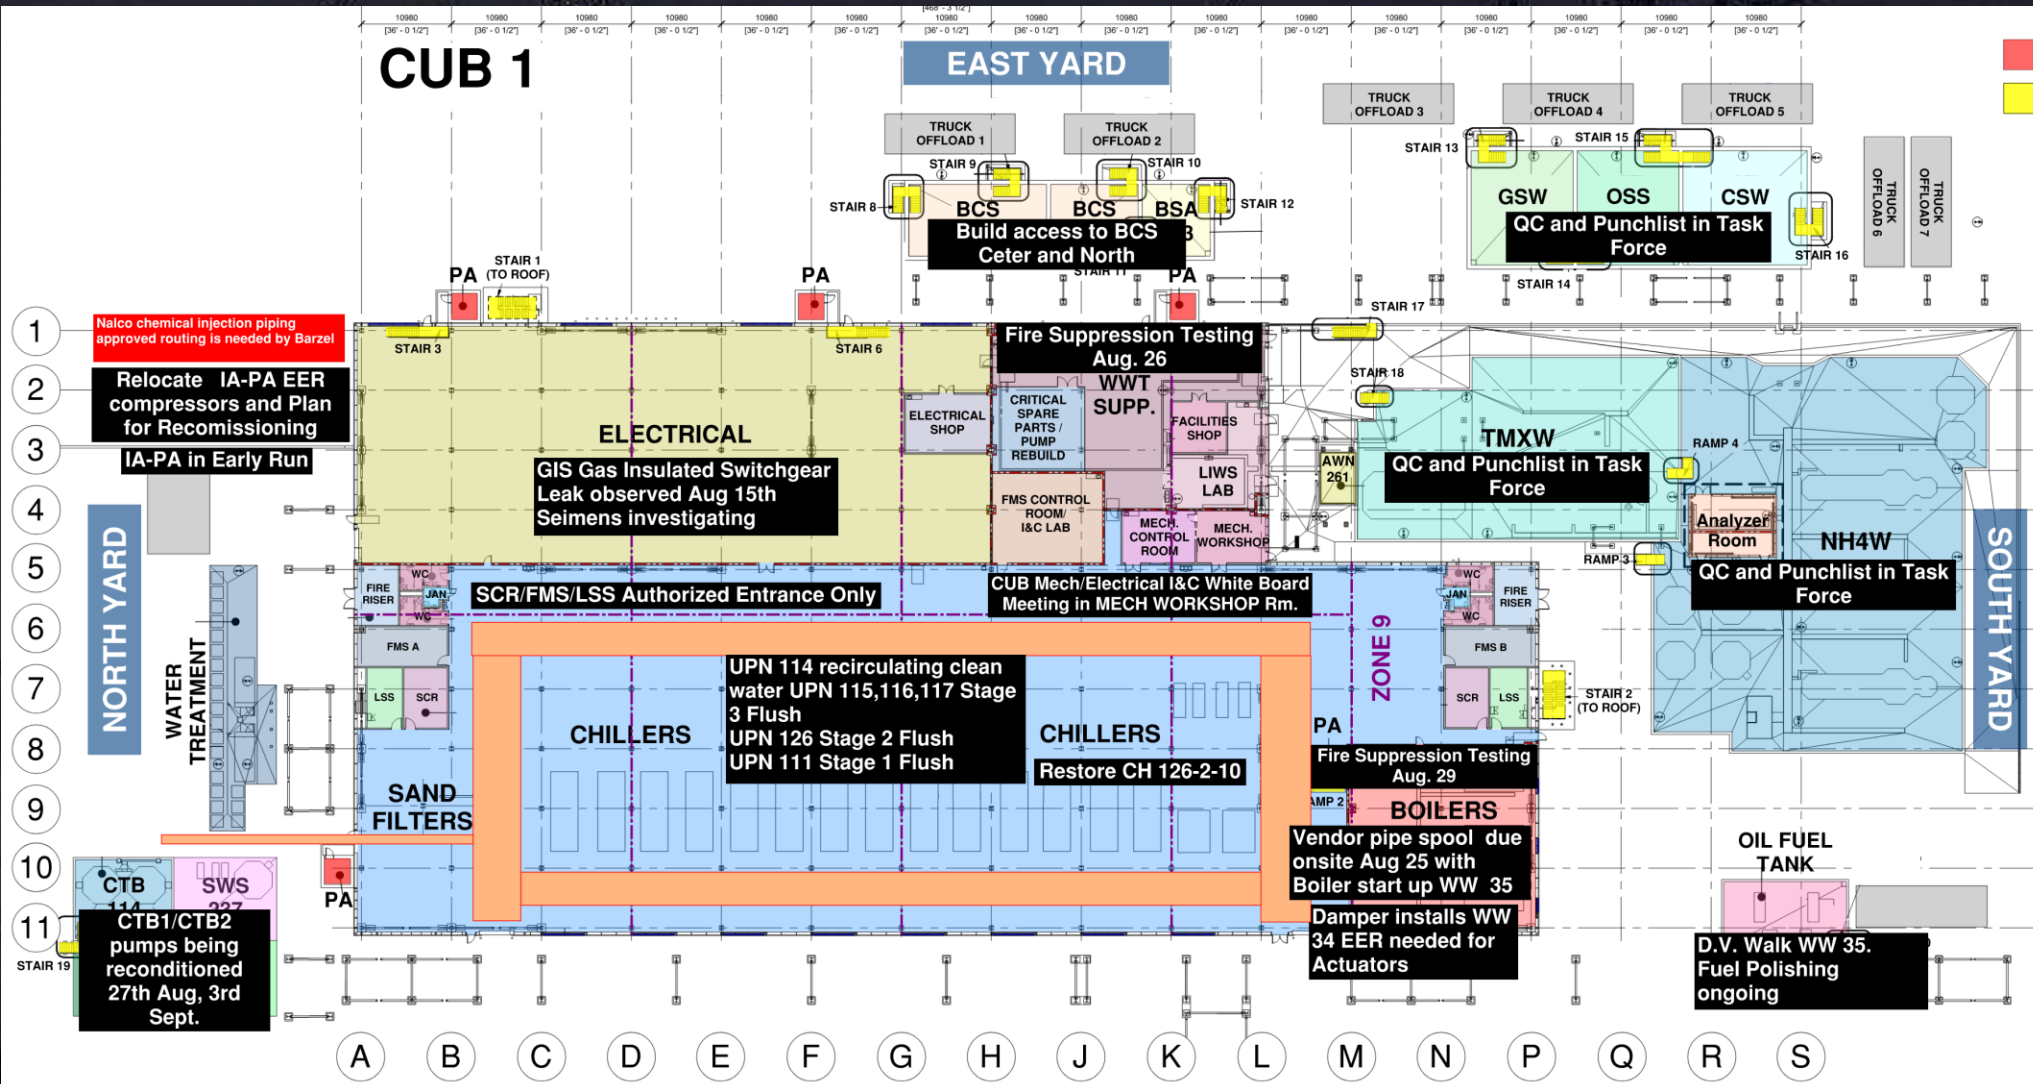


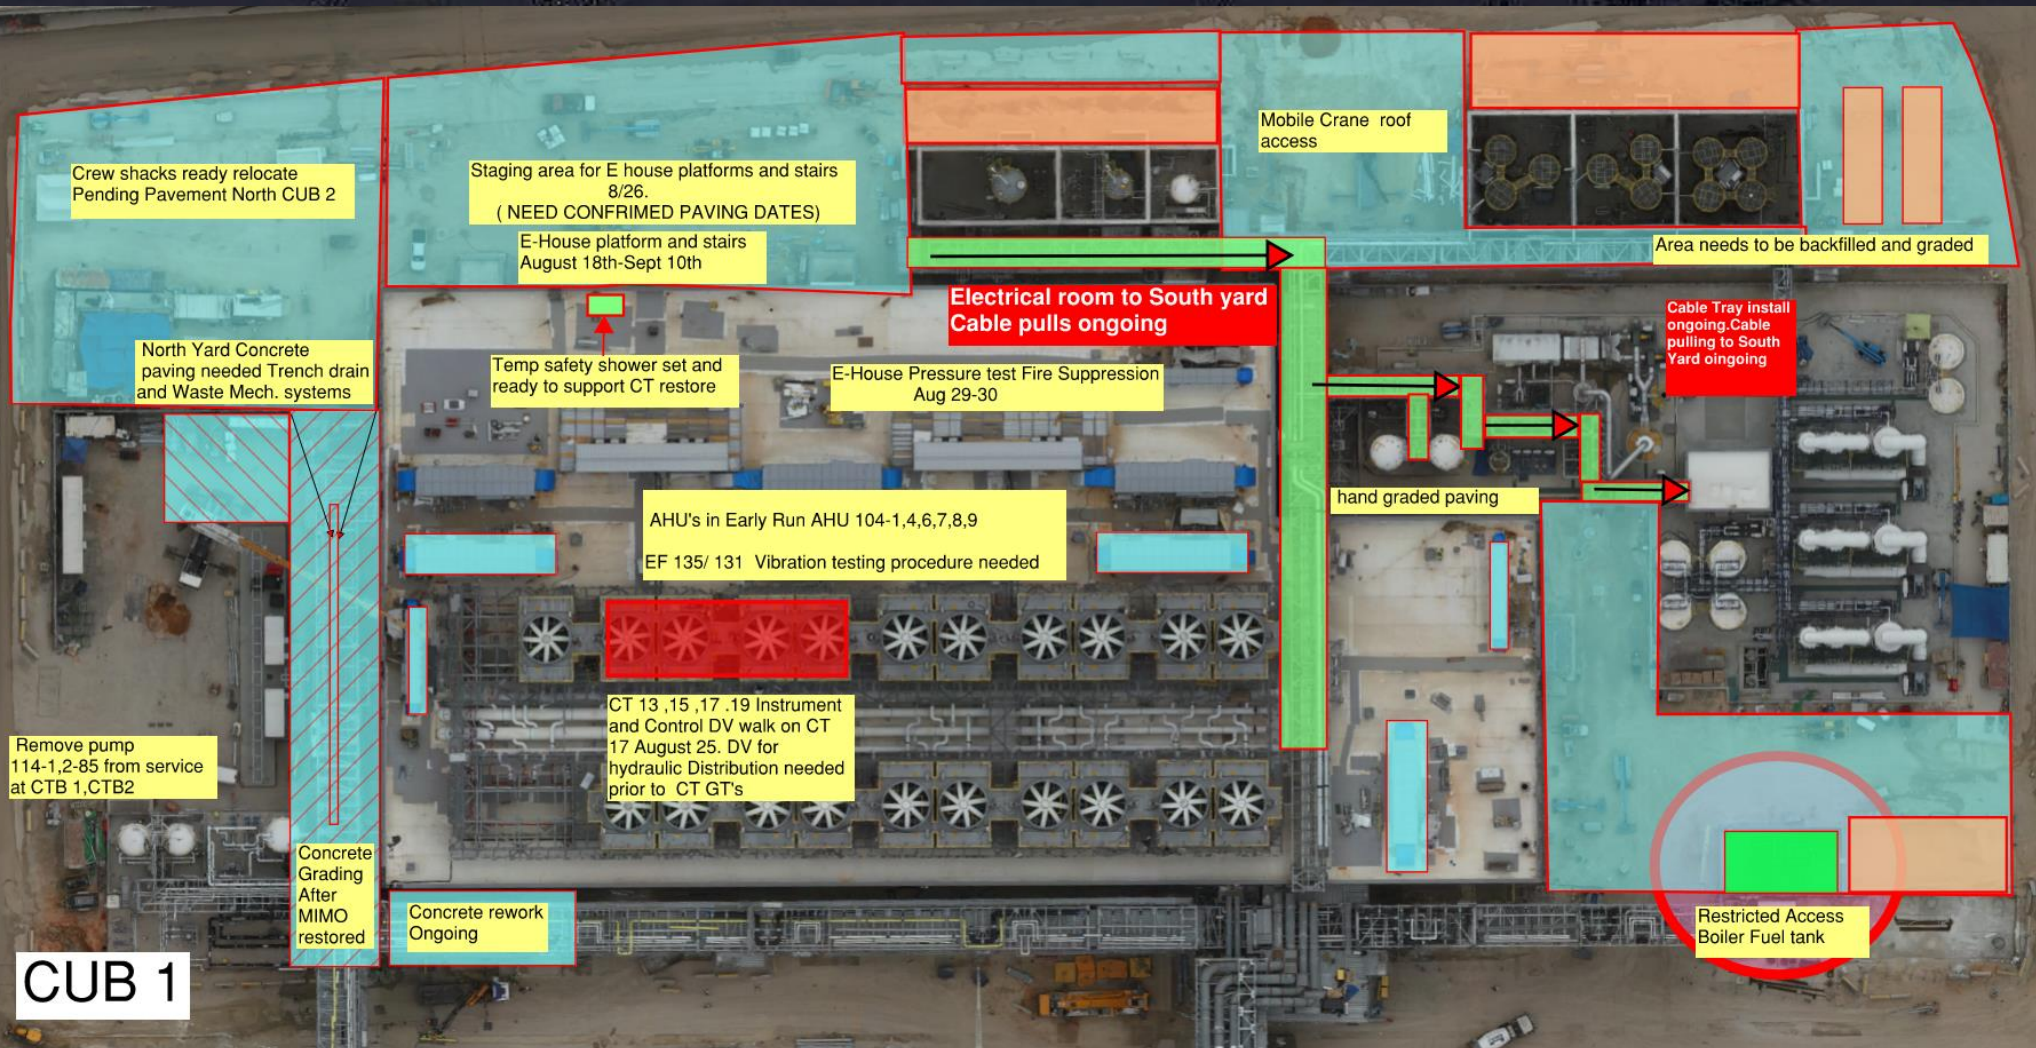

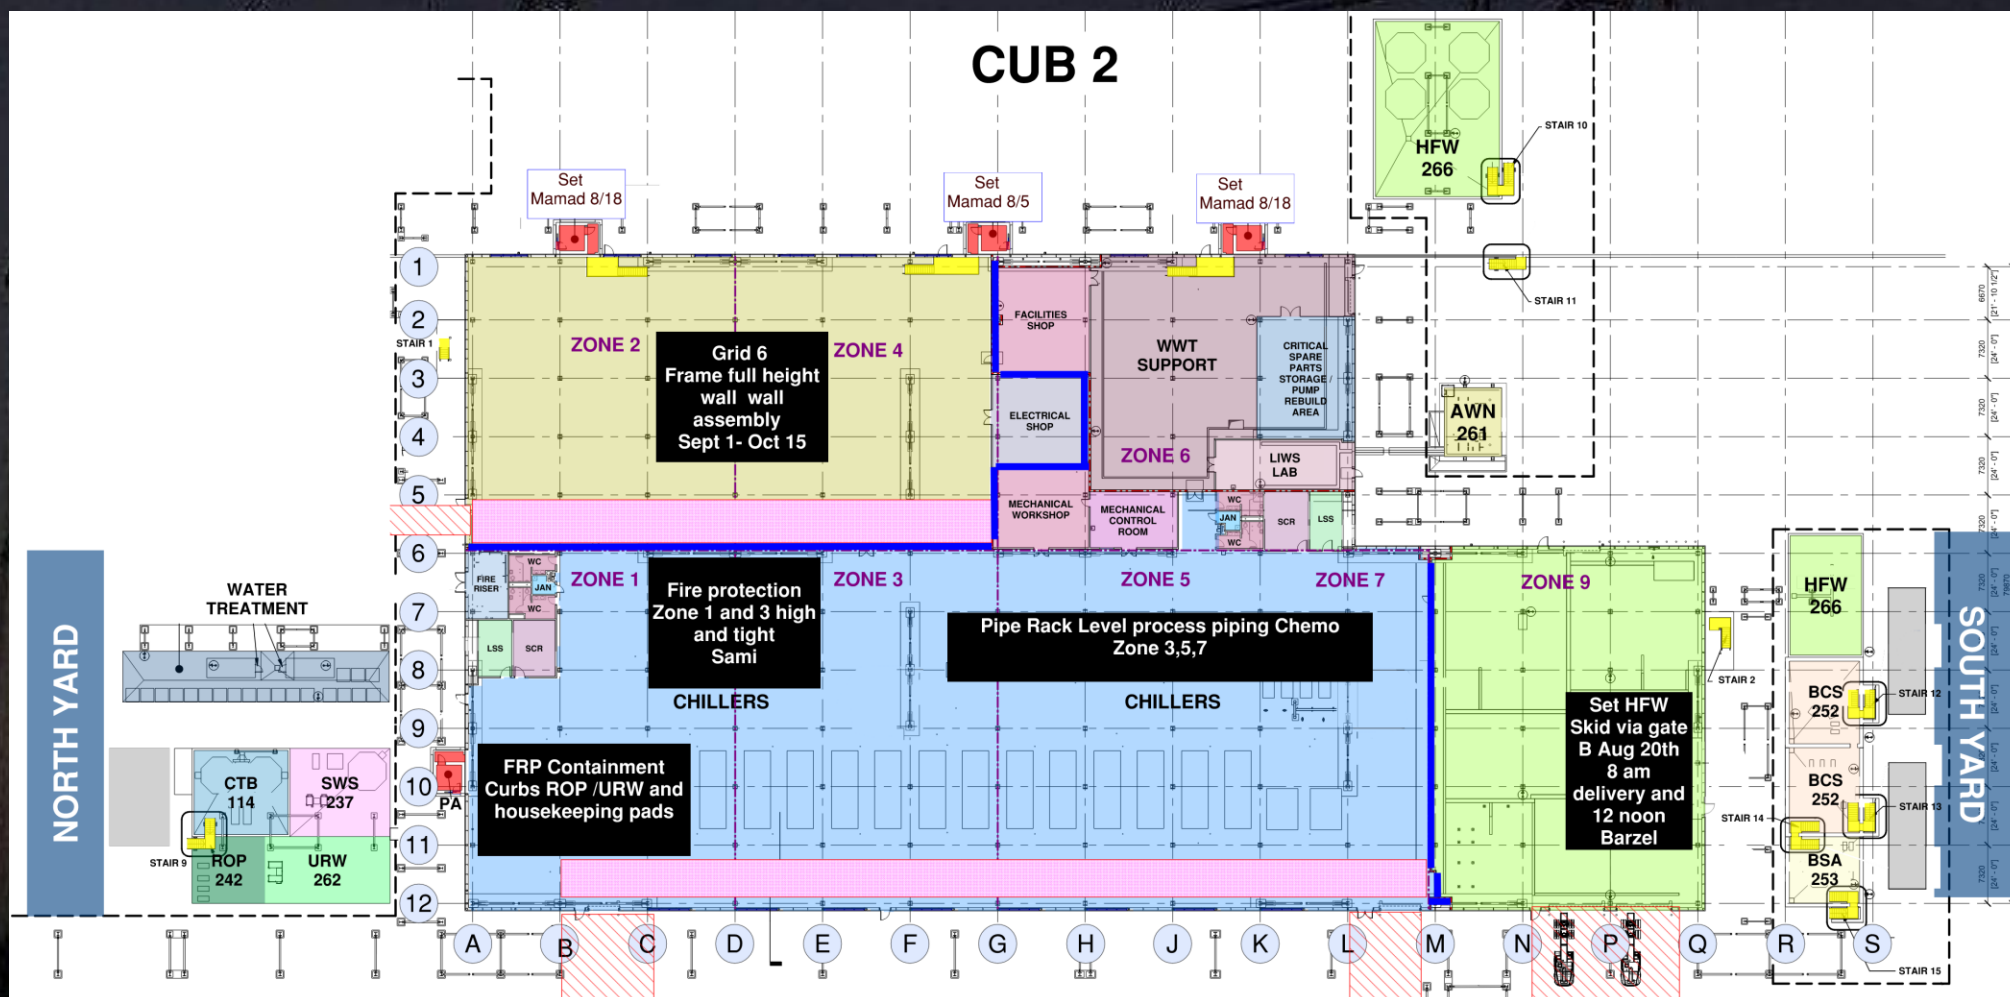

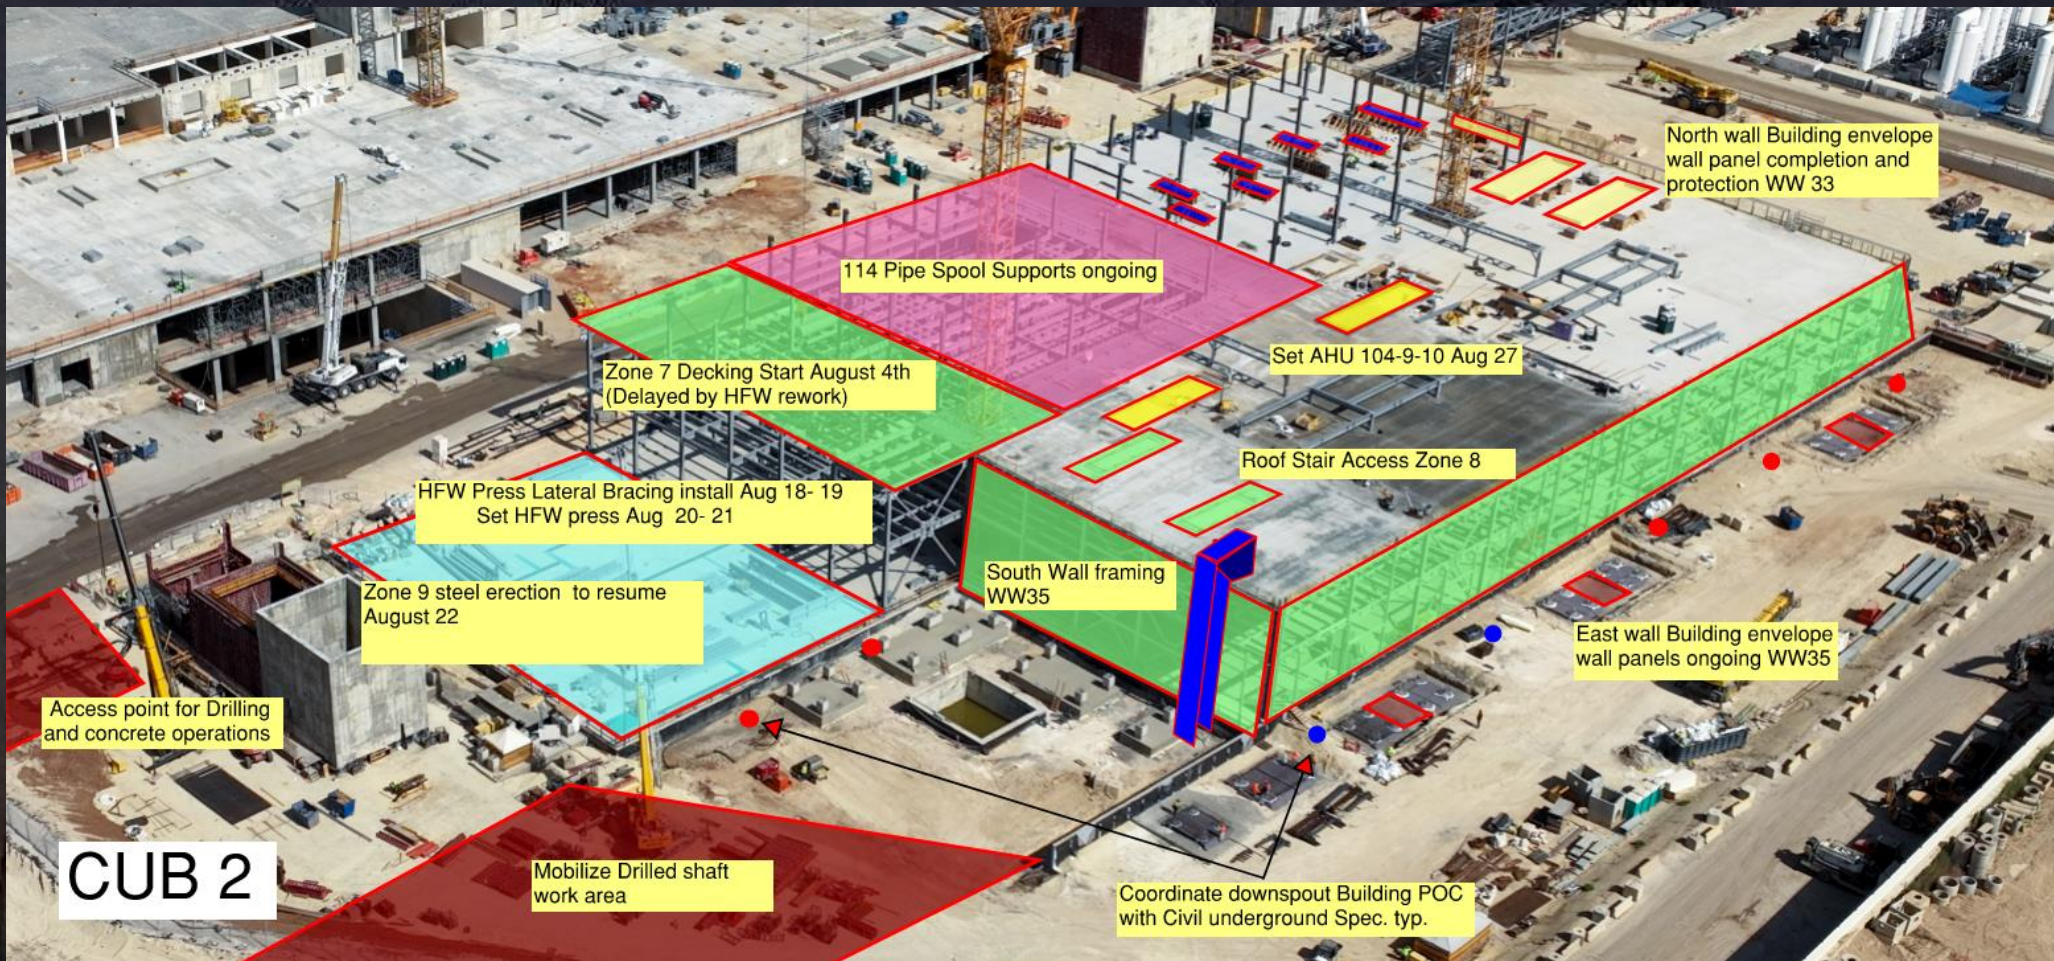


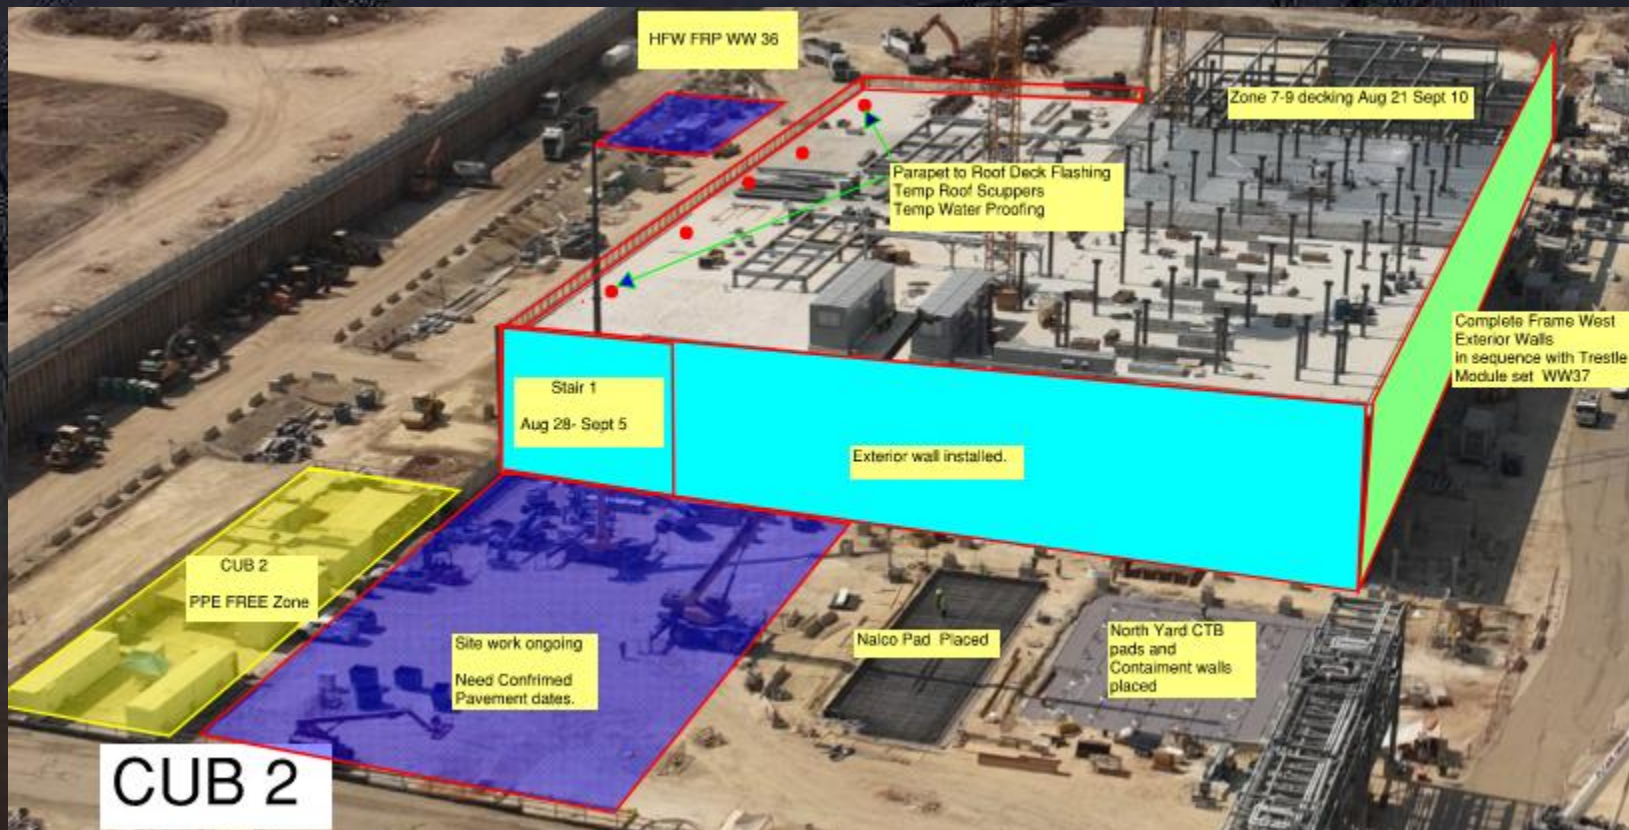

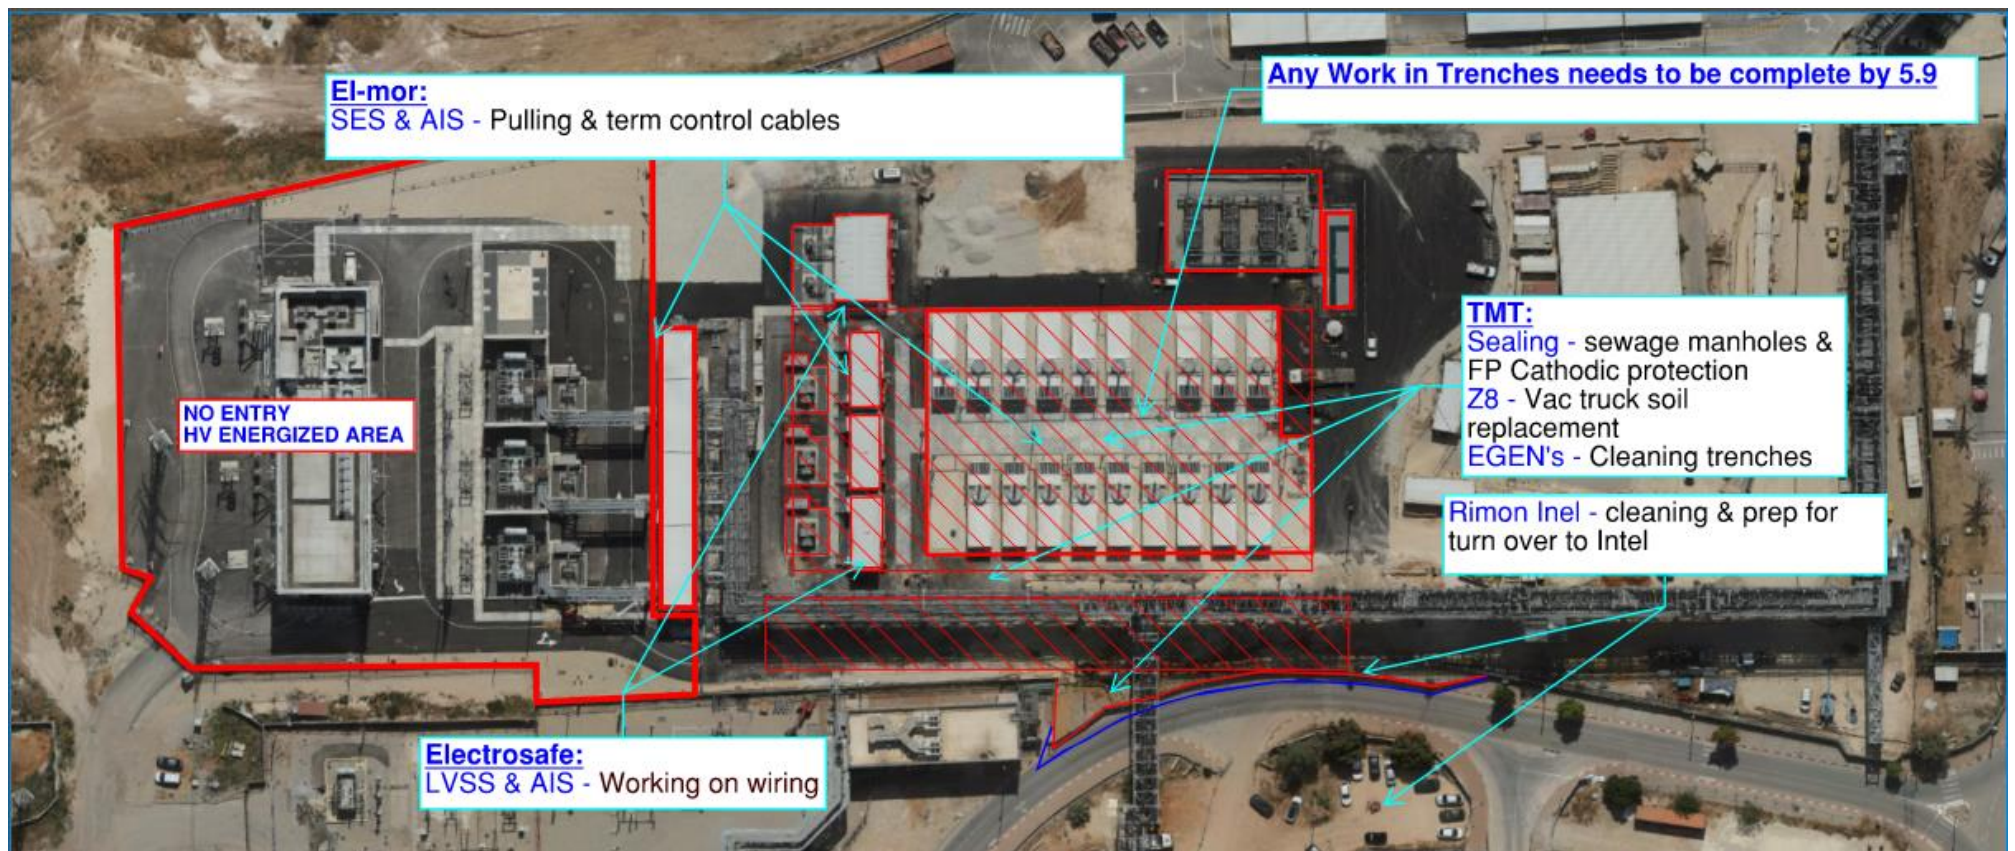



FAB GIS 33&34 Train C PERMENENT POWER September 3rd 7:00am to 8:00am.

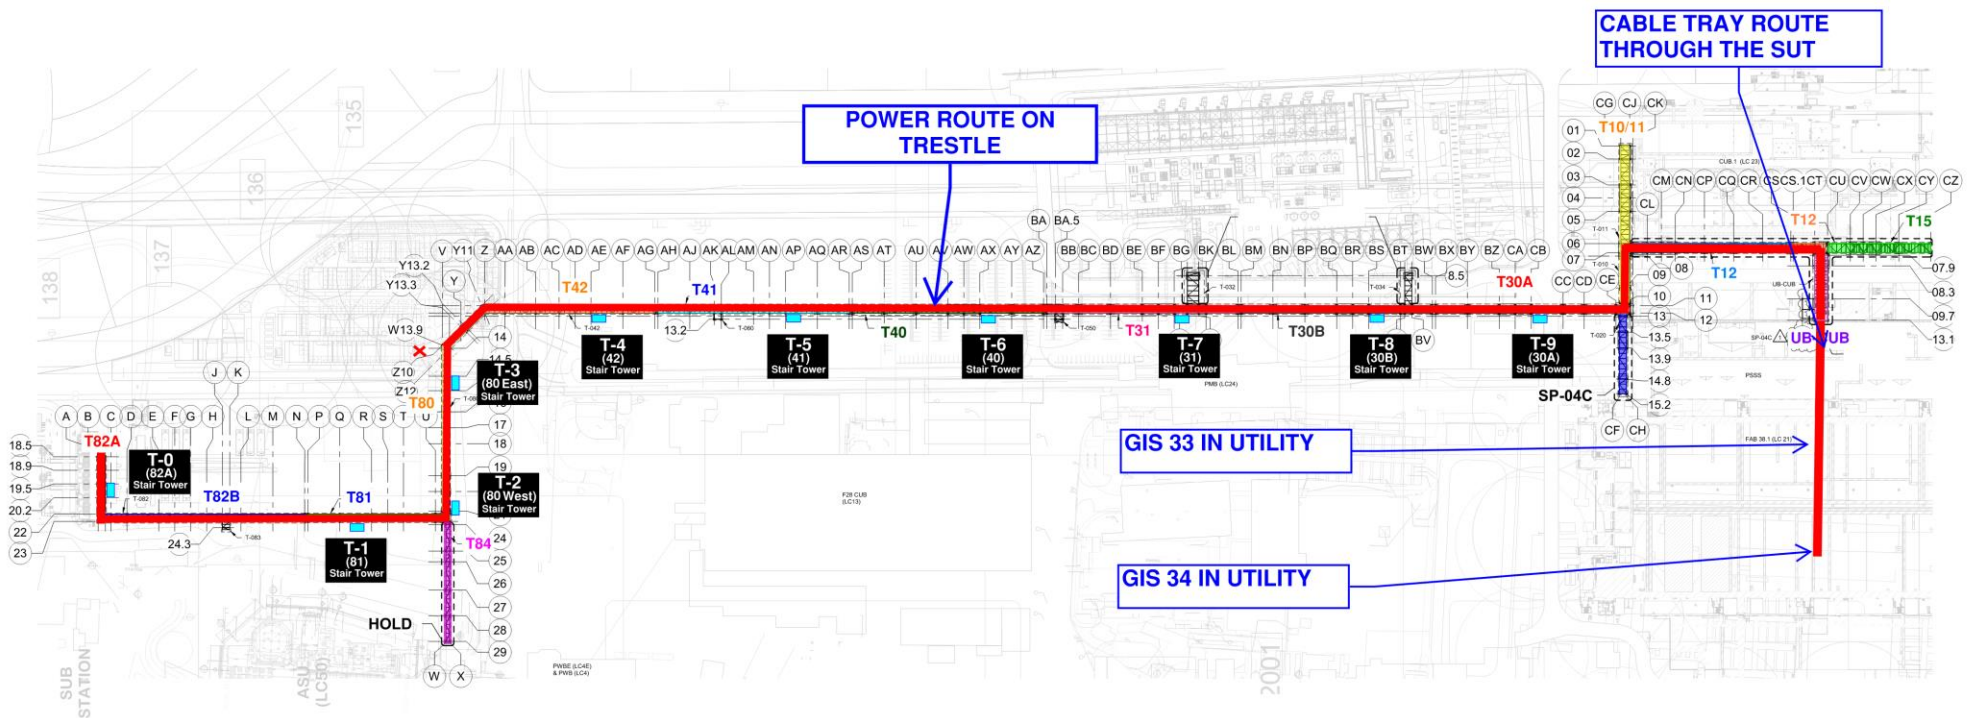



Trestle - MOD 2 Steel erection

T-17 Lvl 2

August 19

August 25

August 27

August 21

August 20


August 22


August 26

#1

#2

#3

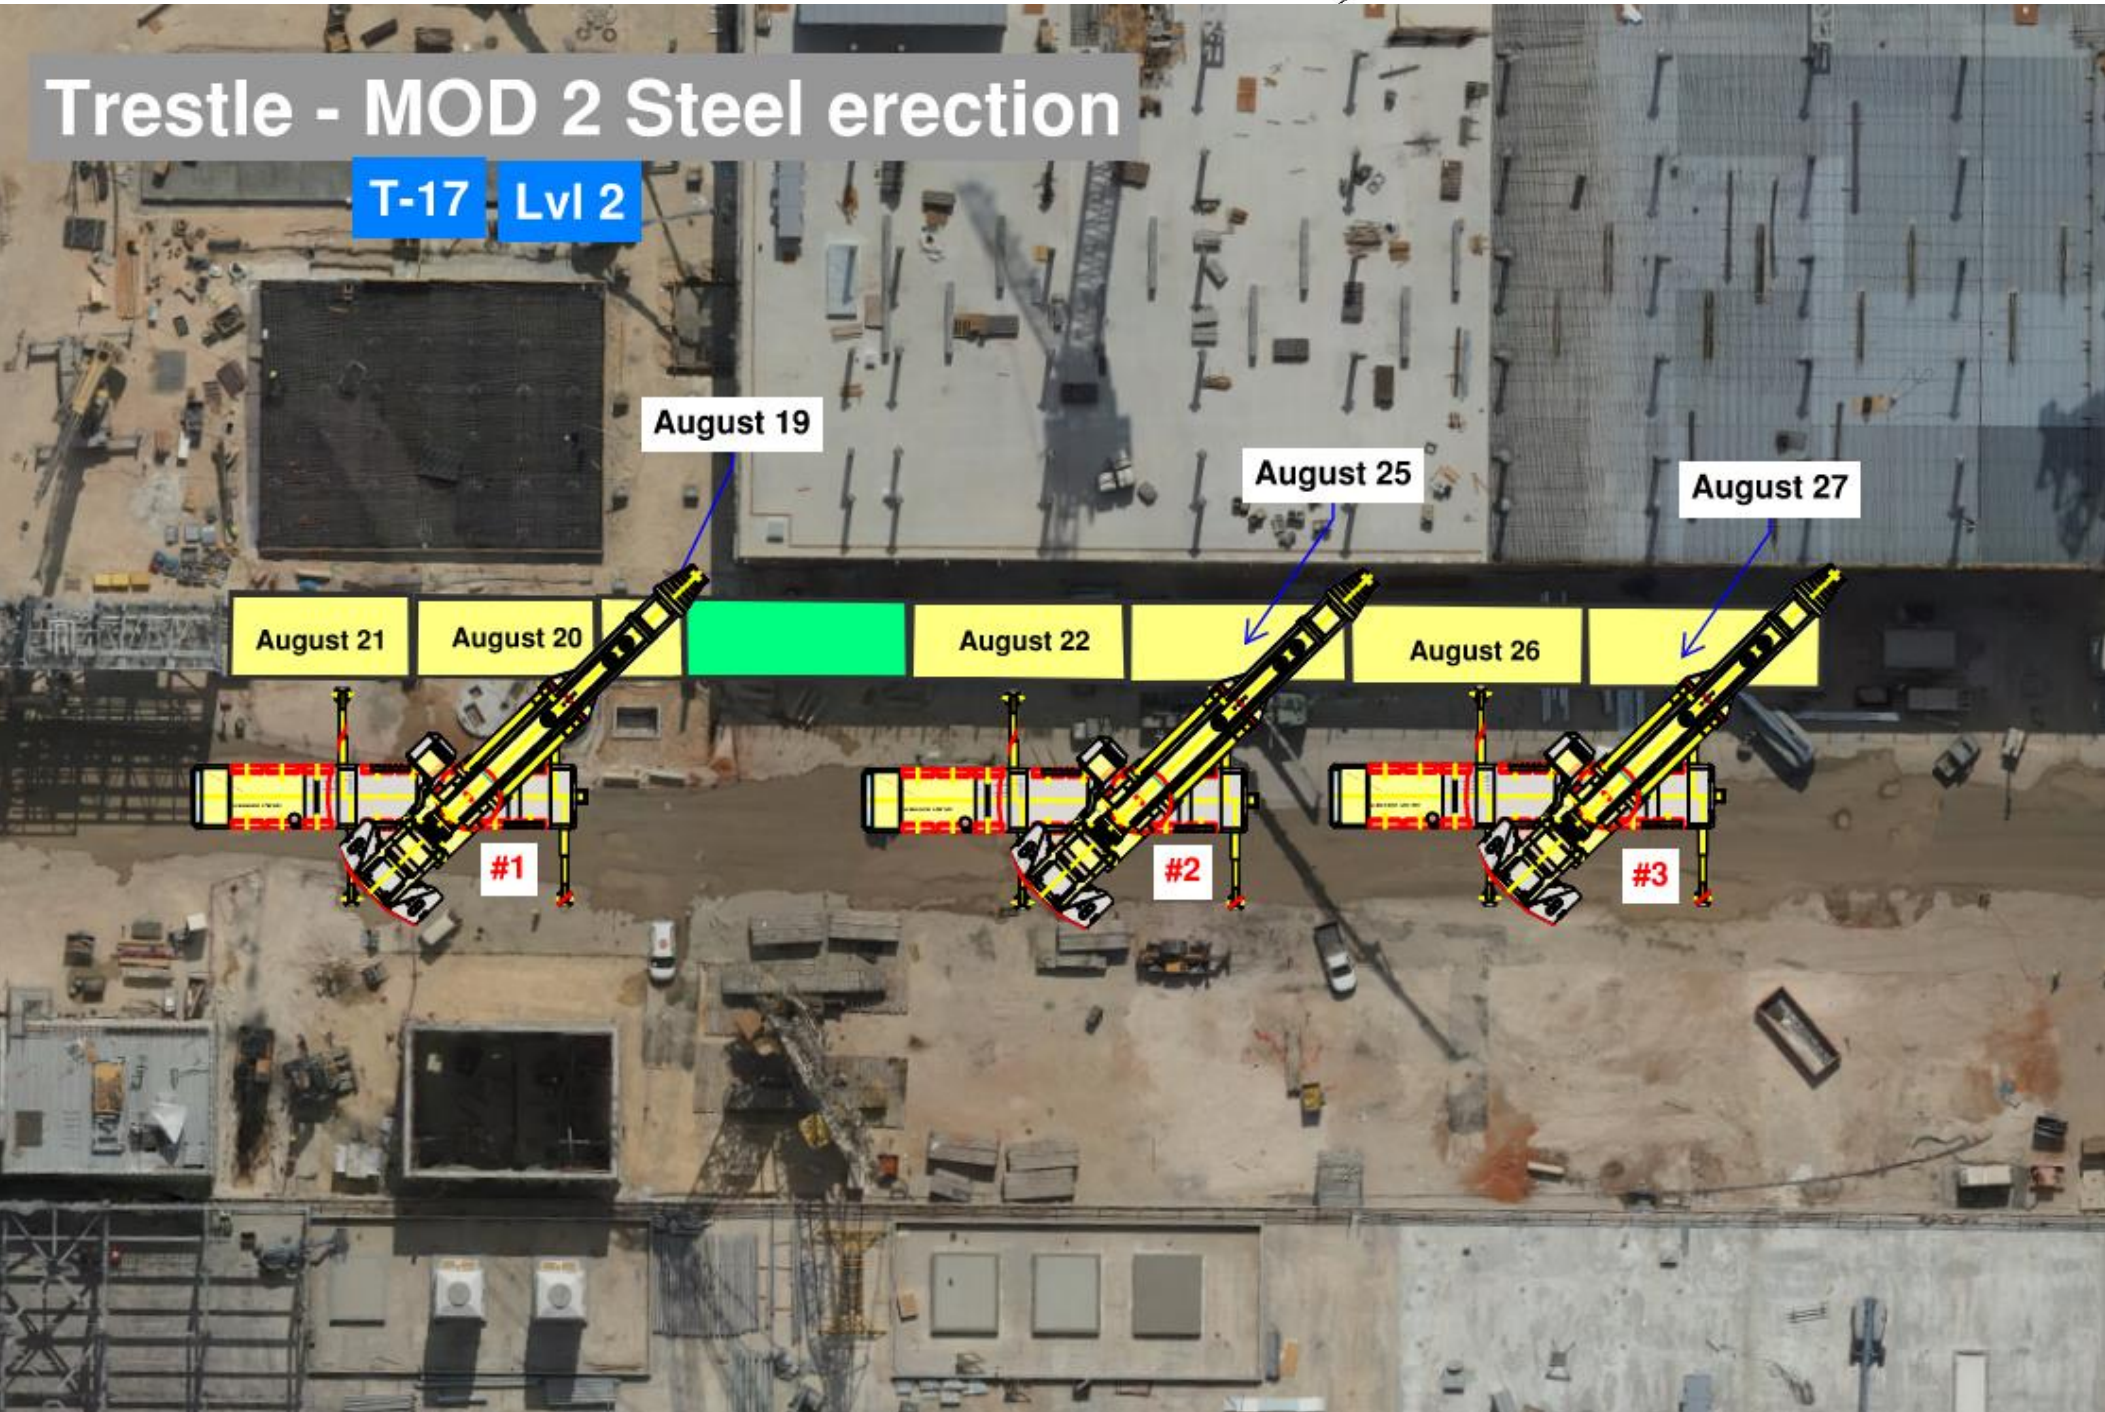



HOFFMAN CONSTRUCTION COMPANY





HOFFMAN
Sparrow  

BSGS

M.B - Fire Sprinklers

Afcon - cable trays

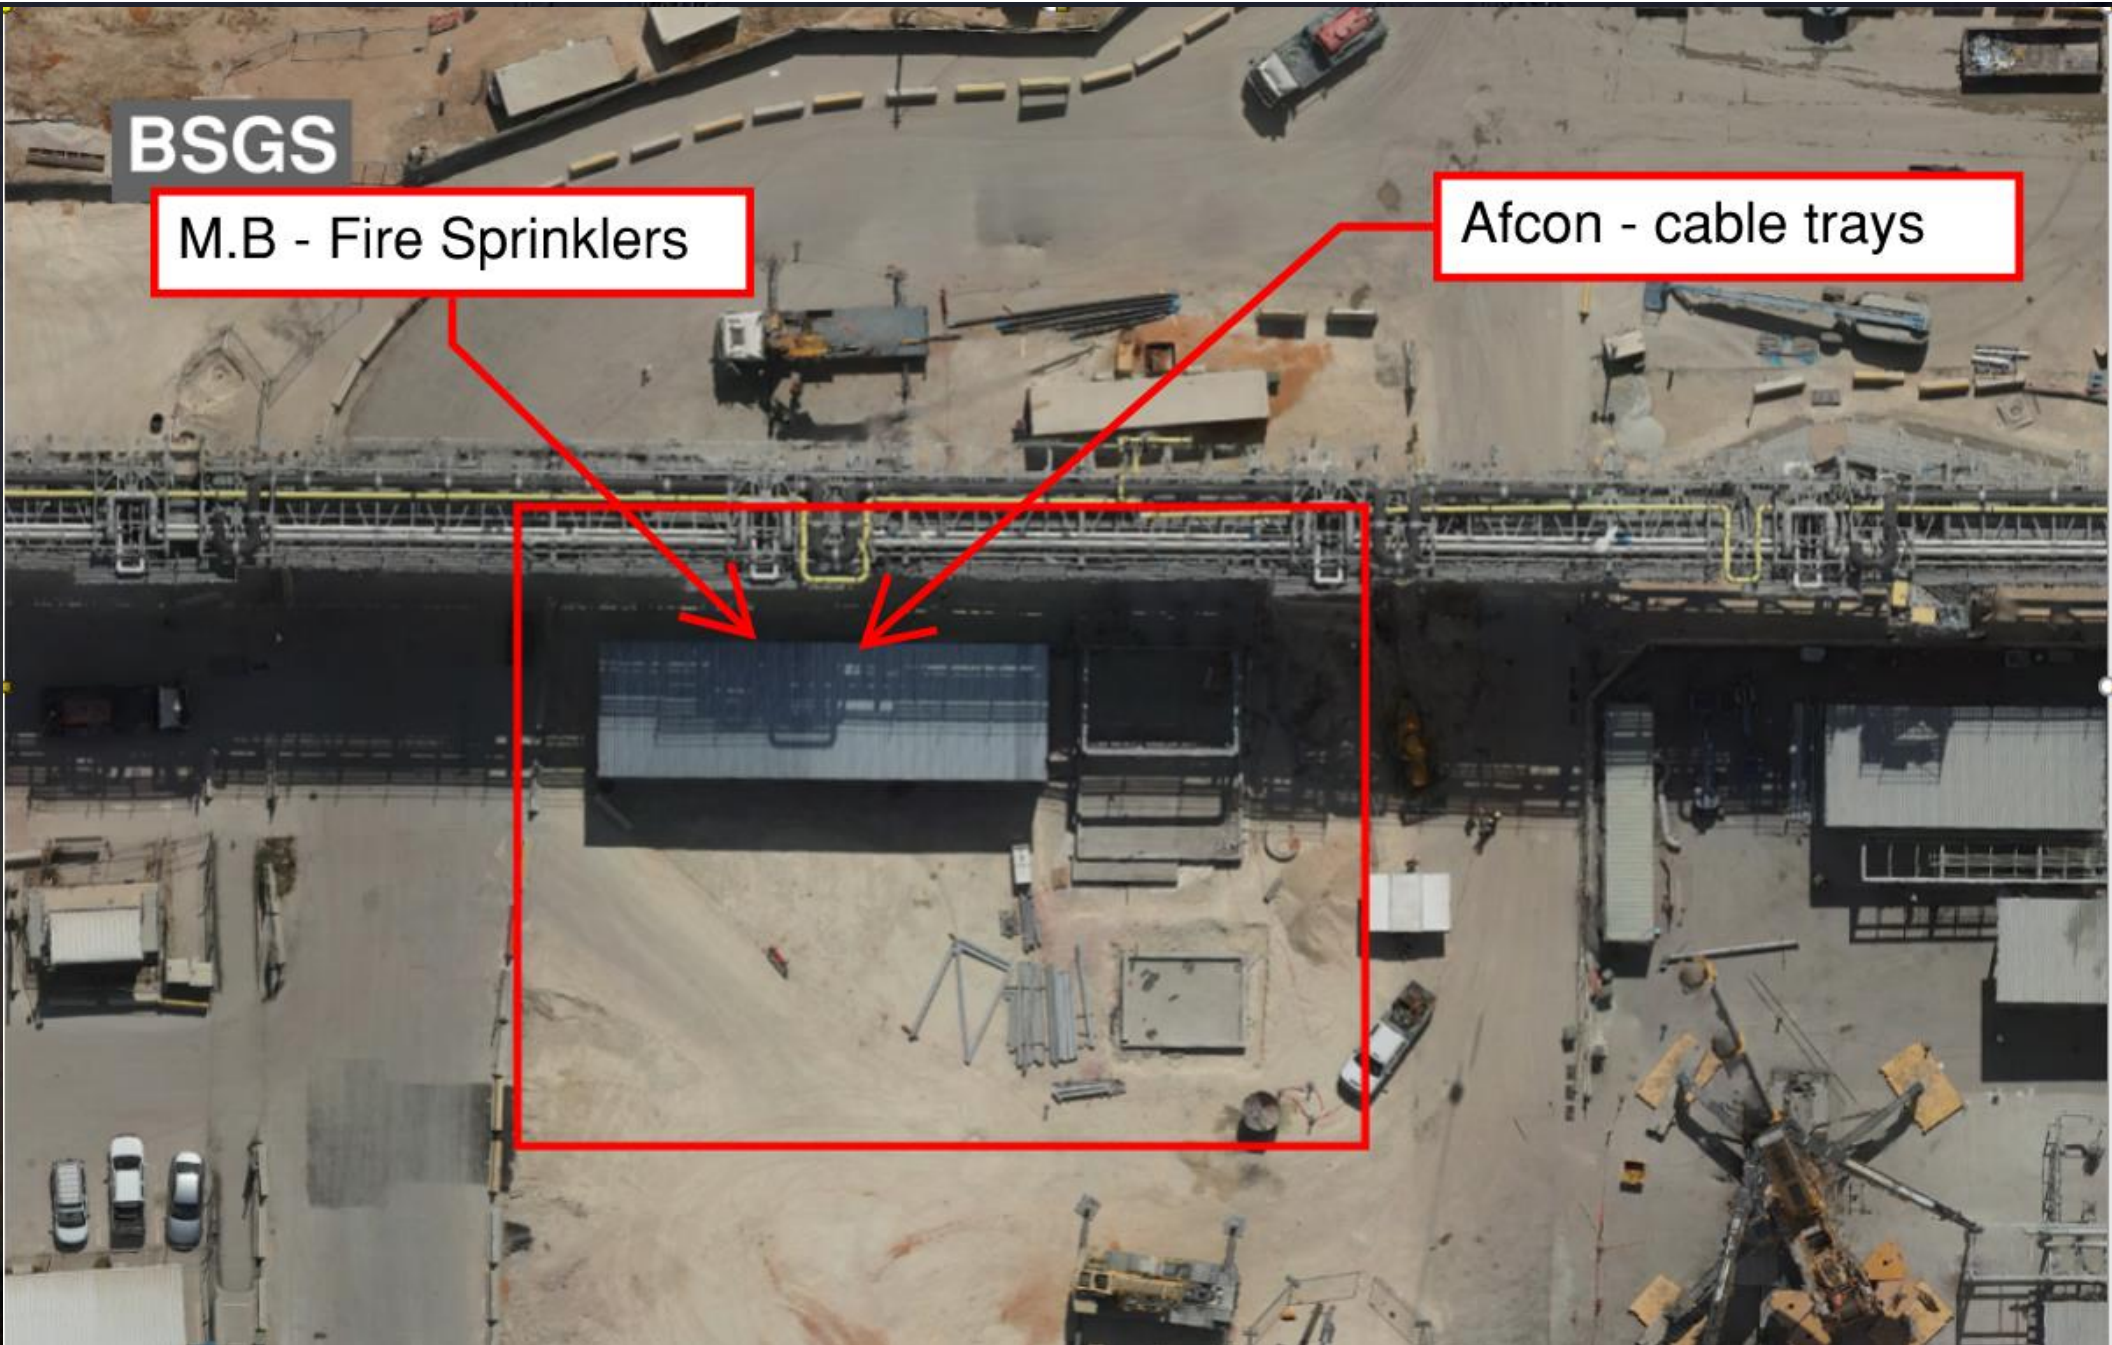




HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

Trestle Lesico NDT-10", 7 welds 28/08/24

22:00-05:00

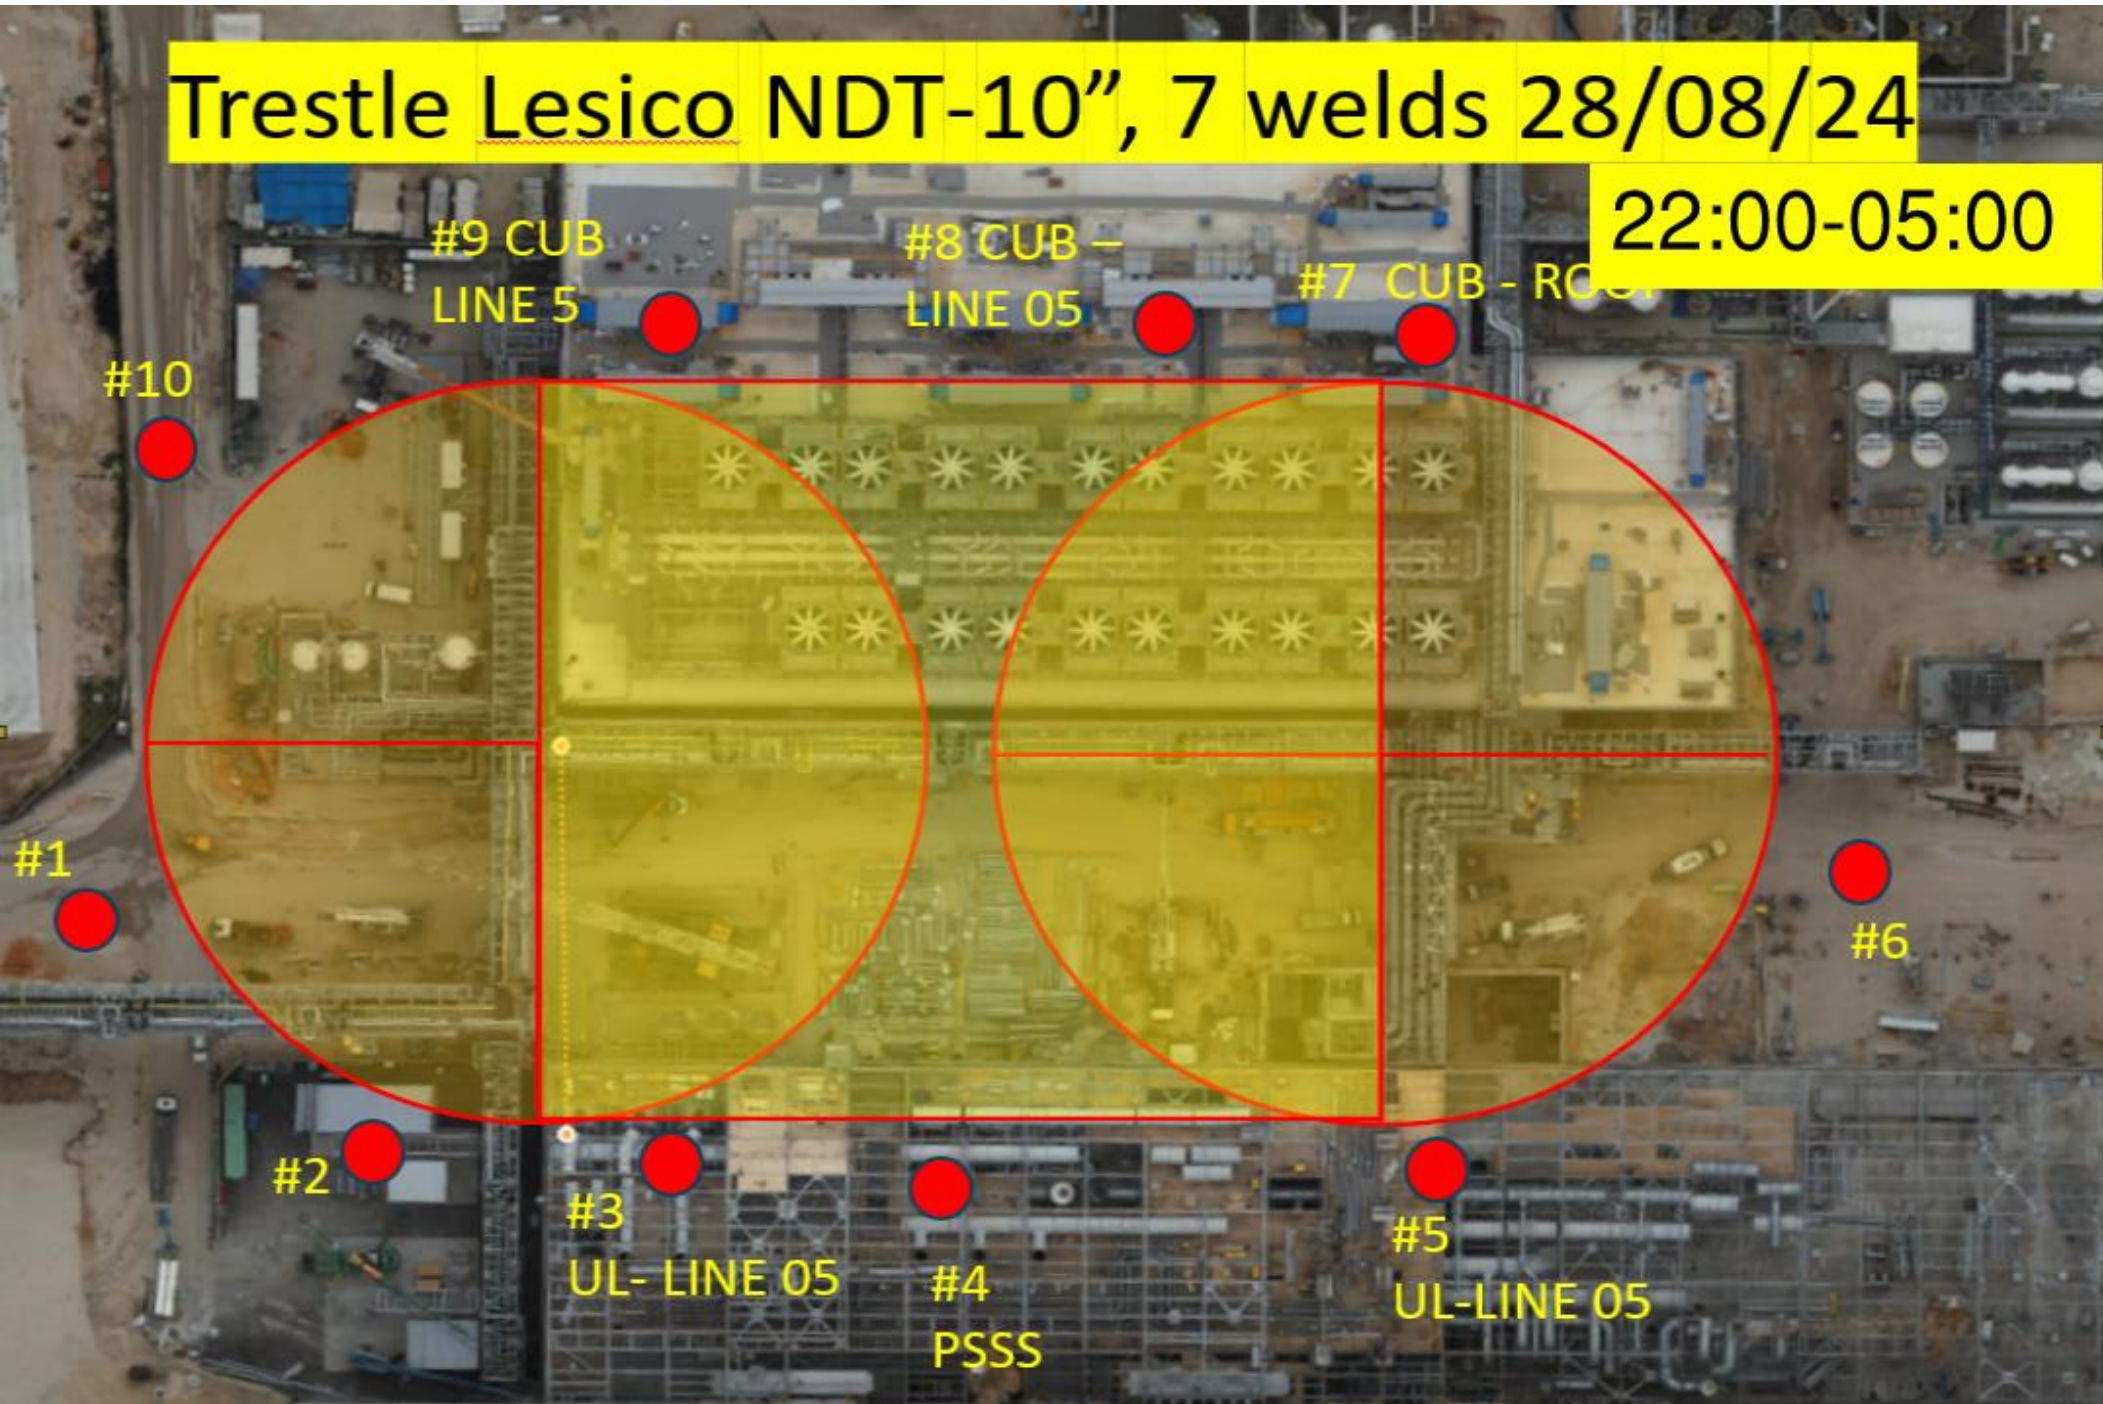




HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

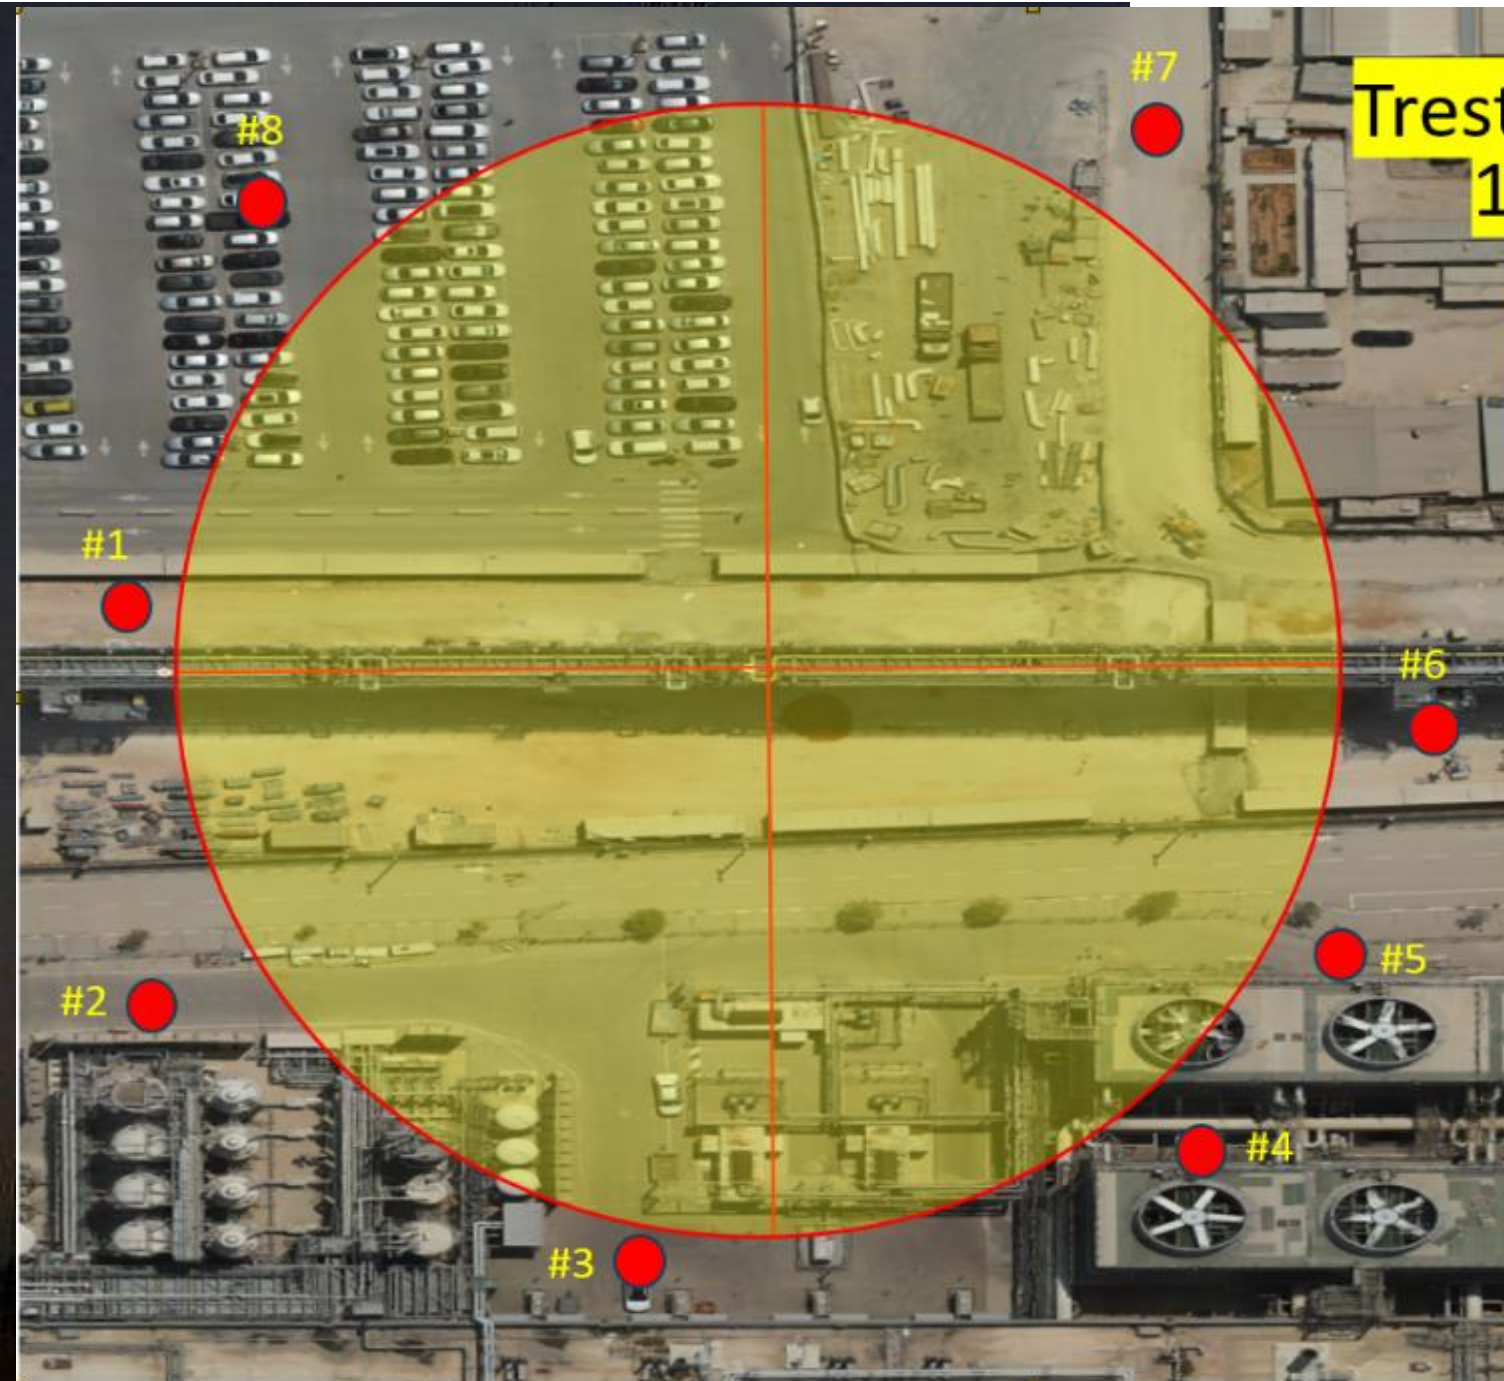

**Trestle Lesico NDT-
12", 2 welds**

29/08/24

22:00-05:00

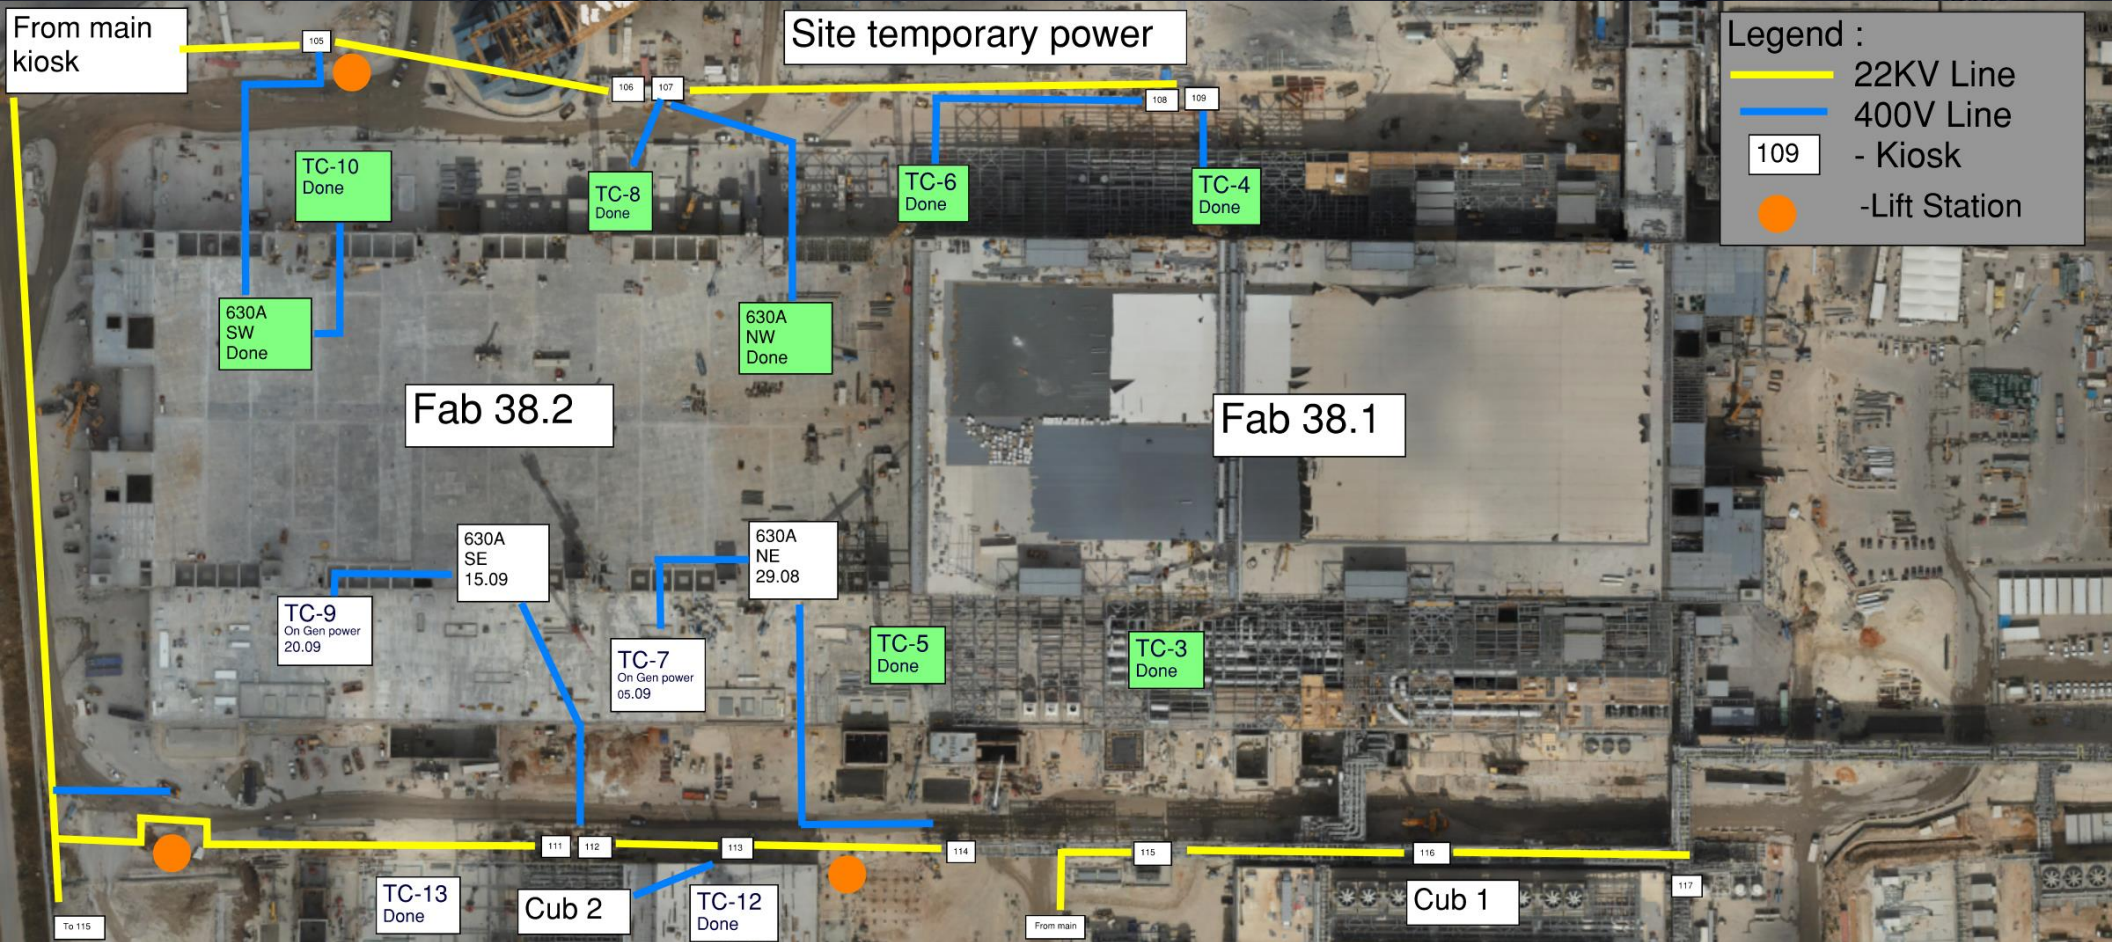

Daily Coordination Meeting


Site Logistics
North Gate B



Daily Coordination Meeting

Site Logistics

North

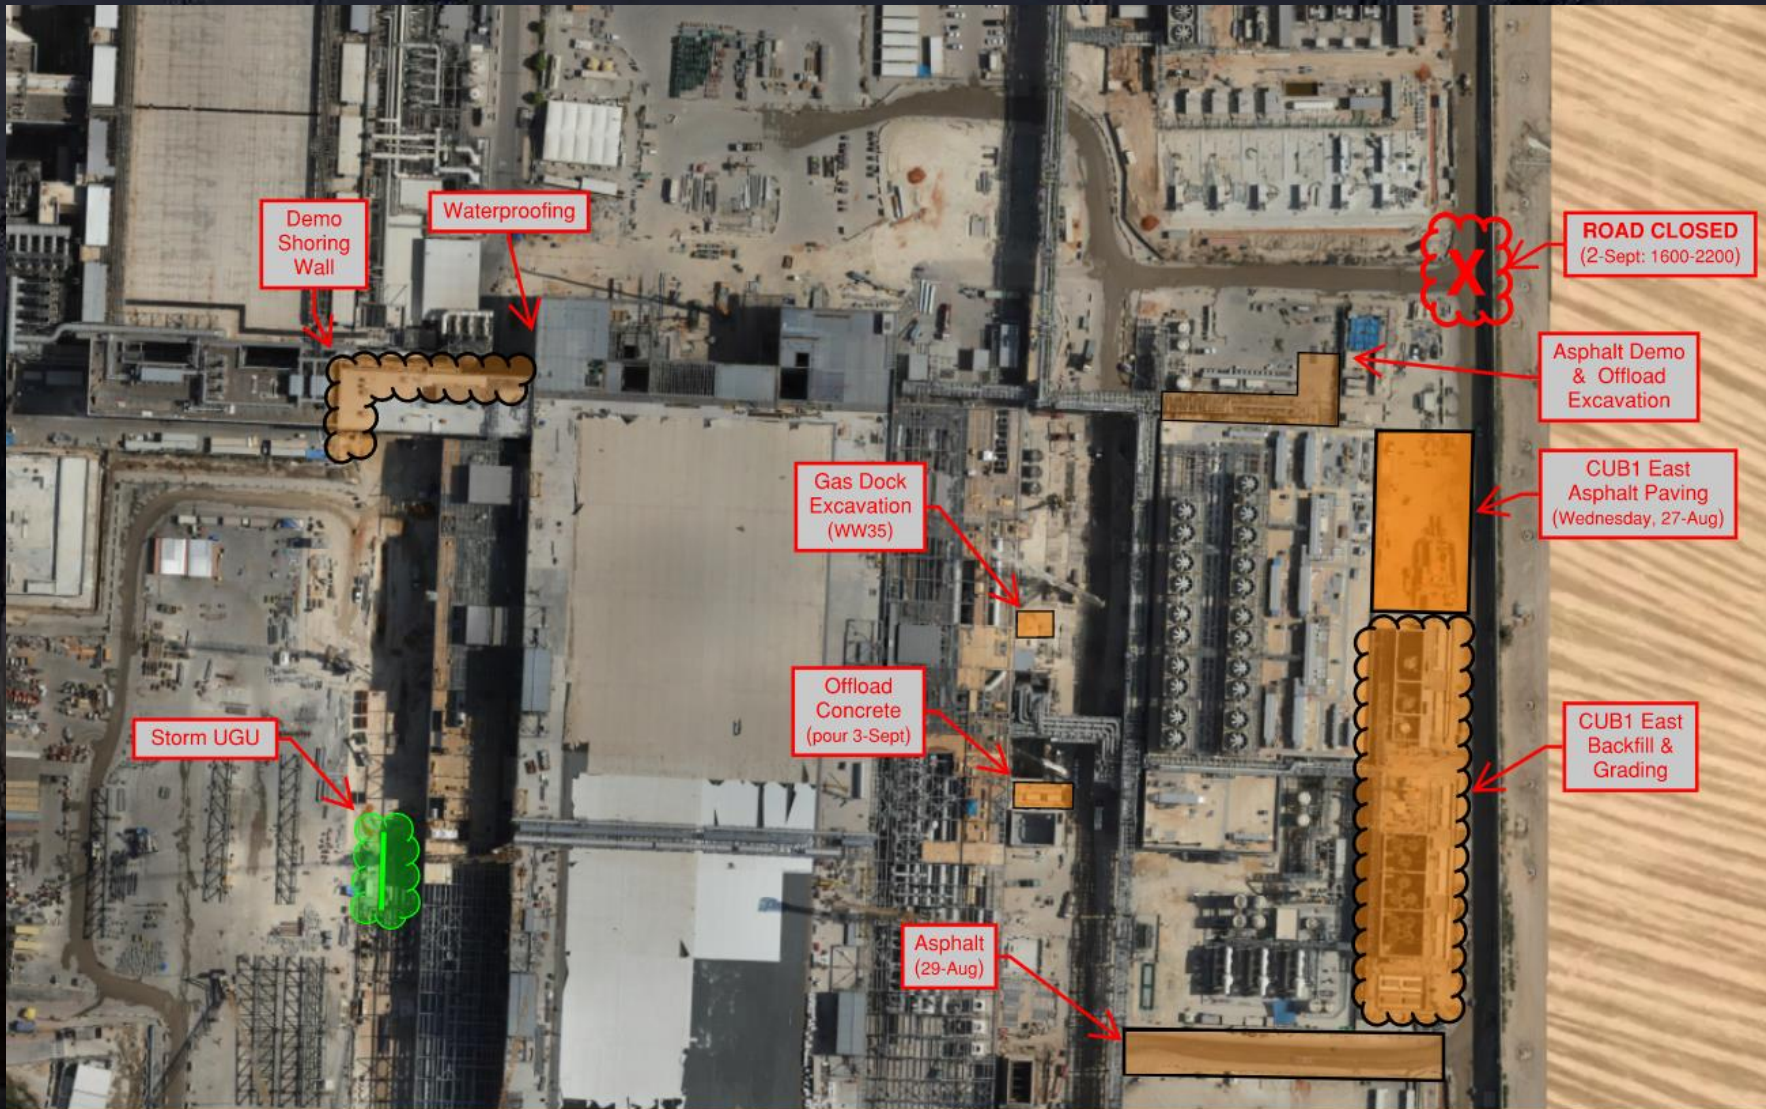




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics


South

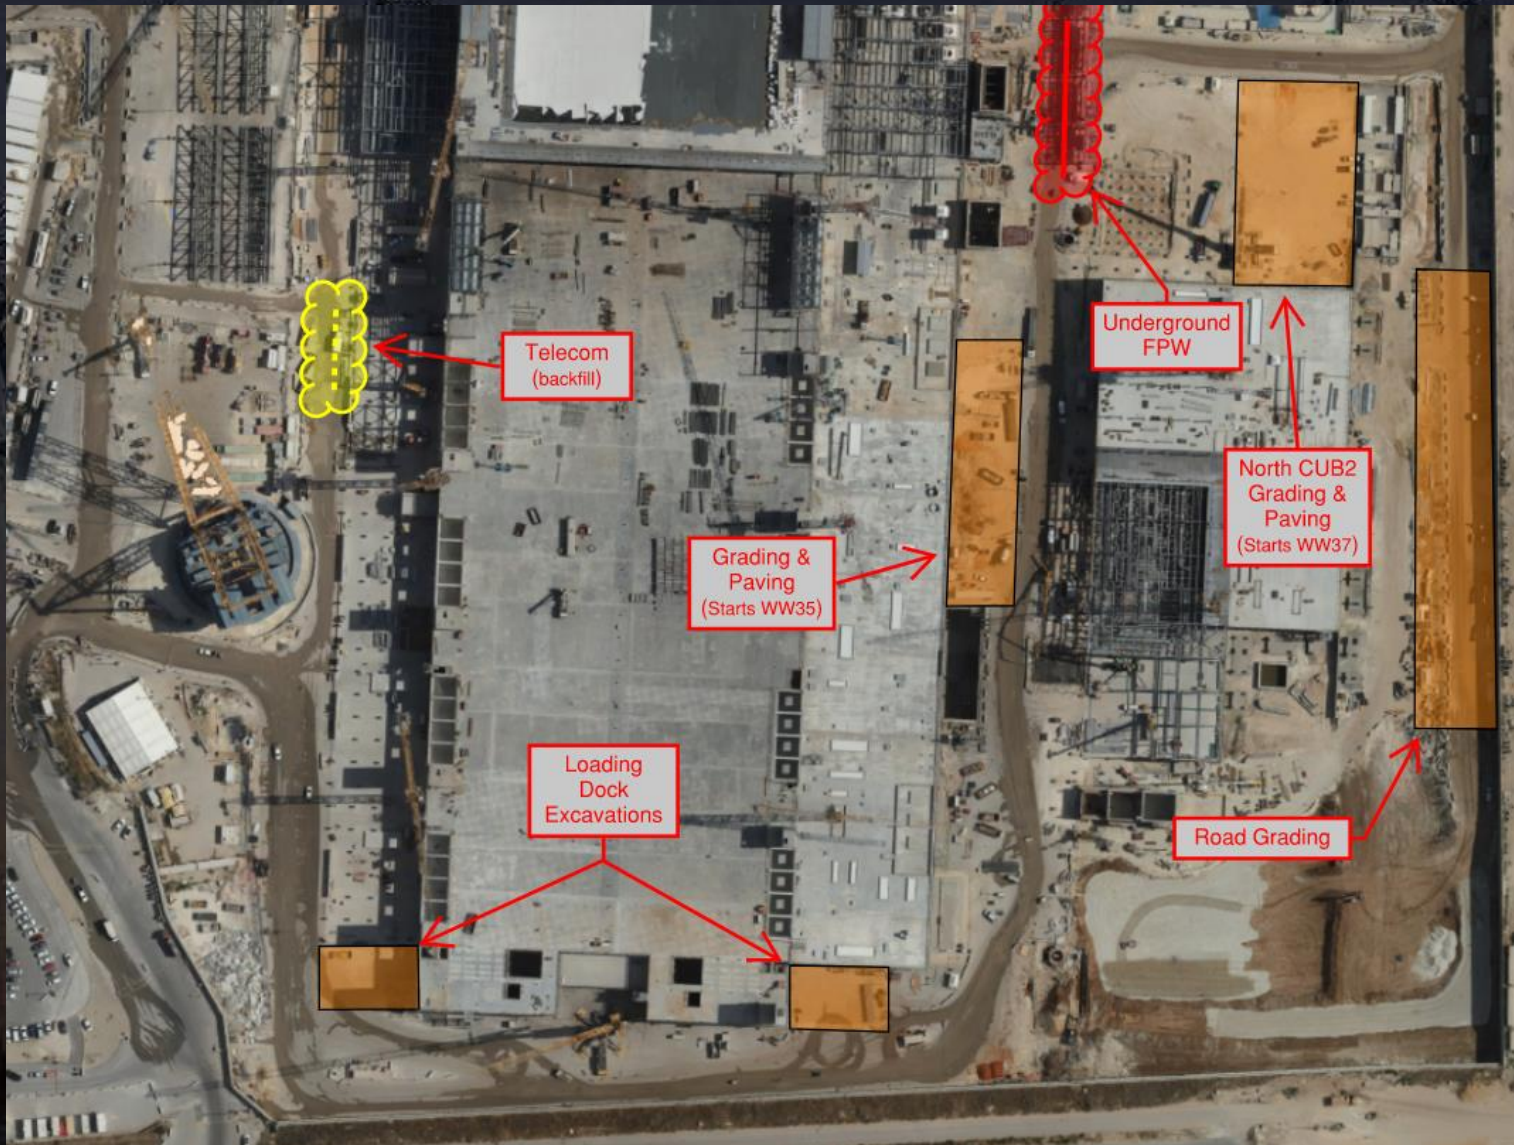


Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

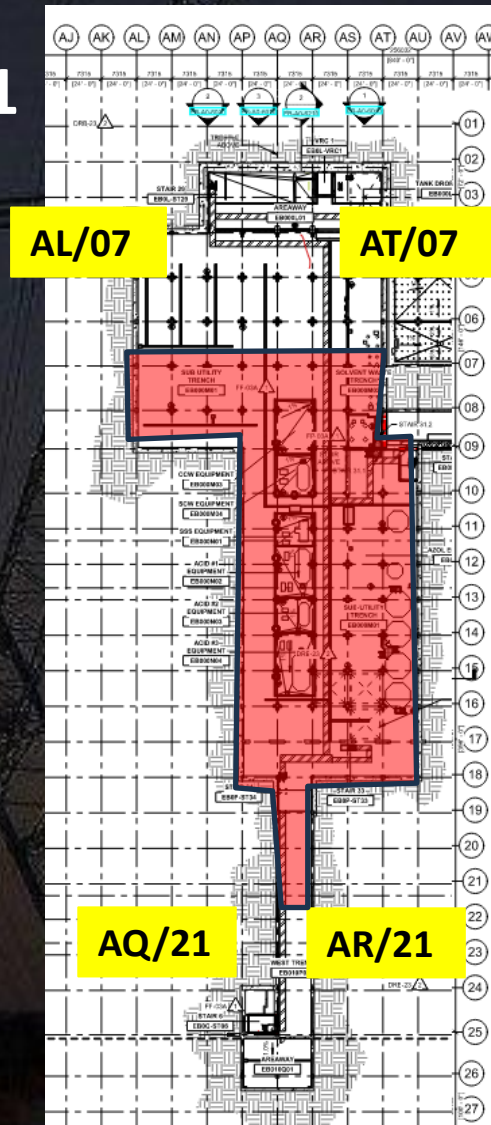


SUT2

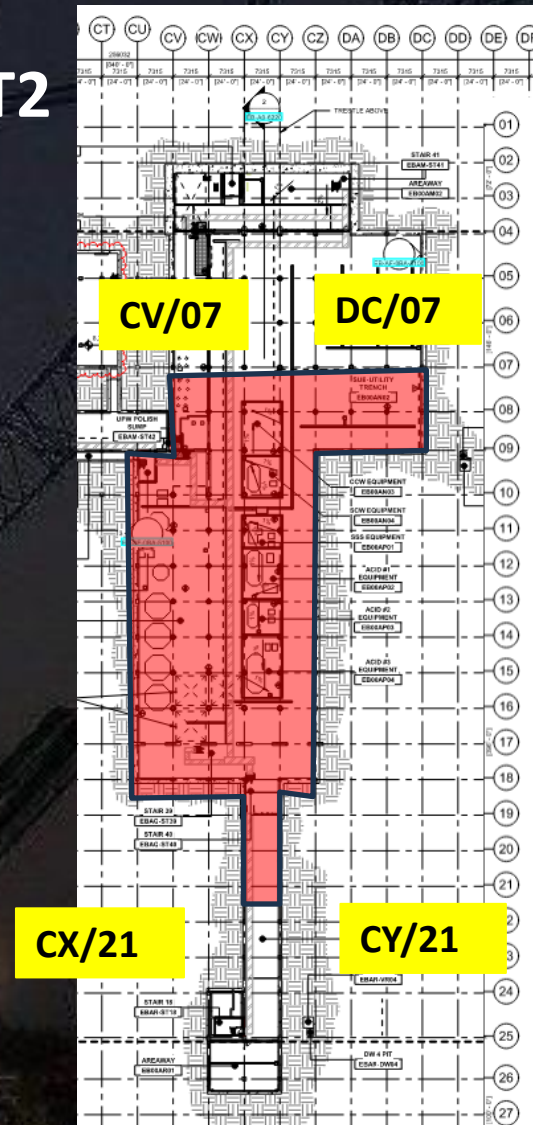

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

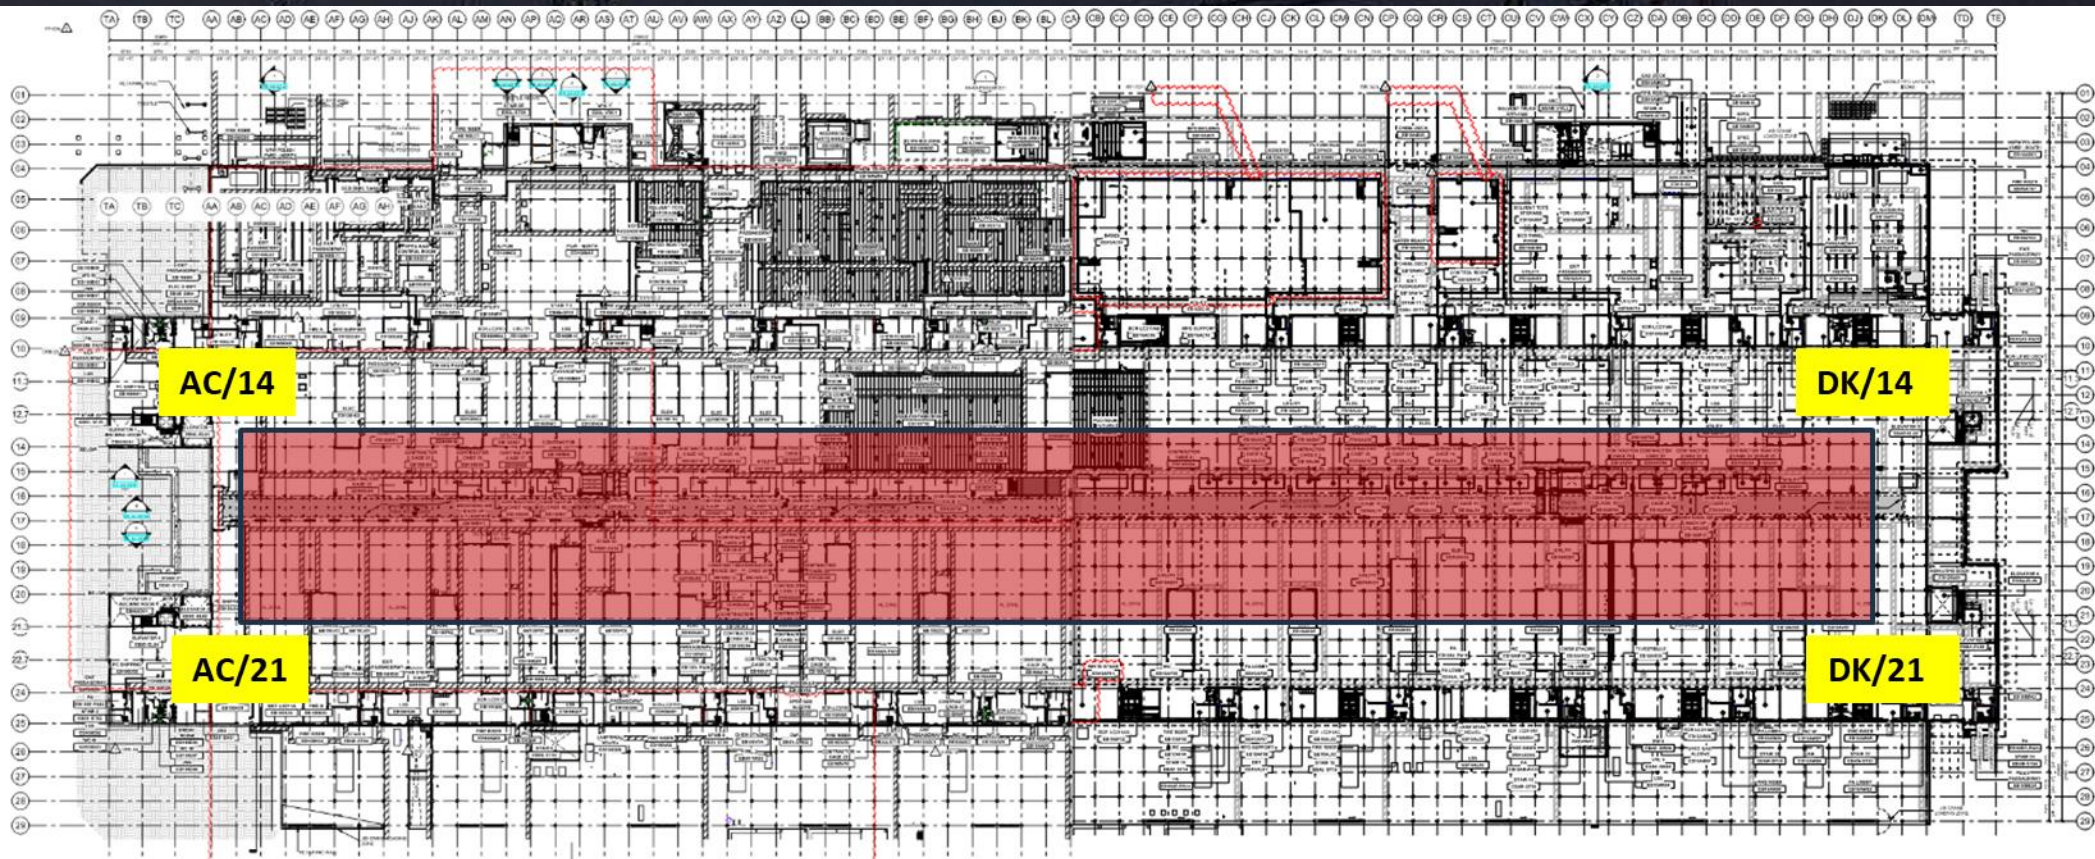



Daily Coordination Meeting


Site Logistics - Protected Areas (Subfab Level)

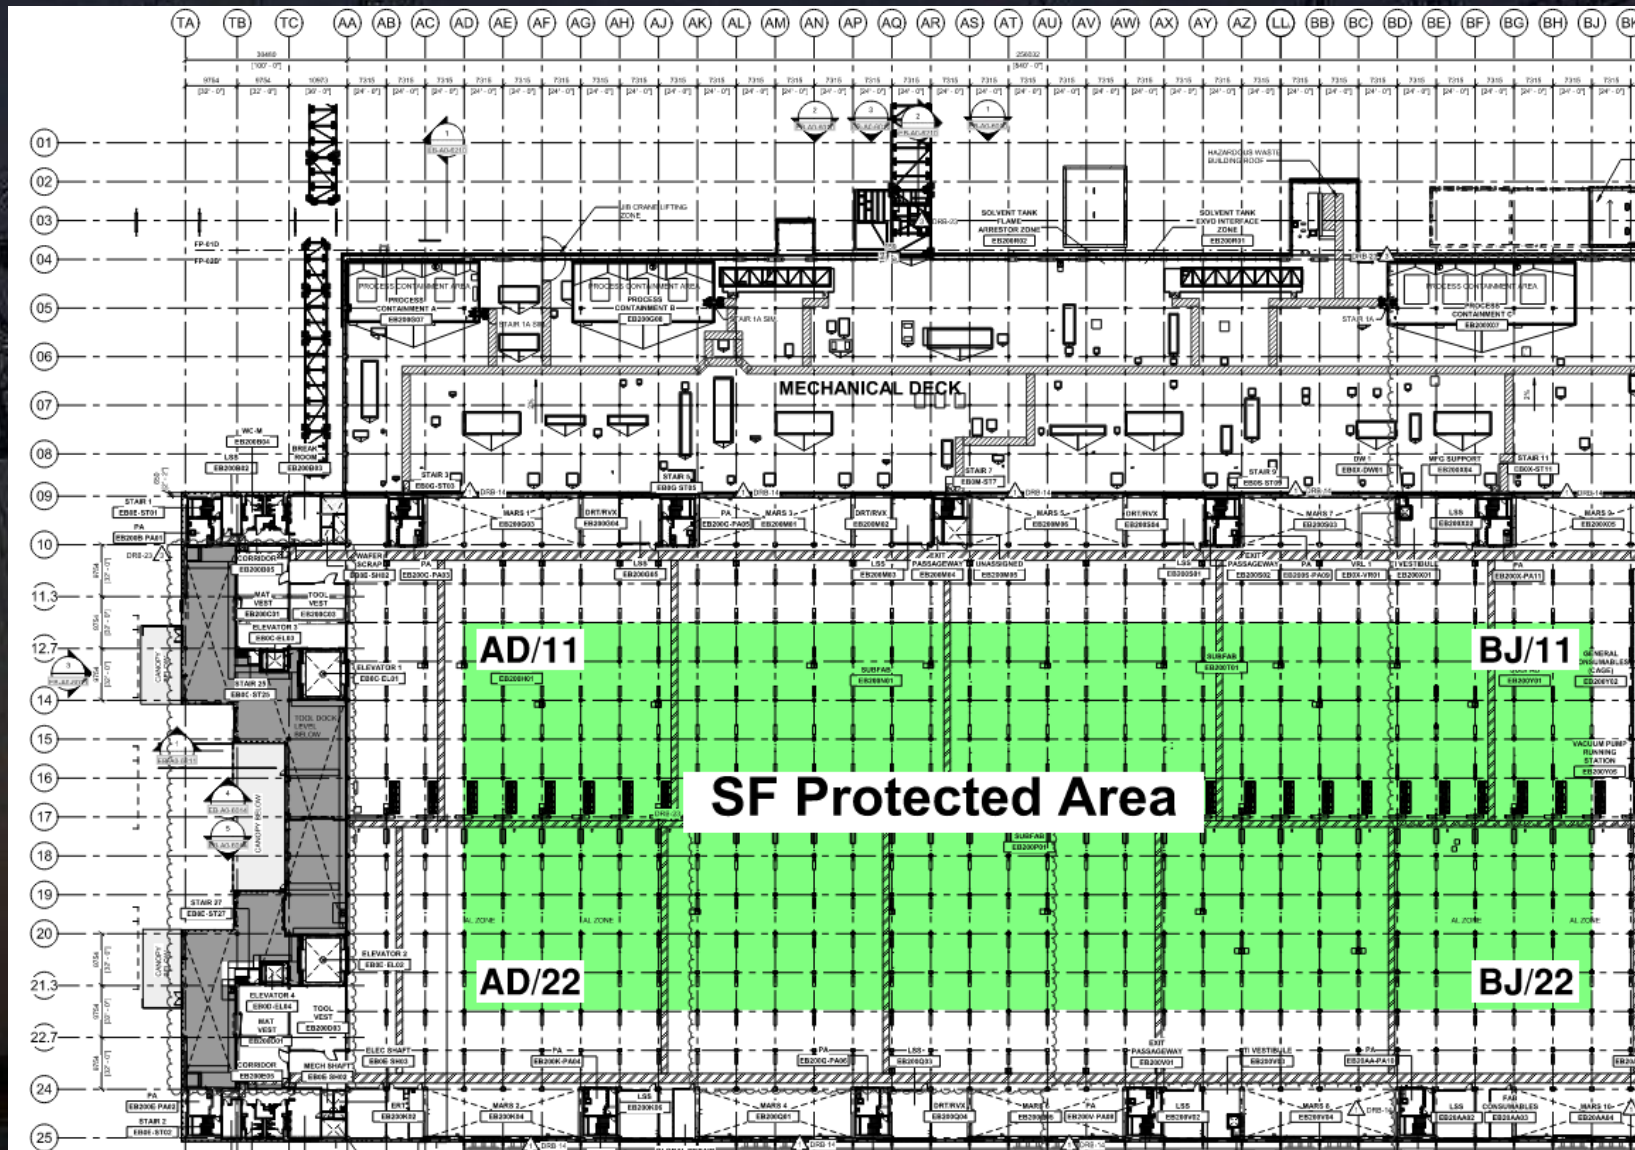

Daily Coordination Meeting

Site Logistics

Protected Areas

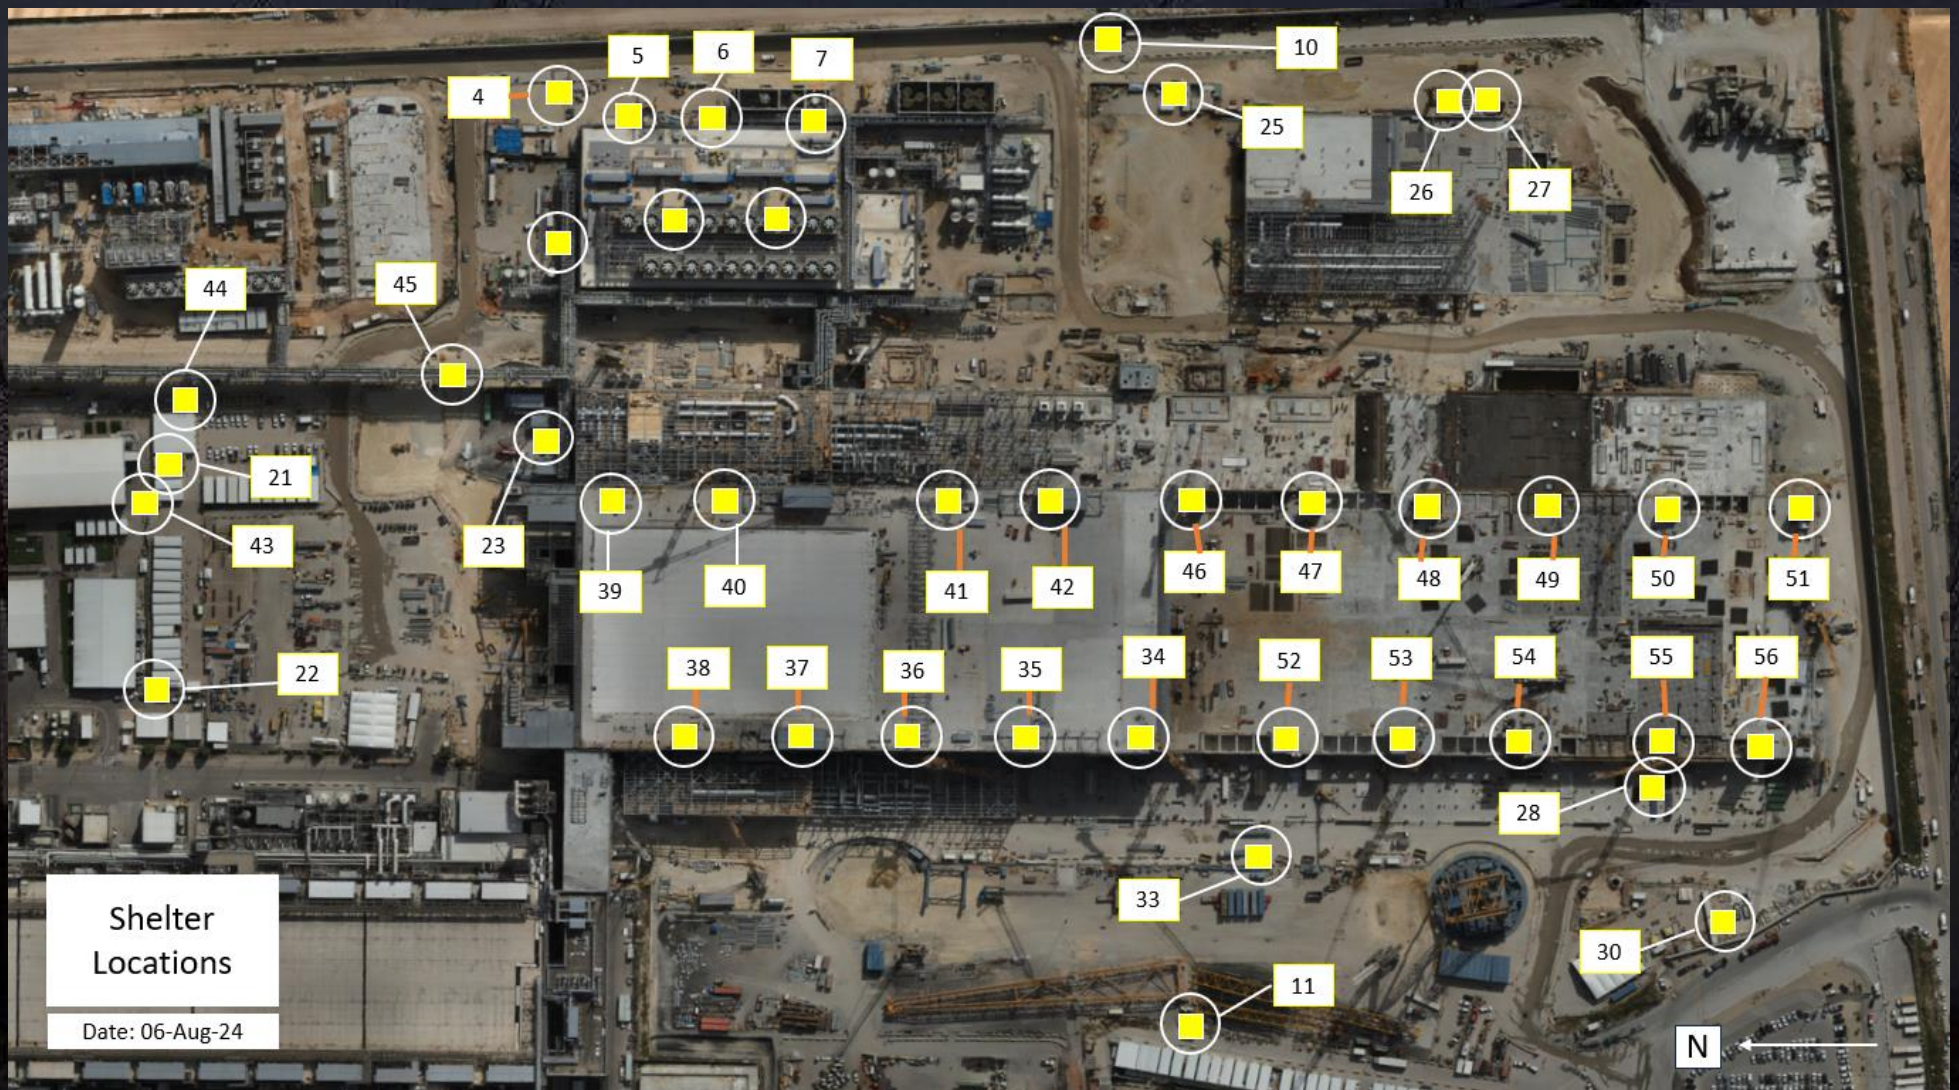

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS



Deep Cleaning of Break Tent A on Friday 30th Aug




Tent A

663 Meters

Beavers


FAB-28

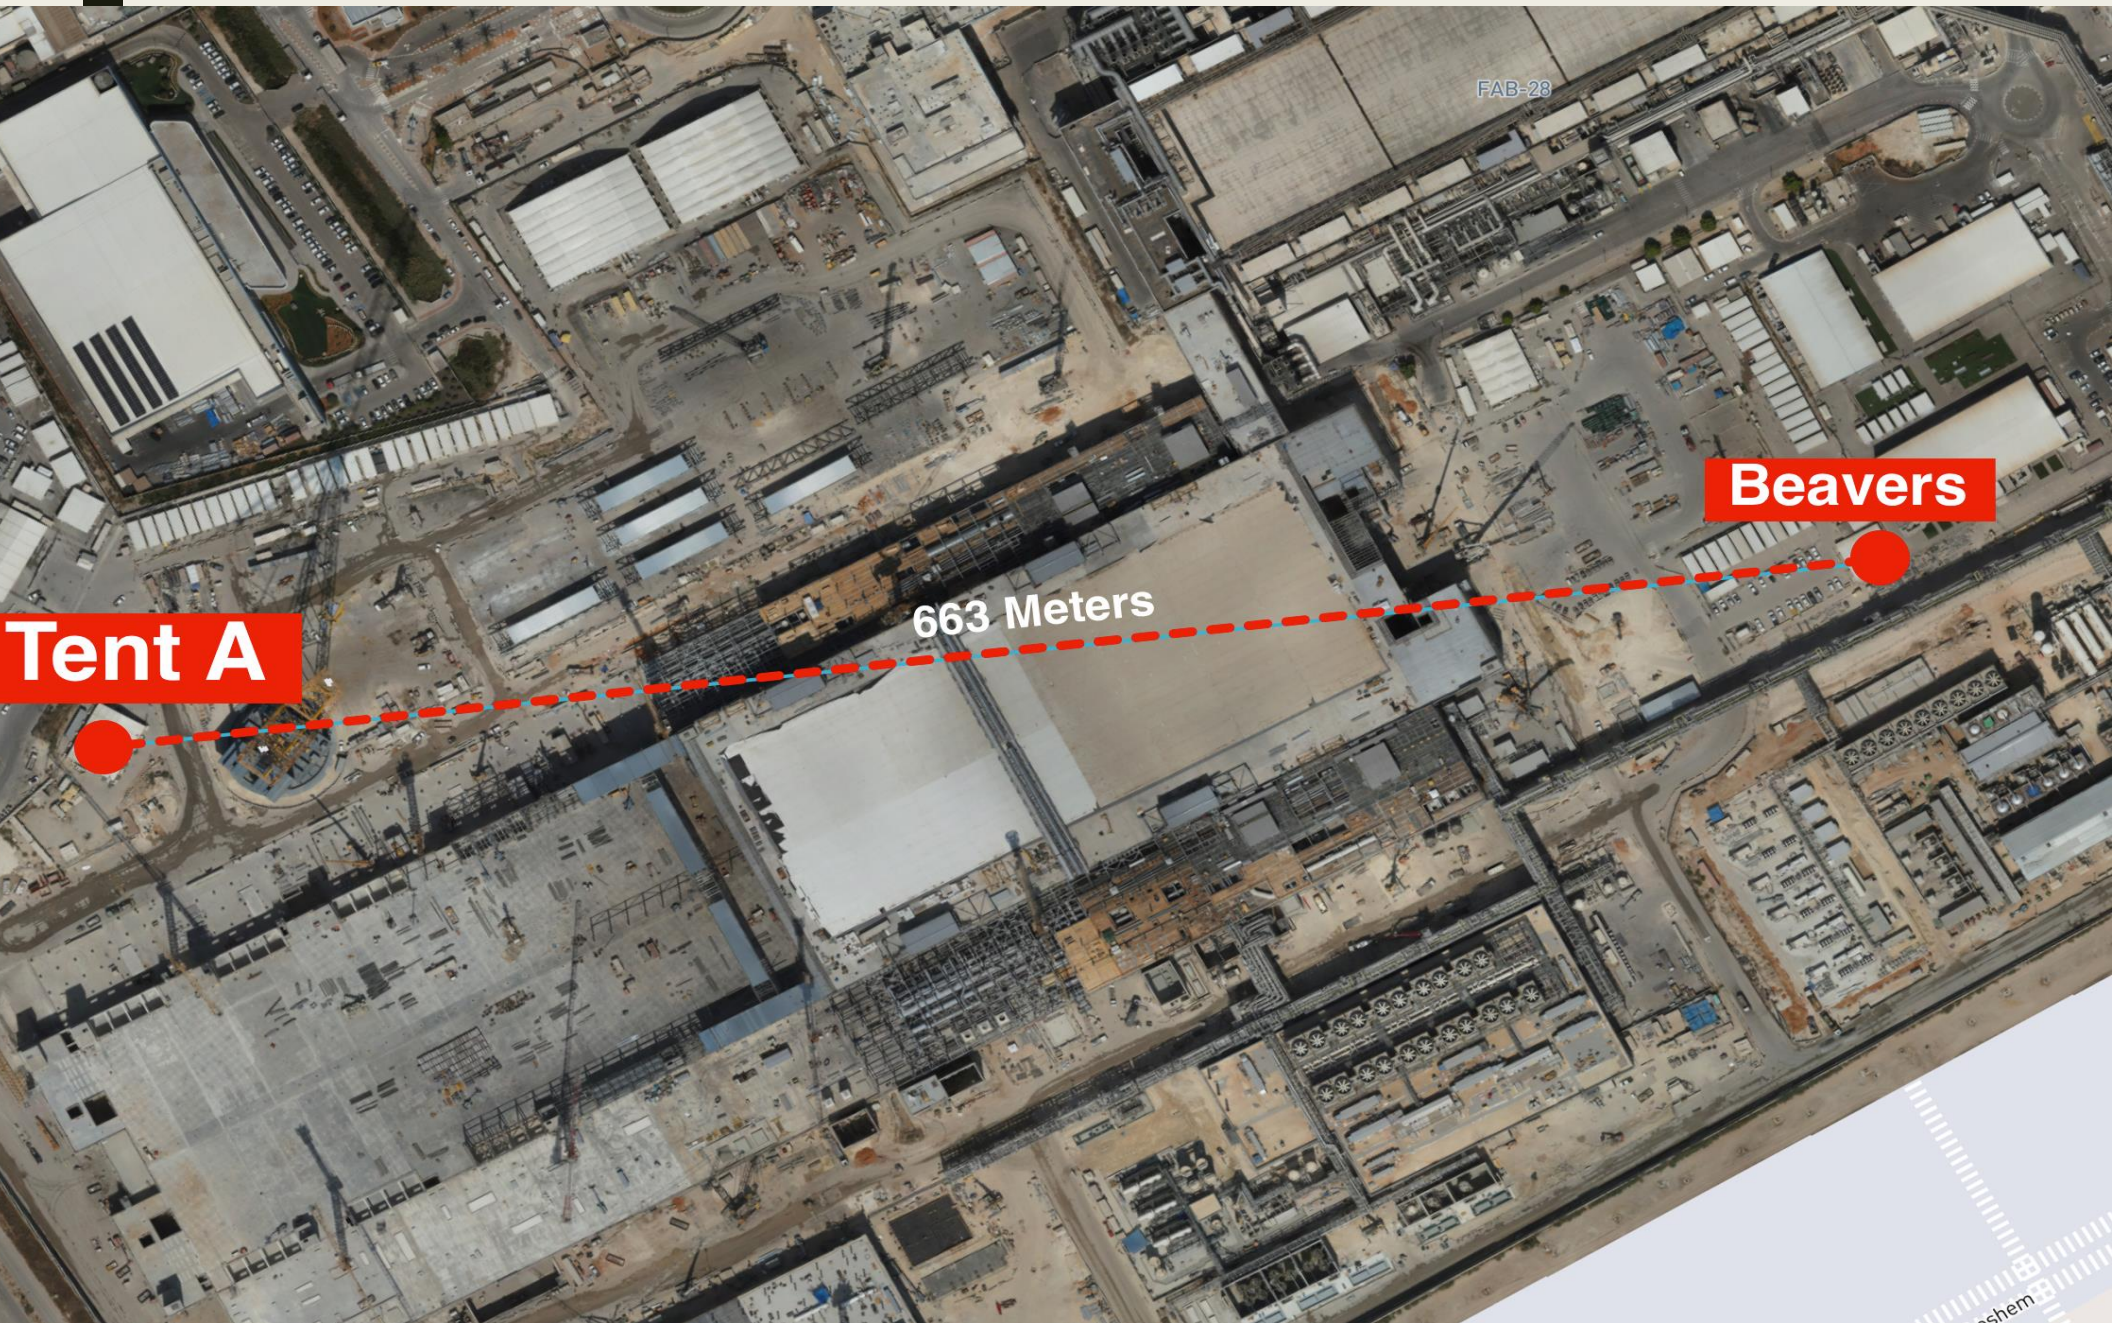





Stretch and Flex

- Stretch and flex is a mandatory part of the program at Sparrow.
- We understand that people new to the program may find it silly or pointless. However, there are many benefits to stretching before work.
- Stretching increases blood flow to your muscles, making them more able to perform the work needed.
- It increases the joint fluid, allowing for greater range of motion and decreases the chance of injury.
- It also decreases muscle tightness further reducing the chance of injuring the muscle when used.
- It also improves balance and muscle coordination.
- Please make sure all of your crews are stretching before they go to work.

Heat Index- August 28th

		temperature (°F)															
		80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
Relative Humidity (%)	40	80	81	83	85	88		94	97	101	105	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
	55	81	84	86	89	93	97	101	106	112	117	124	130	137			
	60	82	84	88	91	95	100	105	110	116	123	129	137				
	65	82	85	89	93	98	103	108	114	121	128	136					
	70	83	86	90	95	100	105	112	119	126	134						
	75	84	88	92	97	103	109	116	124	132							
	80	84	89	94	100	106	113	121	129								
	85	85	90	96	102	110	117	126	135								
	90	86	91	98	105	113	122	131									
	95	86	93	100	108	117	127										
	100	87	95	103	112	121	132										

 Caution
 Extreme Caution
 Danger
 Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
