

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- **Hole Covers – don't remove and leave a trap for others.**
- **Exclusion Zones – do not share with overhead work.**



UTILITY LEVEL MOD1

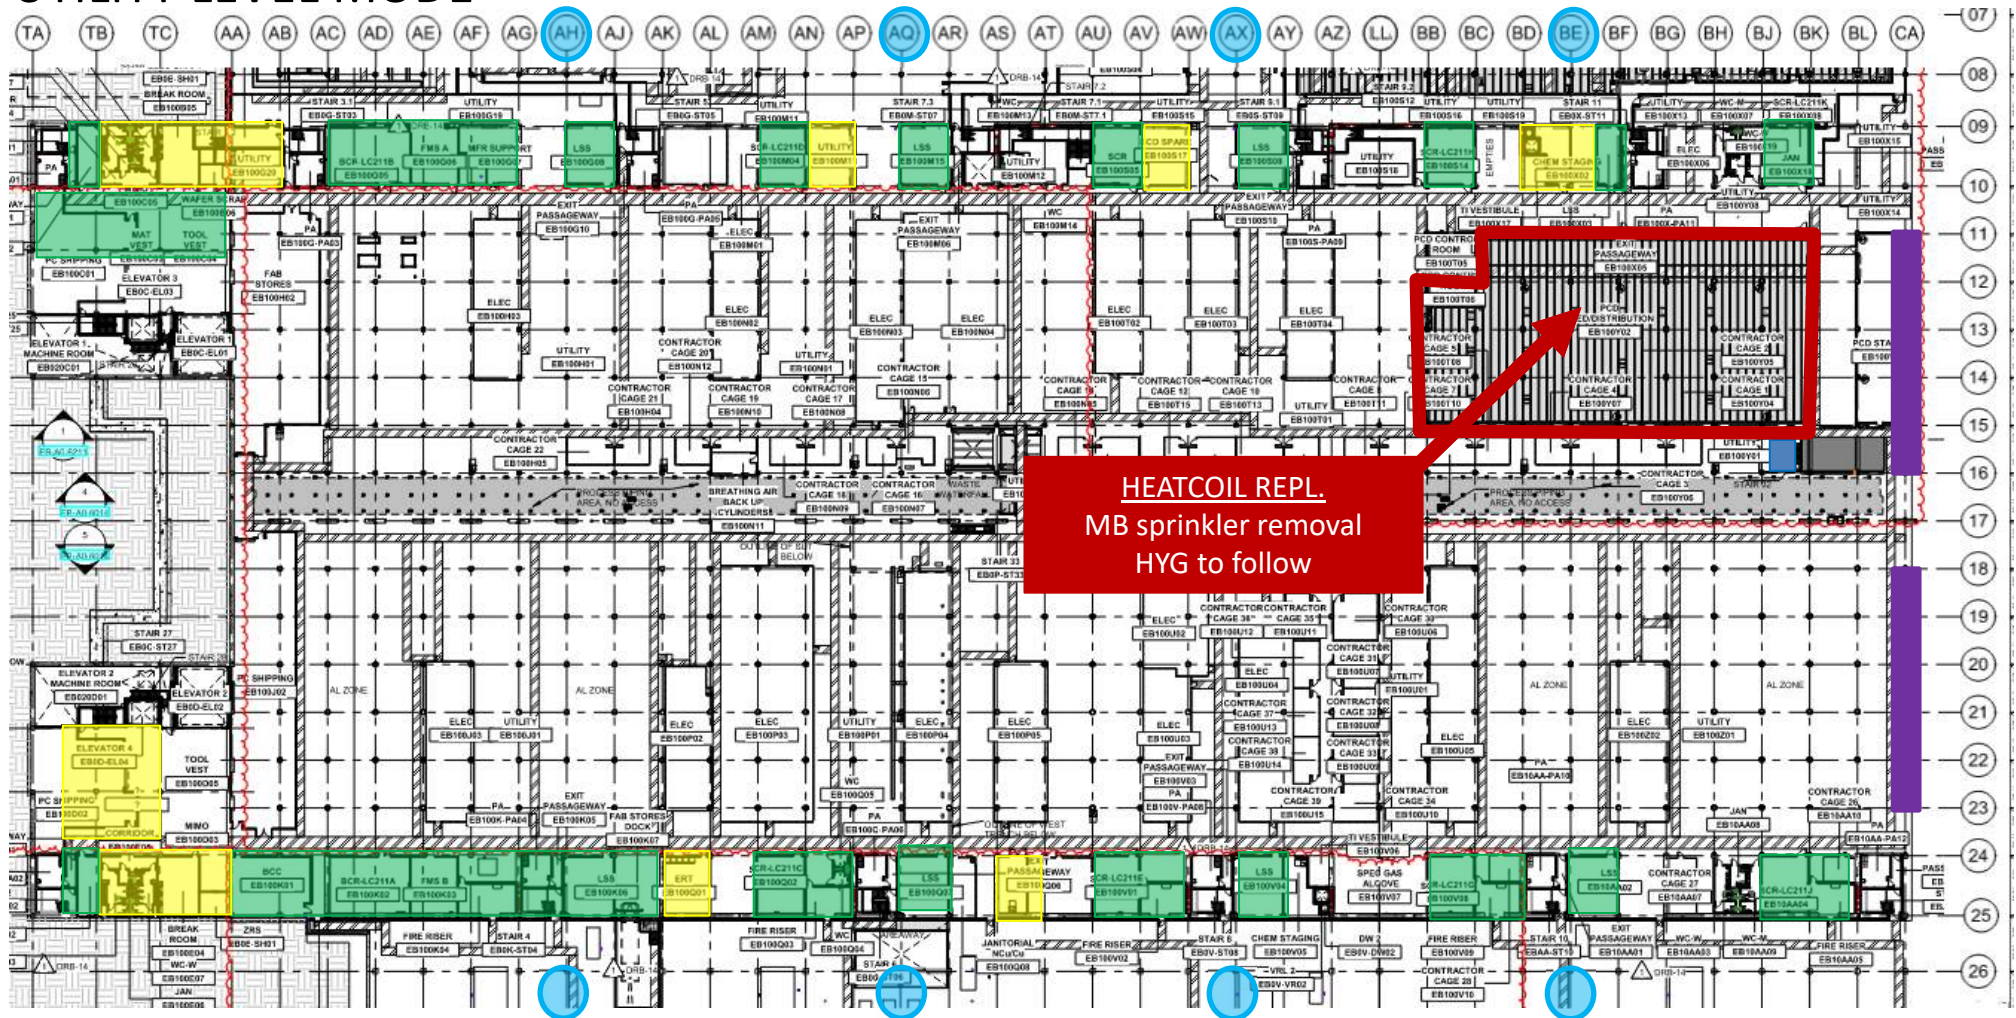


ELRAM
Drywall install


MEP+Elctrical
Ready for re-install



UTILITY LEVEL MOD2

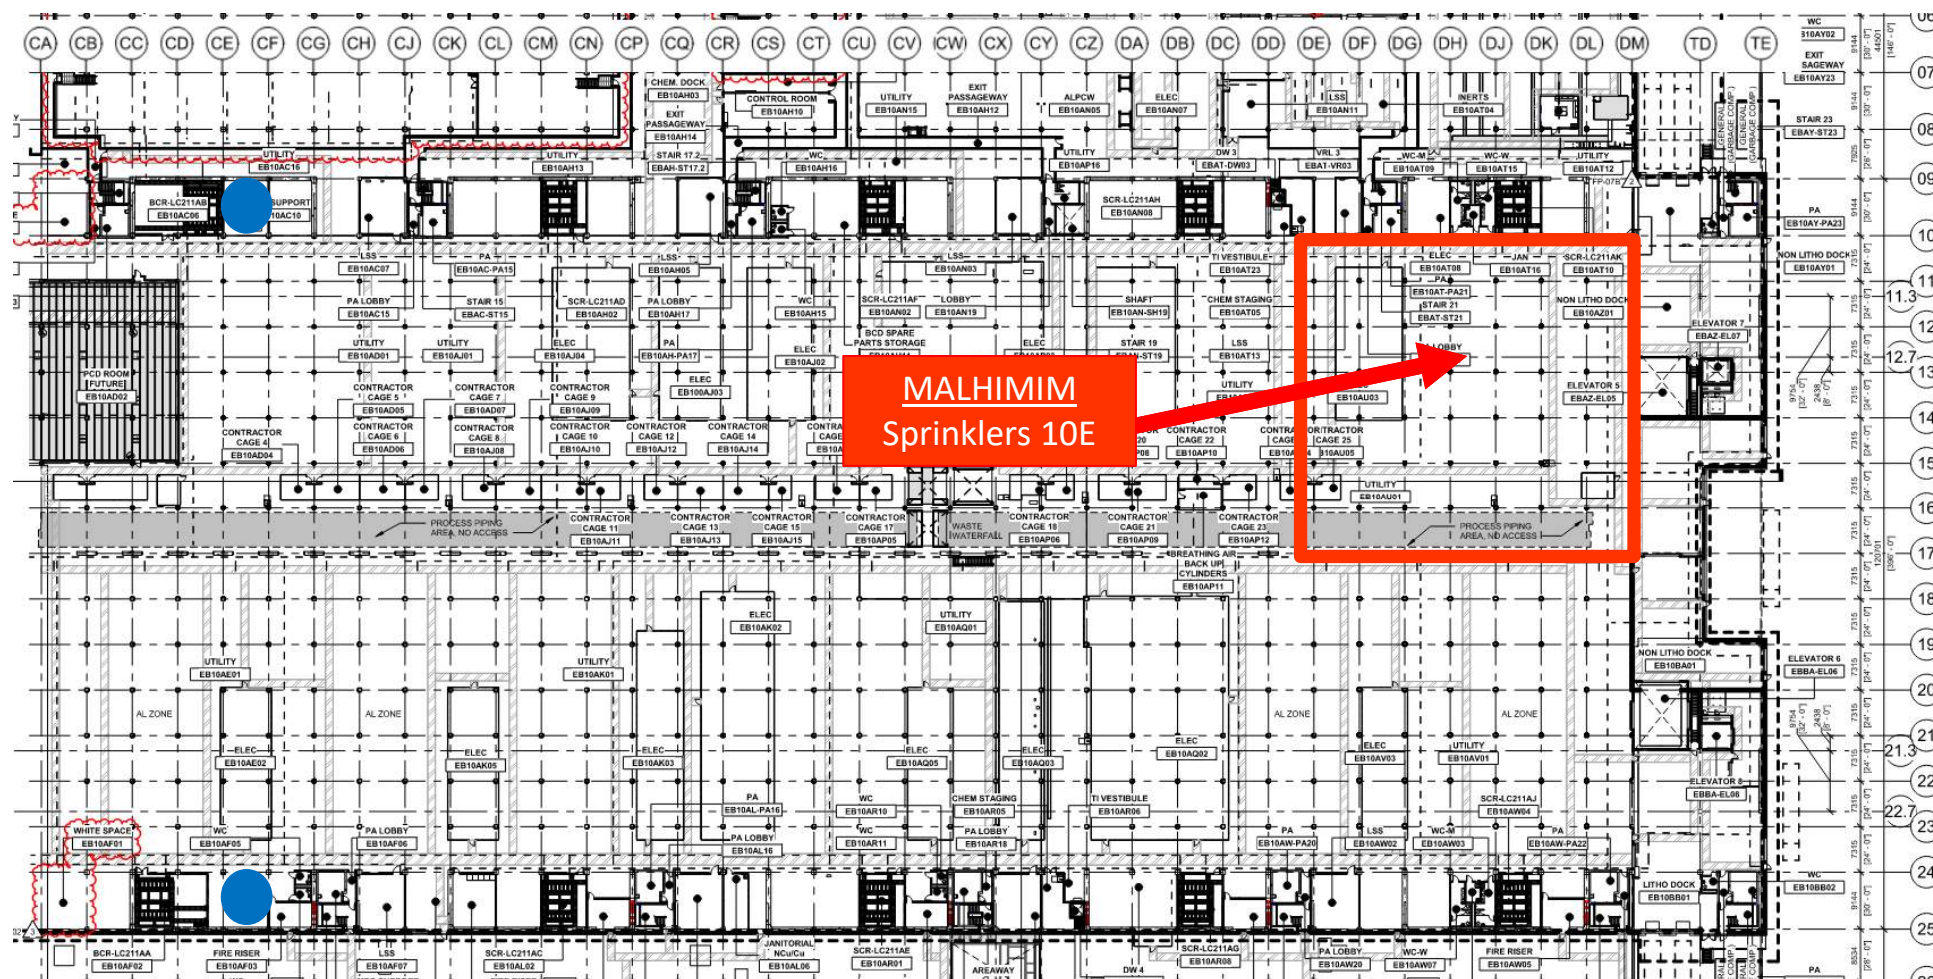

SUT 38.1 Accesses& Egress

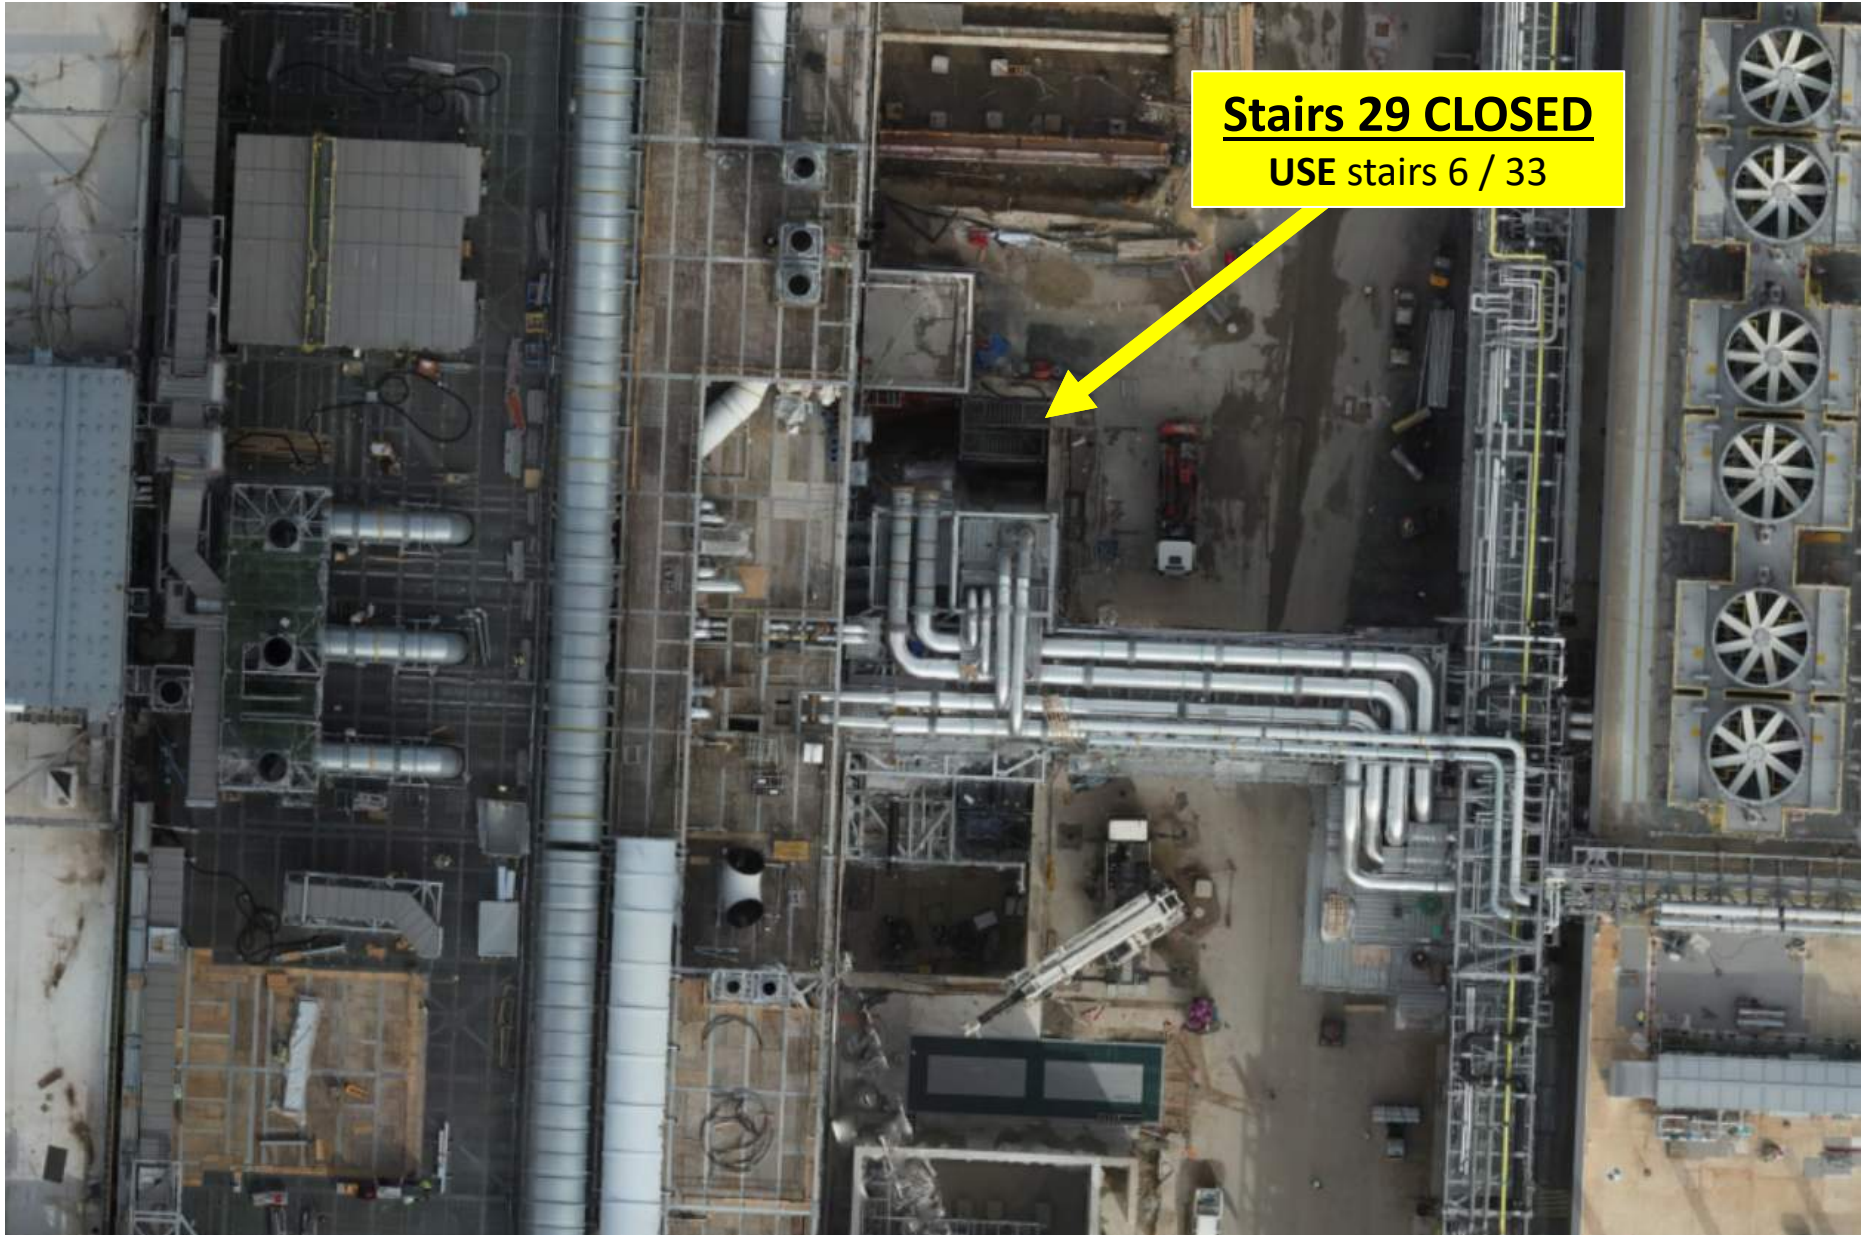

SUT 38.1 LEVEL

Scaffolding removal
NEED TO PROCEED

Stairs 29 CLOSED



STARIS 6

STARIS 33

CRC

- 1.HFW VFD
- 2.AW Pads x4
- 3.Biocide Curb Sump

Topping slab Schedule


- Pour 1 – 1/9 – 1/15
- Pour 2 – 1/15 – 1/22
- Pour 3 -1/22-1/27
- Pour 4 – 1/28-2/4



HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

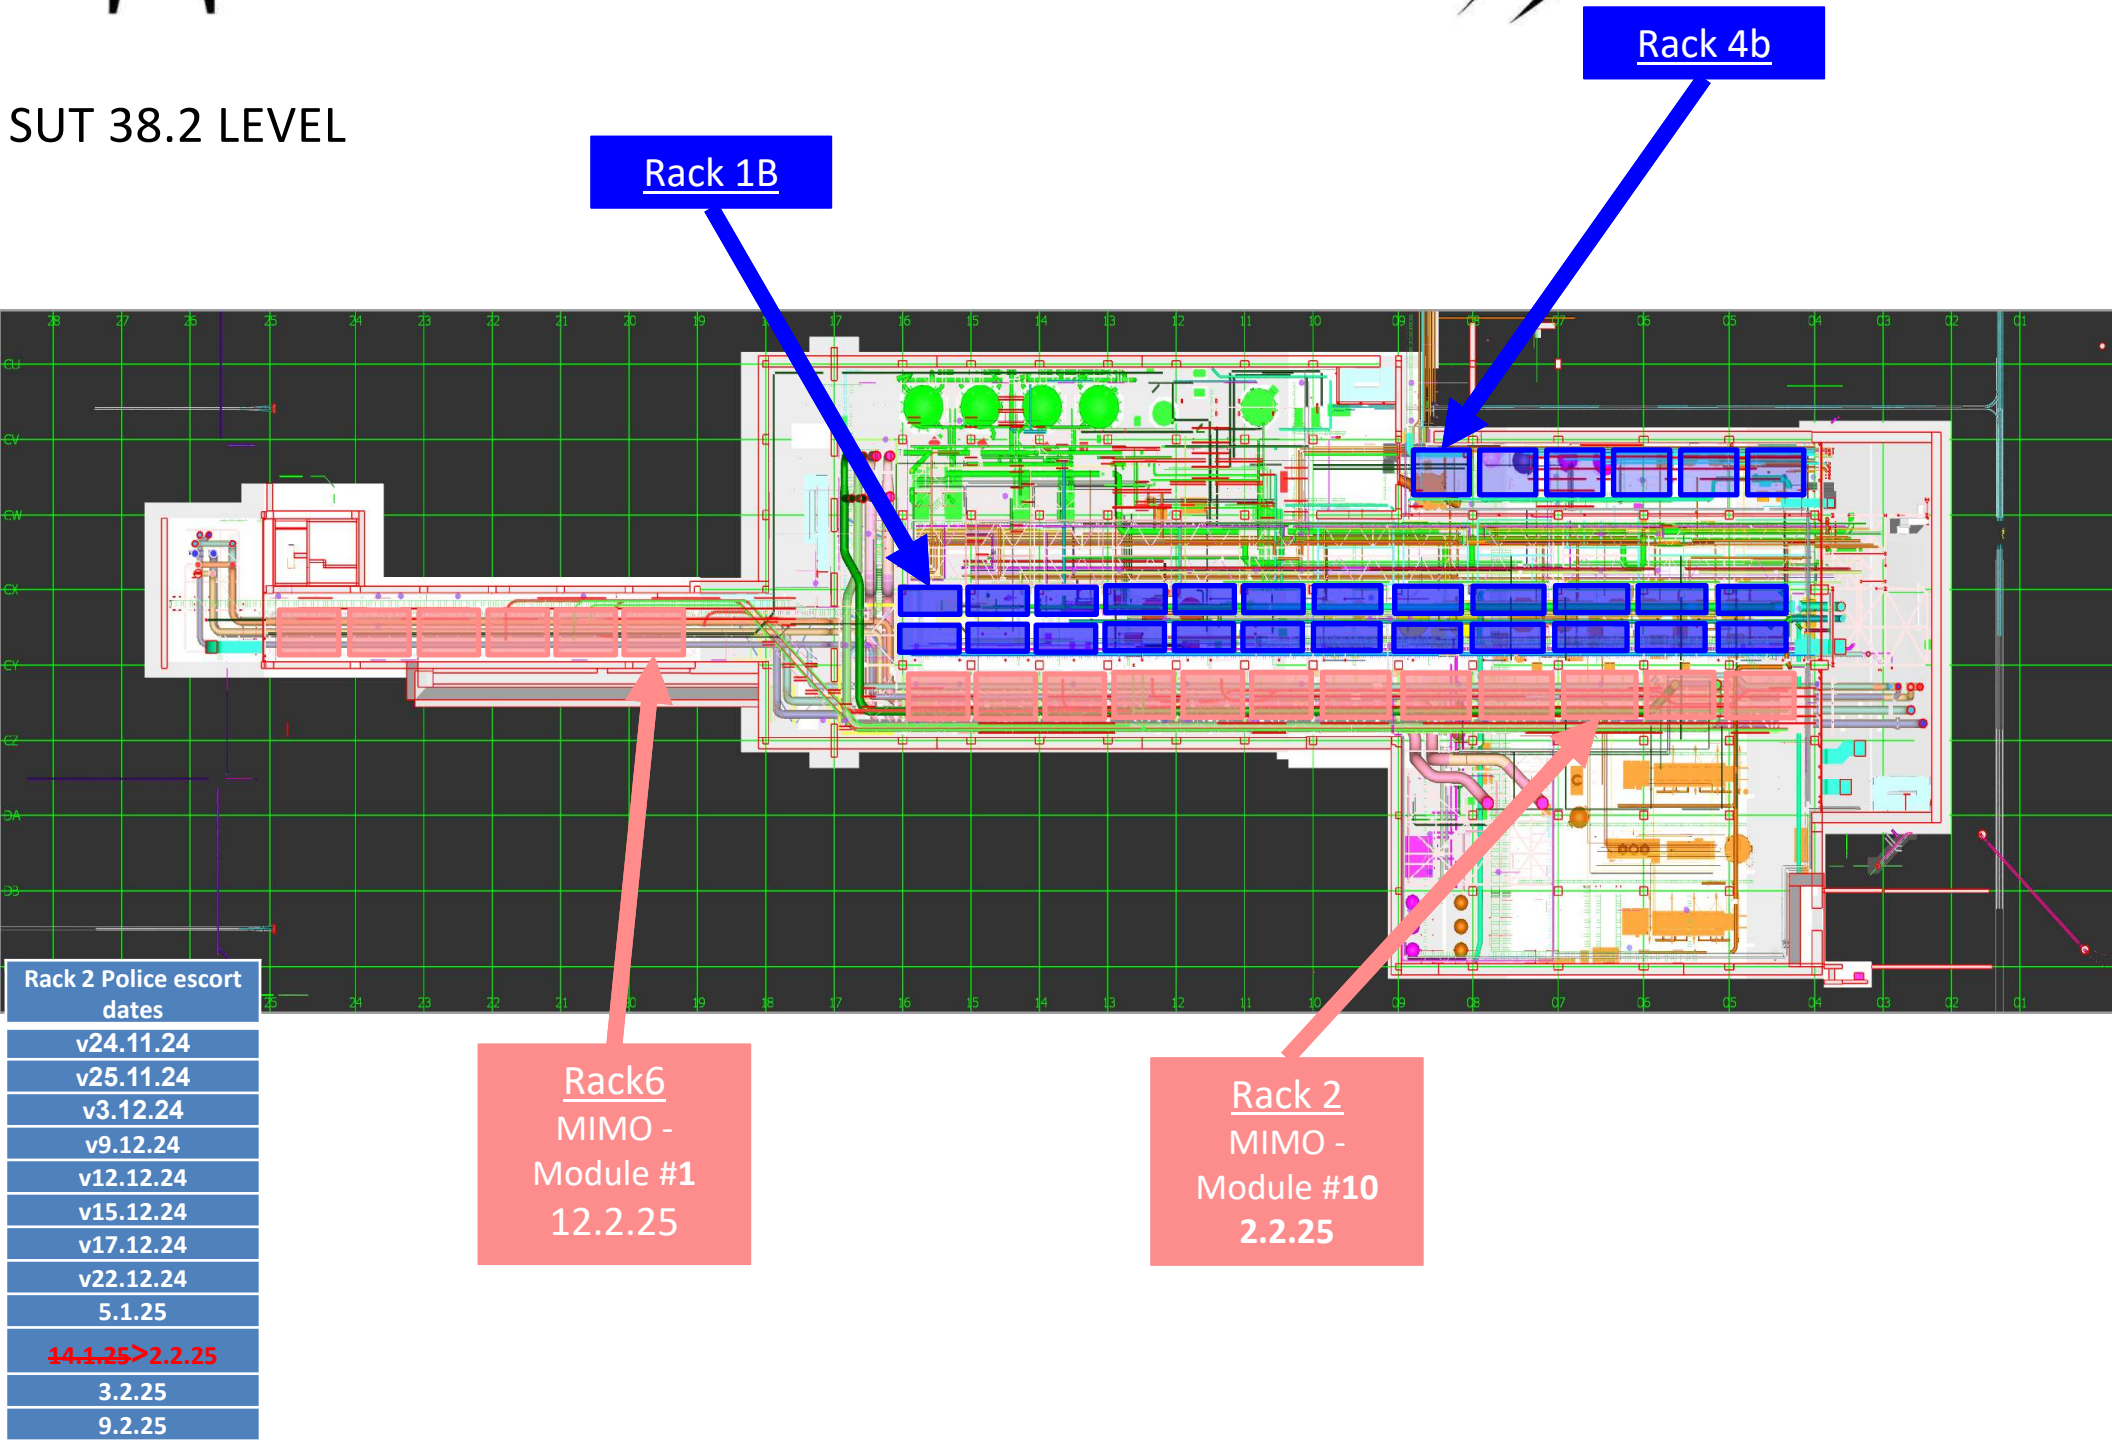


Rack 1B

Rack 4b


Rack 6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25


SUBFAB BUILDOUT MOD 1

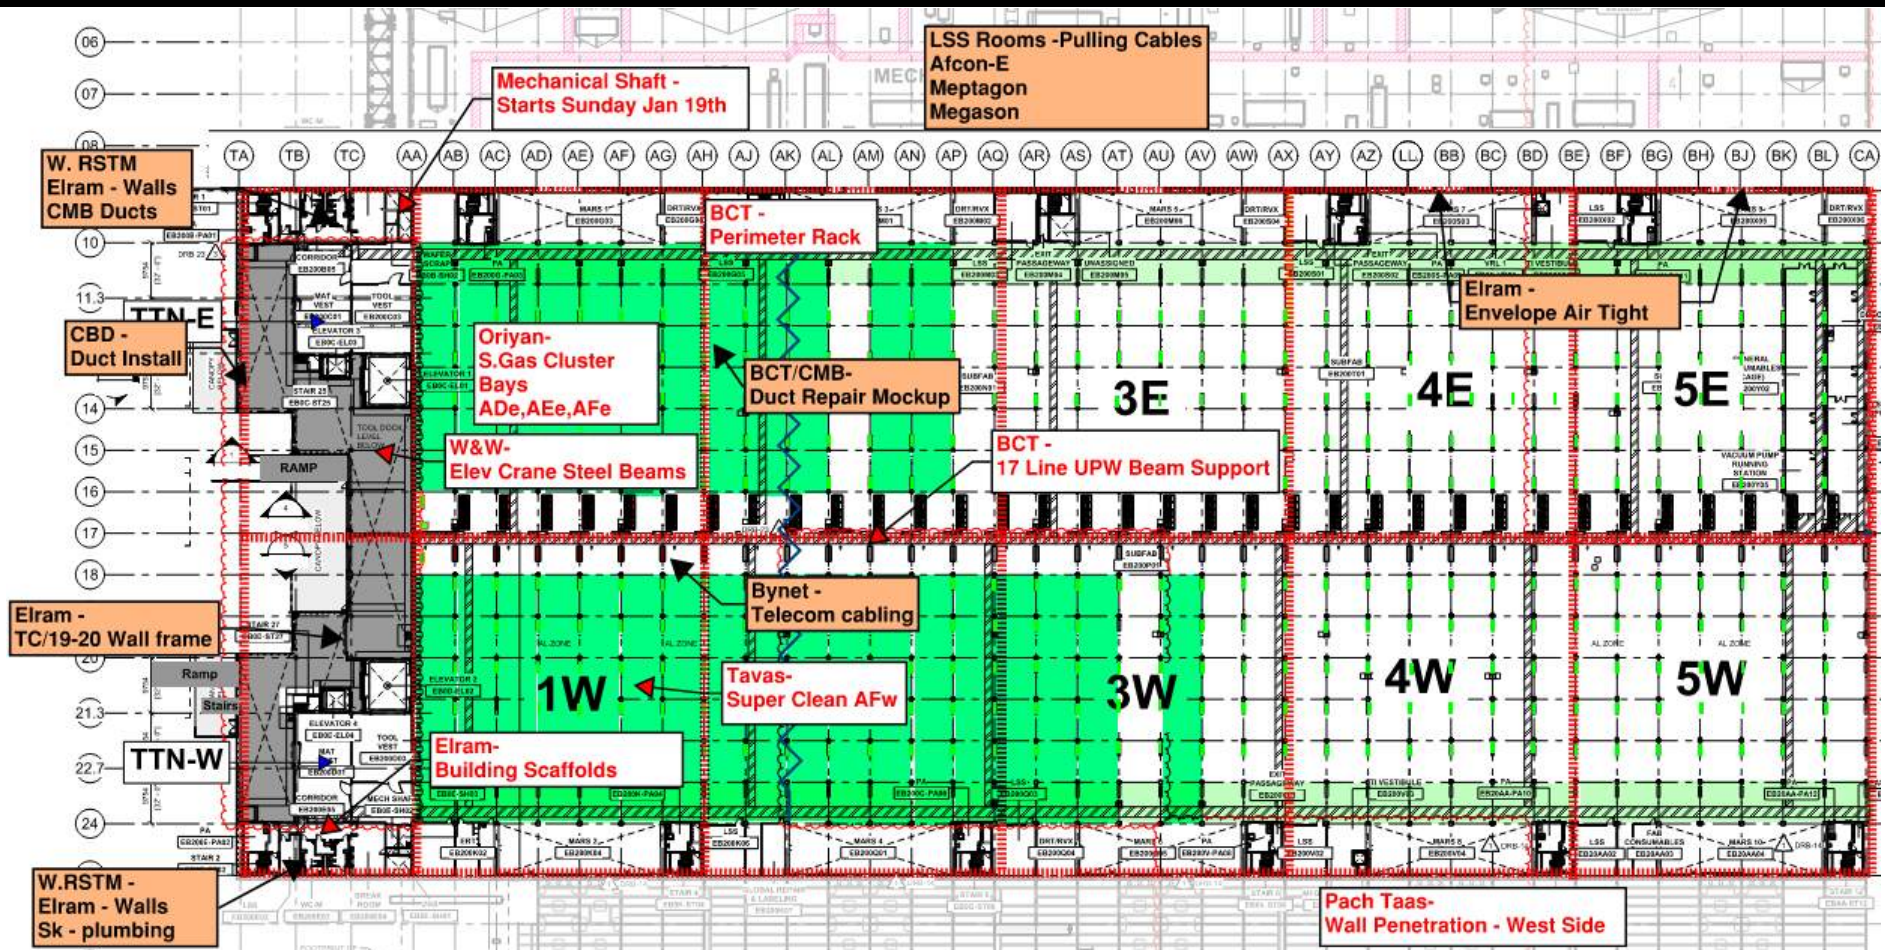


SUBFAB CRC TOPCOAT

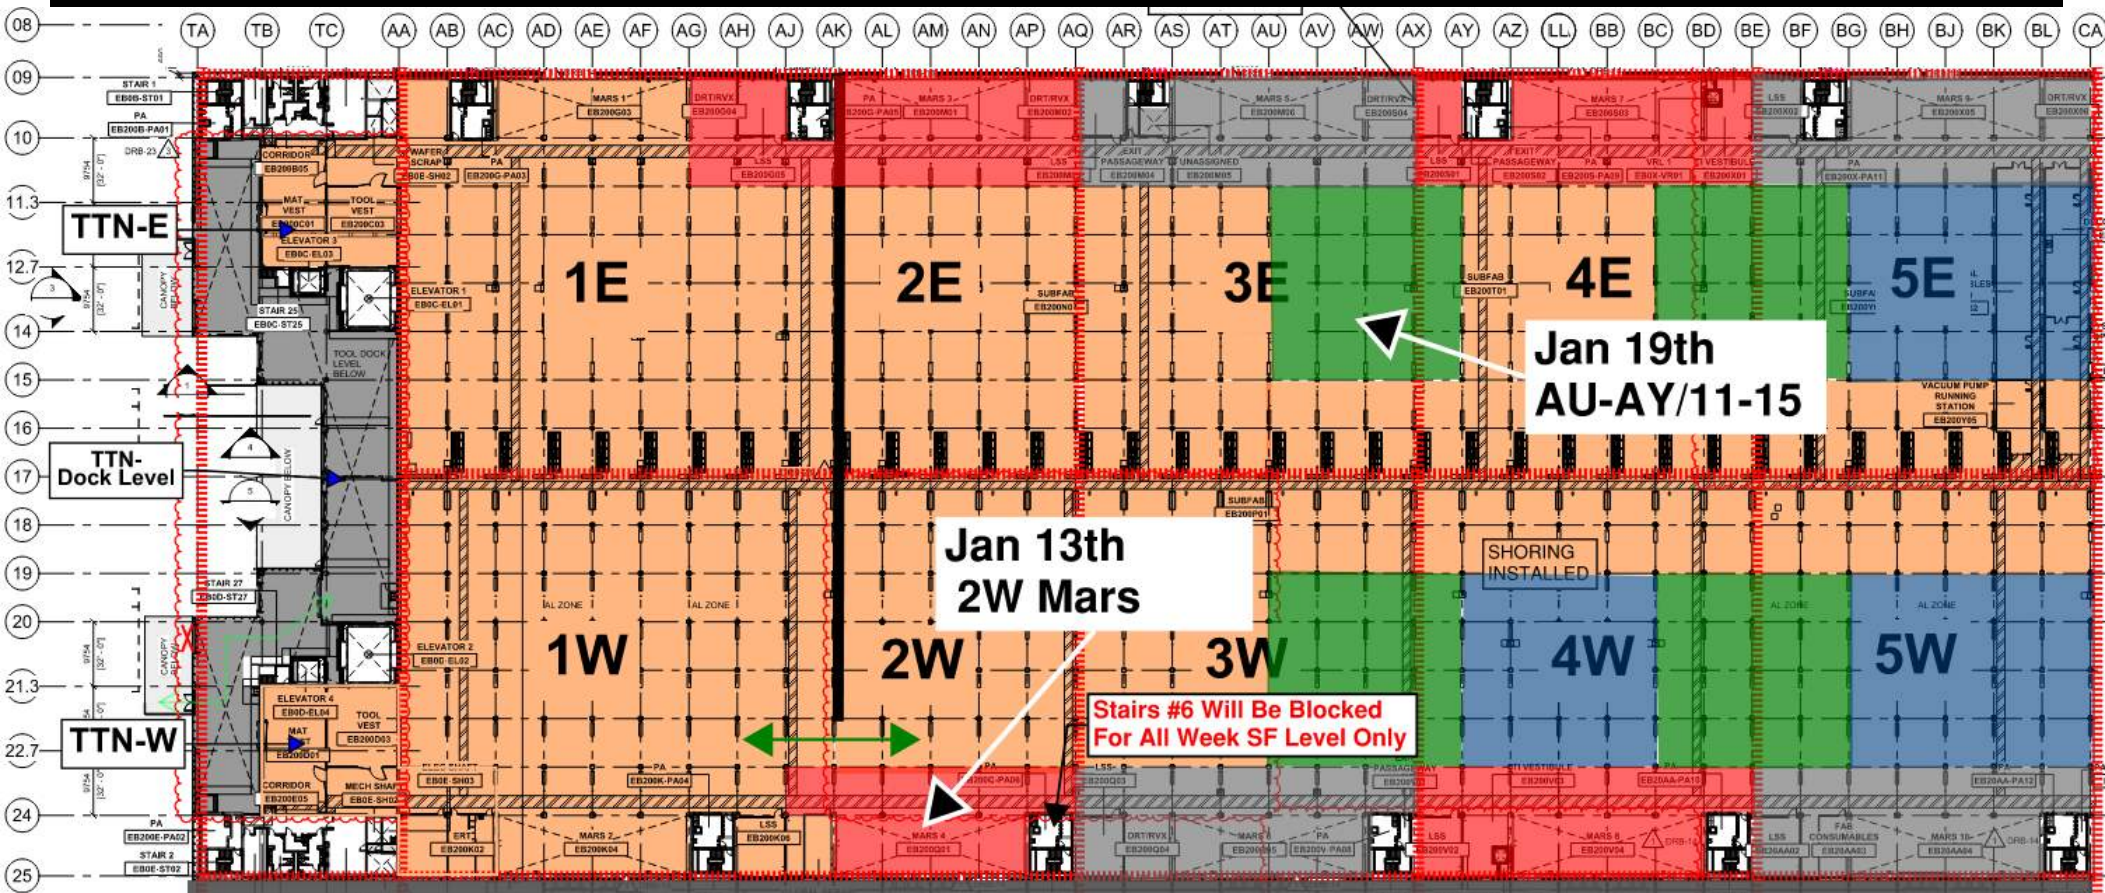


BCT Pressure Test Tomorrow

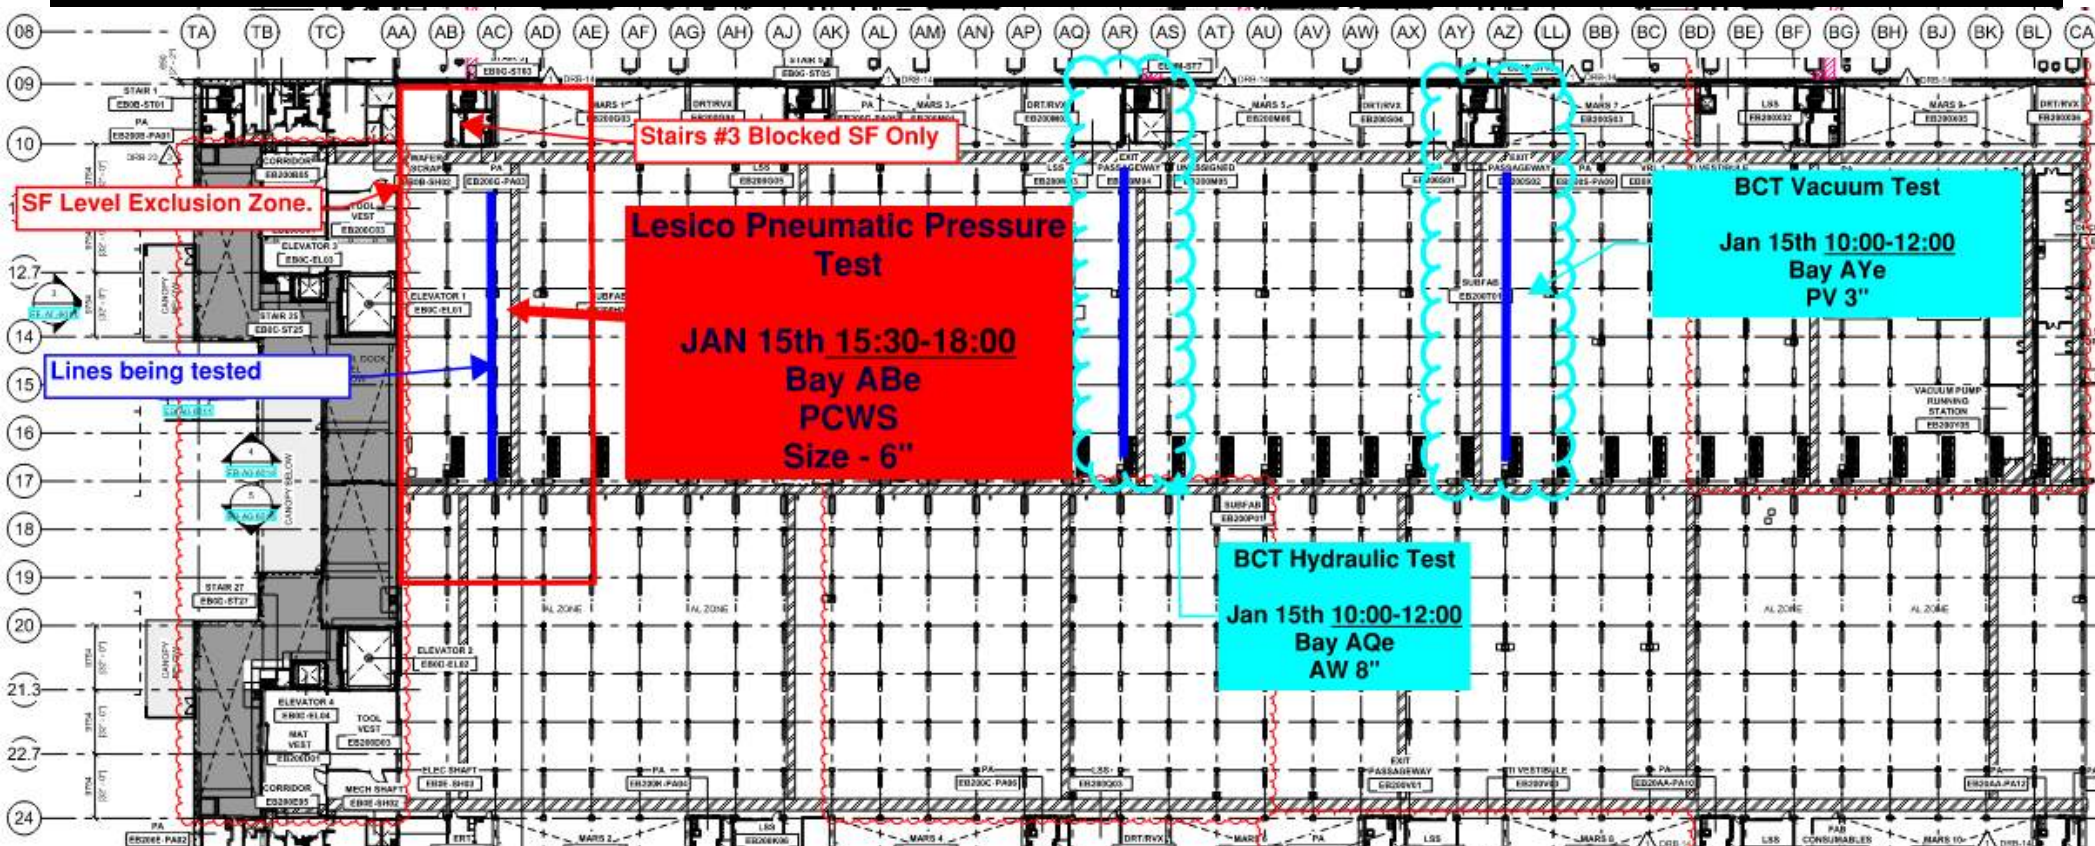

SUBFAB BUILDOUT MOD 2

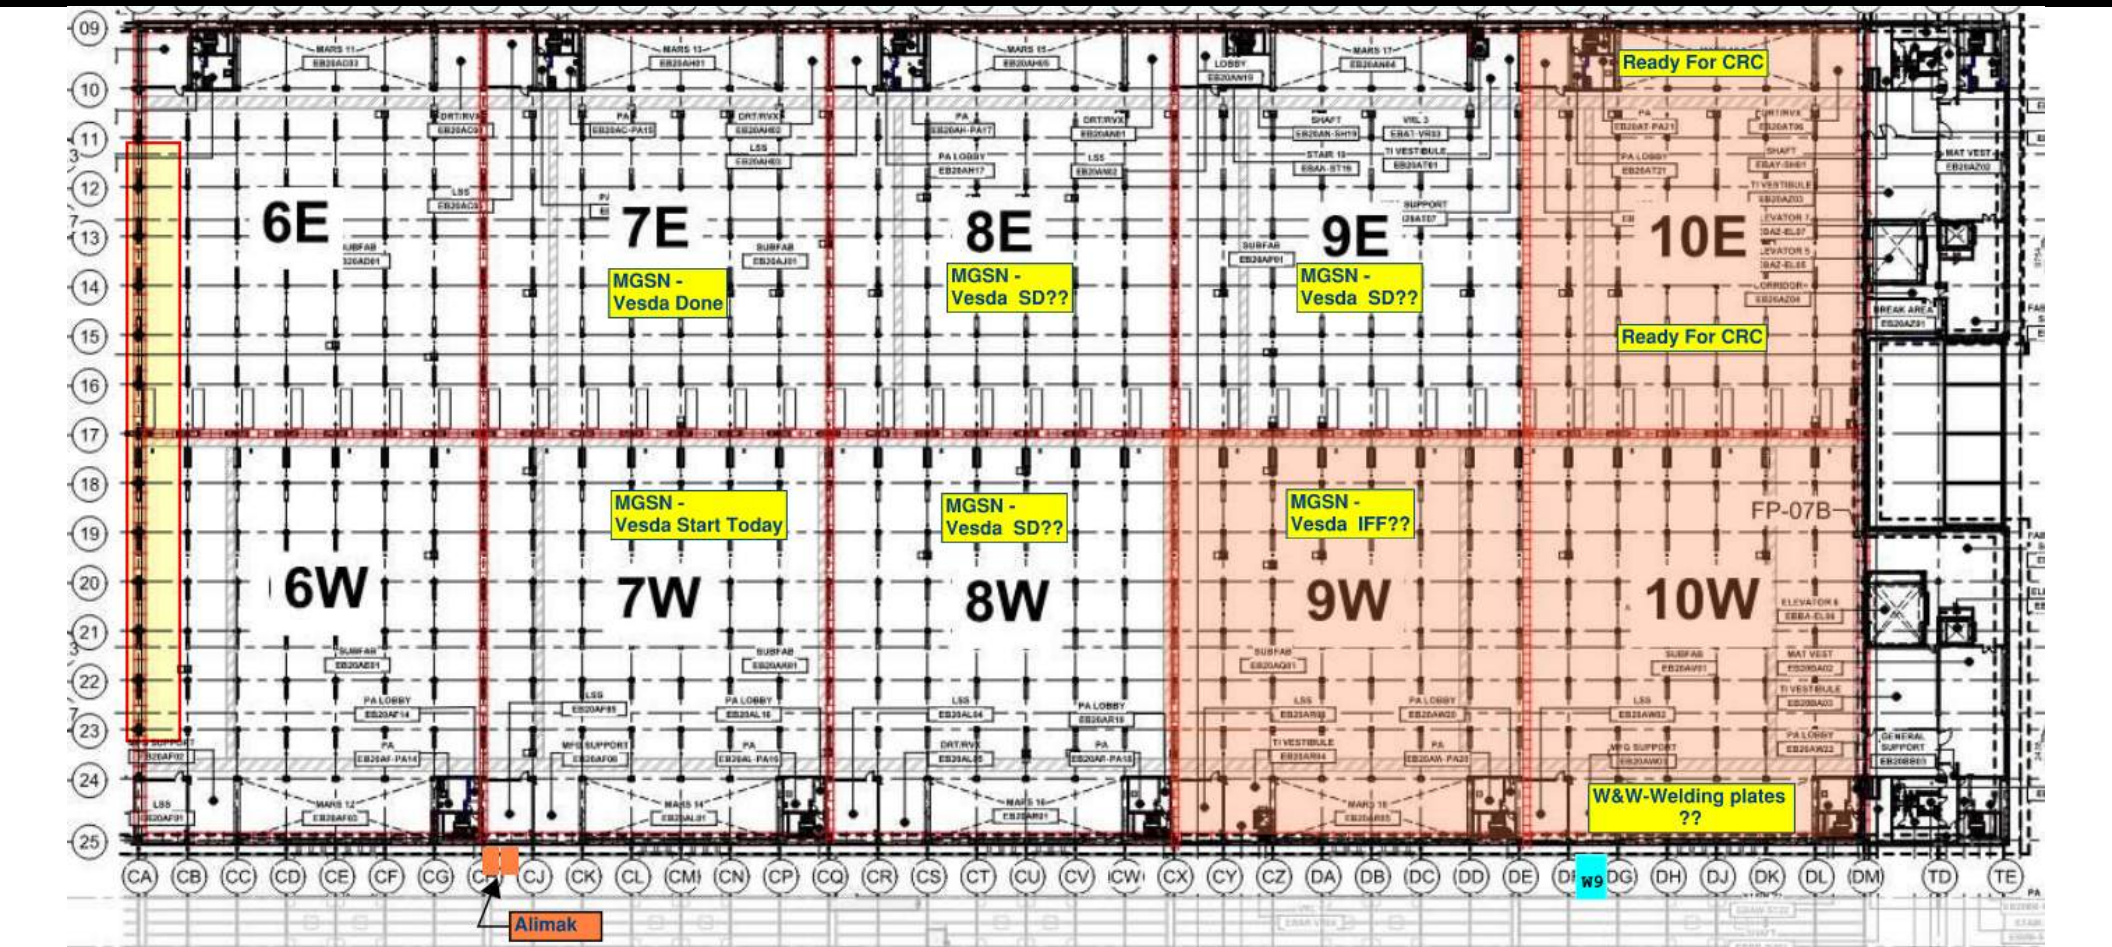



4da mimo goes
down on 26th jan.

HSI - Slab poured.

CR level:
Afcon - Cable trays, modules and stickers
MB - Pipes and drops
Elram - Columns/shaft walls.
Meptagon - EMT Pipes+devices. TET/NET devices all areas
D&P - Stick build+ separation walls+FFU
Tzur-esh - 1W blade paint
HYG - Deck and bent plates
Talad - UPN install, ceiling grid, lids removal

MB - FS install
NETT+NWTT
Elram - G1 wall AA
line
Meptagone- EMT
Pipes+devices
C-B- Duct install

Talent- Super clean 2E
Tavas - Super clean 2W
Sela - 1W-1E touch ups
ongoing. Prep 2W

SELA TURNS
1W
PVC - TALAD

HSAI-started
rebaring somd
west tt.
Sk-verify all
verticals are in
right place

Link
Pach-Taas - exhaust duct install and tie in
SIG- Mobile scaffold install
Afcon- Rack install
Newcotech- Temp wall
Afcon - Cable tray & racks install
Sela - CRC waiting for QC turnover
Talad - CRC protection cover





4da mimo goes down on 26th jan.

Chemo 1E skids-
Passivation ongoing

Int. level

- WW/SN - Catwalk and handrail install. Grating penetrations
- Chemo- 10" pipe racks+skids
- Afcon - Cable trays, modules, cable pulling, 1W,2E,2W,3W
- HYG - 5RA added beams 3E
- MB- 3E,3W pipes
- SK- IA pipes 10/24 line
- Elram - Column wraps 9,10,24,25 lines+ G1 wall
- RP- FP 4DA 4W. 3E - 5RA Girts
- Tzur-Esh - Steel paint 5E,4W,5W
- Megasone - Small wires+ speakers 2W,3E

RPC !!

**SIG- 5E 5RA SCAFFOLD
MOD 2 17 LINE CA:CJ
THURSDAY**

NETT
MB- FS install touch ups
Chemo- Racks on hold
Megasone - Small
wires+Speakers
NWTT
Chemo- Racks on hold
MB- FS install

Tavas - Super
clean 2E-2W

INTERSTITIAL

RPC

**GRATES REMOVAL BY
TALAD WILL FINISH
BY THURSDAY**

Talad-
5W grating removal starts
on sunday Jan-13th

MIMO 4DA the passage will
be narrower


LINK

JUNGLE GYM

Mod 2 E House Roof
Picks.
Jan 14th @ 4:00 AM
Jan 16th @ 4:00 AM

Area to be
Closed for
Swing

Condensed
Barricade
for Bolting.

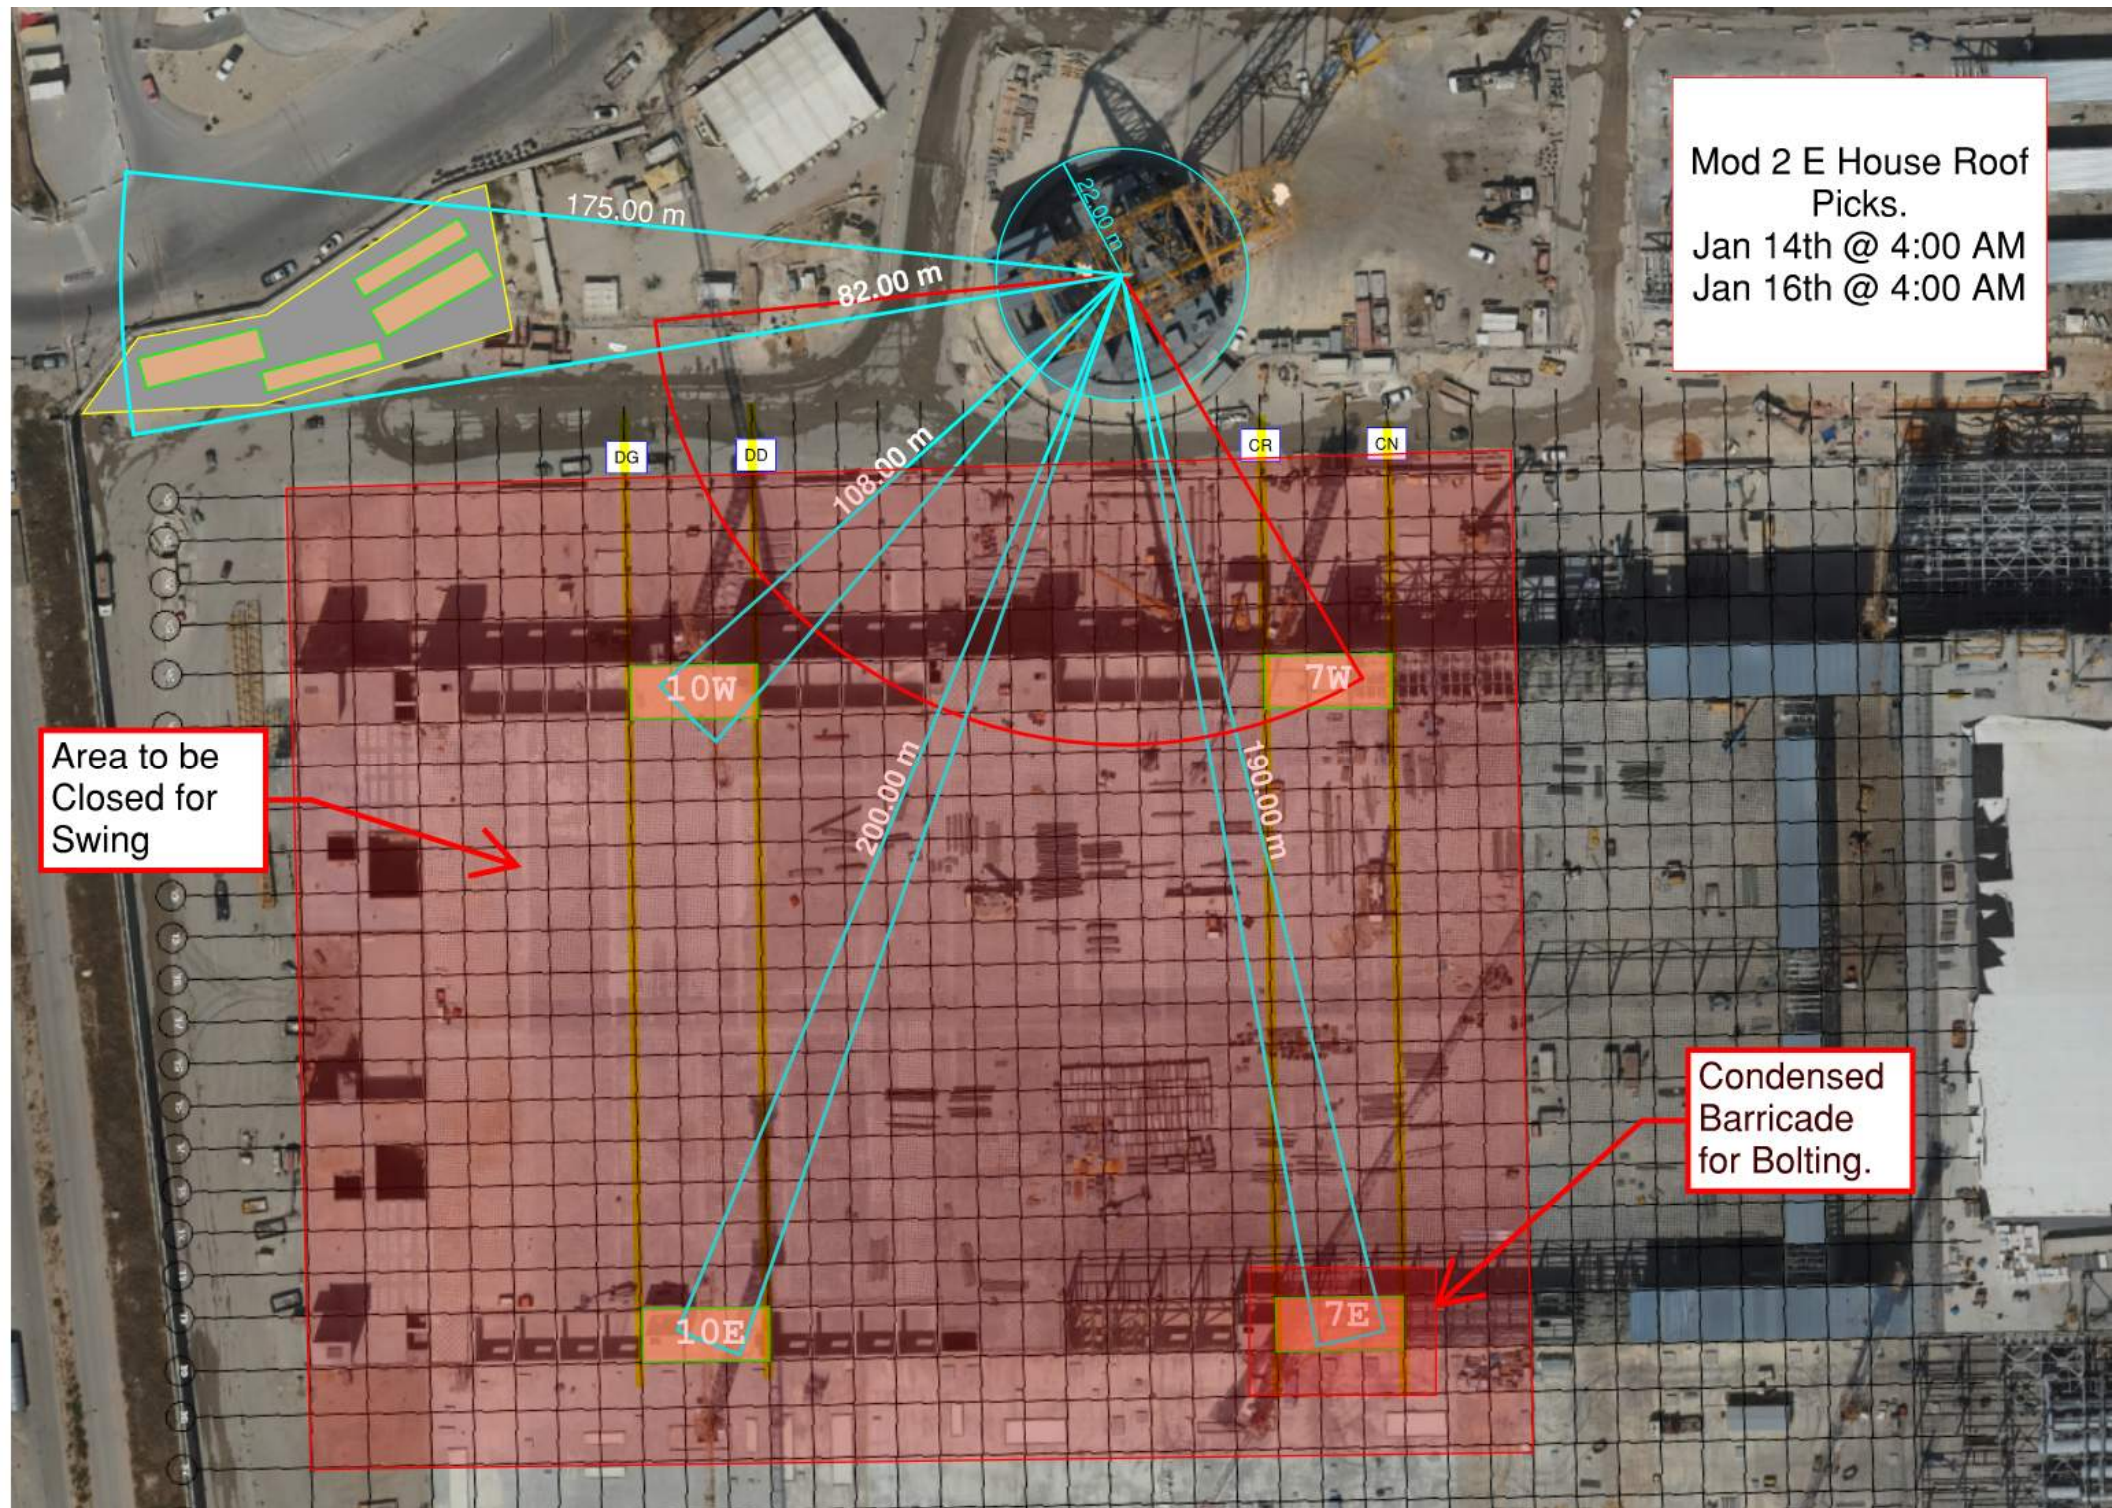

Siding - West FAB - JYG


BLOWDOWN 30%

Link


Siding - East FAB - PSSS


BLOWDOWN 30%

[illegible]

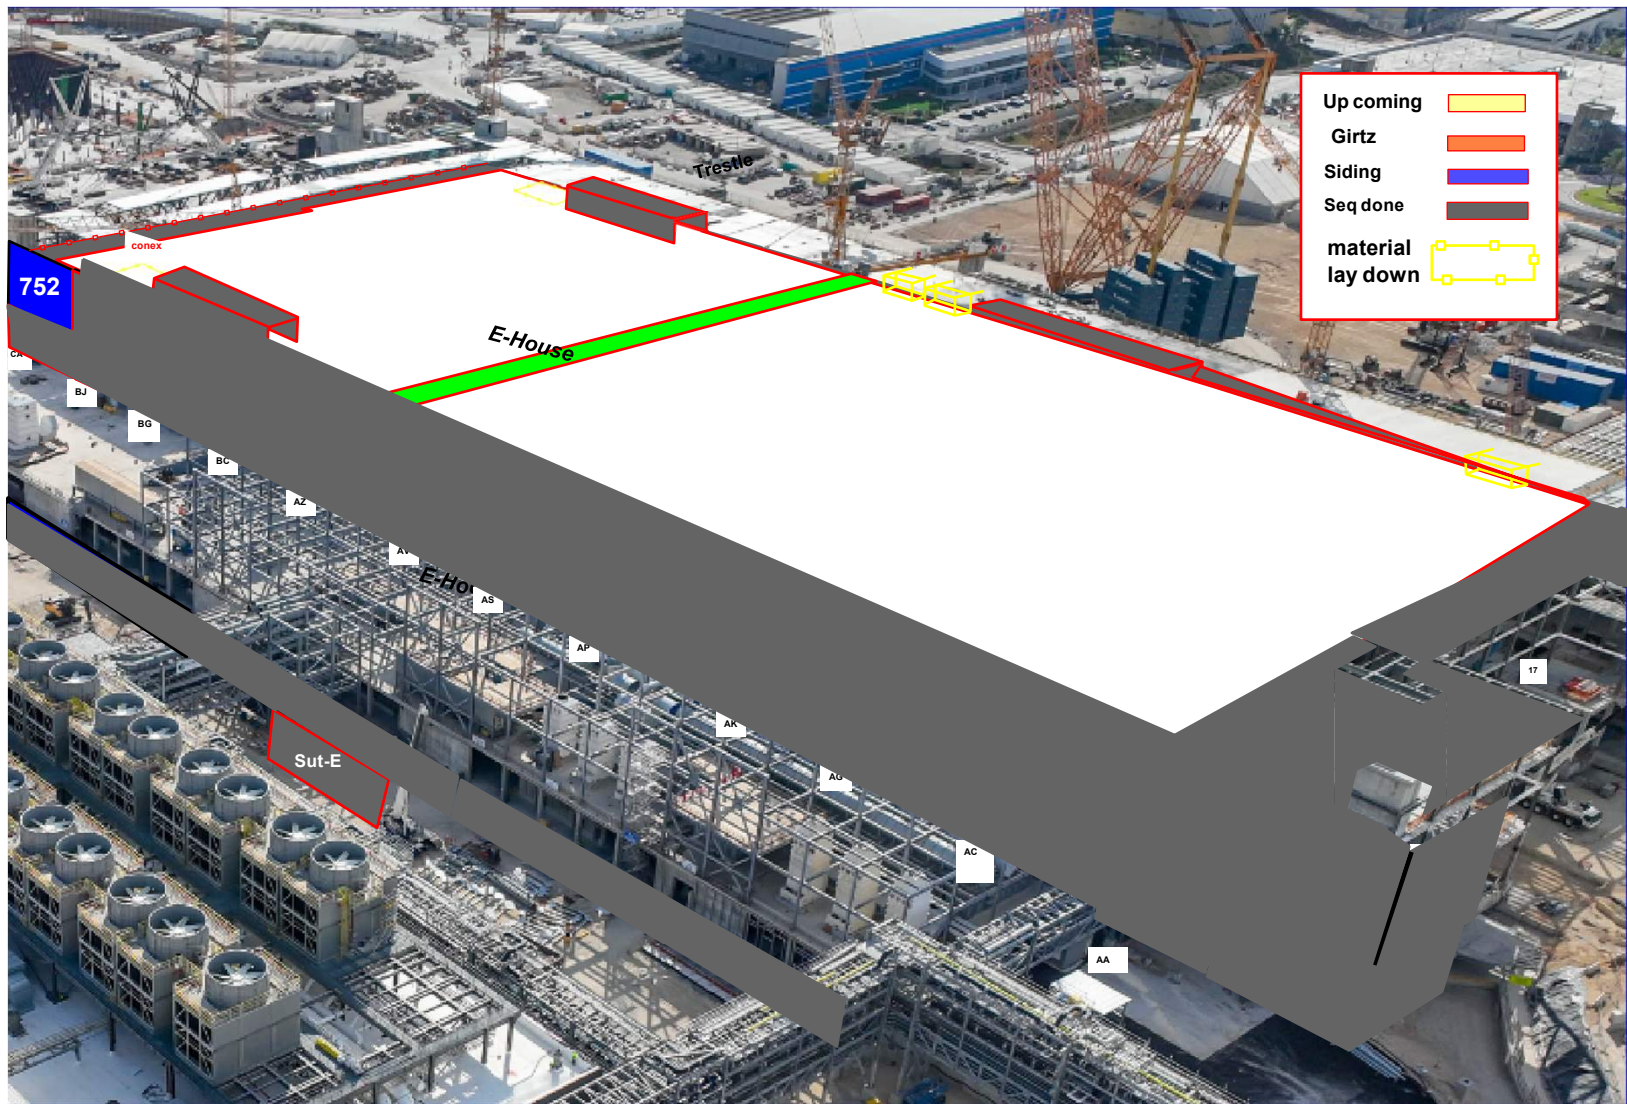

Walkpath

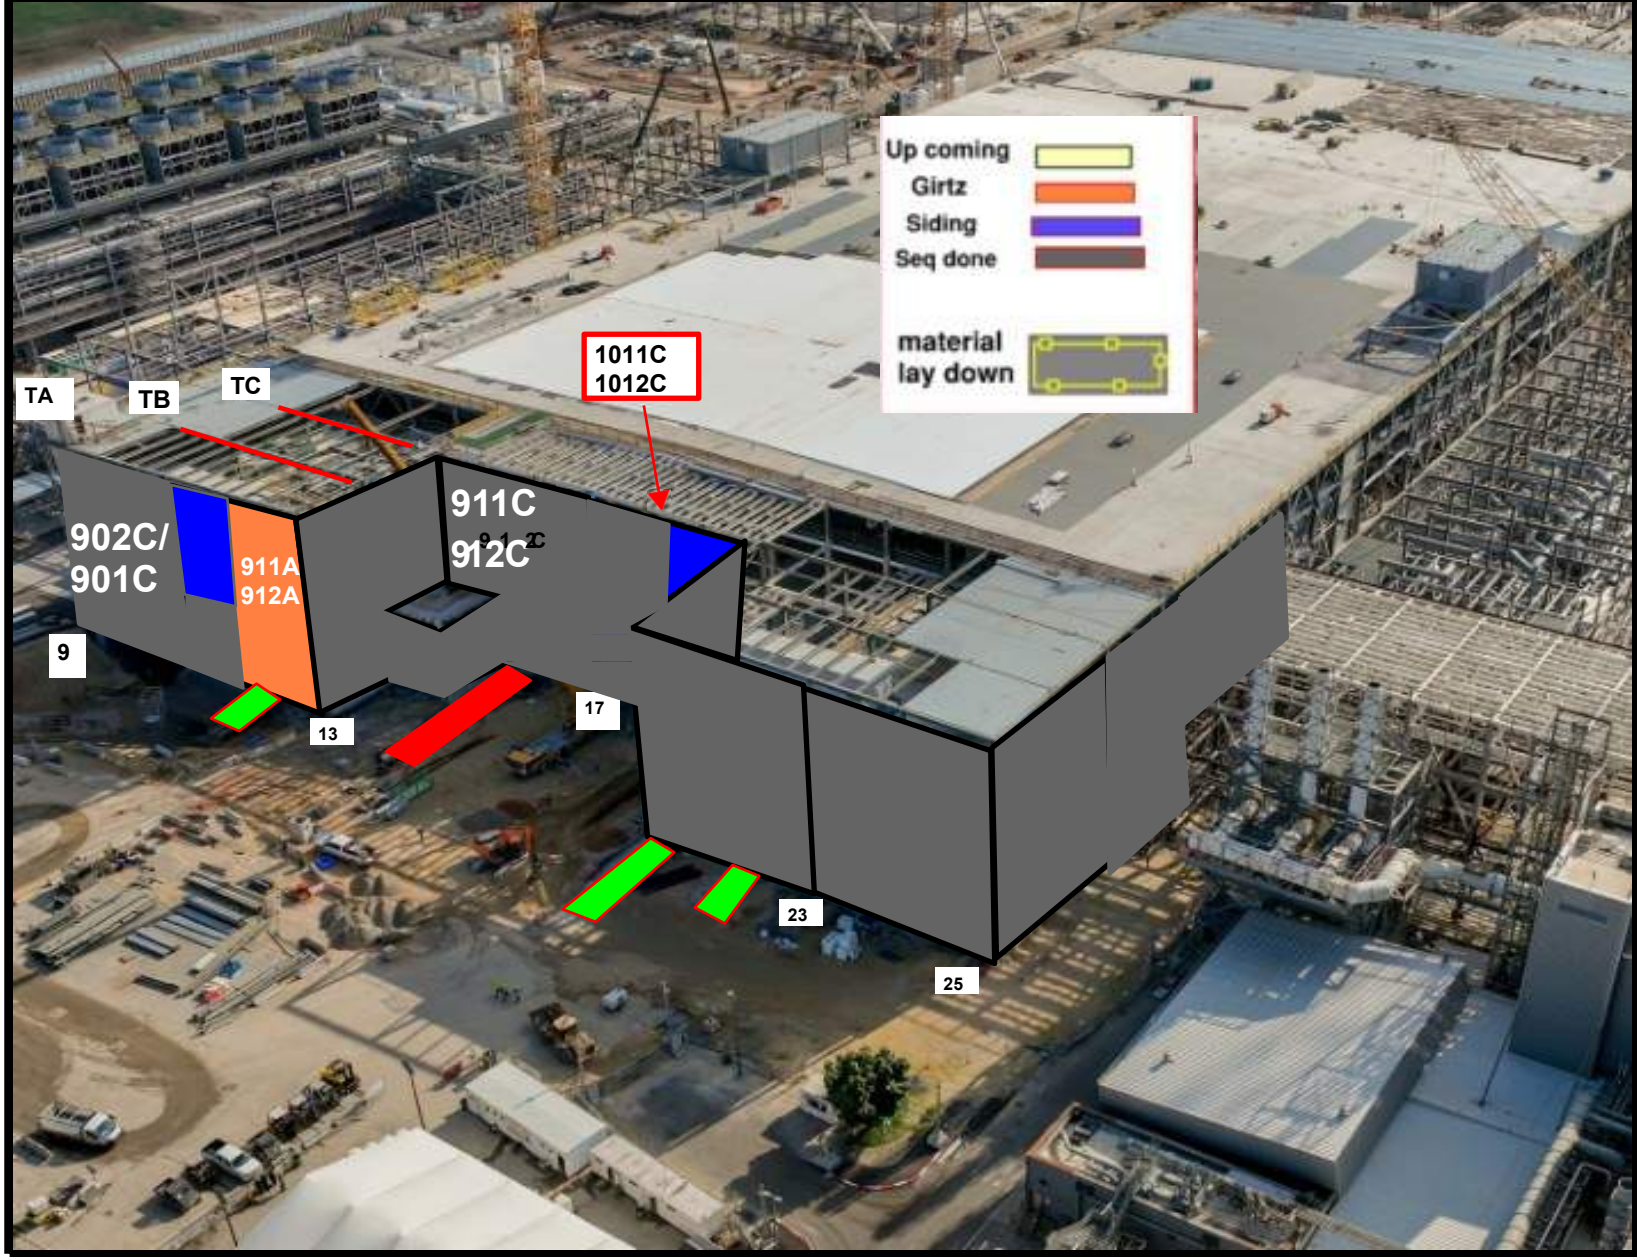

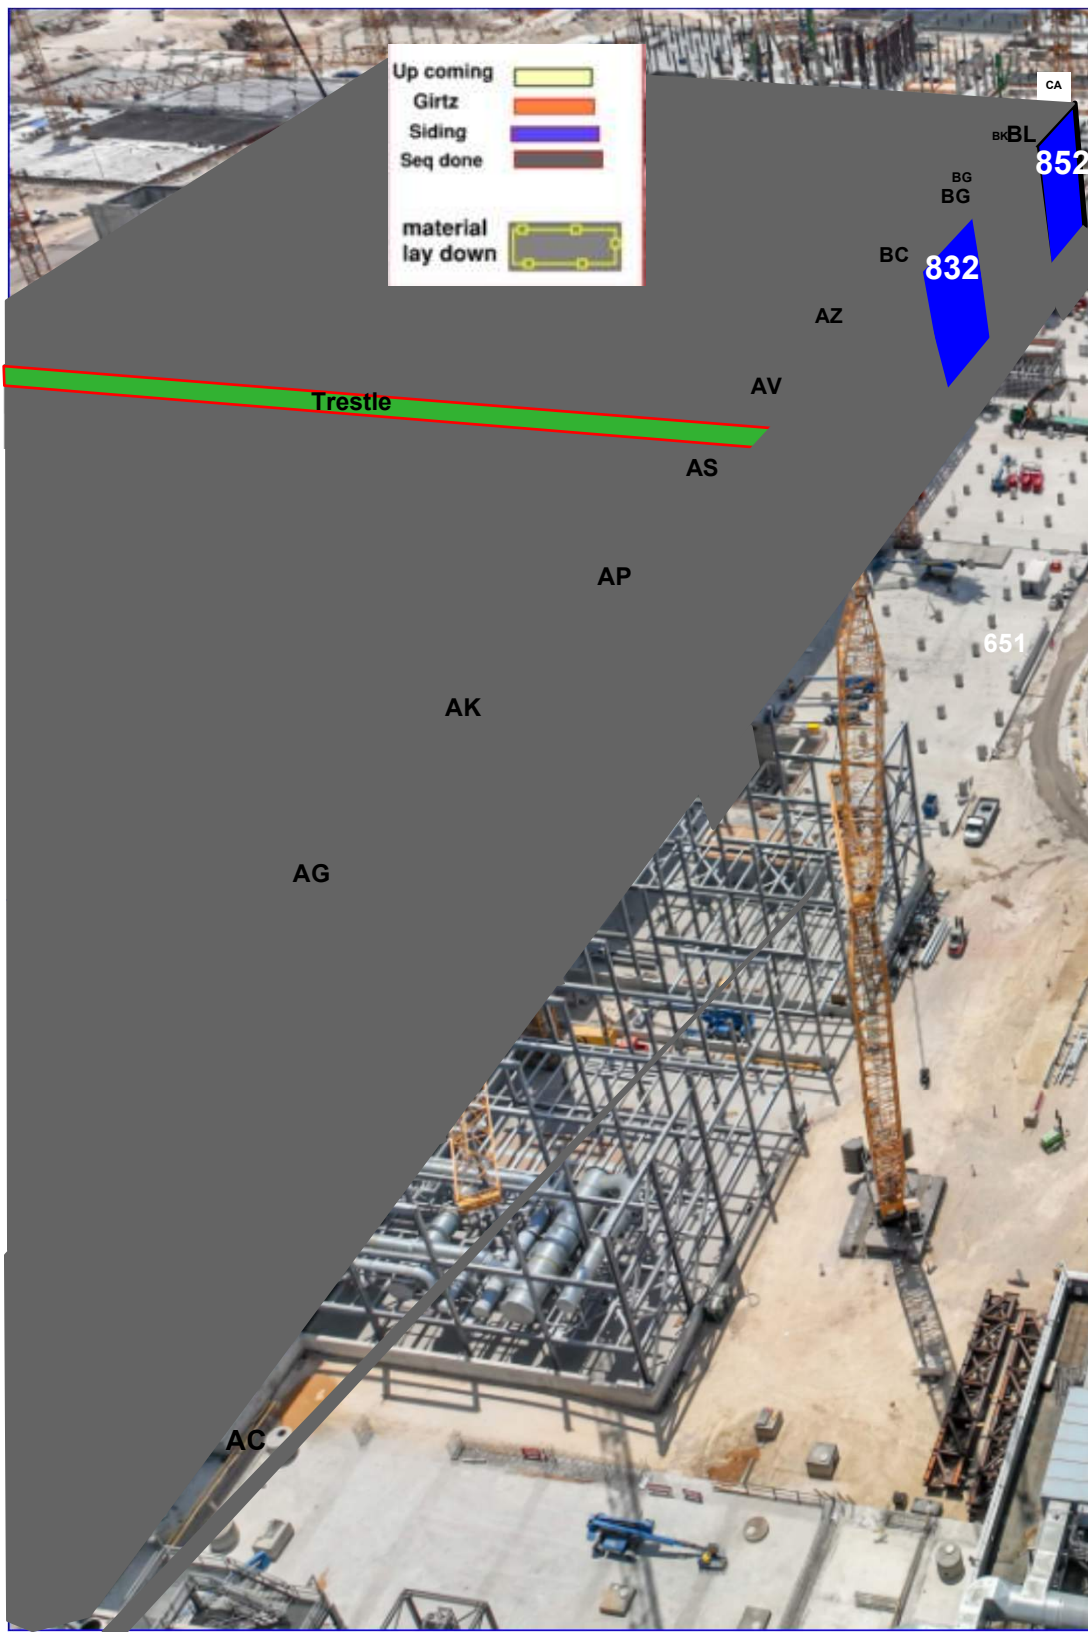

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

Utility Level 1YA



PSSS.2

6P


7P

8P


9P

10P

Utility Level
1YA

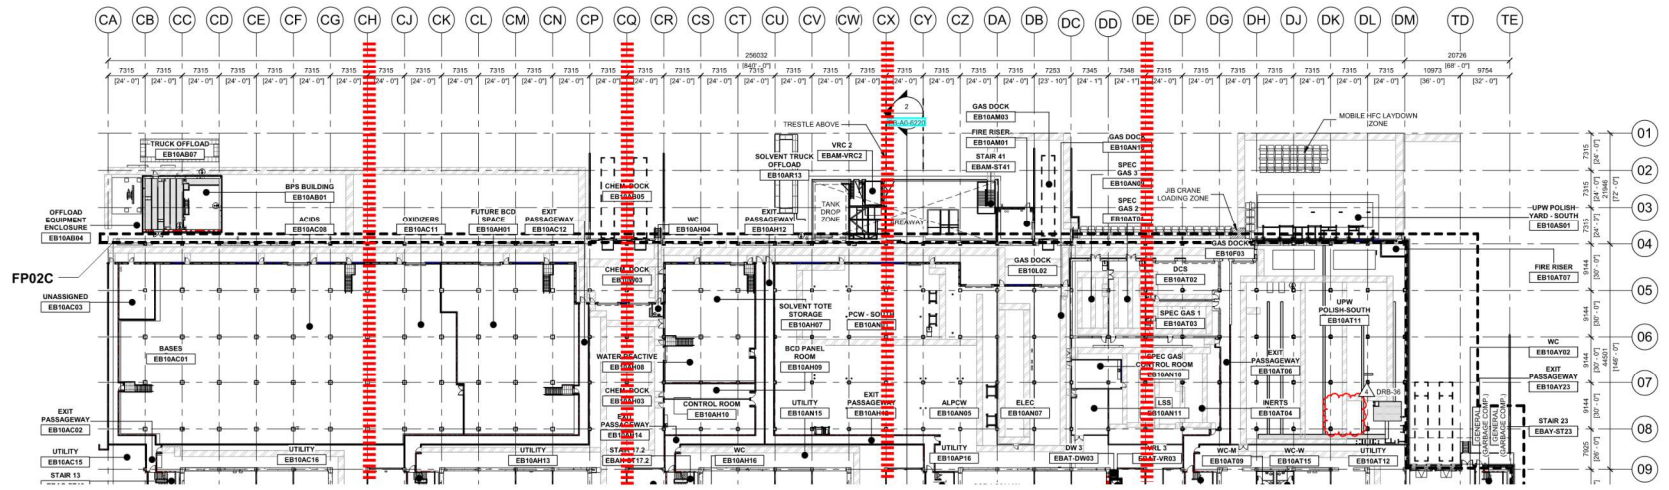

PSSS Roof
2SA

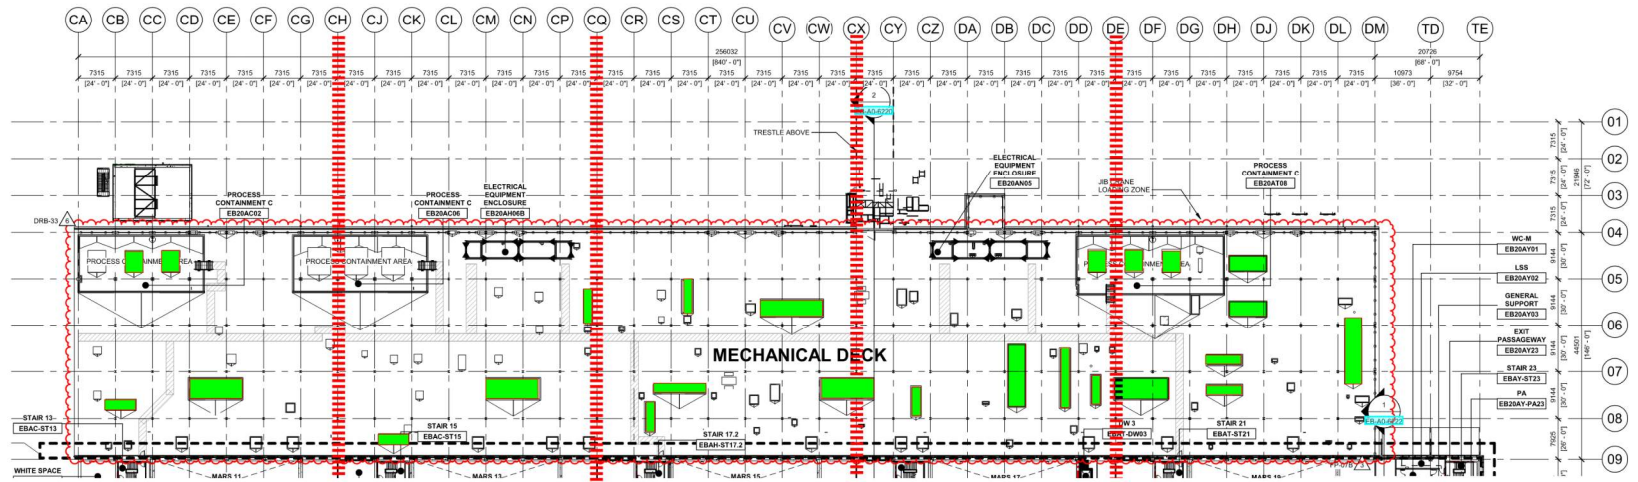


PSSS Pressure Tests

5P

Utility Level

1YA


PSSS Roof 2SA

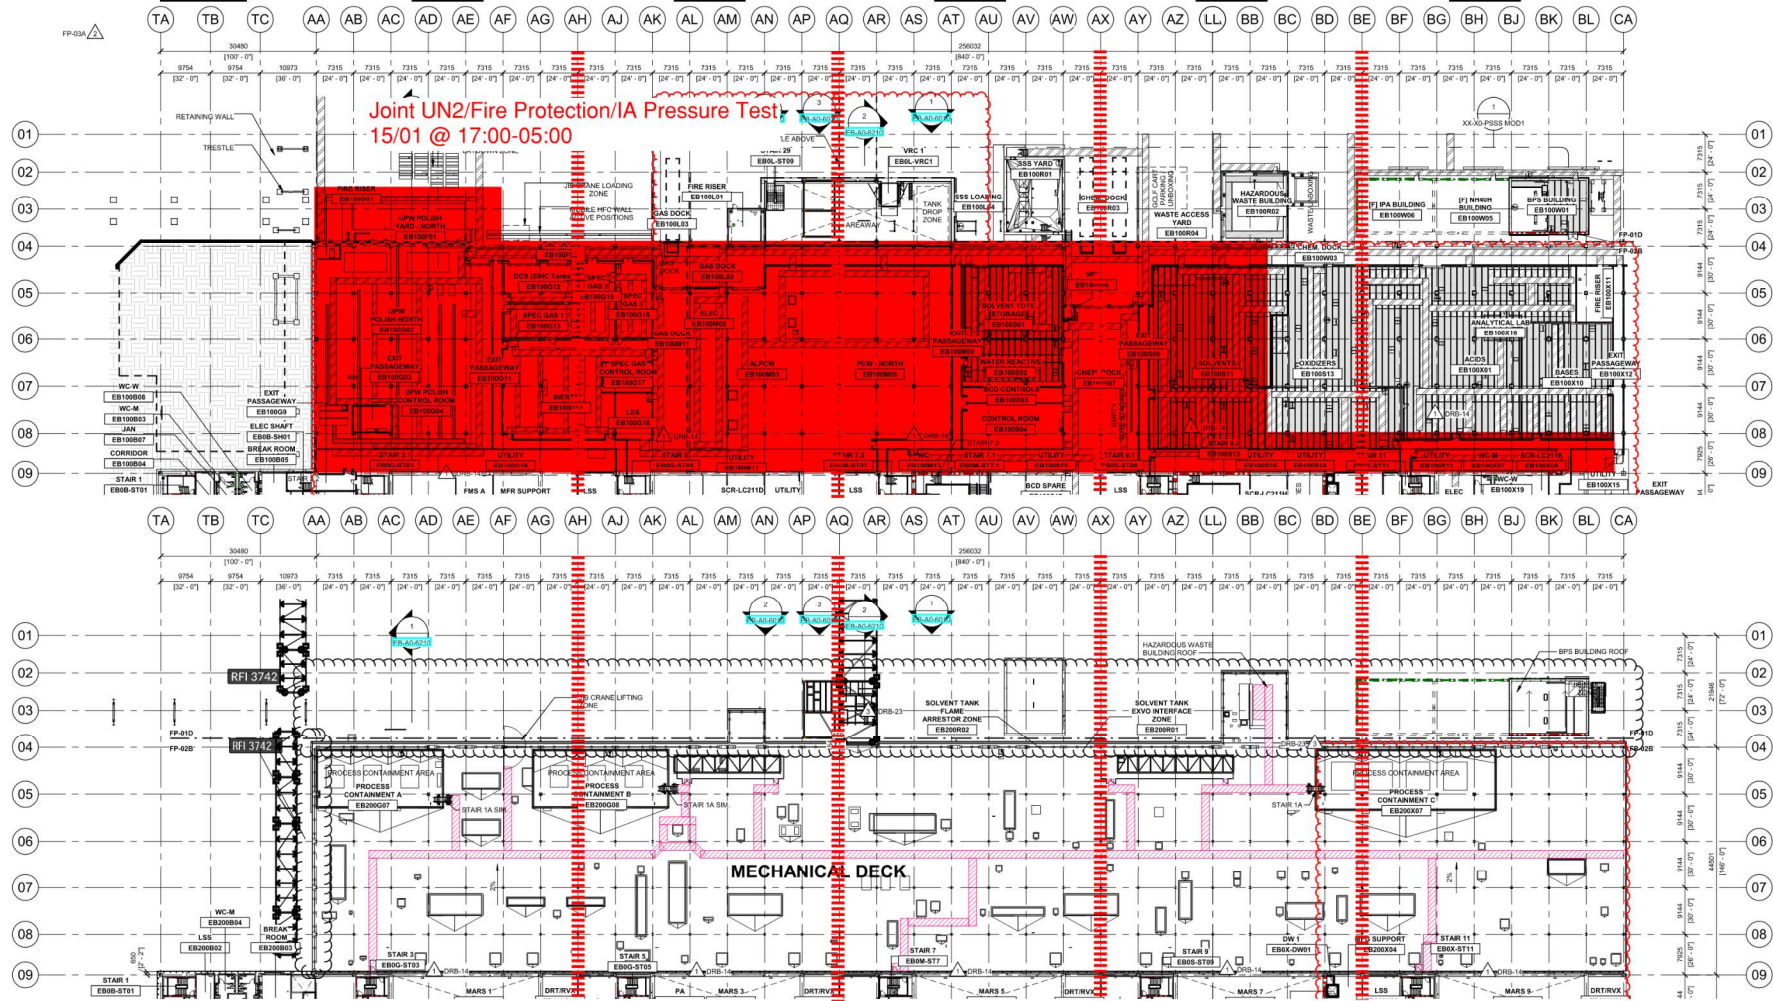


EPA Platform
14/01
15/01
17:00-01:00




H2 Vent
Radiographic
Test
16/01
17:00-01:00

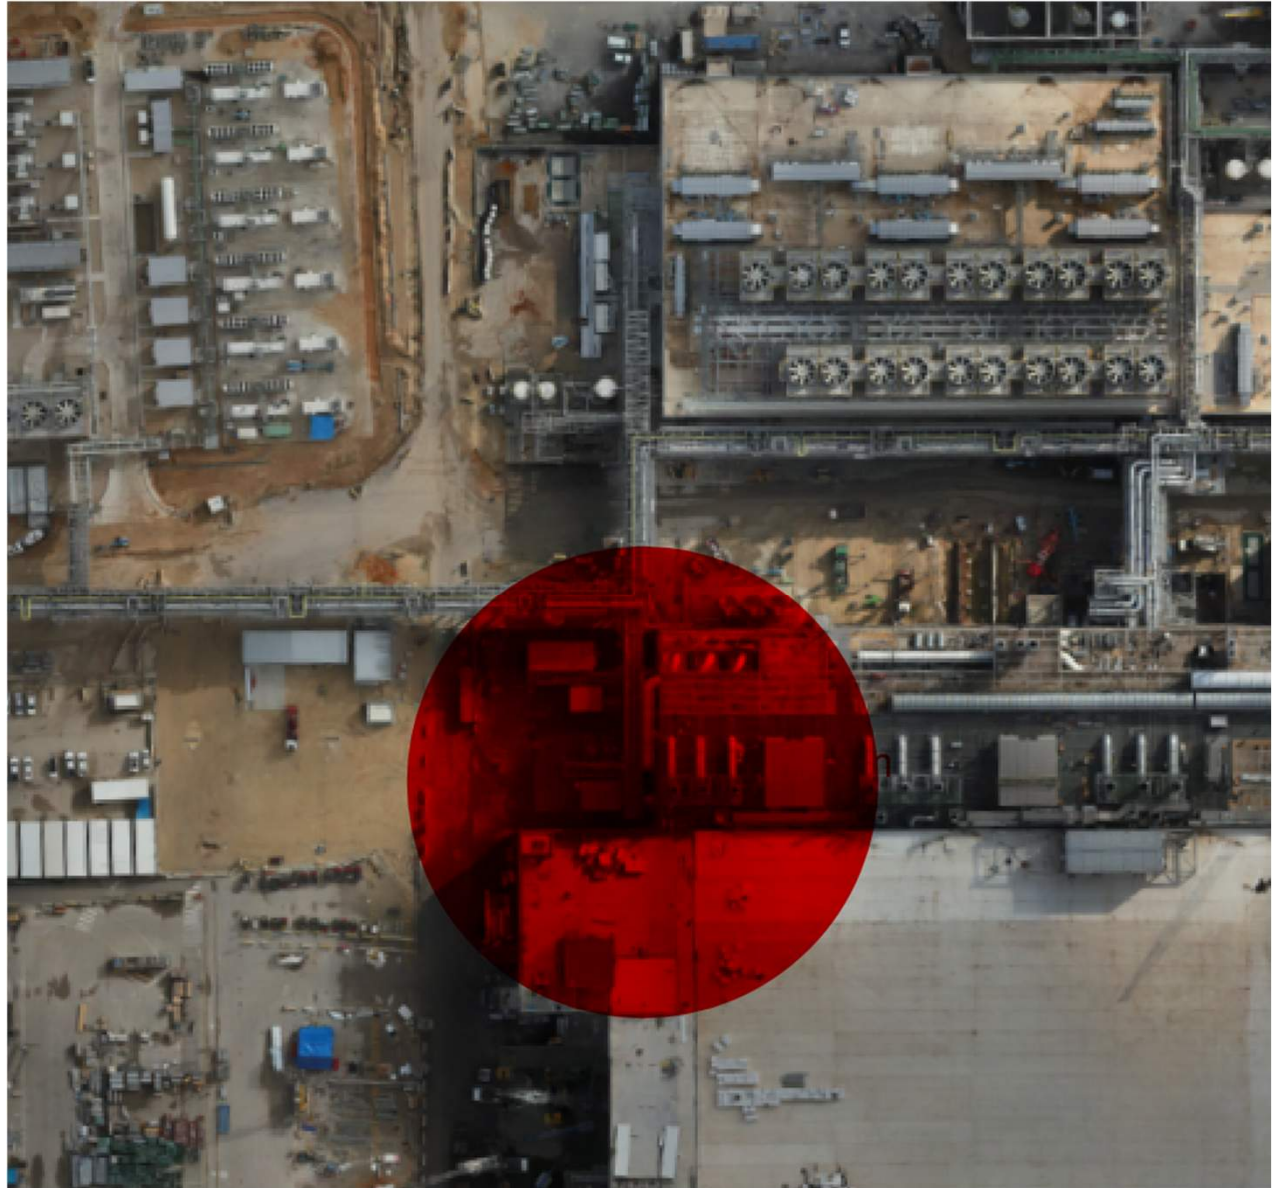




WJG 01J, 02J LIFT 2 & 3

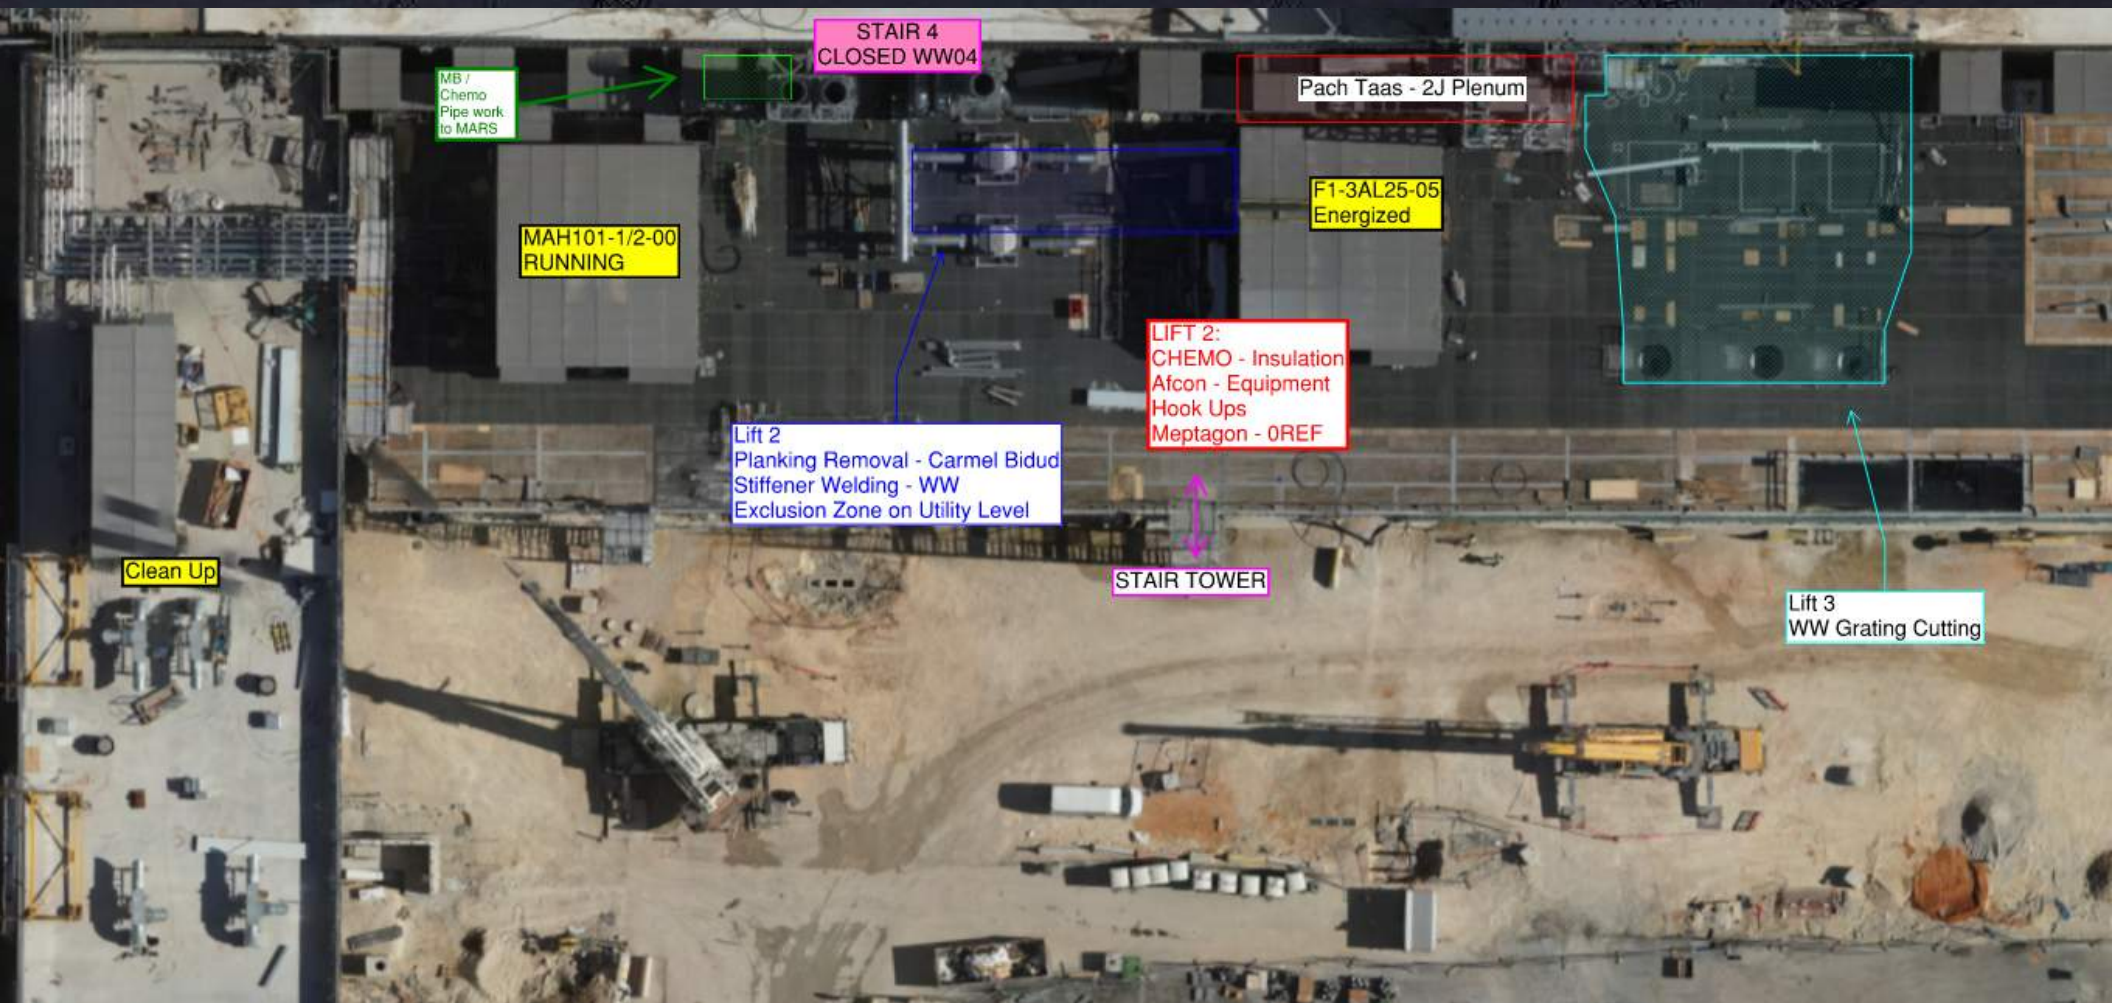


WJG 03J, 04J, 05J LIFT 2 & 3

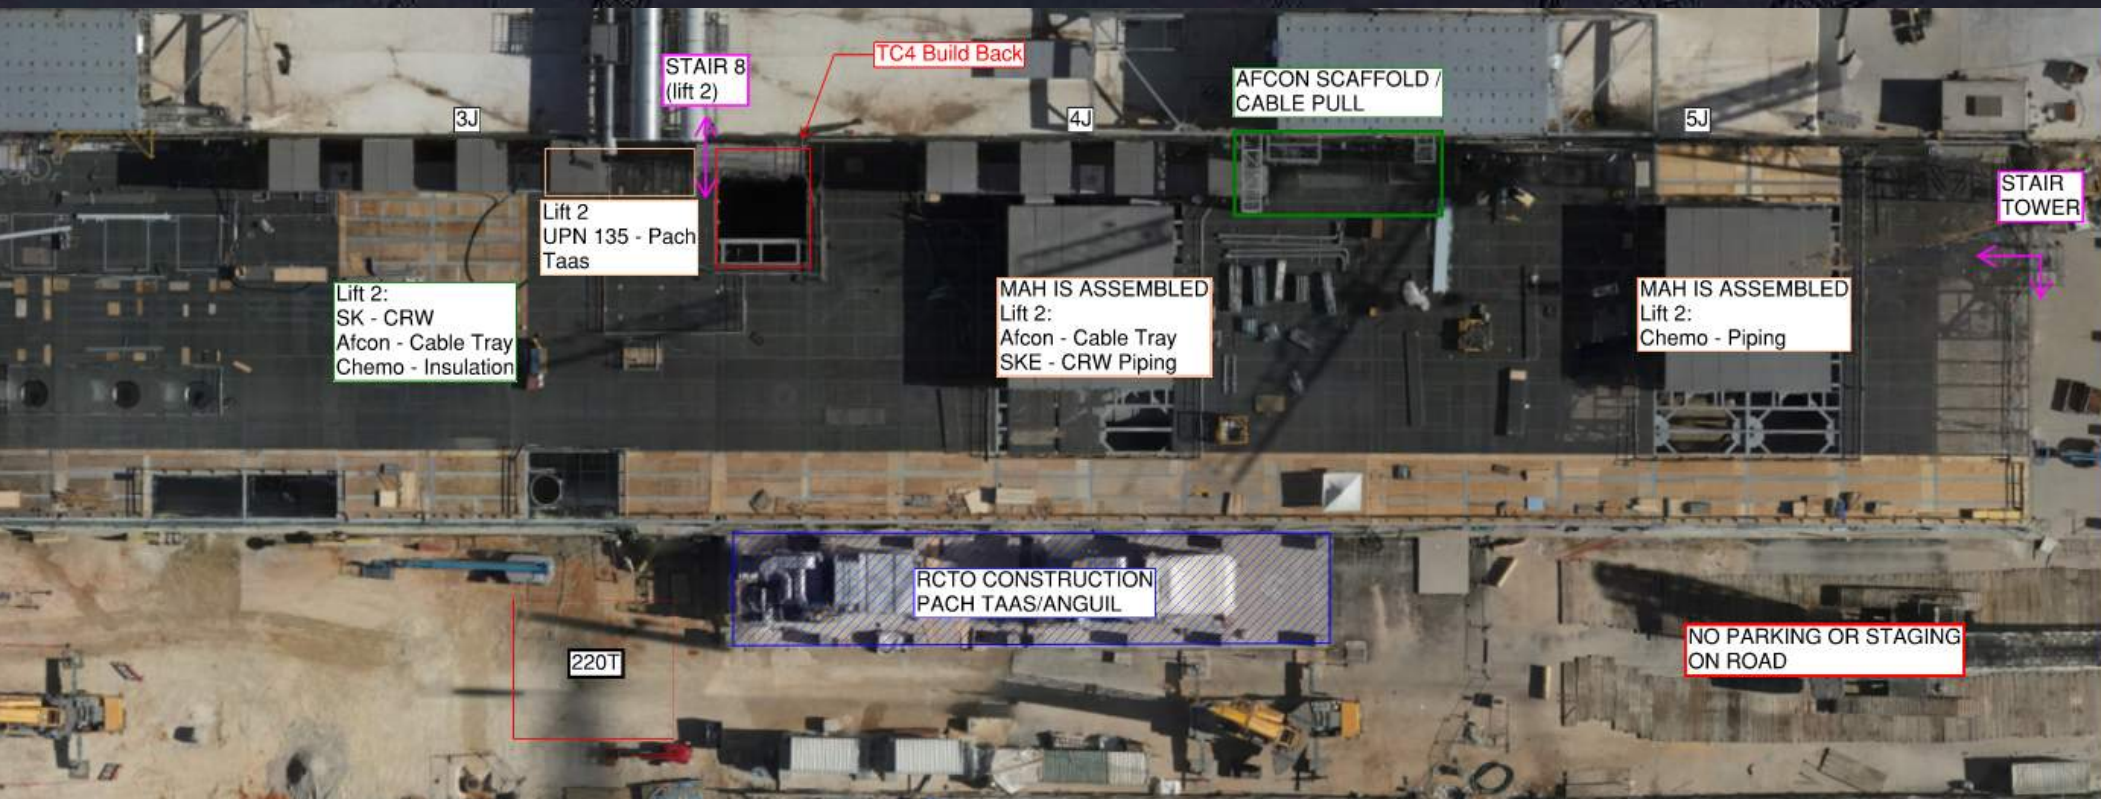




WJG UTILITY LEVEL BUILD OUT

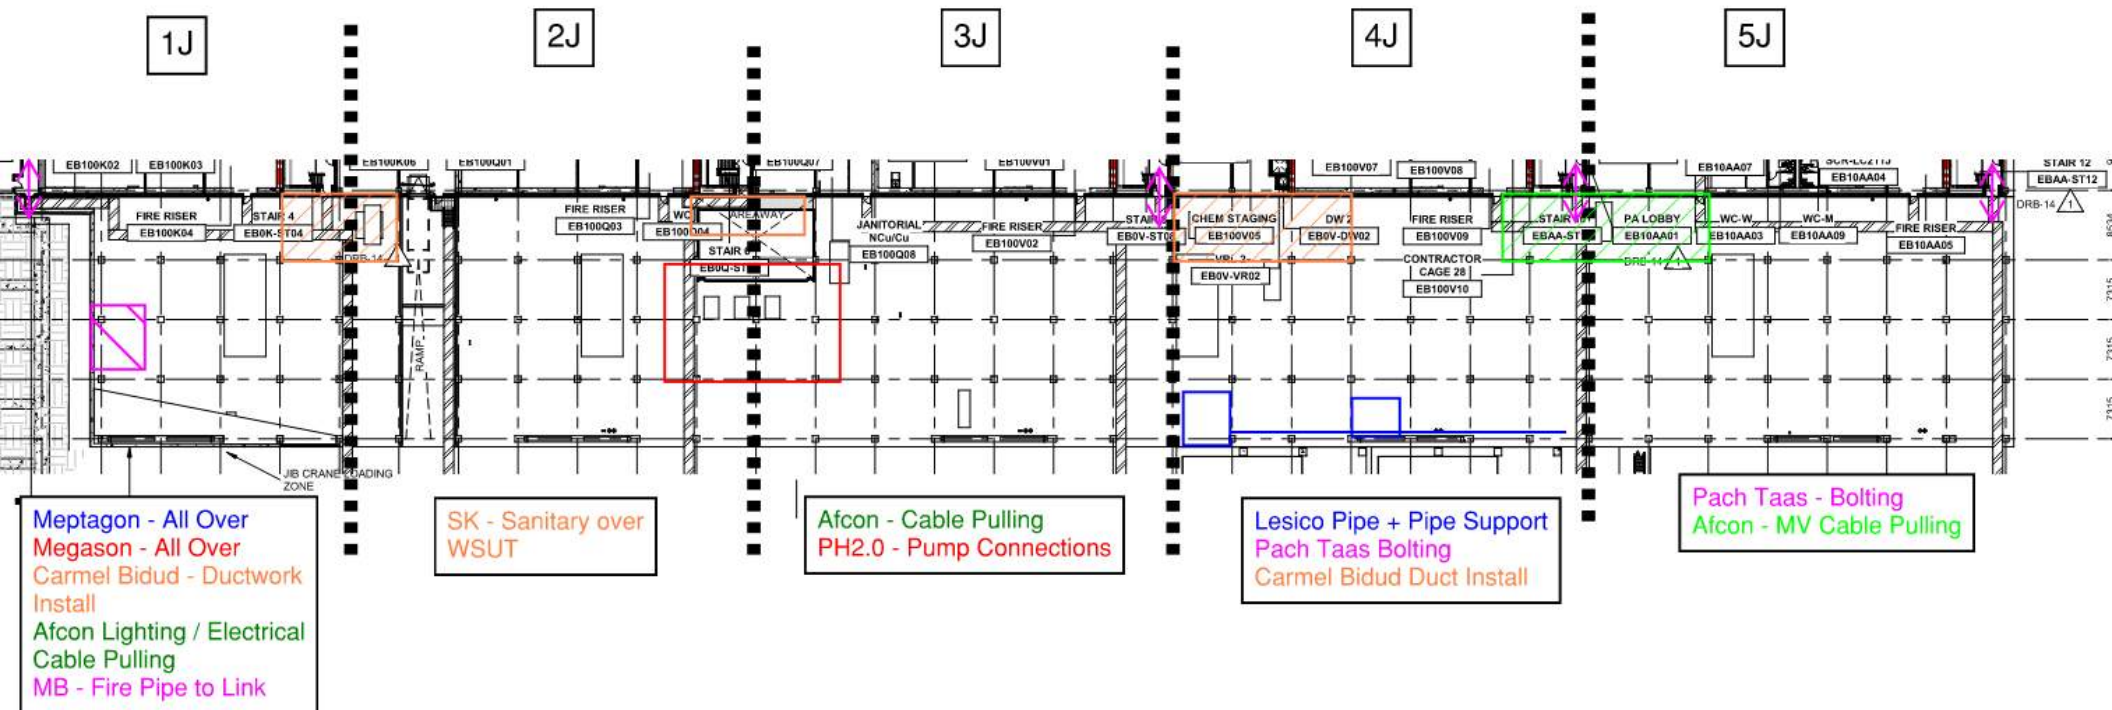


CUB 1 North Yard Site Access




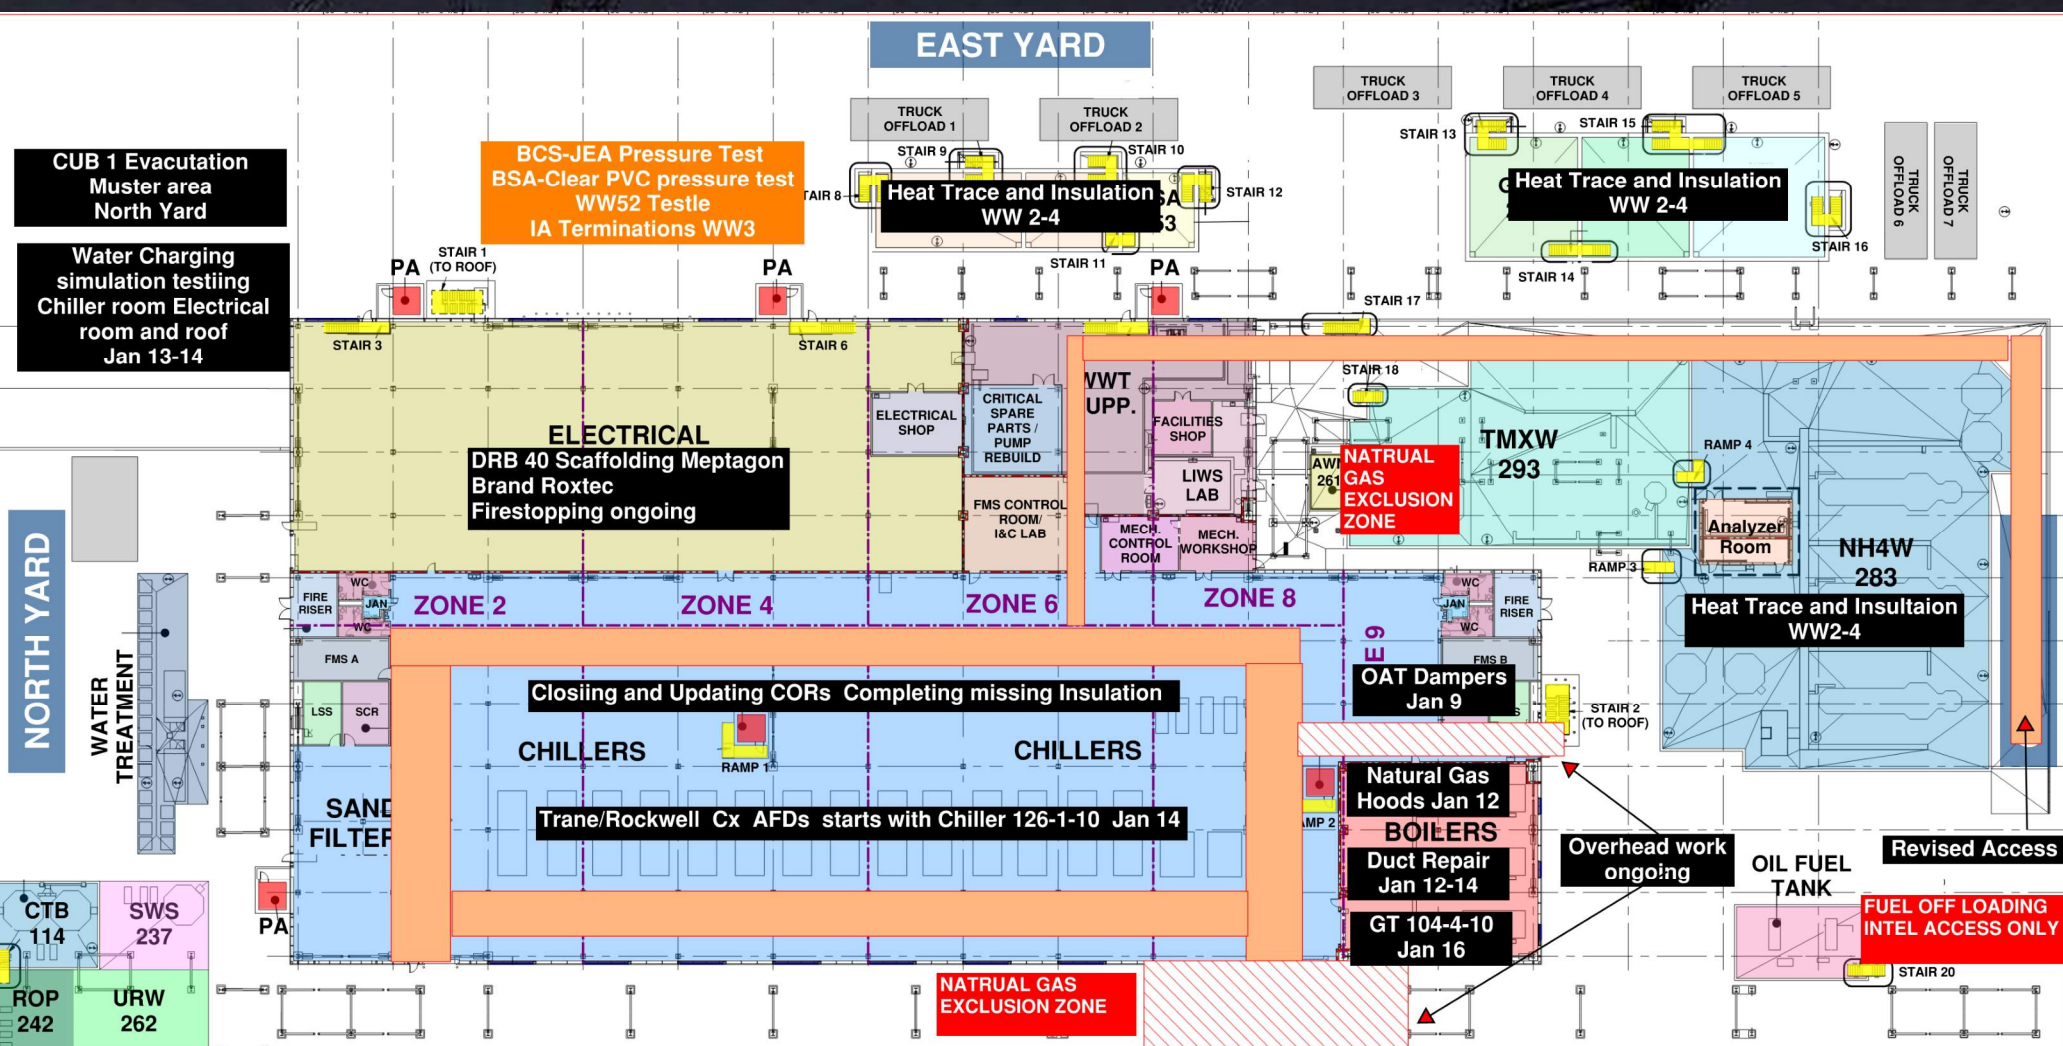

CUB 1 – EXTERIOR/ROOF

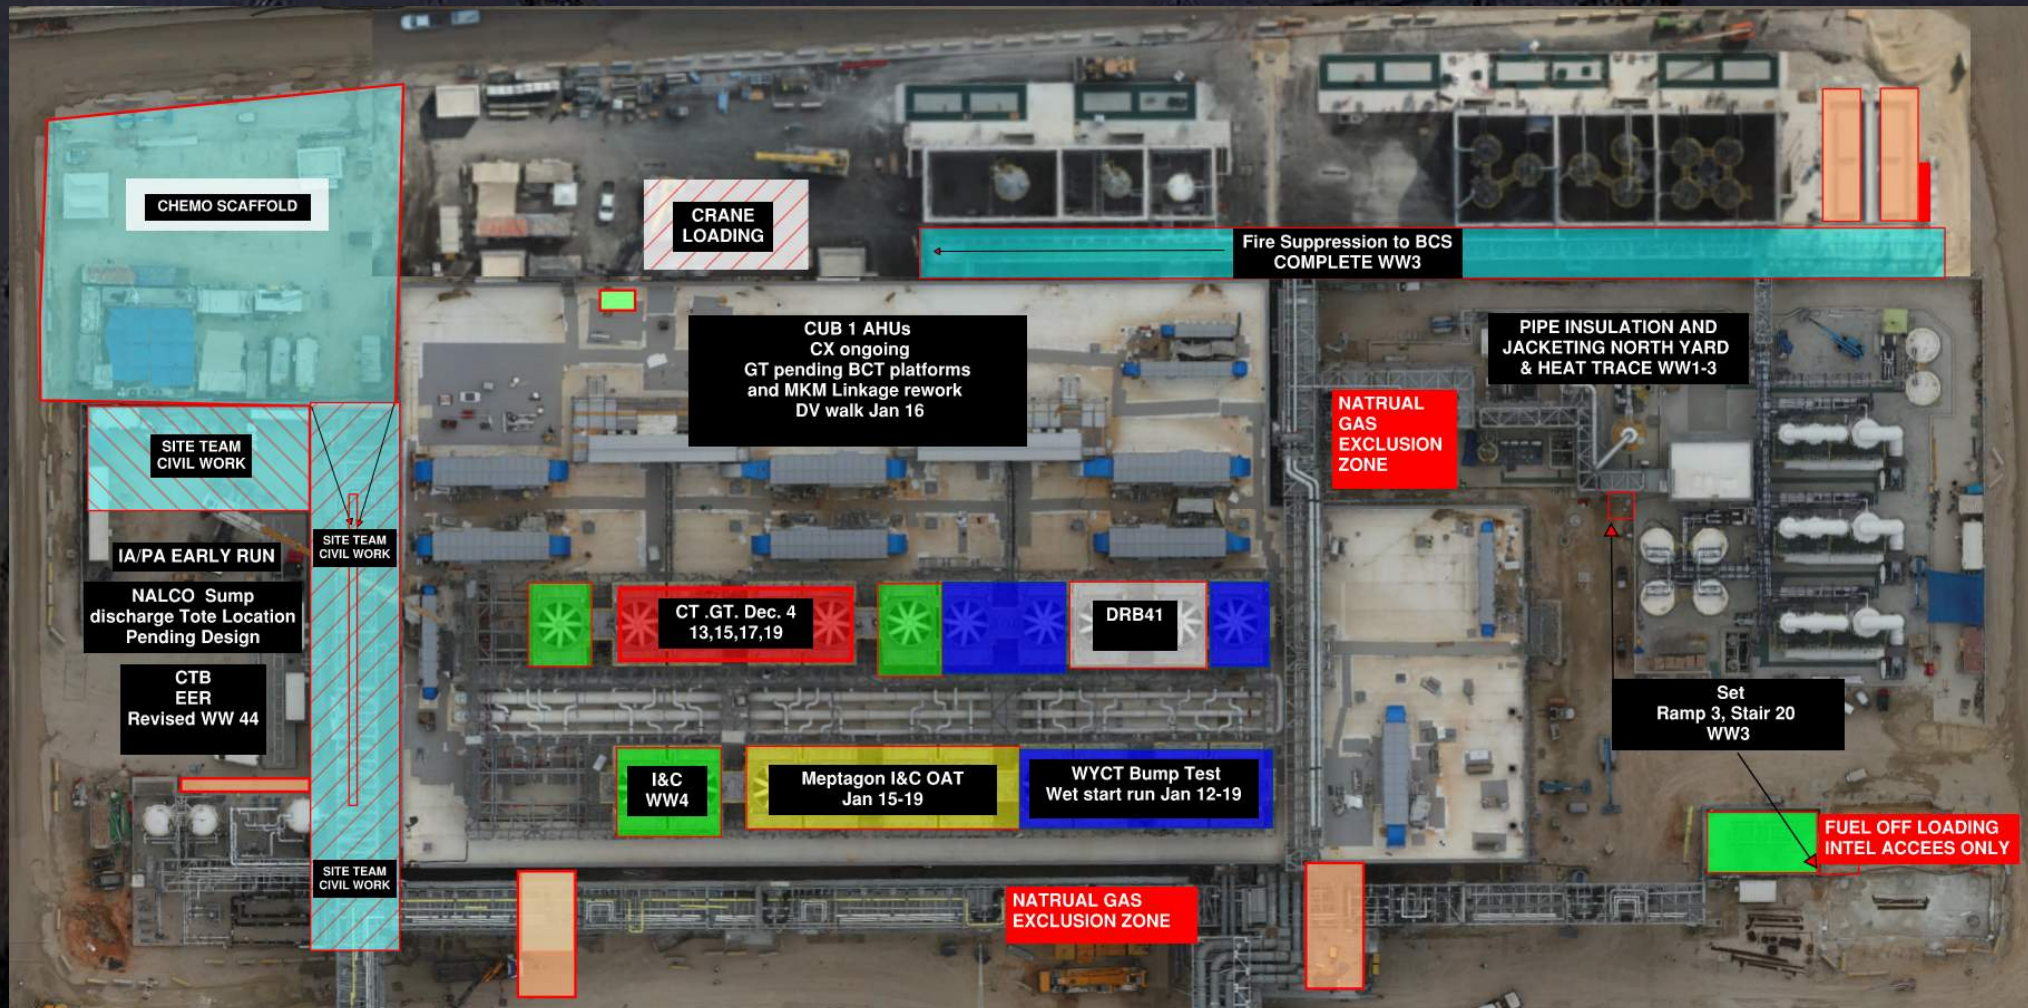


CUB 2- Load in ,H&T, Framing and Sheetrock

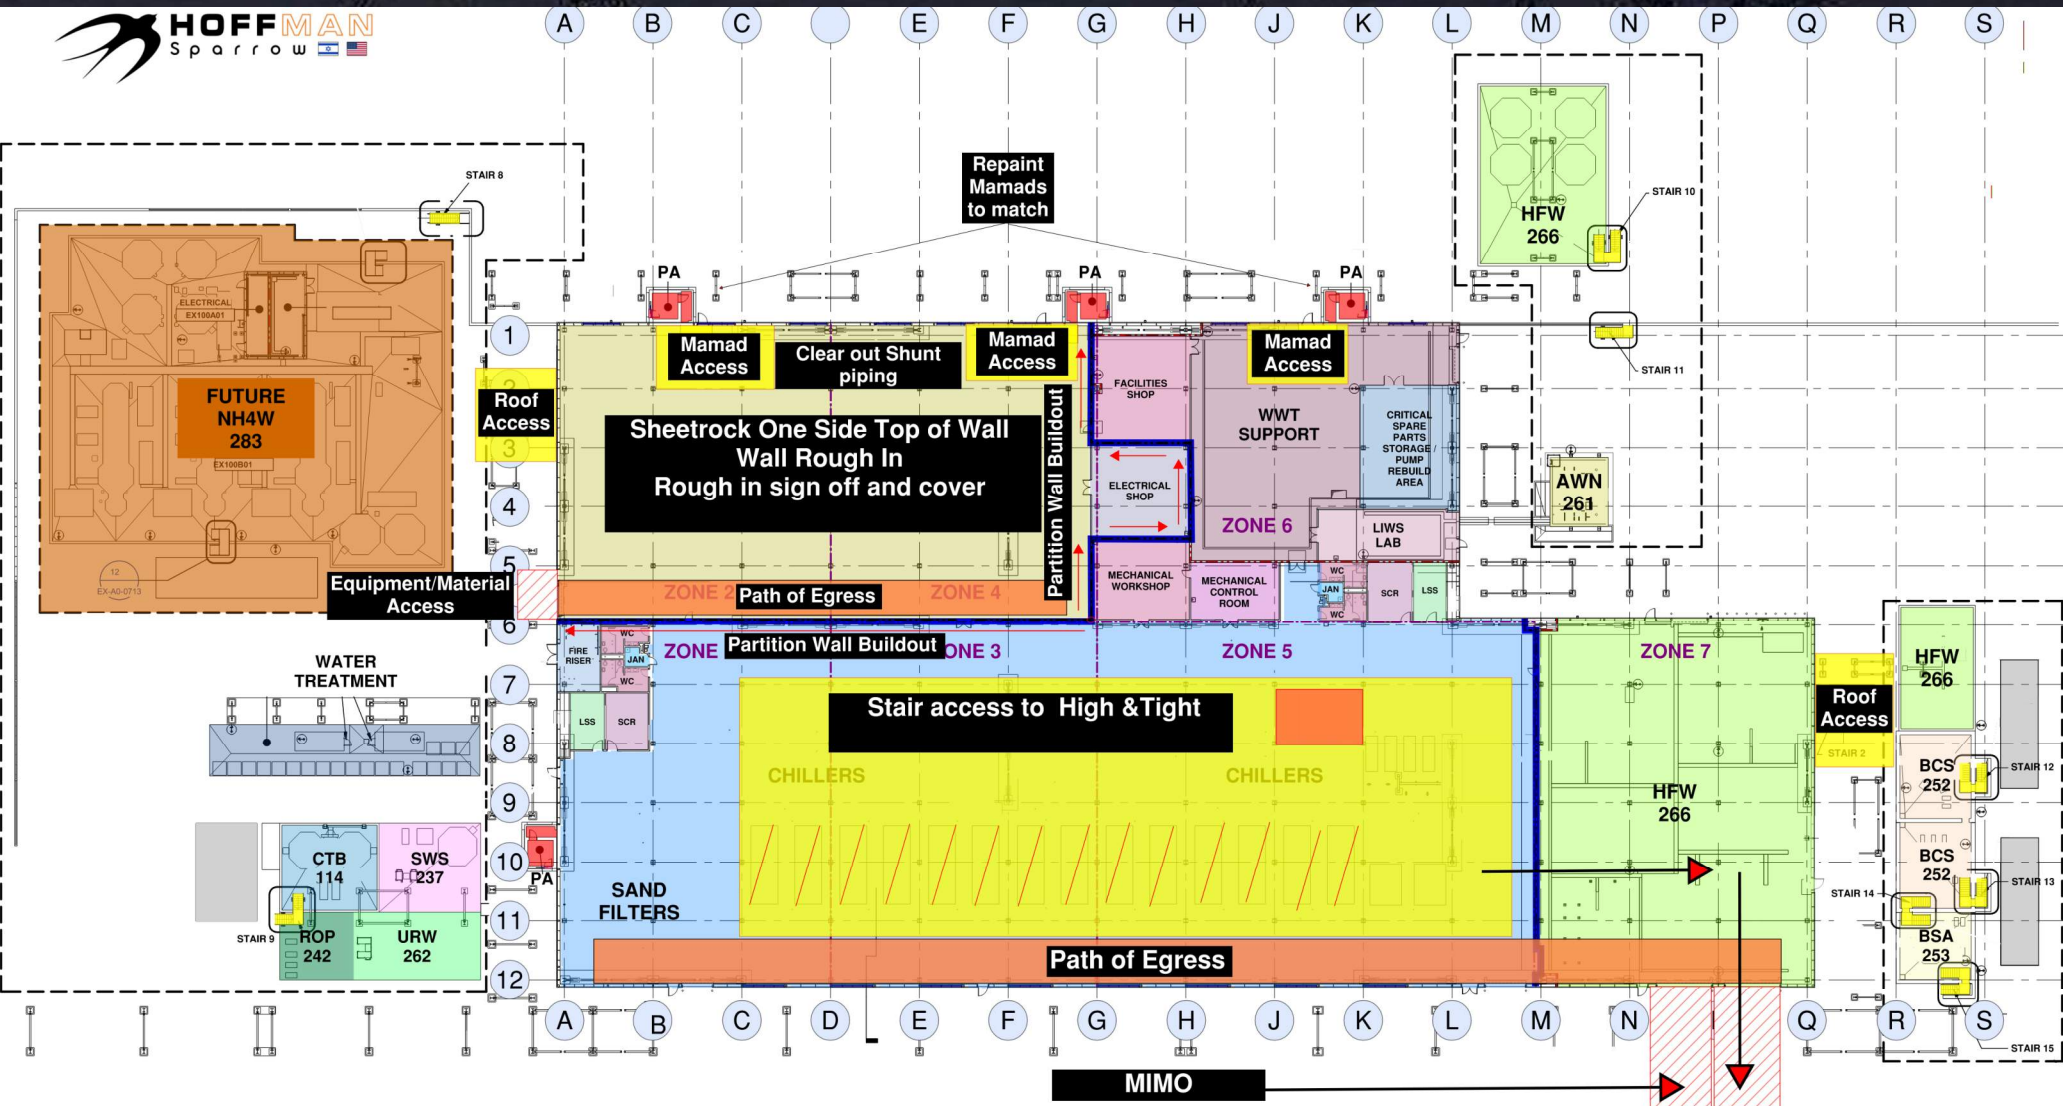


CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY

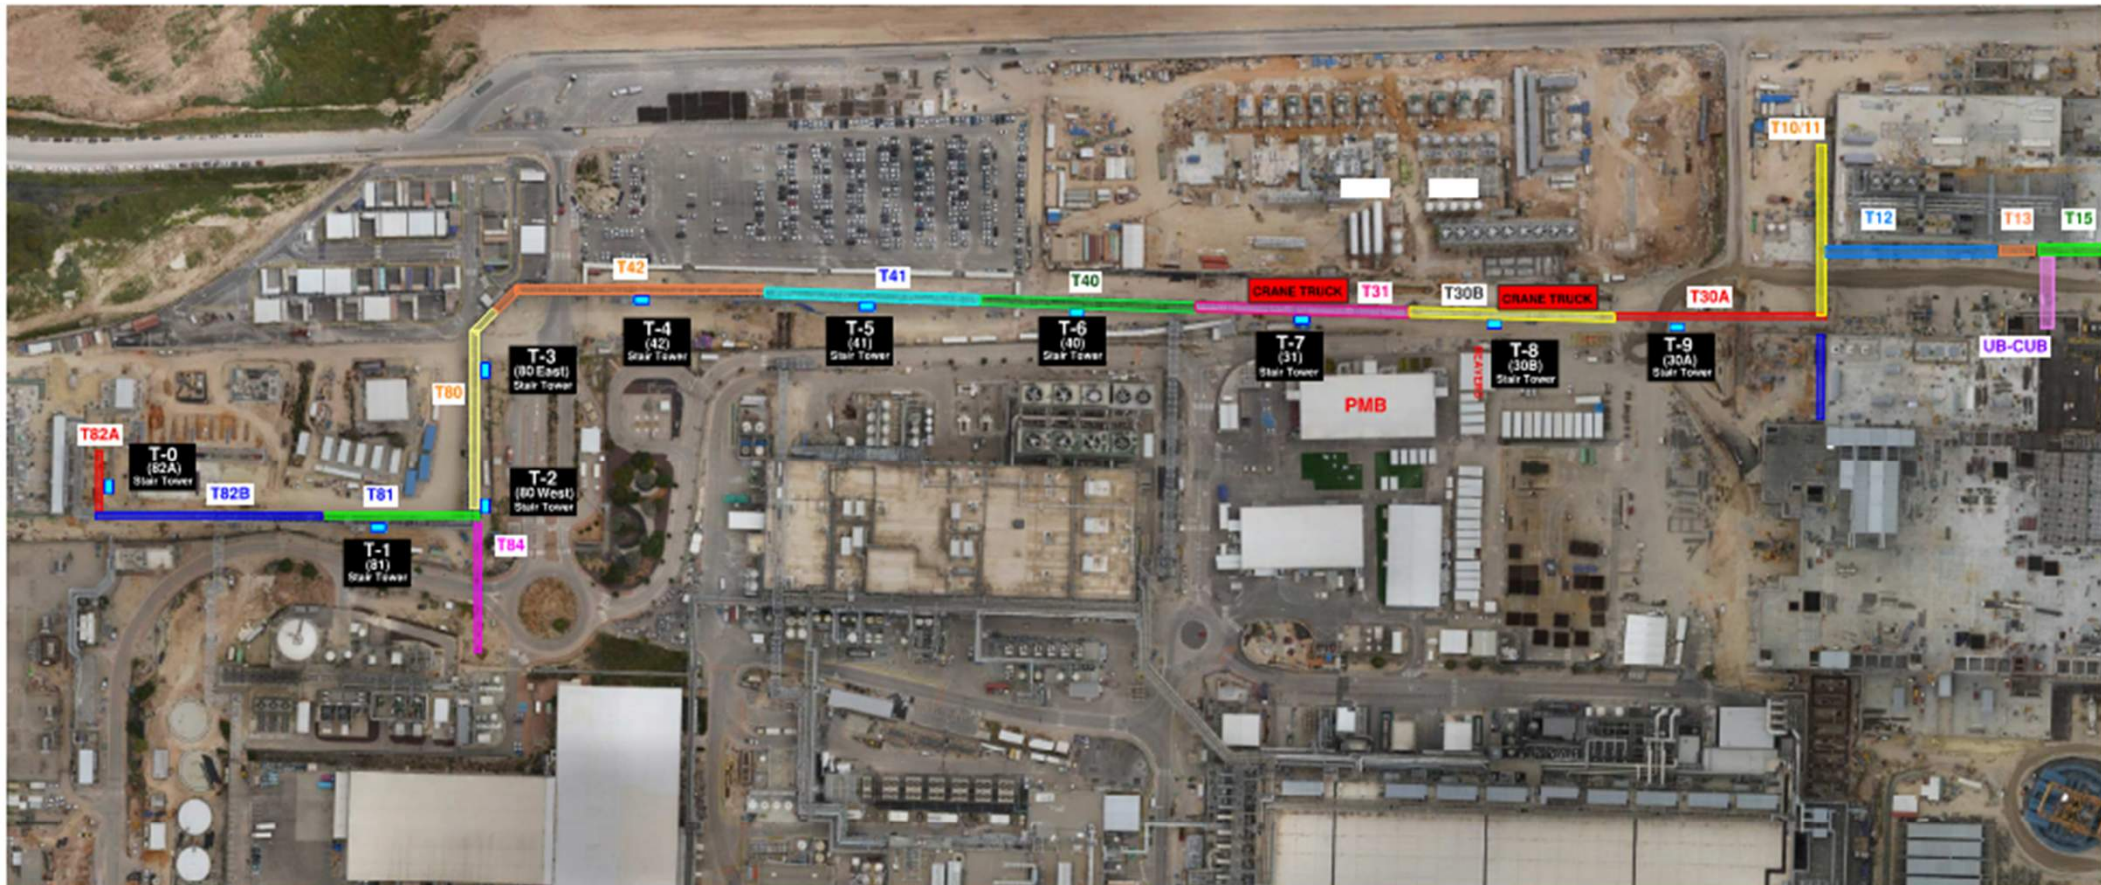





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

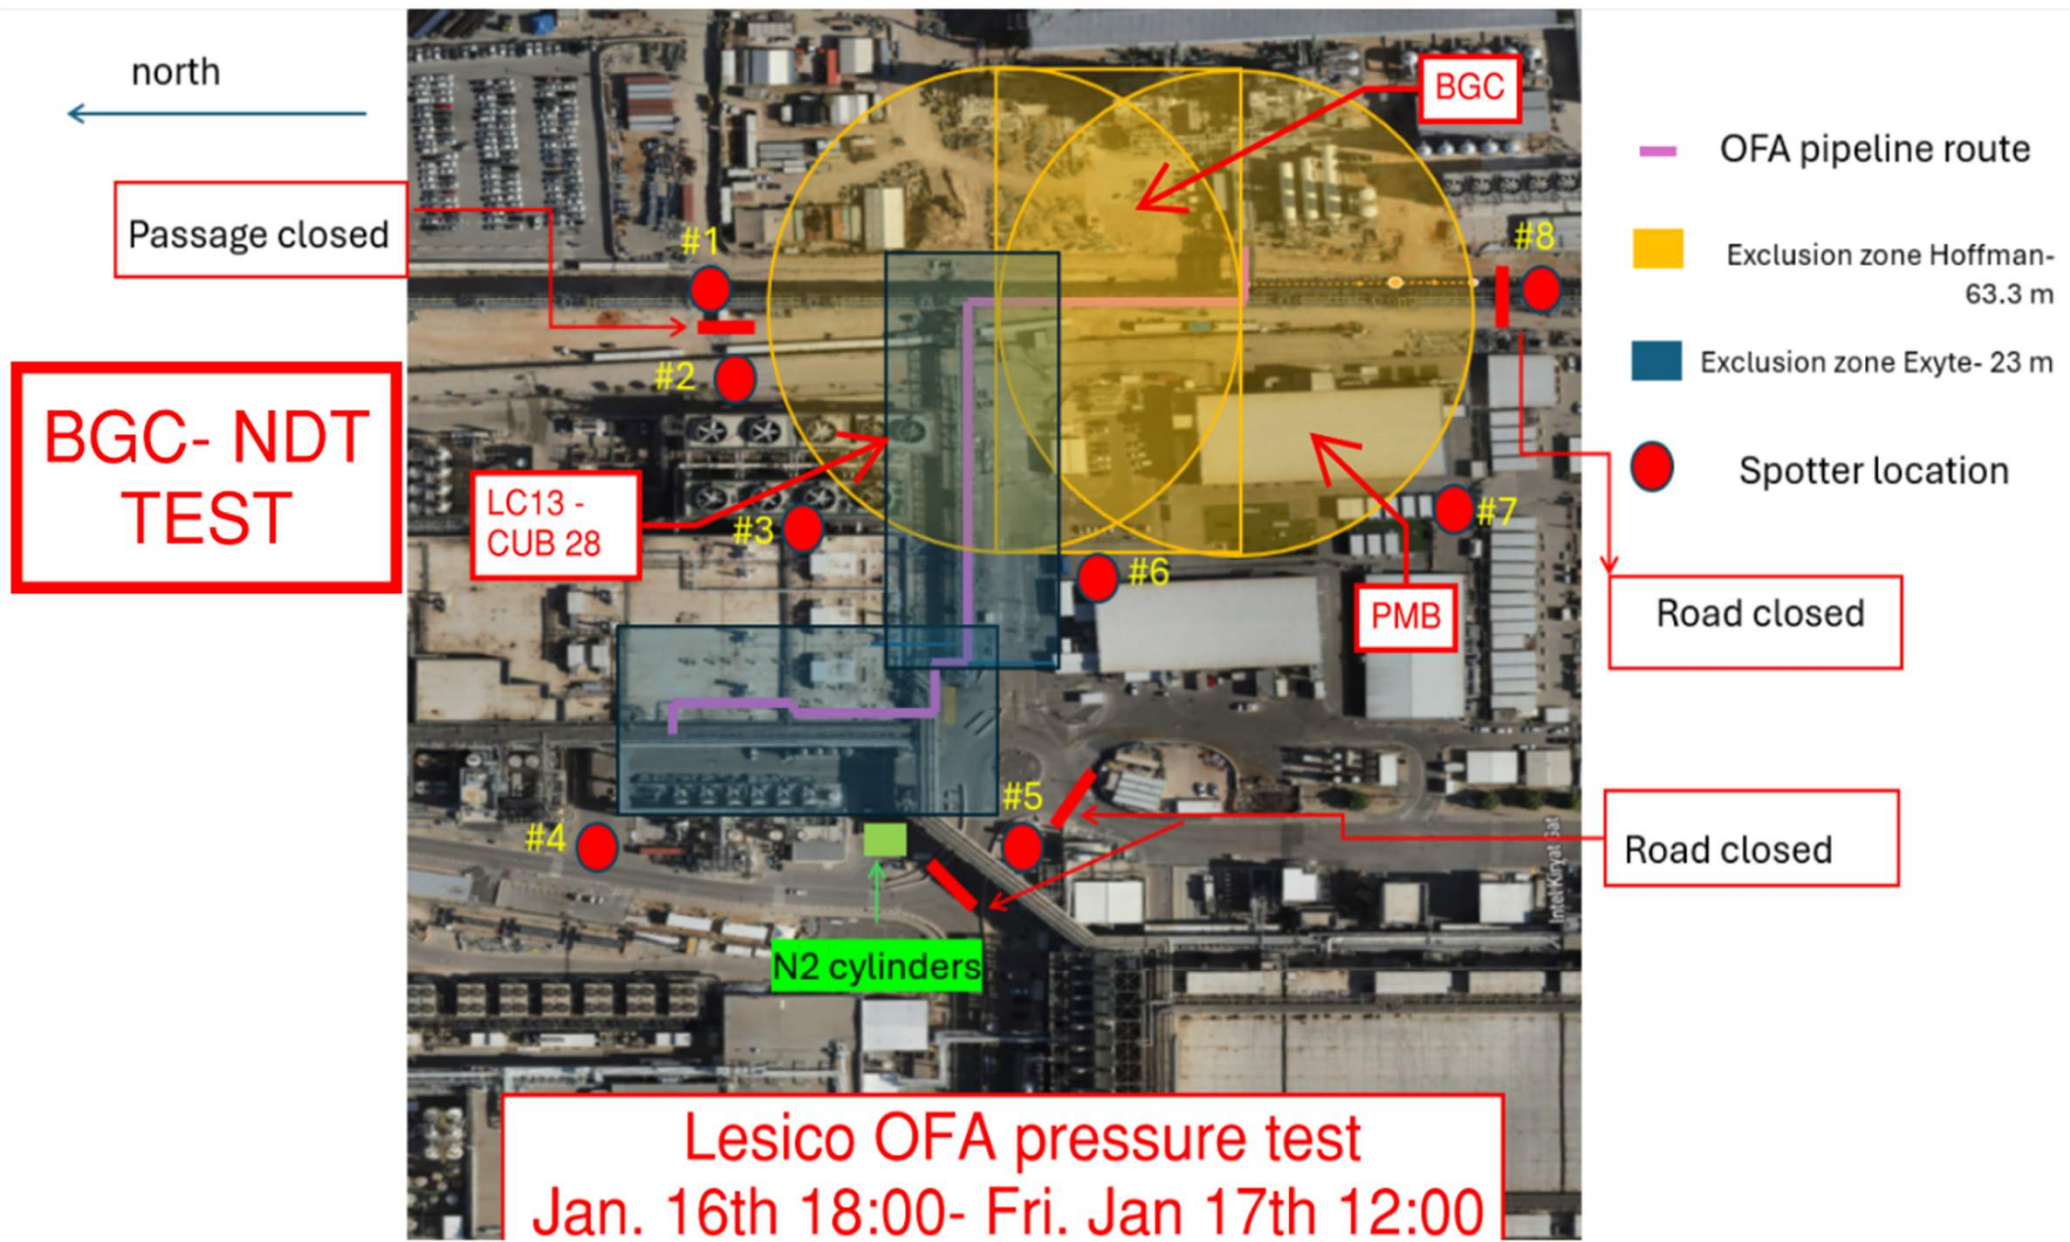



HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  


SAMI NAJAMI – NDT RADIOGRAPHY OFA SYSTEM

AREA PLAN – TRESTLE: T-13 \ UB-CUB

WED 15/1/2025 22:00 - THU 16/1/2025 05:00

SNJ – NDT – OFA – 16" \ 20"

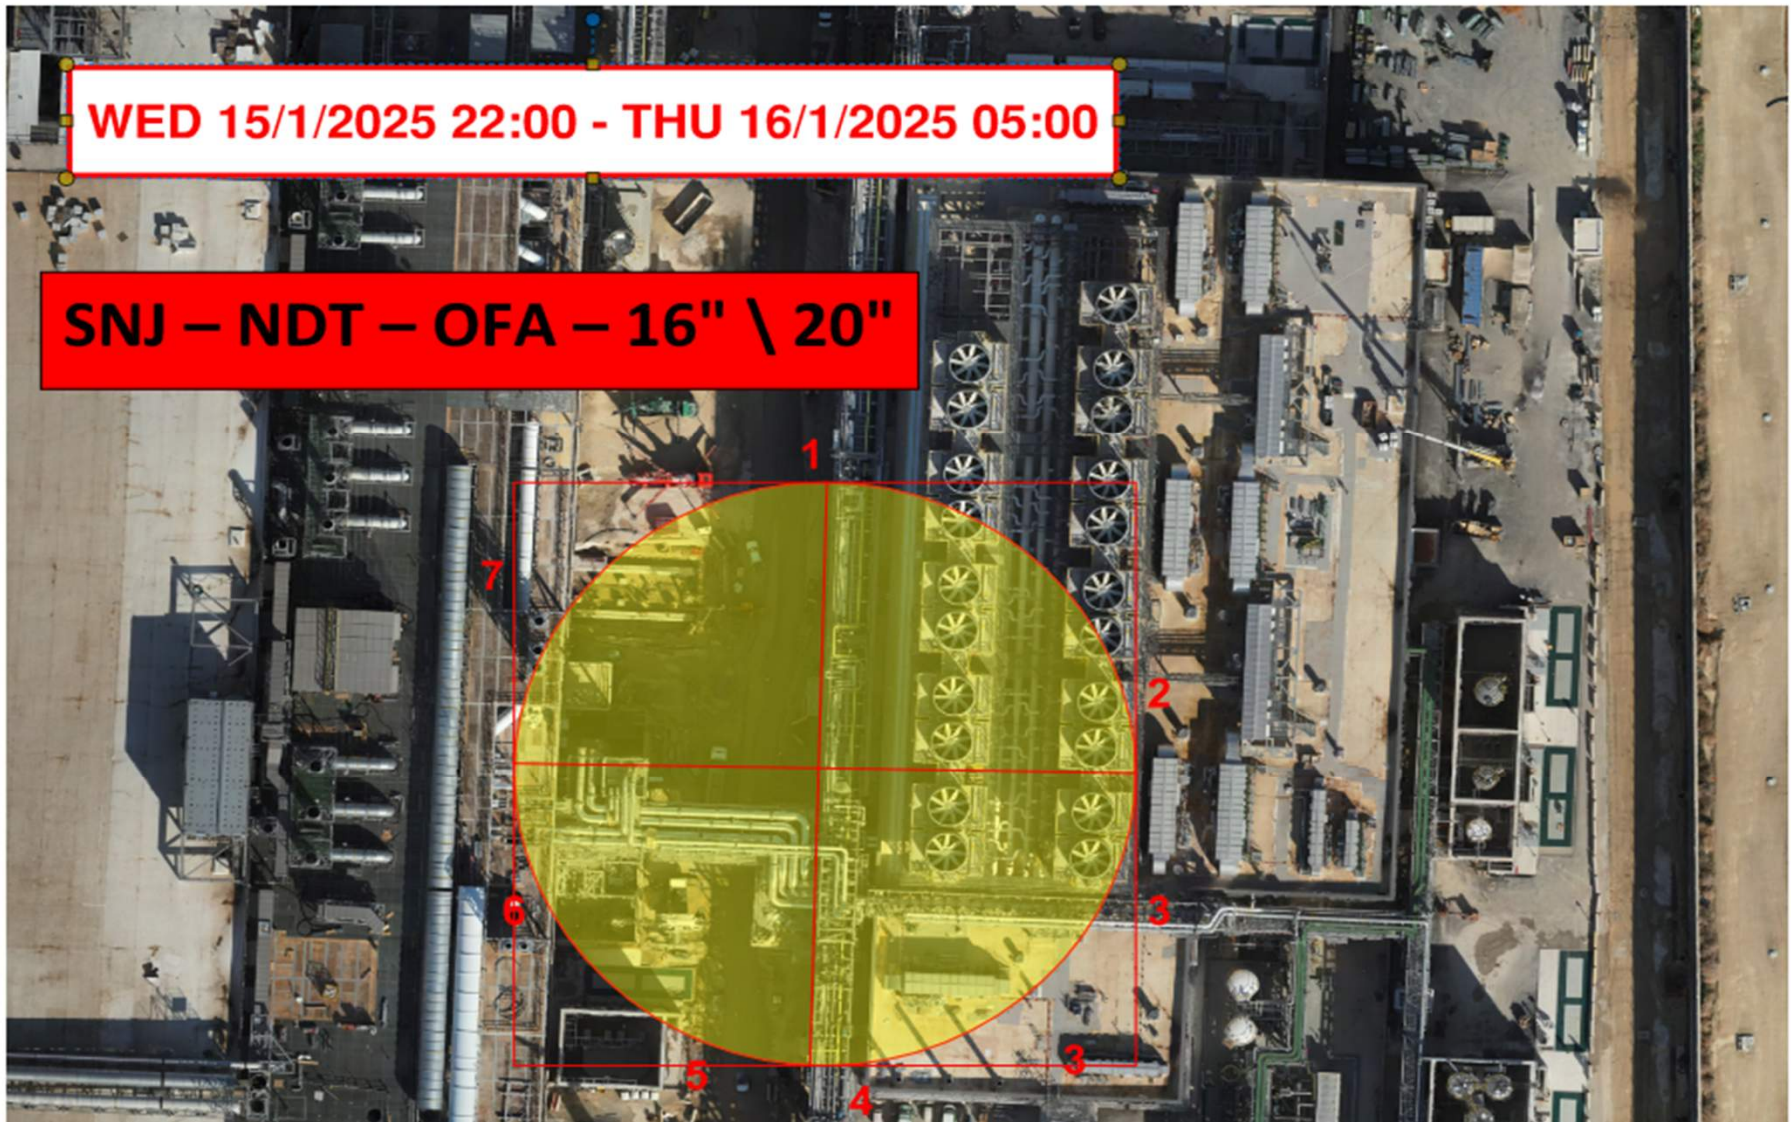

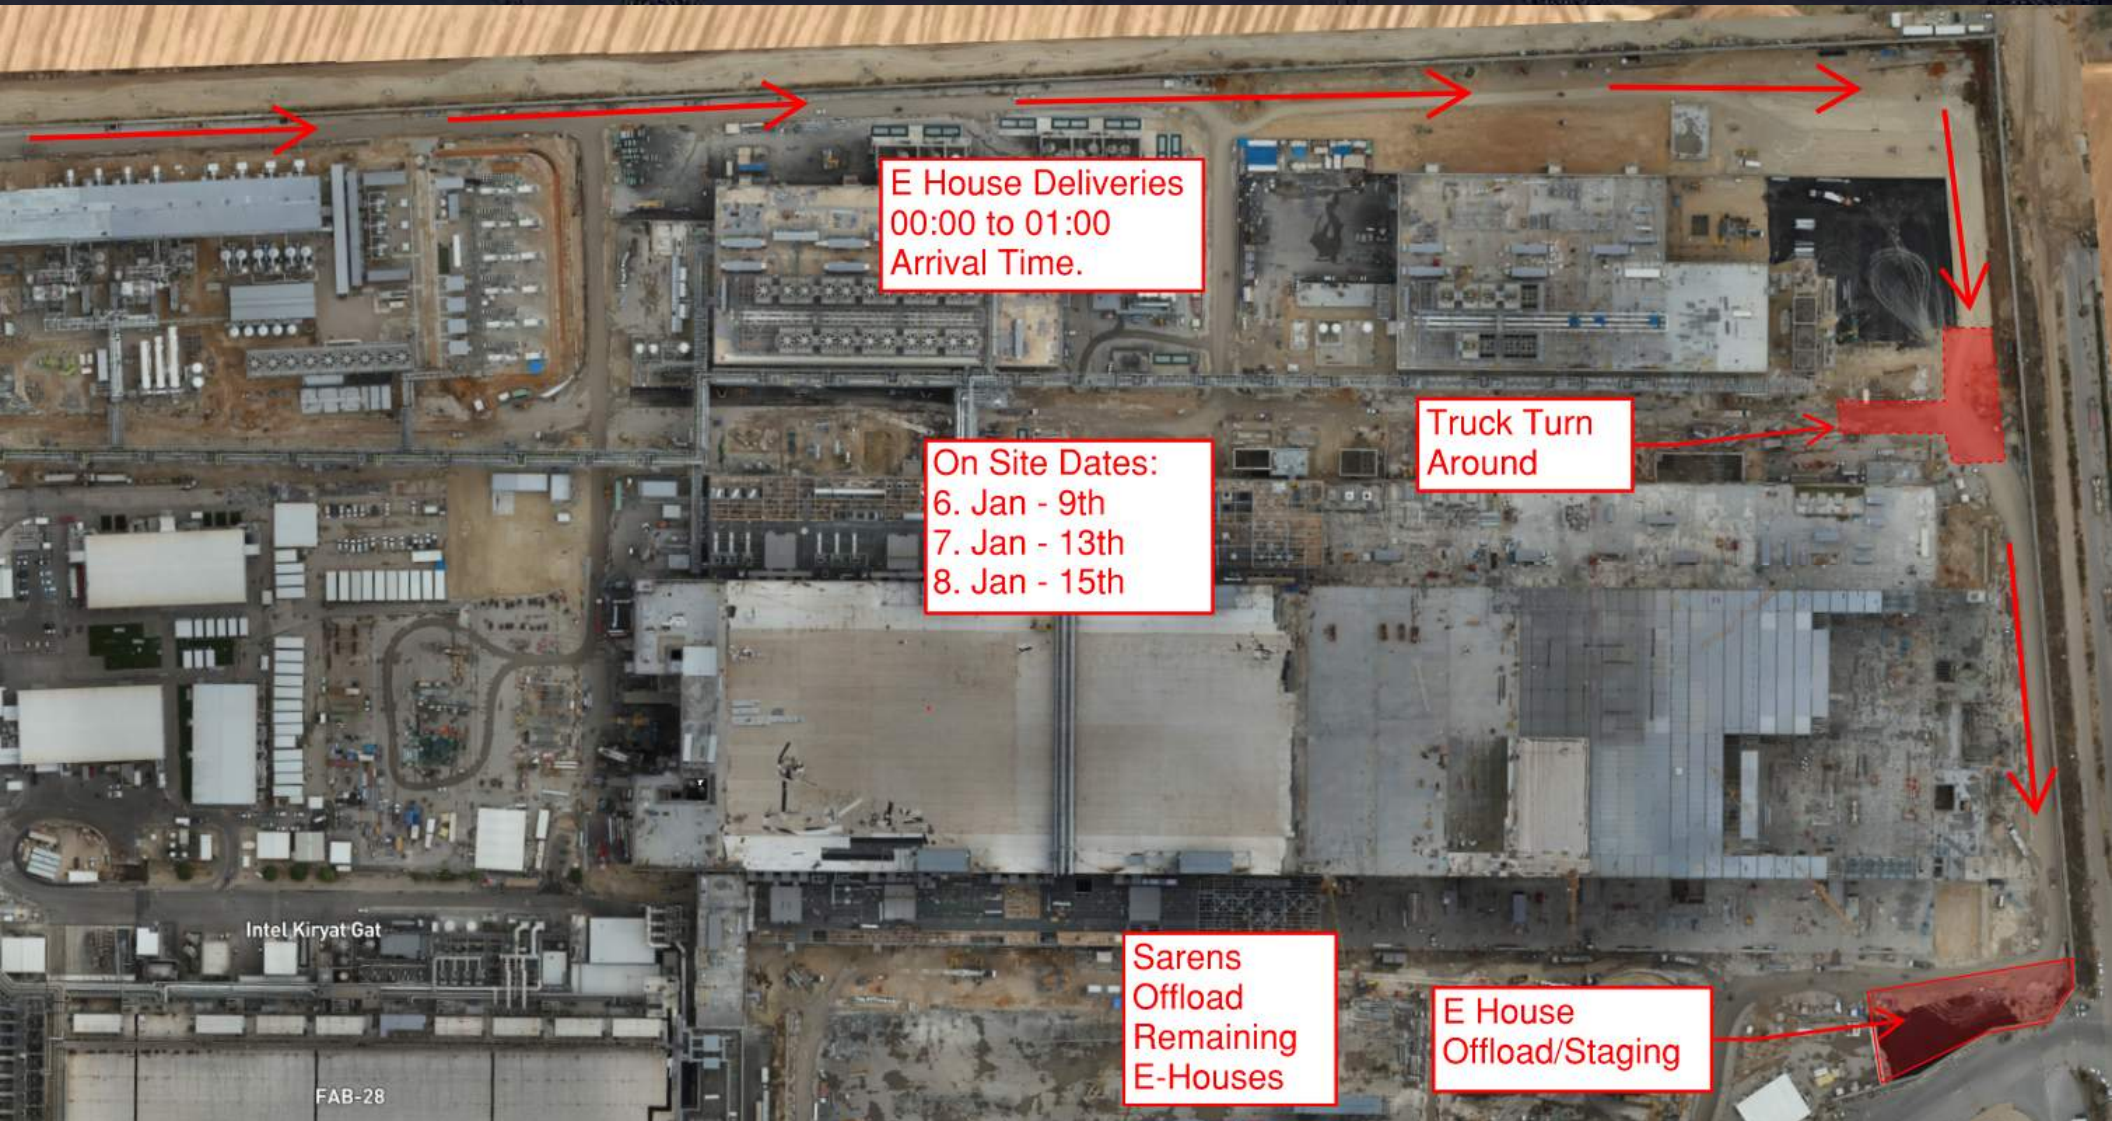

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
6. Jan - 9th
7. Jan - 13th
8. Jan - 15th

Truck Turn
Around

Sarens
Offload
Remaining
E-Houses

E House
Offload/Staging


Intel Kiryat Gat

FAB-28



Daily Coordination Meeting

Site Logistics North

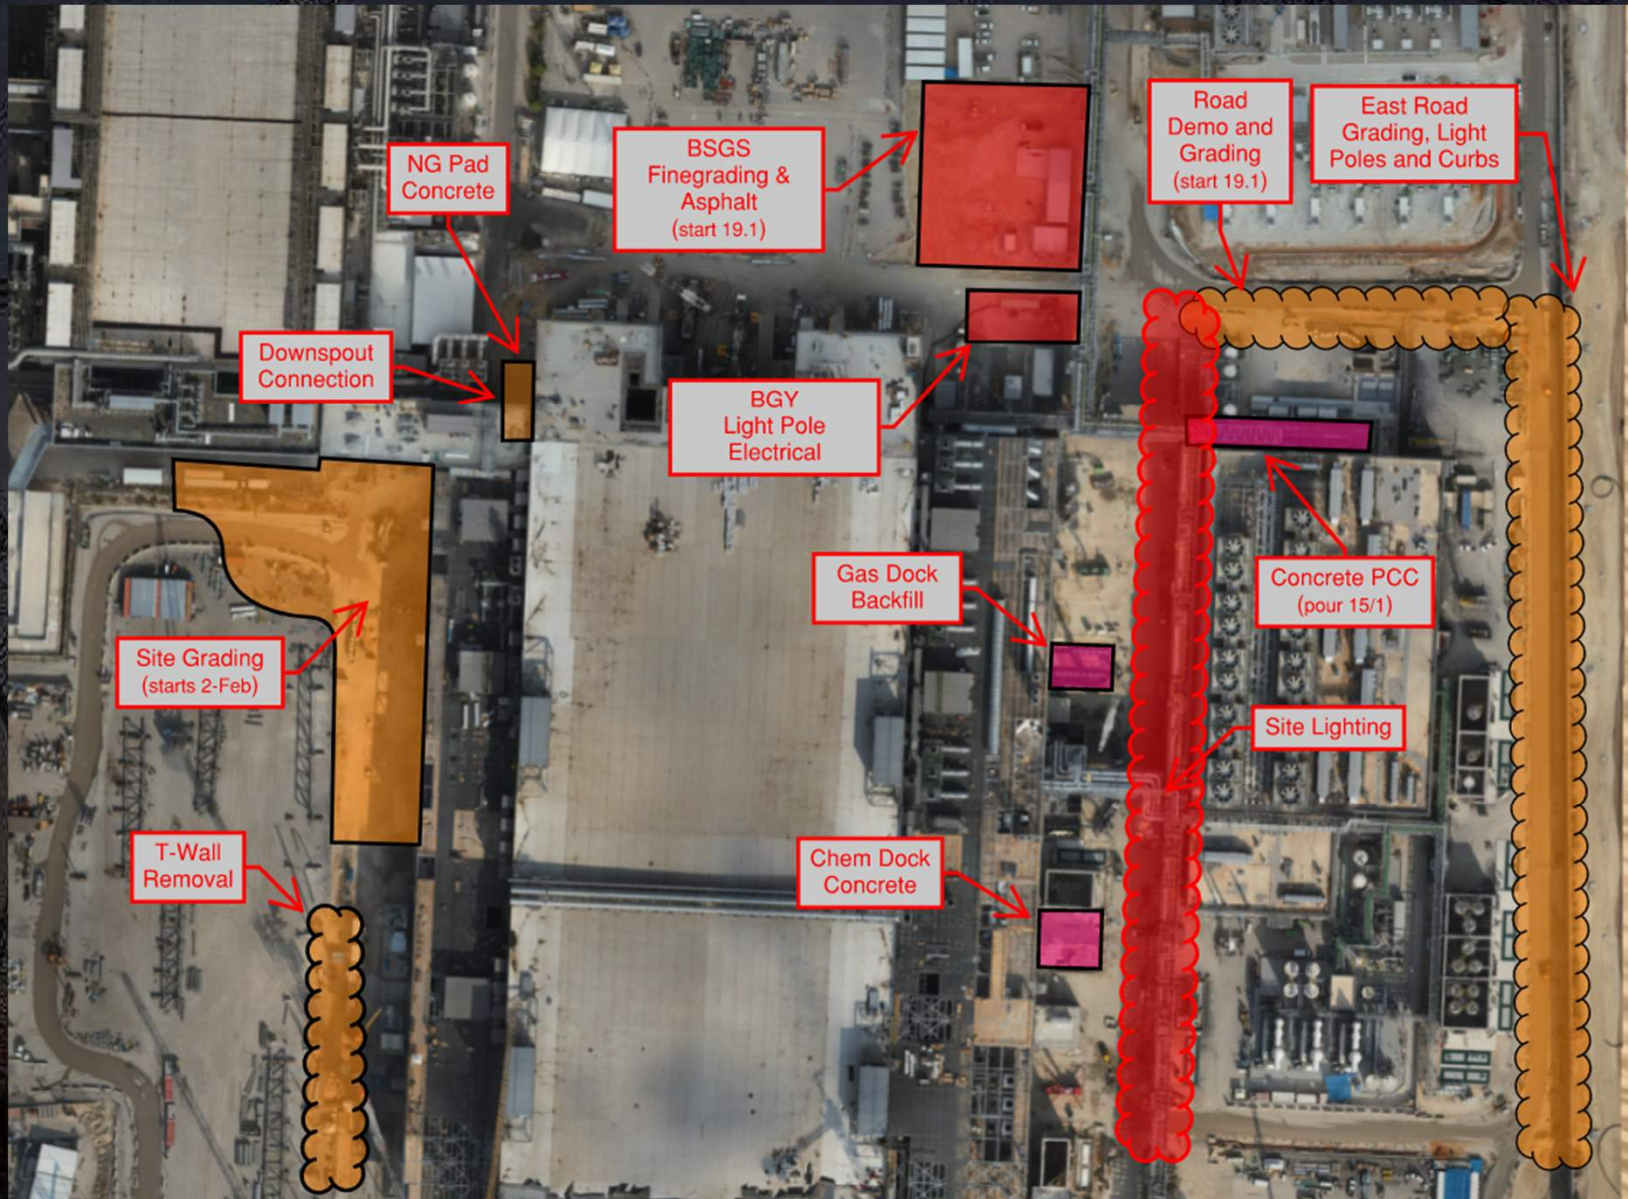



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South



Keep Access Clear

- There are many areas of the site that have become critical to maintain access to. We need help from each of you to ensure that we are maintaining that access.
- Maintaining access means no tools, equipment or material can be placed or staged there. Work needing to be performed here will require approval.
- Key areas or equipment where access must be maintained:
 - Fuel Offload south of CUB 1
 - CUB 1 North Riser Room
 - Live Electrical equipment
 - Safety showers
 - Stairs and doorways

HCC/EHS Weekend Work- 10.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jeremy Lee 052-6042279
Oscar Macias 052-4845469
Shimon Simo Ben Shetrit 052-5952059

CSA CM

Joe Nicpon 052-2962036
Nick Dailey 052-3308928
Andy Jollands 052-9659290

MEP

Ken Power 052-2531428
Abhilash Parameswaran 052-6938827

Cx

Calum Martin 052-4372208

Cranes

Hadar Shem Tov 054-6693626

Safety

- Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 10.01.2025

FAB

Utility Level / Roof / Stair Shaft

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- Pach Taas
 - 3W-4W-5W Wall Penetration, 1W-4E Perimeter
 - Tomer 0507670575
- Afcon E
 - MARSes, E LSS Rooms
 - Avi Eli: 0526008487
- Chemo
 - TTNW
 - Tomi: 0523759408
- MEGASON
 - 7E
 - Israel 0526869393

Clean Room

- Talad – 10 guys CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 7 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)
- Afcon – 22 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)
- Chemo –15 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Megason - 9 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT
- Sela – 8 2E CRC (Supervisor yoav 0548076339 , EHS SERGEY 0526650046)
- D&p - 16 guys freddie hazan 0503827885

Subcontractor Weekend Work- 10.01.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- HSAI – 3P Roof Curb Stripping
- Foreman – Dave – 052-4121028
- Safety – Hiam
- SK Engineering – GL4 UL Piping, 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- Carmel Bidud– Spec Gas, BCD, and 2P Roof
- Foreman –
- Safety –
- Combe Waste – 2P Waste Piping at GL4
- Foreman – Chaim – 054-5210133
- Safety – Marzuke – 054-447-7112
- Combe UPW – 2P & 5P Scrubbers
- Foreman – Boris – 054-8346412
- Safety – Shimon – 054-5348843

WJG

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

Pach Taas: All over (HRA)

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

SK:

Foreman: Tufik 054 943 3592

Subcontractor Weekend Work- 10.01.2025

CUB

D&P:

Constantin - 0545501602

David - 0548894447

Sami Najami:

Husein - 0526917461

Alon - 0509895008

SK:

Renato- 0548991623

Marzuk - 0548830263

Chemo:

Dudu - 0509808846

Leonid - 0548883878

Trestle

SNJ:

PIPES –T40 UB CUB - 8 workers

STEEL –Galvanized paint + – T30 A+B - 8 workers

Steel adjustment - 12 workers

FORMAN

Adiv asaly- 0526017477

SAFETY TRESTLE

Aviram shriki tel. 0509059920

Siding

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting Underground

Supervision = Shlomi: 050-9182260

EHS = Daniel: 052-2584171

Olizki – Offload 18, CUB1 flatwork, Link NG pad formwork Supervision = Or: 052-

4917313 EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
