

Daily Coordination Meeting




Daily Coordination Meeting

General Topics:

- Ramadan – Starts this weekend – make sure you have coverage plans.



UTILITY LEVEL MOD1

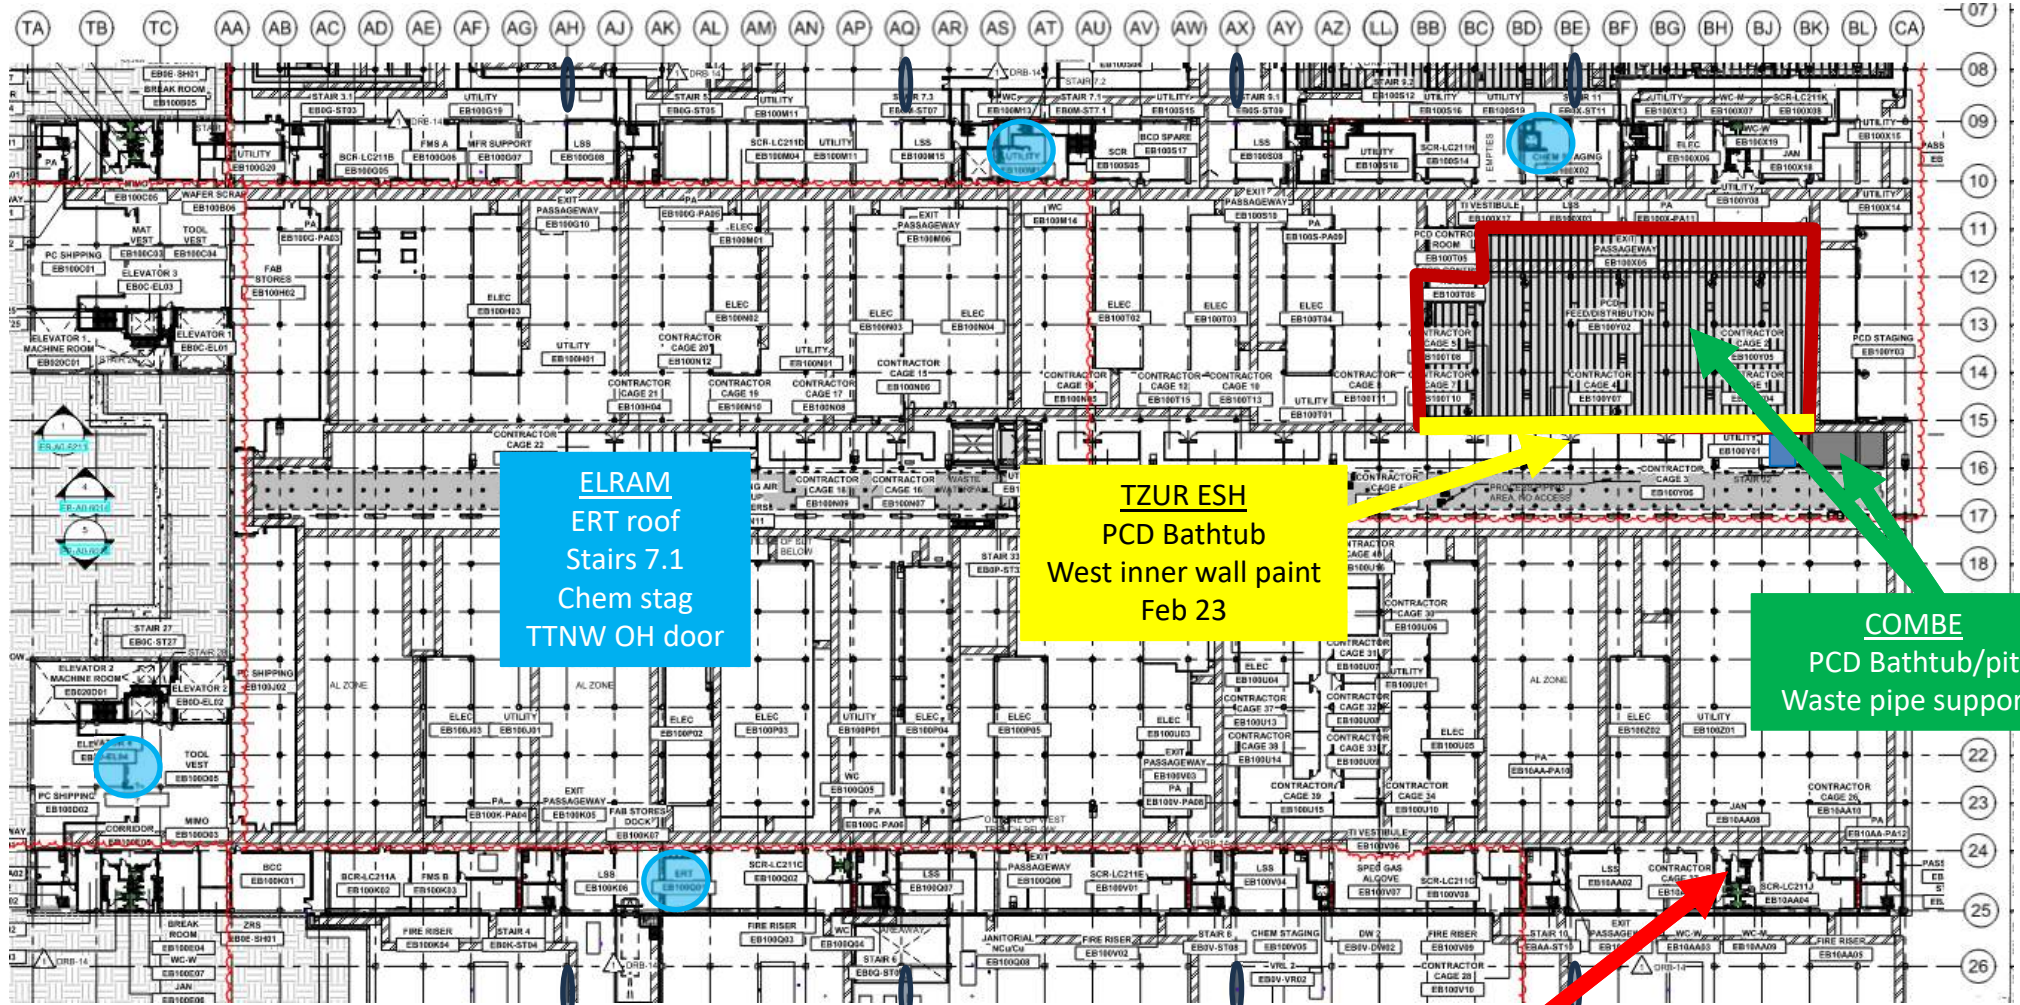


ELRAM
ERT roof
Stairs 7.1
Chem stag
TTNW OH door

TZUR ESH
PCD Bathtub
West inner wall paint
Feb 23

COMBE
PCD Bathtub/pit
Waste pipe supports


SN
Chipping 5W WC's

SUT 38.1 LEVEL

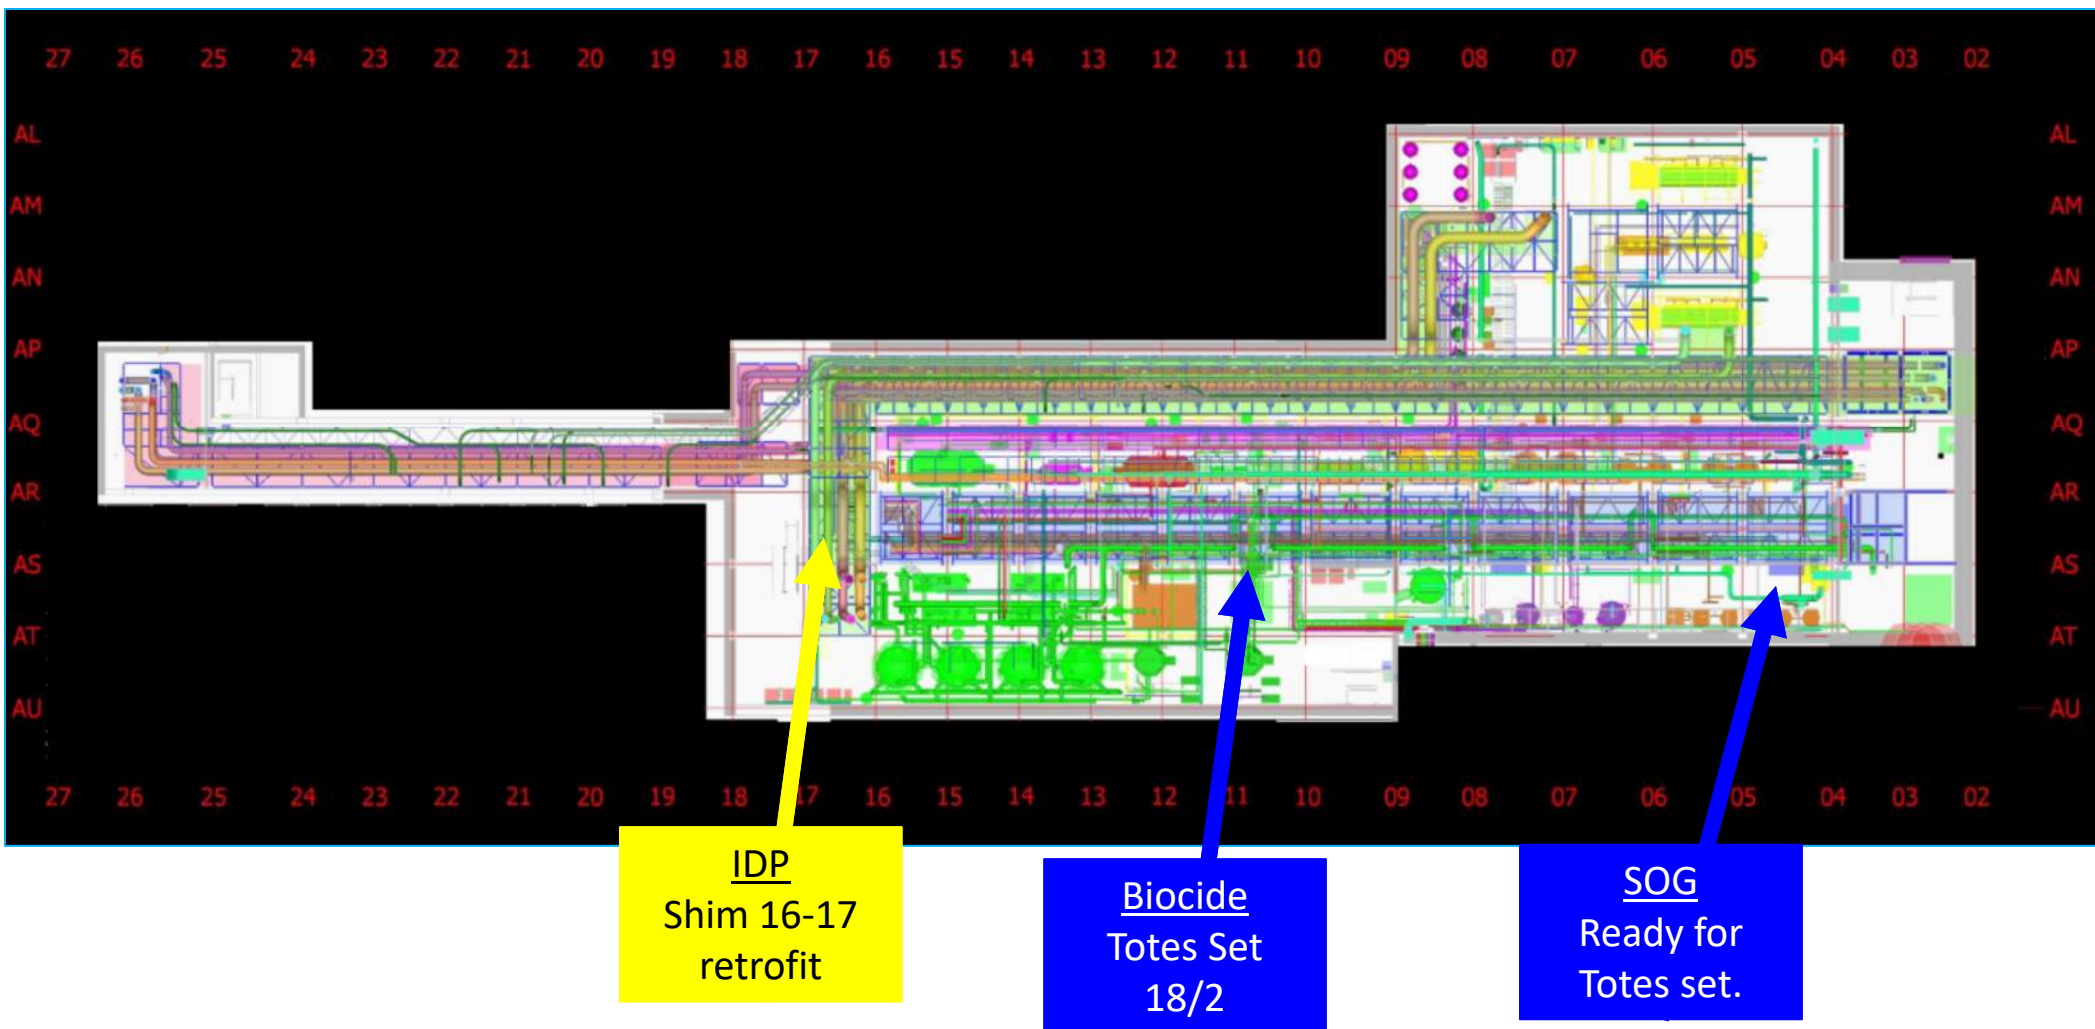

SUT 38.2 LEVEL


Rack 4b
Inter
Connection's

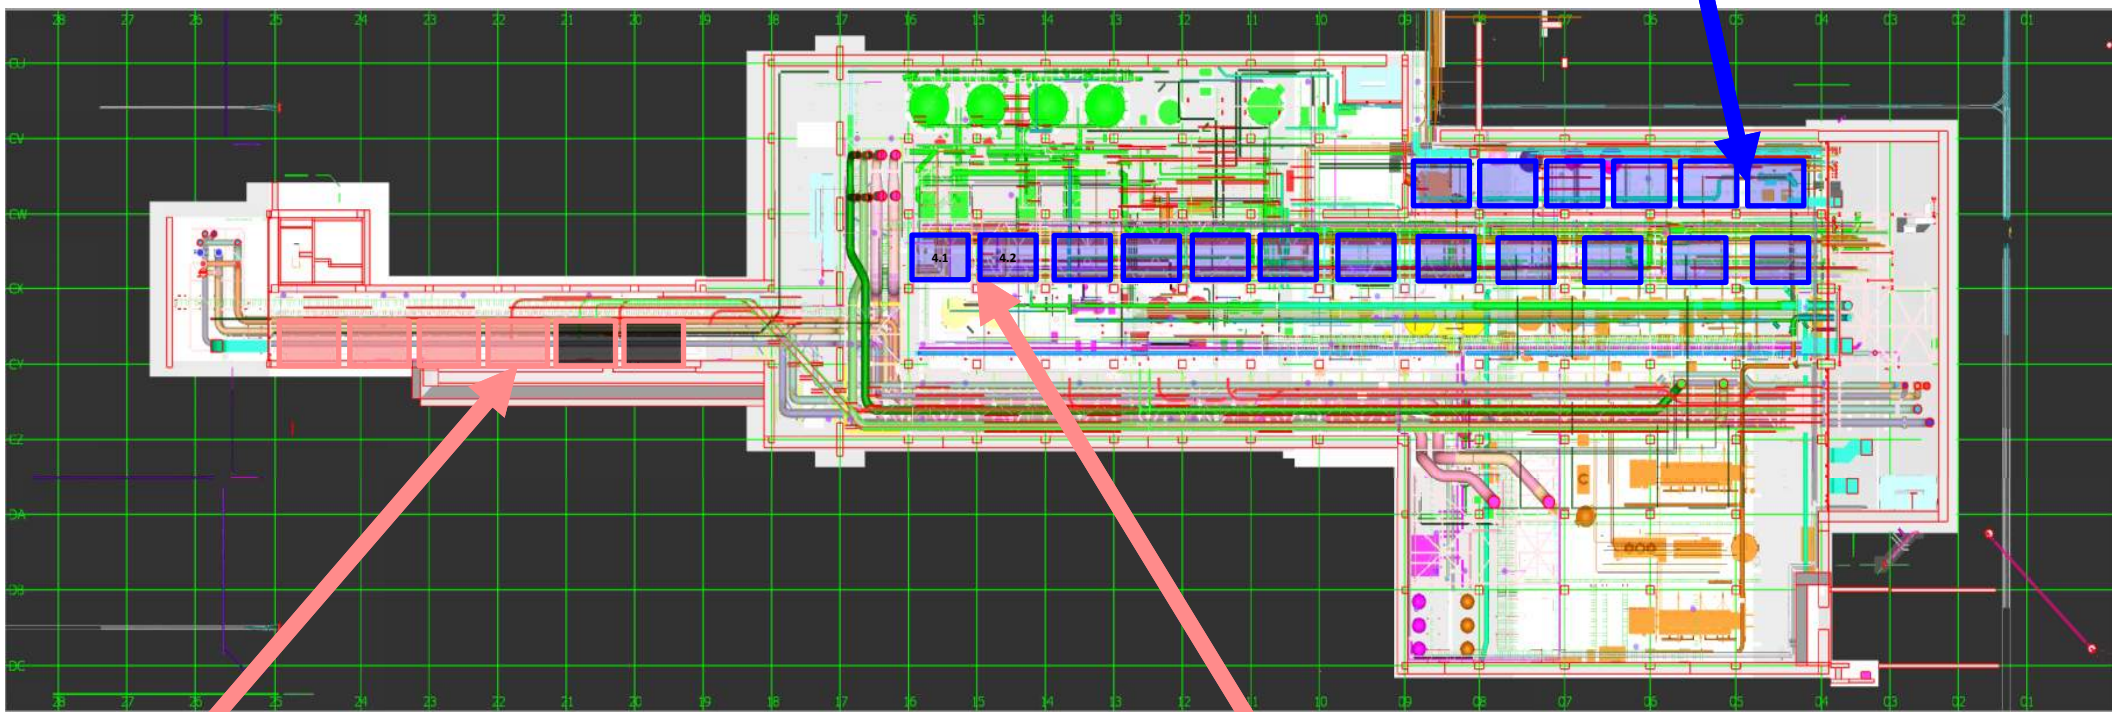


Temp stairs
relocation

16.2.2025	Module 1
17.02.2025	Module 2
24.02.2025	Module 3
25.02.2025	Module 4
03.03.2025	Module 5
04.03.2025	Module 6


SUBFAB BUILDOUT MOD 1

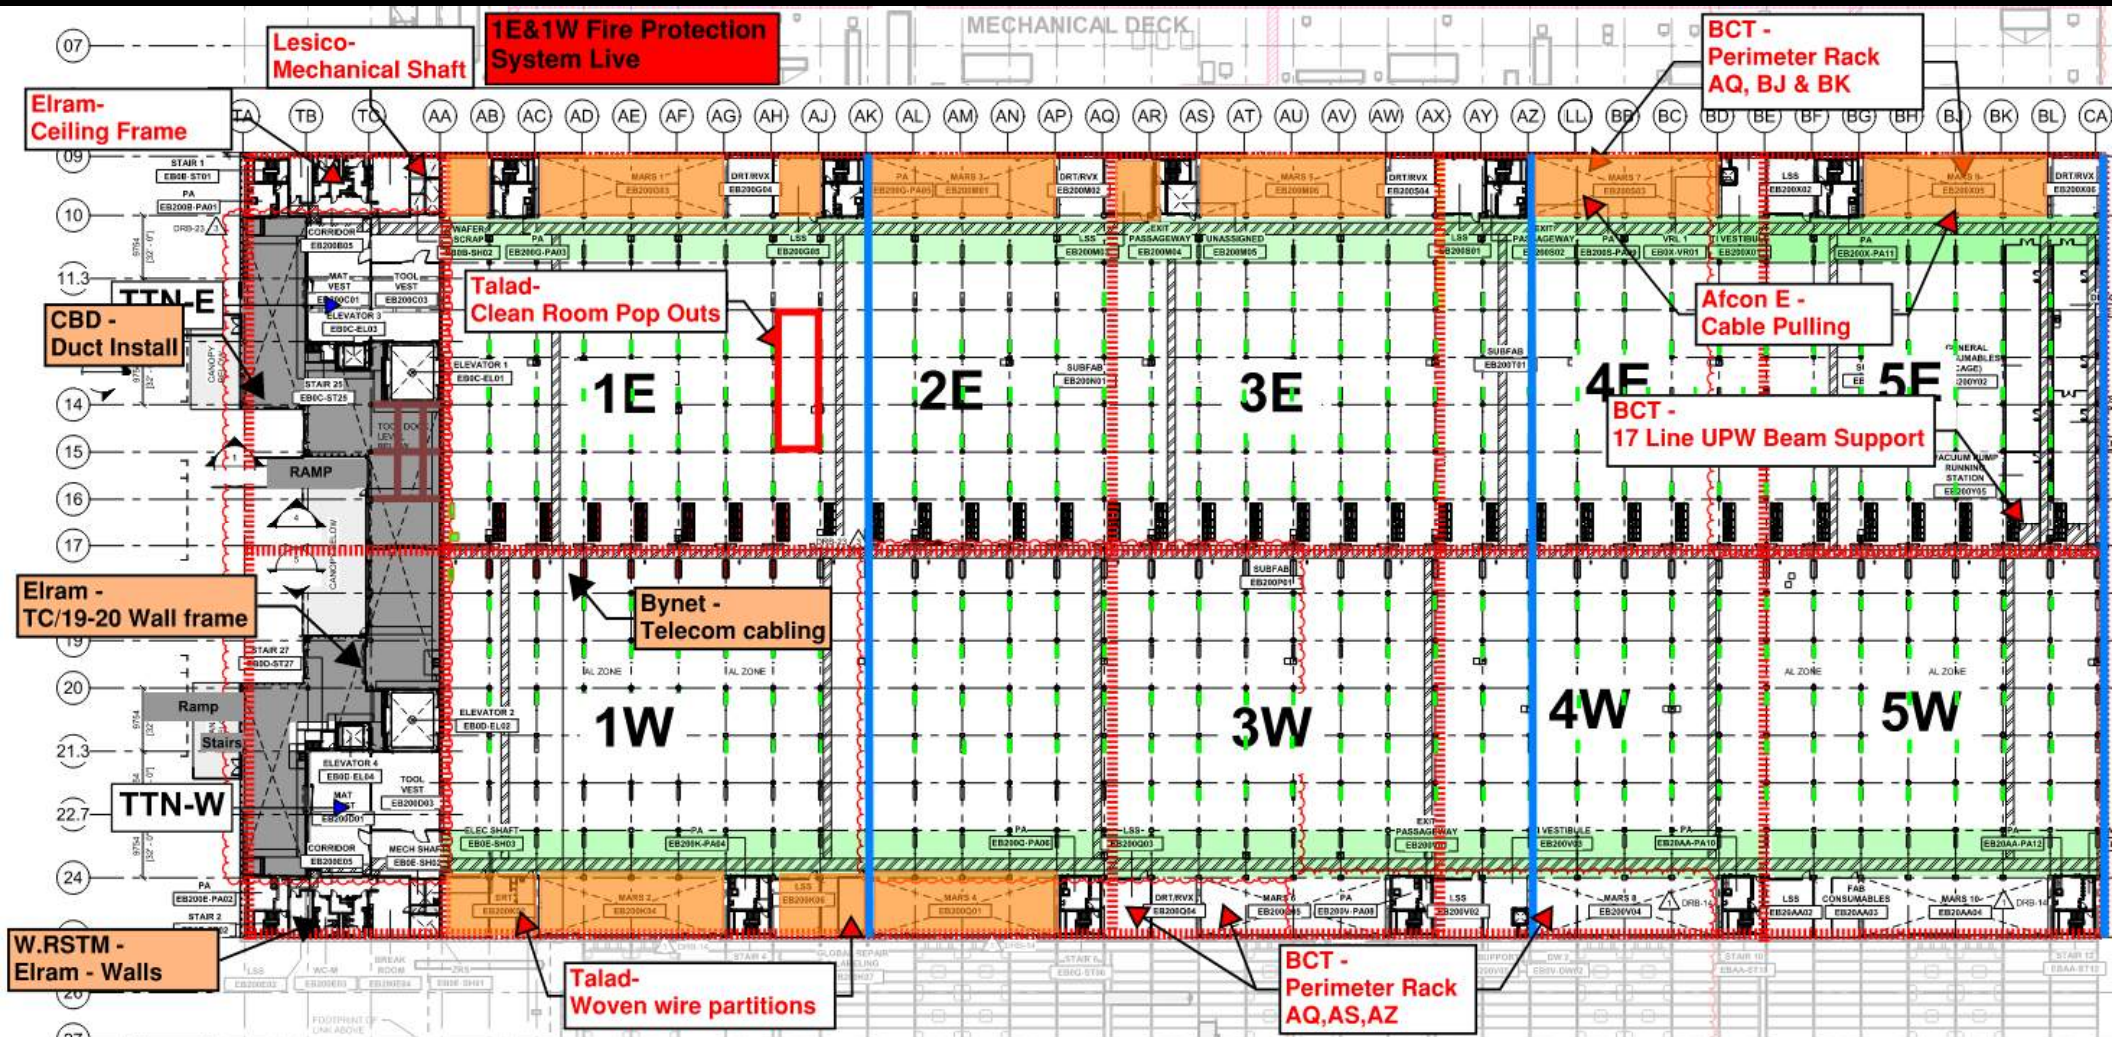


SUBFAB CRC TOPCOAT

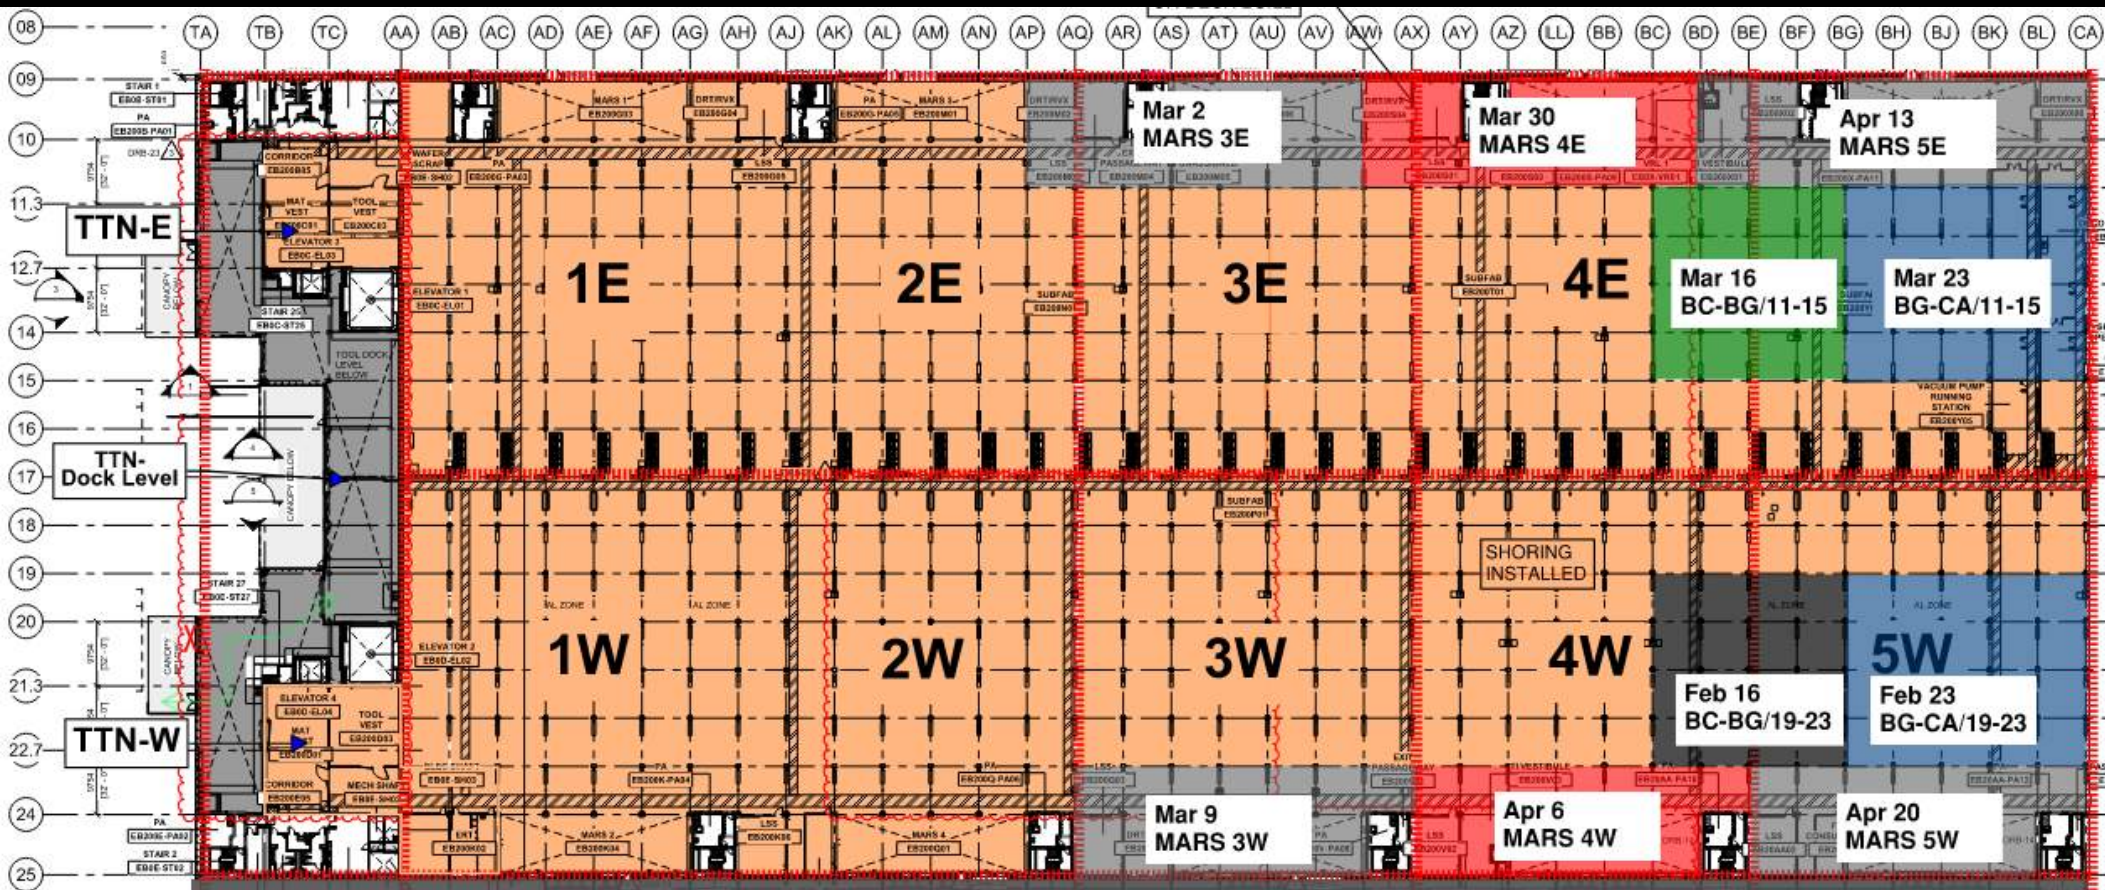


BCT Pressure Tests Today

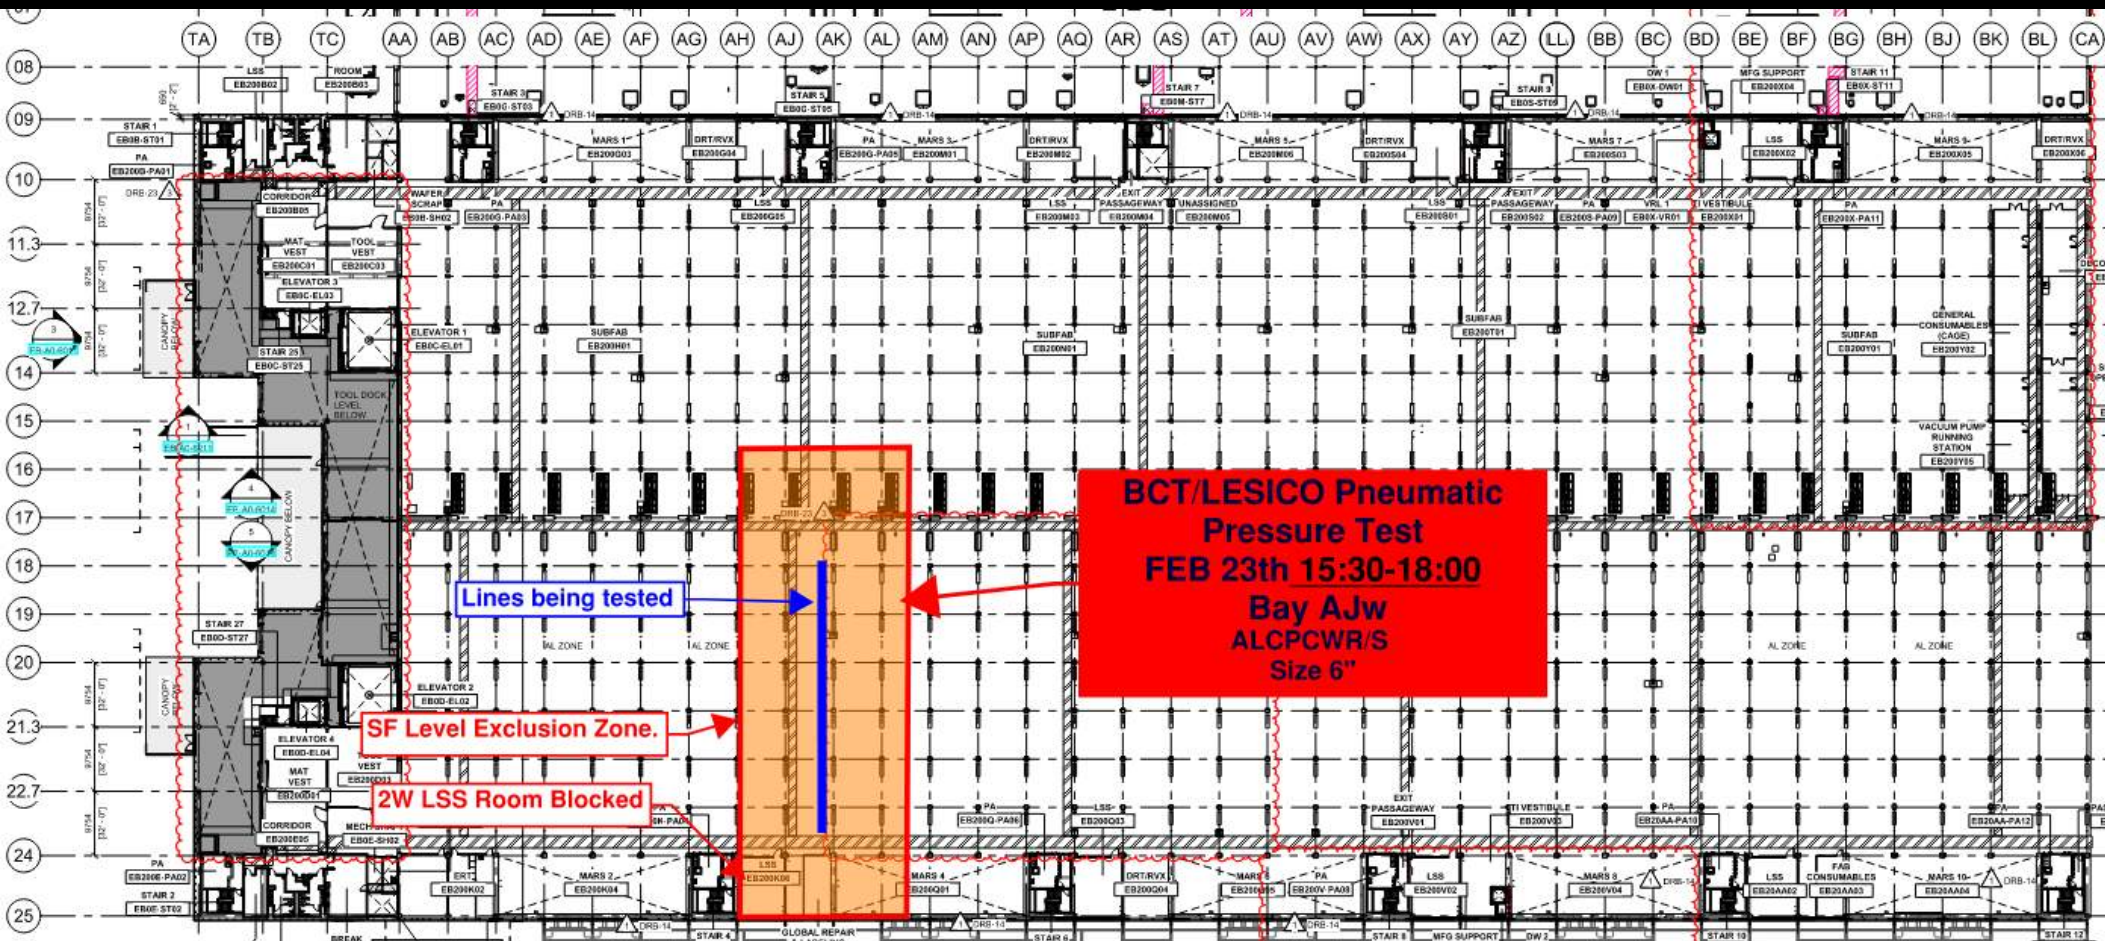



BCT Pressure Tests Tomorrow

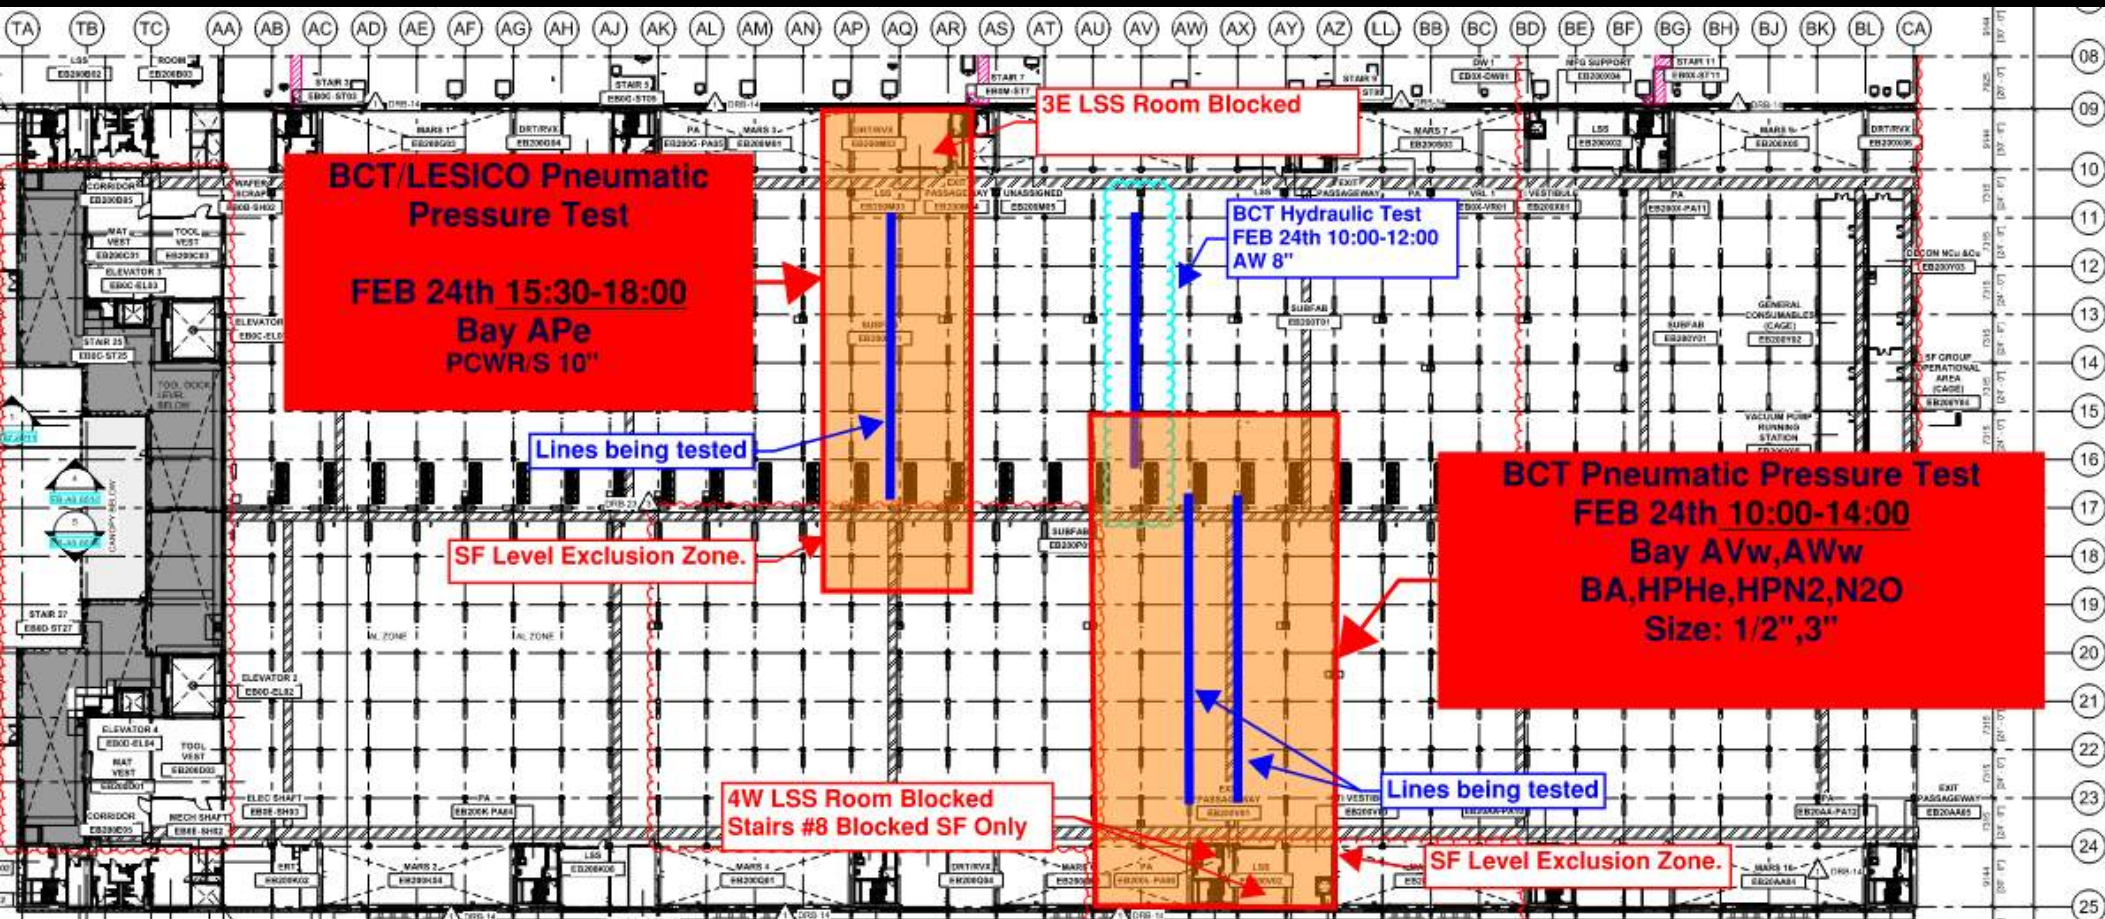



SUBFAB BUILDOUT MOD 2

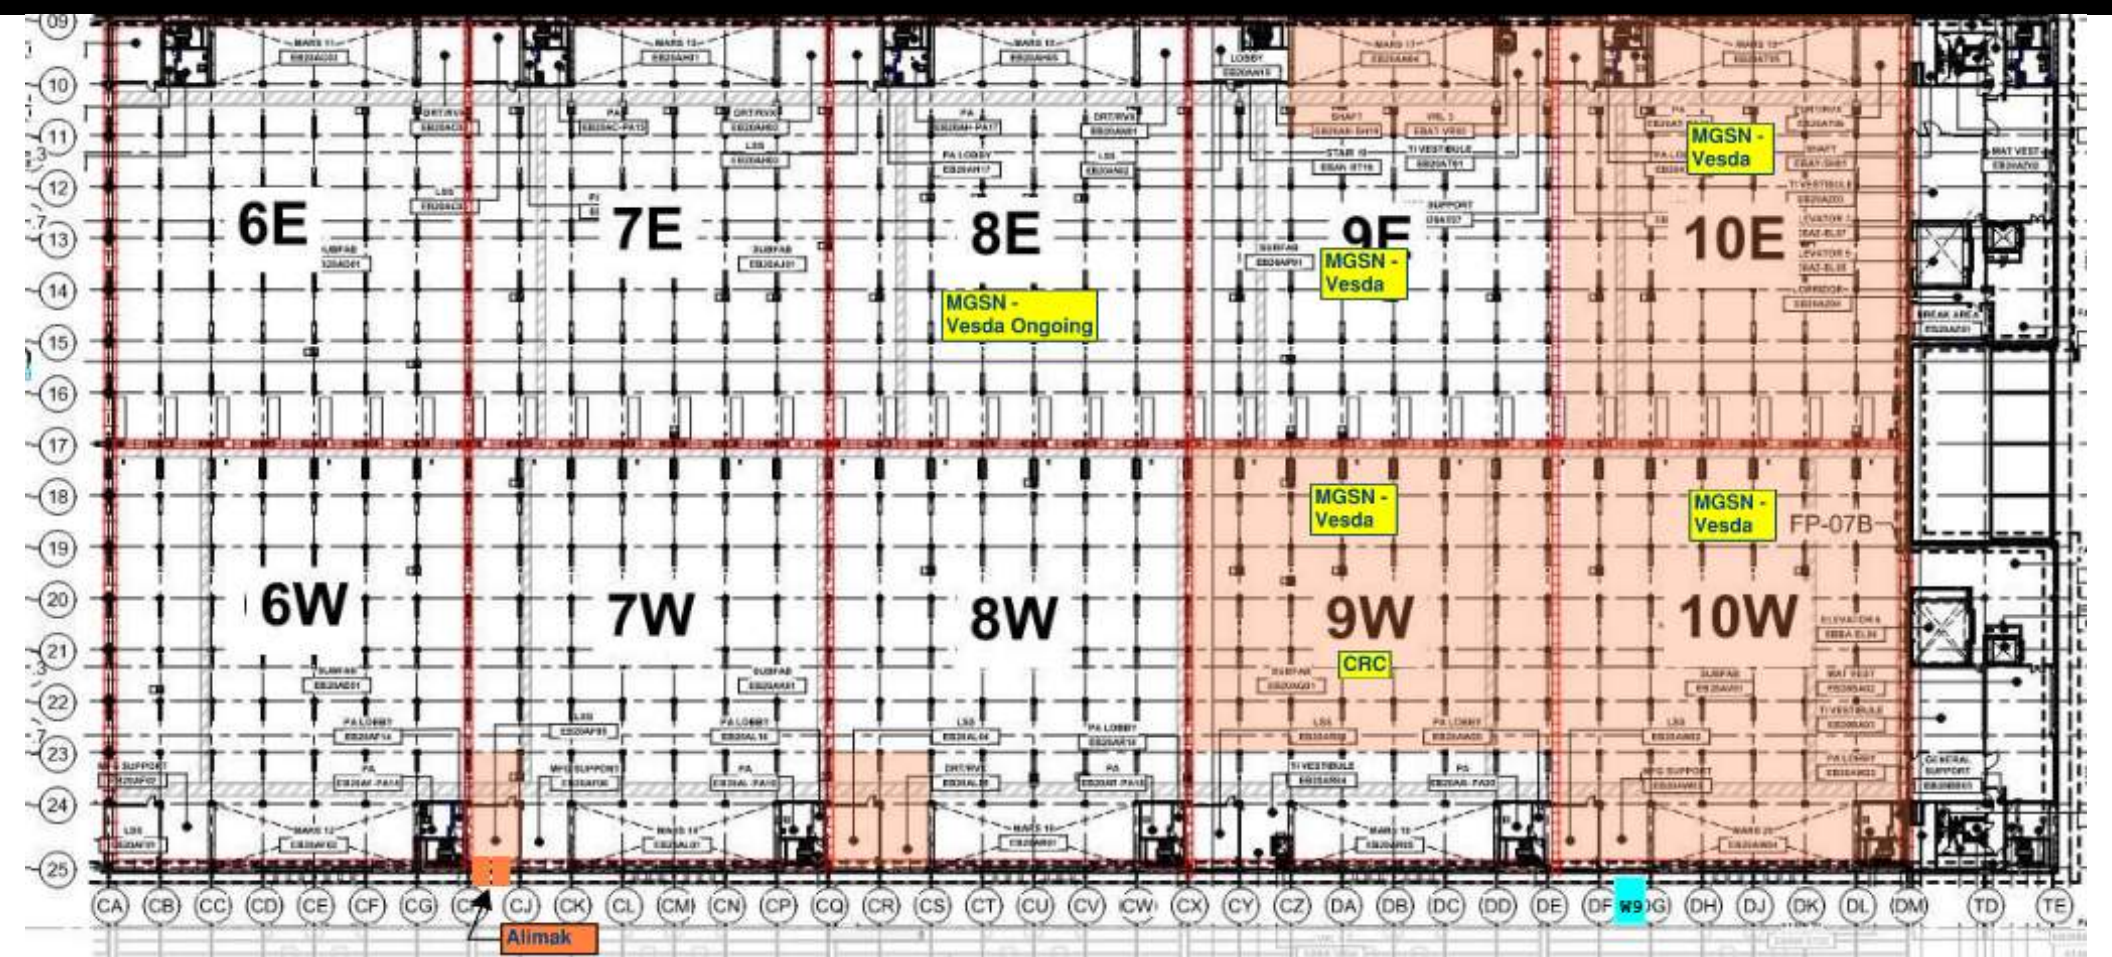

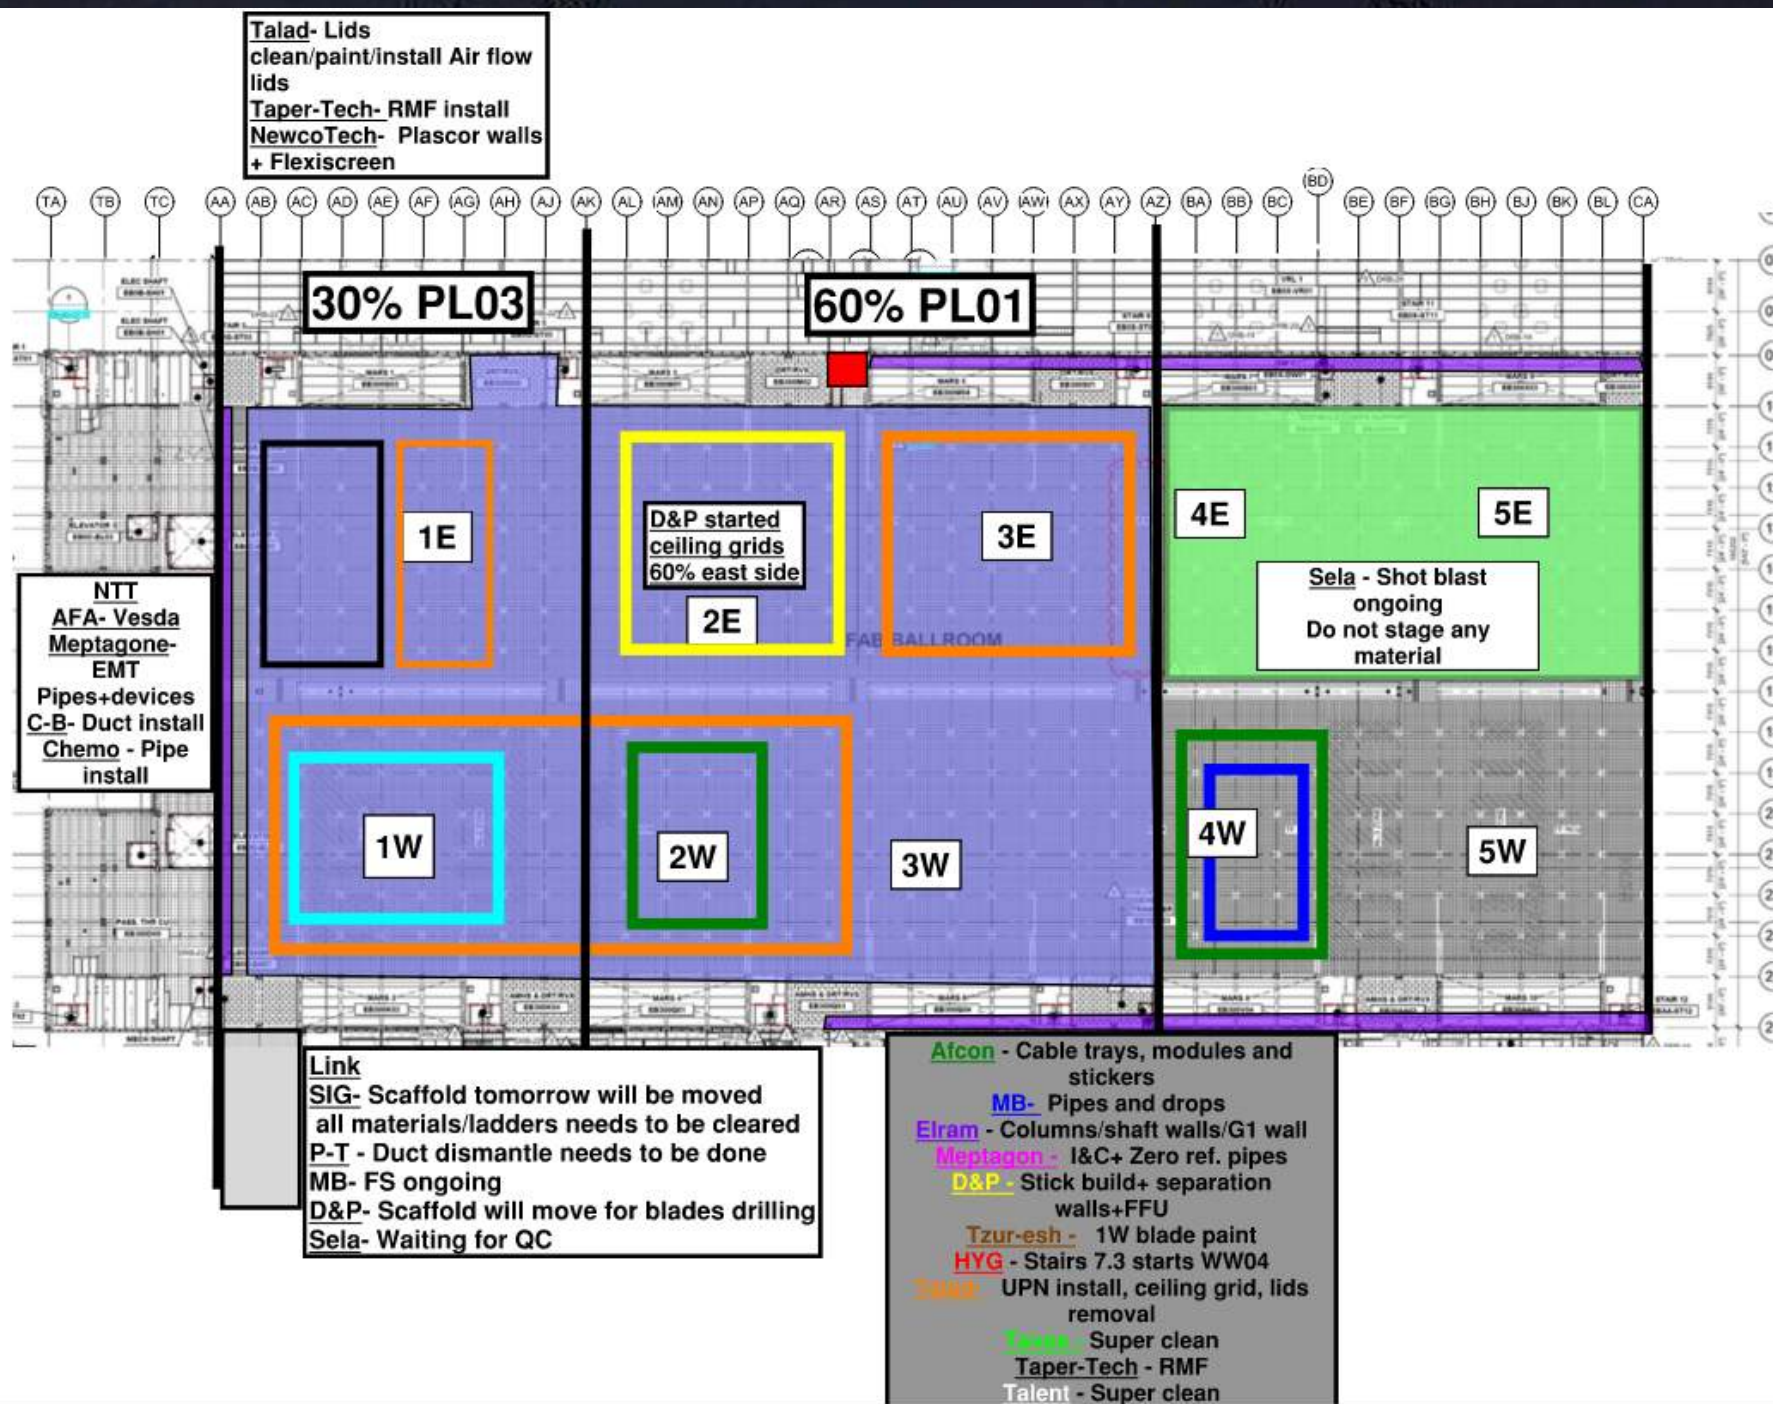


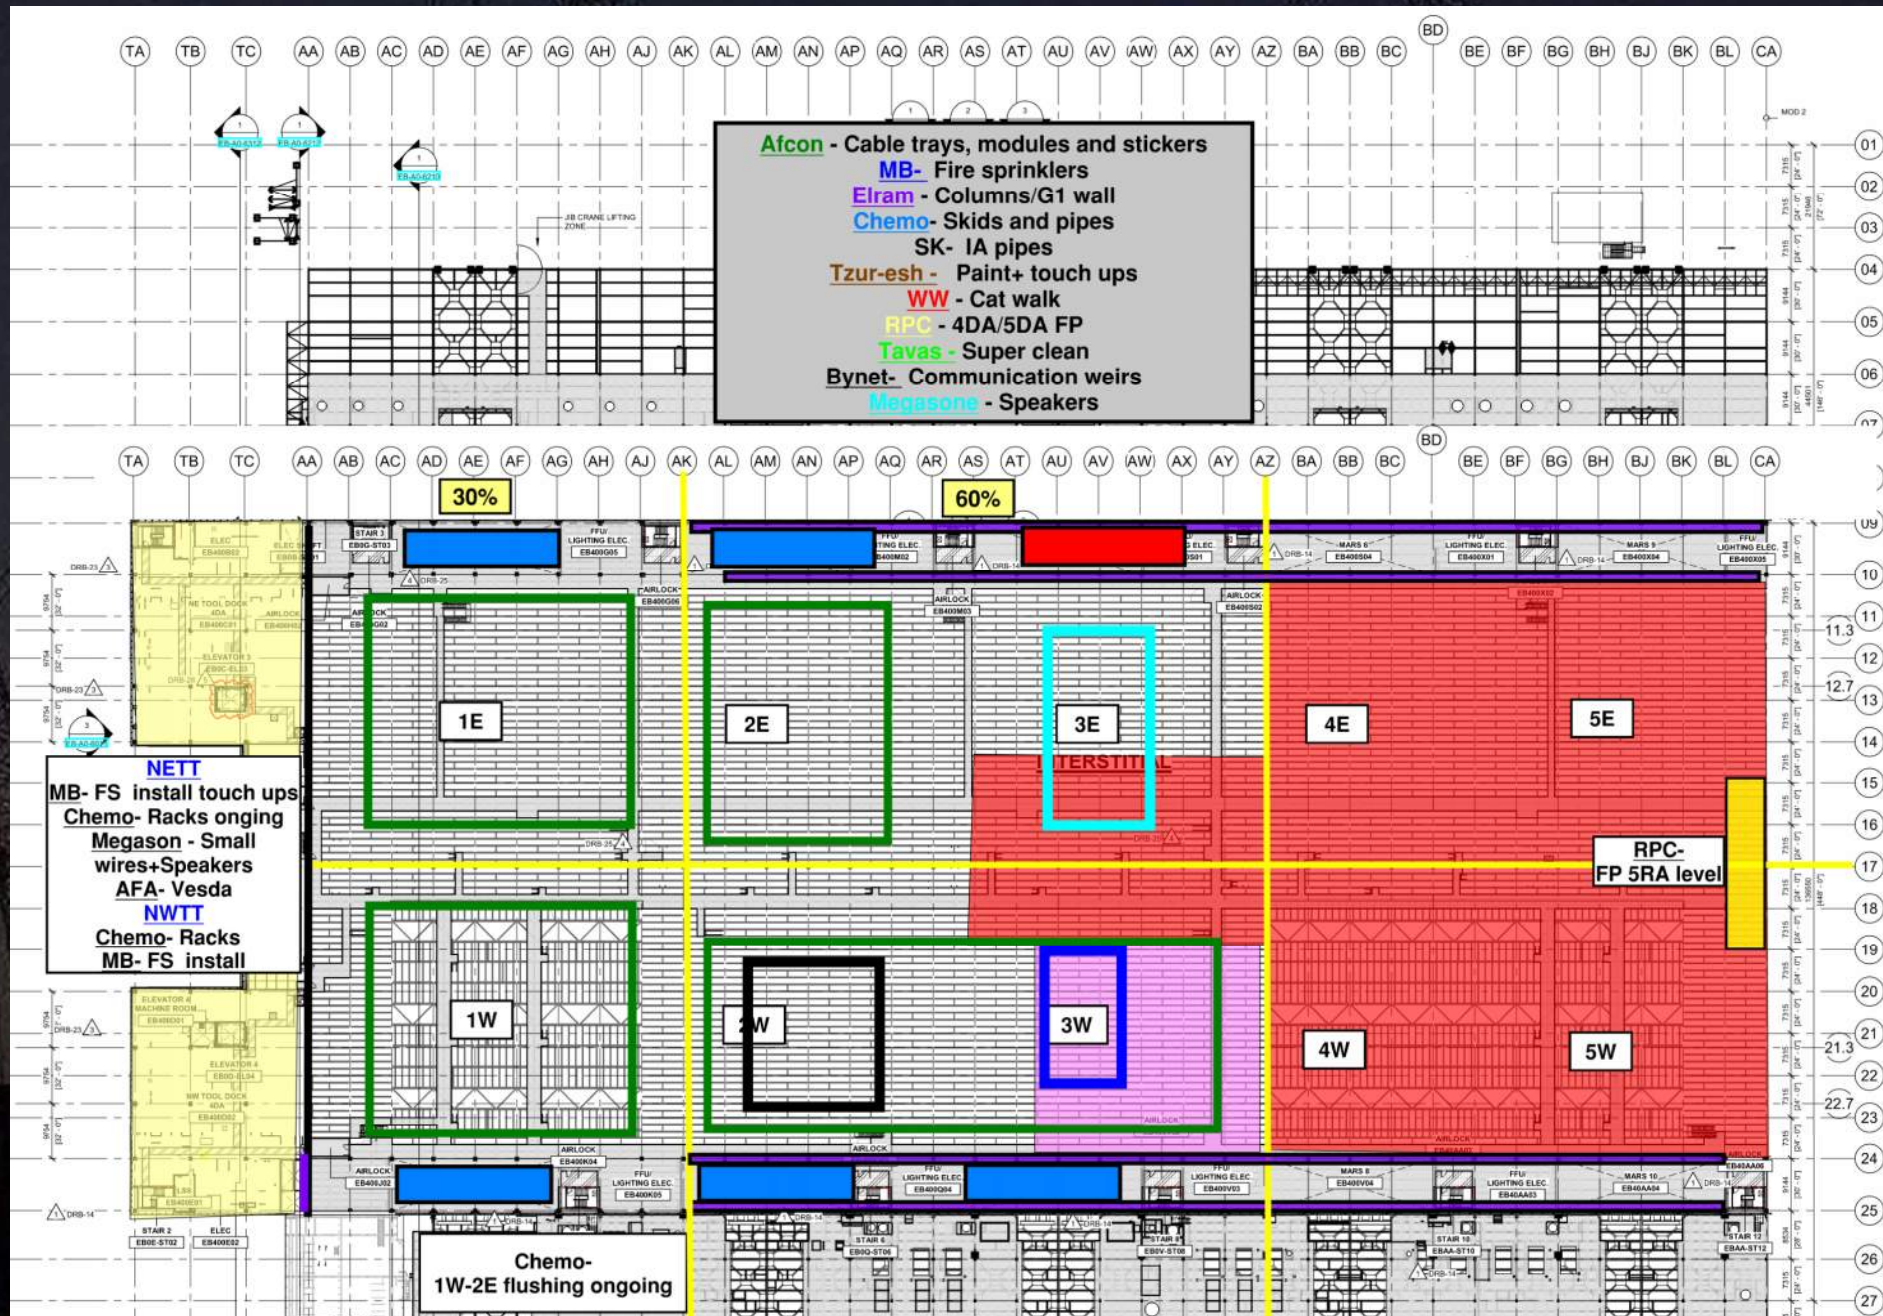

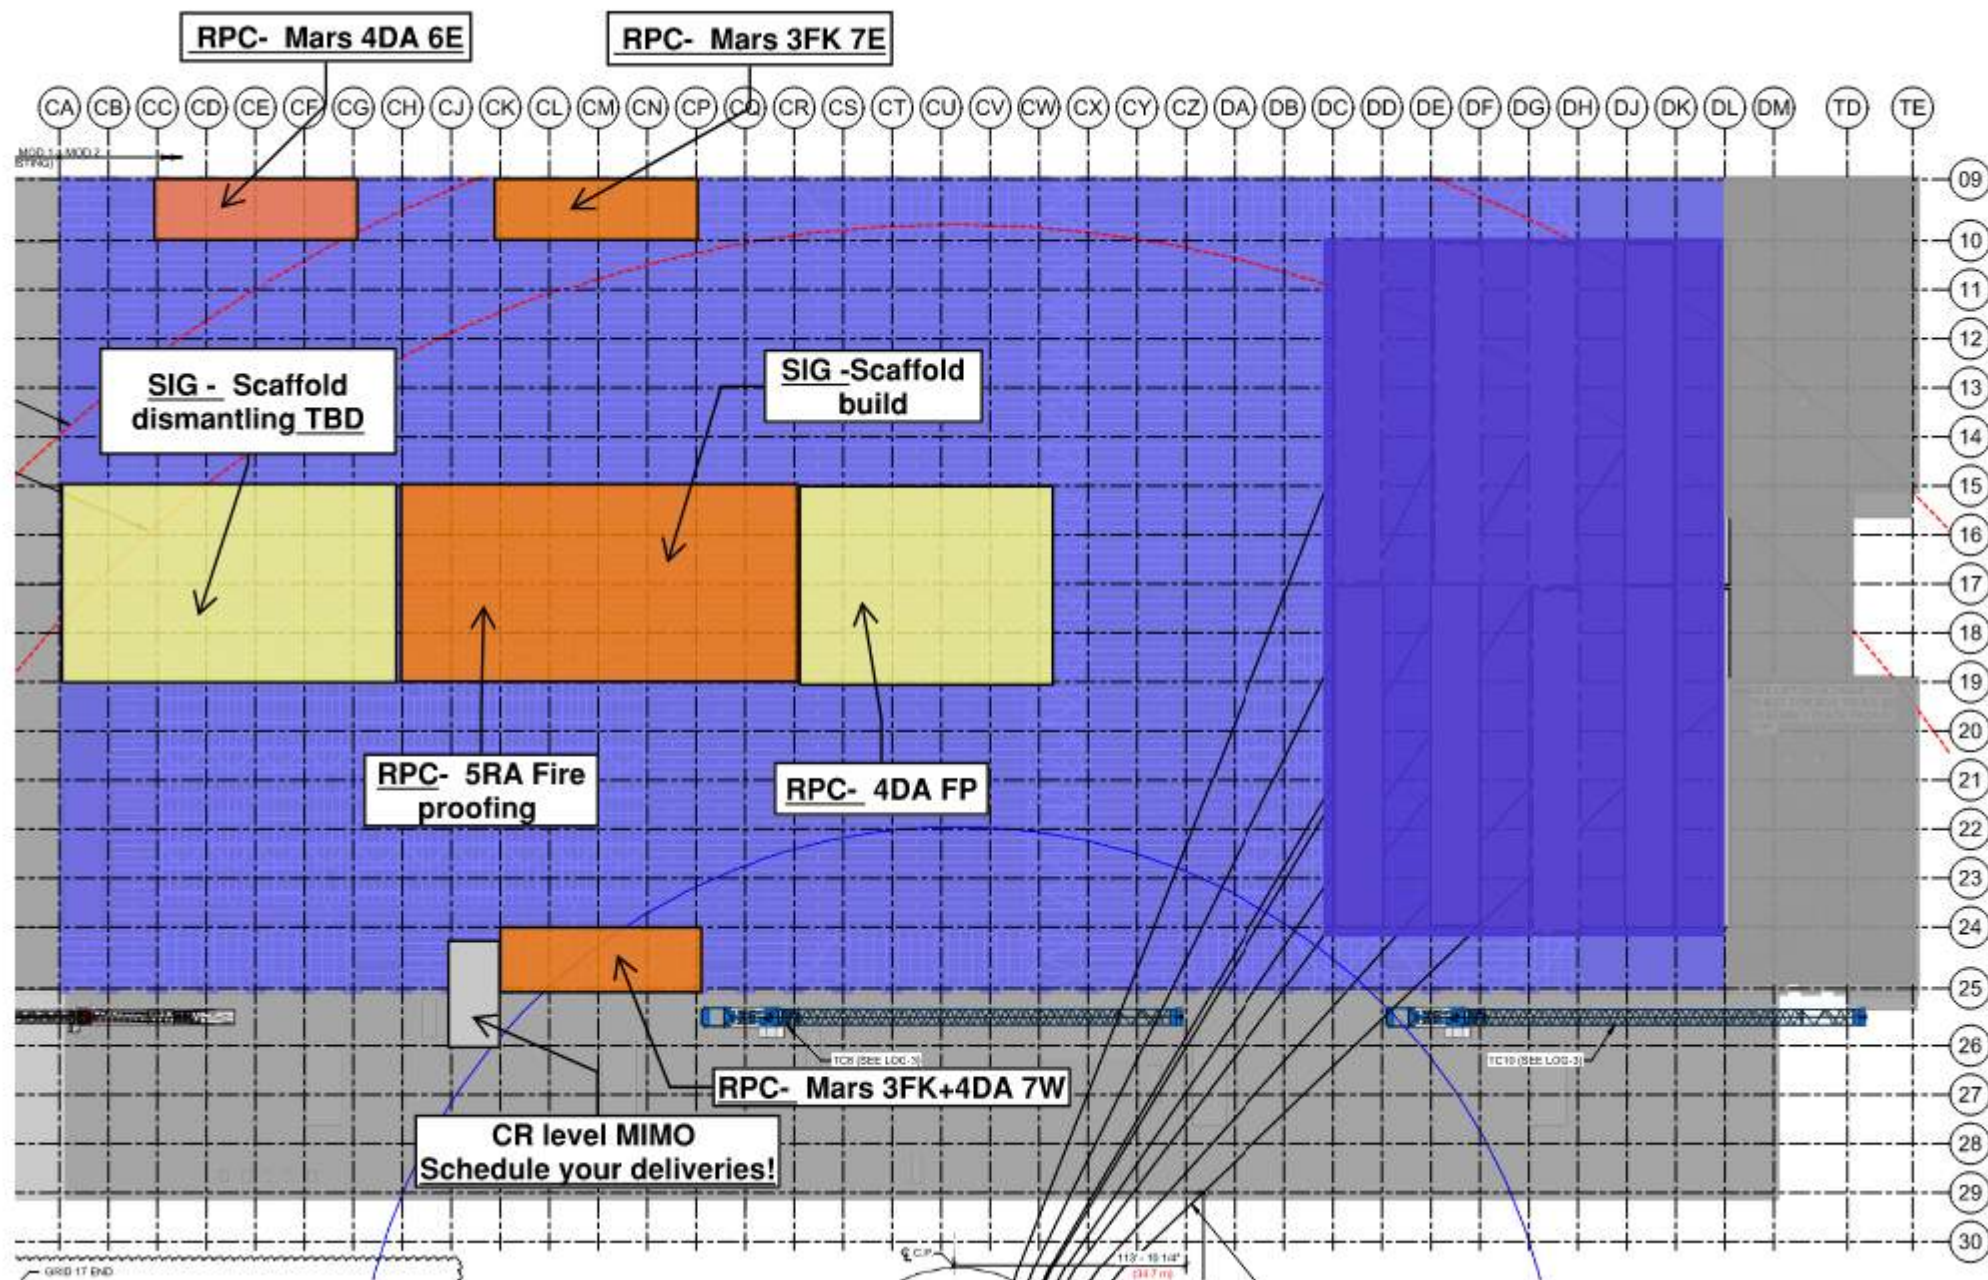


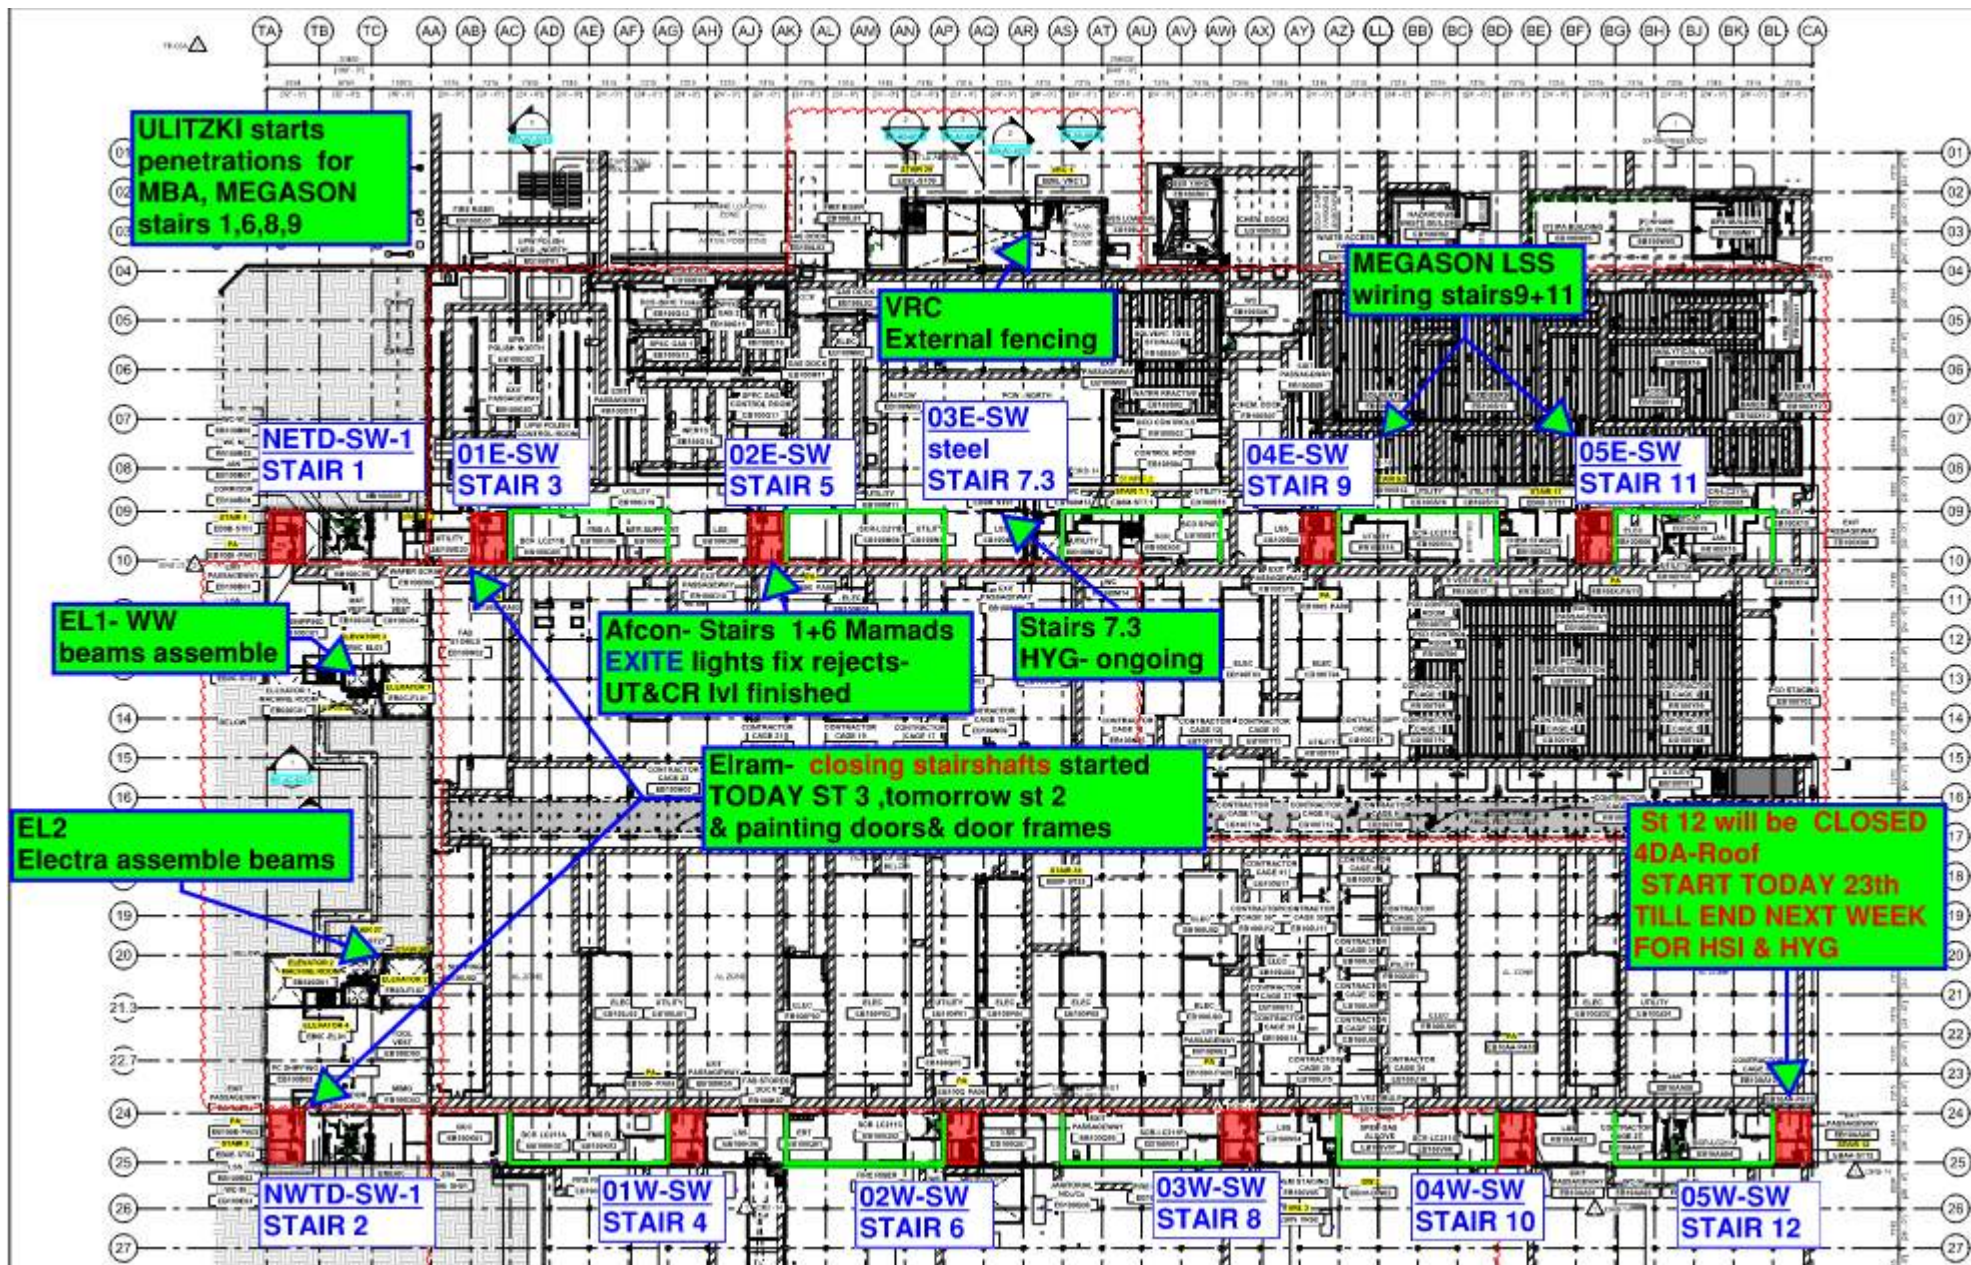


Siding Penetration Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

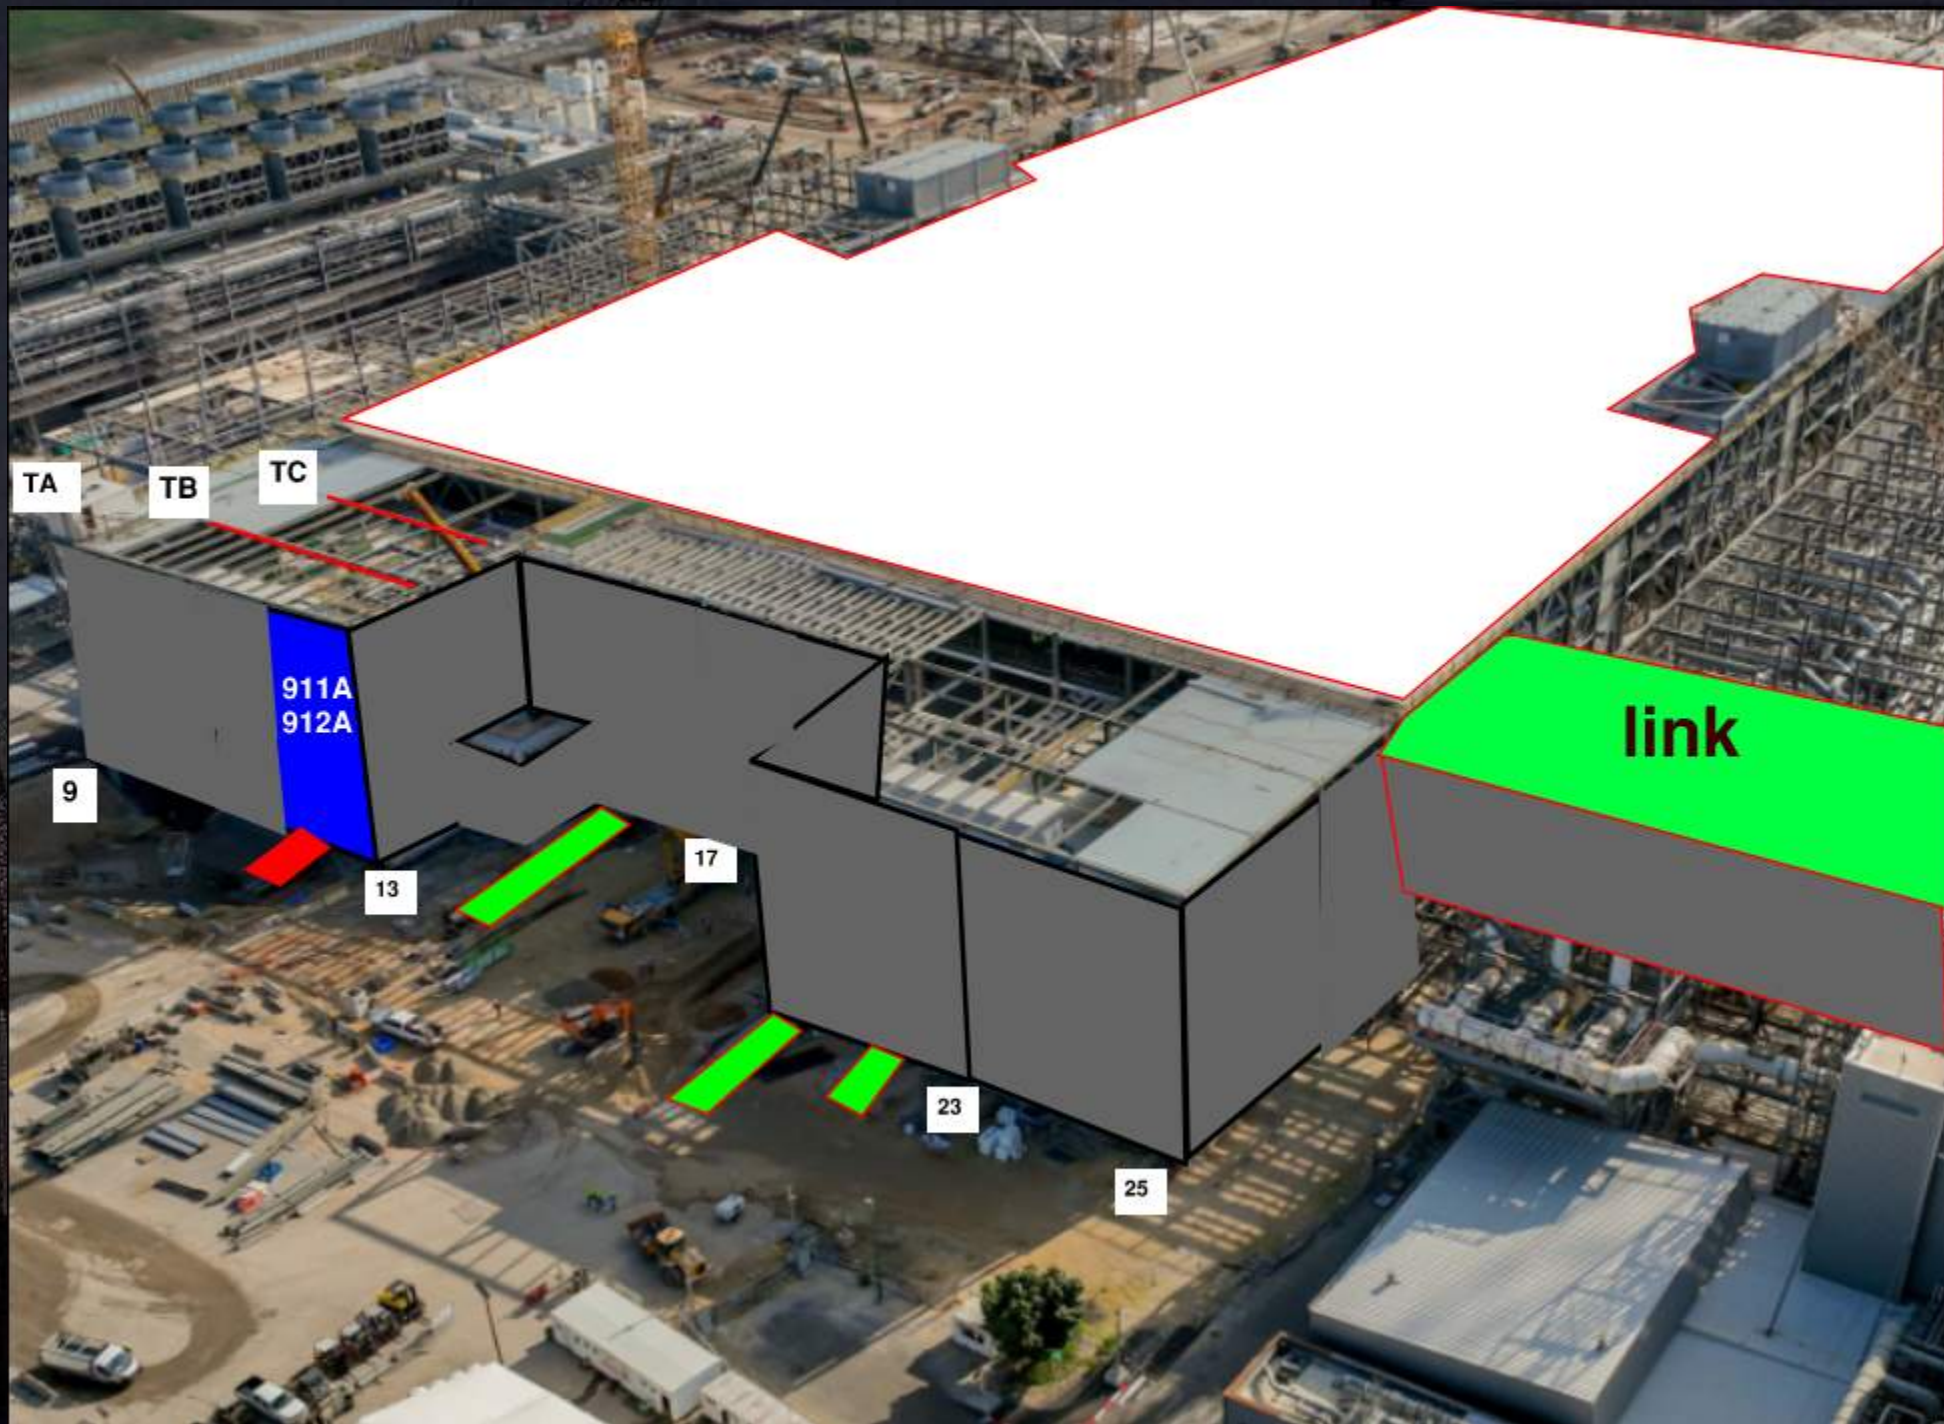

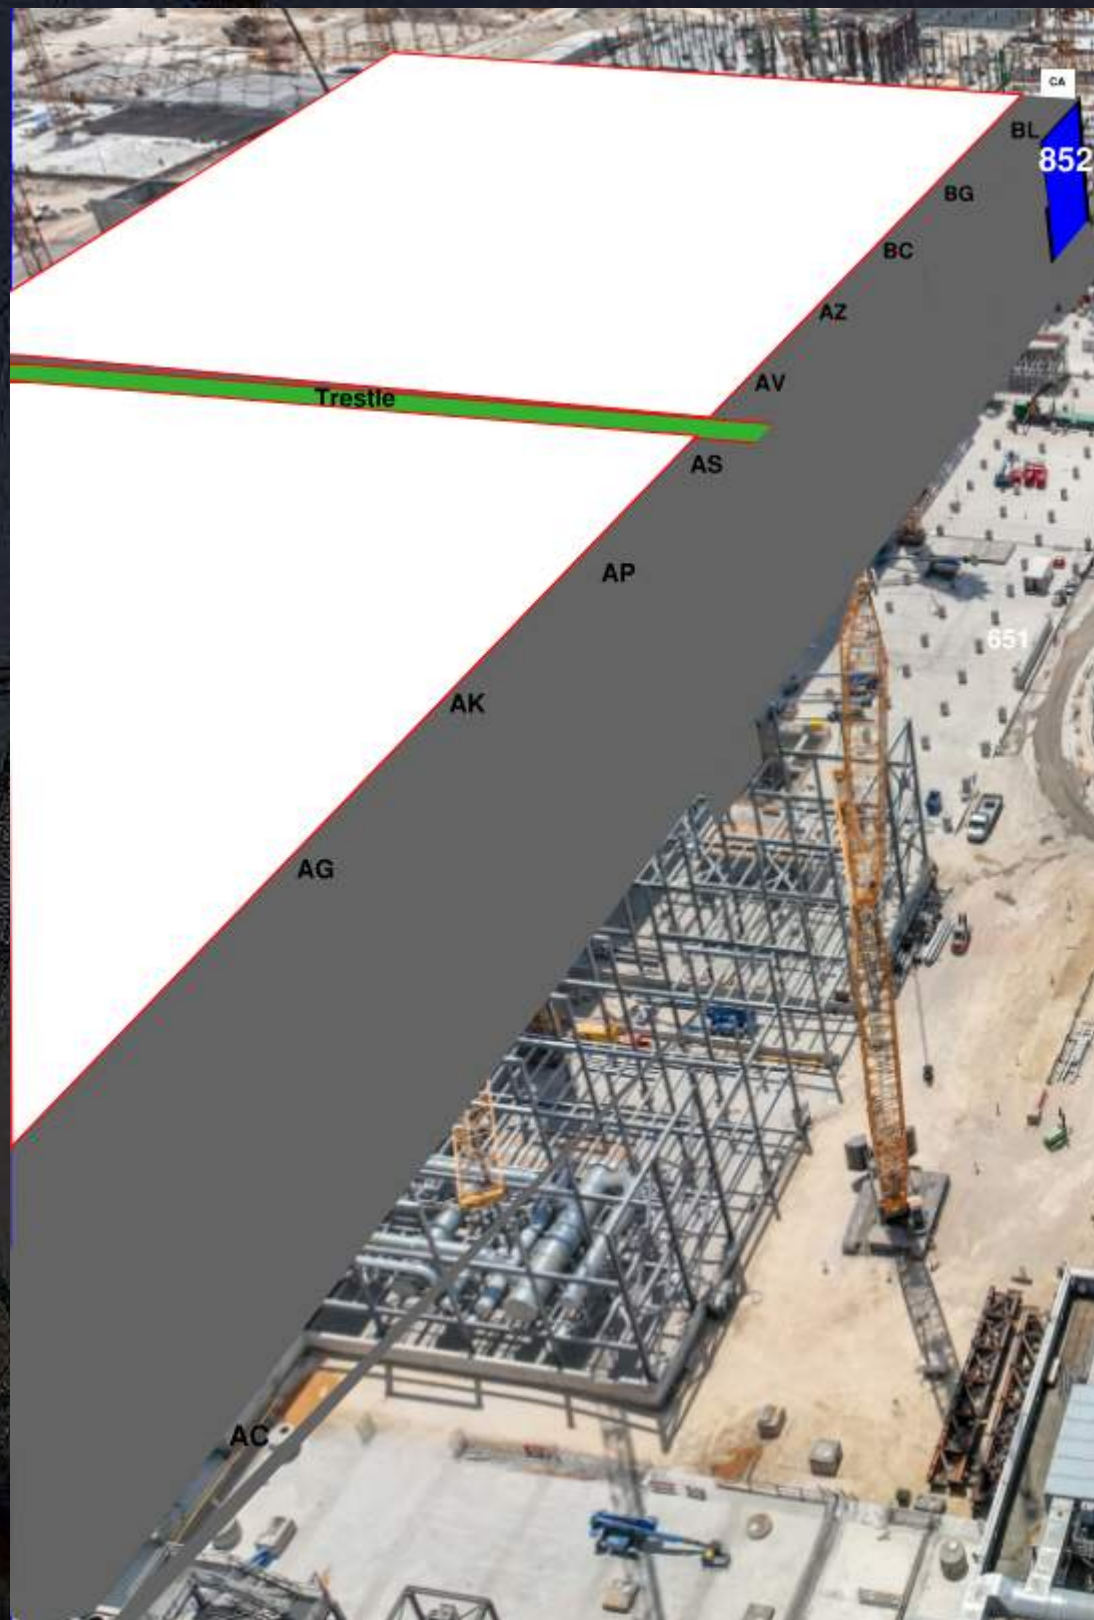

MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 

PANELS INSTALLED 

2602/
2601

2612/
2611

2622/
2621

2632/
2631

2642/
2641

2652/
2651

2812/
2811


2822/
2821

2832/
2831

2842/
2841


2852/
2851

PSSS.1

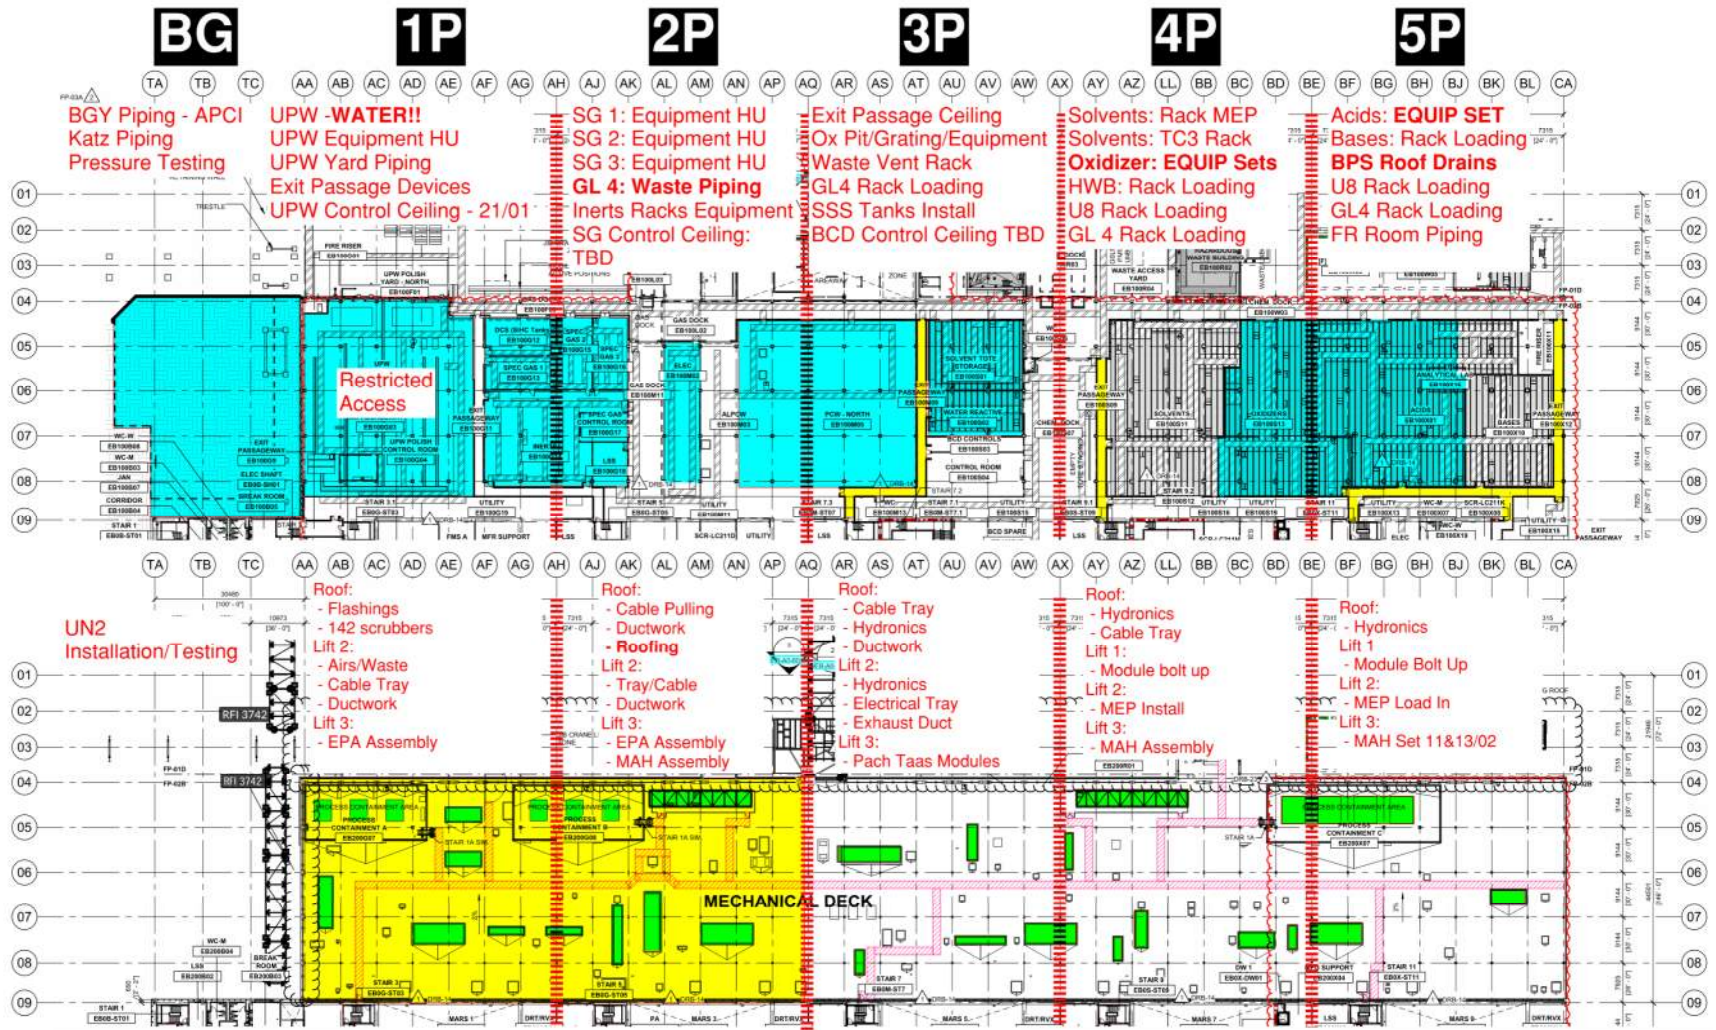


PSSS.2

Utility Level
1YA

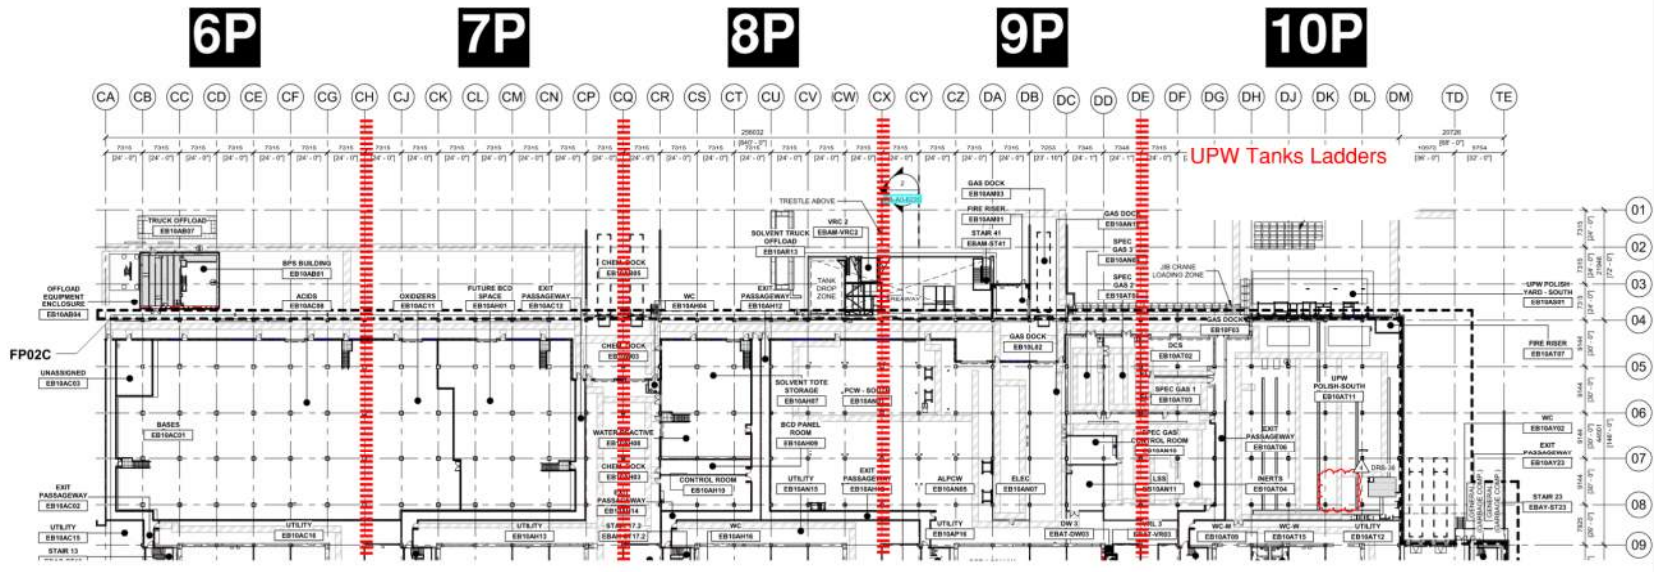

PSSS Roof
2SA

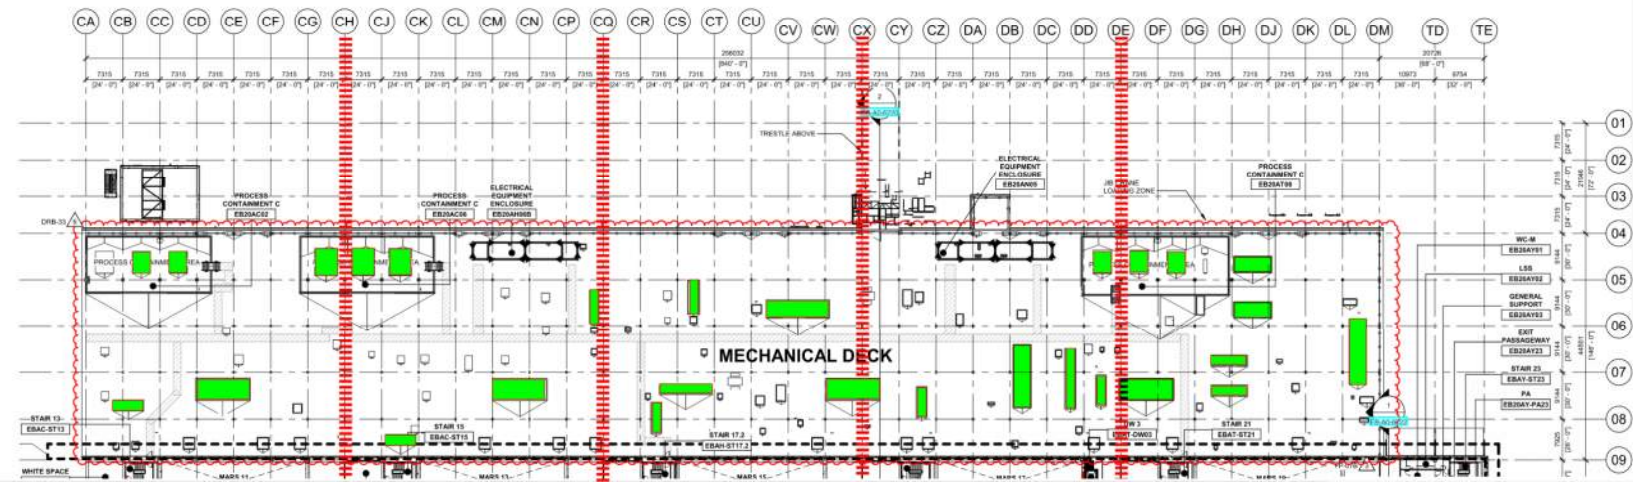




WJG – UL

* Megason - working on fire detection and alarm

* Afcon - installation of permanent lighting and cable pulling.
* Pach Taas - installation of modules in west SUT.
* Carmel Bidud - working on dampers and ducts into the FAB

* Afcon - installation of permanent lighting and cable pulling to the fixtures.
* Pach Taas - installation of wall penetrations

* SK - installation of 3" cooper pipe
* W&W - welding of shims for outriggers

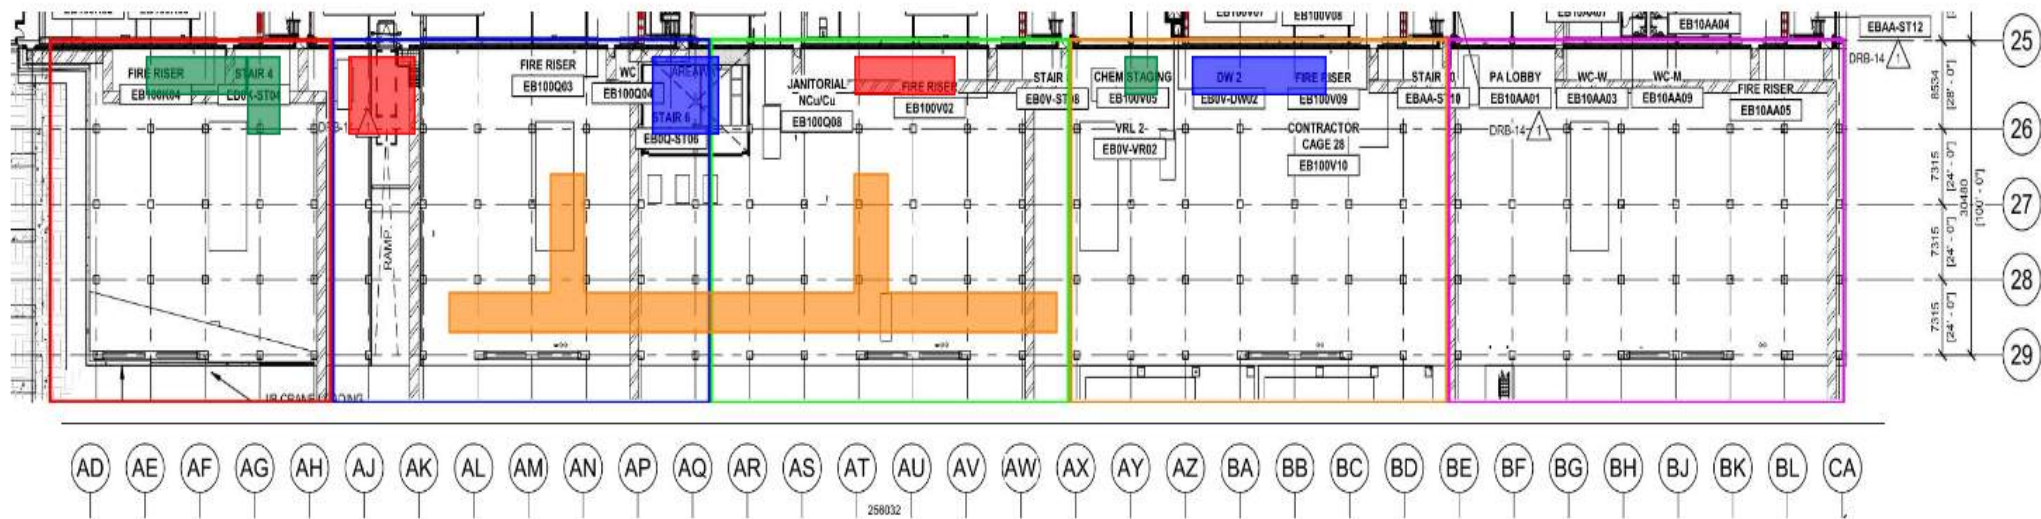


WJG – Lift 2

* Pach Taas - installation of 1800 mm module and WP.

* SK - installation of CRW pipes to MAH.
 * Afcon - pulling cables and doing connections to MAH.
 * 4J MAH scaffold will be dismantled on 27/02/25

* Chemo Aharon - finishing Insulation and filling UPN 117 with water for pressure test.
 * Chemo - pipe fitting for MARS pipes

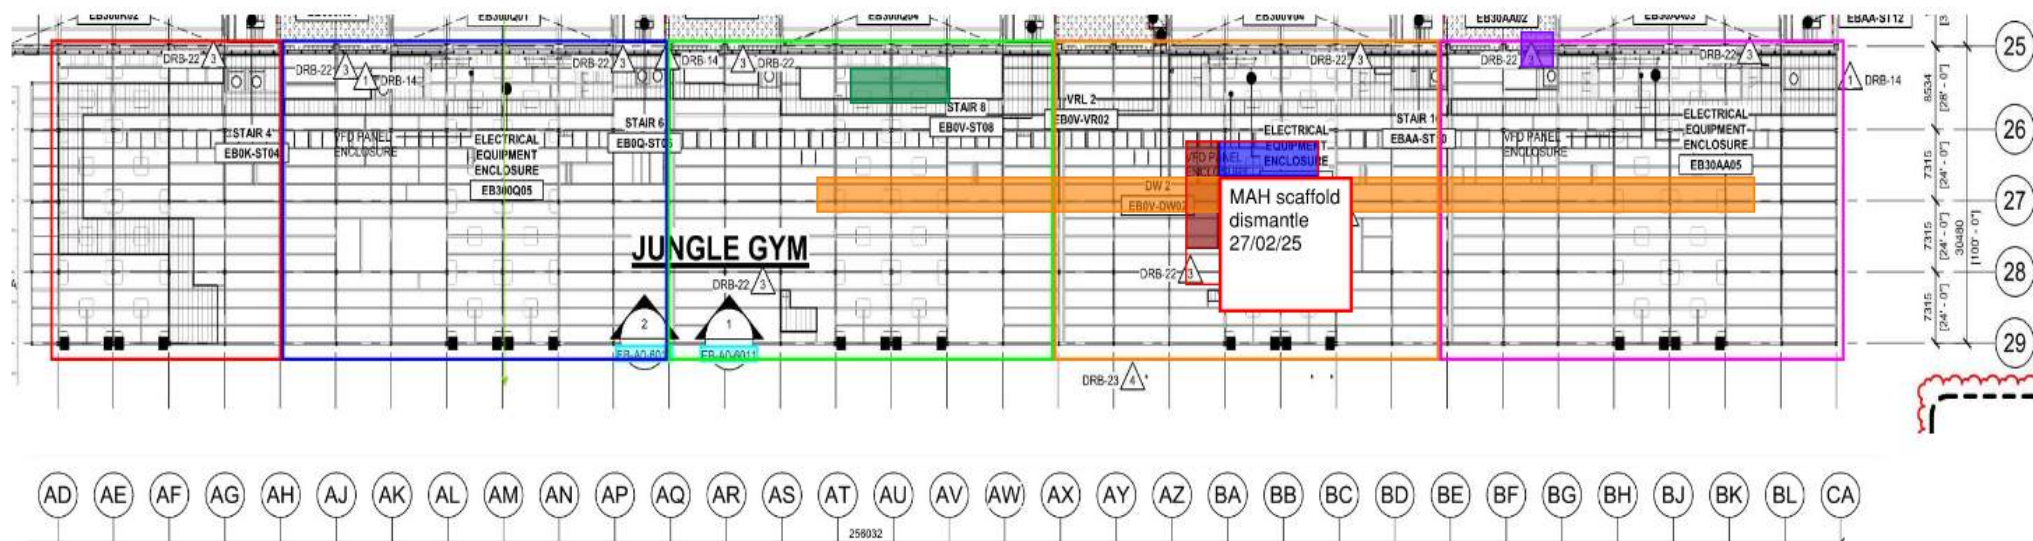

WJG – Lift 3

		* Pach Taas - working on bypass ductworks. * Sami Najami - cutting grating penetrations.	* Sami Najami - cutting grating penetrations.	Sami Najami - cutting grating penetrations. * Chemo - pipe fitting for MARS pipes
--	--	--	--	---



Pressure check for UPN 117 – UL

UL level(West JG) - Grids AL to BJ, 25 to 27



Pressure check for UPN 117 – LIFT2

Lift 2 - Grids AL to BJ, 25 to 27




Crane logistics

Crane: 220 ton crane
location: AF on west
road
leaves the WJG on
27/02/25

Crane: 500 ton crane
location: AQ on west
road

Crane: 650 ton crane
location: BE-BK on west
road

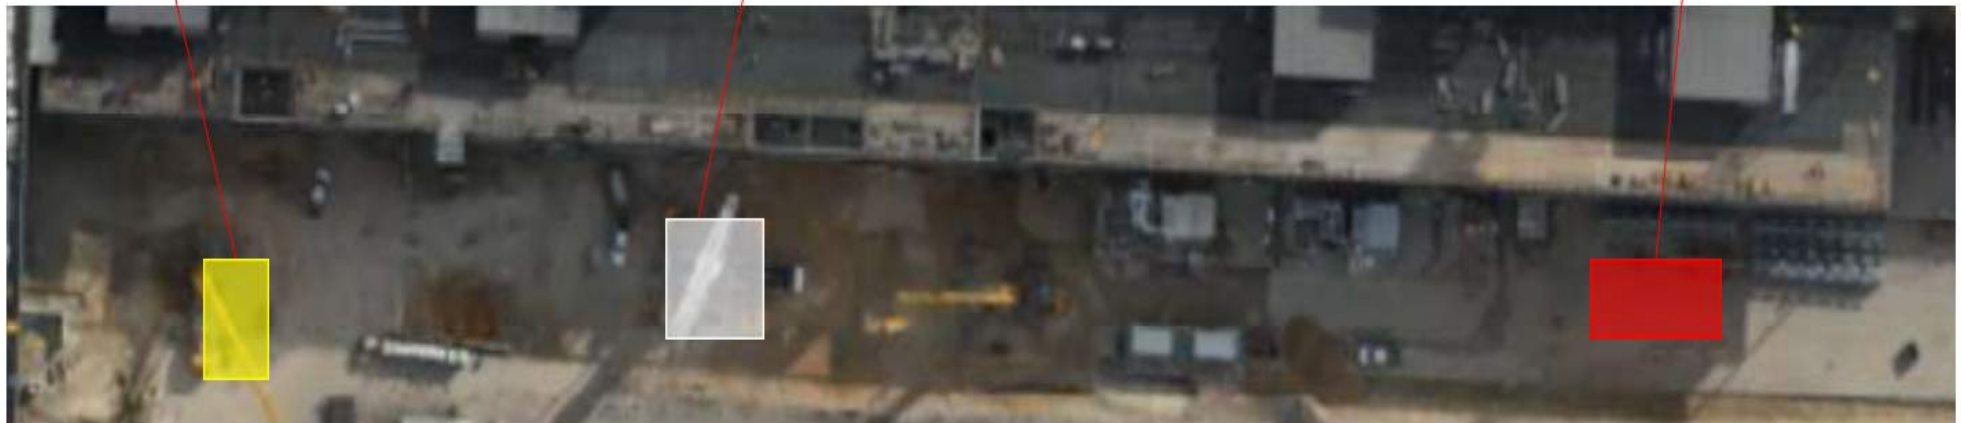

Map Labels:

- North Yard:** WATER TREATMENT, NORTH YARD
- Buildings:** CTB 114, SWS 237, ROP 242, URW 262, SAND FILTERS, CHILLERS, ELECTRICAL, OPS READY / PUNCHLIST RESTRICTED ACCESS SEE RED AREAS, FMS CONTROL ROOM, MECH CONTROL ROOM, MECH WORKSHOP, LIWS LAB, ANALYZER ROOM, NH4W 283, BOILERS, OIL FUEL TANK
- Stairs:** STAIR 1 (TO ROOF), STAIR 2 (TO ROOF), STAIR 3, STAIR 6, STAIR 7, STAIR 8, STAIR 9, STAIR 10, STAIR 11, STAIR 12, STAIR 13, STAIR 14, STAIR 15, STAIR 16, STAIR 17, STAIR 20
- Offload Areas:** TRUCK OFFLOAD 1, TRUCK OFFLOAD 2, TRUCK OFFLOAD 3, TRUCK OFFLOAD 5, TRUCK OFFLOAD 6, TRUCK OFFLOAD 7
- Other Labels:** PA, FIRE RISER, JAN, W.C., RAMP, RAMP 2, RAMP 3, RAMP 4, RAMP 5, RAMP 6, RAMP 7, RAMP 8, RAMP 9, RAMP 10, RAMP 11, RAMP 12, RAMP 13, RAMP 14, RAMP 15, RAMP 16, RAMP 17, RAMP 18, RAMP 19, RAMP 20


Callouts:

- BCS/BSA-JEA IA status for Tie in 253 complete 252 Feb 19-20**
- Pump 261-1,2,3,5,7 Start up WW 9 Bump Test 261-1,2-95 Feb 24**
- LVSS Shut down for Com cable pull Feb 20 0900-1200 Brand Roxtec Firestopping ongoing**
- Paving North Yard WW 7**
- TMWX to Roof Trestle Pressure Tests Jan 26 RE Test ongoing**
- Insulation, Labeling Feb 5 QC walk DV Feb 10**
- NH4W to Roof Trestle Pressure Tests Inner pipe Jan 23 RE Test ongoing**
- Overhead Catwalk install ongoing Feb 10-March 27**
- Chiller starts : 111-7 Feb 20. 111-6 Feb 25. (Rockwell Trane CX onsite) : March 4-11 126-3 A/B March 12-19 111-1 A/B.**
- Natural Gas to Boiler Feb.20**
- CX Natural Gas to Boiler Feb.24-27**
- Purge Lines and Charge Natural Gas To Site Feb.19**
- Natural Gas EXCLUSION ZONE**
- Revised Access**
- FUEL OFF LOADING INTEL ACCESS ONLY**
- Scaffold Removal or Modify March 6**


Table:

From	Circuit Number	To	Owner
3C11 E03-DNS023	5	LC23-FLT114-1-60	@Cooney_ZacaryX
3C11 E03-DNS023	6	LC23-FLT114-4-60	@Cooney_ZacaryX
3C11 E03-DNS023	18	LC23-VFD114-16-60	@Cooney_ZacaryX


CUB 1 Exterior Pre-Punch Status

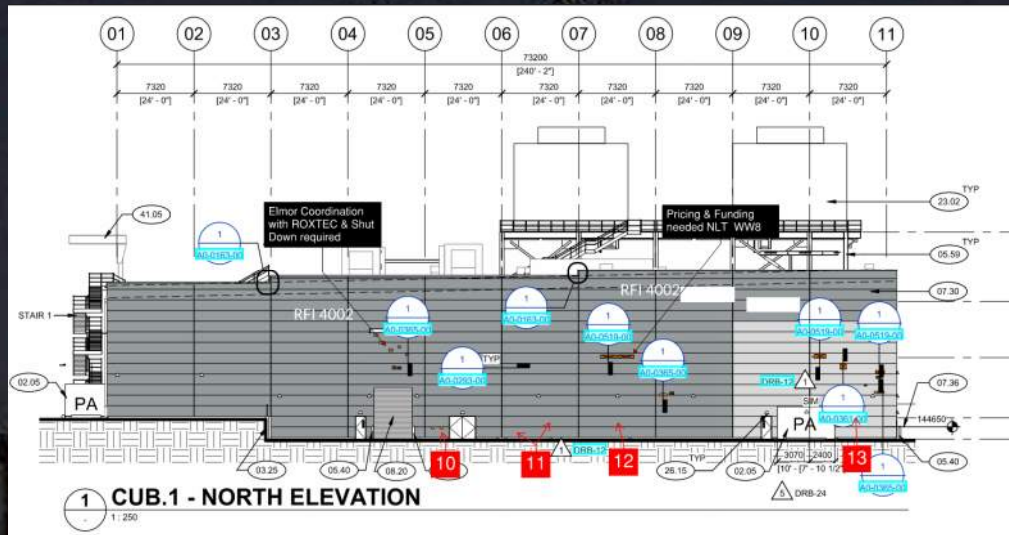


1. North Elevation ROXTEC Electrical in Coordination with Elmor WW 9
2. West Elevation pending UN2 tie in, Blank out Conditioned water to CUB 2
3. Set Final Man door complete Access Controls March 6- 20
4. Light Fixtures ongoing West El.

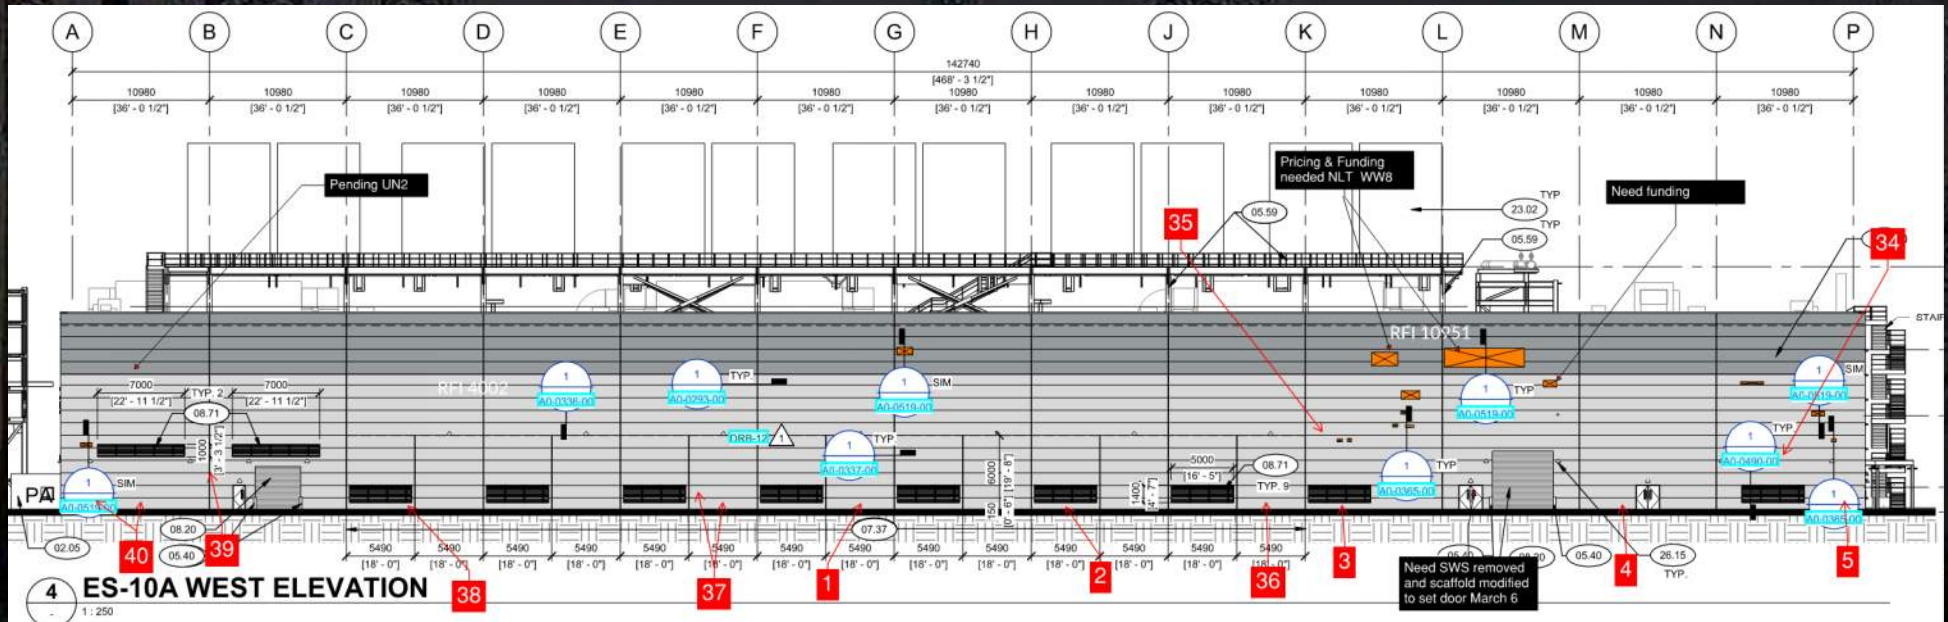

CUB 1 – EXTERIOR/ROOF

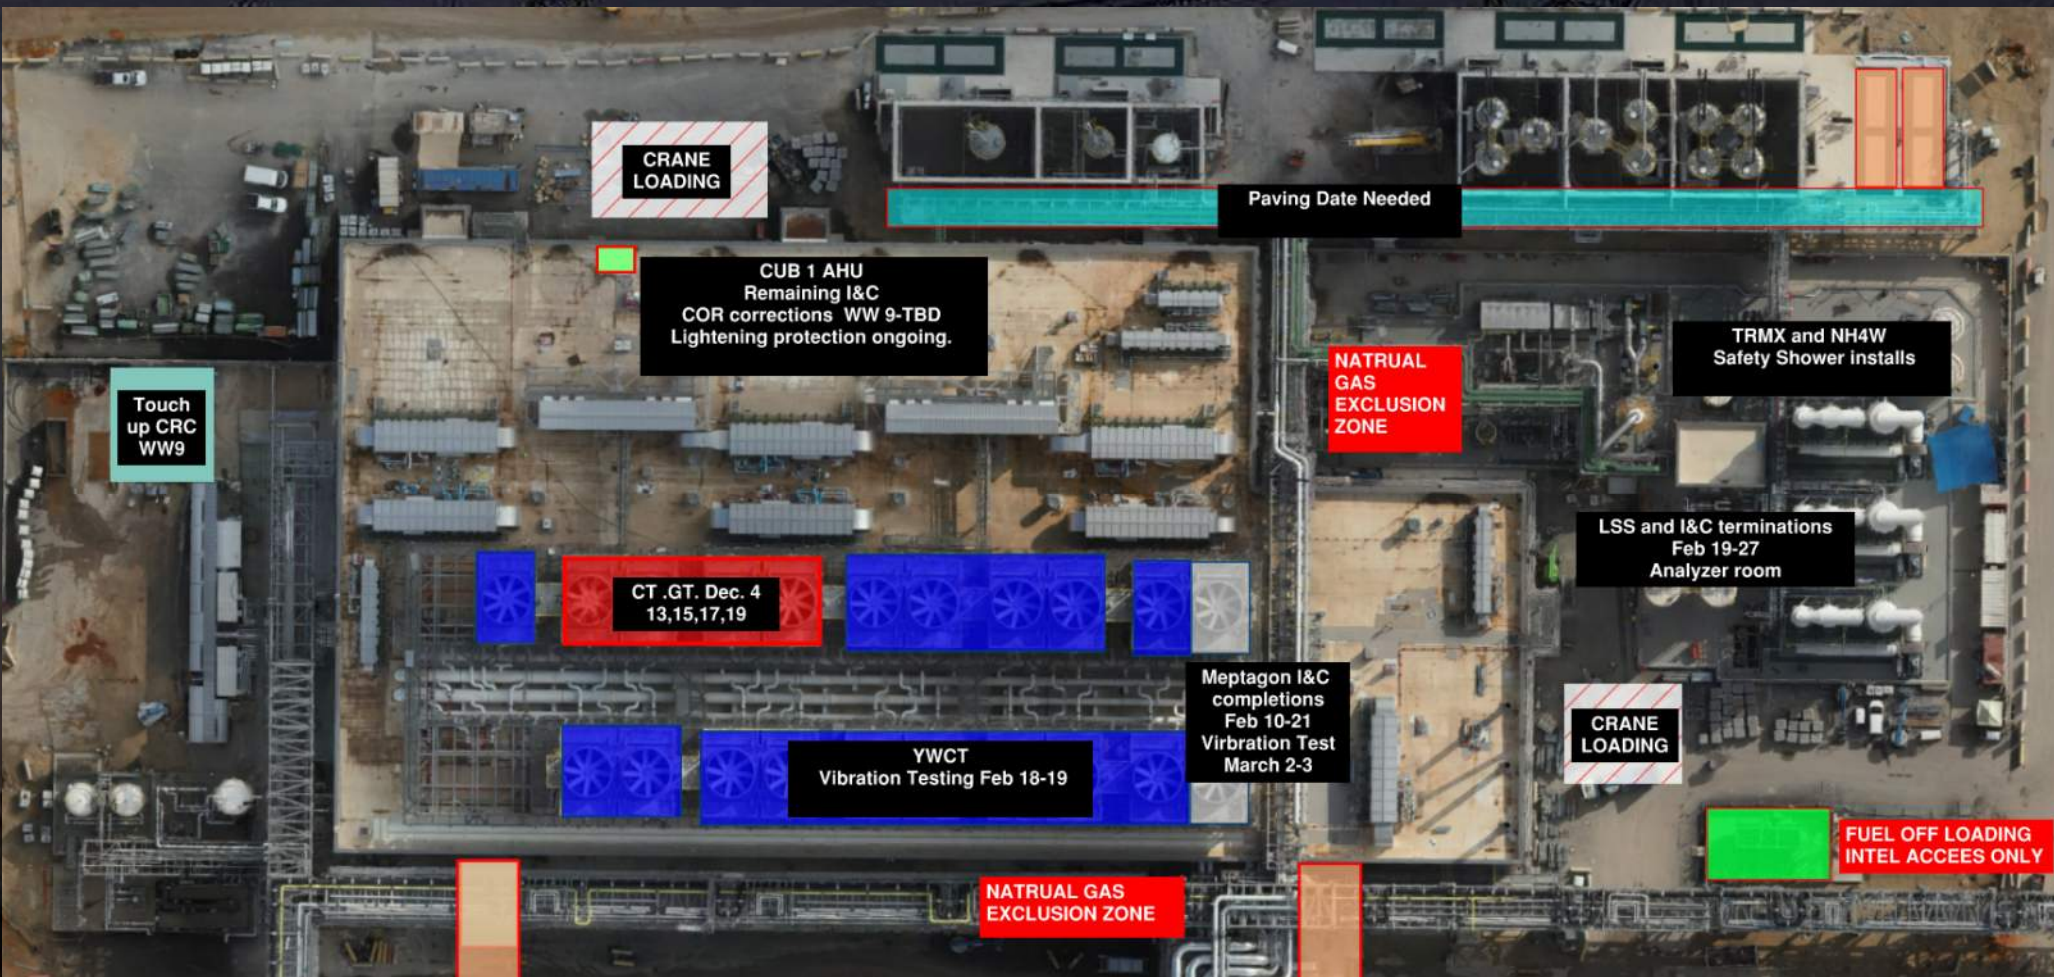

CUB 2- Load in ,H&T, Framing and Sheetrock

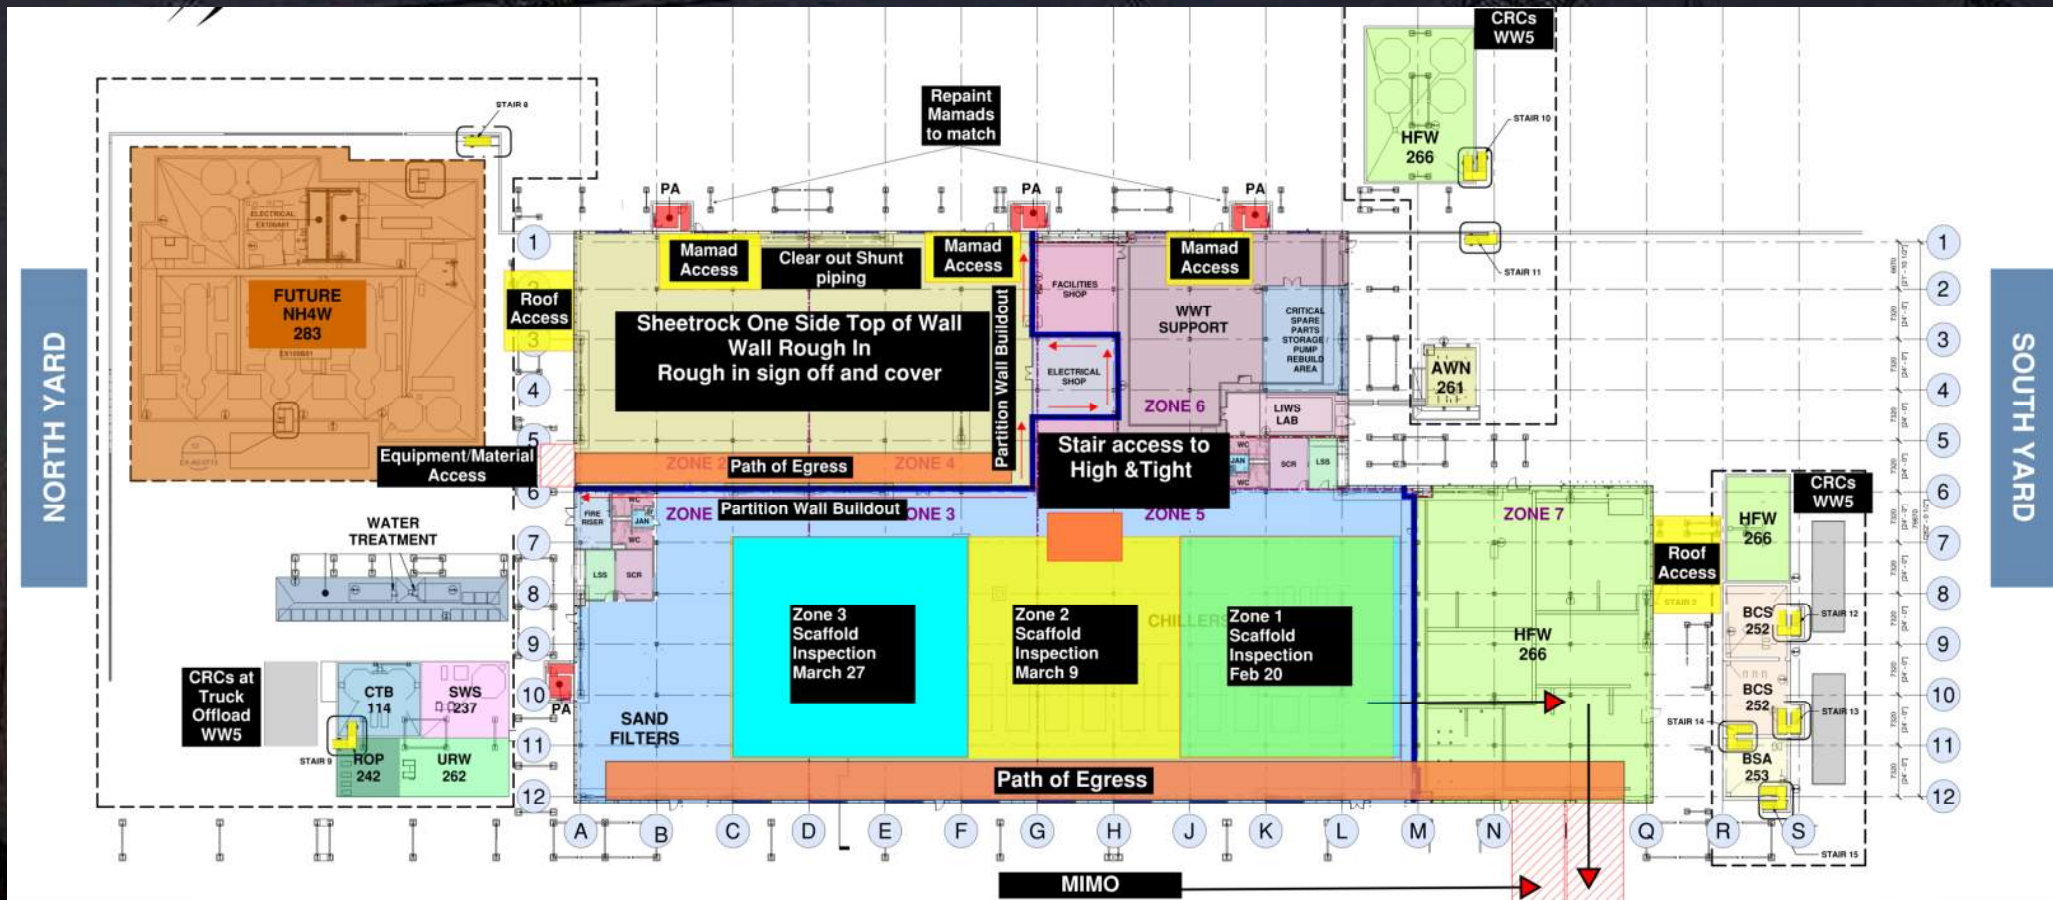


CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY



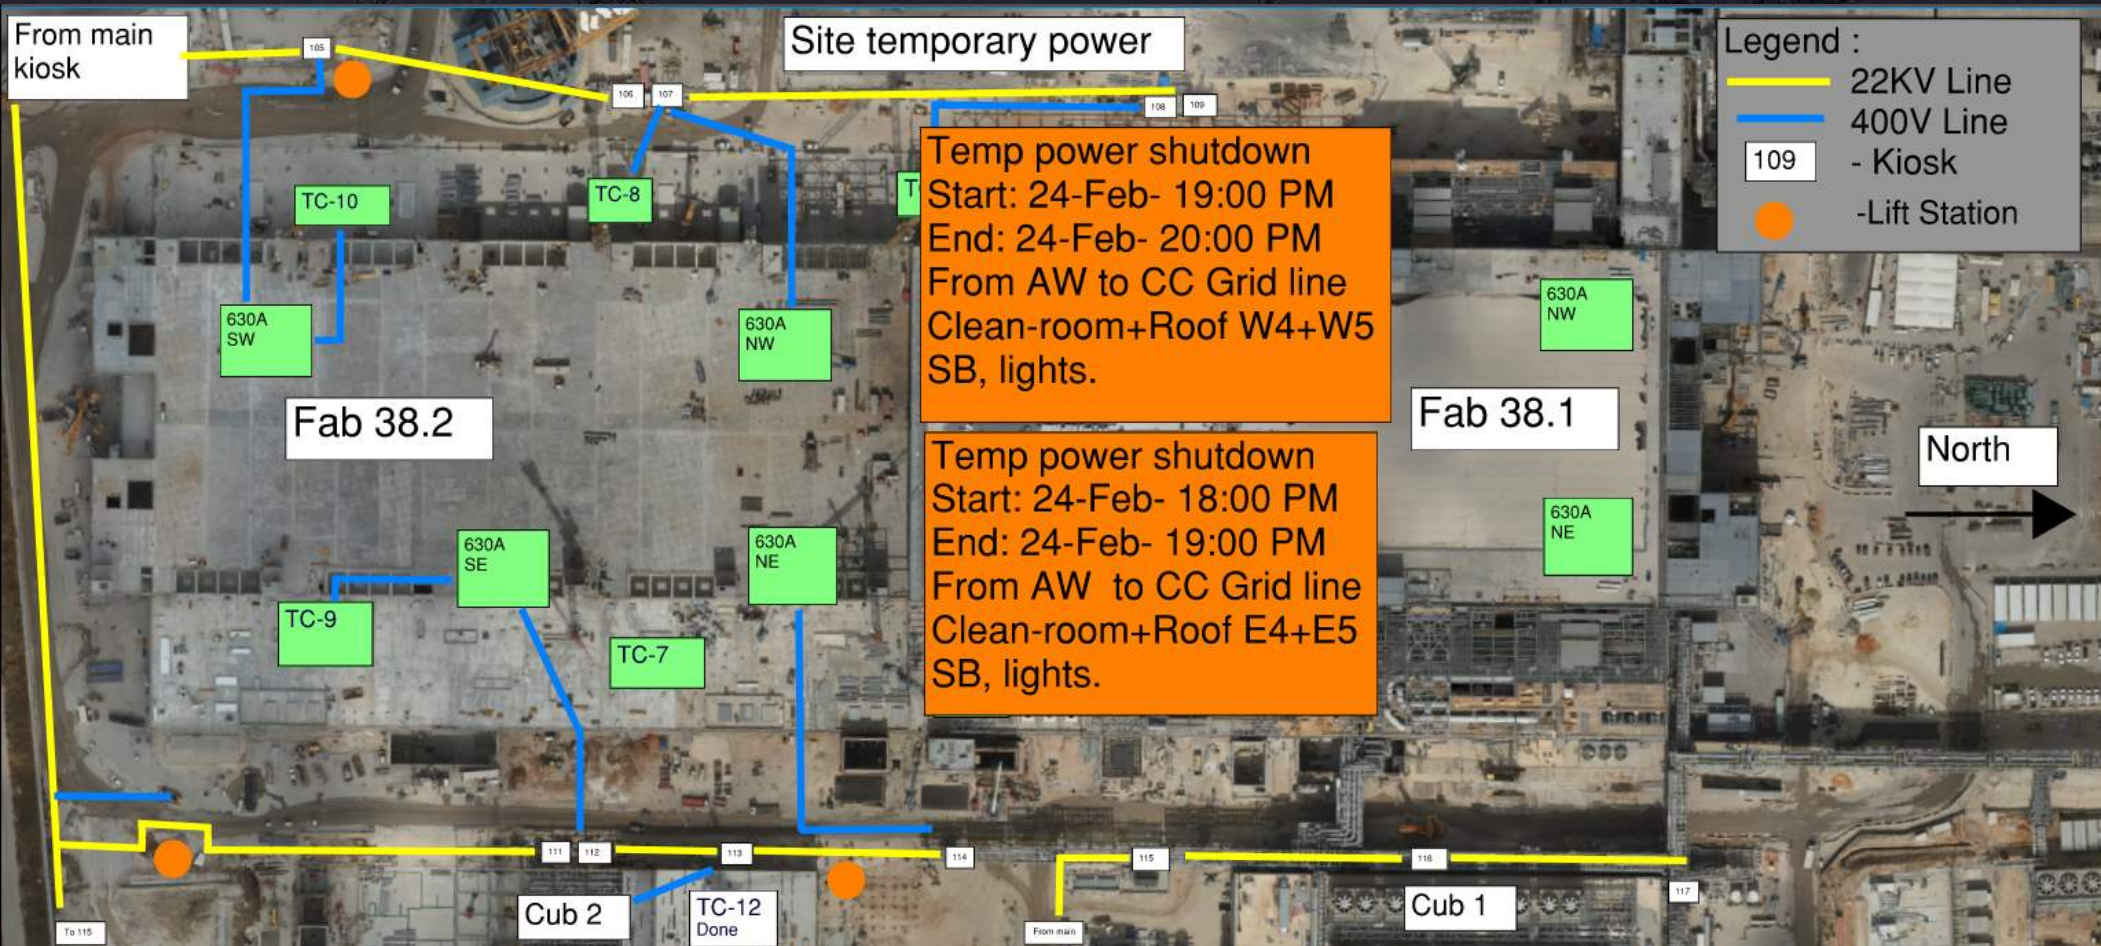




Daily Coordination Meeting

Site Logistics


North

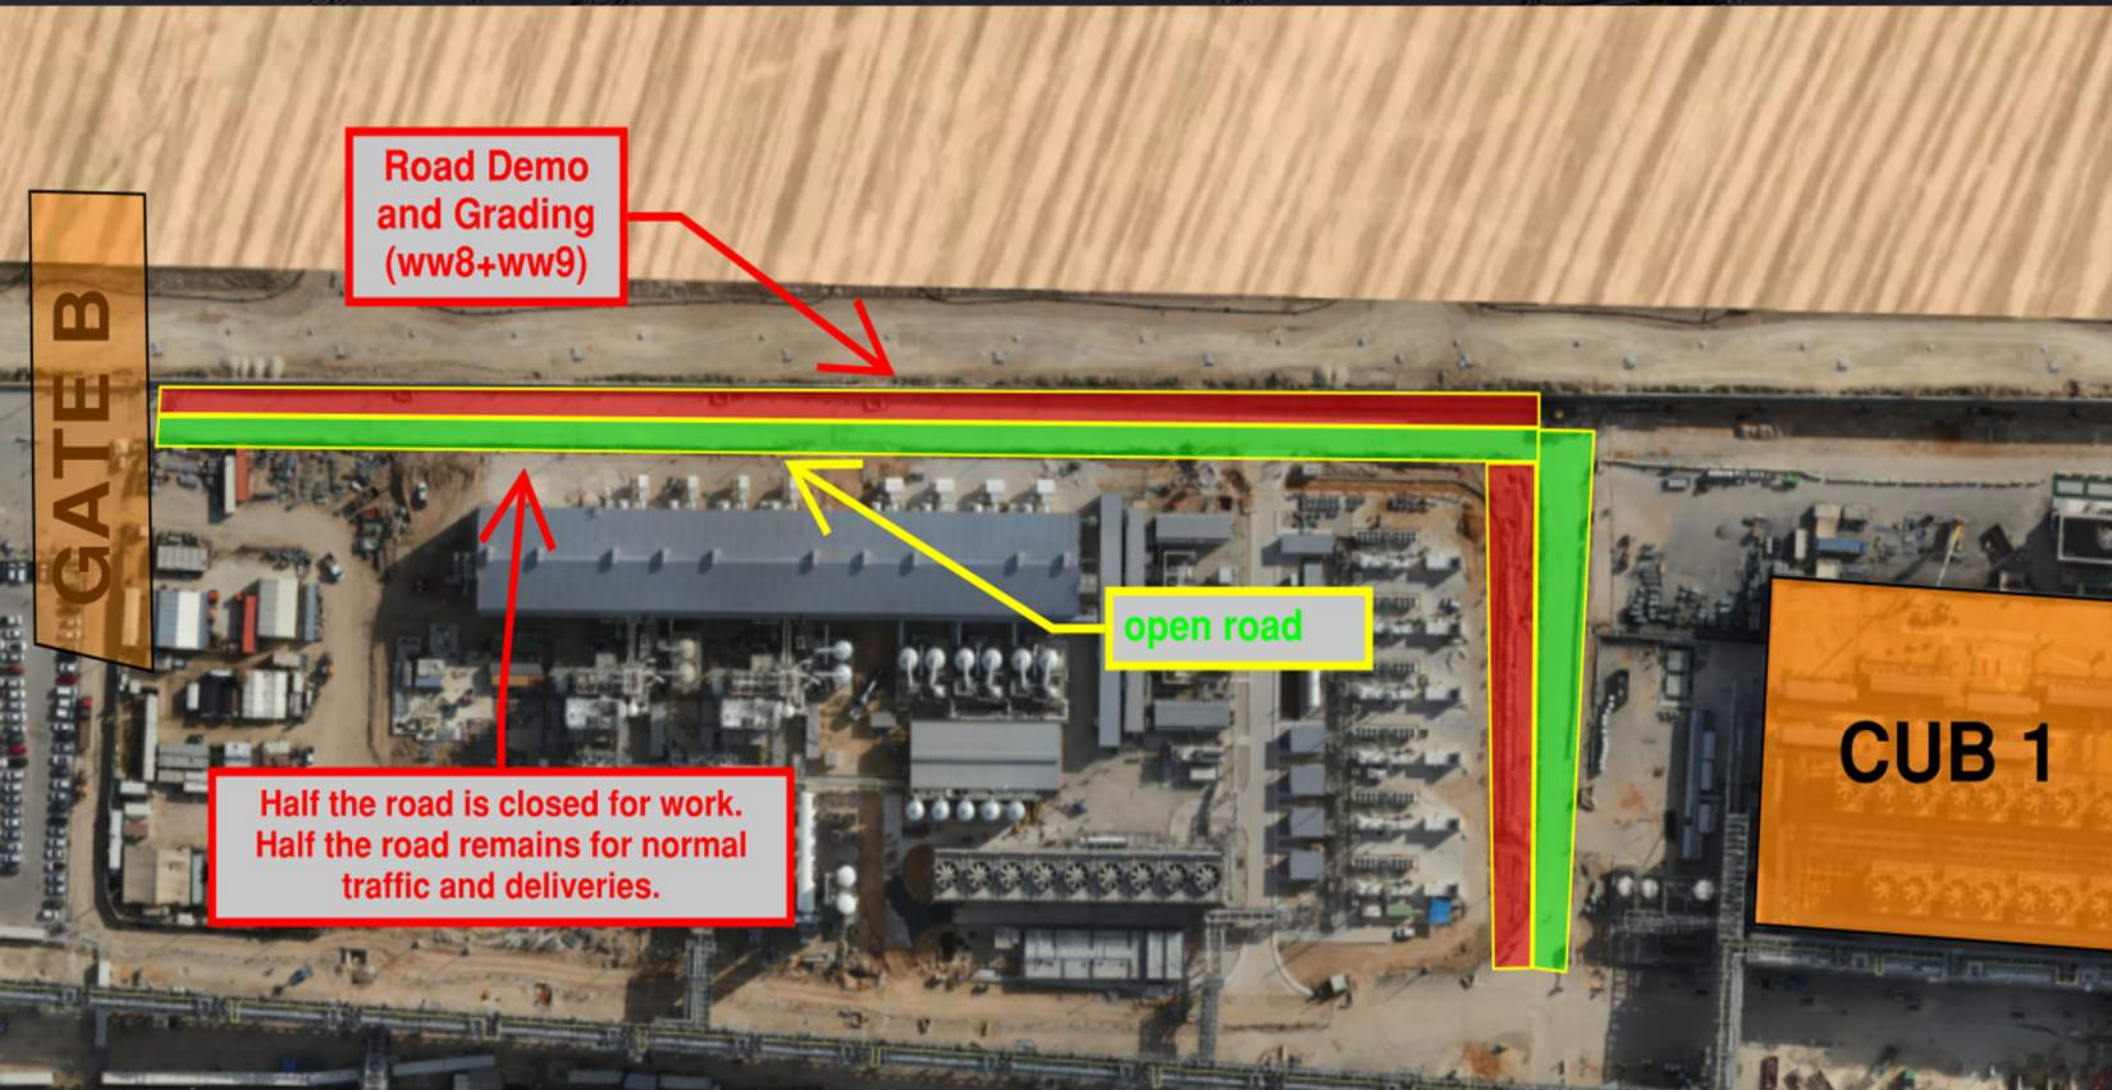



Daily Coordination Meeting

Site Logistics North

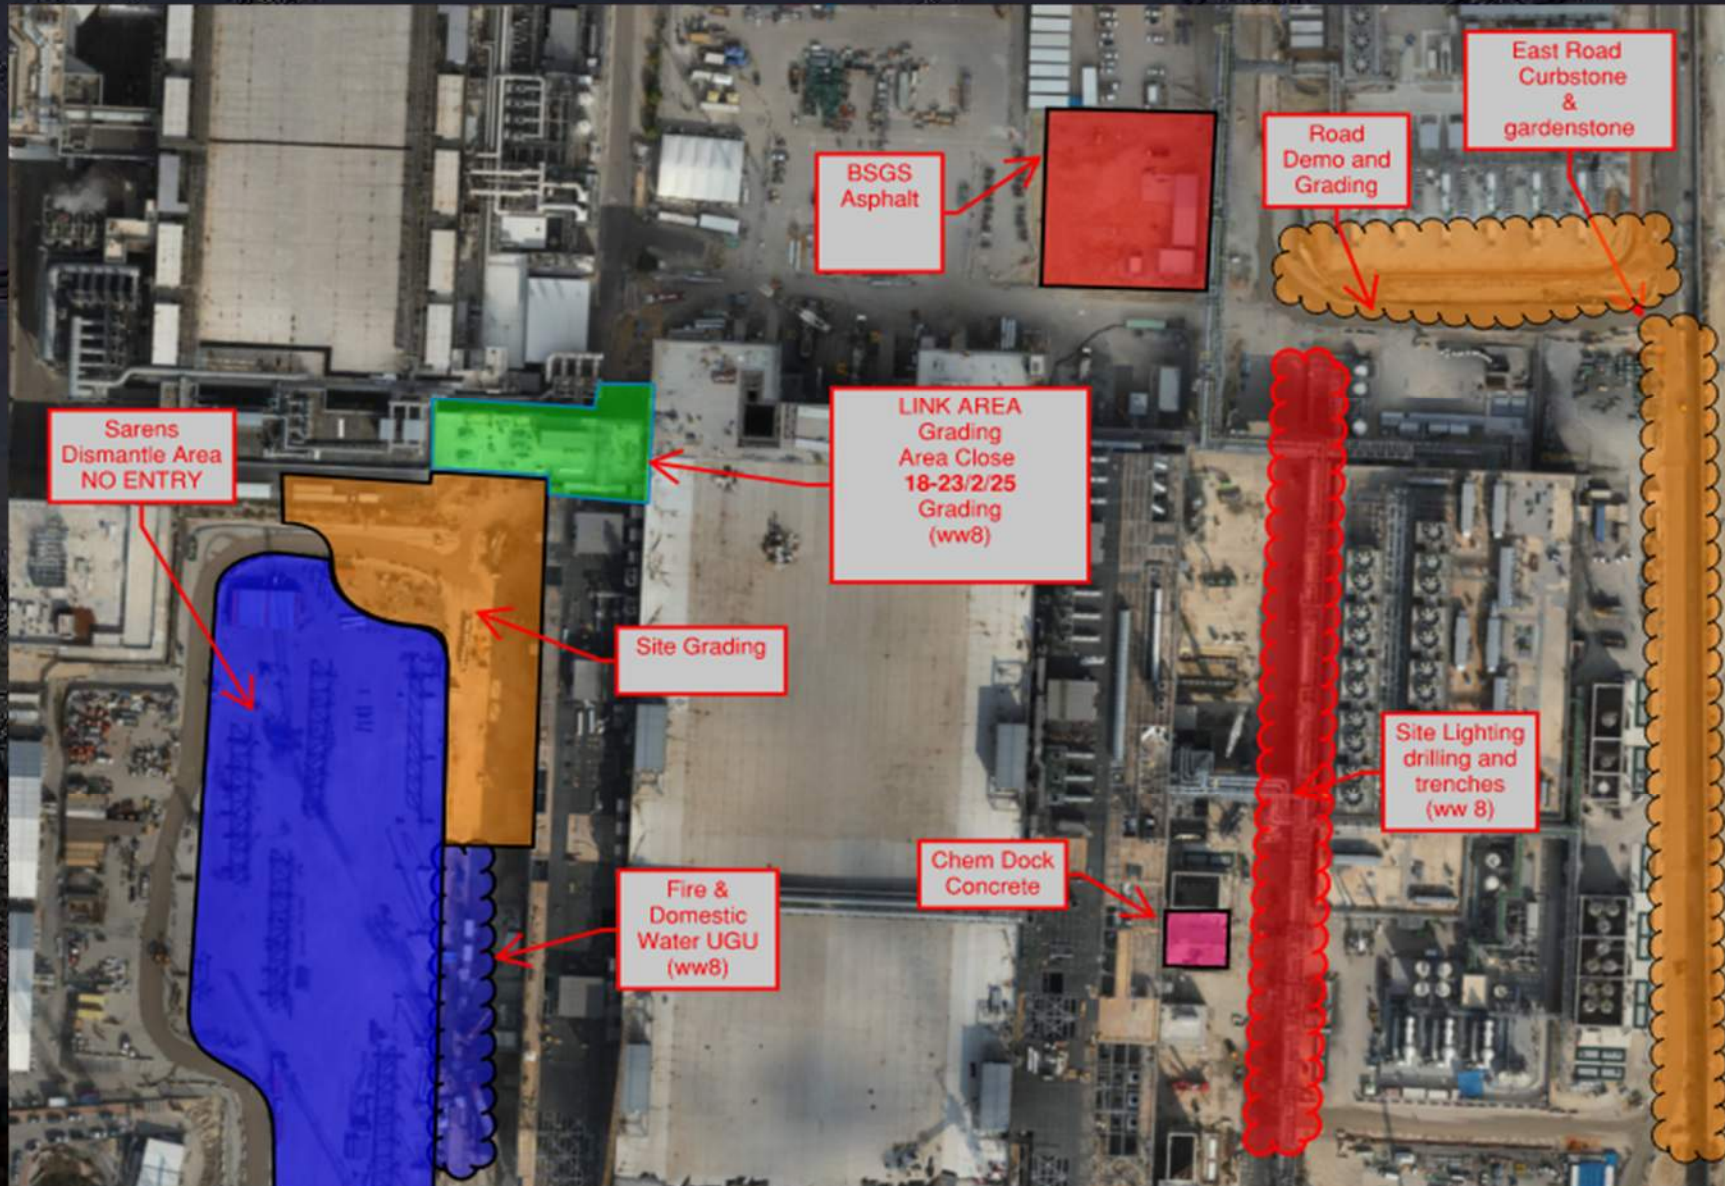




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South

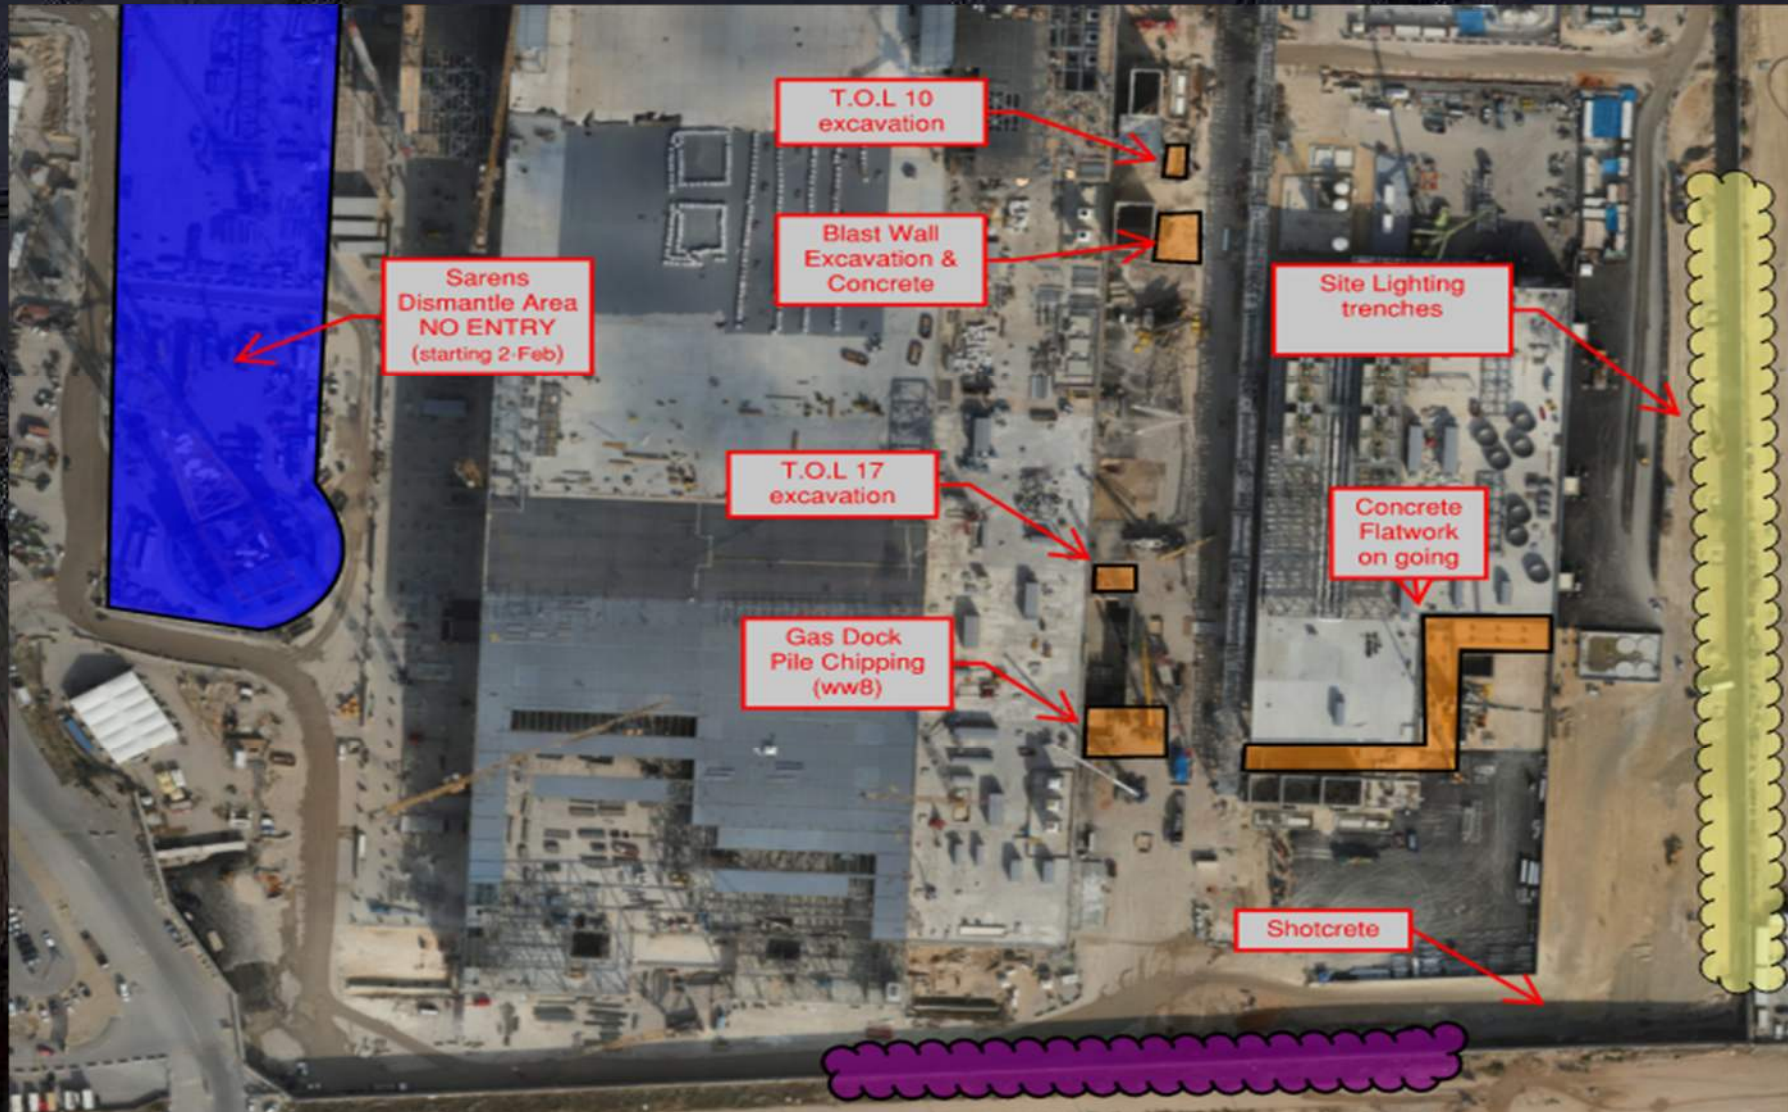



Report of Thefts

As everyone knows, if something has been stolen or broken into, please report it immediately to *3911 when you identify the case, as the sooner you report it, the higher the chances of figuring out what happened.

Additionally, this is a reminder to make sure that all your tools and equipment are marked on an organized list, including purchase receipts, as this makes it easier to identify stolen items.

If you already have a list and are keeping track, that's great. If not, it might be a good idea to start creating one.

HCC/EHS Weekend Work- 21.02.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Standefer - 052-3440752

Soly Nir - 052-3126049

Asher Amar - 052-8801316

CSA CM

Nick Dailey - 052-3308928

Nissim A

Leonid Khomich - 053-2722138

Andy Jollands - 052-9659290

Hillel Mashiah - 052-6175084

Kenny C

David S

MEP

Cx

Cranes

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 21.02.2025

FAB

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- Pach Taas
 - Wall Penetration
 - Valiry: 0528762468
- Afcon E
 - E,W MARSes
 - Avi Eli: 0526008487
- Lesico
 - SF East Mechanical Shaft
 - Elia 0543369795

Clean Room

- Talad – 30 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Elad 0546654473)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Roni 0542496363, Eden 0585335445)
- Talent solution 14 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Super Musat 0505135022)
- Sig – 19 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Codrin 0546594273, EHS Ovidiu 0546993648)
- Afcon – 10 guys CR – Cable tags, INT Cable puling , cable tags (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Subcontractor Weekend Work- 21.02.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/SSS Building
- Foreman – Chaim – 054-5210133
- Safety – Marzuke – 054-447-7112
- Lesico – H2 Vent/SUT East Area Way Rack
- Foreman – Suju Pally – 052-7755967
- Safety – Tal Madar – 052-8229109
- Combe UPW – BCD/UPW Rooms
- Foreman – Boris – 054-8346412
- Safety – Shimon – 054-5348843
- SK Engineering – 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- SK Engineering – 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- Carmel Bidud Duct – Spec Gas, BCD, and 2P Roof
- Foreman –
- Safety –
- SNJ –
- Foreman –
- Safety –

WJG

Afcon:

Team leader – Montu: 0559116973

Safety – Steven: 0559129333

Pach Taas:

Team leader – Valery: 0528762468

Safety – Ofek: 0507838486

Chemo:

Team leader – Maor: 0509889071

Safety – Rotem: 0544477112

Subcontractor Weekend Work- 21.02.2025

CUB

Meptagon CUB 1:

Sergey - 0537981592

Itzik - 0587441140

Chemo Aharon CUB 1:

Dudu - 050-9808846

Leonid - 0548883878

HSAI CUBs:

Sergey - 0552728807

Haim - 054-8038554

SKE CUB 2:

Mario - 0548991051

Marzuk - 0548830263

D&P CUBs:

Constantino - 0545501602

David - 0548894447

Trestle

Site

Daily Coordination Meeting



14:00 Sign In
