

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- Jobsite closed Friday 27 December




UTILITY LEVEL LOGISTICS

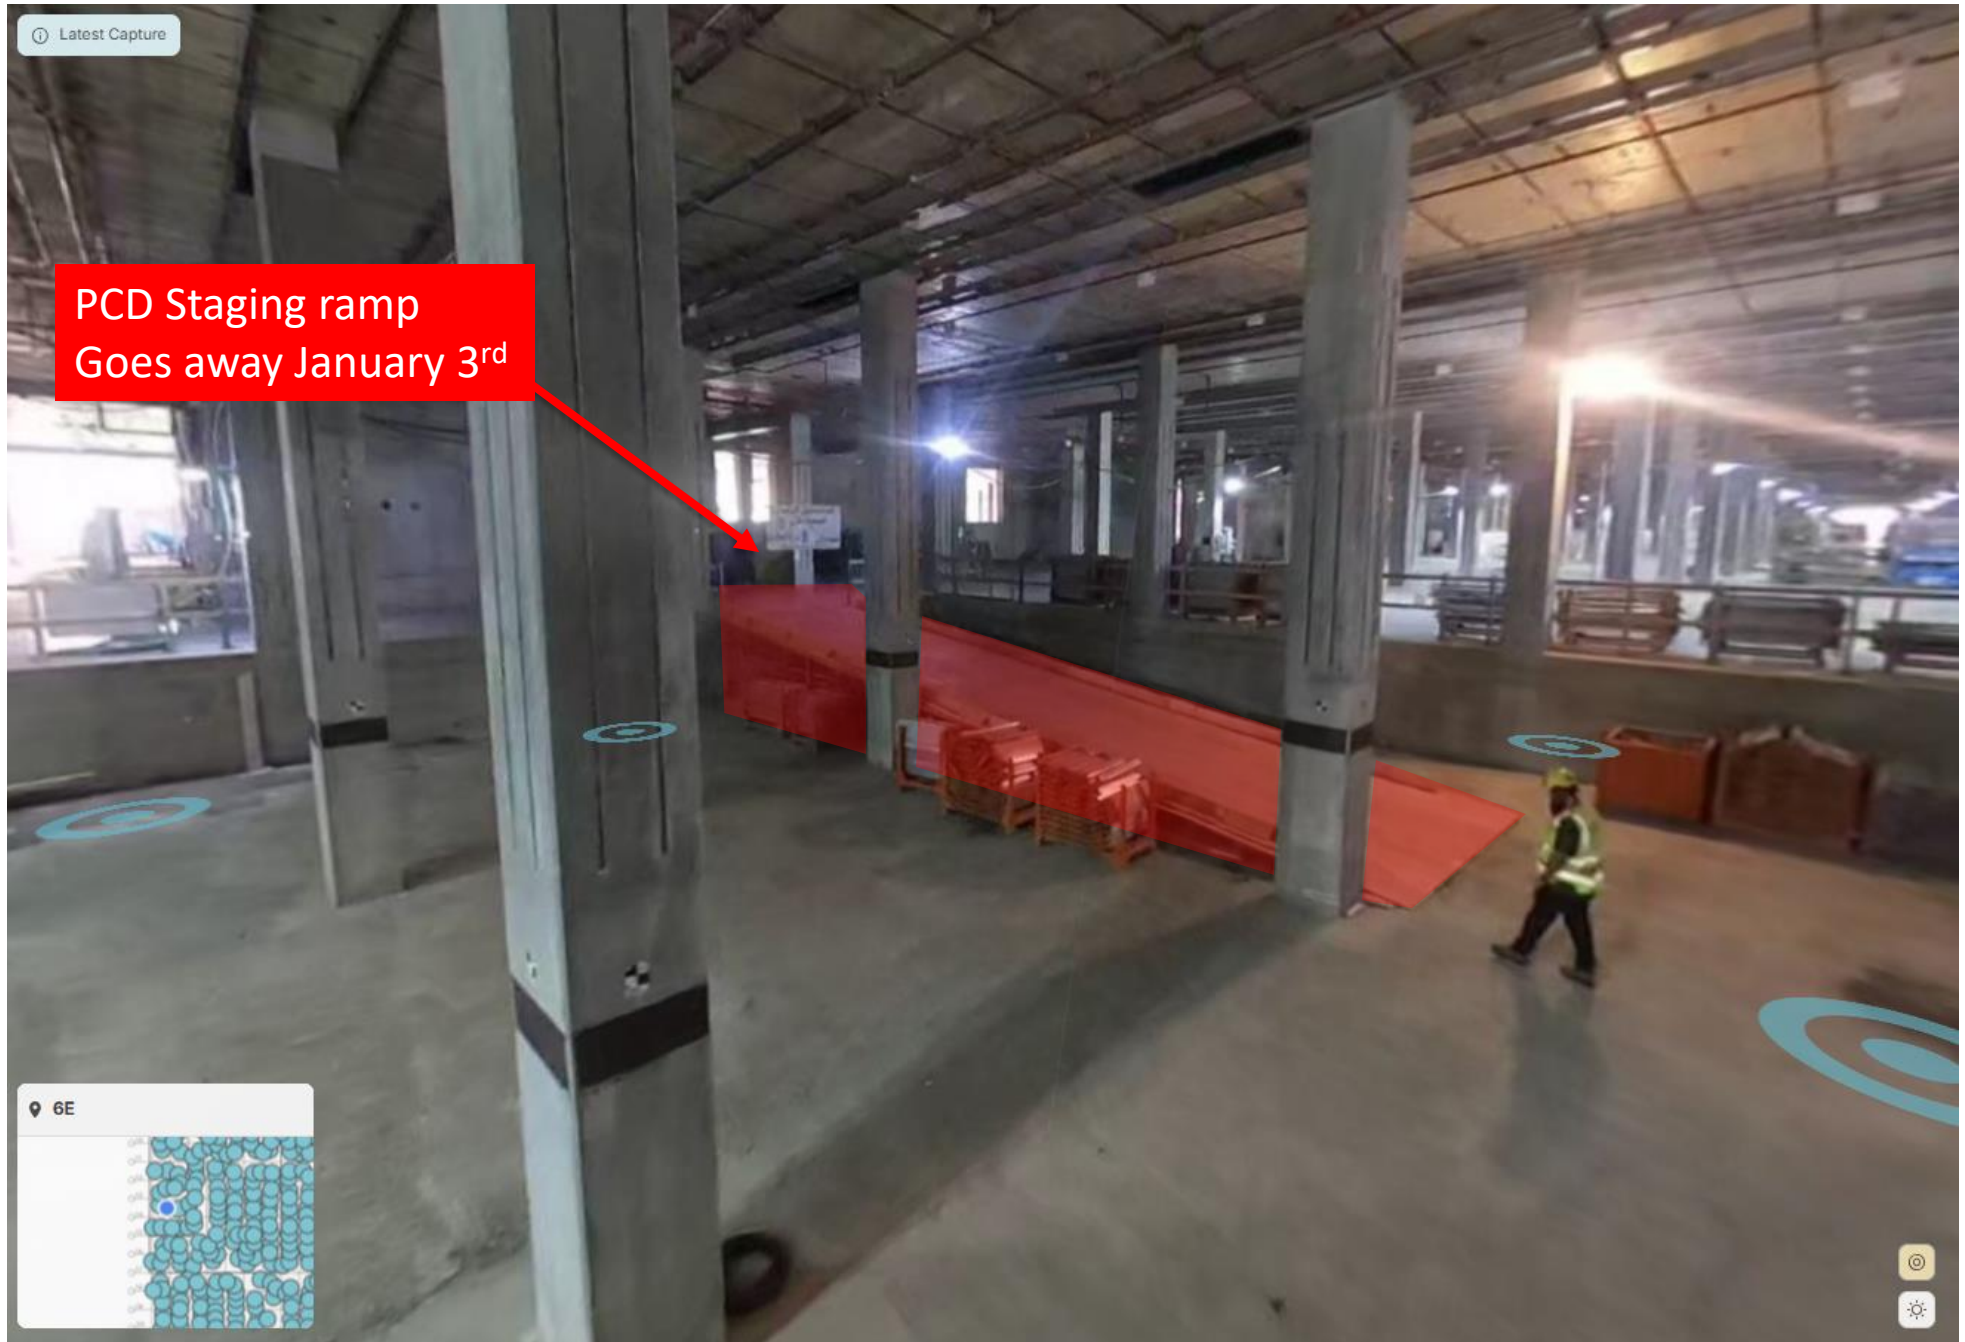




UTILITY LEVEL LOGISTICS

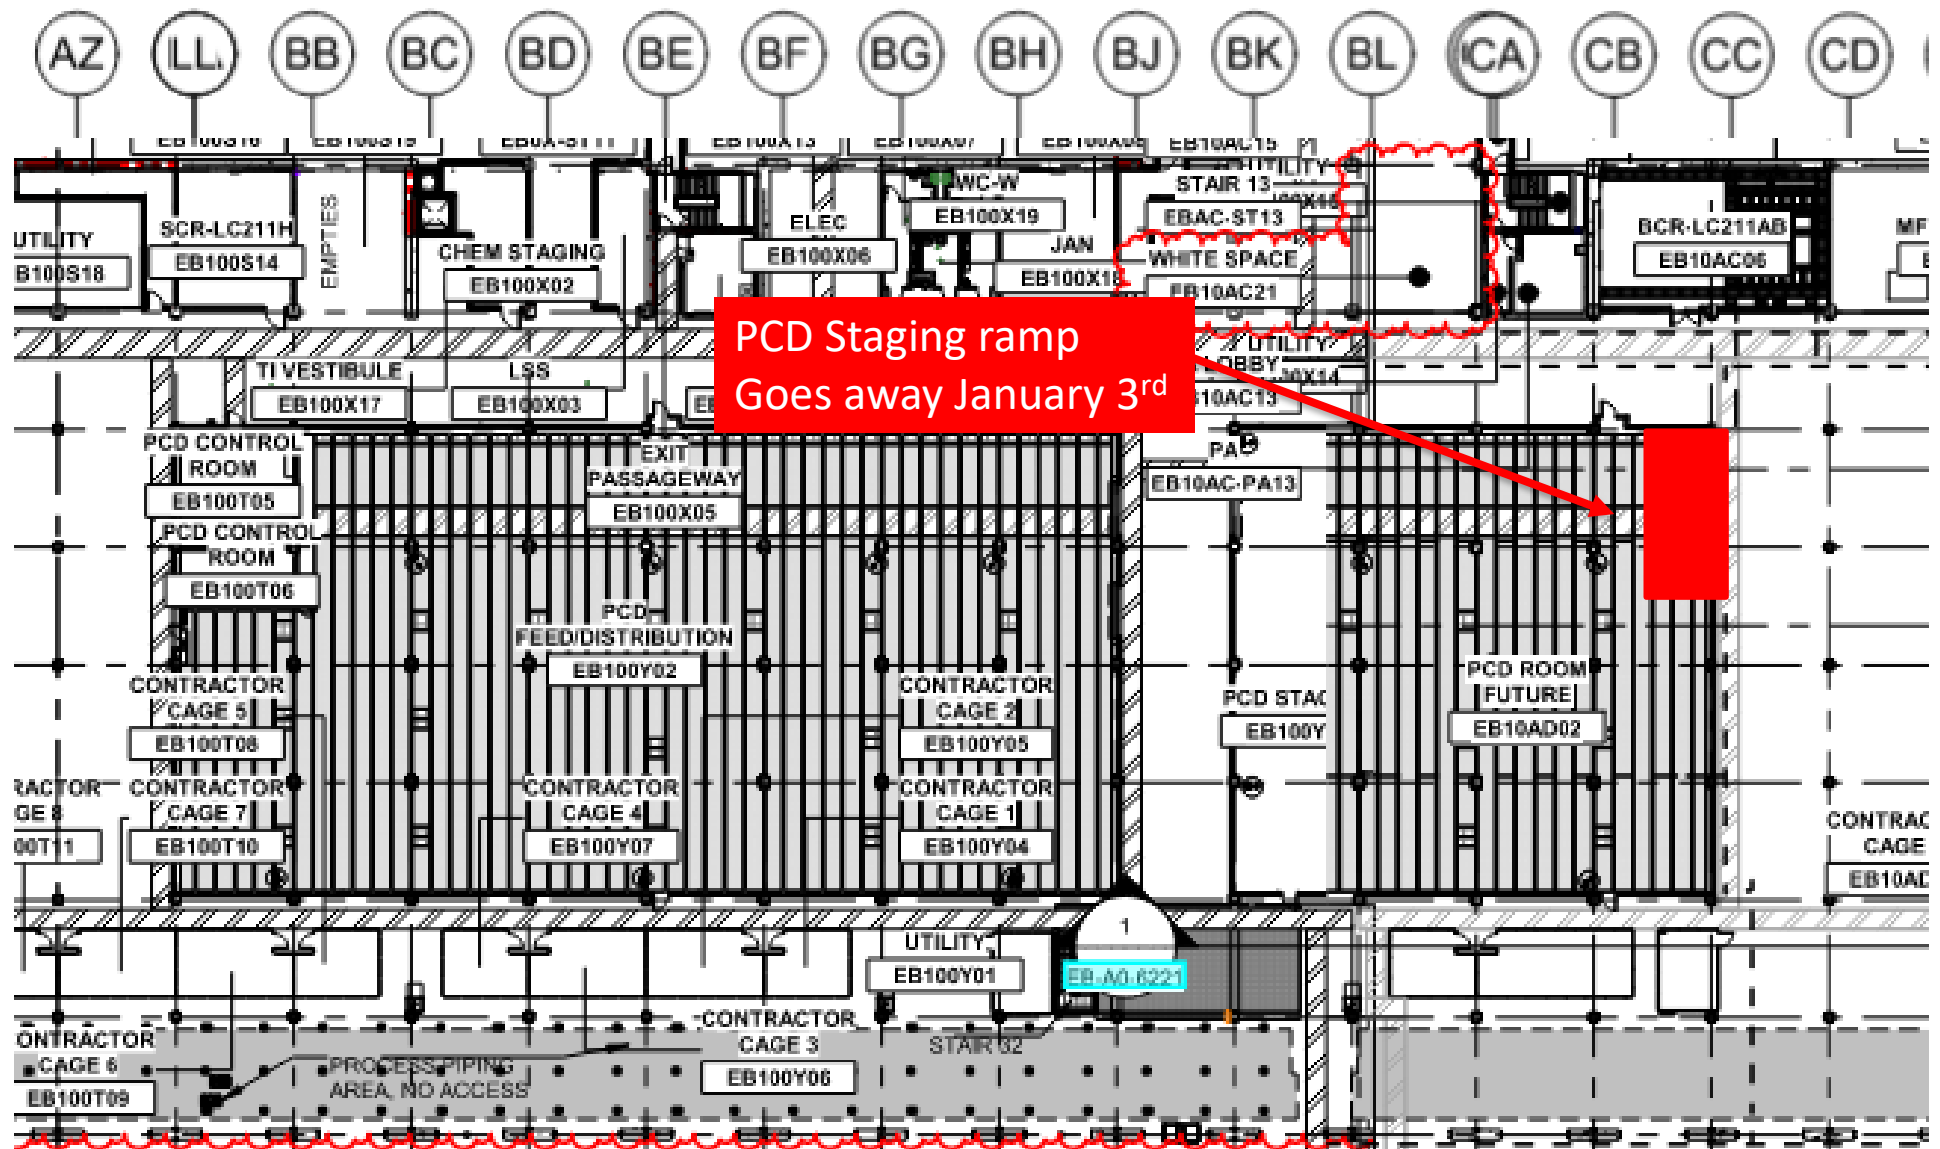



UTILITY LEVEL MOD1

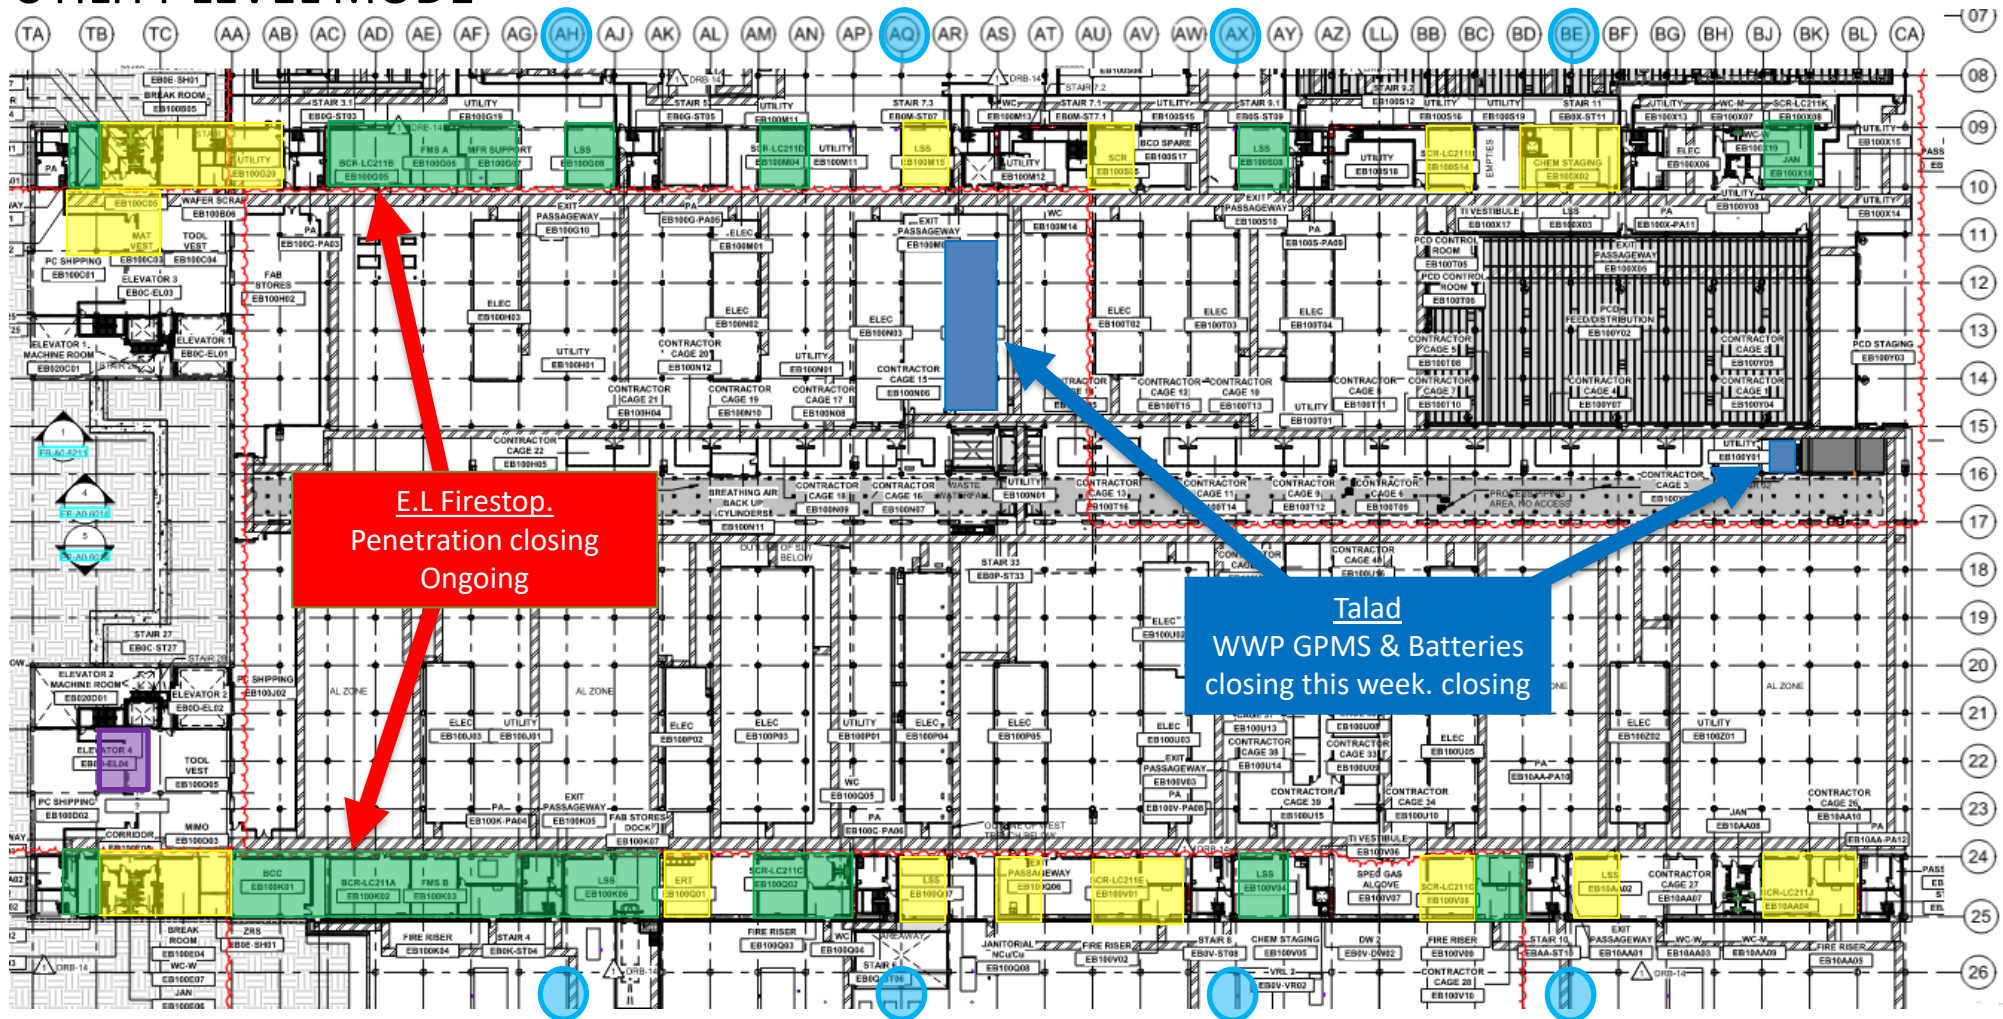

**E.L Firestop.
Penetration closing
Ongoing**

**Talak
WWP GPMS & Batteries
closing this week. closing**

BELFOR
Mold remediation

ELRAM
Drywall install

MEP+Electrical
Ready for re-install




MALHIMIM
9E 9W & 8W
Ongoing

MALHIMIM
9E 9W & 8W
Ongoing
Need completion date




SUT 38.1 LEVEL

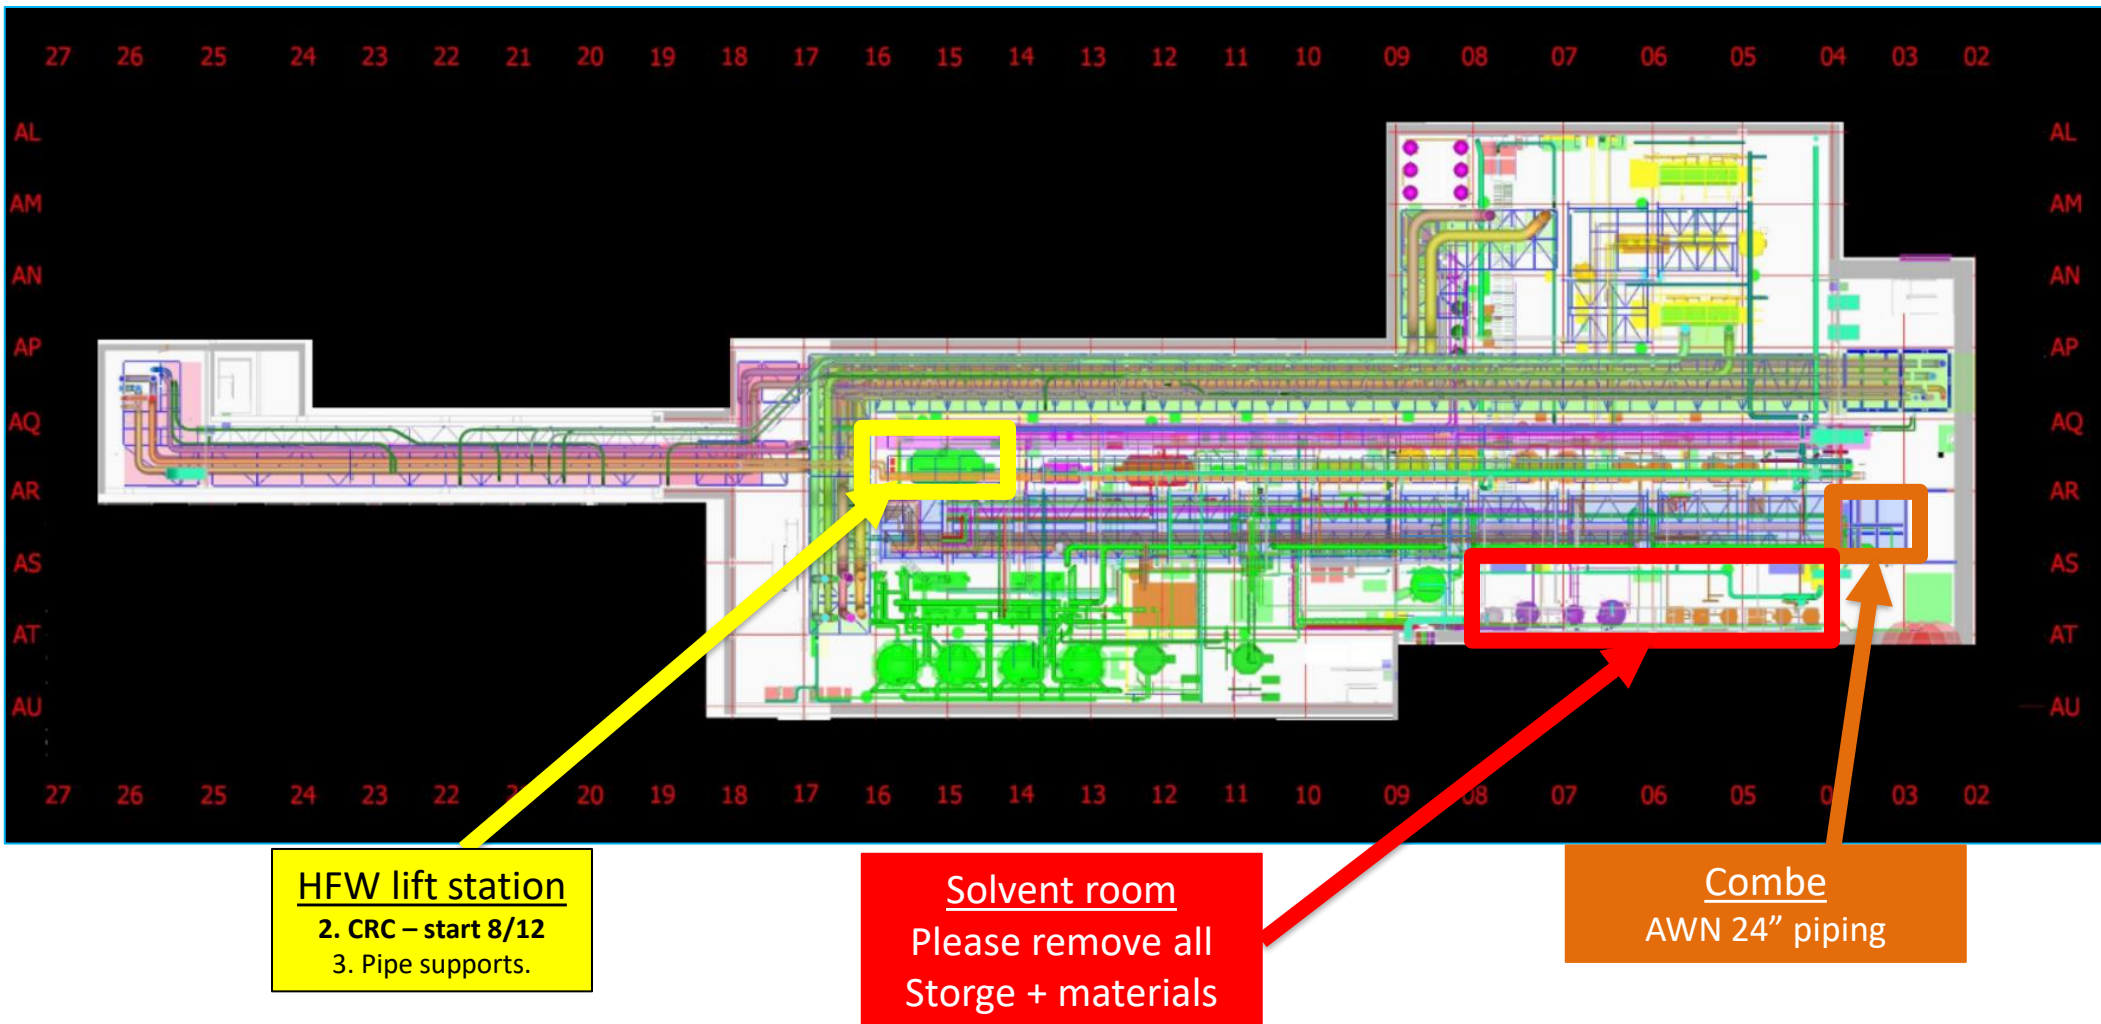


SUT 38.2 LEVEL

Rack 4b
Lifting
#1-08/12v
#2-11/12
#3-16/12

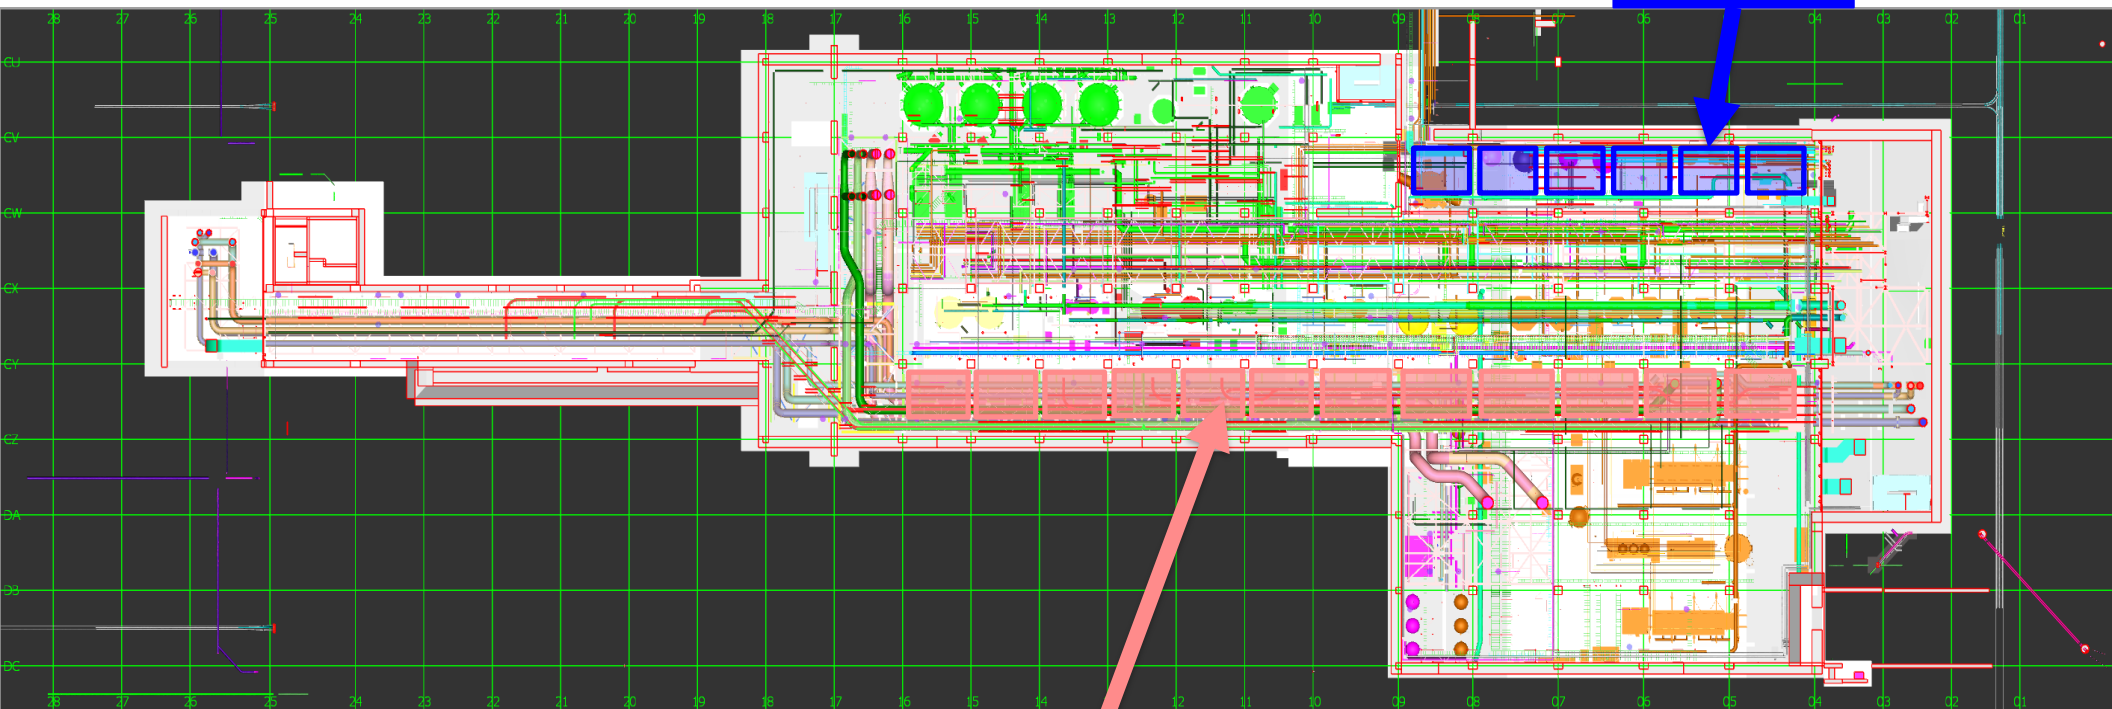


Rack 2
MIMO -
Module #5
12th of Dec


SUBFAB BUILDOUT MOD 1

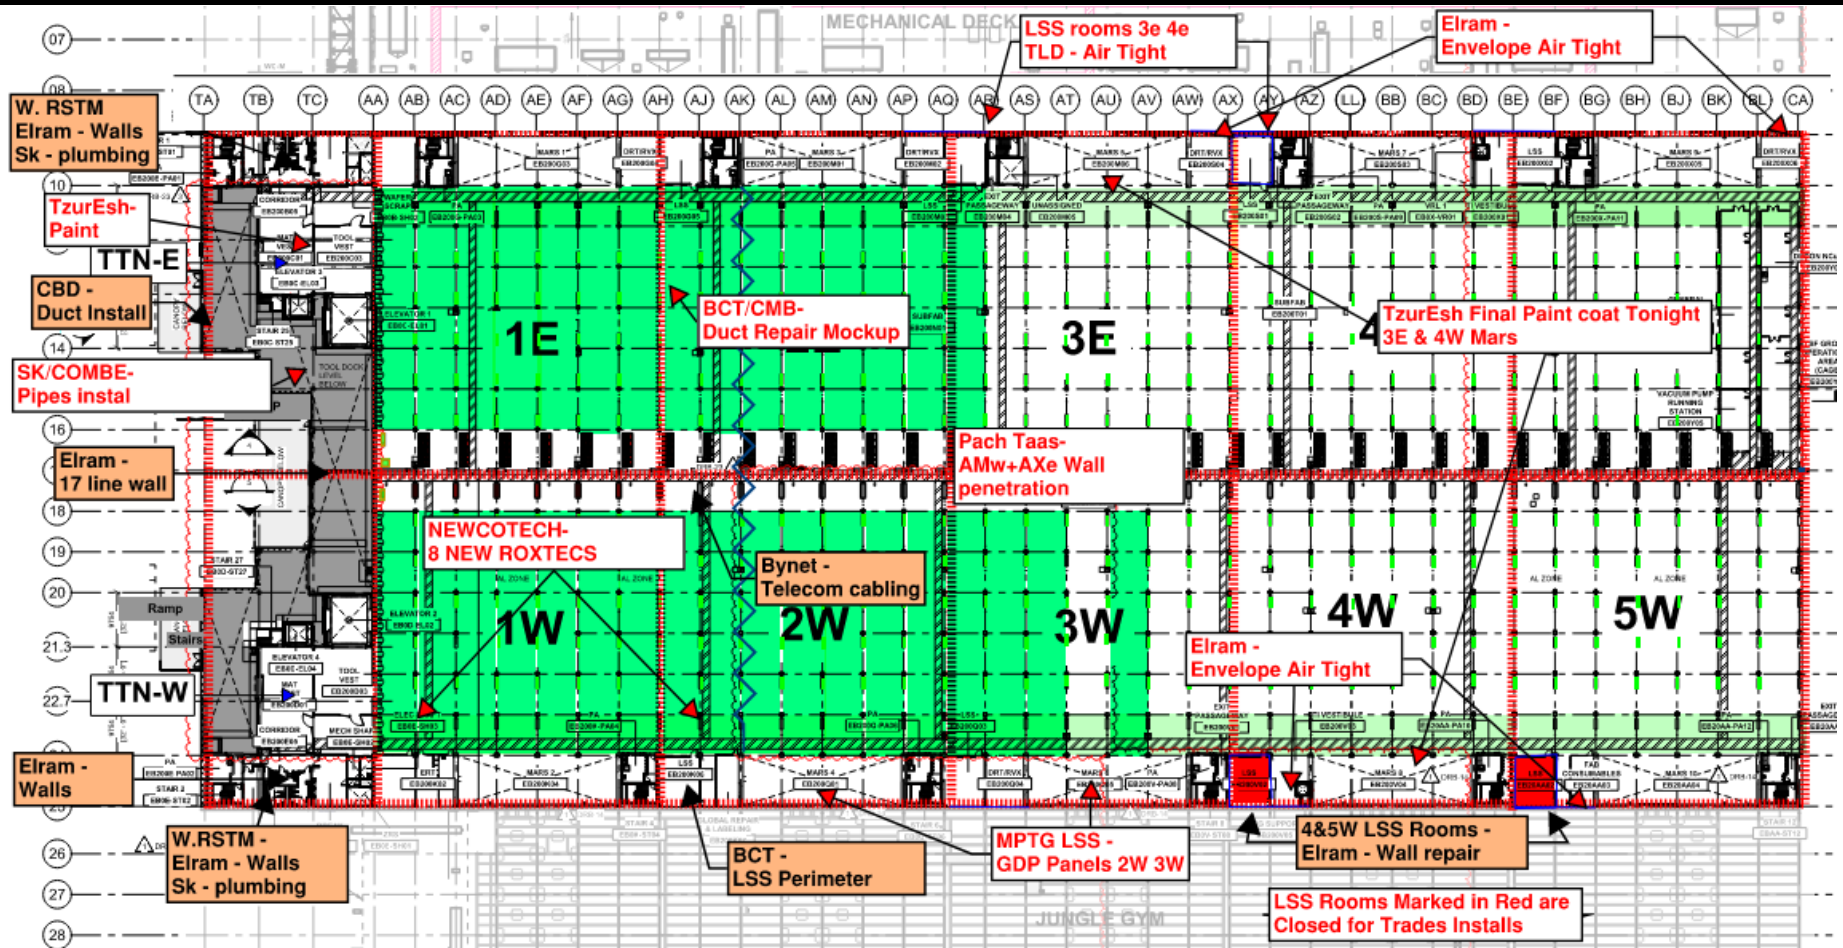


SUBFAB CRC TOPCOAT

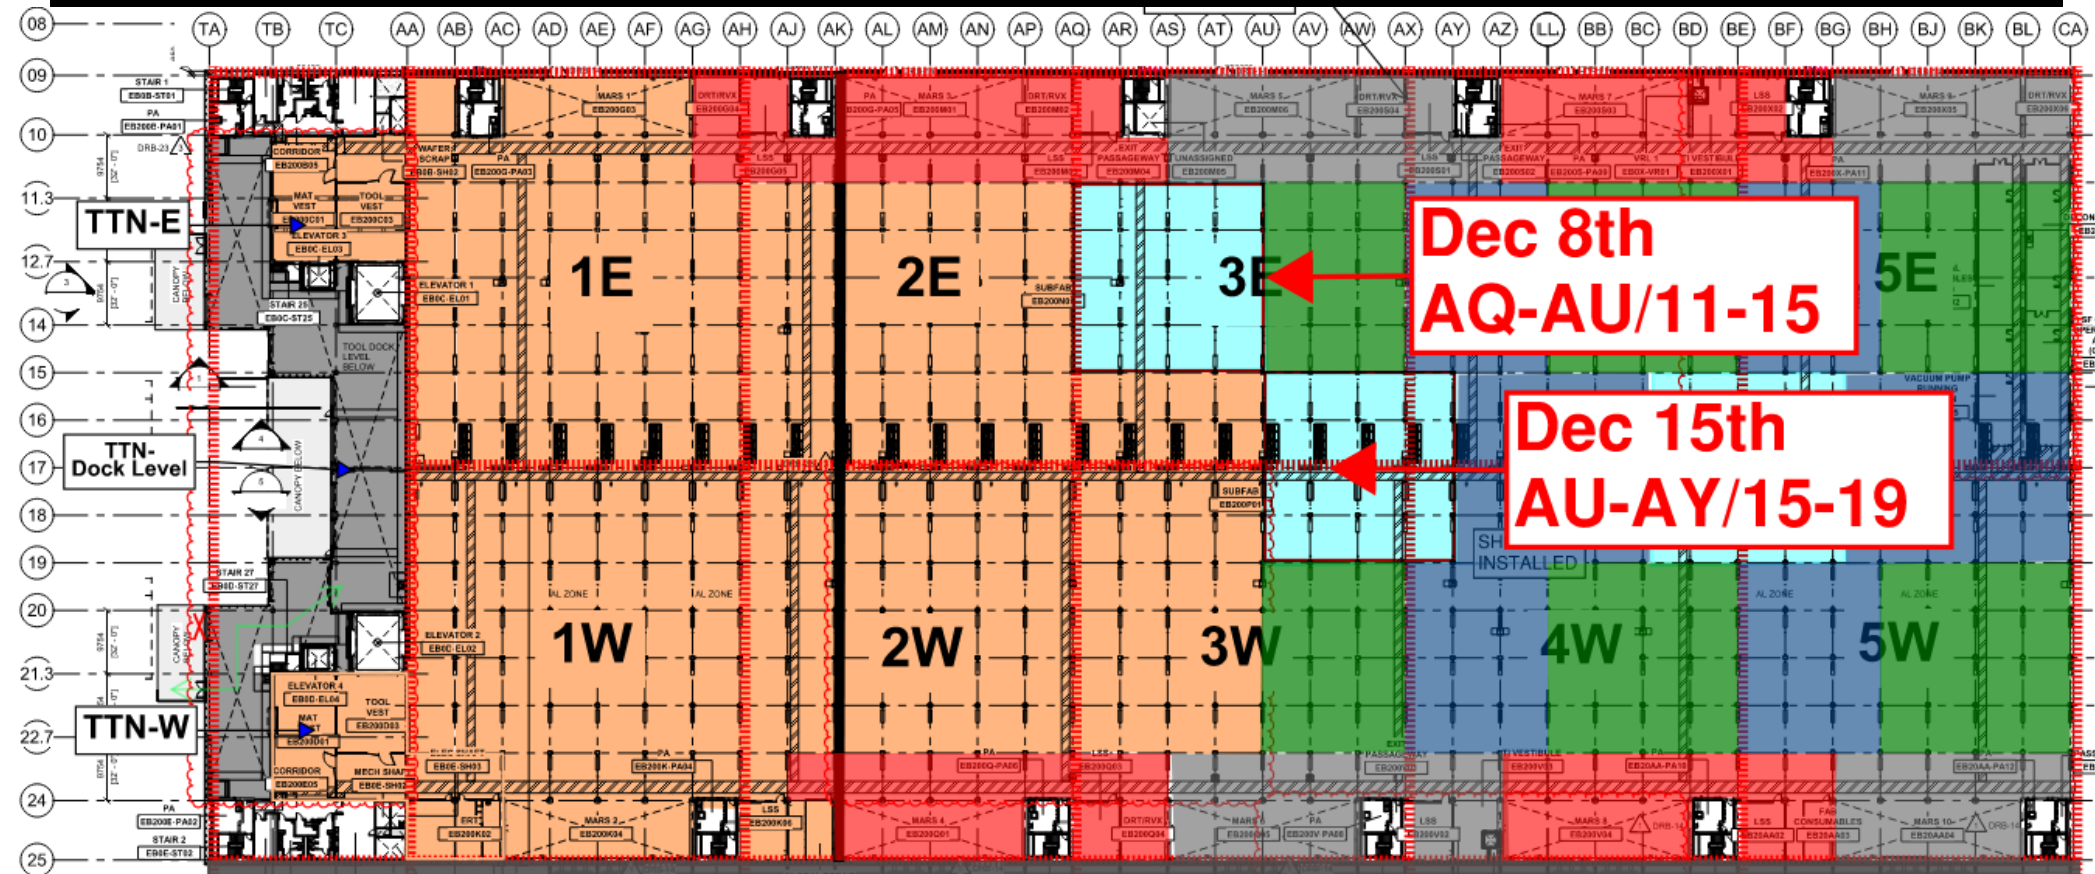



SUBFAB BUILDOUT MOD 2


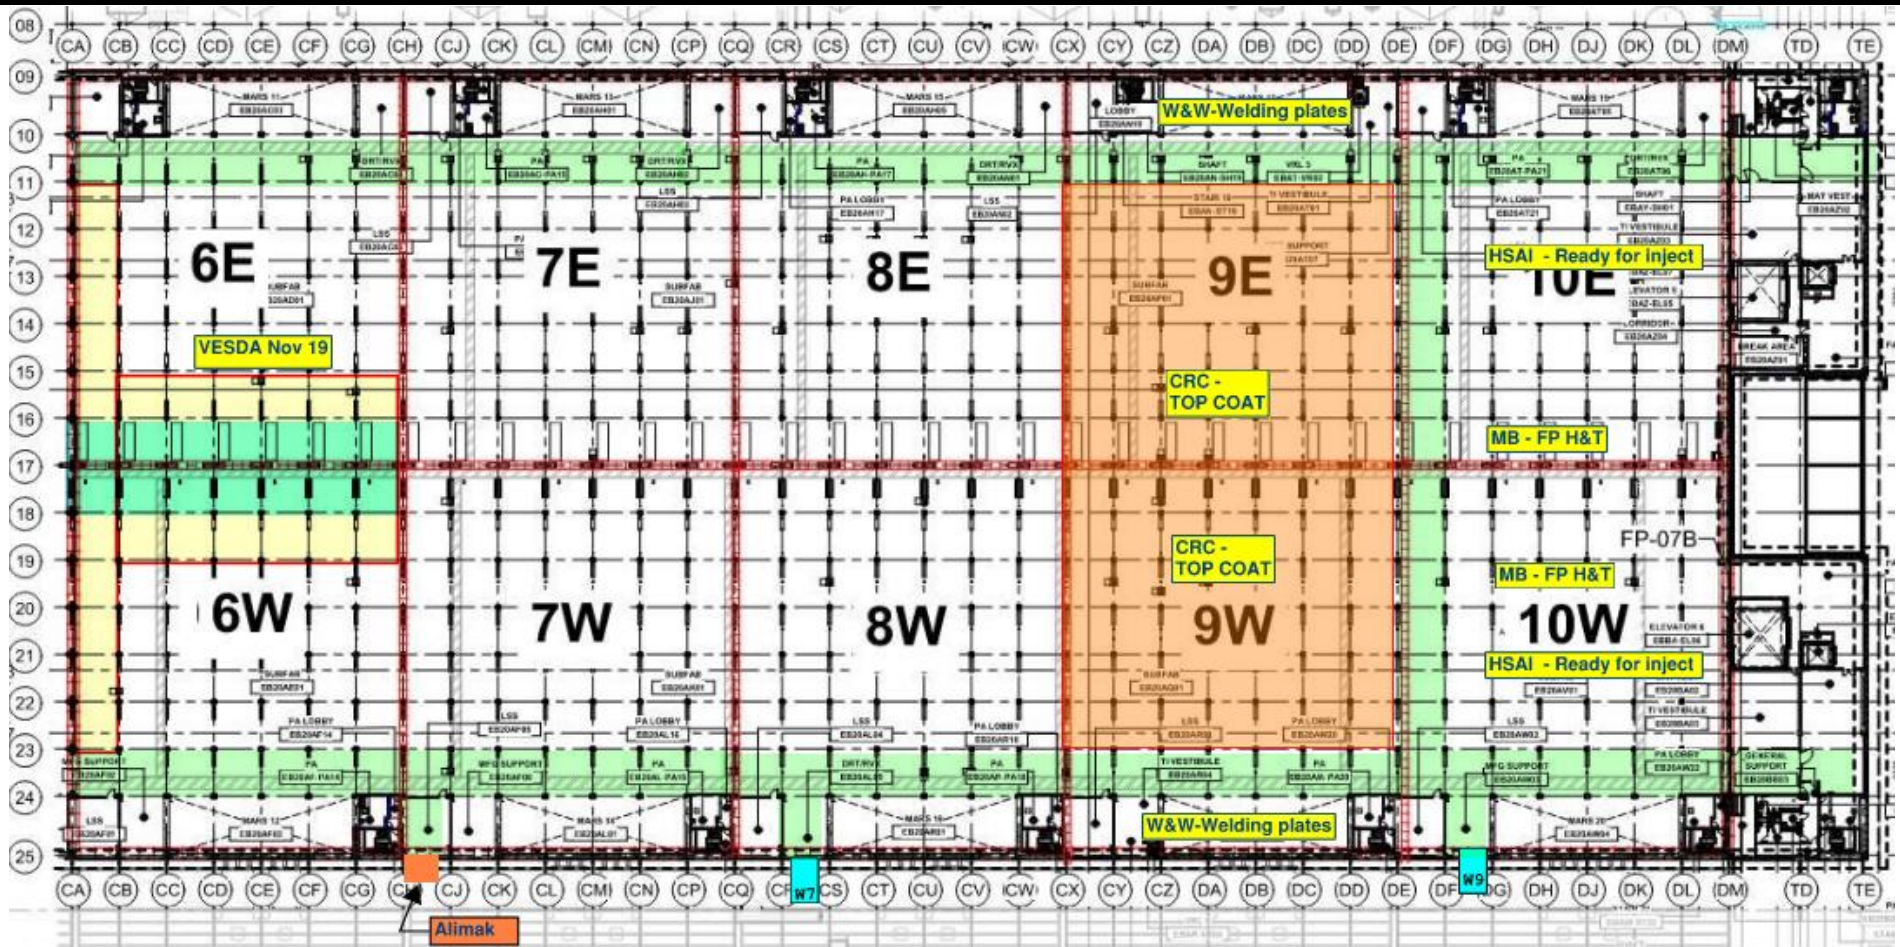



SUBFAB MEPTAGON GDP PANELS

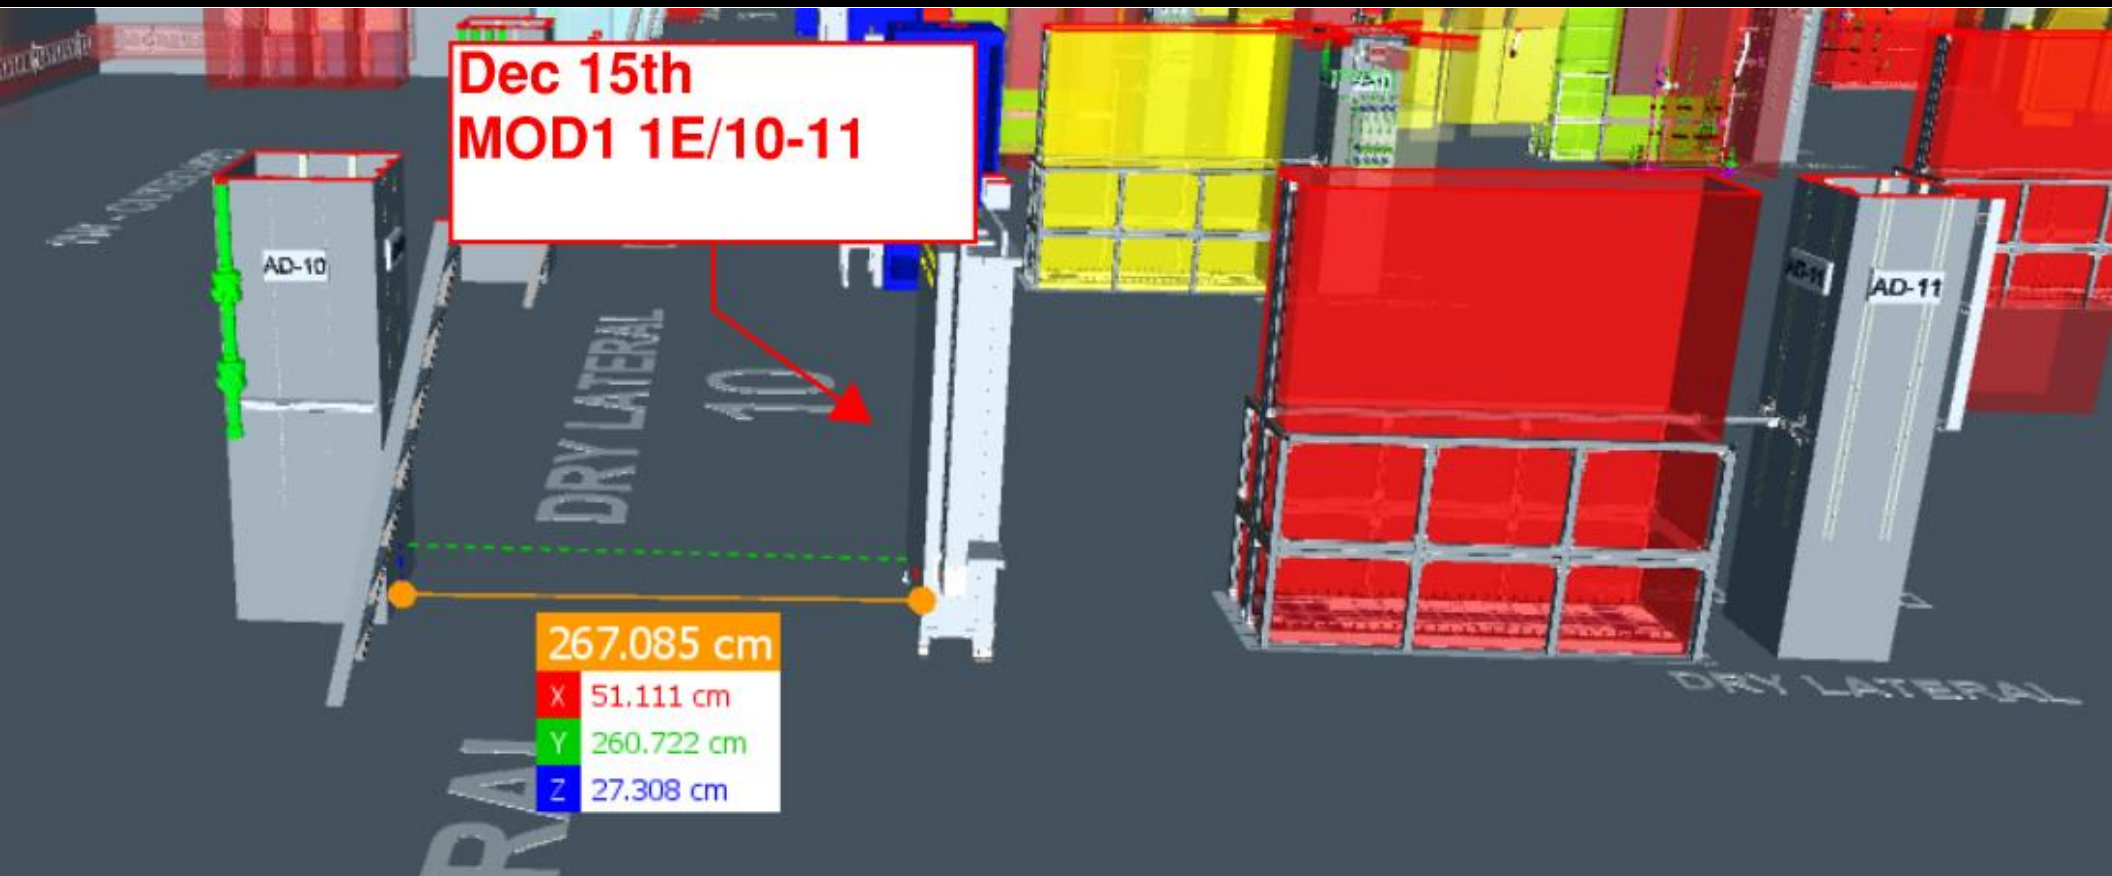


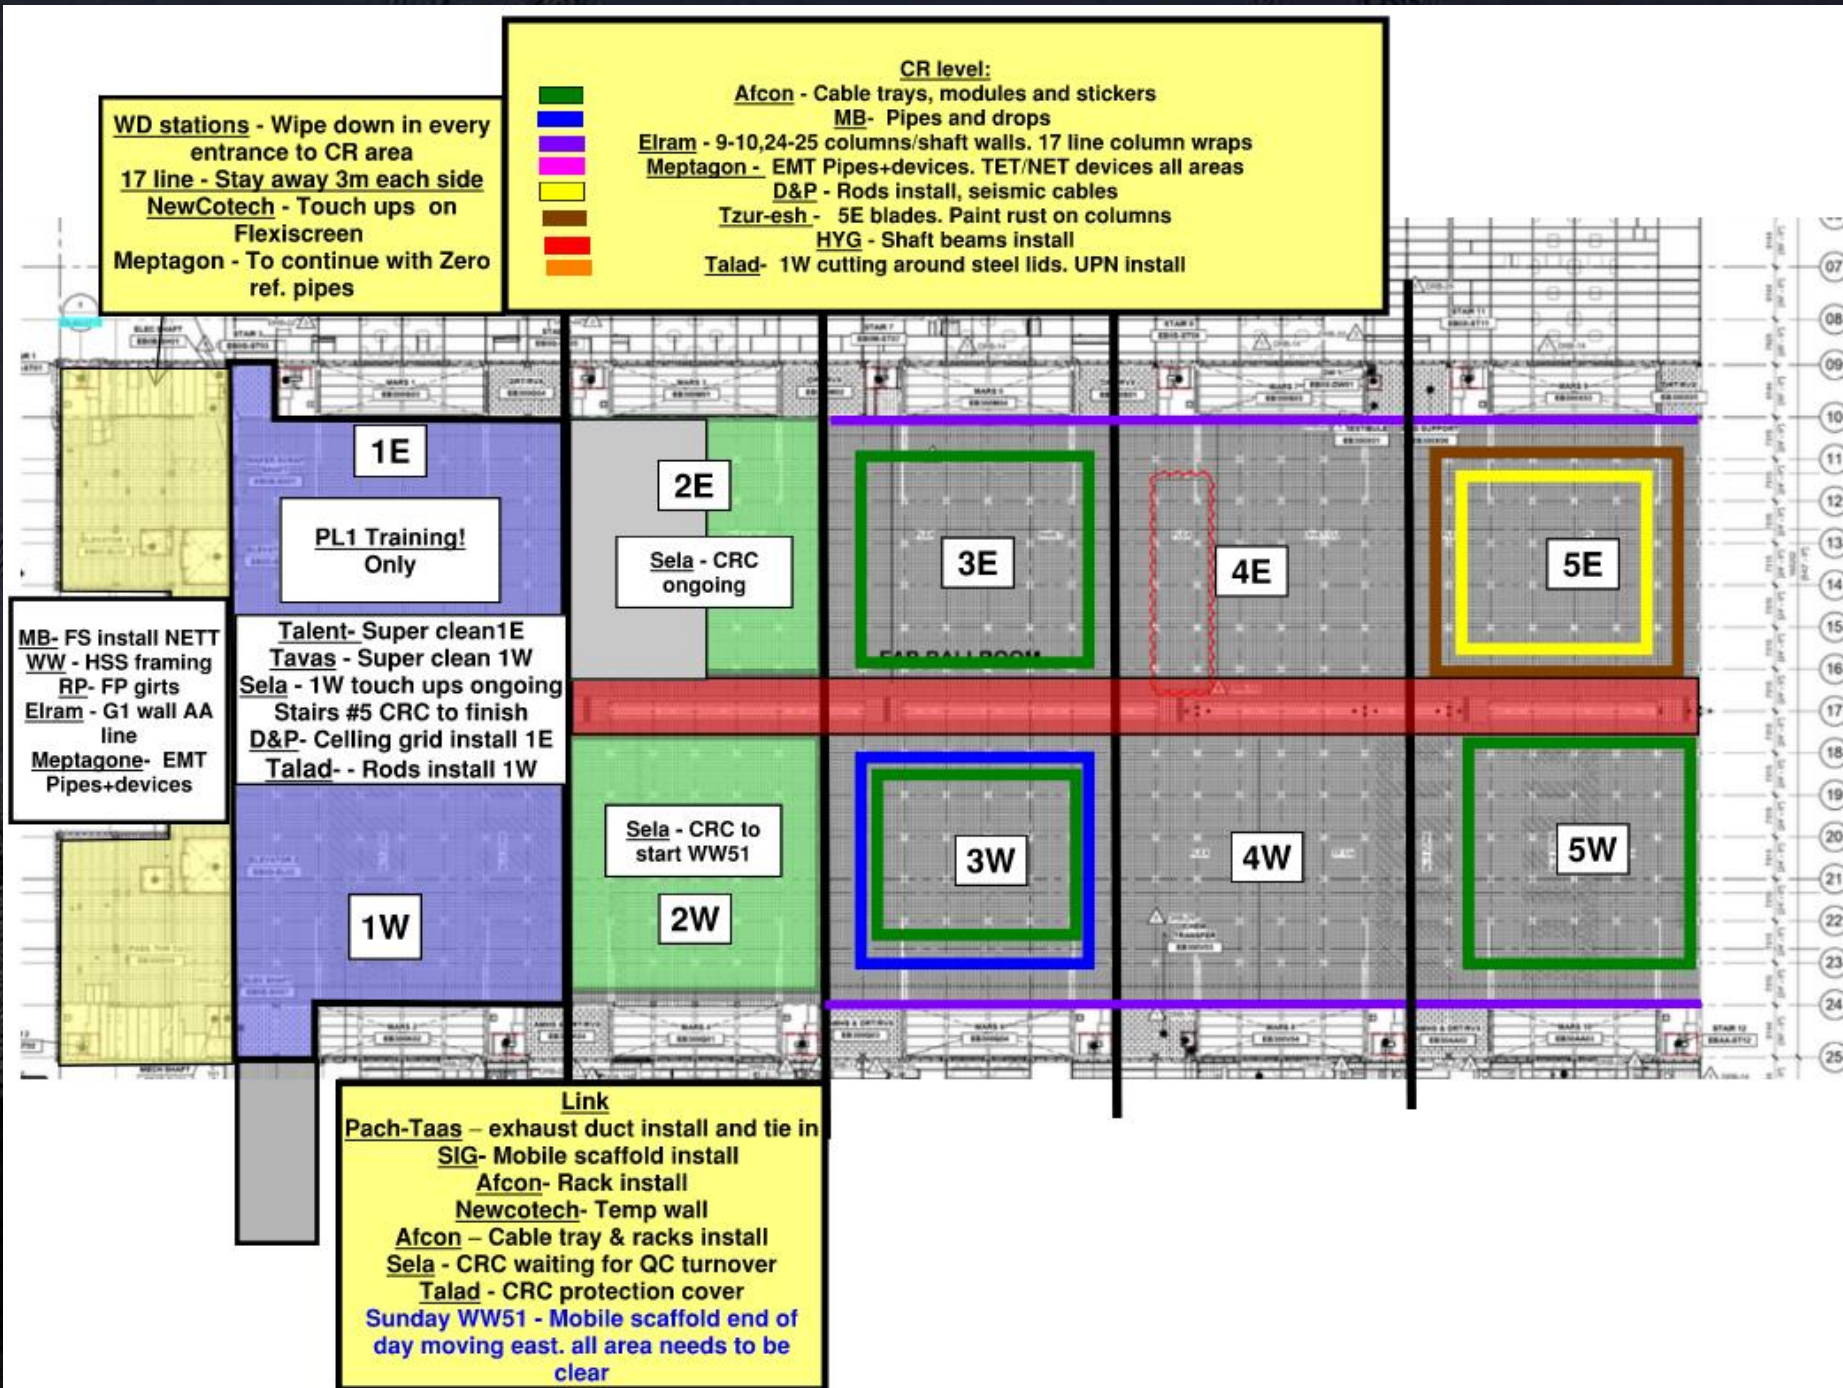

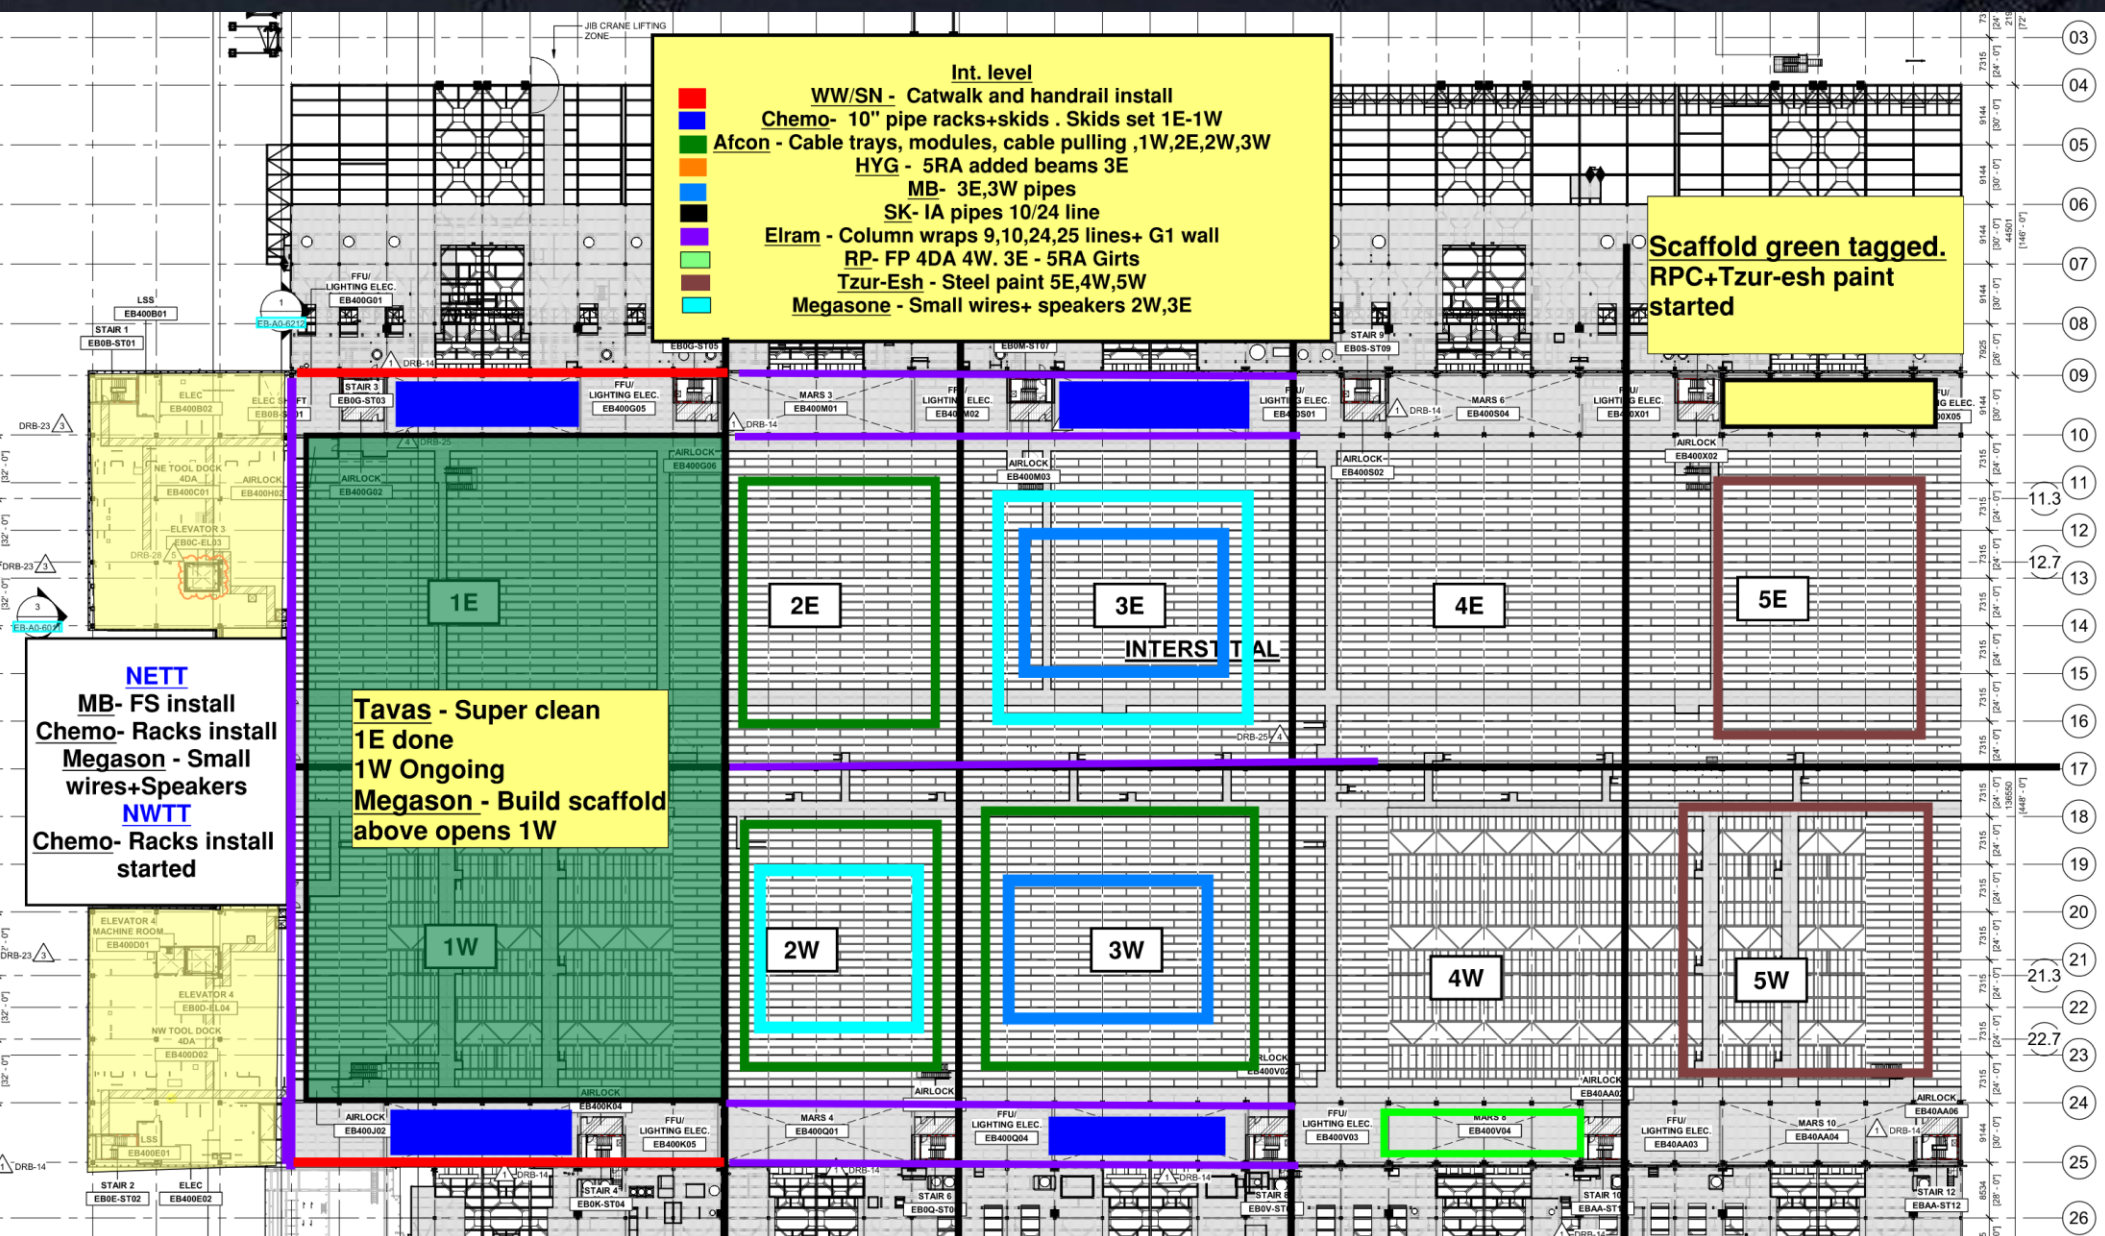

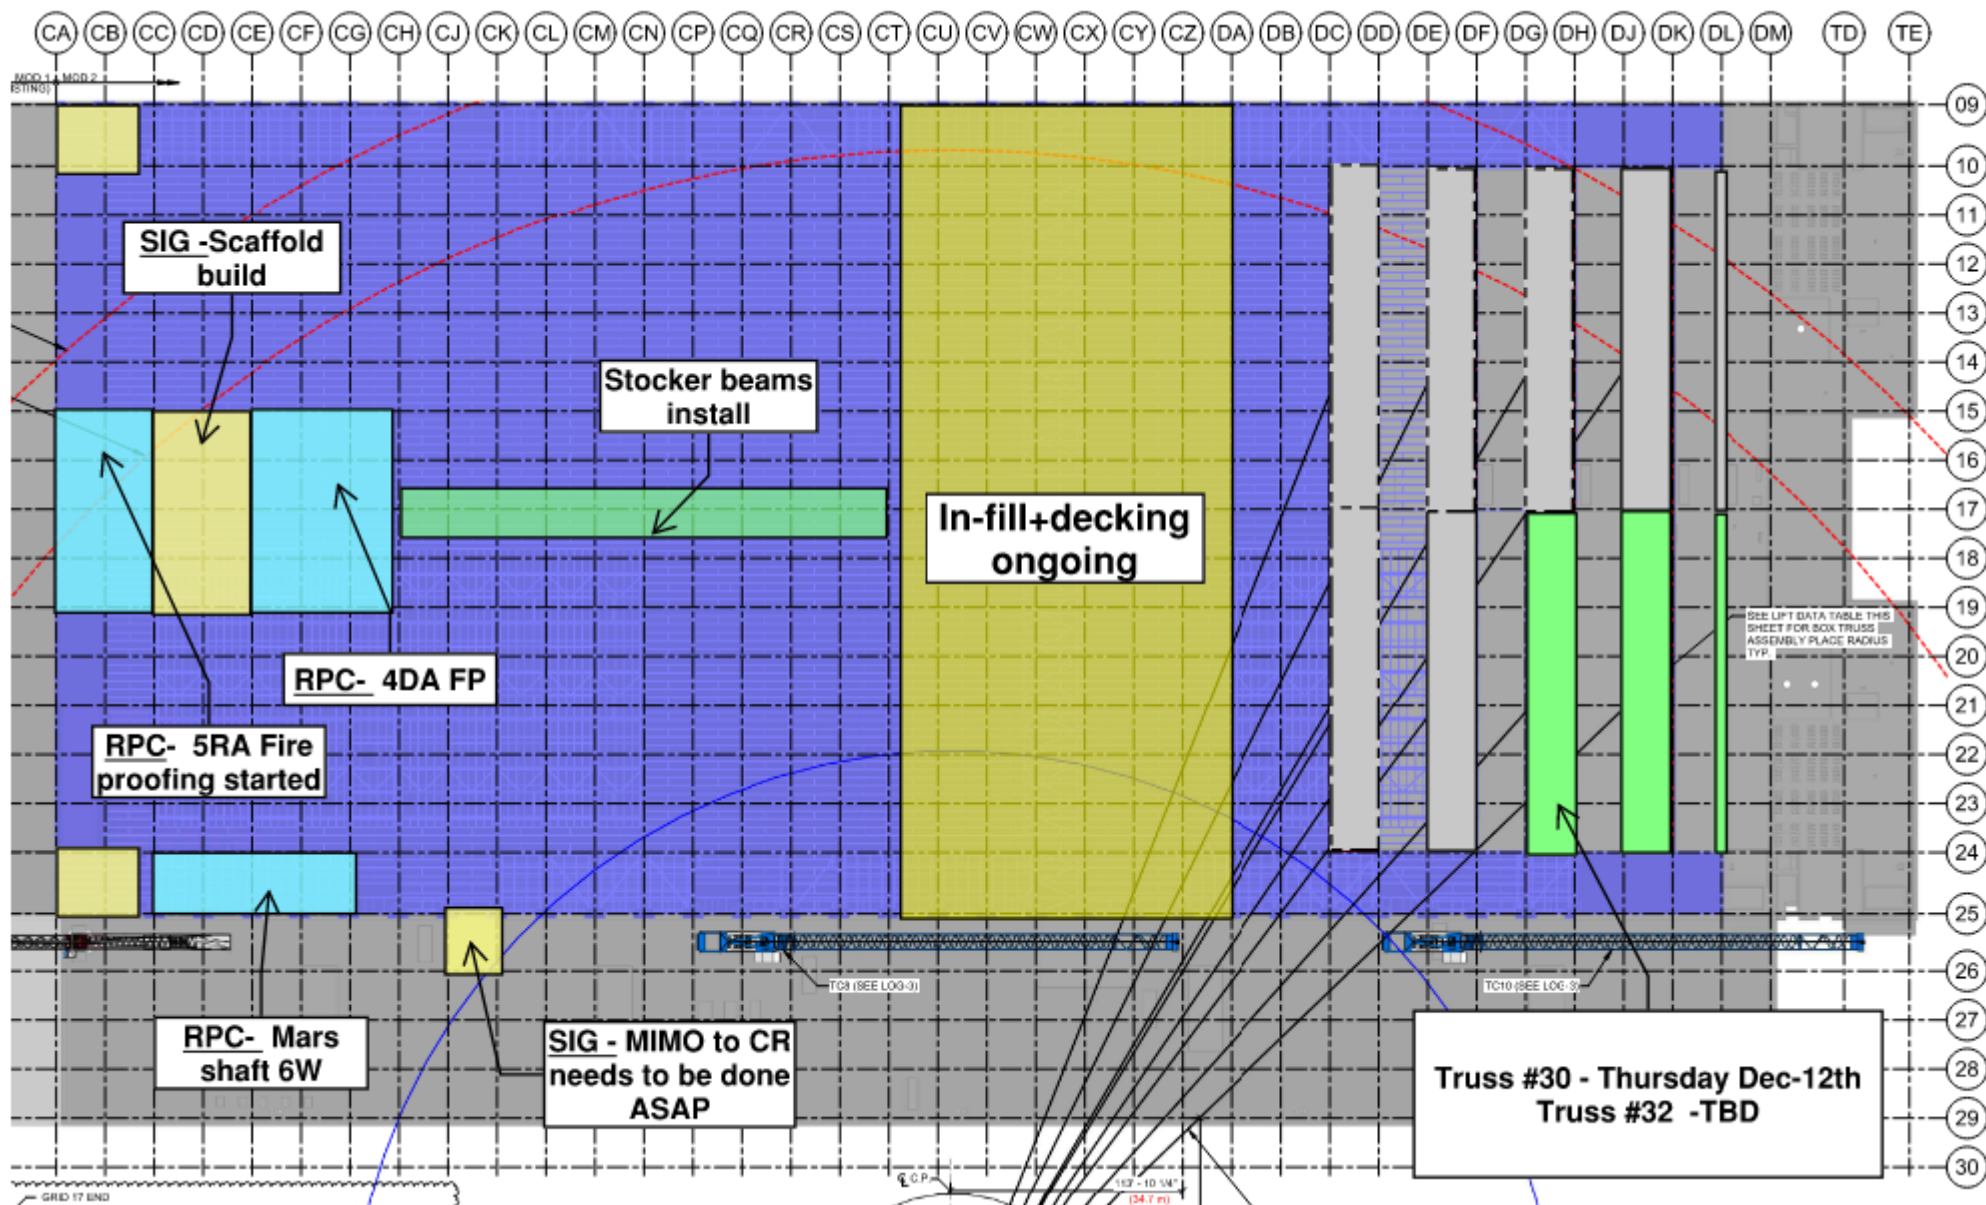

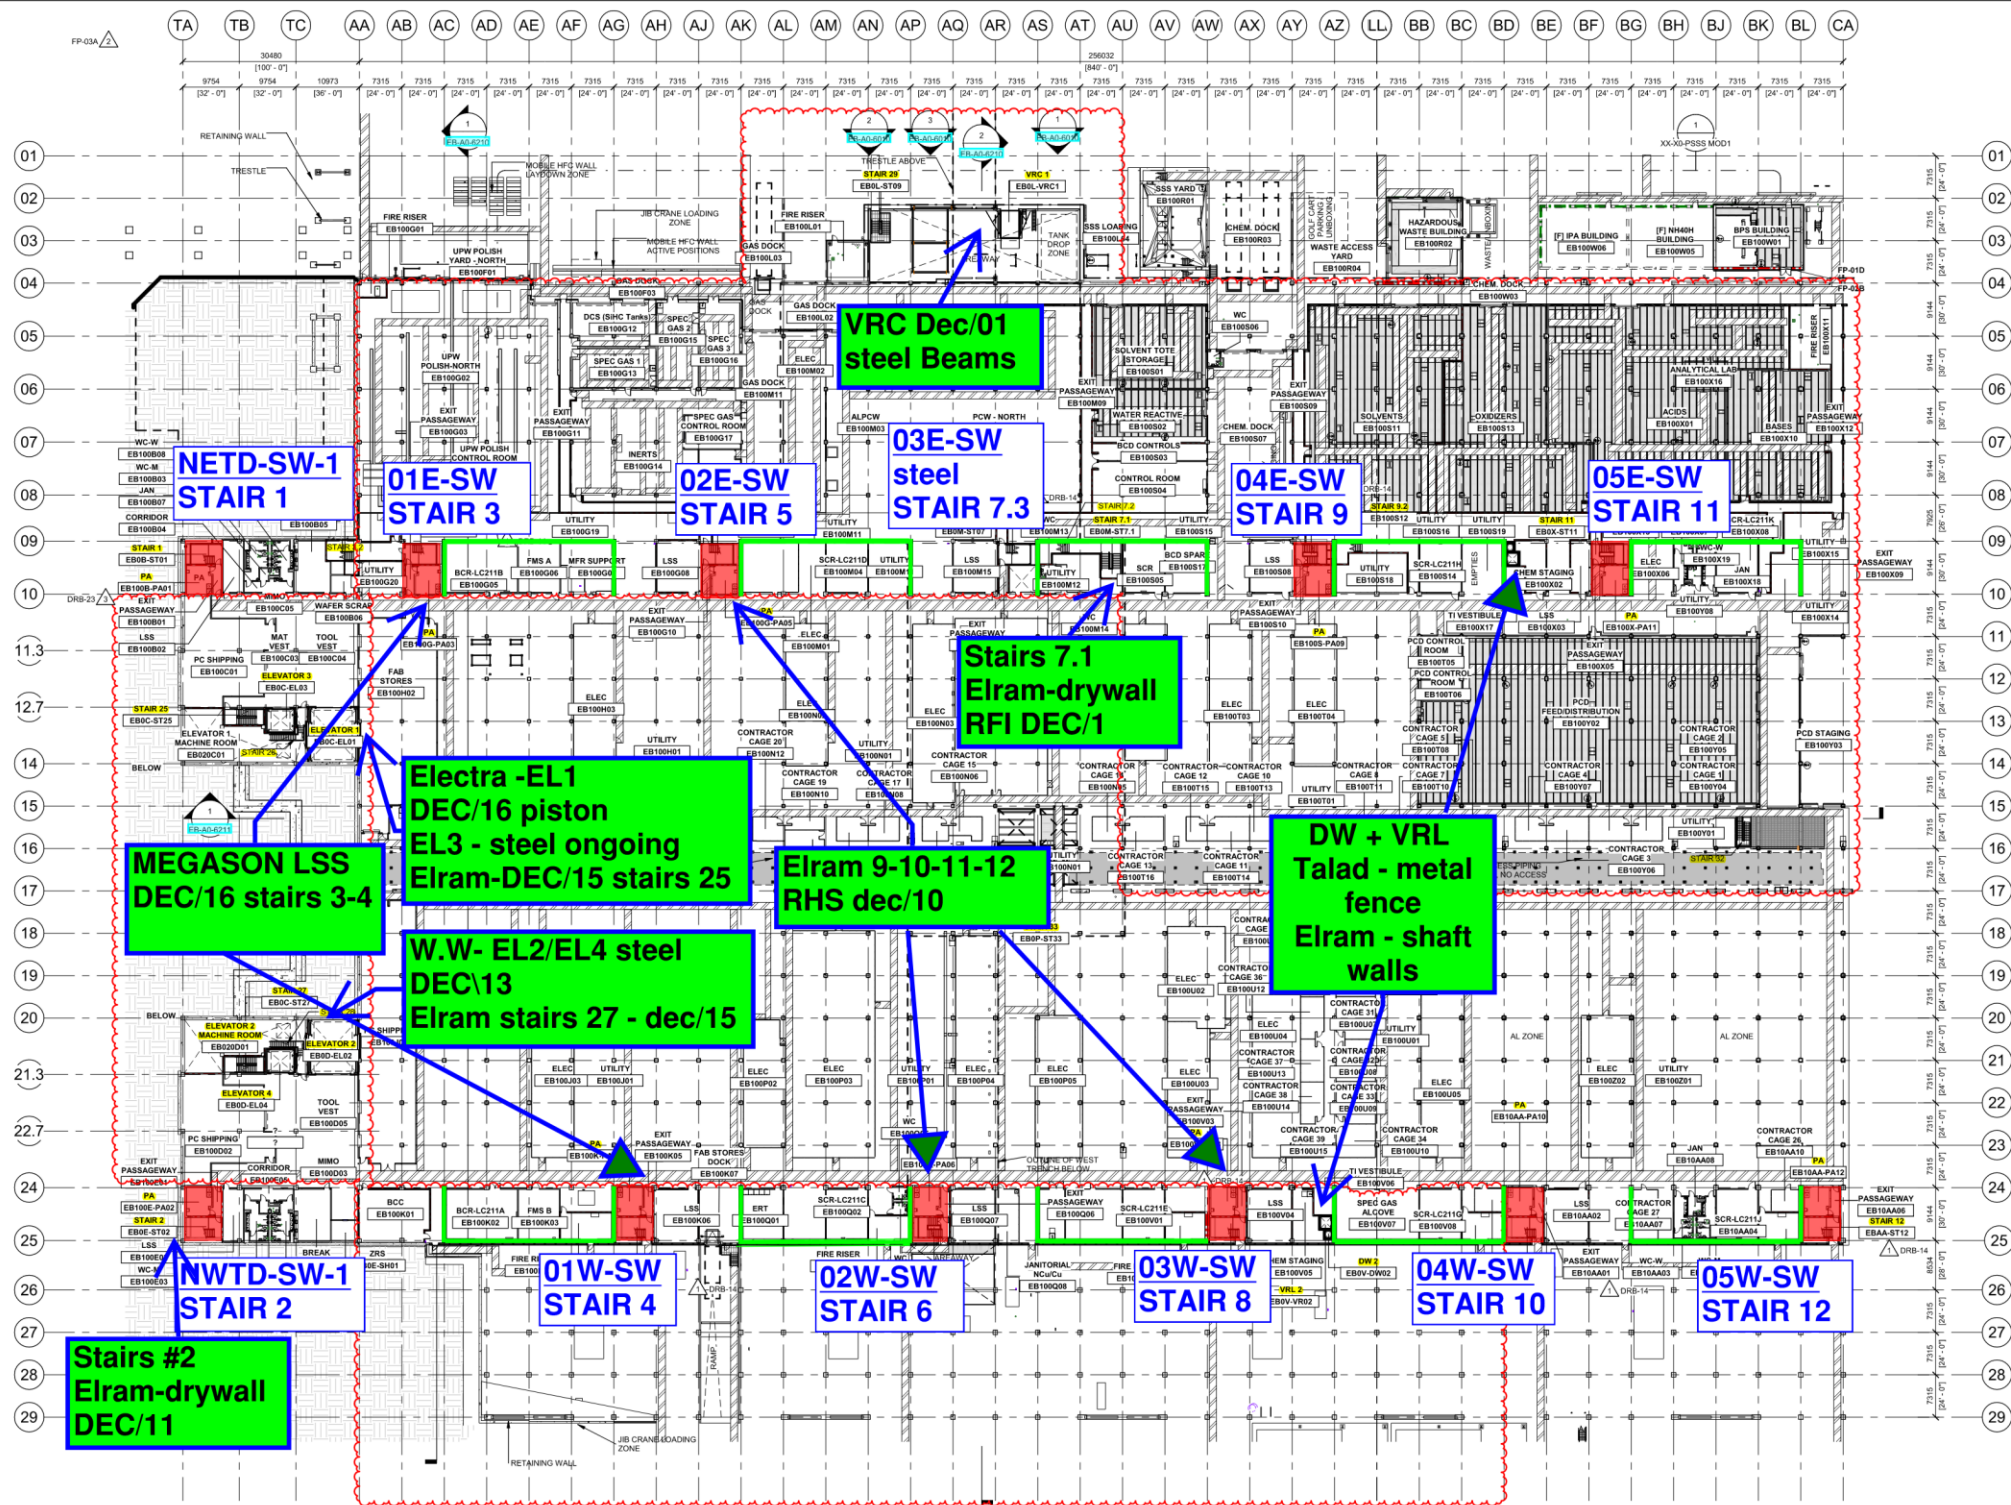

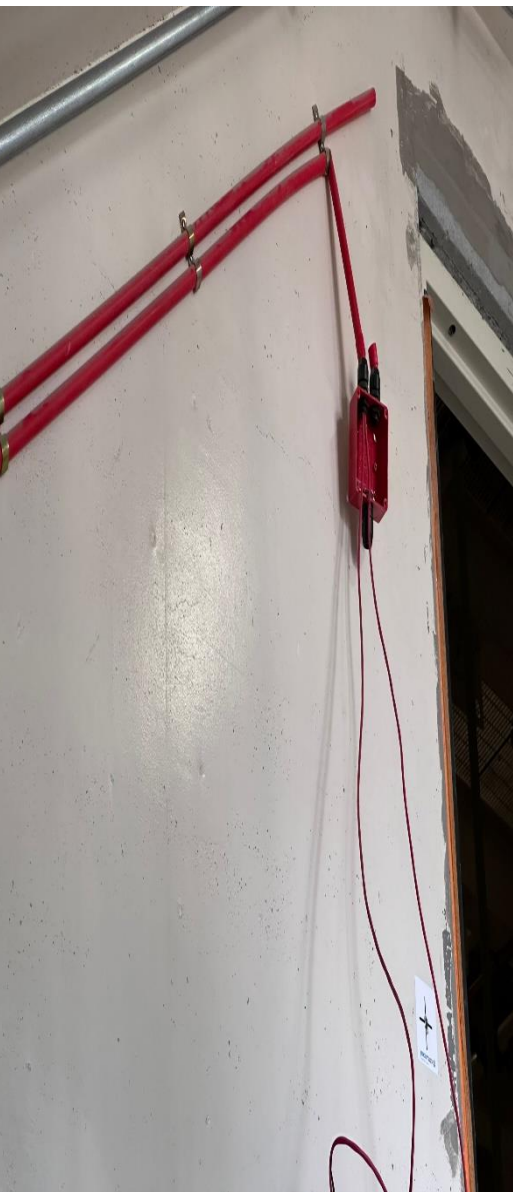


Siding - East FAB - PSSS


[illegible]


Siding - West FAB - JYG

[illegible]

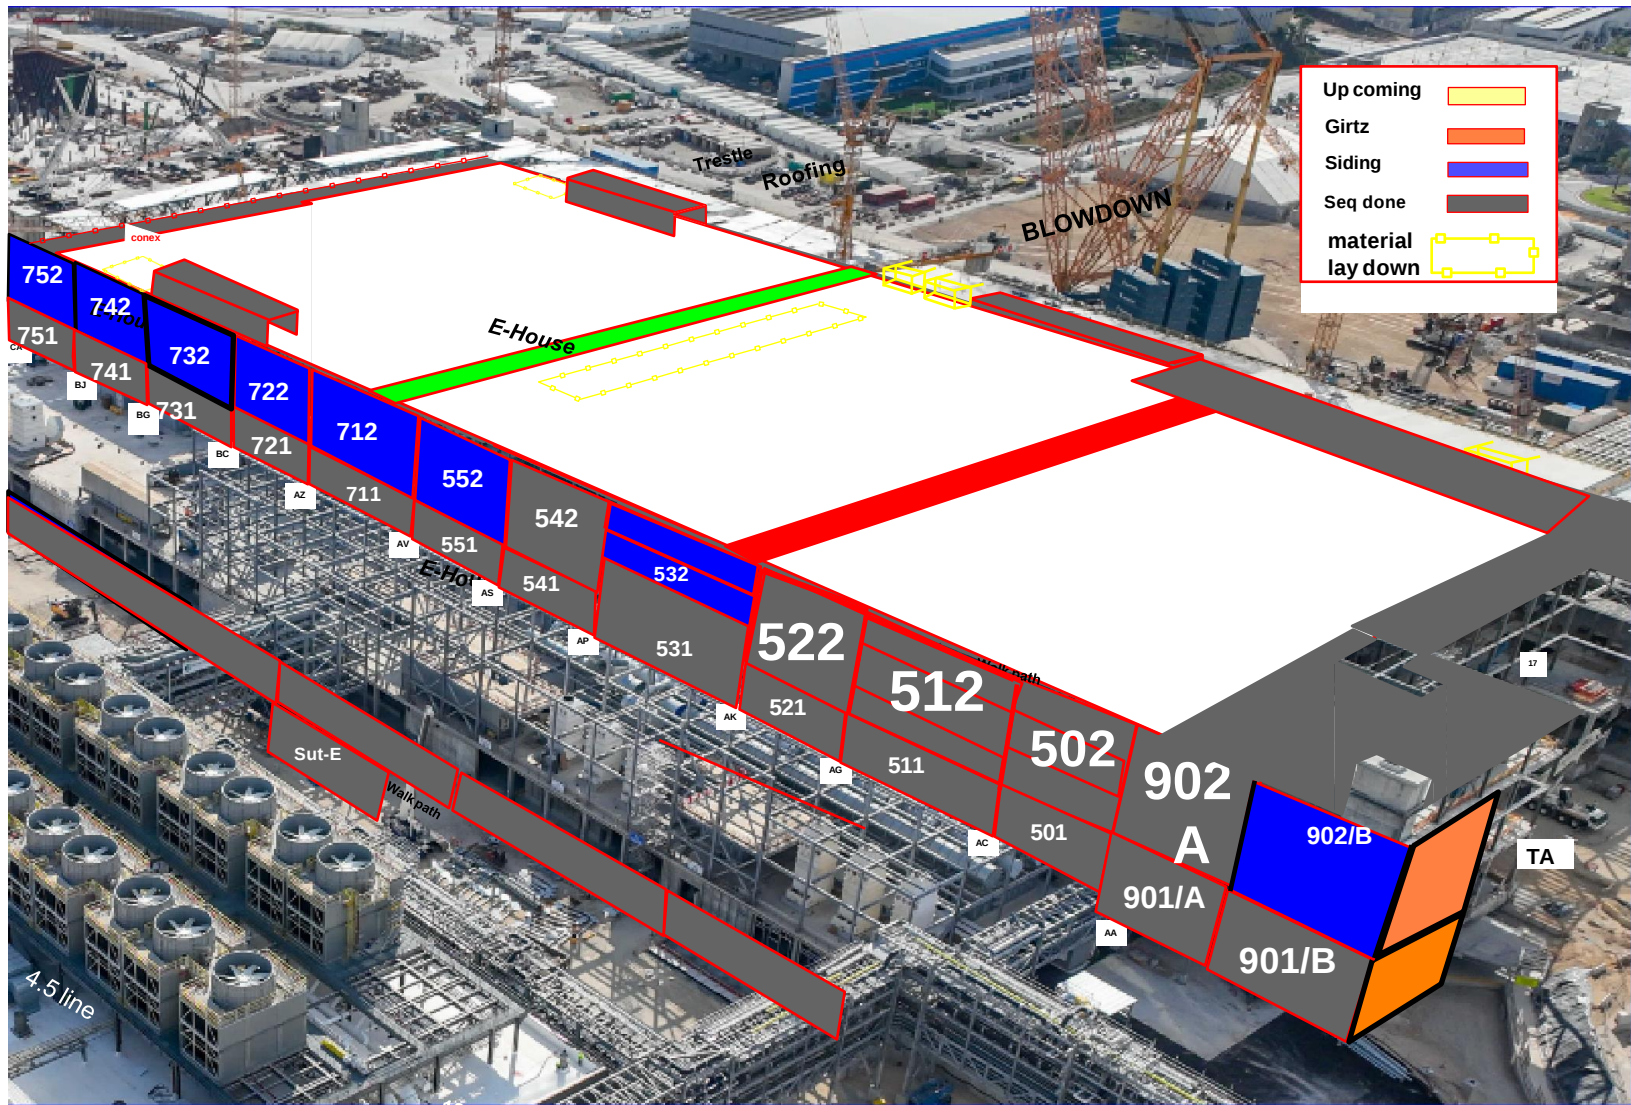

Walk path

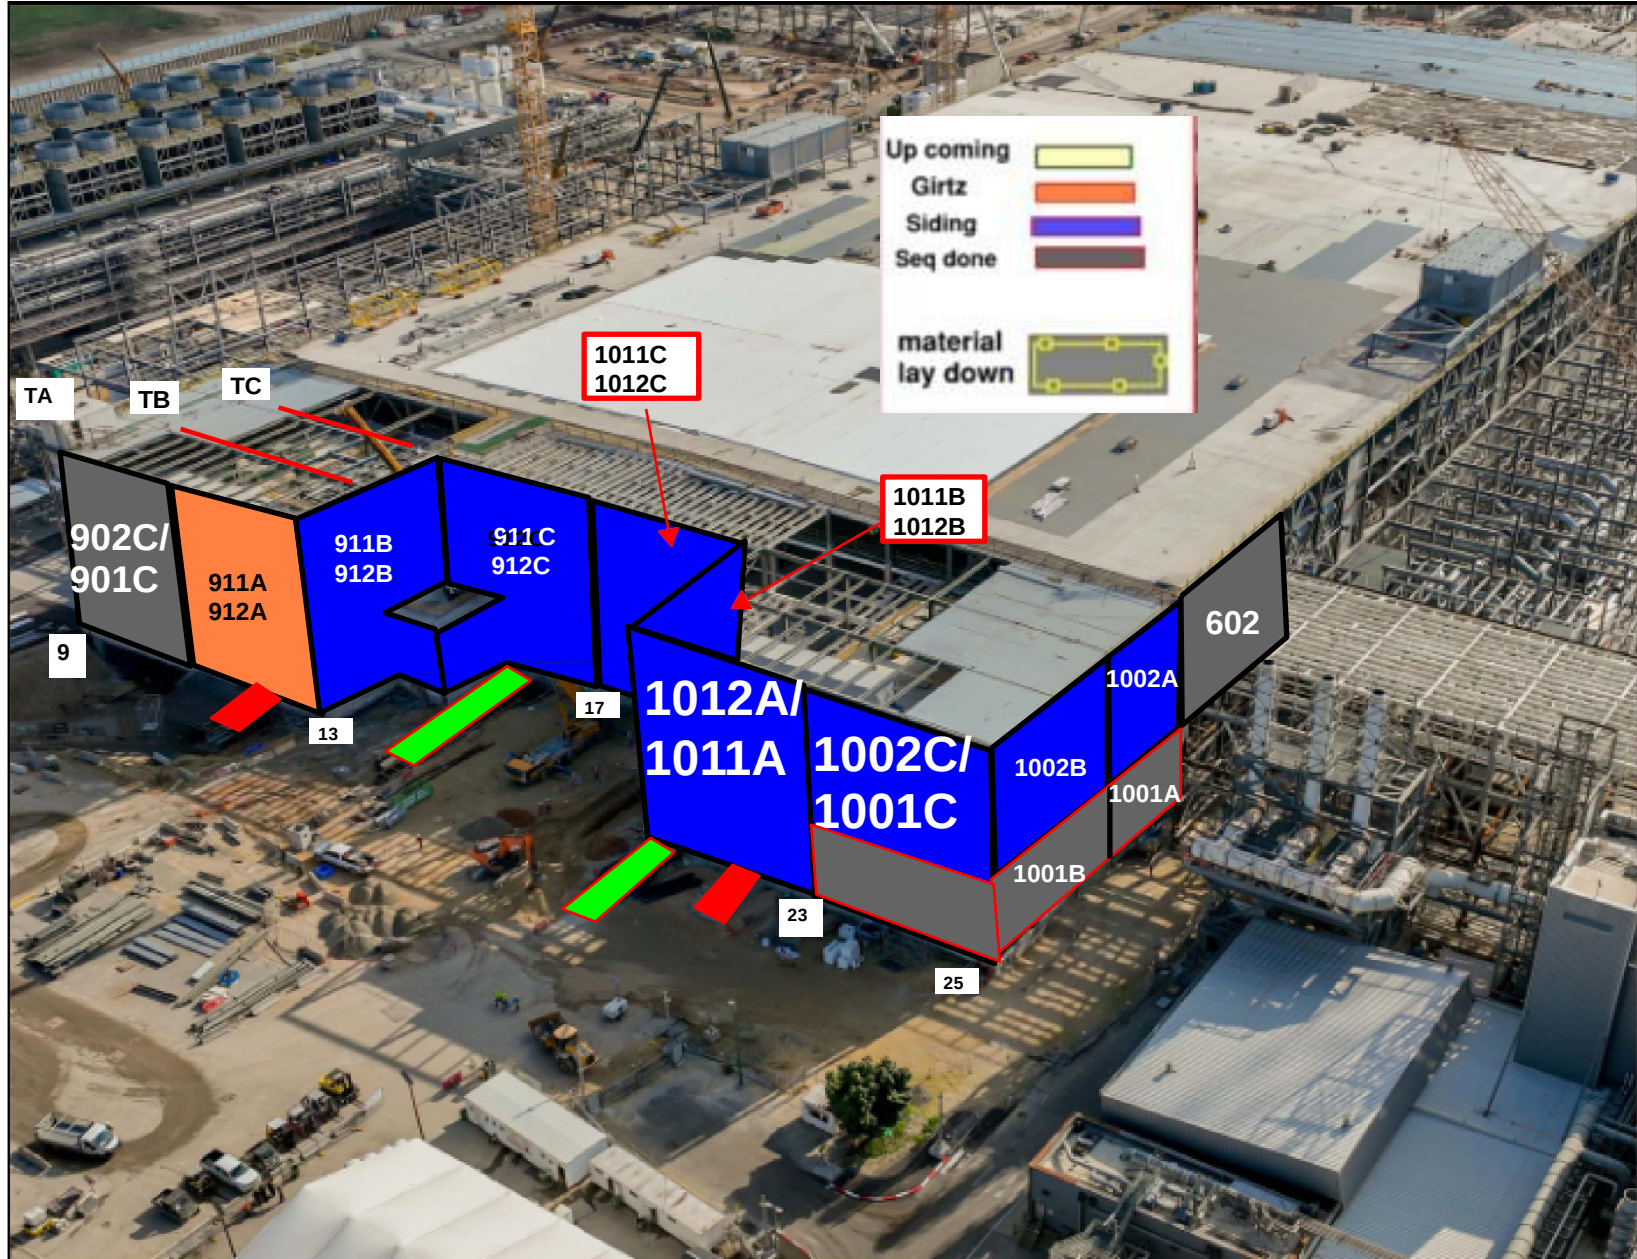


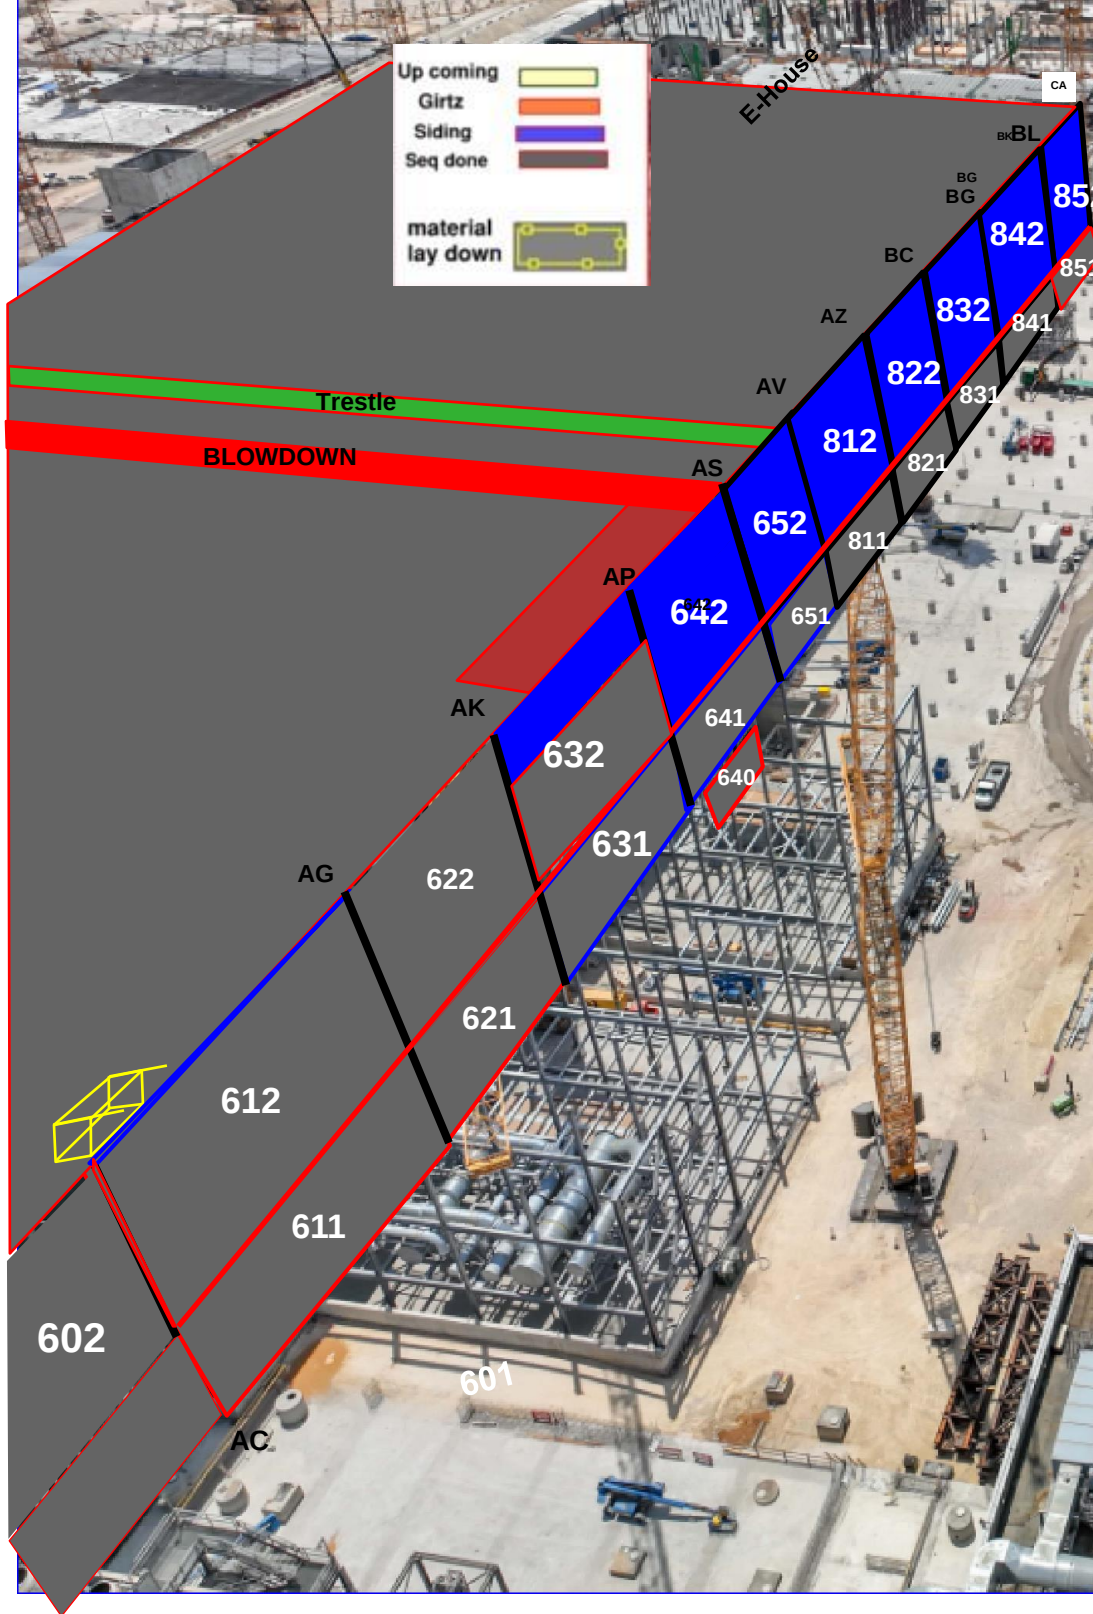

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

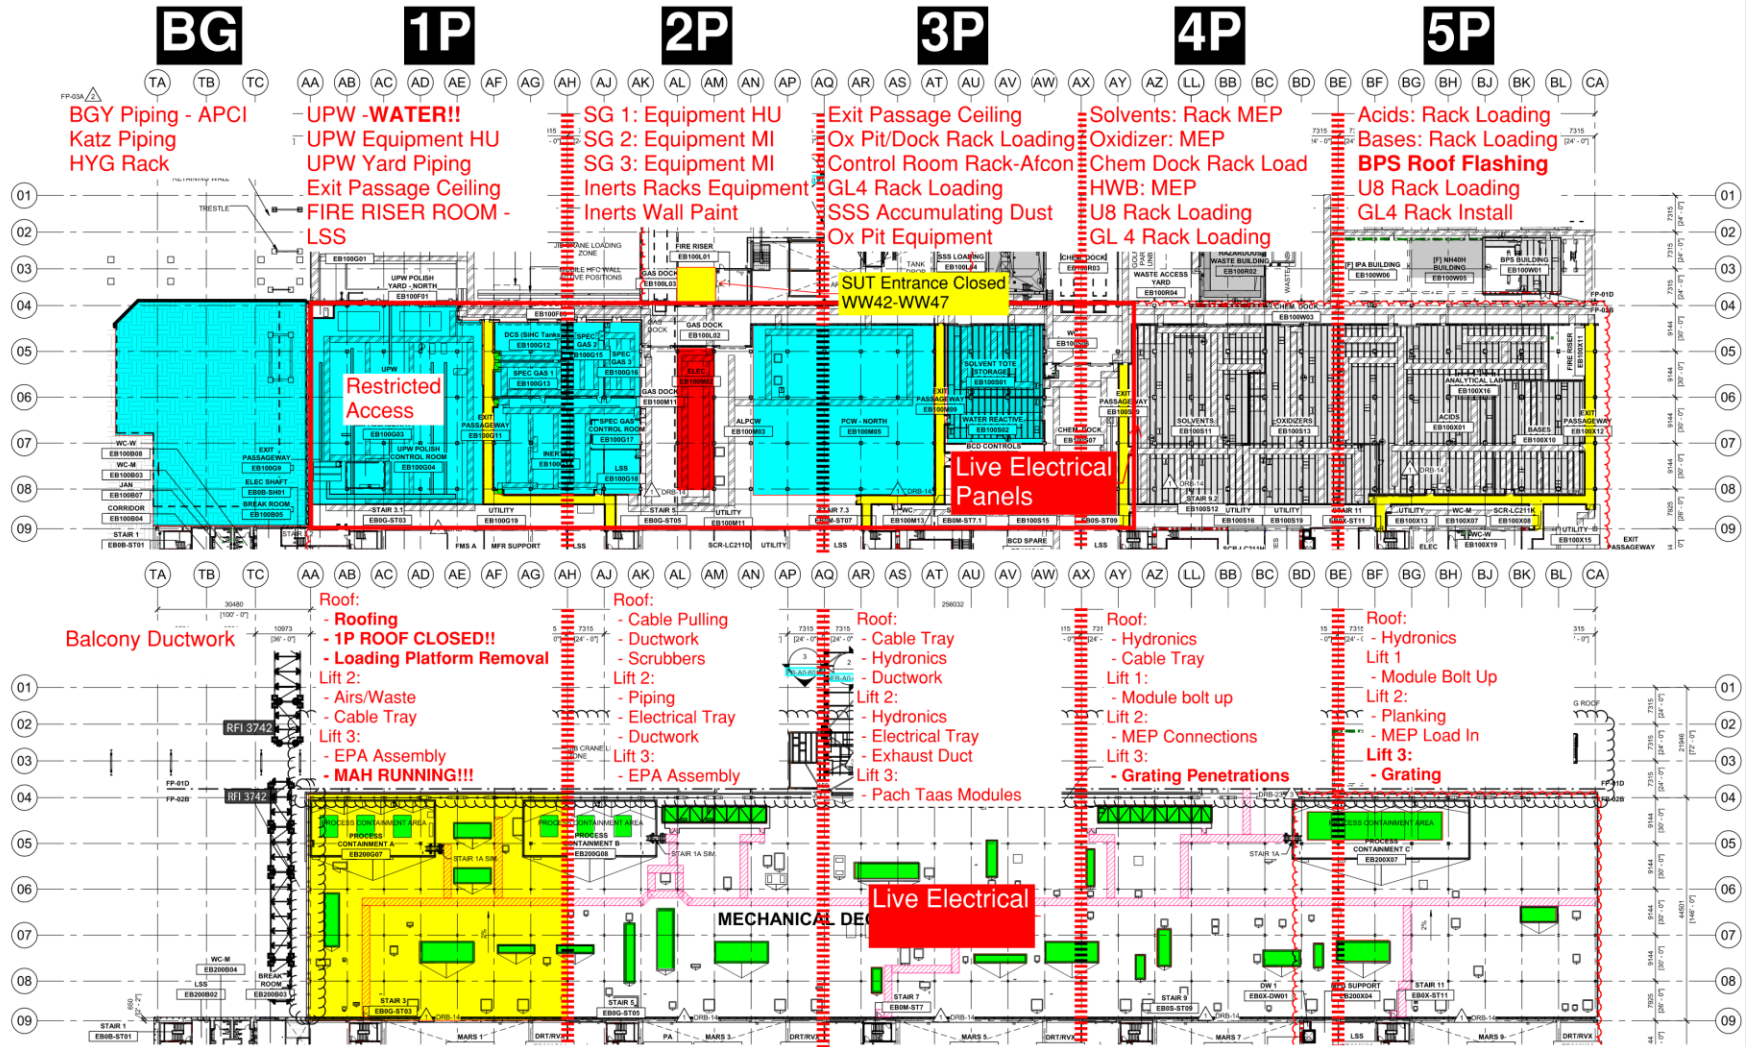


PSSS.2

Utility Level
1YA


PSSS Roof
2SA

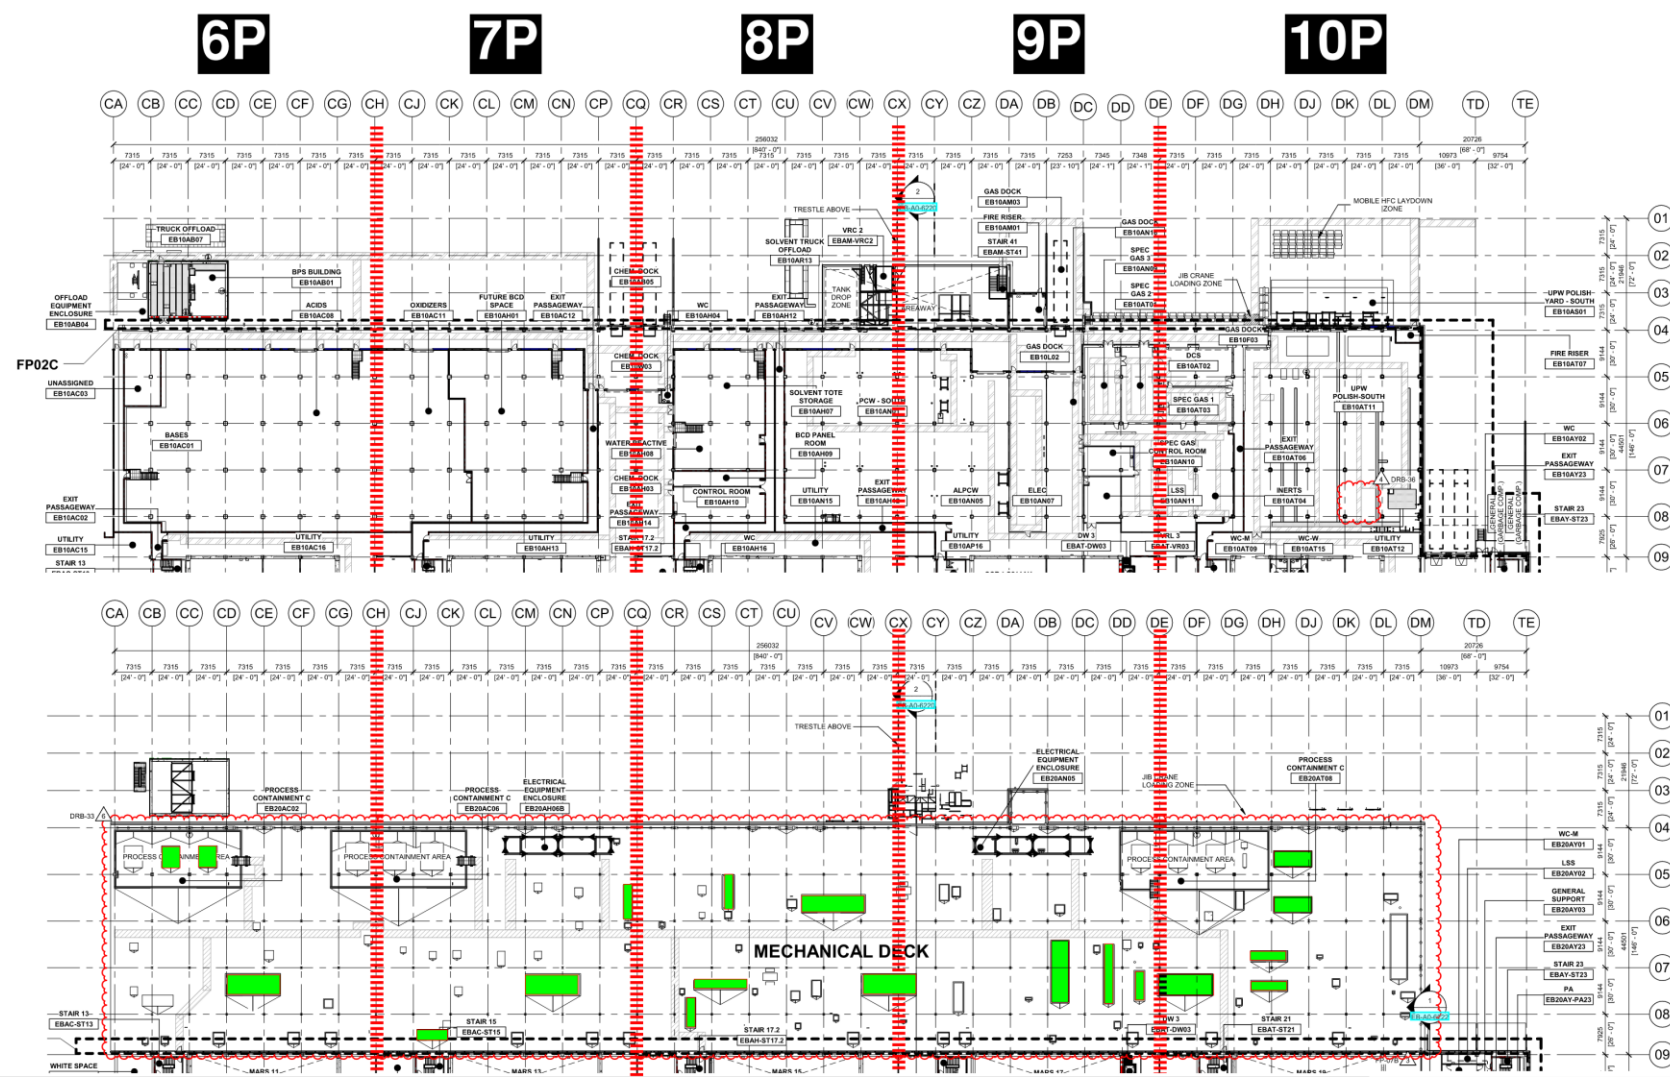

PSSS.1 UN2 Pressure Test

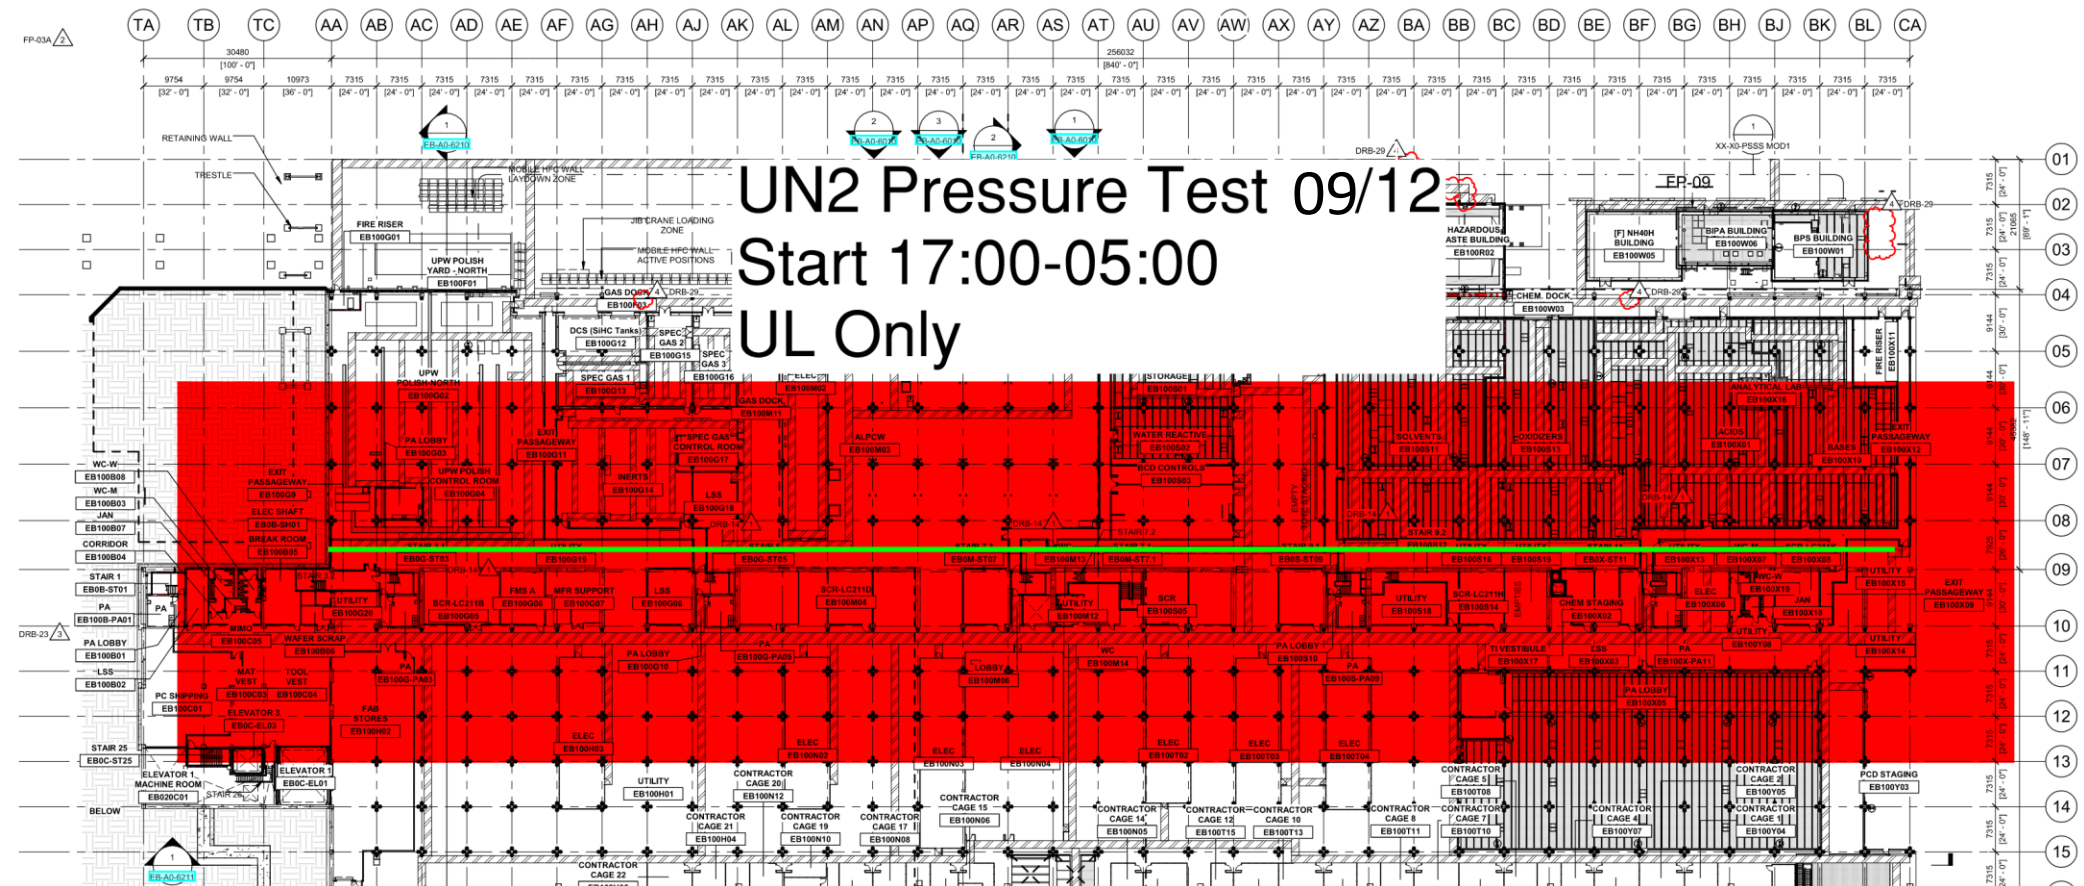

500T
Moving
Dec.
13-15

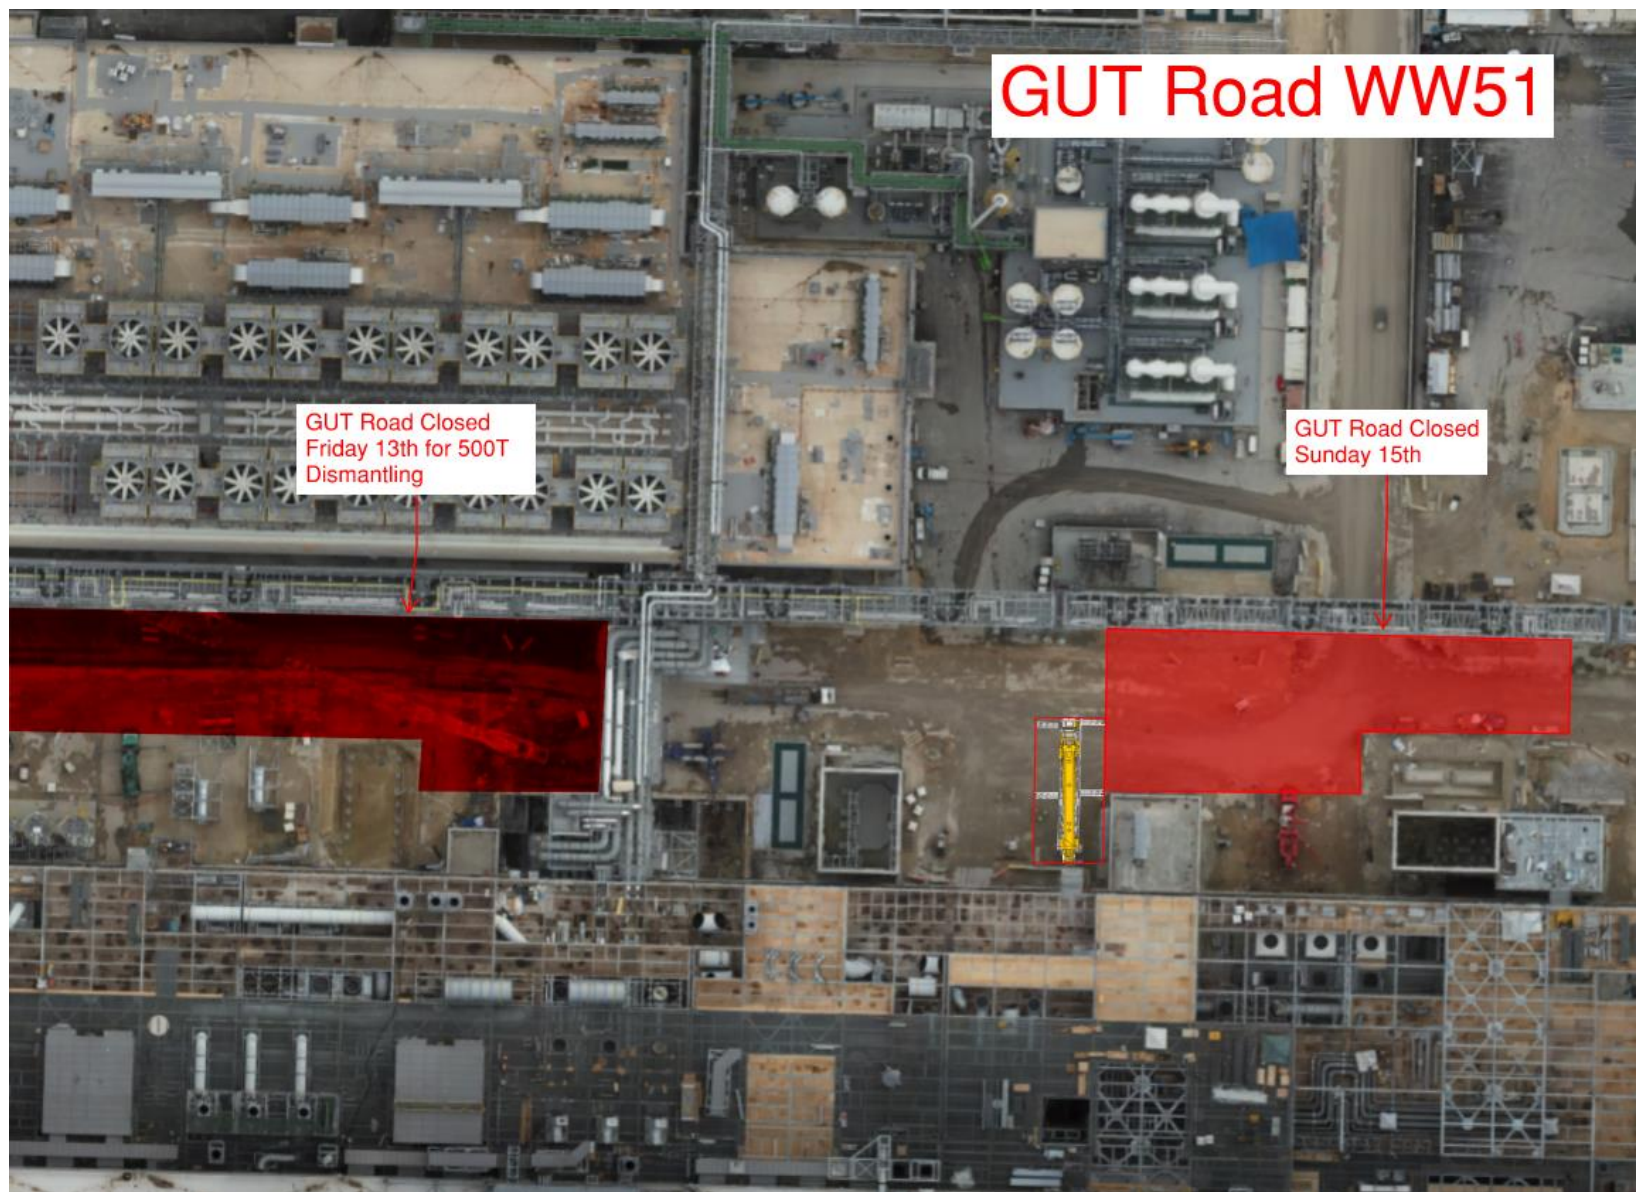



WJG 01J, 02J LIFT 2 & 3







WJG 03J, 04J, 05J LIFT 2 & 3





MAH101-9/10-00 Set WW50

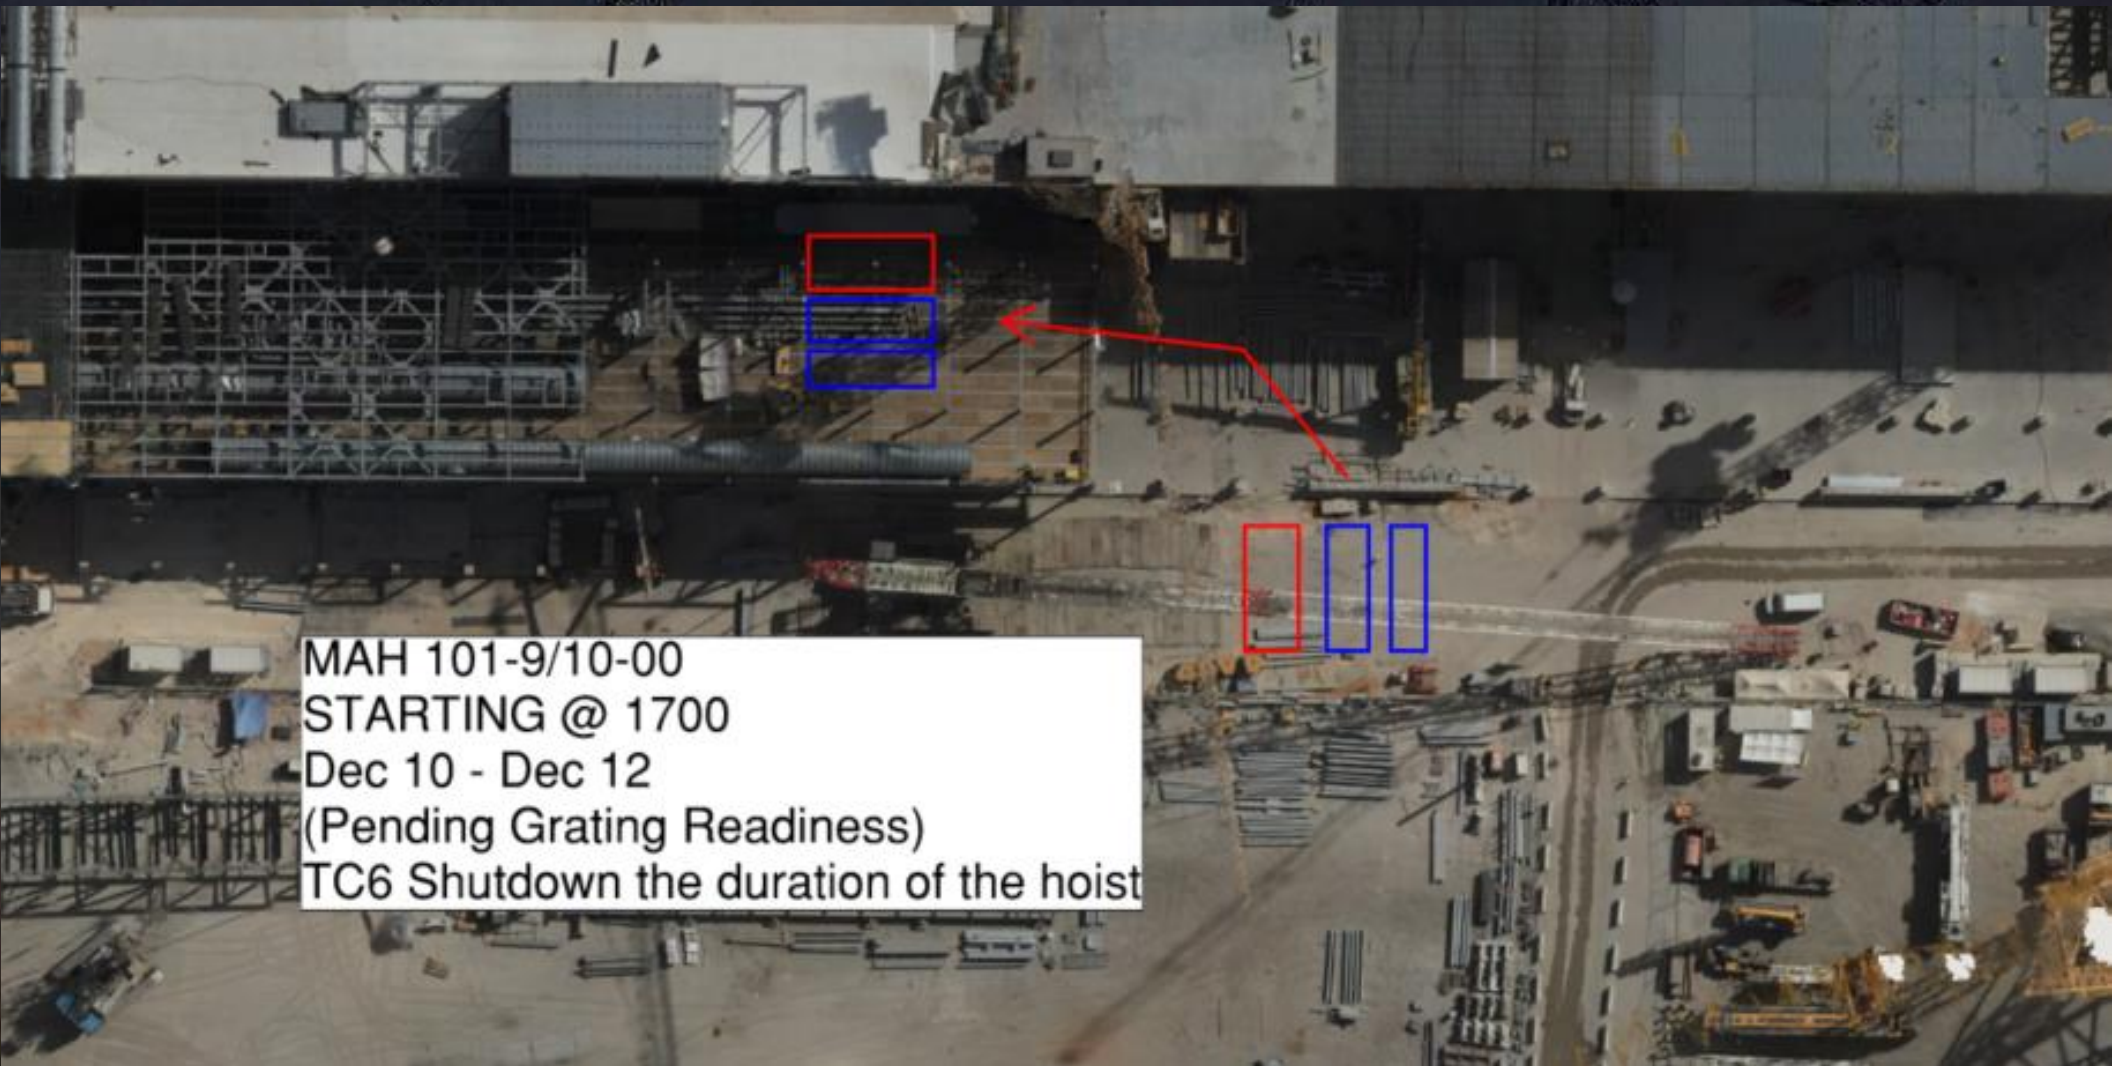

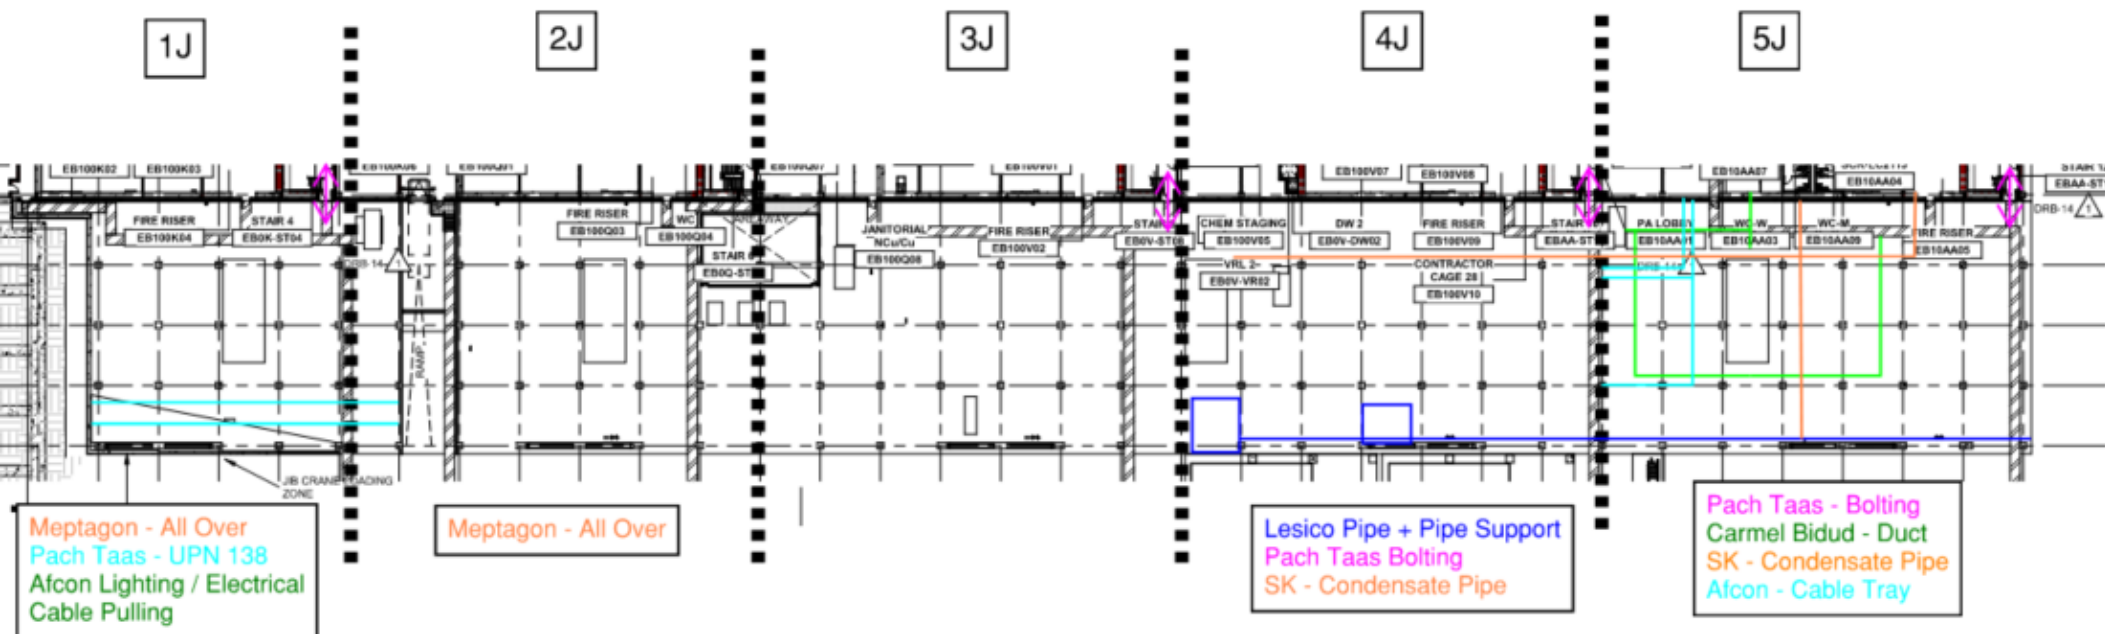



HOFFMAN CONSTRUCTION COMPANY




CC3800 DEMOB WW51




CUB 1

CUB COORDINATION MAP

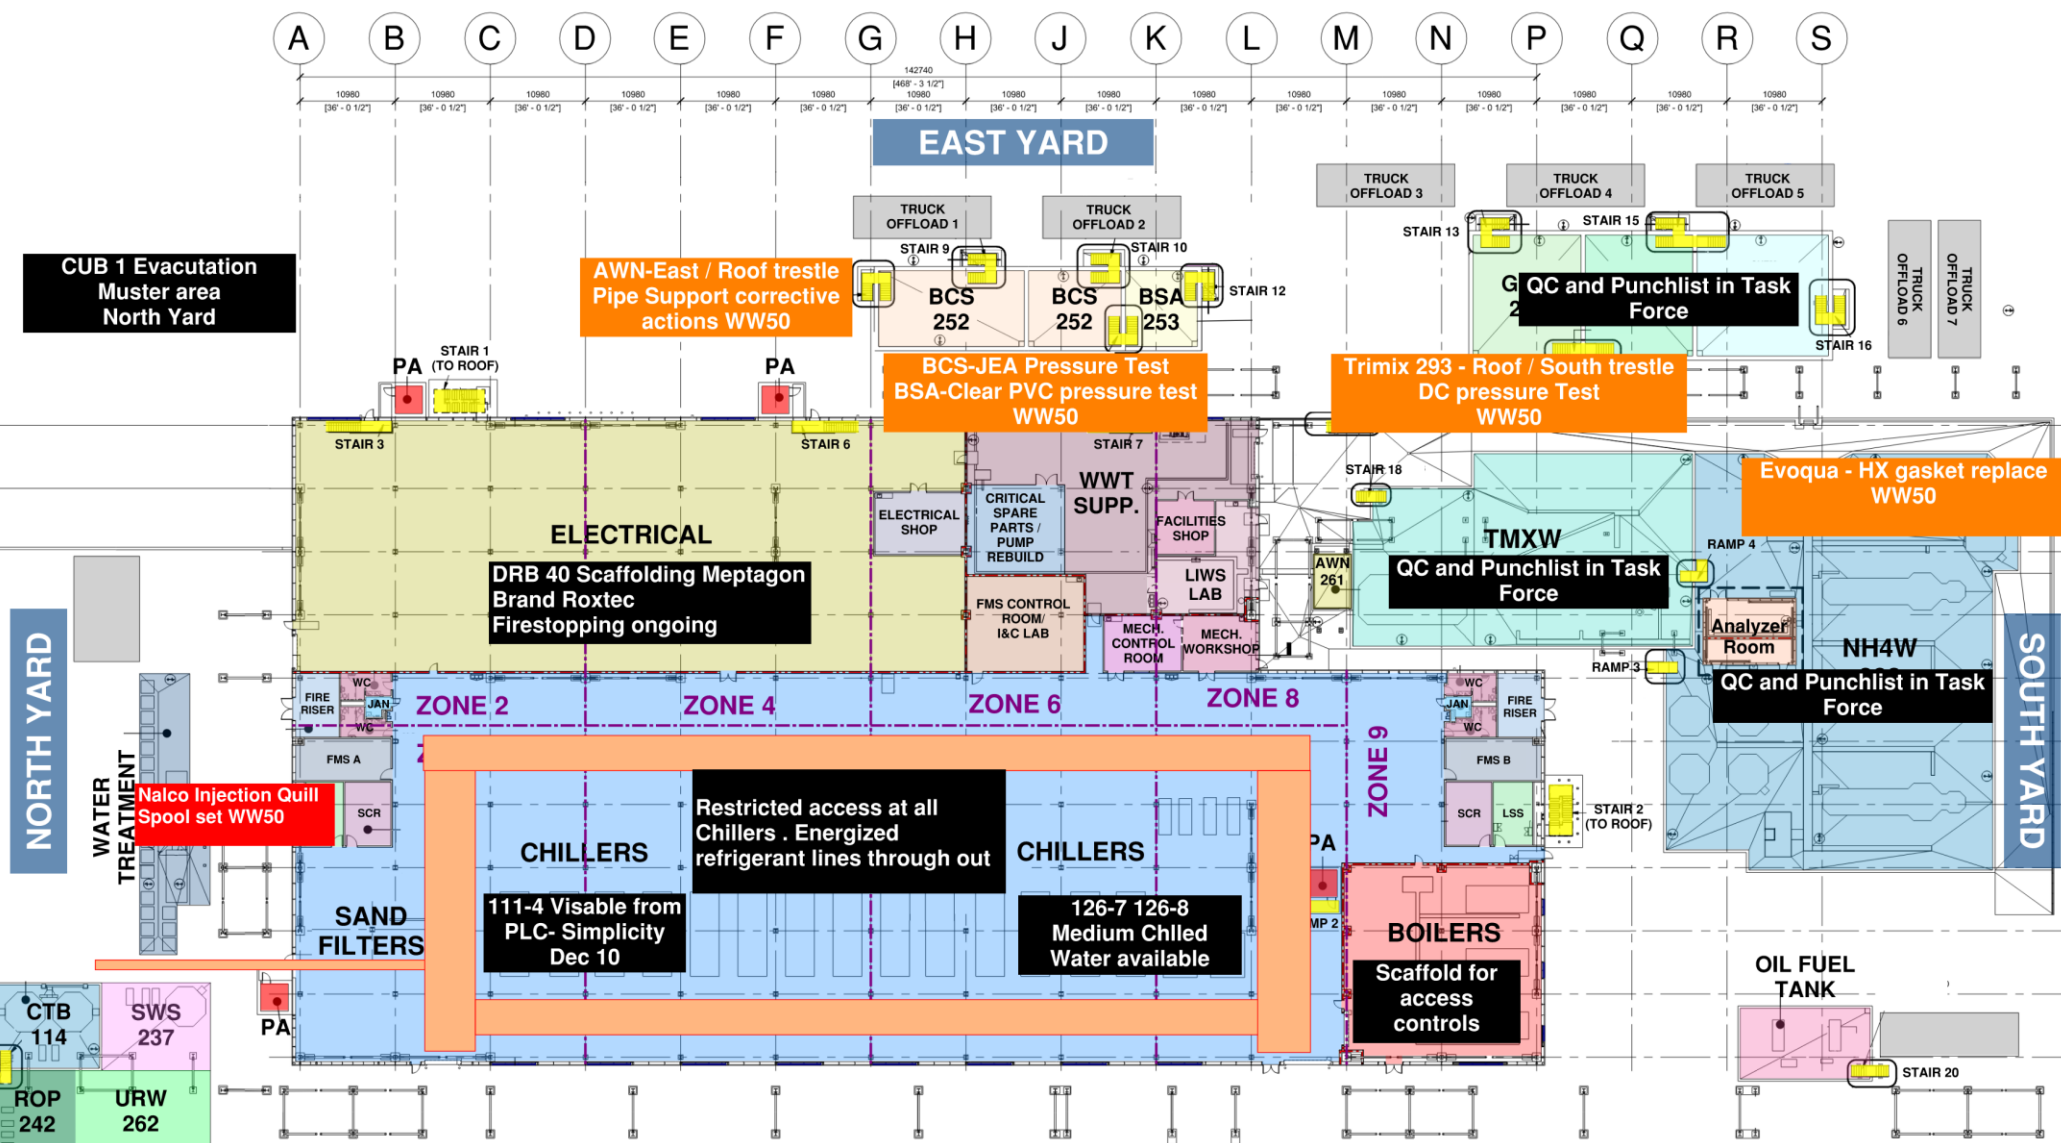


CUB 1 – EXTERIOR/ROOF

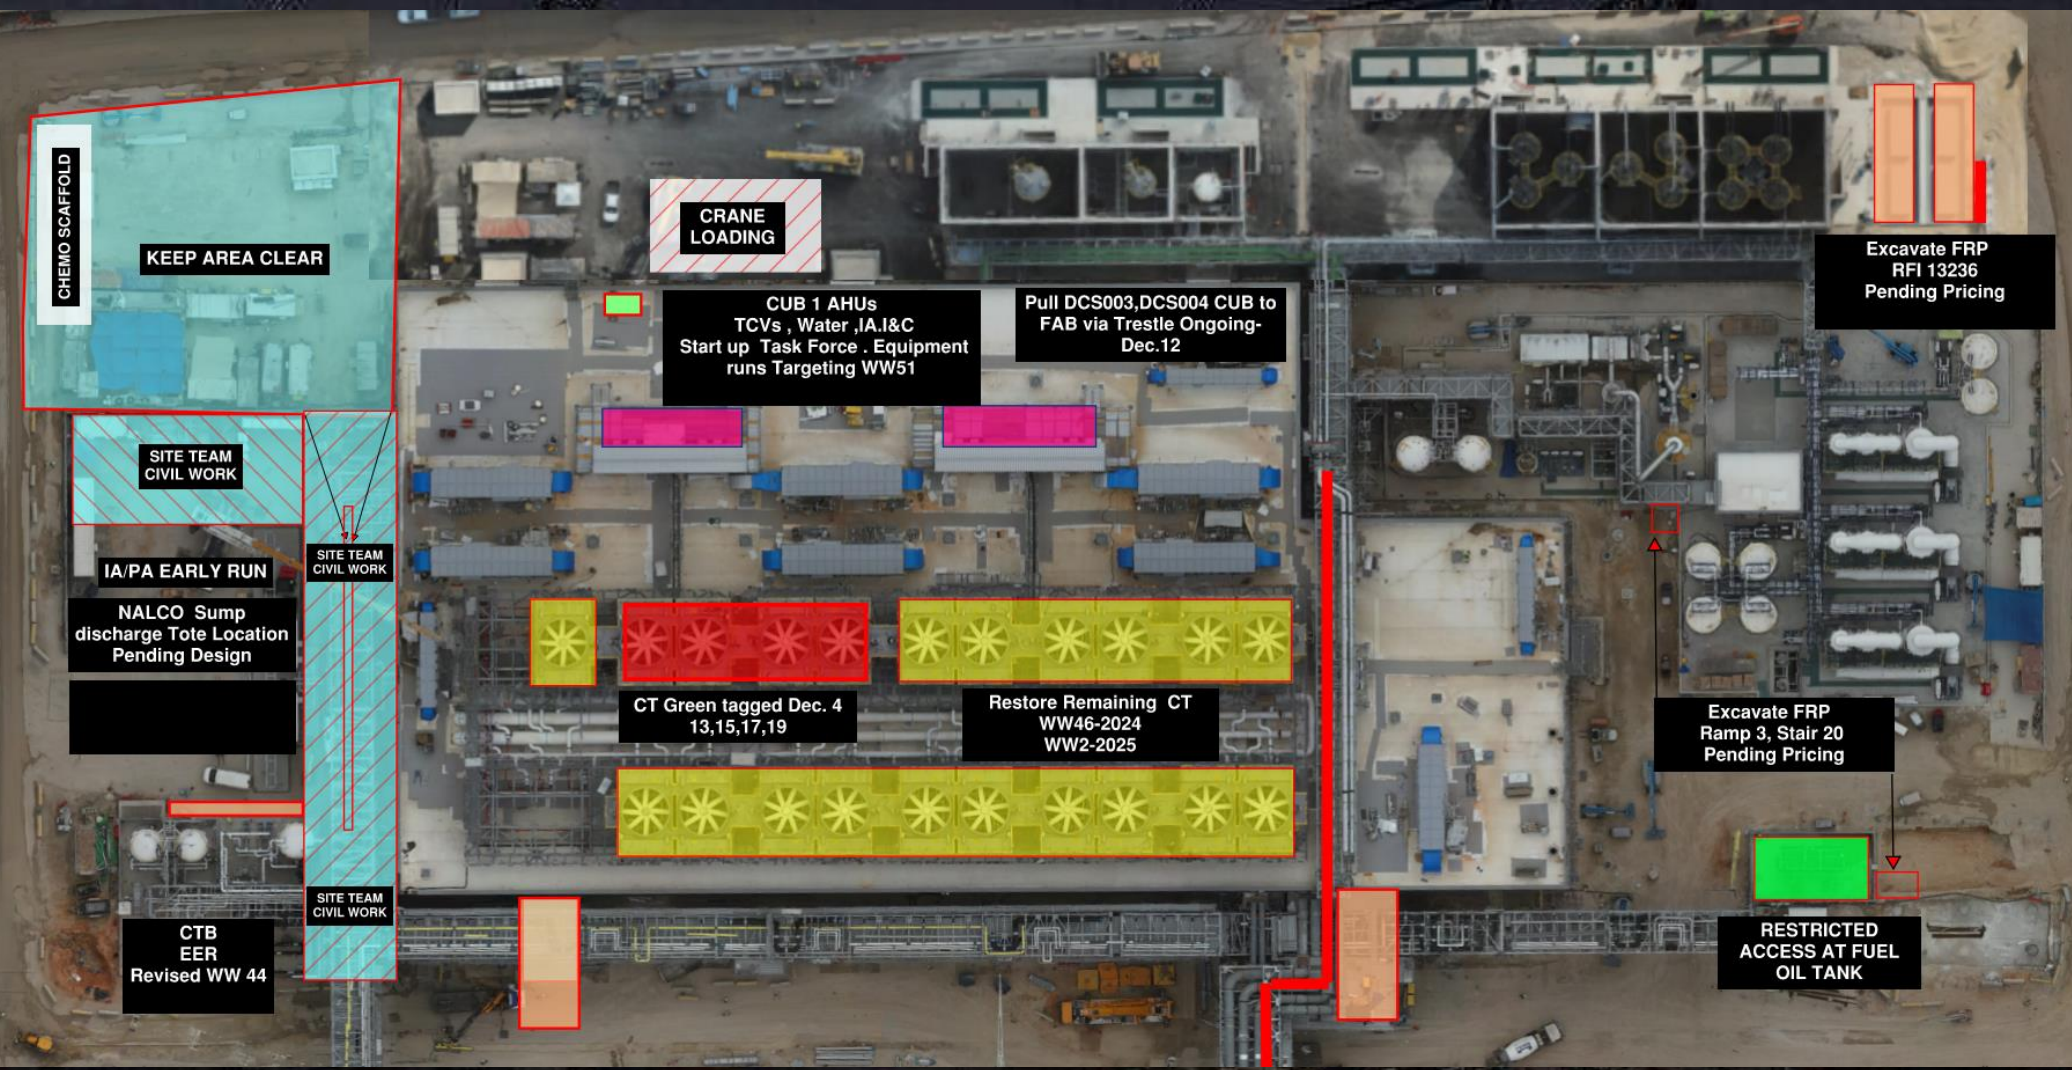





CUB 2- Load in and H&T

CUB 2 COORDINATION MAP

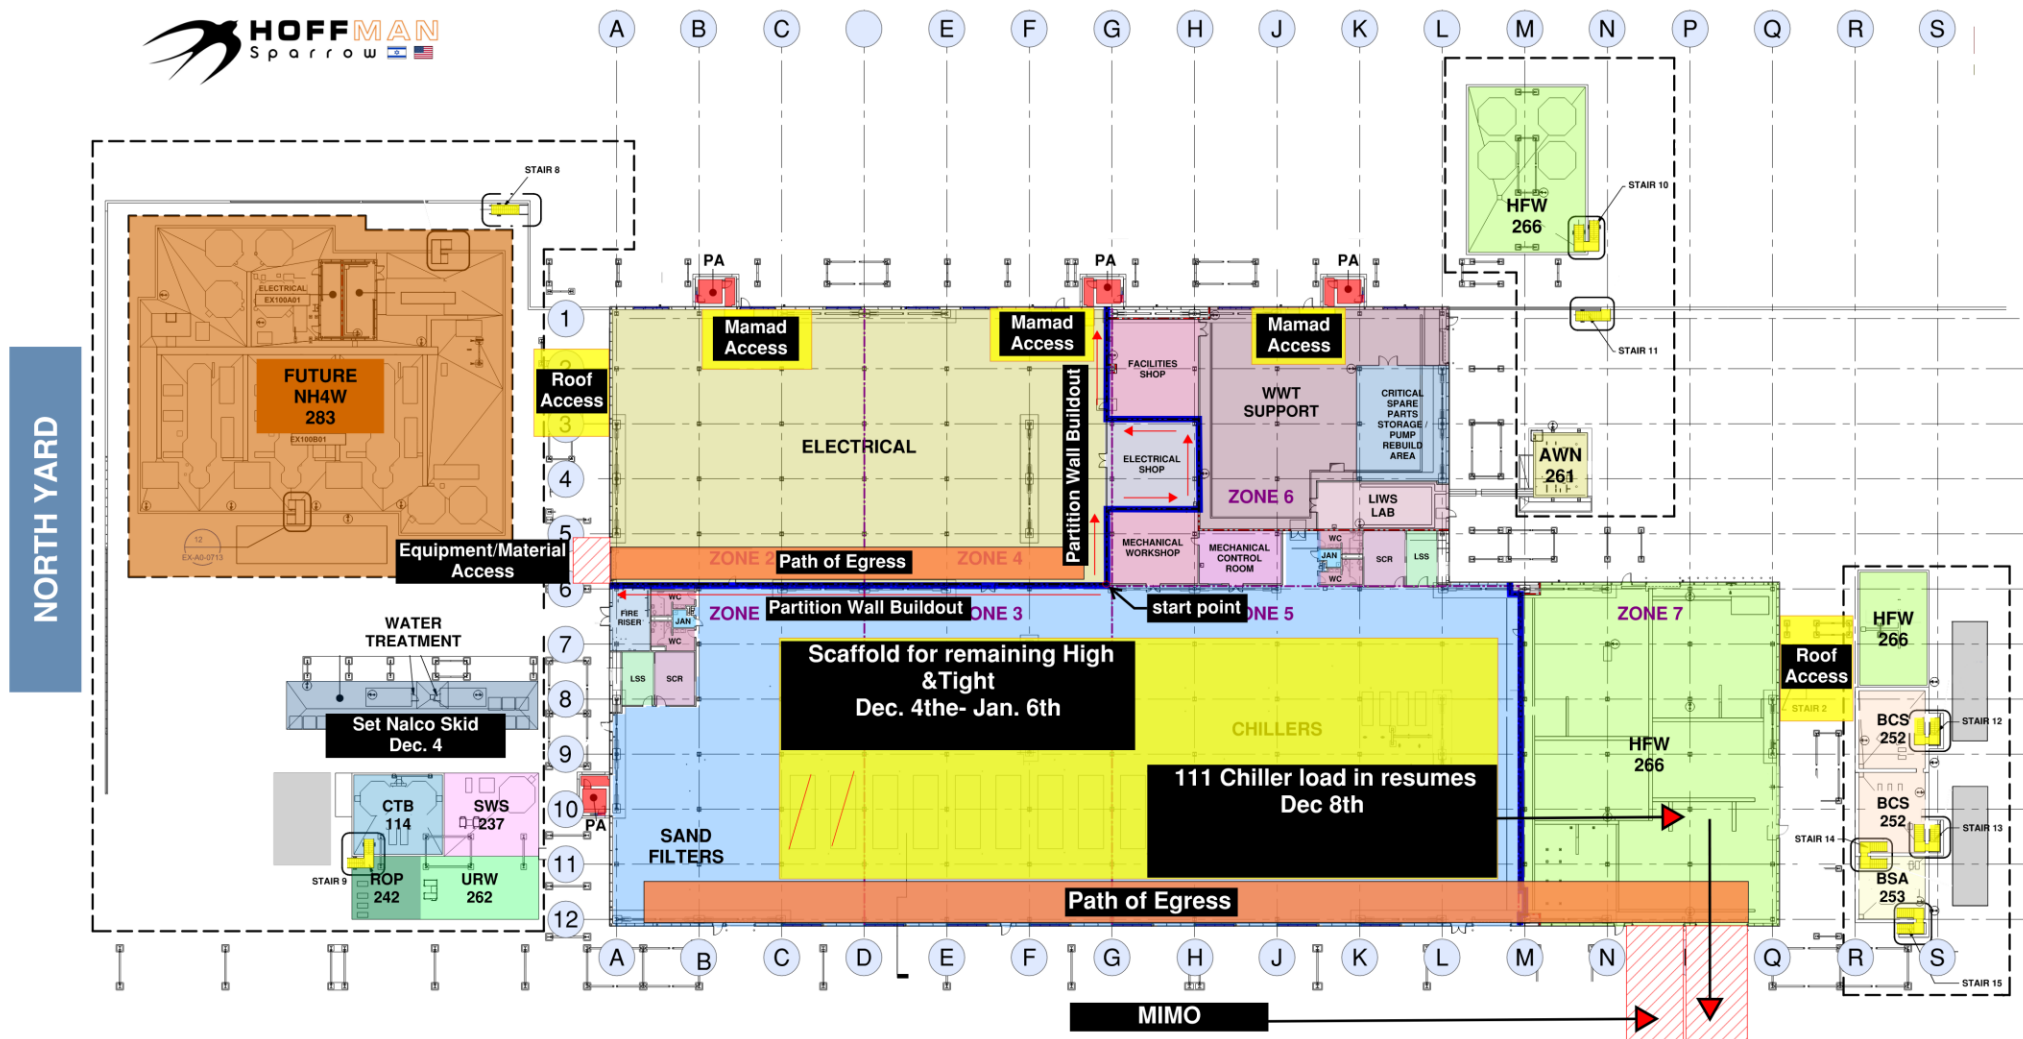


CUB 2 – EXTERIOR/ROOF

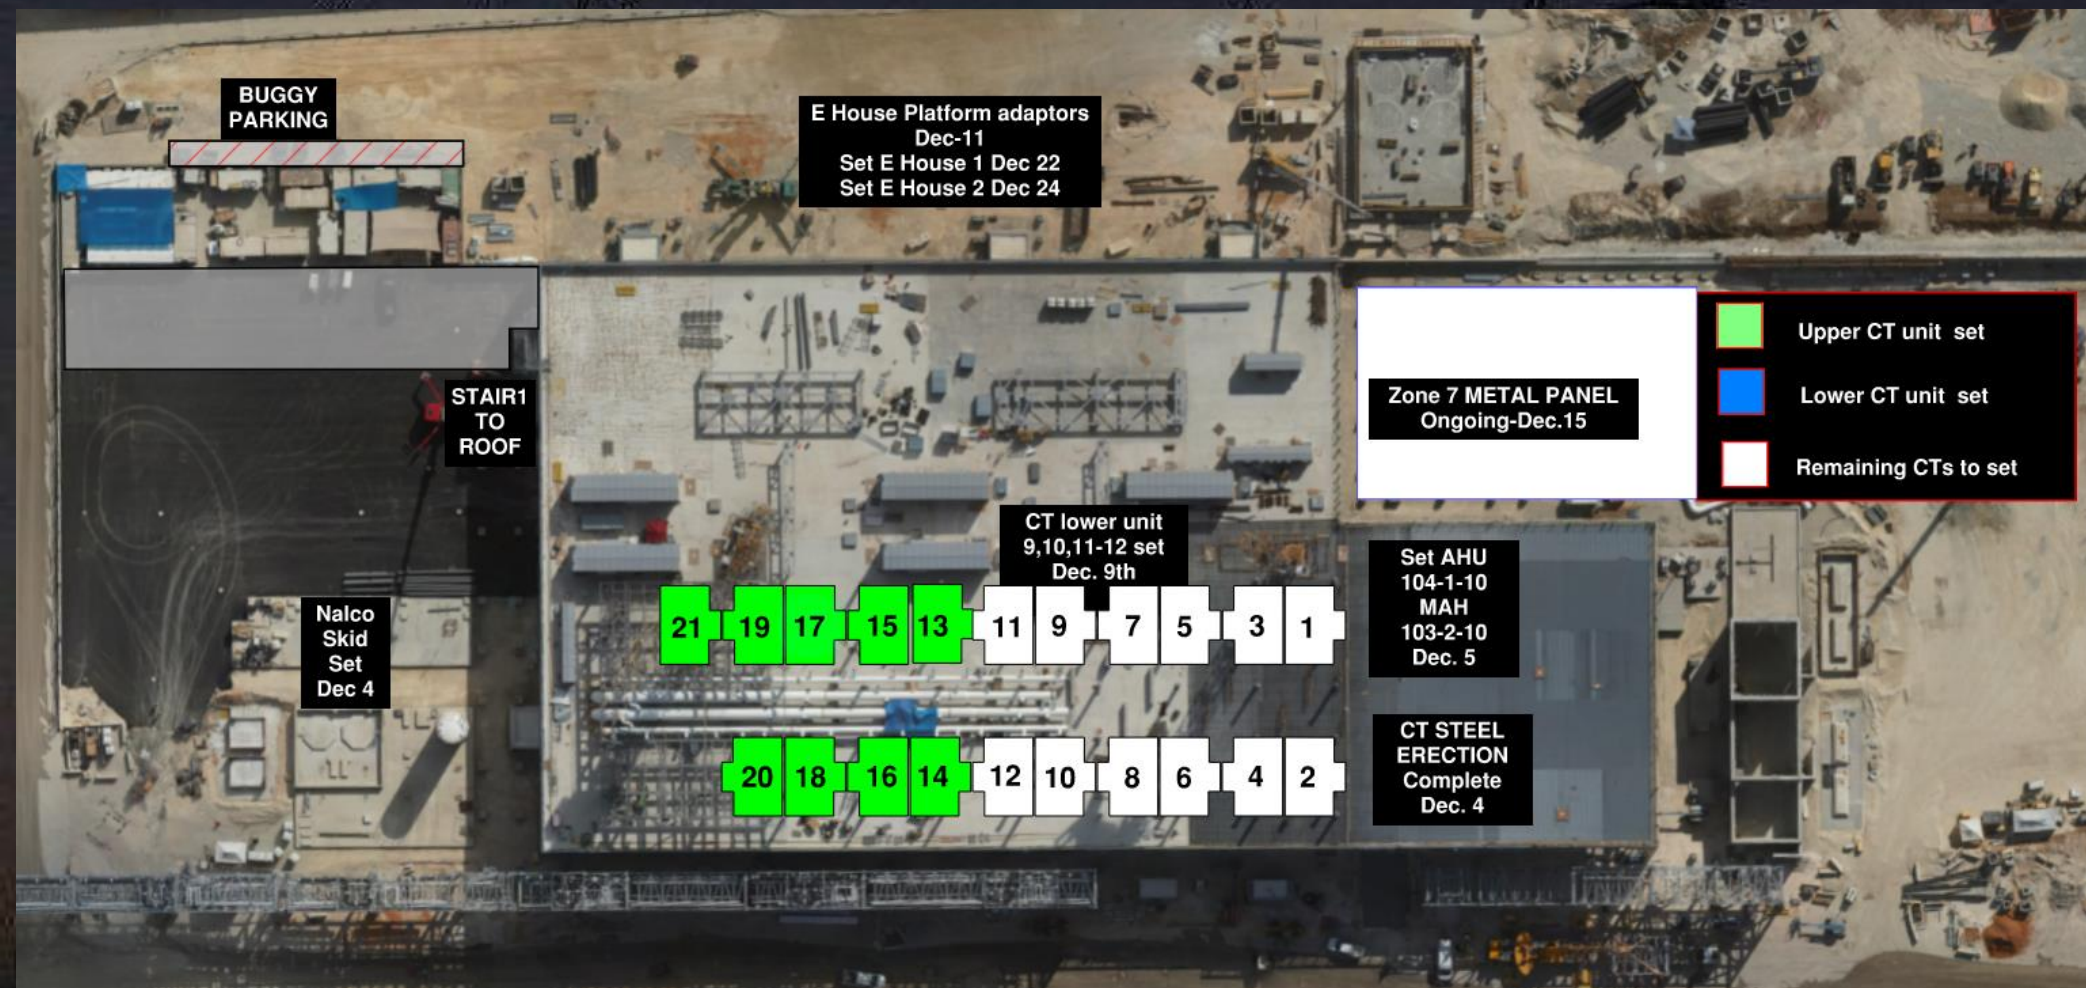



GIS GATE
closed 29/Dec /2024





HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

T18
DEC 3th - DEC 11th

DONE



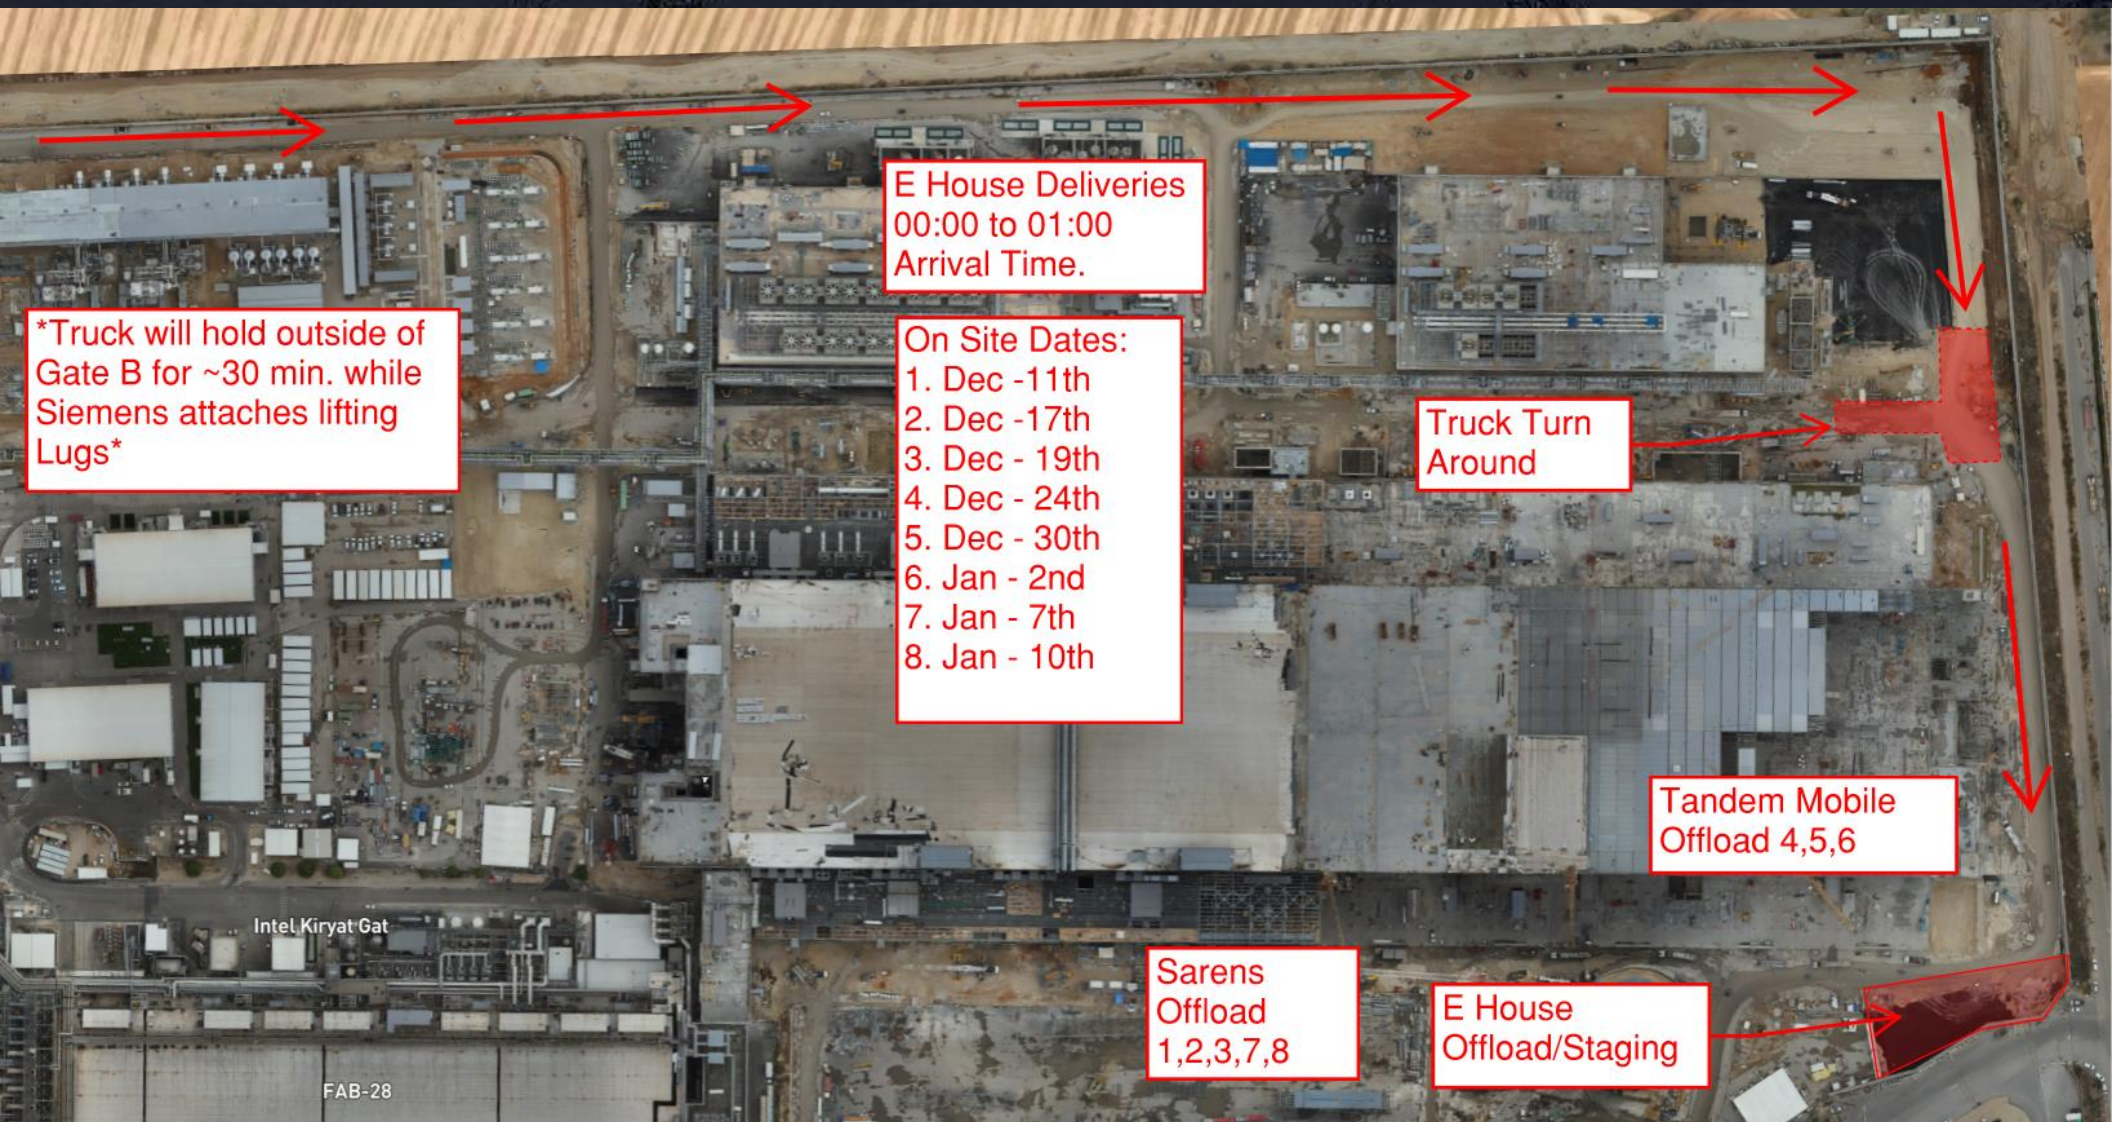

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:

1. Dec -11th
2. Dec -17th
3. Dec -19th
4. Dec -24th
5. Dec -30th
6. Jan -2nd
7. Jan -7th
8. Jan -10th

Truck Turn
Around

Tandem Mobile
Offload 4,5,6

Sarens
Offload
1,2,3,7,8

E House
Offload/Staging

*Truck will hold outside of
Gate B for ~30 min. while
Siemens attaches lifting
Lugs*

Intel Kiryat Gat


FAB-28



Daily Coordination Meeting

Site Logistics


North

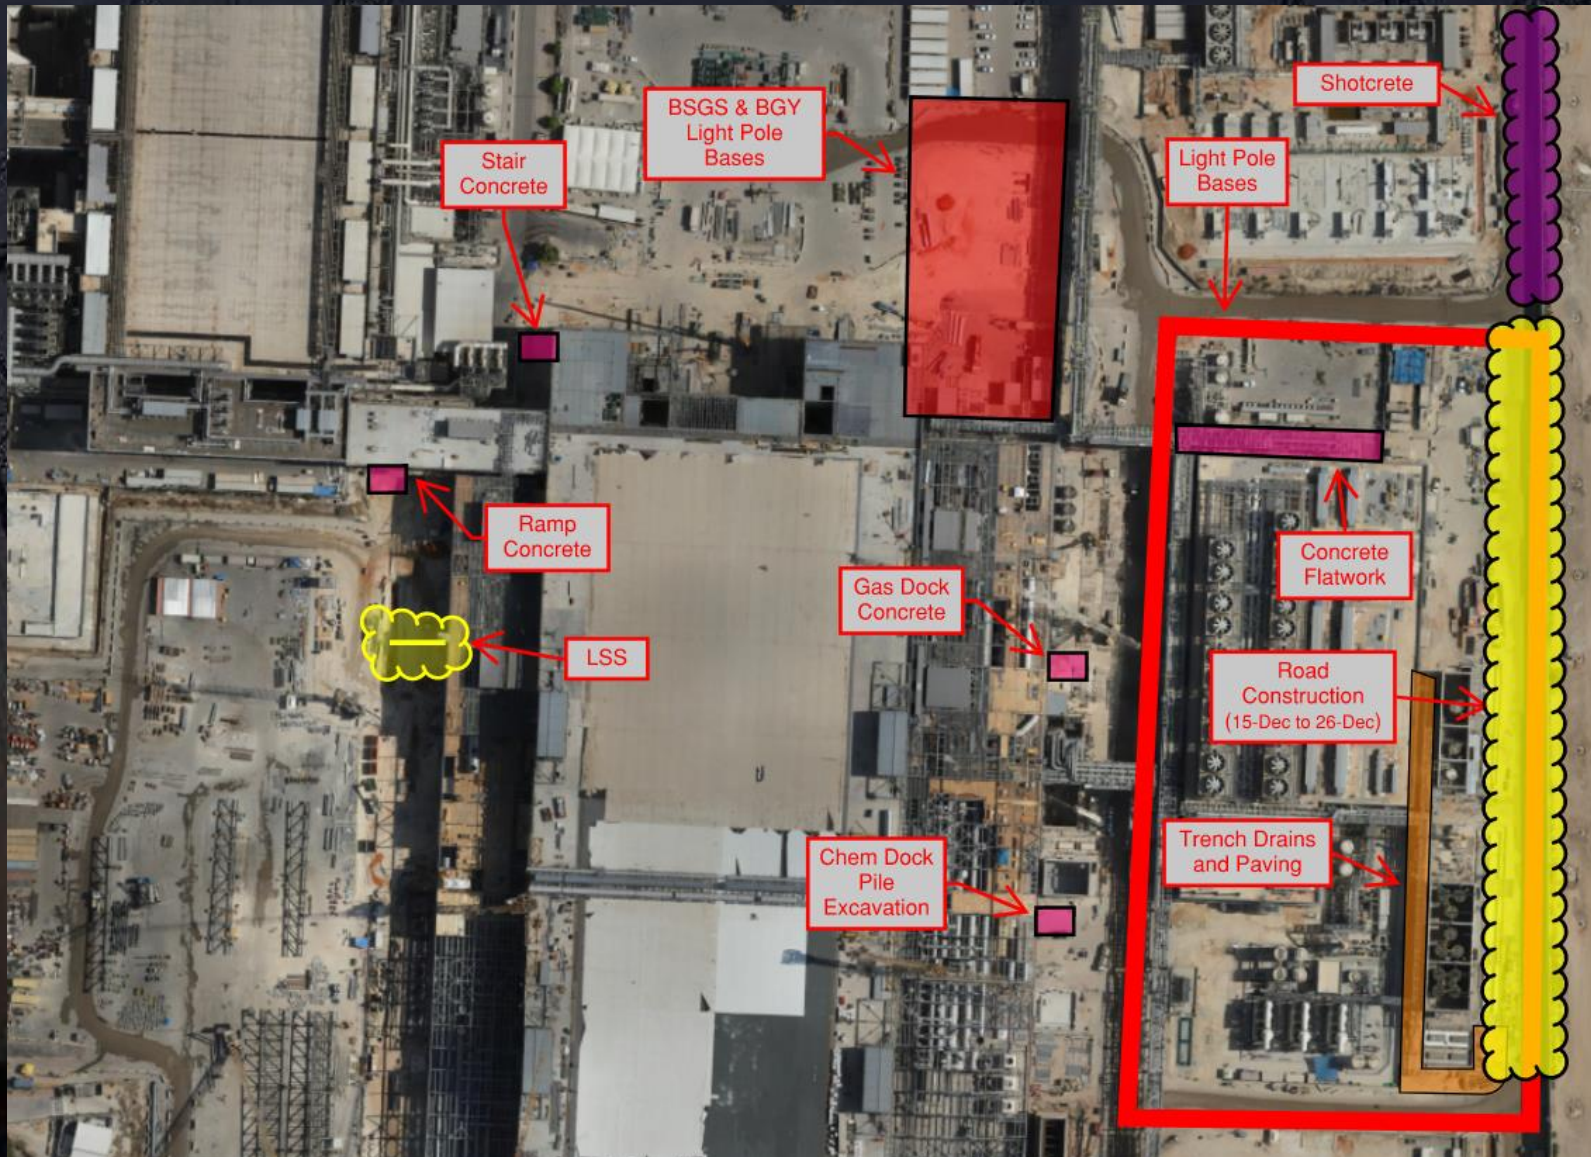

Daily Coordination Meeting

Site Logistics


East CUB1 Road Closure

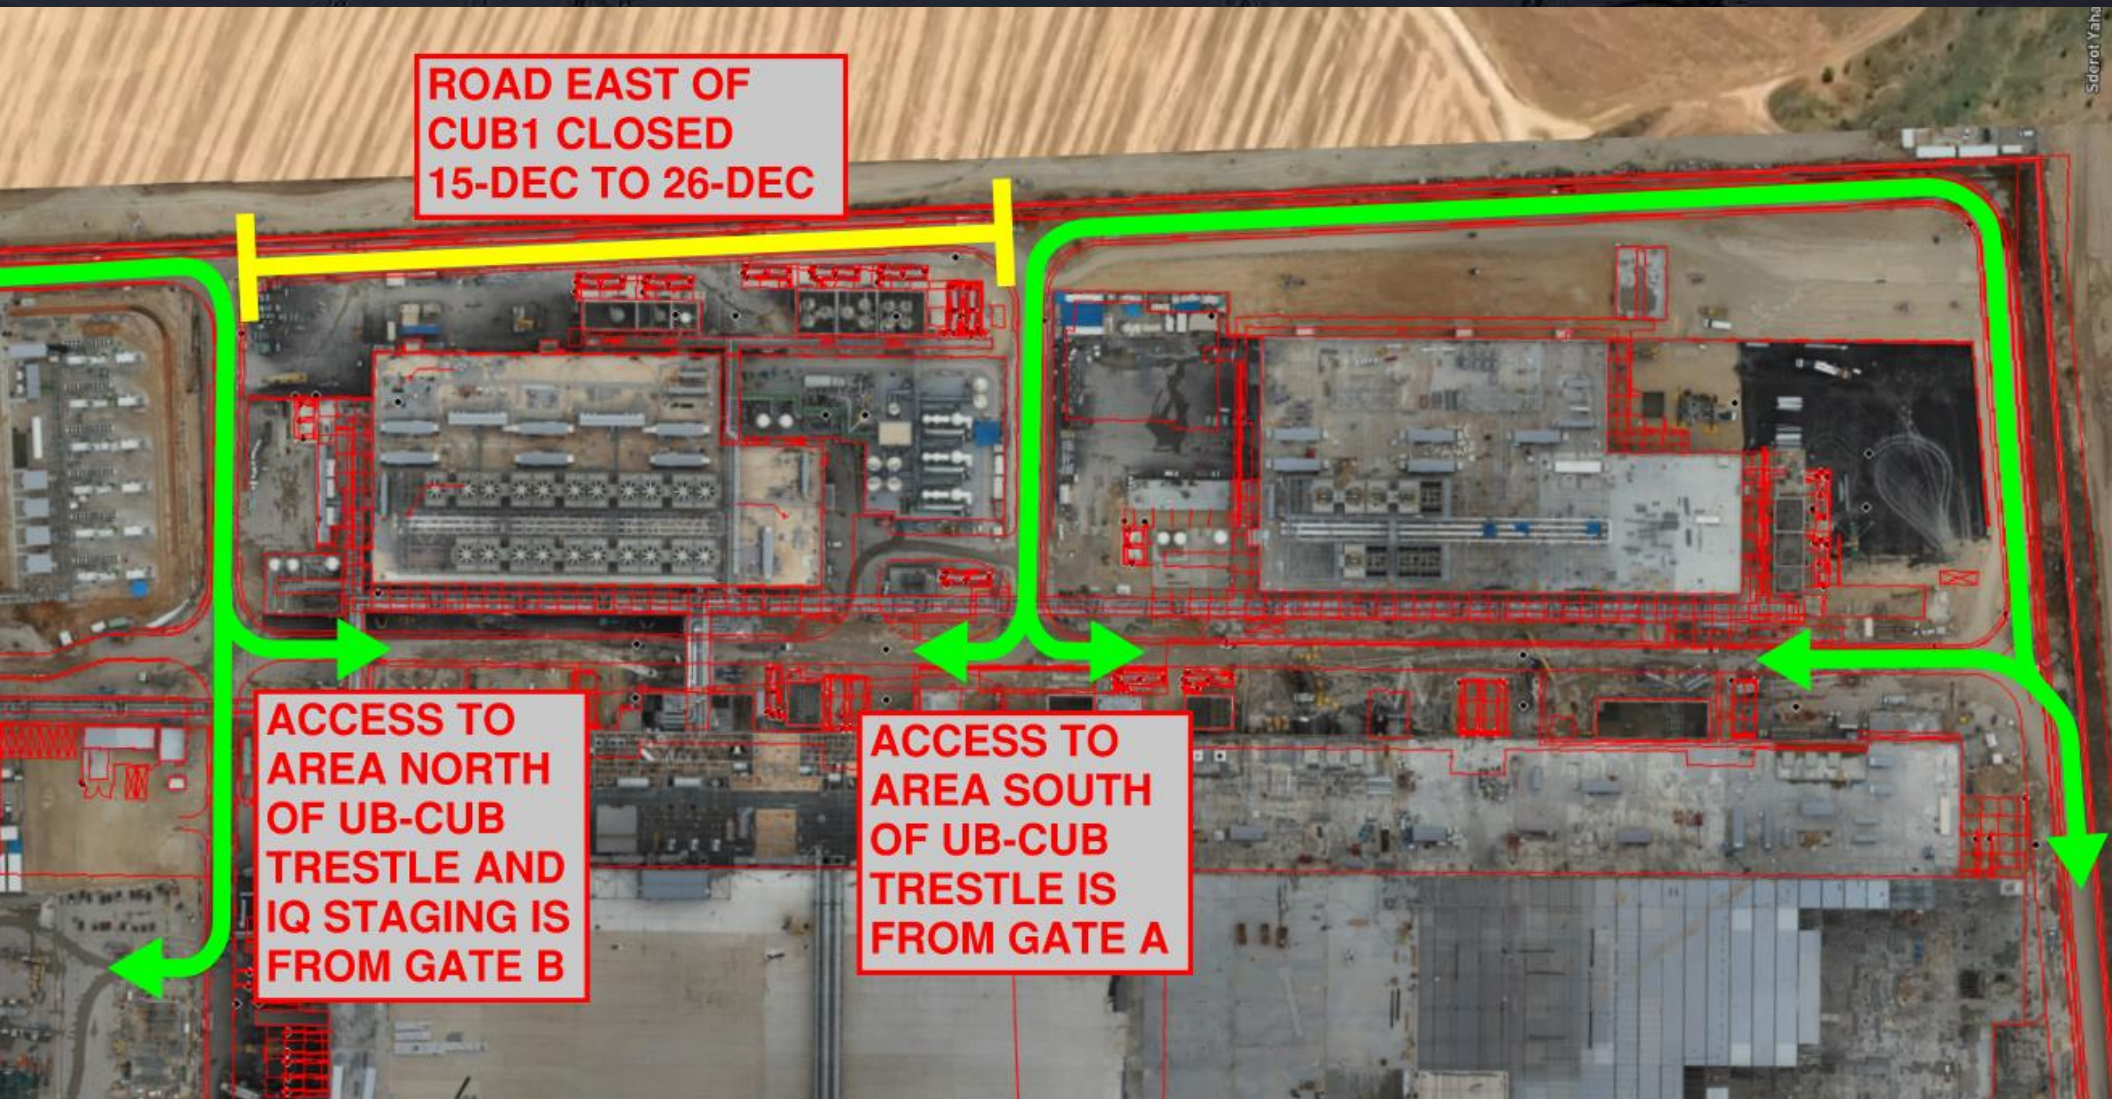

Daily Coordination Meeting


Site Logistics


South

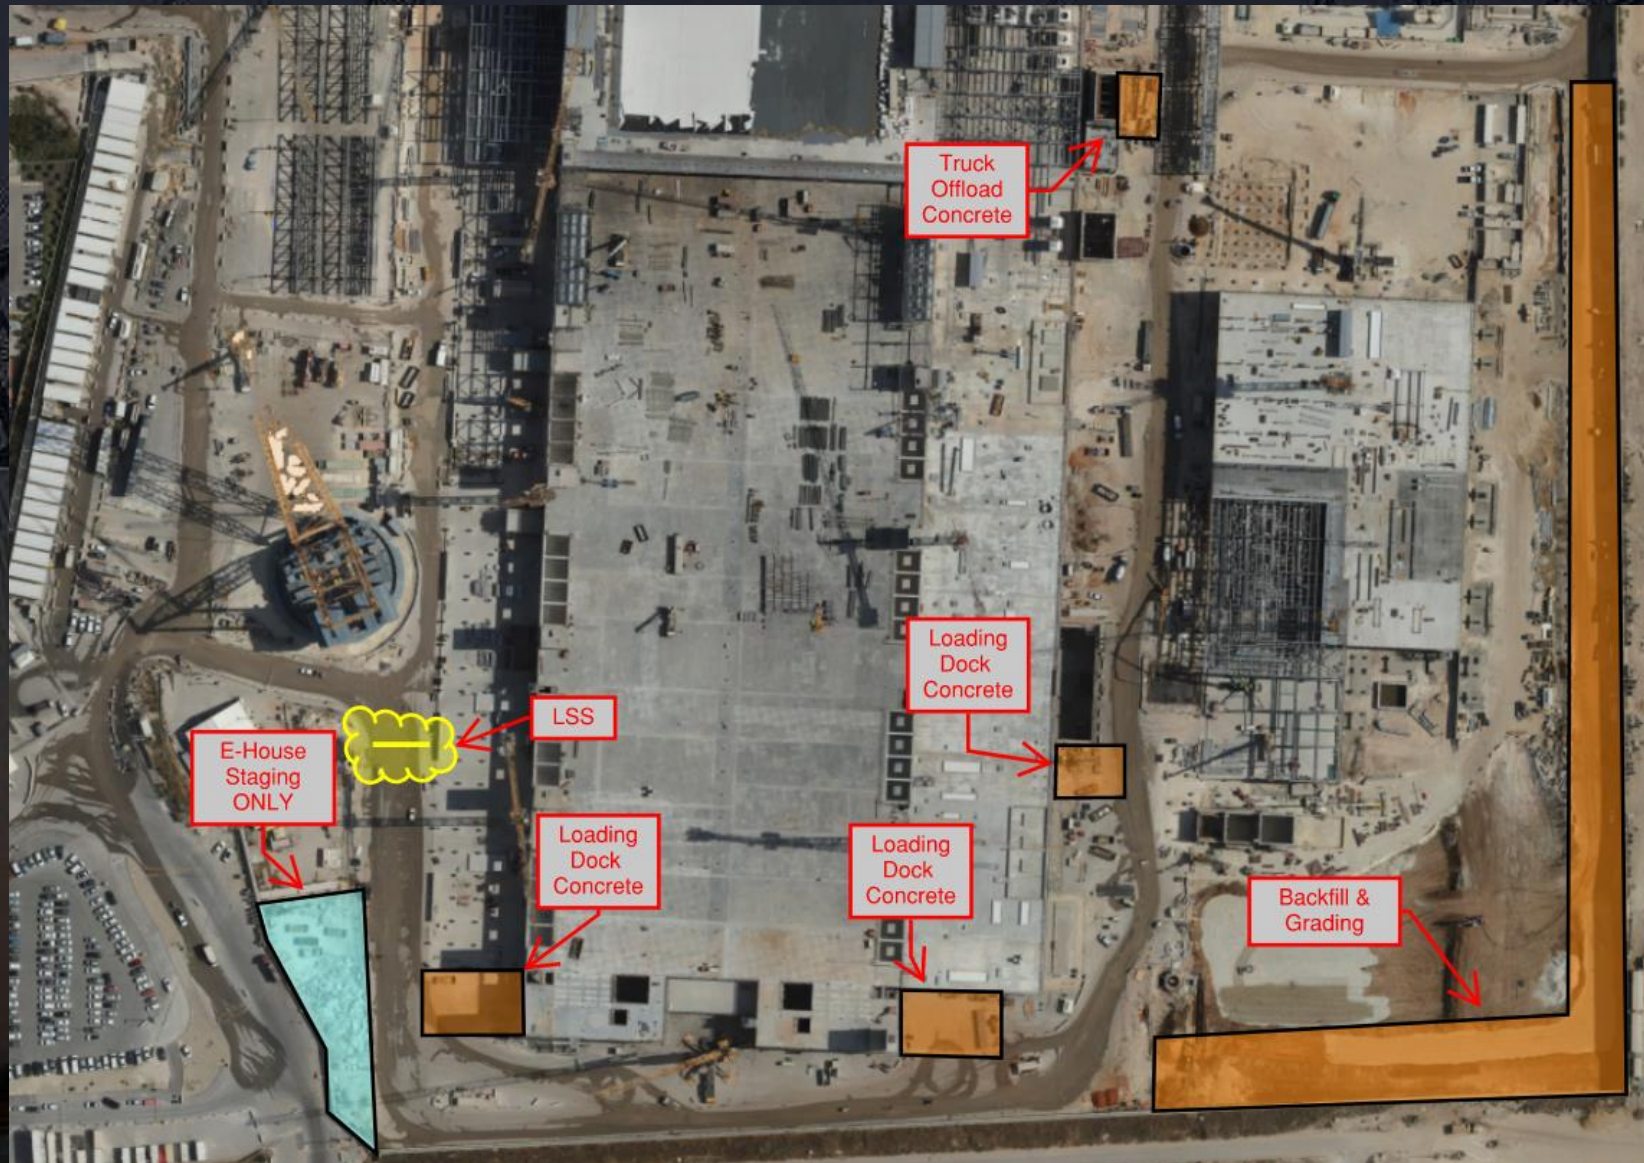



Fall protection swing fall hazards

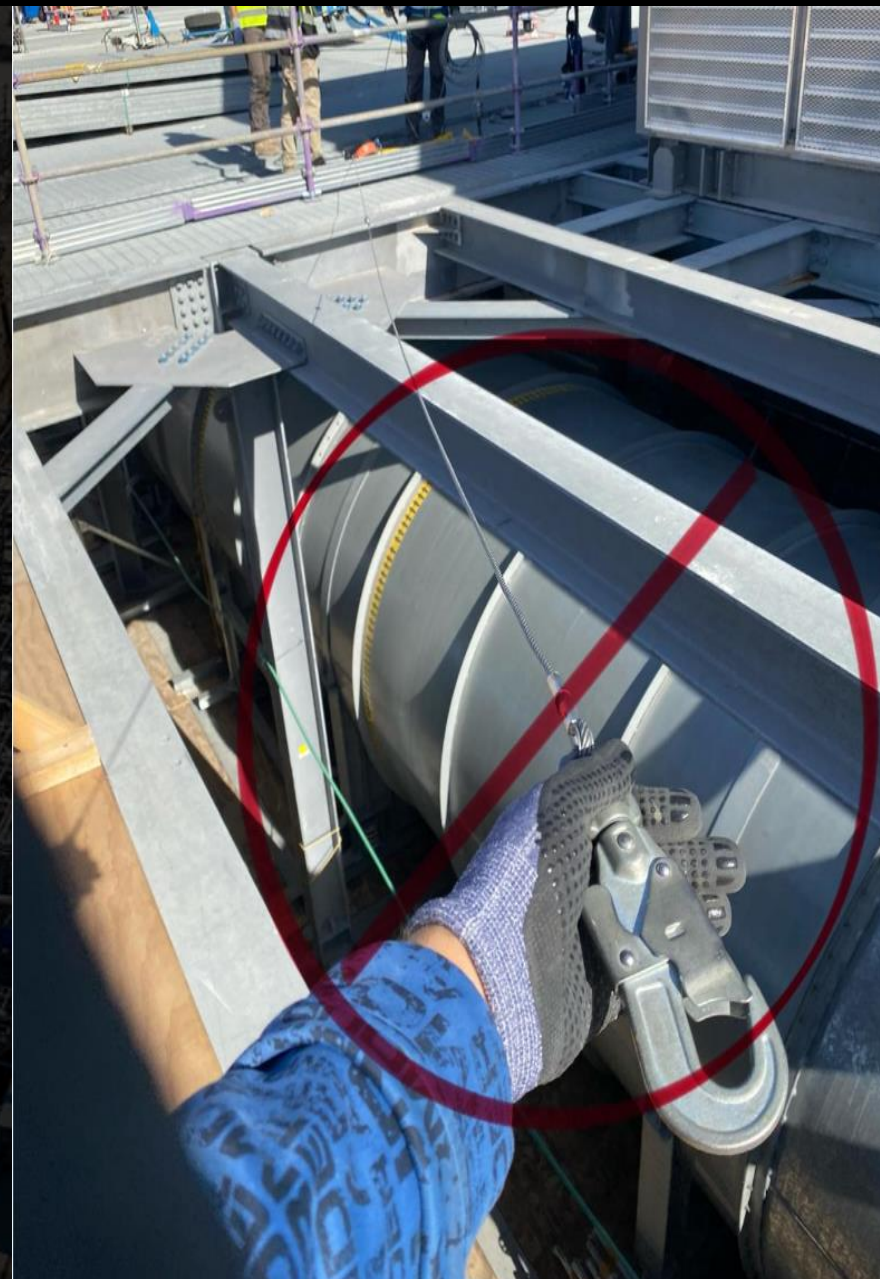

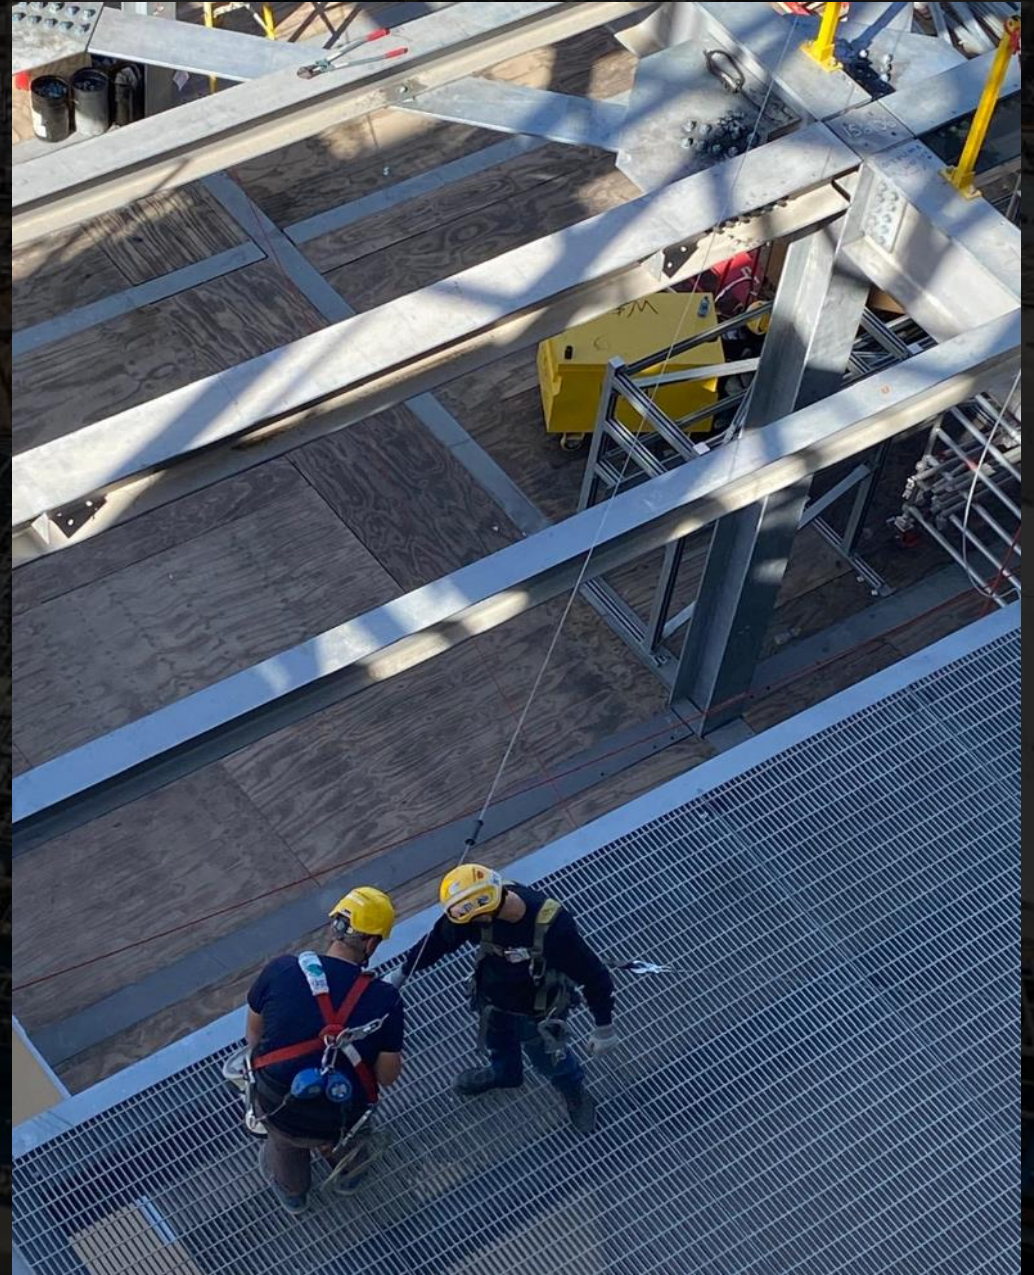

Daily Coordination Meeting



14:00 Sign In
