

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting



General Topics:

- Little things matter- get out in the field.
- MEWP use- not even trying.

UTILITY LEVEL MOD1

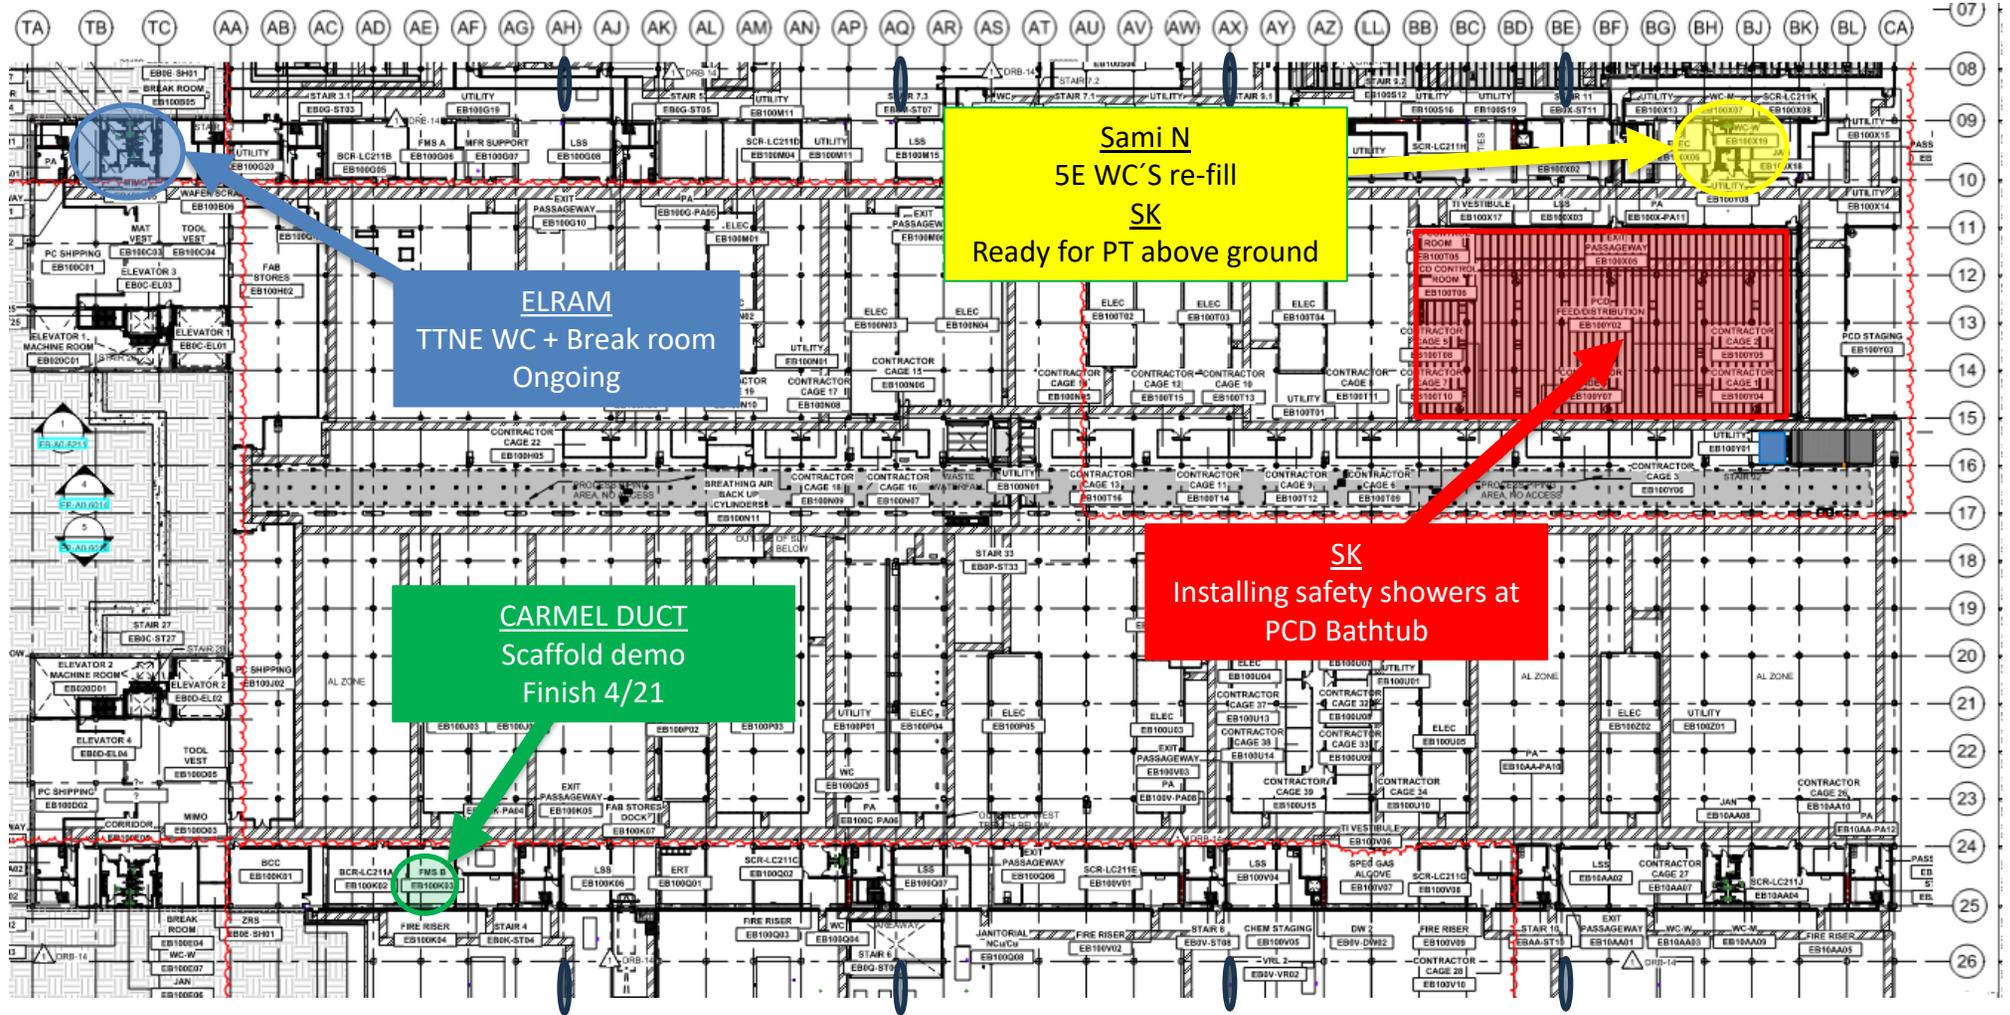

SUT 38.1 LEVEL

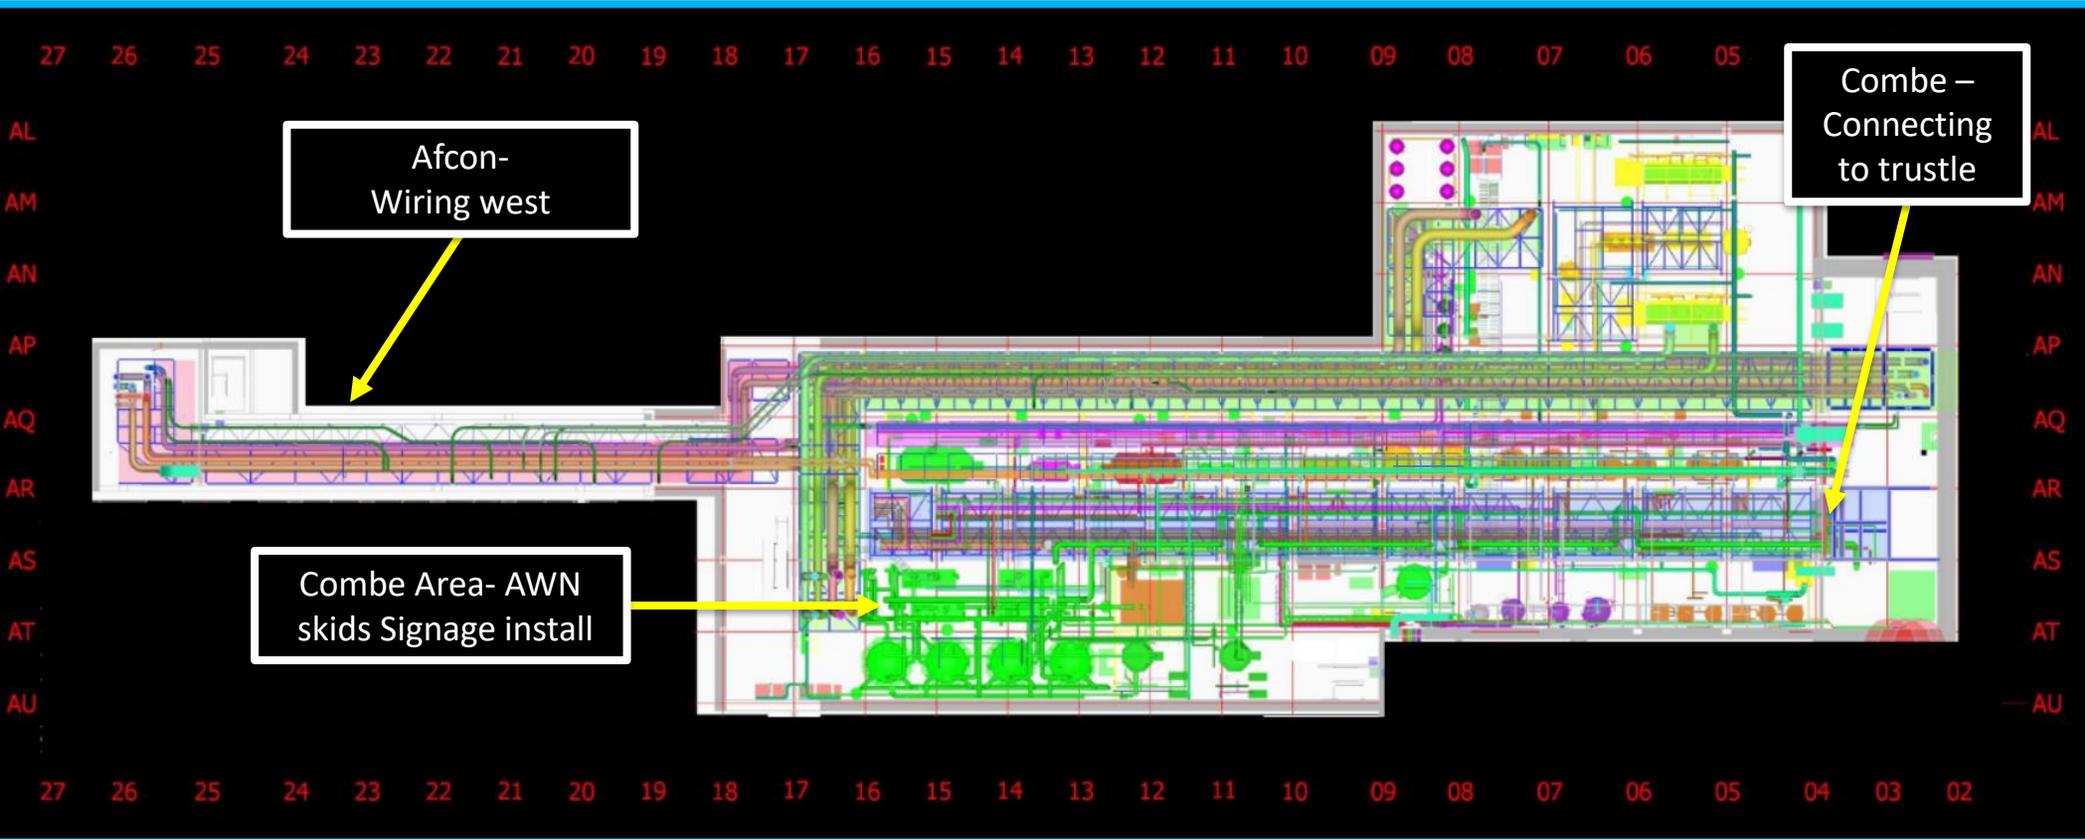





**Evacuate materials not enough !!!
On Wednesday 23 th
Job service cleanup & evacuate
unapproved materials to the dumpster**







SUBFAB BUILDOUT MOD 1

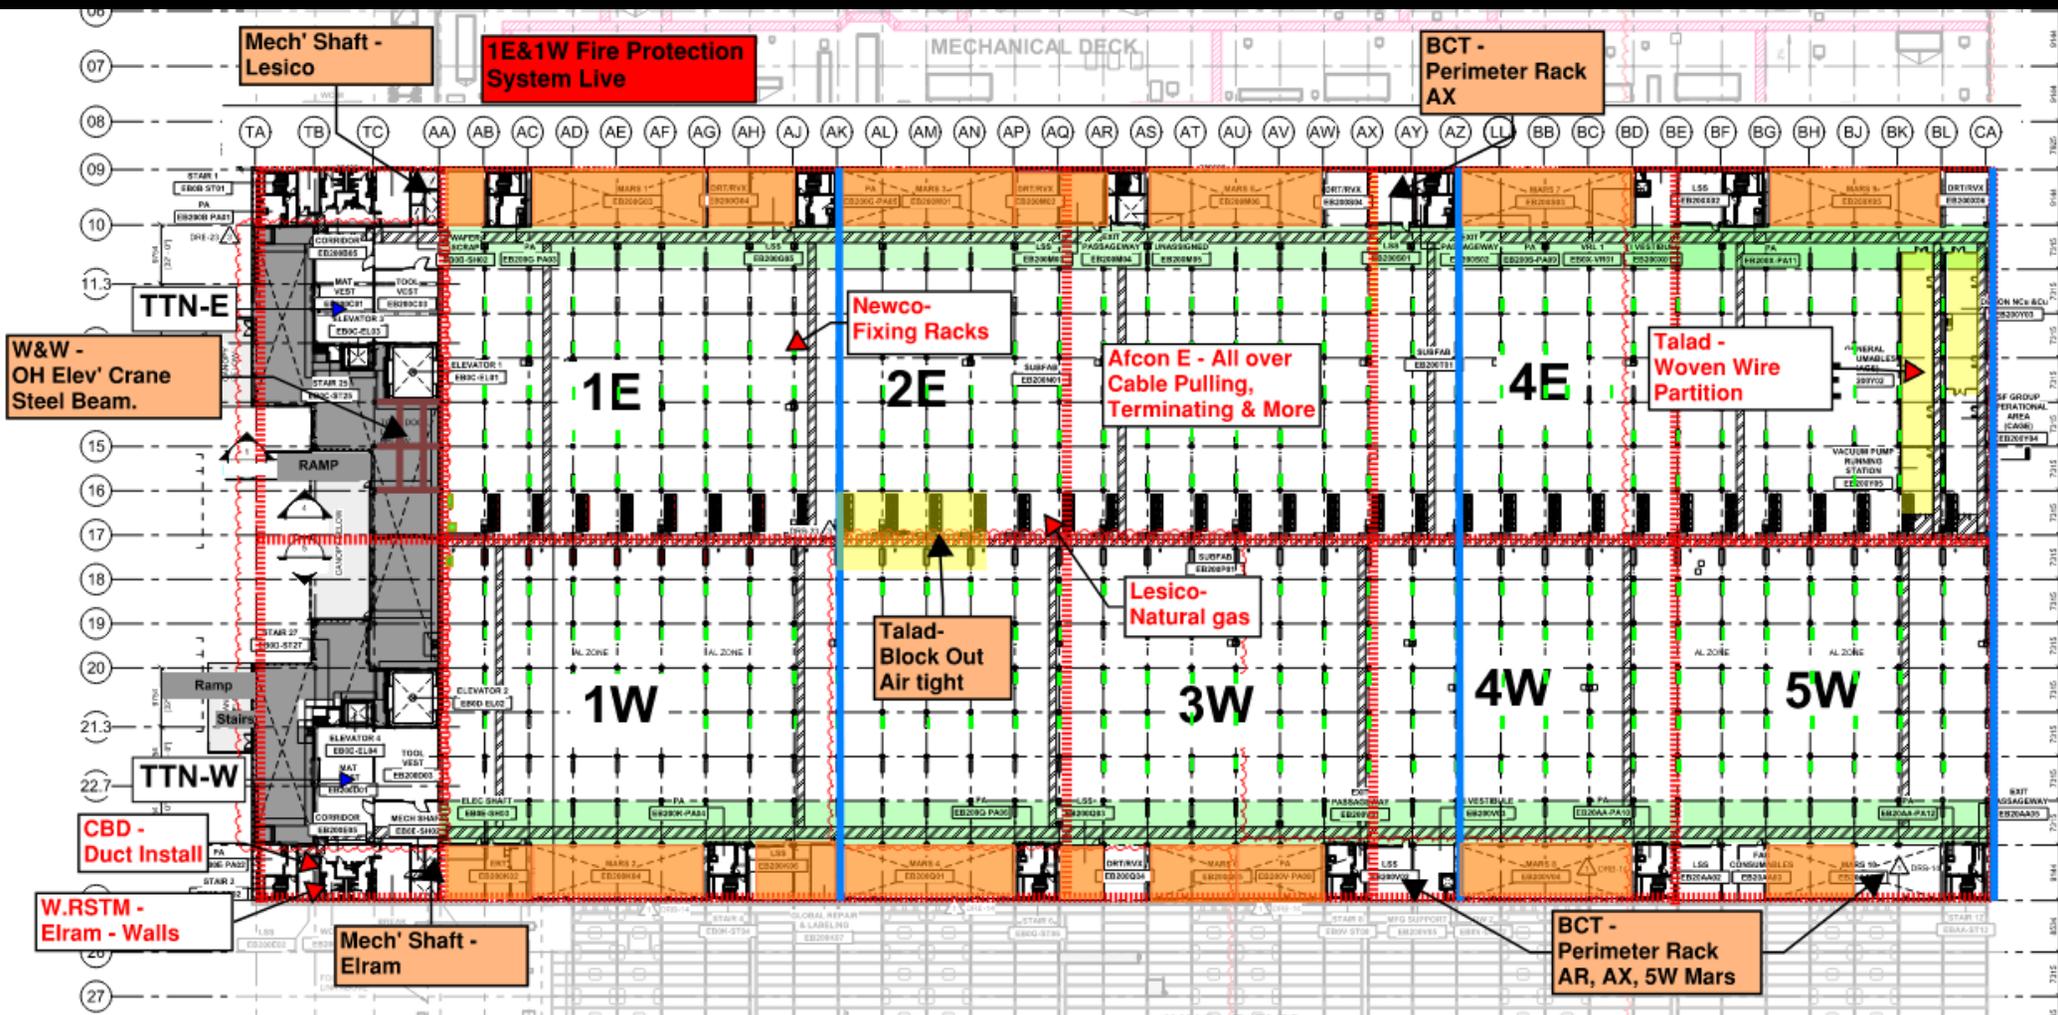

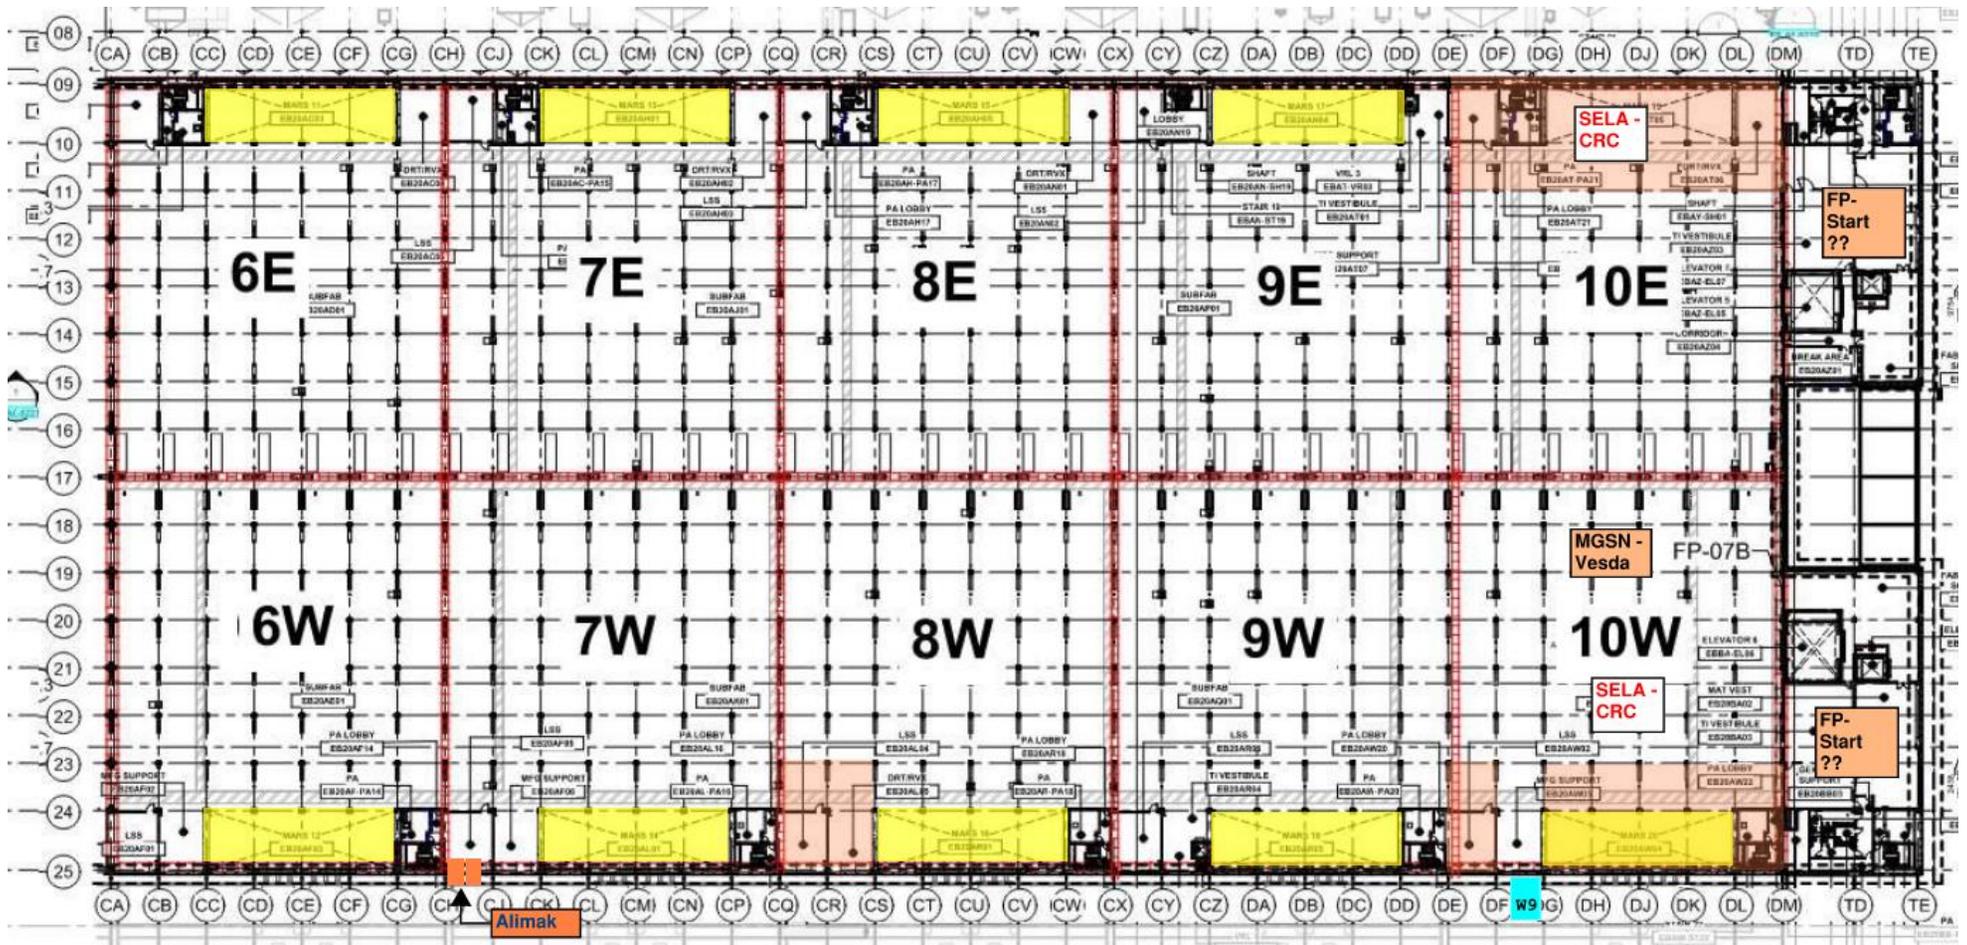



CR level
60% All equipments/tools should be wiped down before entering the area PL03
Stairs 6,8 and 9 closed CR-Int. level

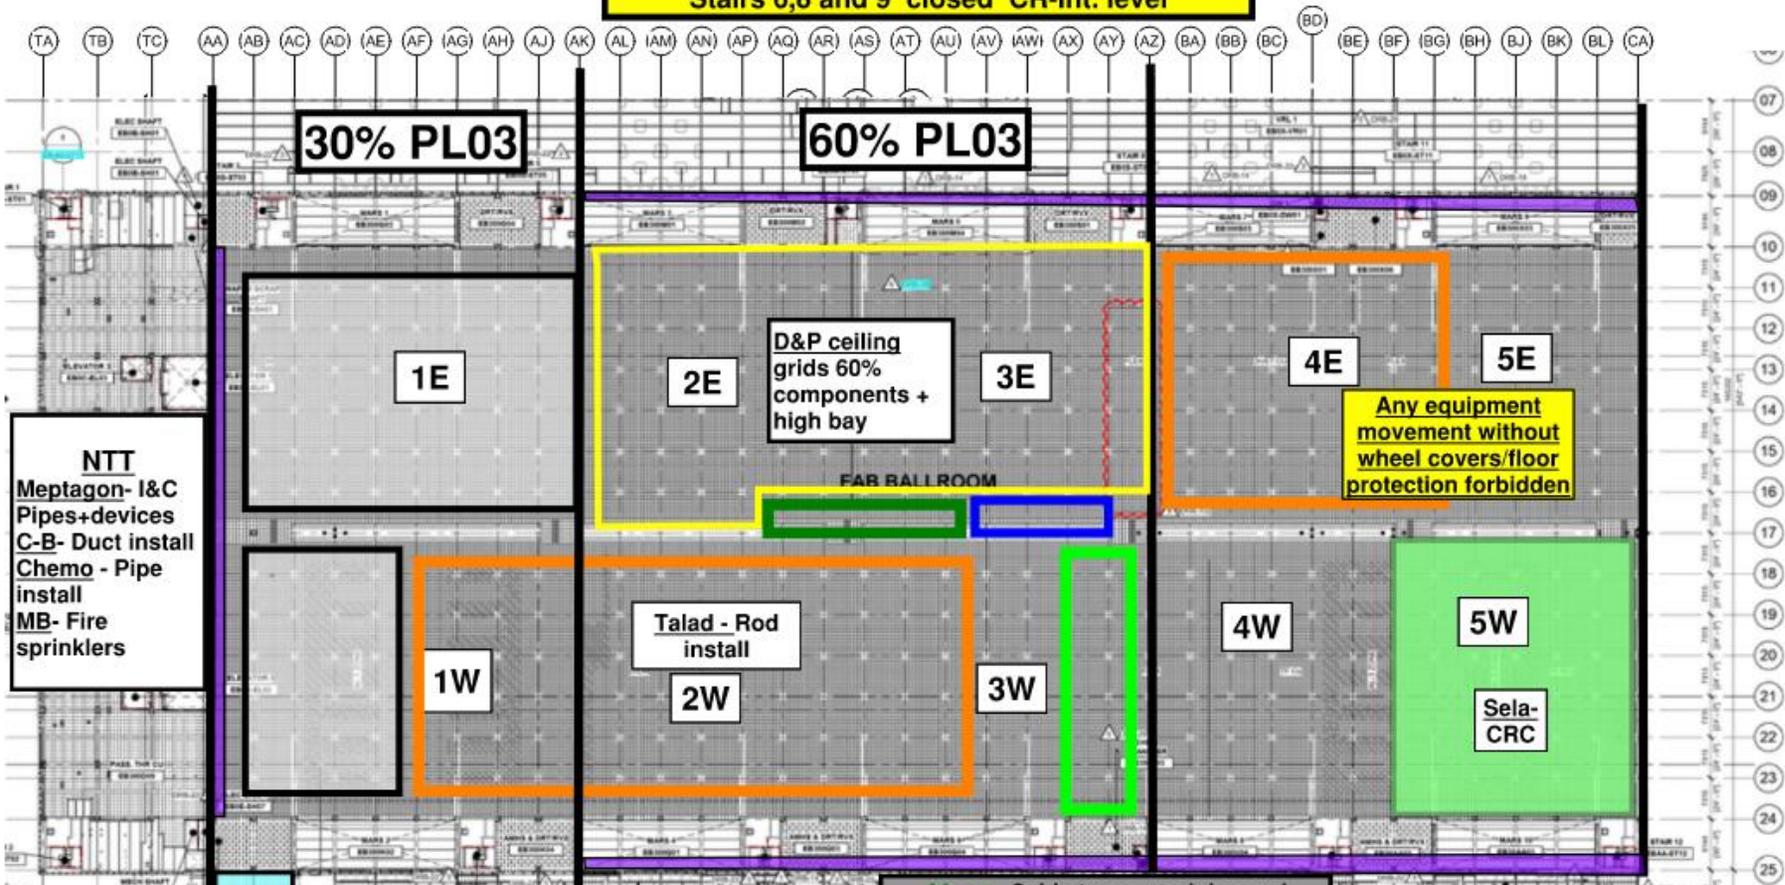

30% PL03

60% PL03

1E

2E

3E

4E

5E

D&P ceiling grids 60% components + high bay

Any equipment movement without wheel covers/floor protection forbidden

FAB BALL ROOM

NTT
Meptagon- I&C Pipes+devices
C-B- Duct install
Chemo - Pipe install
MB- Fire sprinklers

1W

Talad - Rod install

2W

3W


4W

5W

Sela-CRC

Link
SIG- Scaffold green tagged
D&P - Holes drolling
P-T- Duct work
Afcon- Moduls+ cable pulling
Megason- Small wires


Afcon - Cable trays, modules and stickers
MB- Pipes and drops
Elram - Columns/shaft walls/G1 wall
Meptagon - I&C+ Zero ref. pipes
D&P - Stick build+ separation walls+FFU
Tzur-esh - 1W blade paint
HYG - Stairs 7.3 starts WW04
Talad - UPN install, ceiling grid, lids removal
Taves - Super clean
Taper-Tech - RMF
Bynet - Small wiers

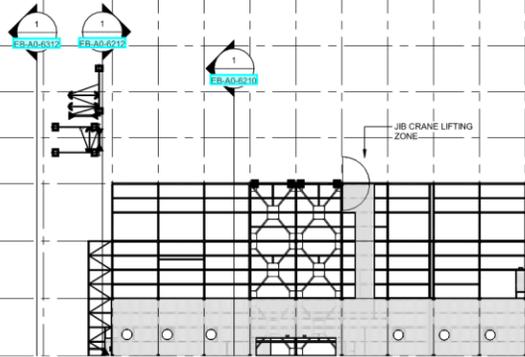

- Afcon** - Cable trays, modules and stickers
- MB** - Fire sprinklers
- EIram** - Gypsum/G1 wall
- Chemo** - Skids and pipes
- SK** - IA pipes
- Tzur-esh** - Paint+ touch ups
- WW** - Cat walk
- RPC** - 4DA/5DA FP
- Tavas** - Super clean
- Bynet** - Communication weirs
- Megasone** - Speakers
- Meptagon** - I&C

Int. level
Walk on FRP is approved.
Do not move carts/ stage material without plywood

TA TB TC AA AB AC AD AE AF AG AH AJ AK AL AM AN AP AQ AR AS AT AU AV AW AX AY AZ BA BB BC BD BE BF BG BH BJ BK BL CA

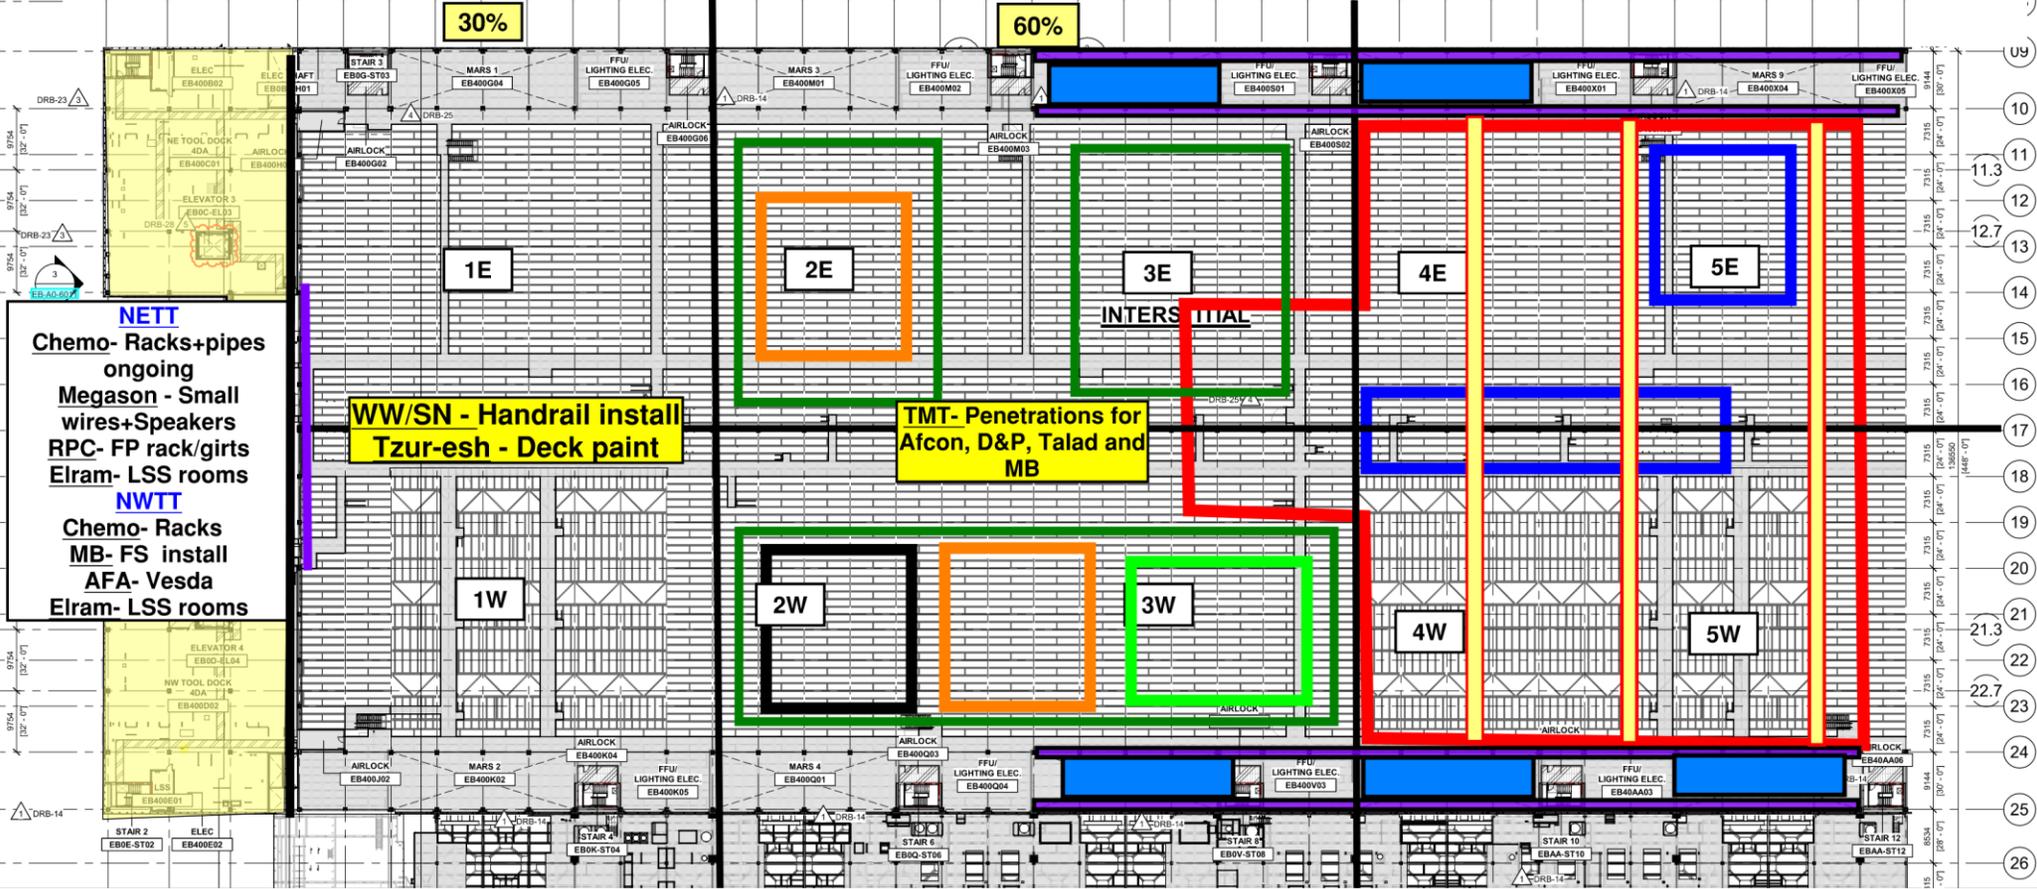

30%


60%


- NETT**
Chemo- Racks+pipes ongoing
Megason - Small wires+Speakers
RPC- FP rack/girts
EIram- LSS rooms
NWTT
Chemo- Racks
MB- FS install
AFA- Vesda
EIram- LSS rooms

WW/SN - Handrail install
Tzur-esh - Deck paint

TMT- Penetrations for Afcon, D&P, Talad and MB

01
02
03
04
05
06
07
08
09
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26

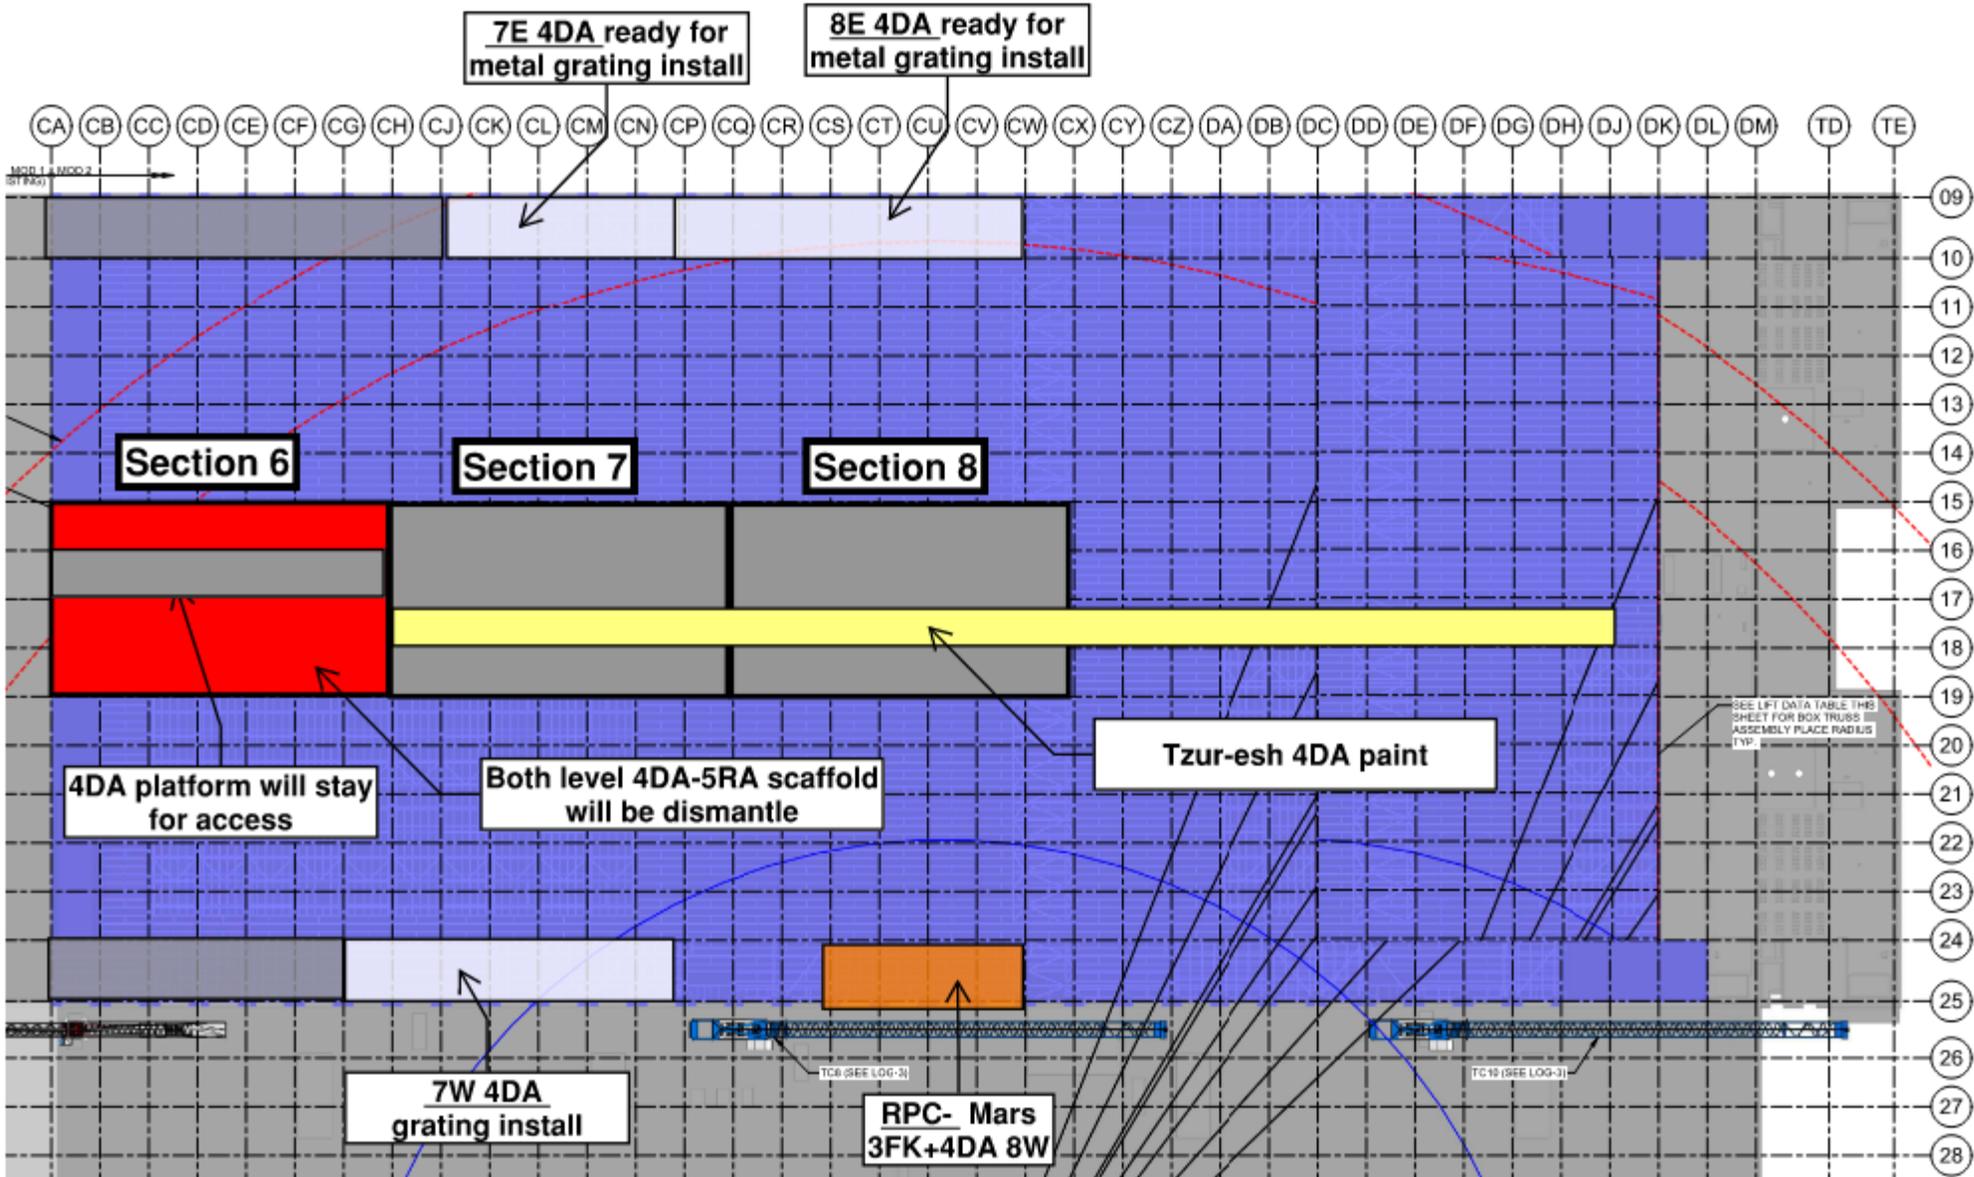

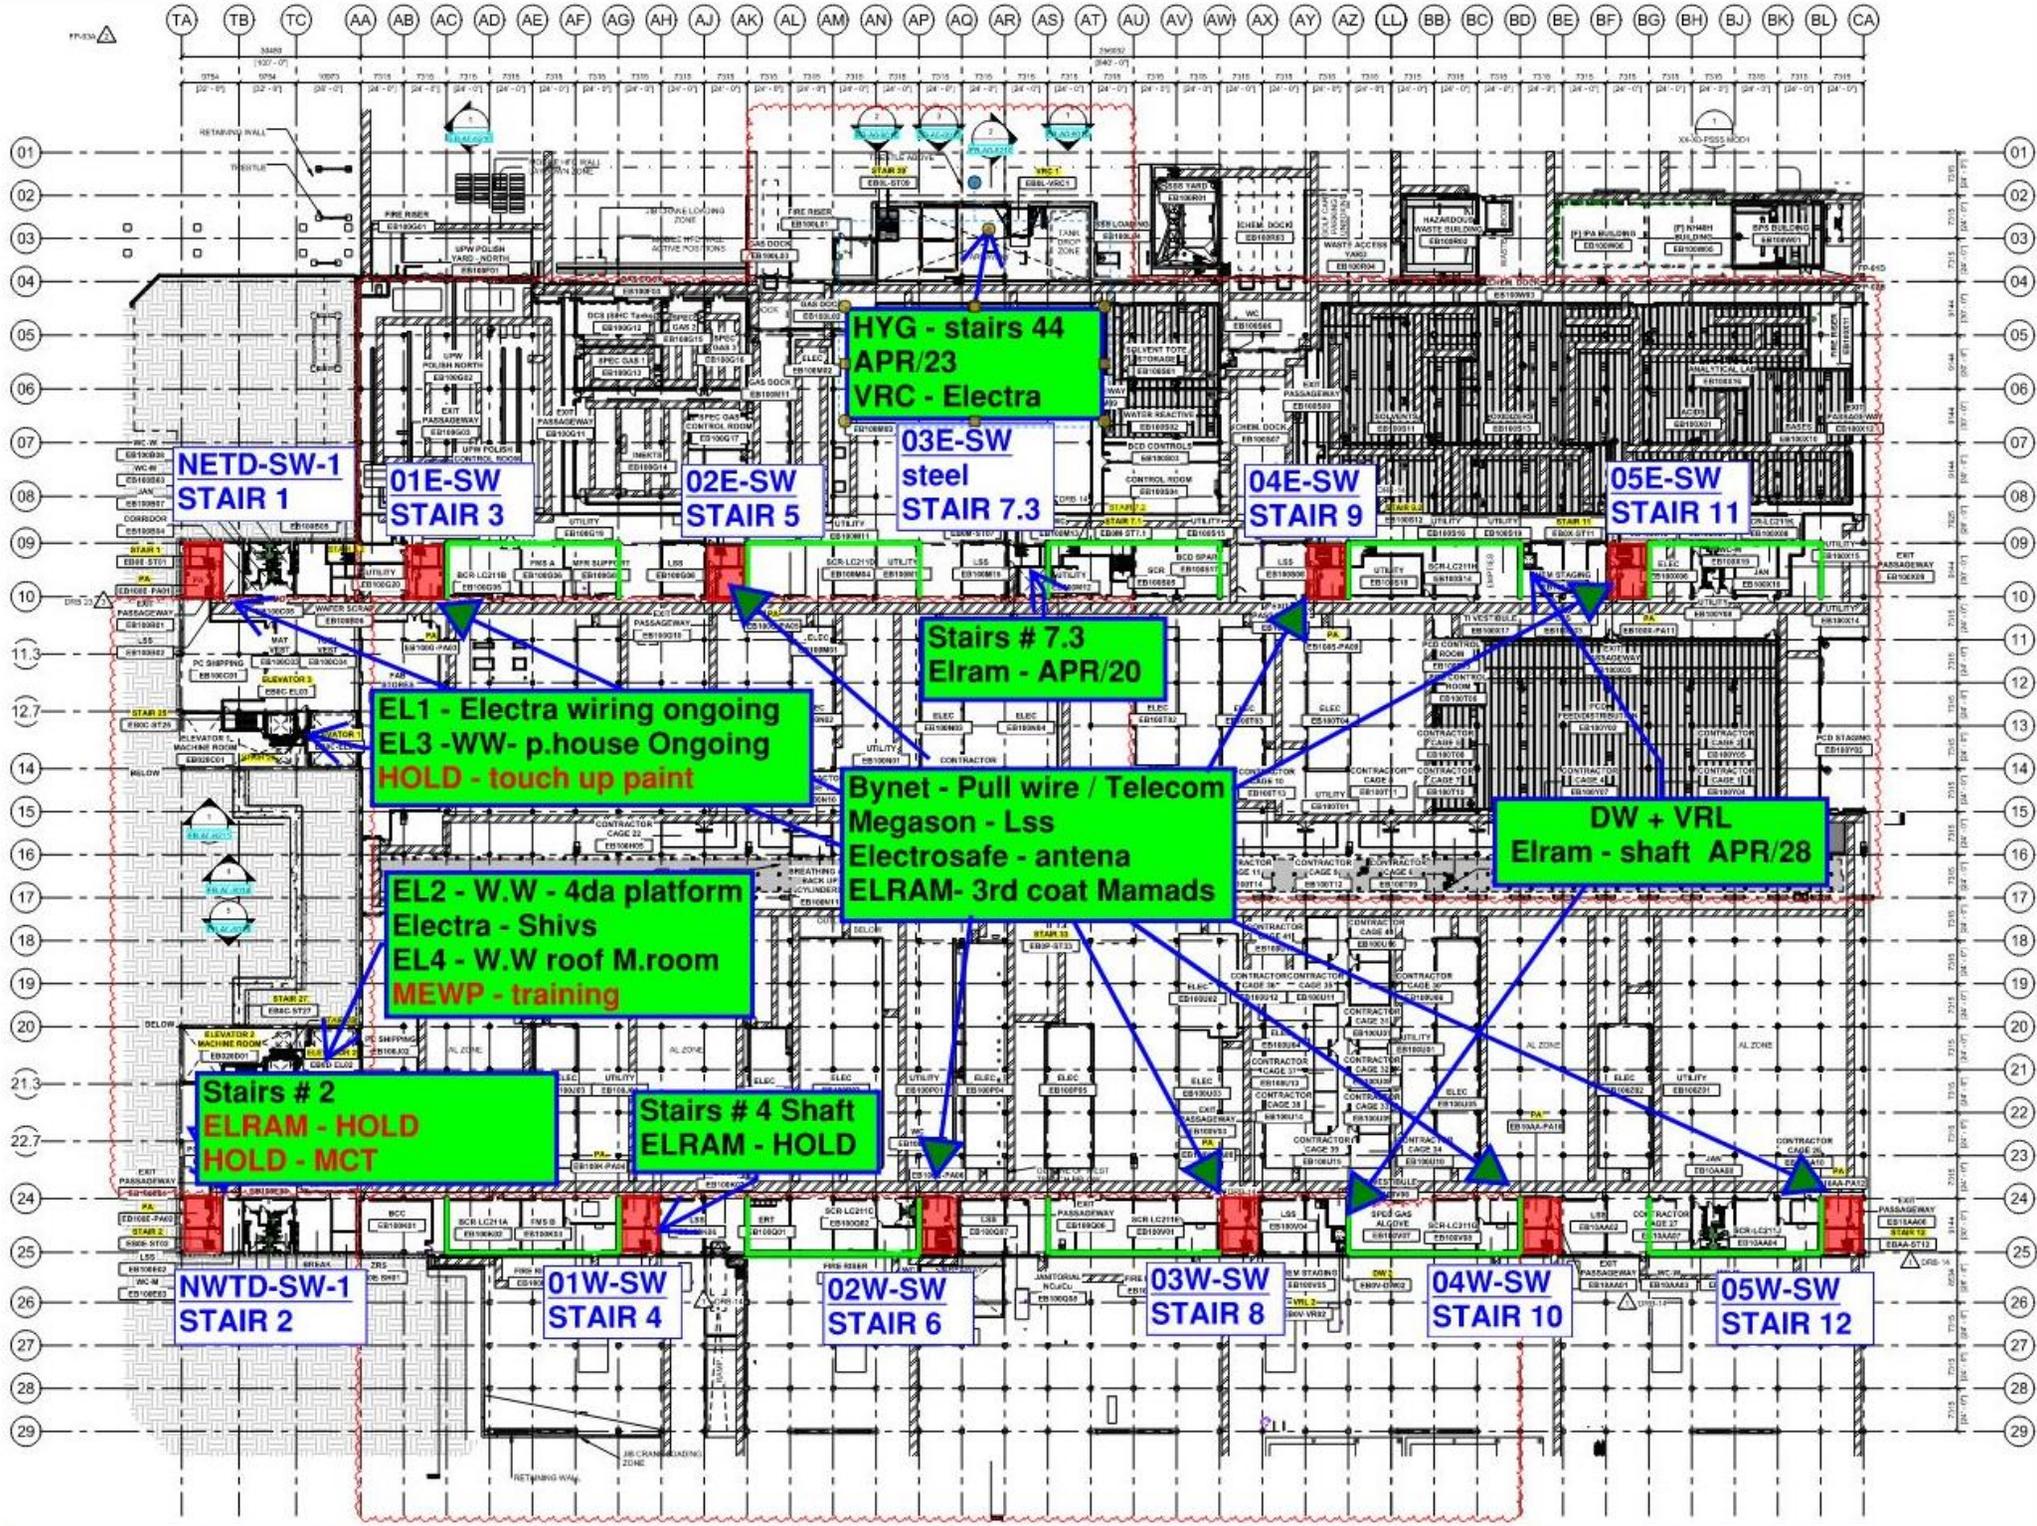

HYG - stairs 44
APR/23
VRC - Electra

03E-SW
steel
STAIR 7.3

NETD-SW-1
STAIR 1

01E-SW
STAIR 3

02E-SW
STAIR 5

04E-SW
STAIR 9

05E-SW
STAIR 11

Stairs # 7.3
Elram - APR/20

EL1 - Electra wiring ongoing
EL3 - WW - p.house Ongoing
HOLD - touch up paint

Bynet - Pull wire / Telecom
Megason - Lss
Electrosafe - antenna
ELRAM - 3rd coat Mamads

DW + VRL
Elram - shaft APR/28

EL2 - W.W - 4da platform
Electra - Shivs
EL4 - W.W roof M.room
MEWP - training

Stairs # 2
ELRAM - HOLD
HOLD - MCT

Stairs # 4 Shaft
ELRAM - HOLD

NWTD-SW-1
STAIR 2

01W-SW
STAIR 4


02W-SW
STAIR 6

03W-SW
STAIR 8


04W-SW
STAIR 10

05W-SW
STAIR 12

Request Form




Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

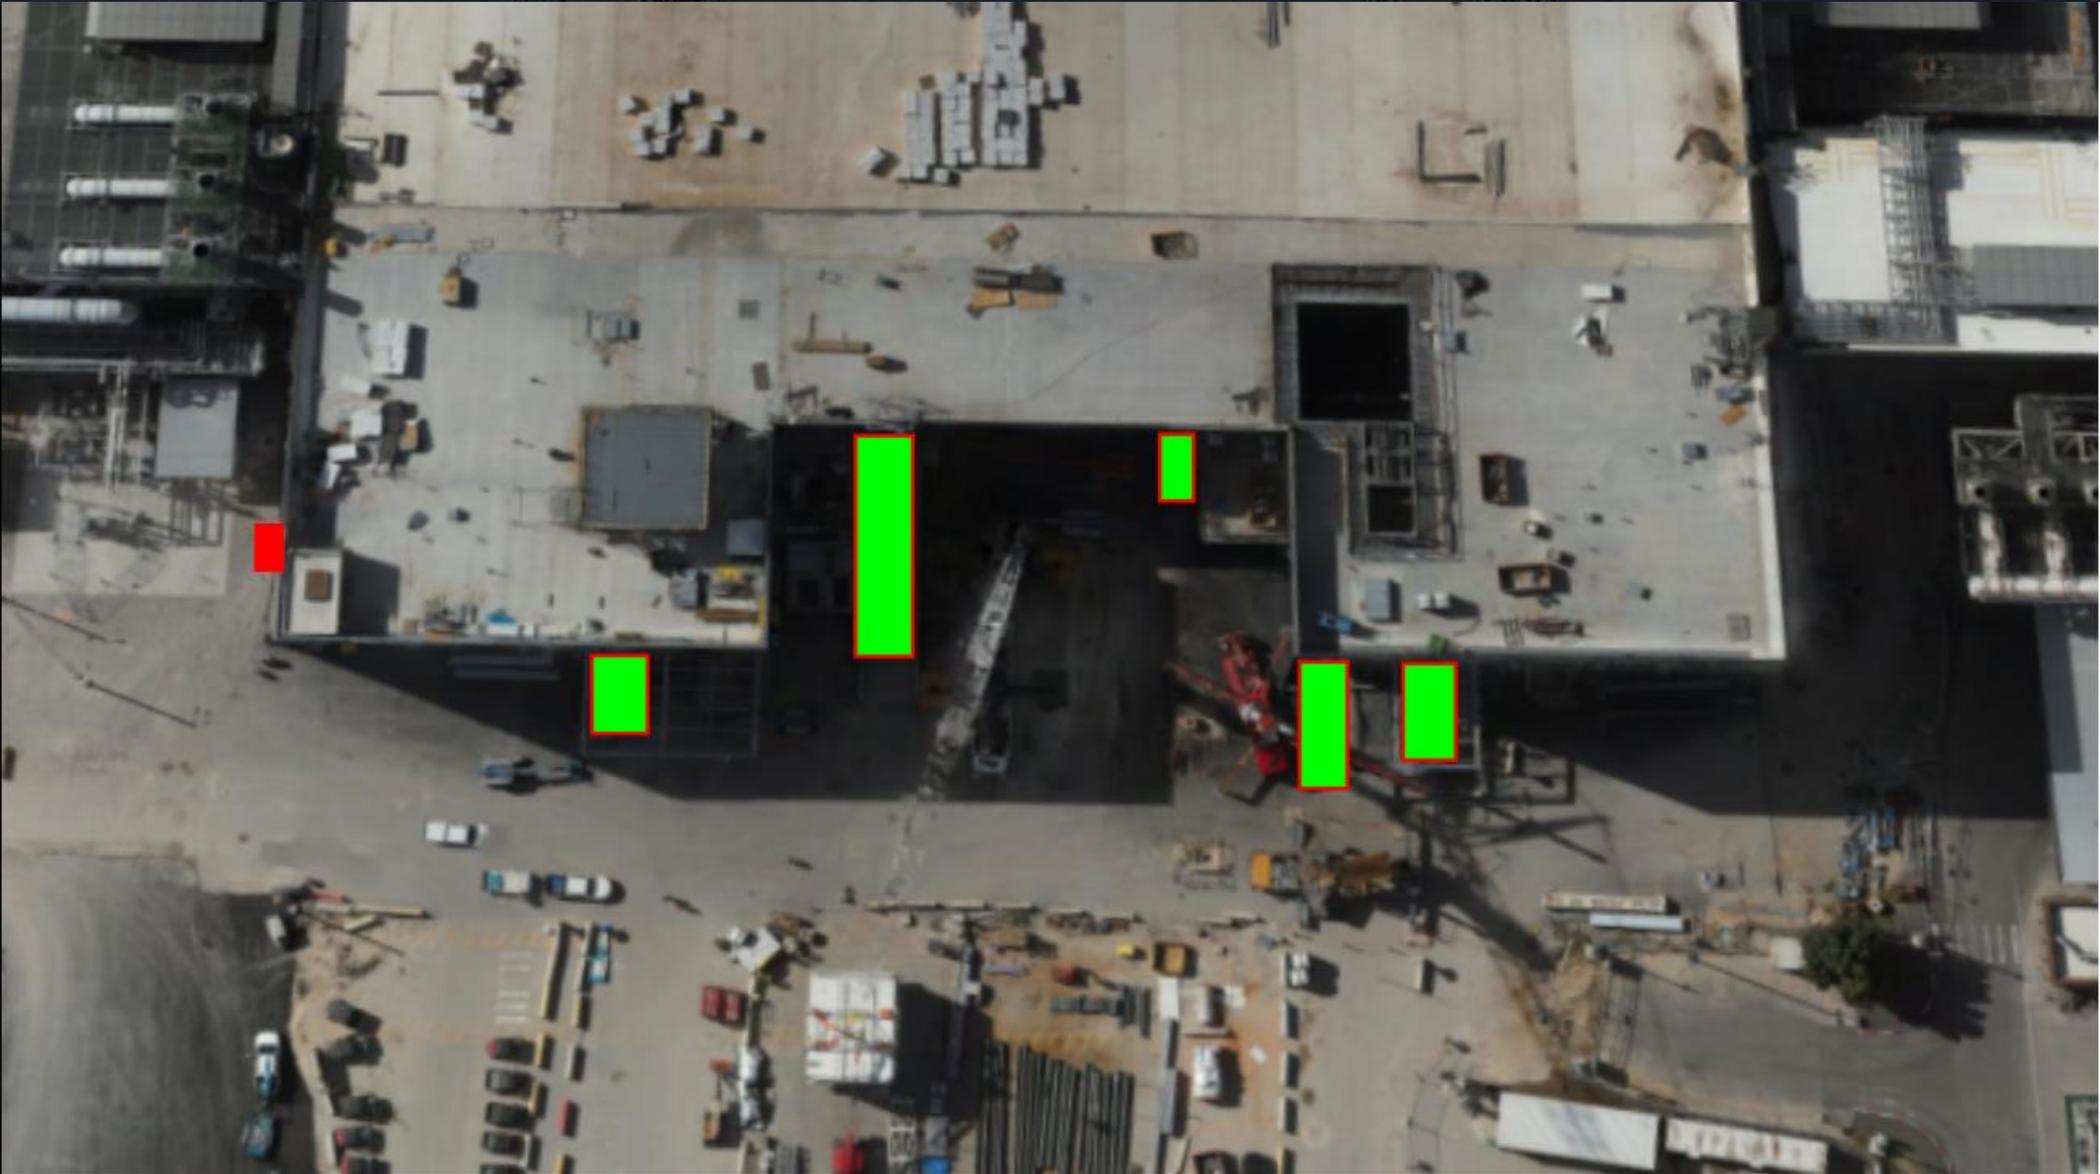



- READY FOR GIRTS
- INSTALLING GIRTS
- READY FOR PANELS
- PANELS INSTALLED

MOD 2 WESTSIDE GIRTS/SIDING

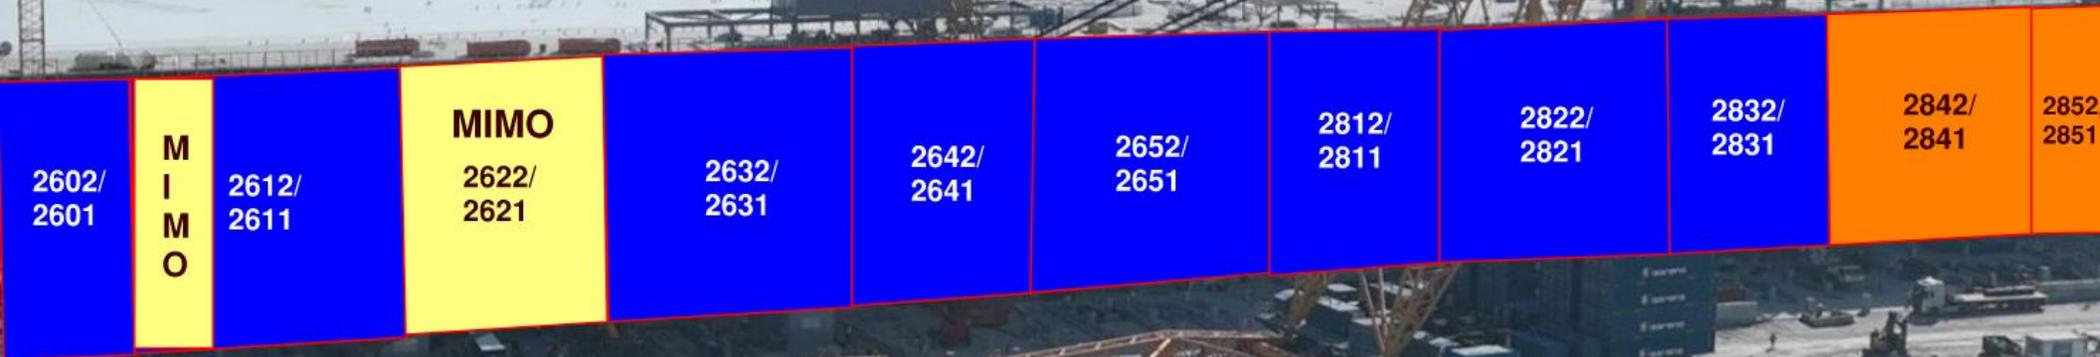

MOD 2 EASTSIDE GIRTS/SIDING



2752/
2751

2742/
2741

2732/
2731

2722/
2721

2712/
2711

2552/
2551

2542/
2541

2532/
2531

2522/
2521

2512/
2511


2502/
2501

- READY FOR GIRTS 
- INSTALLING GIRTS 
- READY FOR PANELS 
- PANELS INSTALLED 



PSSS.1

Utility Level 1YA

PSSS Roof 2SA

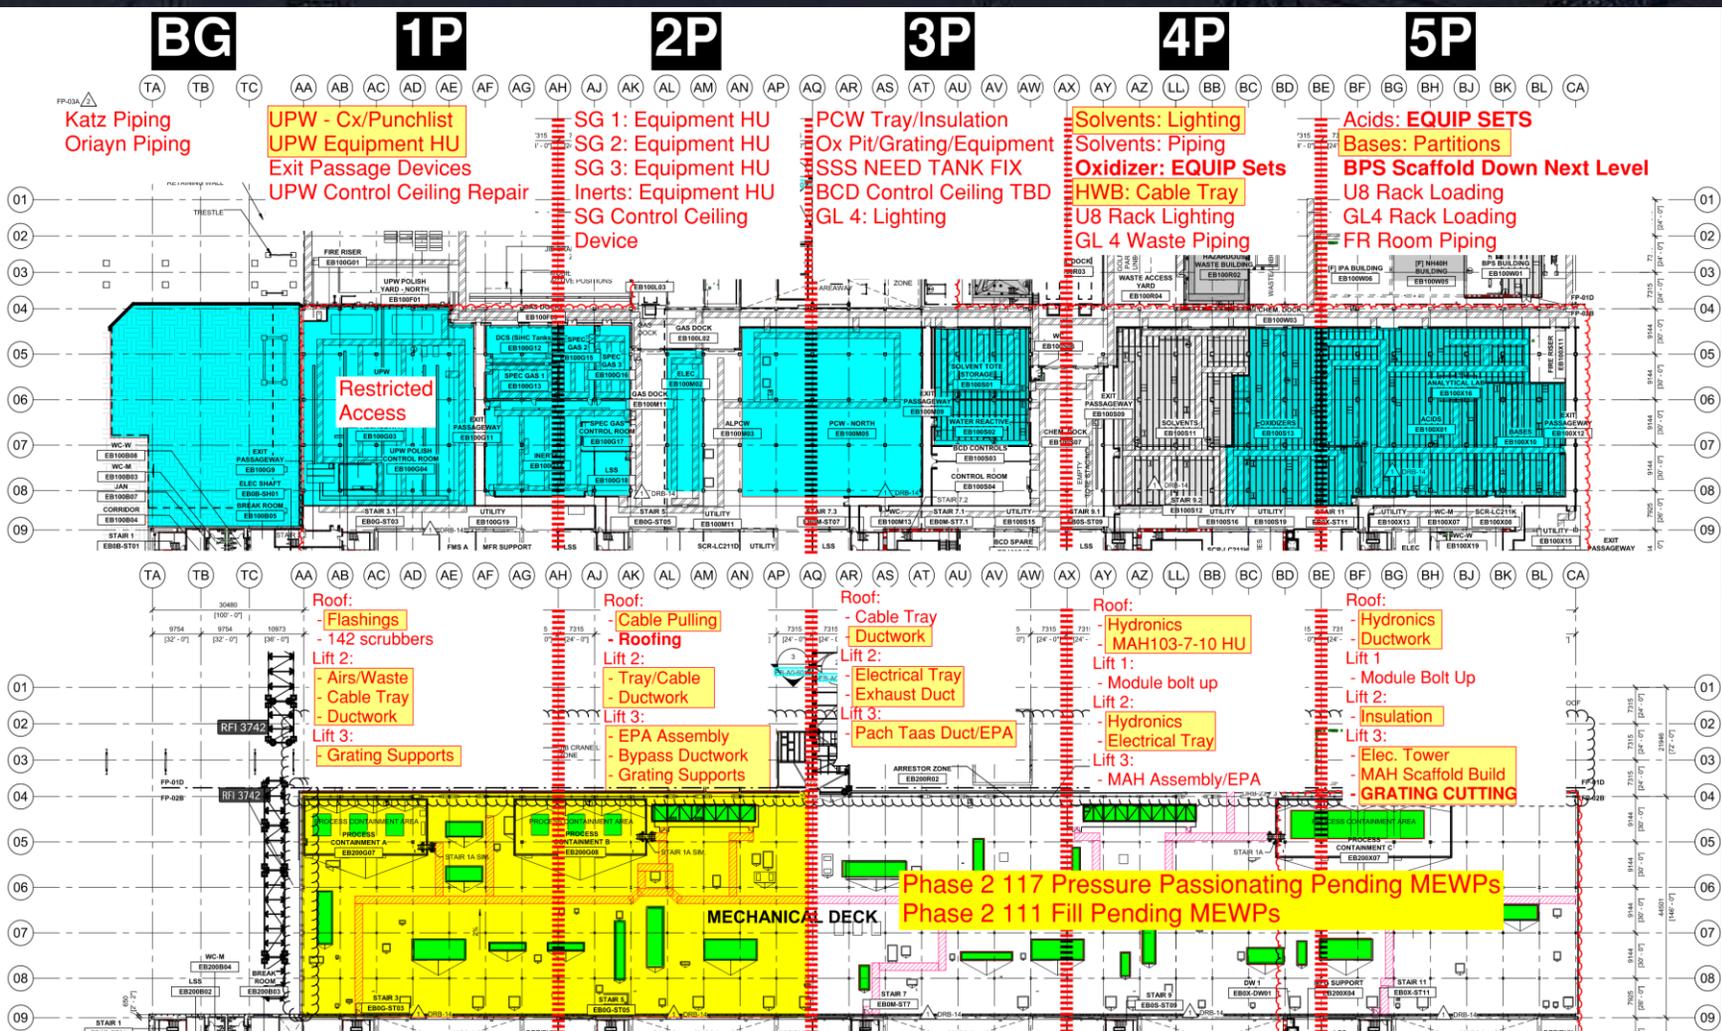


PSSS.2

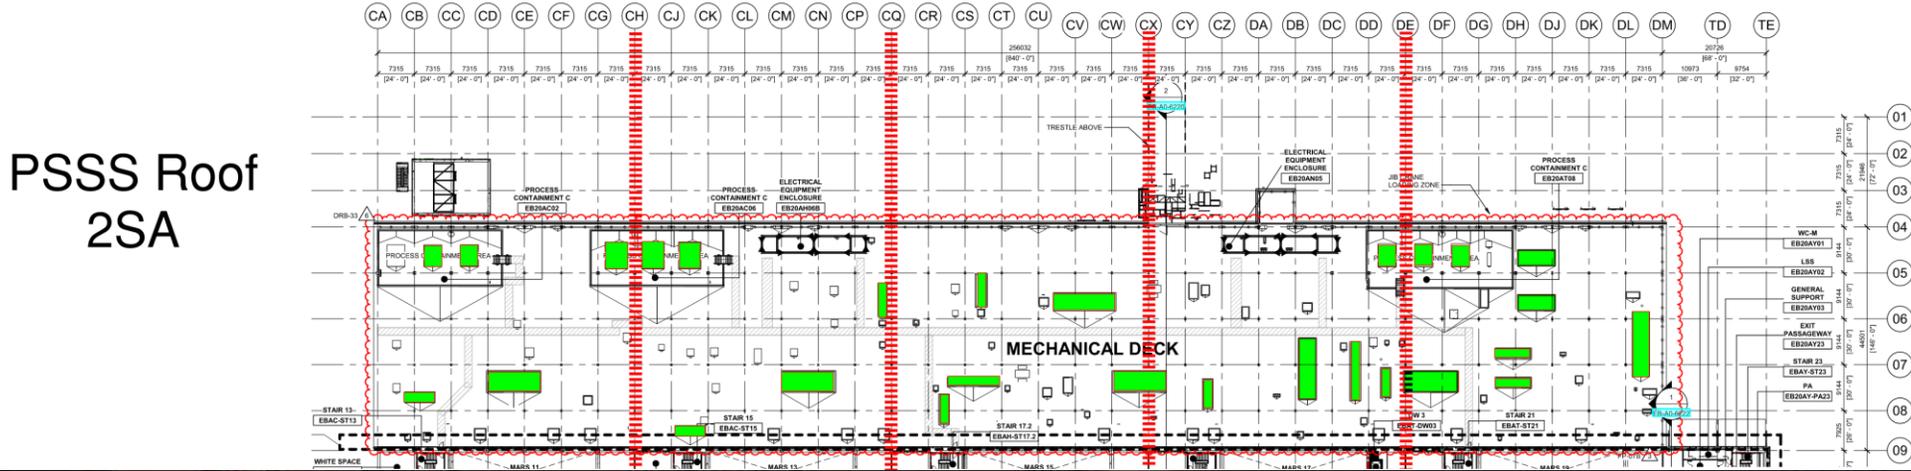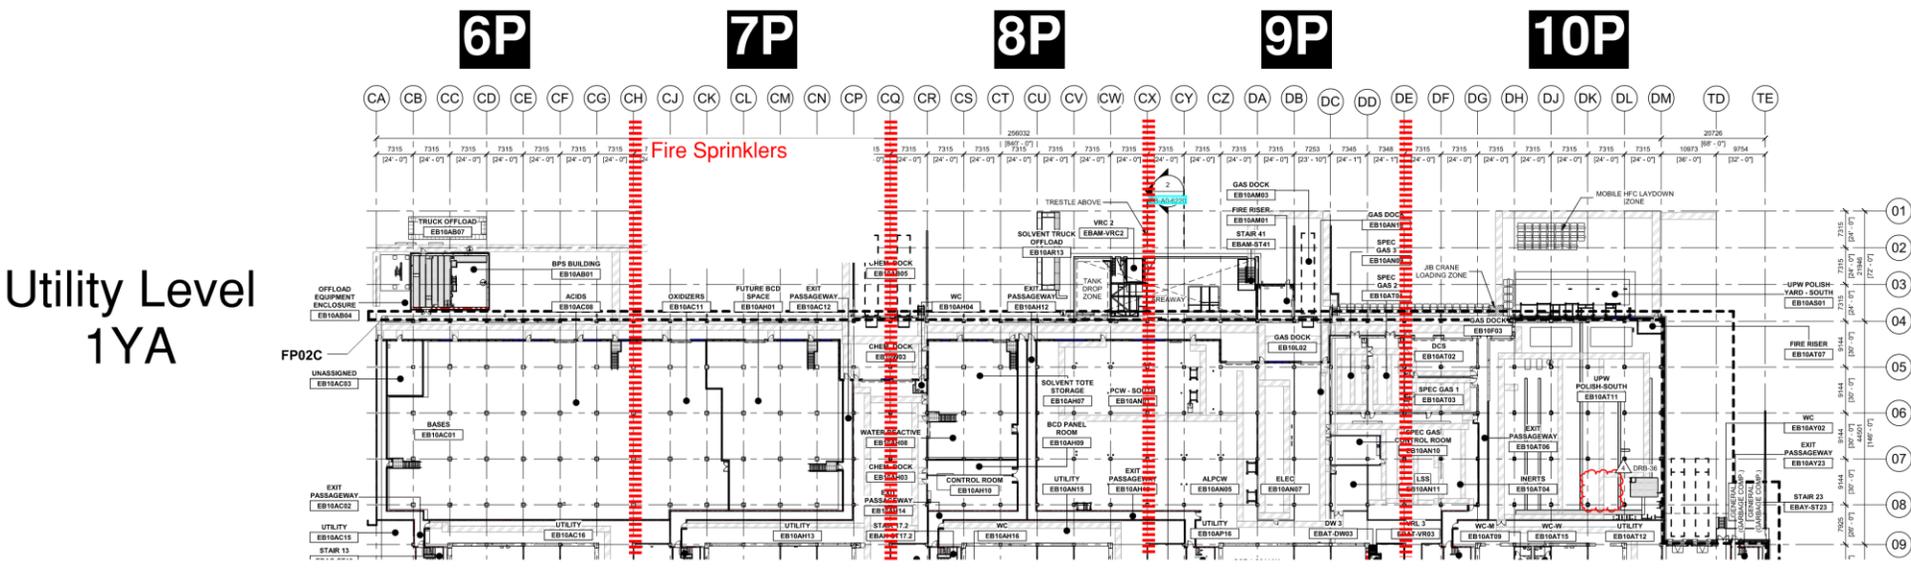


WJG – UL

	<p>* Carmel Bidud - erection of scaffold in the west SUT</p>		<p>* Carmel Bidud - measurements for final duct connections to FAB *Lesico - welding and grouting pipe support</p>	
--	--	--	--	--

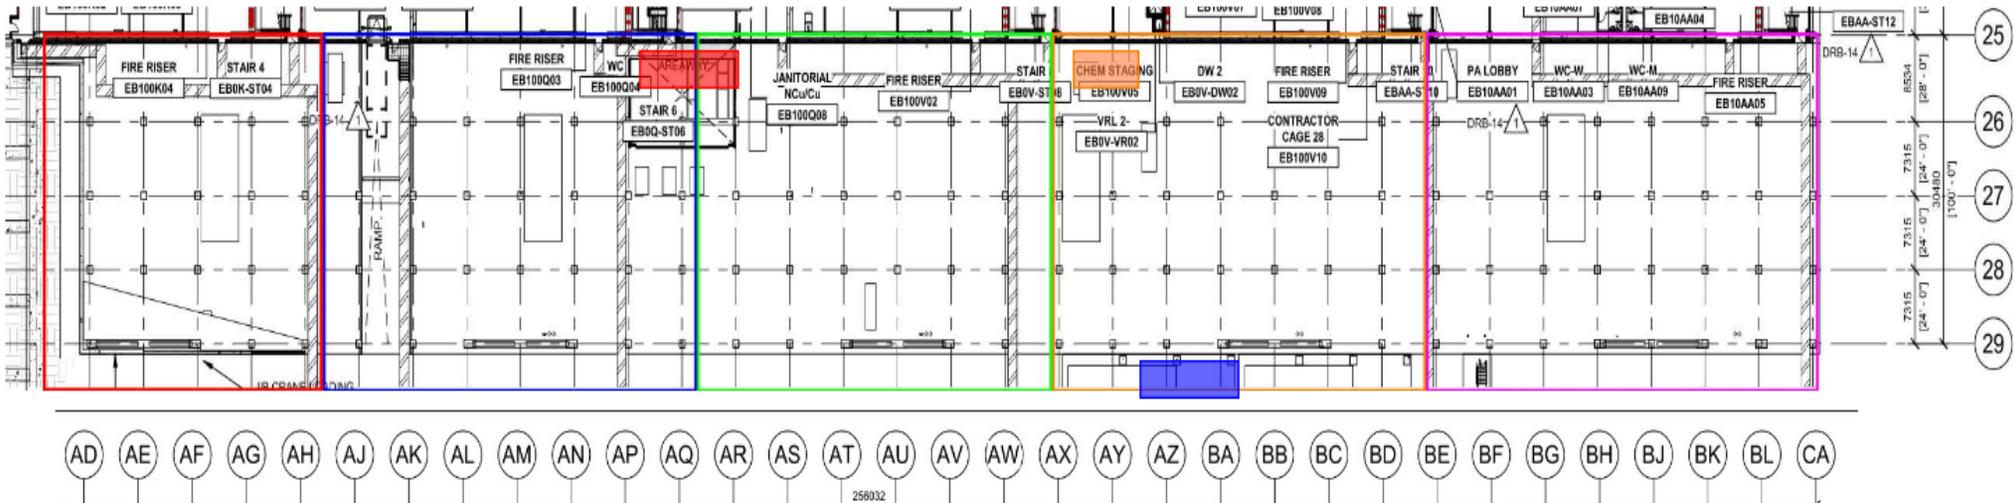

WJG – Lift 2

- * Taper tech - fixing planking after stiffeners installation
- * Chemo - finished restoration on UPN 113
* W&W - welding stiffeners
-
-
- * SK - working on connections to MAH
* Afcon - installation of cable tray underneath MAH and finishing cable pulling to VFD

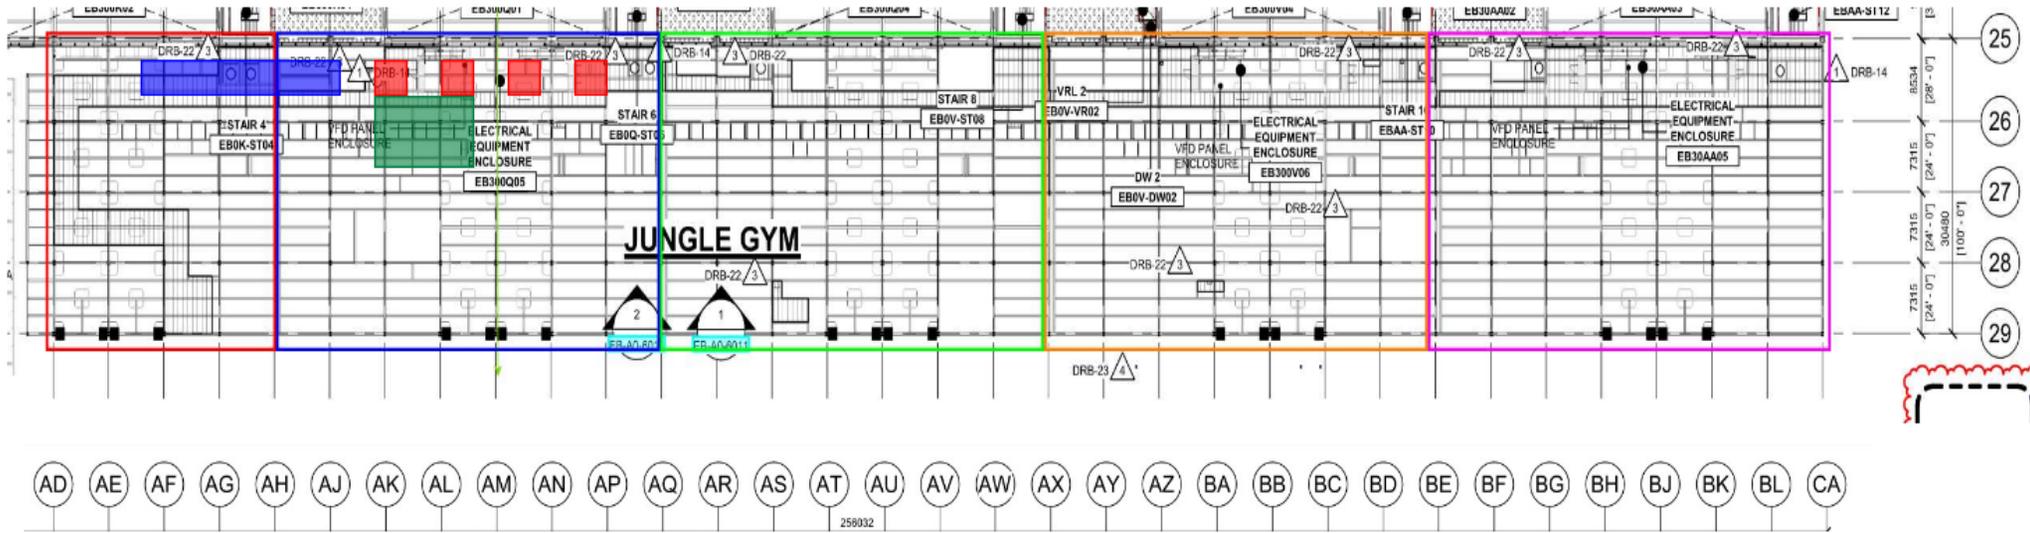

WJG – Lift 3

* SN - installing and welding penetrations supports

* Taper tech - performing planking penetrations and removing ramps for permanent handrails
* SN - handrails installation



Crane logistics

Crane: 750 ton crane
moved south of RCTO
Tuesday 15/04/25.
waiting for crane to
start 5J equipment set
(Pach Taas) on
20/04/25






CUB 1 Ops Ready April 29






CUB 1

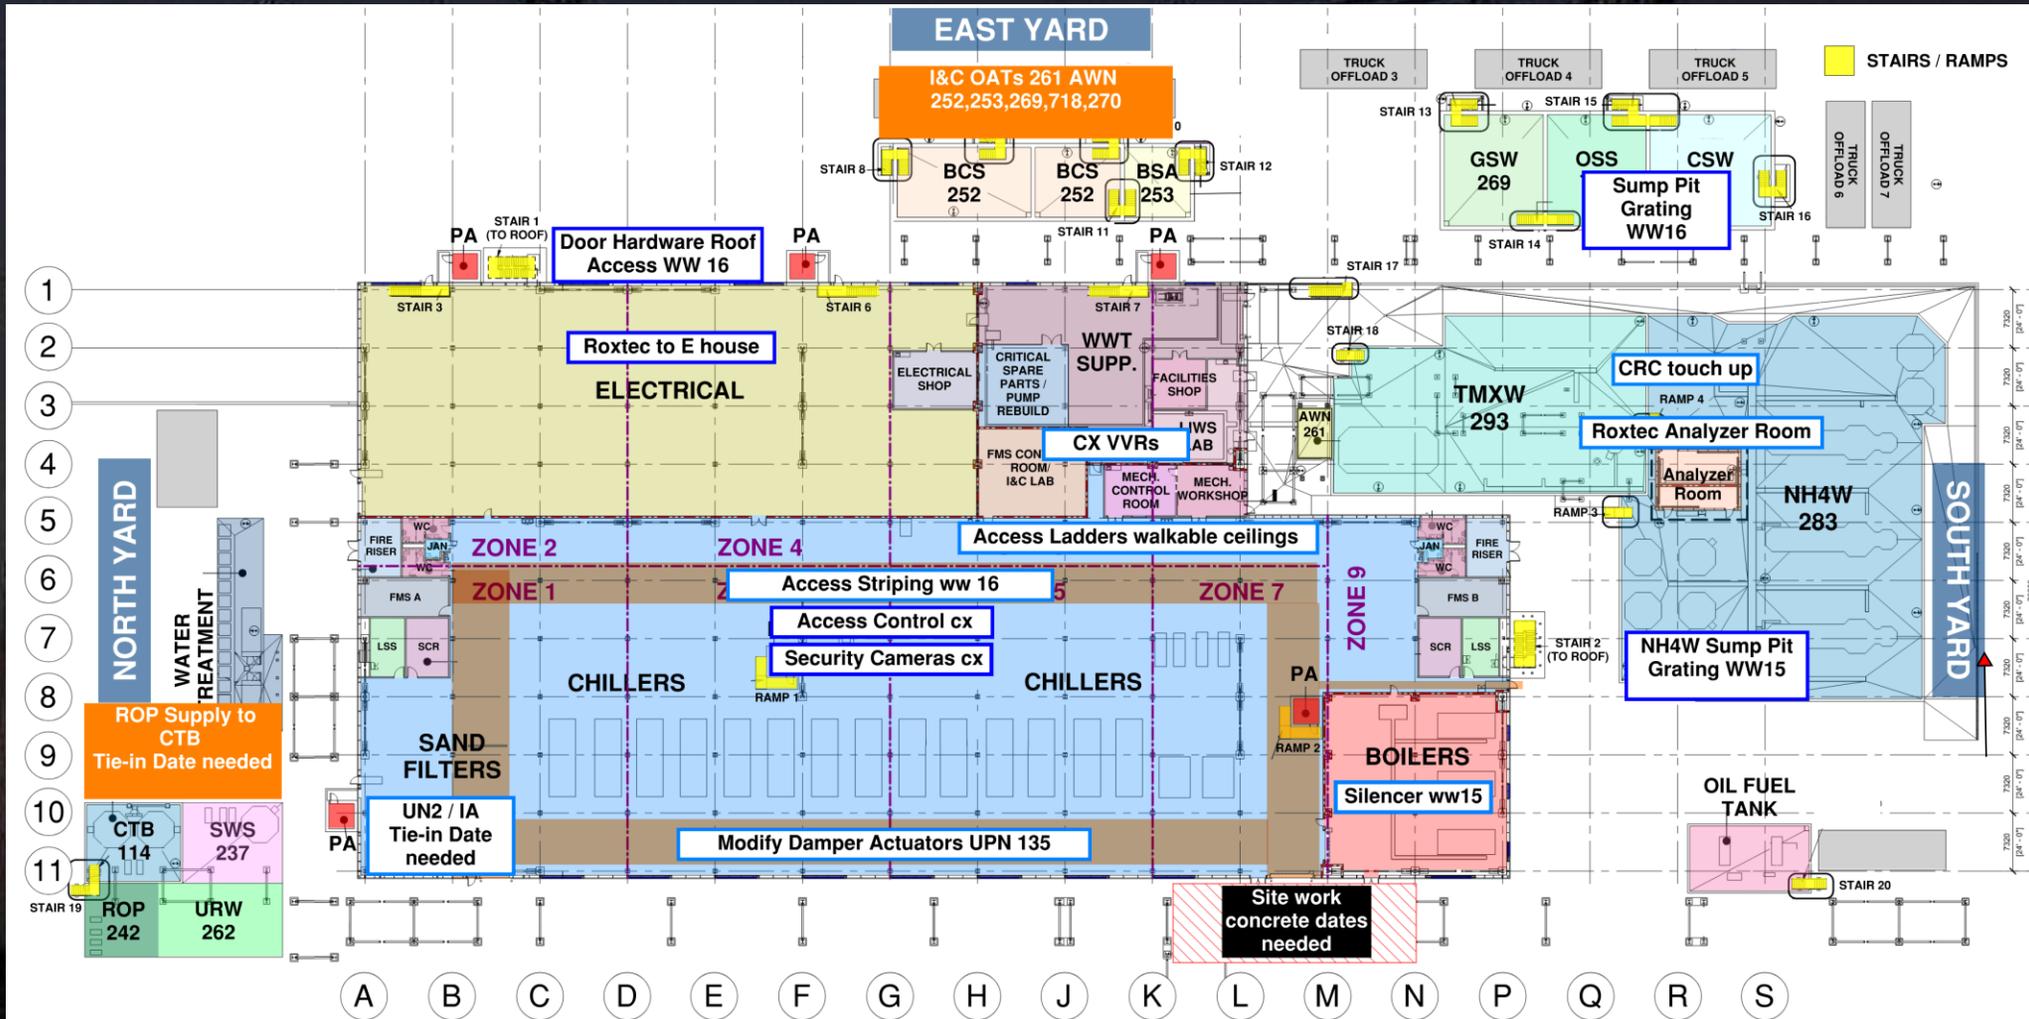




CUB 1 – EXTERIOR/ROOF

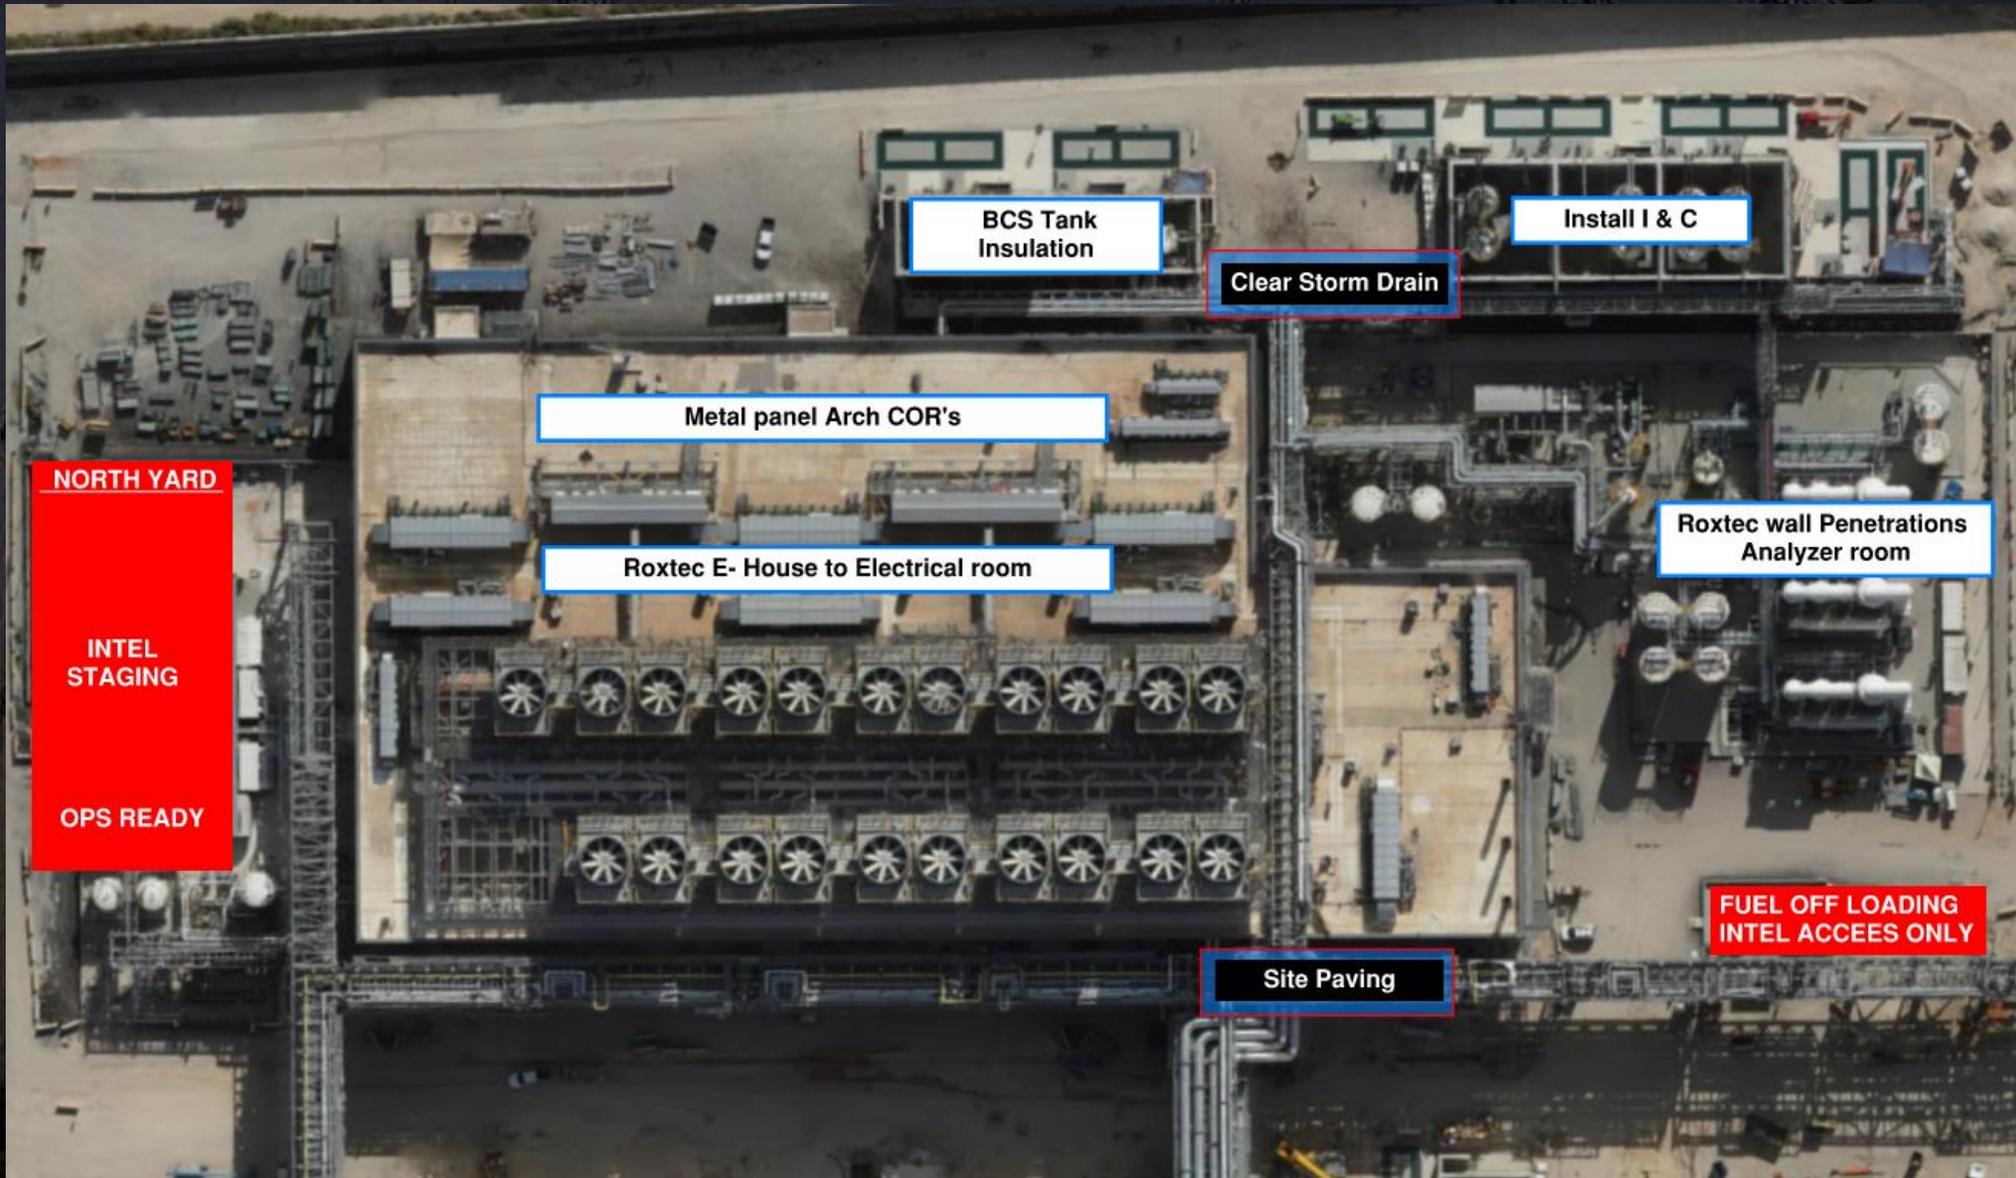




CUB 2- Load in & H&T

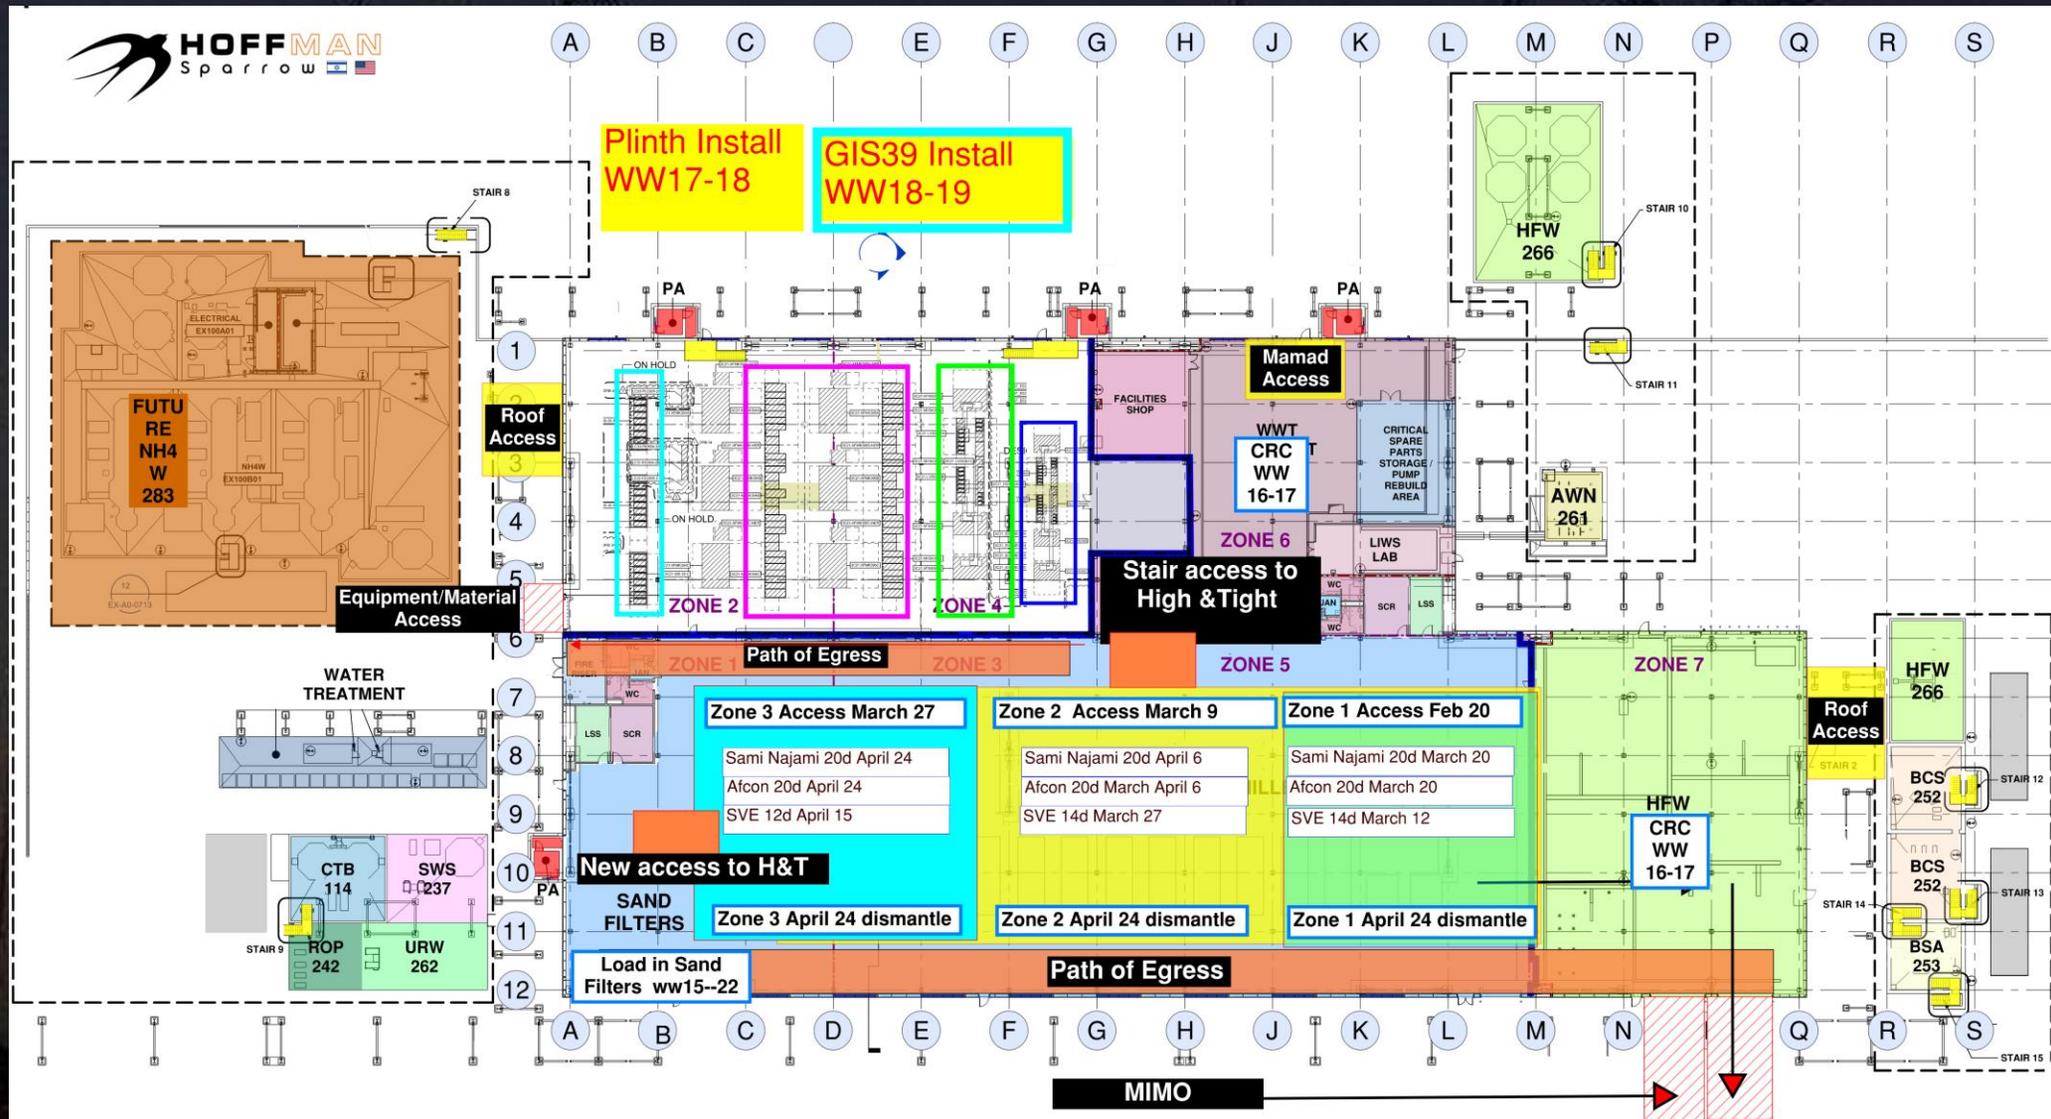




CUB 2- Trestles/Roof/Guardrails

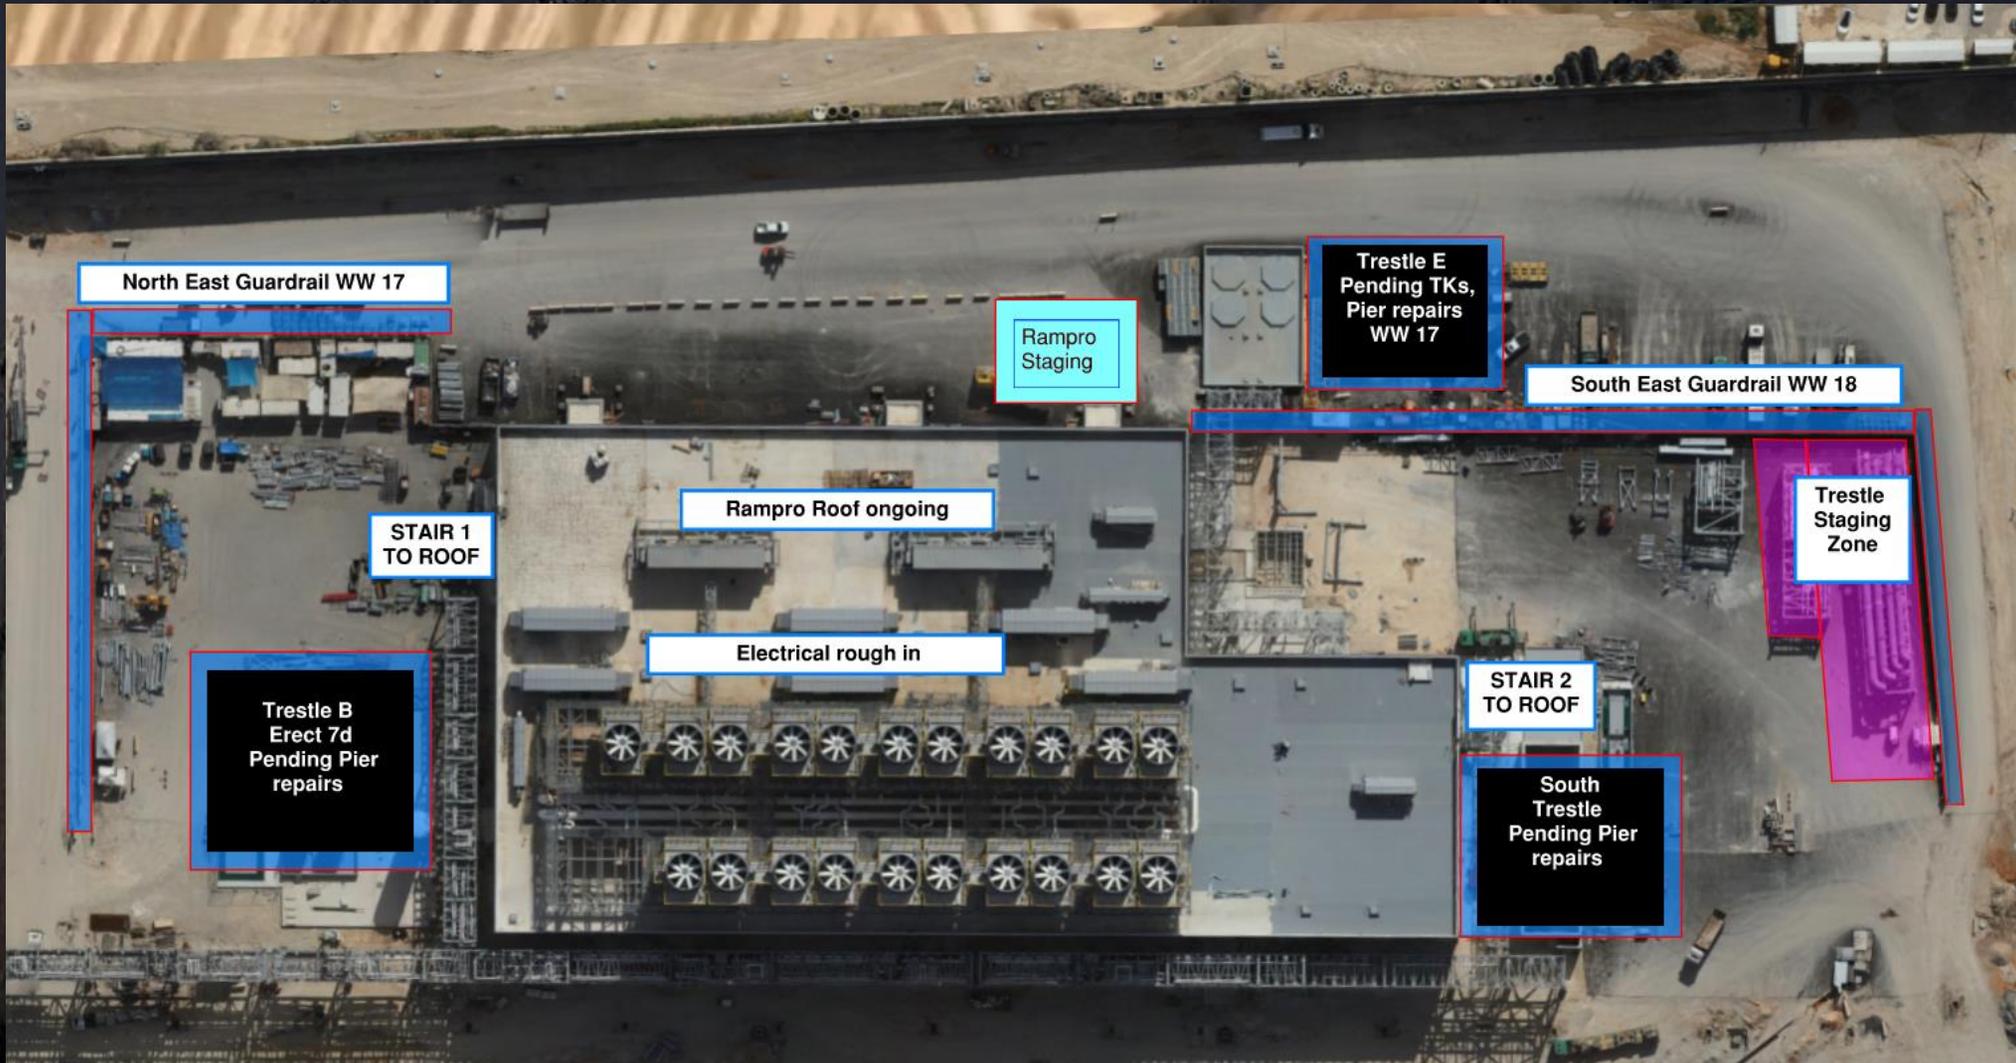



Daily Coordination Meeting

Site Logistics

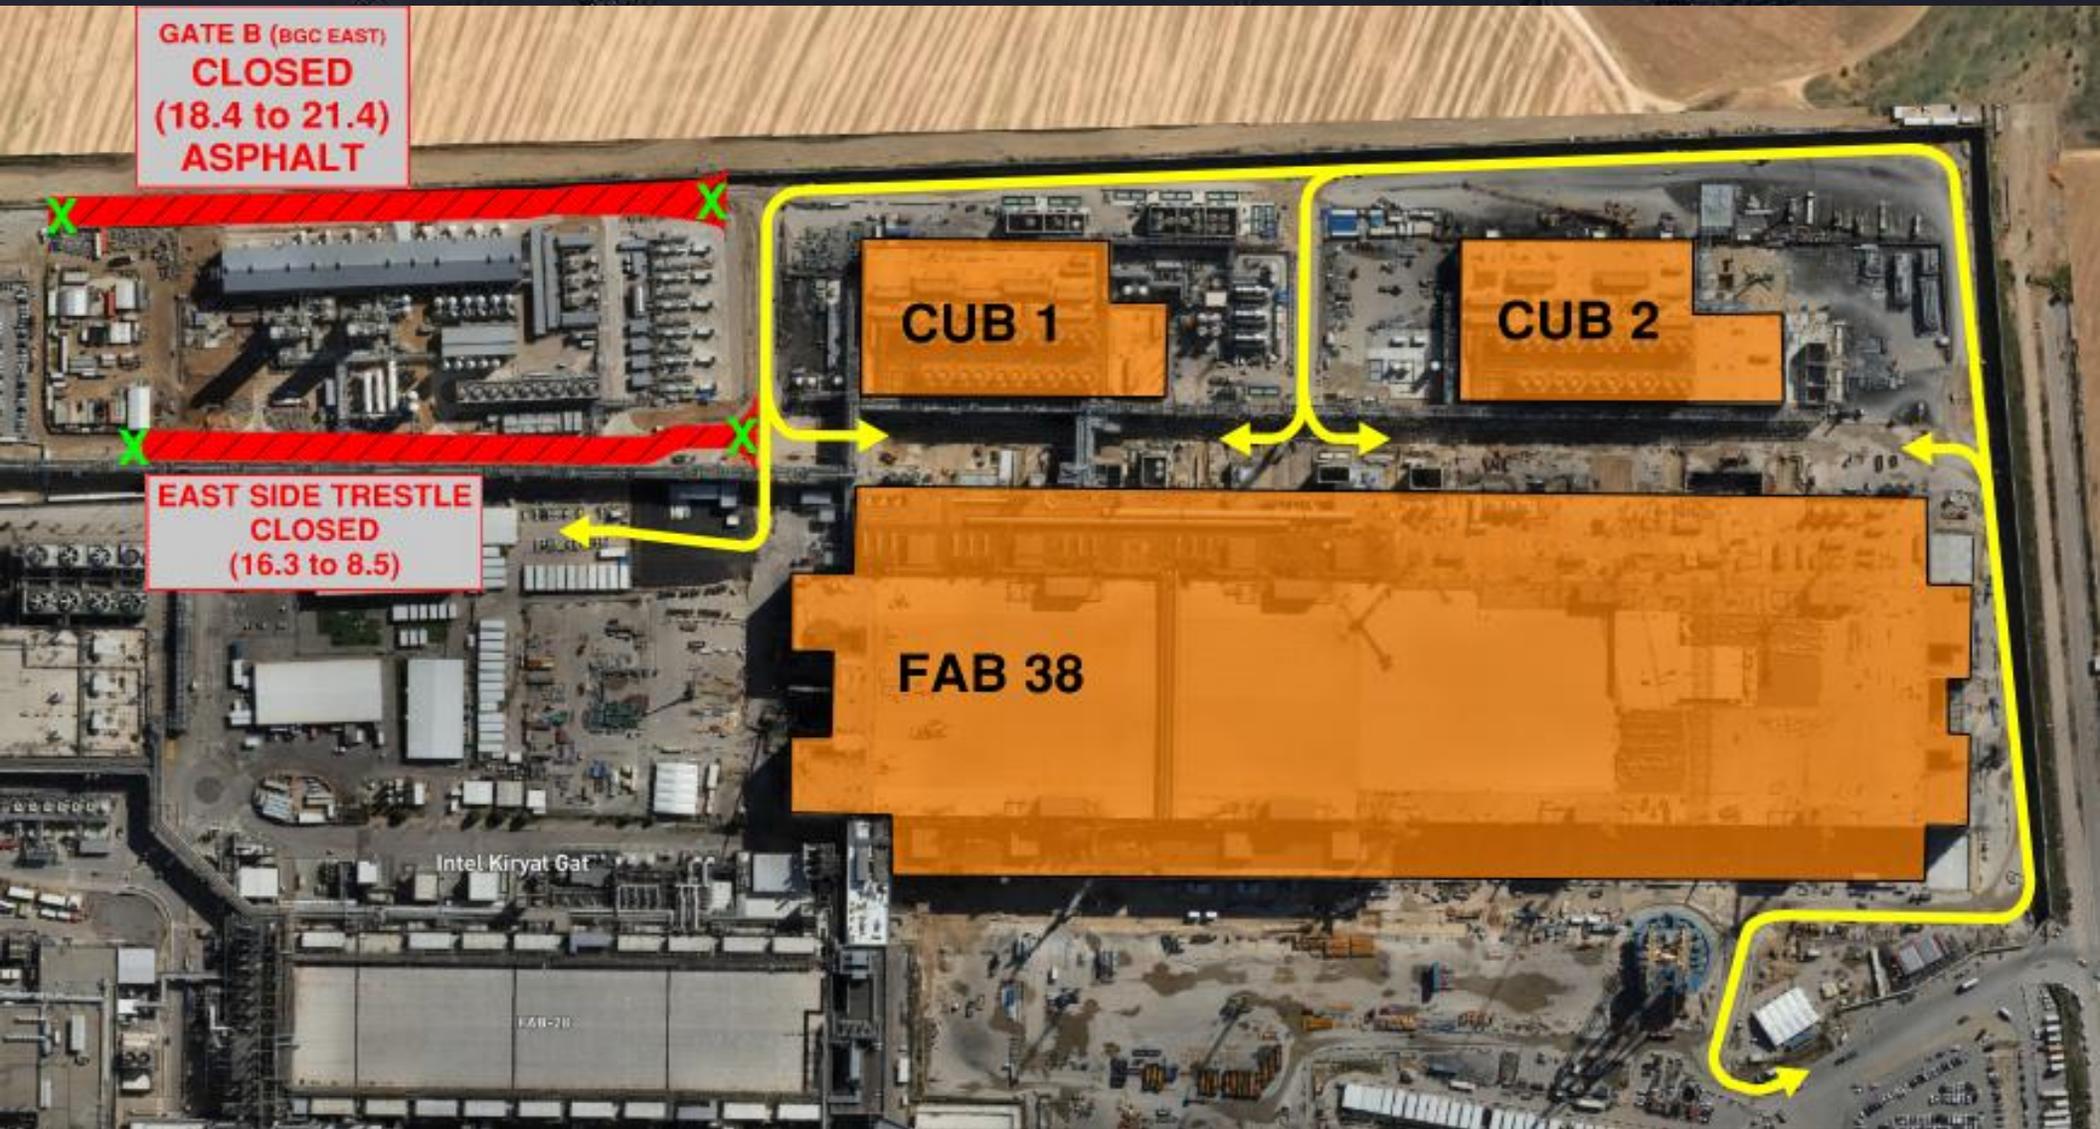


Daily Coordination Meeting

Site Logistics: North



Daily Coordination Meeting

Site Logistics: South

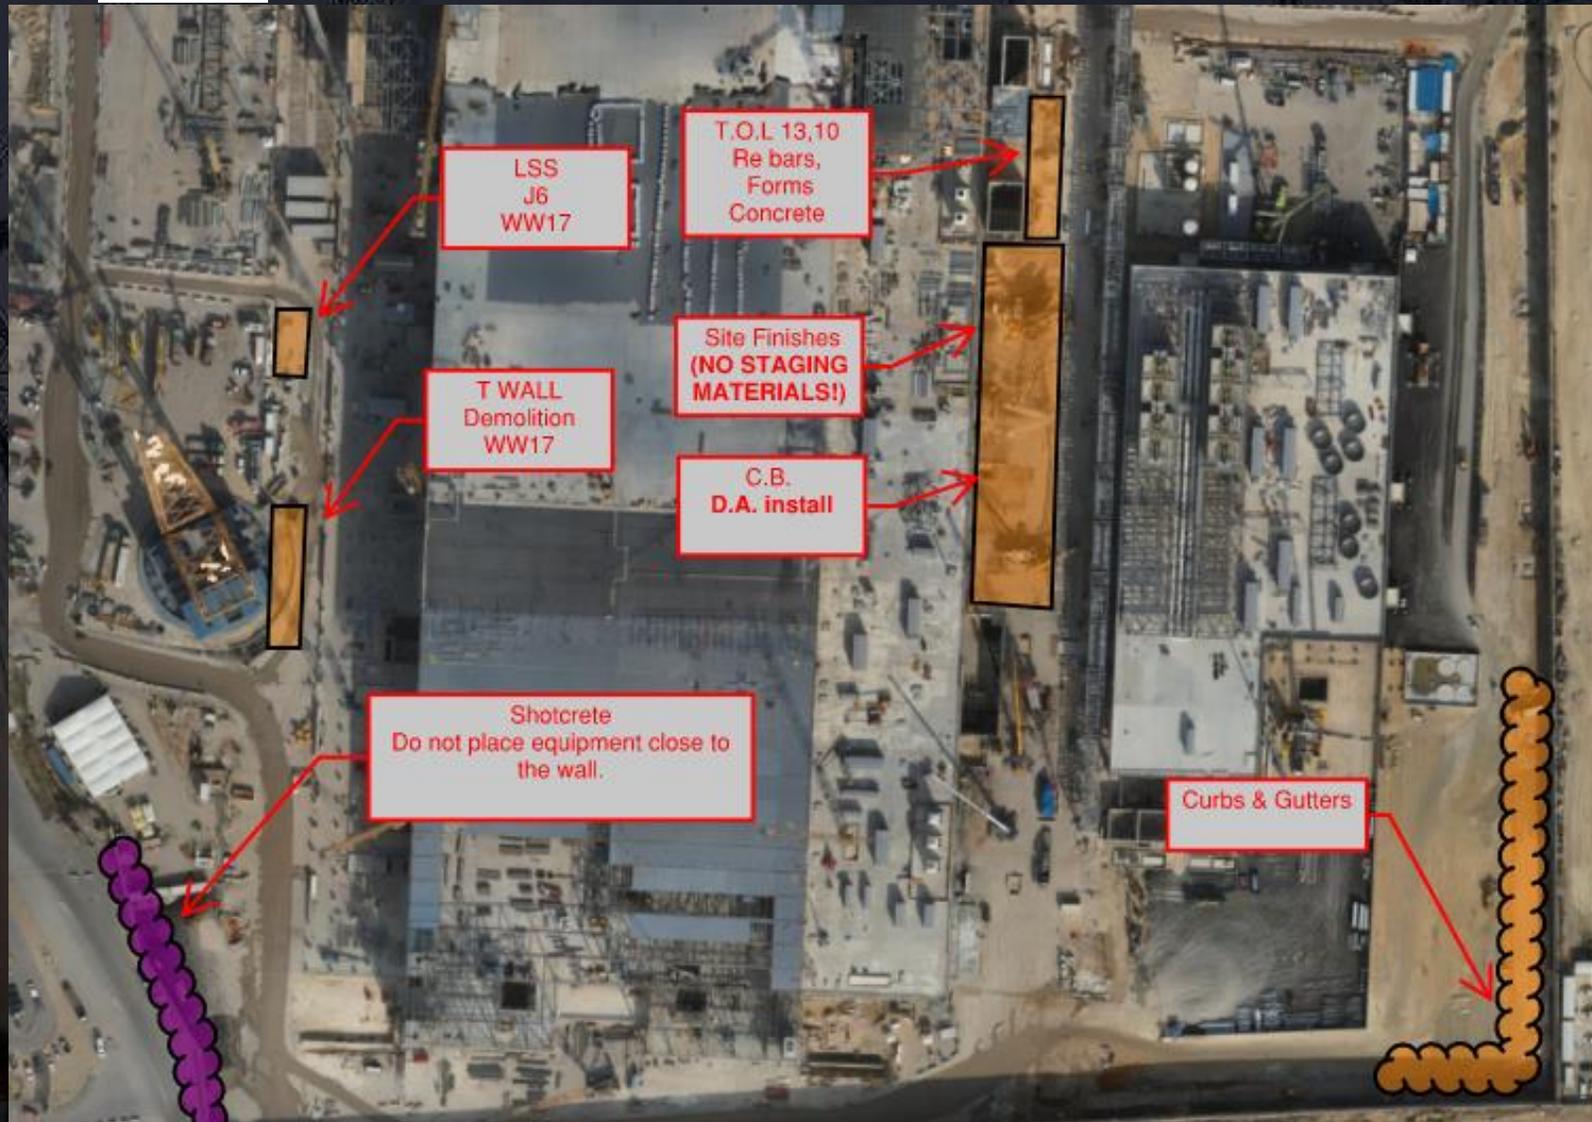

Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)


- LARGE
- SMALL
- BUILDING



Daily Coordination Meeting

WATER BOTTLE FILLING STATIONS

WATER BOTTLE FILLING STATIONS

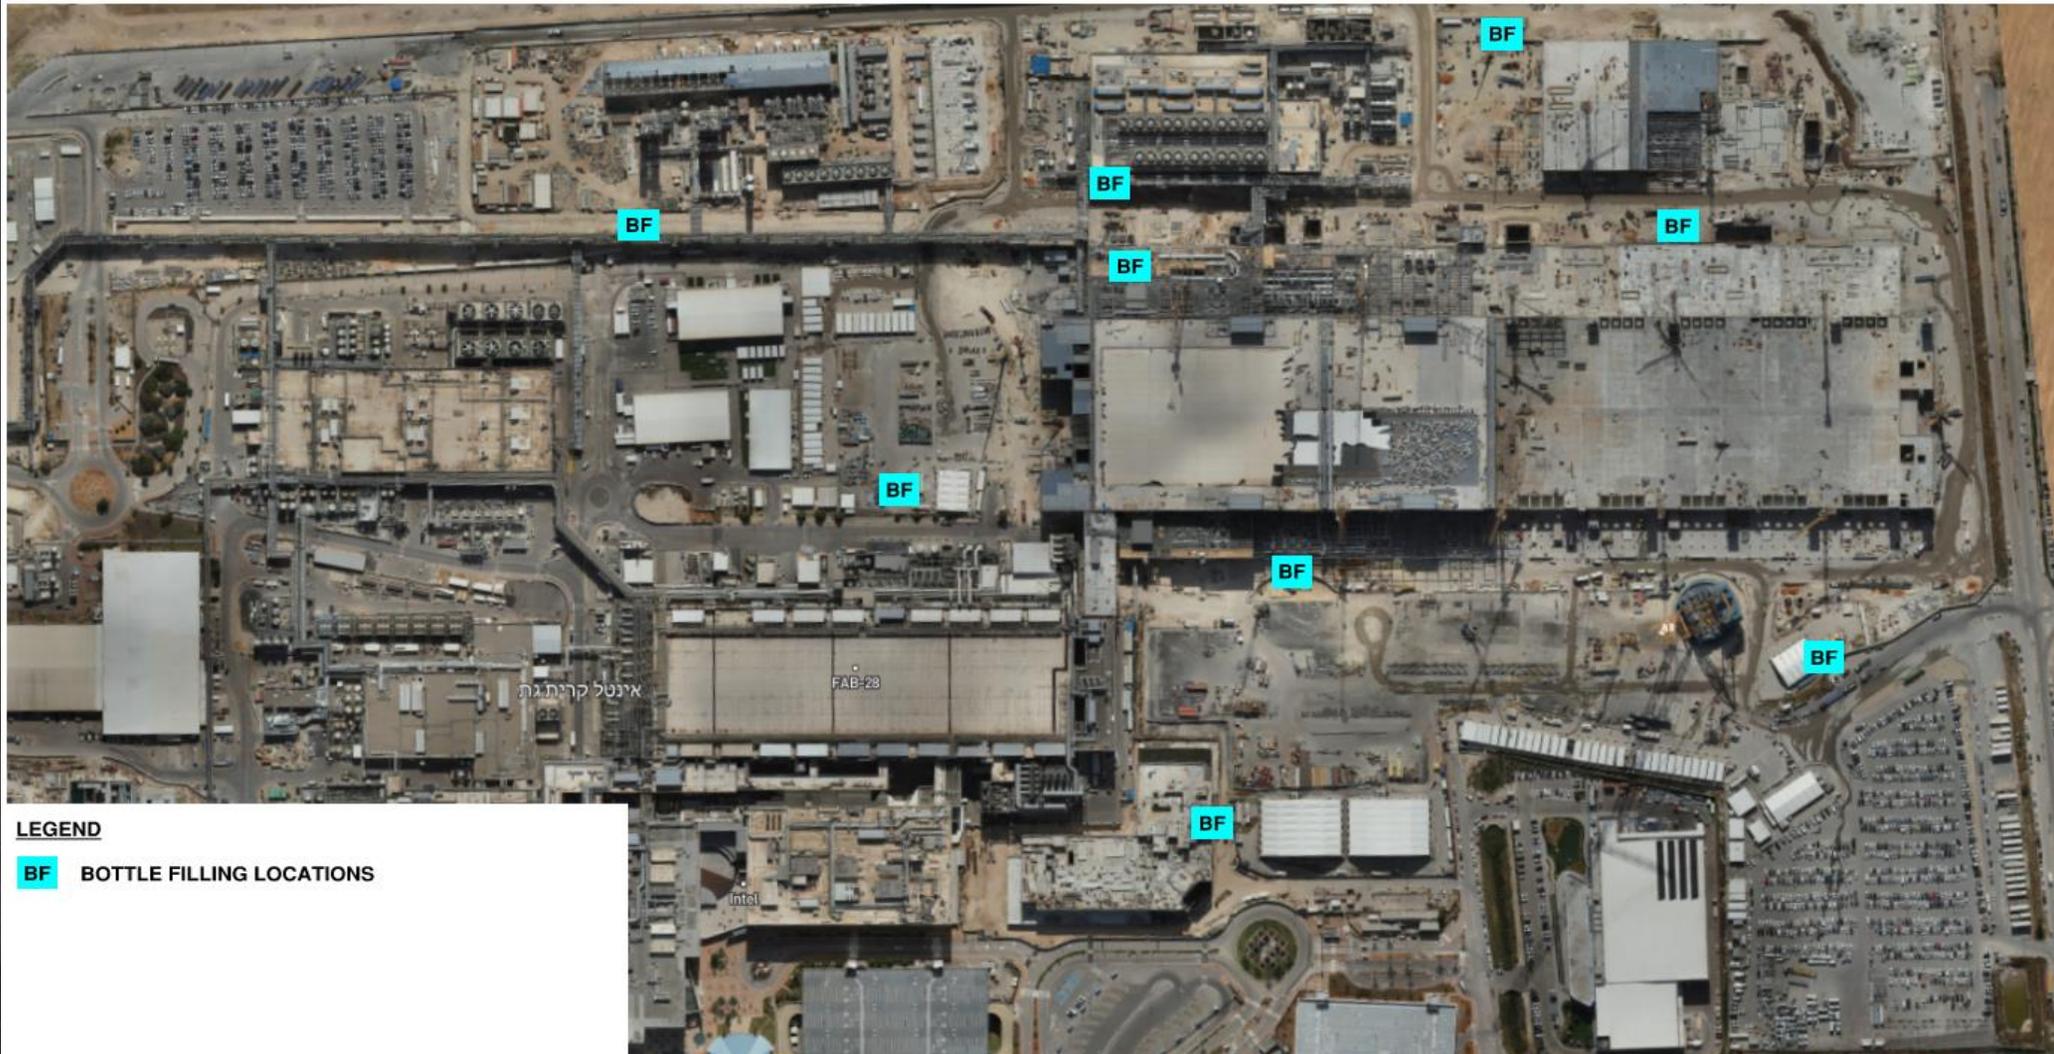



BACK TO MEWP WORK

MEWP inspections:

- Talk to your subs.
- Get with your safety team and management.
- Get out to the field.
- Help your teams to go back to work!

WE CAN'T DO YOUR WORK FOR YOU!

Hot weather:

Be prepared – water stations, heat illness symptoms, etc.

BACK TO MEWP WORK

1. Documentation available on the equipment in the field:

- I. Equipment registration document (Rishayon).
- II. Valid Bodek inspection report (Tasker) – must be valid within 6 months of inspection.
- III. Equipment insurance document (Bituach). The identification number for this equipment must be written in the insurance.
- IV. Supplier inspection report – signed and available for review.
- V. Supplier training certificate for equipment operation.
- VI. 18C designation letter listing approved operators and spotters for the specific equipment.
- VII. Equipment manual – must be available in Hebrew and in the language of the operator (QR code acceptable for one language).

2. Equipment marking:

Each MEWP must be clearly marked with:

- I. The company name.
- II. A printed list of approved operators and spotters assigned to that equipment.

BACK TO MEWP WORK

3. Intel MEWP Checklist:

Must be fully completed and signed for each piece of equipment and ready for review in the field.

4. Intel MEWP Assessment:

Must be available in the field and ready for review.

5. Visual Inspection of the MEWP:

- I. All handrails and doors must function properly and be free of damage.
- II. MEWP oil diapers must be properly installed. No red/yellow ropes or wires are permitted.
- III. No temporary or improvised fixes are allowed on any operational system.
- IV. The MEWP must be clean, including the operator's remote control.
- V. Please make sure all items are ready before the scheduled inspection.

Daily Coordination Meeting



14:00 Sign In
