

Daily Coordination Meeting




Daily Coordination Meeting

General Topics:

- **Trestle Testing** - out of PMB by 18:00 tonight, no PMB access tomorrow
- **BGY closure for blowdown, includes stair 1 exit**
- **Weekend Work**


UTILITY LEVEL PRESS TEST

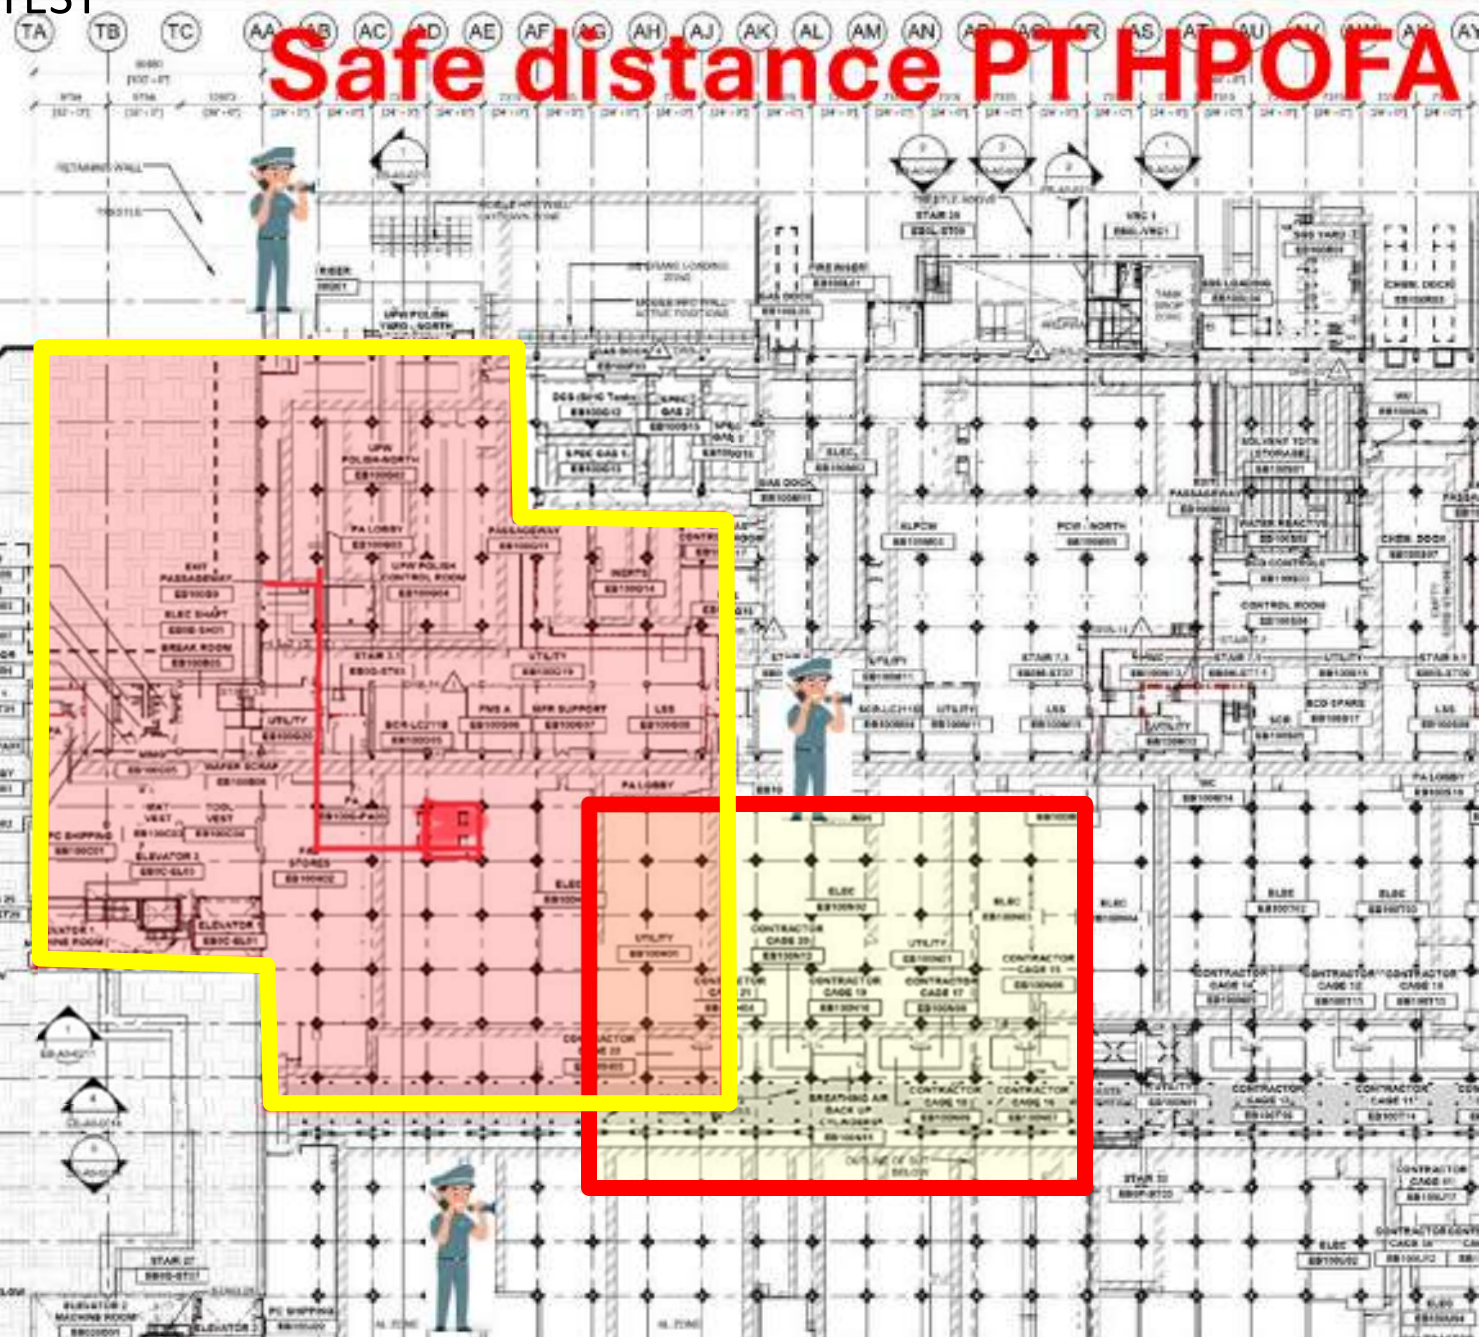

Lesico
HPOFA test
NDT test
3/6
From 17:00
till 4:00



UTILITY LEVEL PRESS TEST

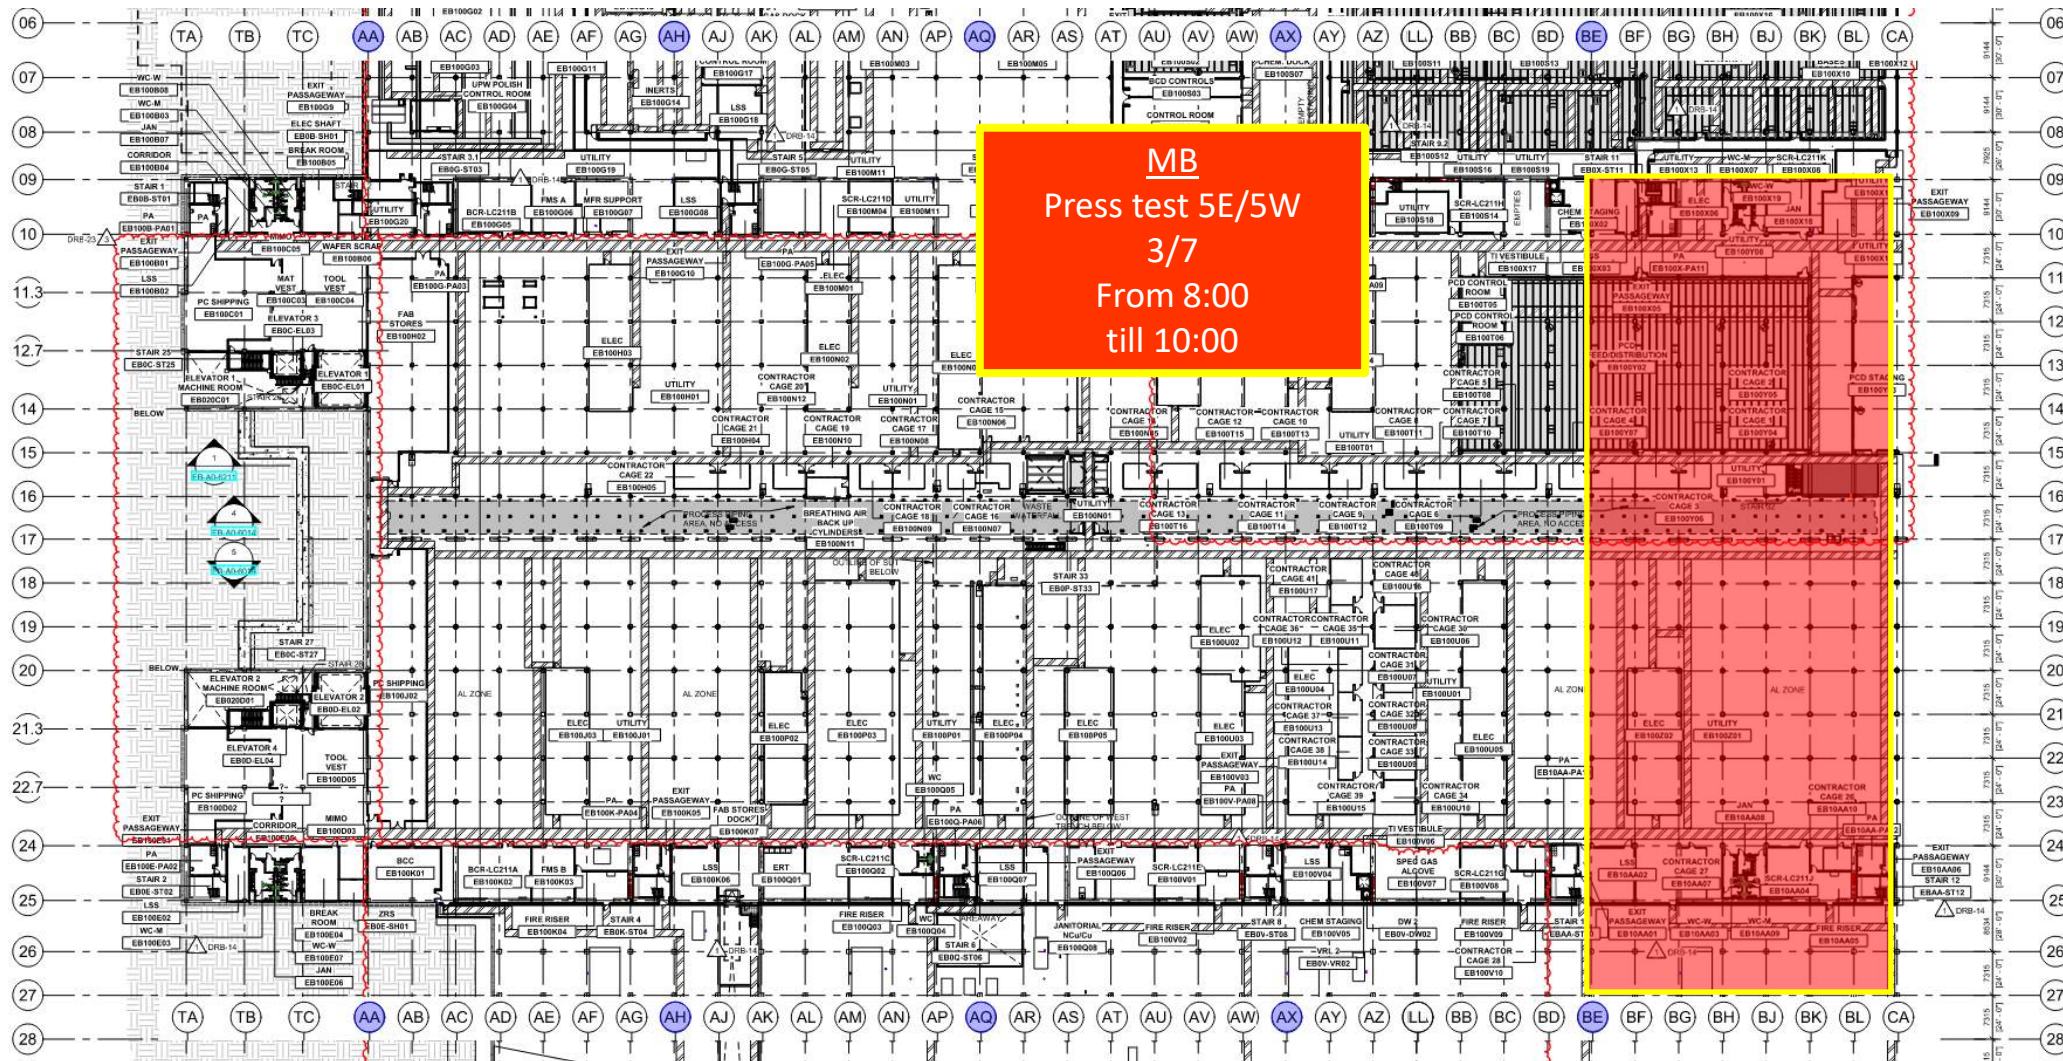

[illegible]

SK
TTNE WC'S
pressure test
Ongoing

ELRAM
ERT roof
Stairs 7.1
Chem stag
TTNW OH door
Break room E

TZUR ESH
PCD Bathtub
Done

COMBE
PCD Bathtub/pit
Waste pipe supports

CARMEL DUCT
Remove duct for RHS install
Till 3/11

HYG

Install RHS 3/4


SamiN
TTNW WC'S
pressure test done
SK Go Time!!

SUT 38.2 LEVEL

SUT 2 west Curb pour seq:
1. Mep started insert CW
conduits finish monday
EOD the latest!
2. HSAI Tuseday morning

Combe Rack 4
Upper
Lifting schedule:
M#4.5 – 4/3/25
M#4.6 – 6/3/25
M#4.7 – 10/3/25

MEP Rack 2
Piping connection

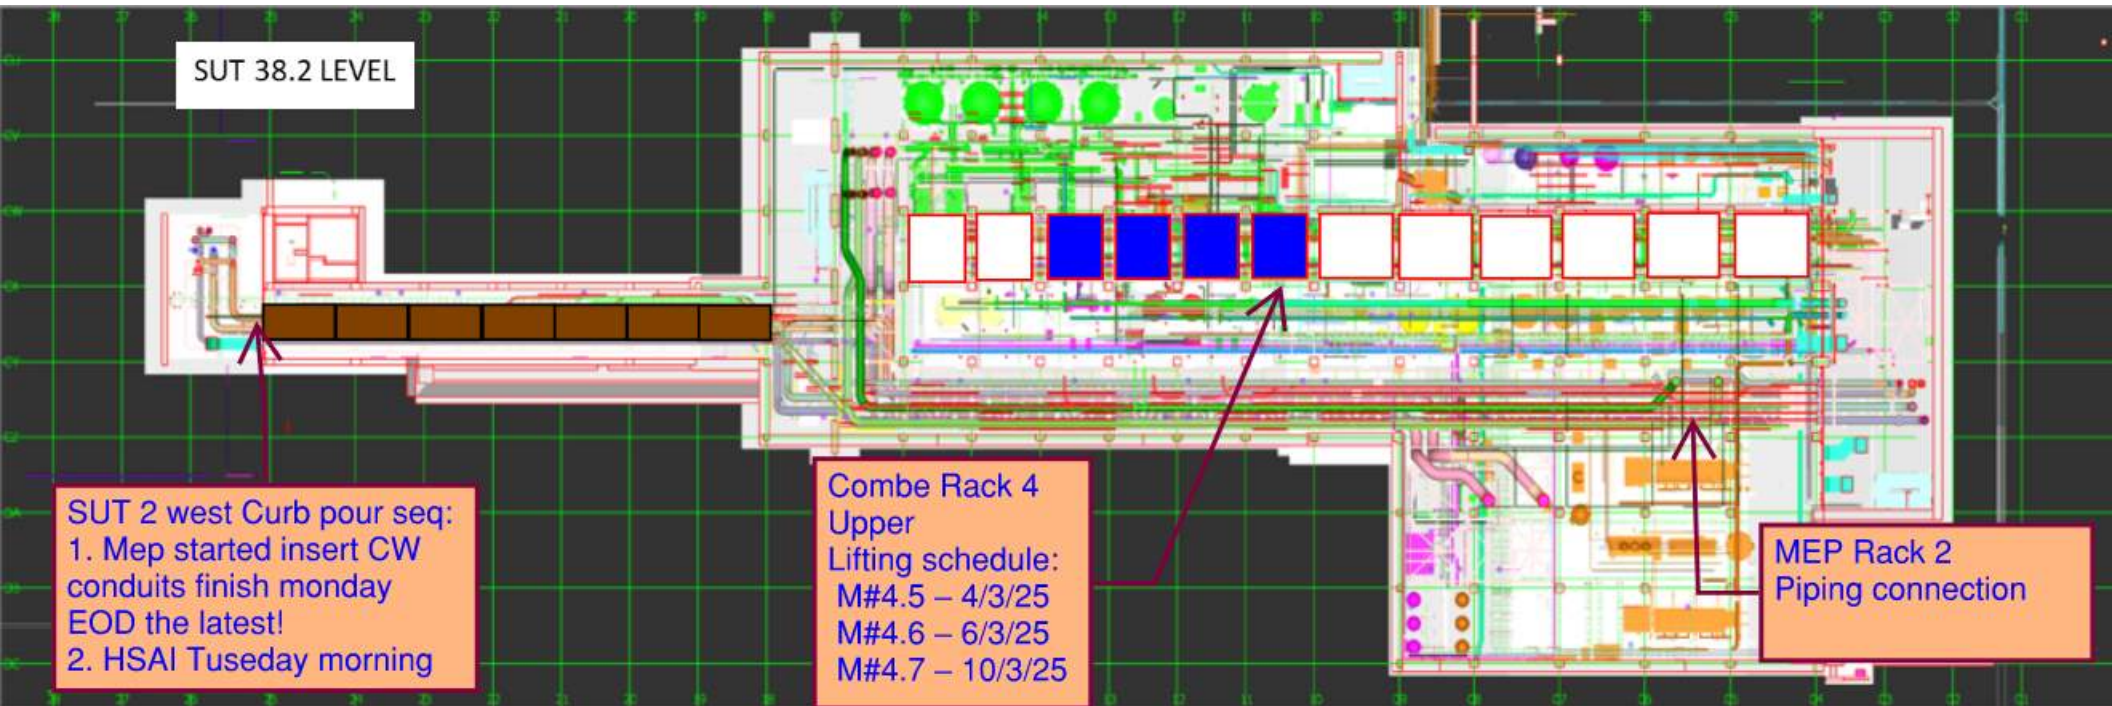


SUT 38.1 LEVEL


HSAI
Solvent room
Curb Re-pour

Megason need to
modify conduit for
roll-up instal


South wall
waterproofing Rejects
fix's 6th completed

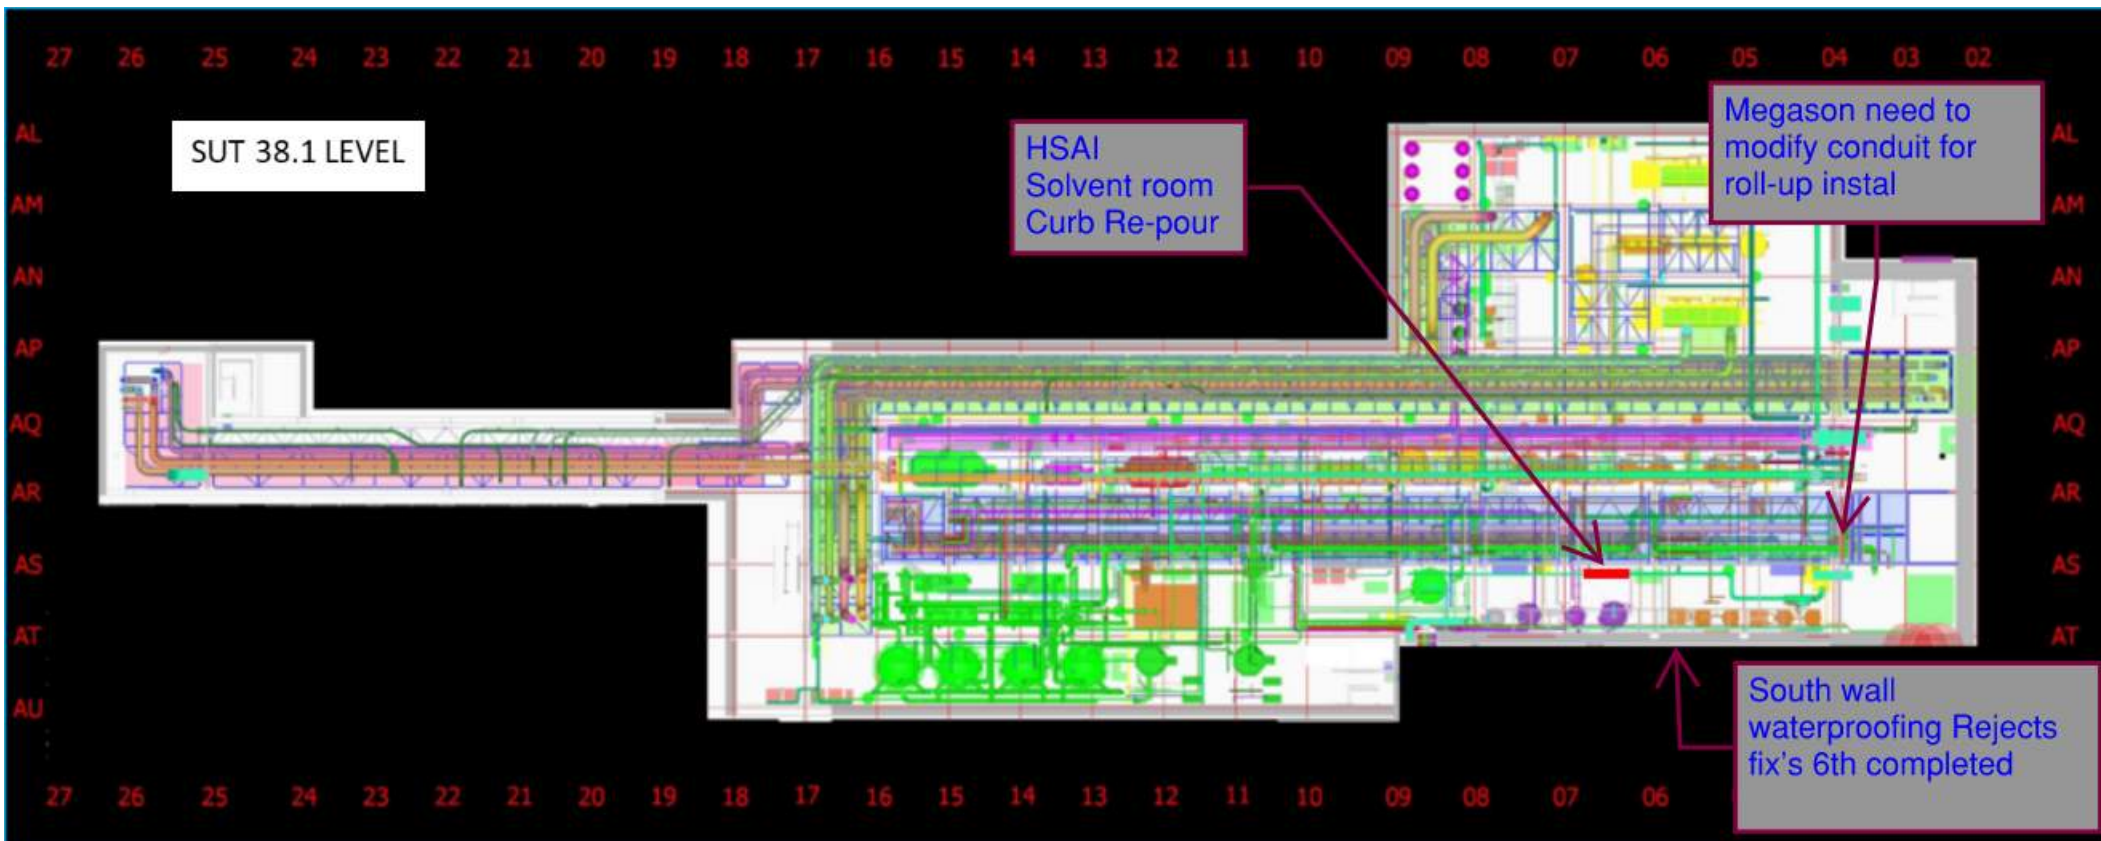


SUBFAB BUILDOUT MOD 1

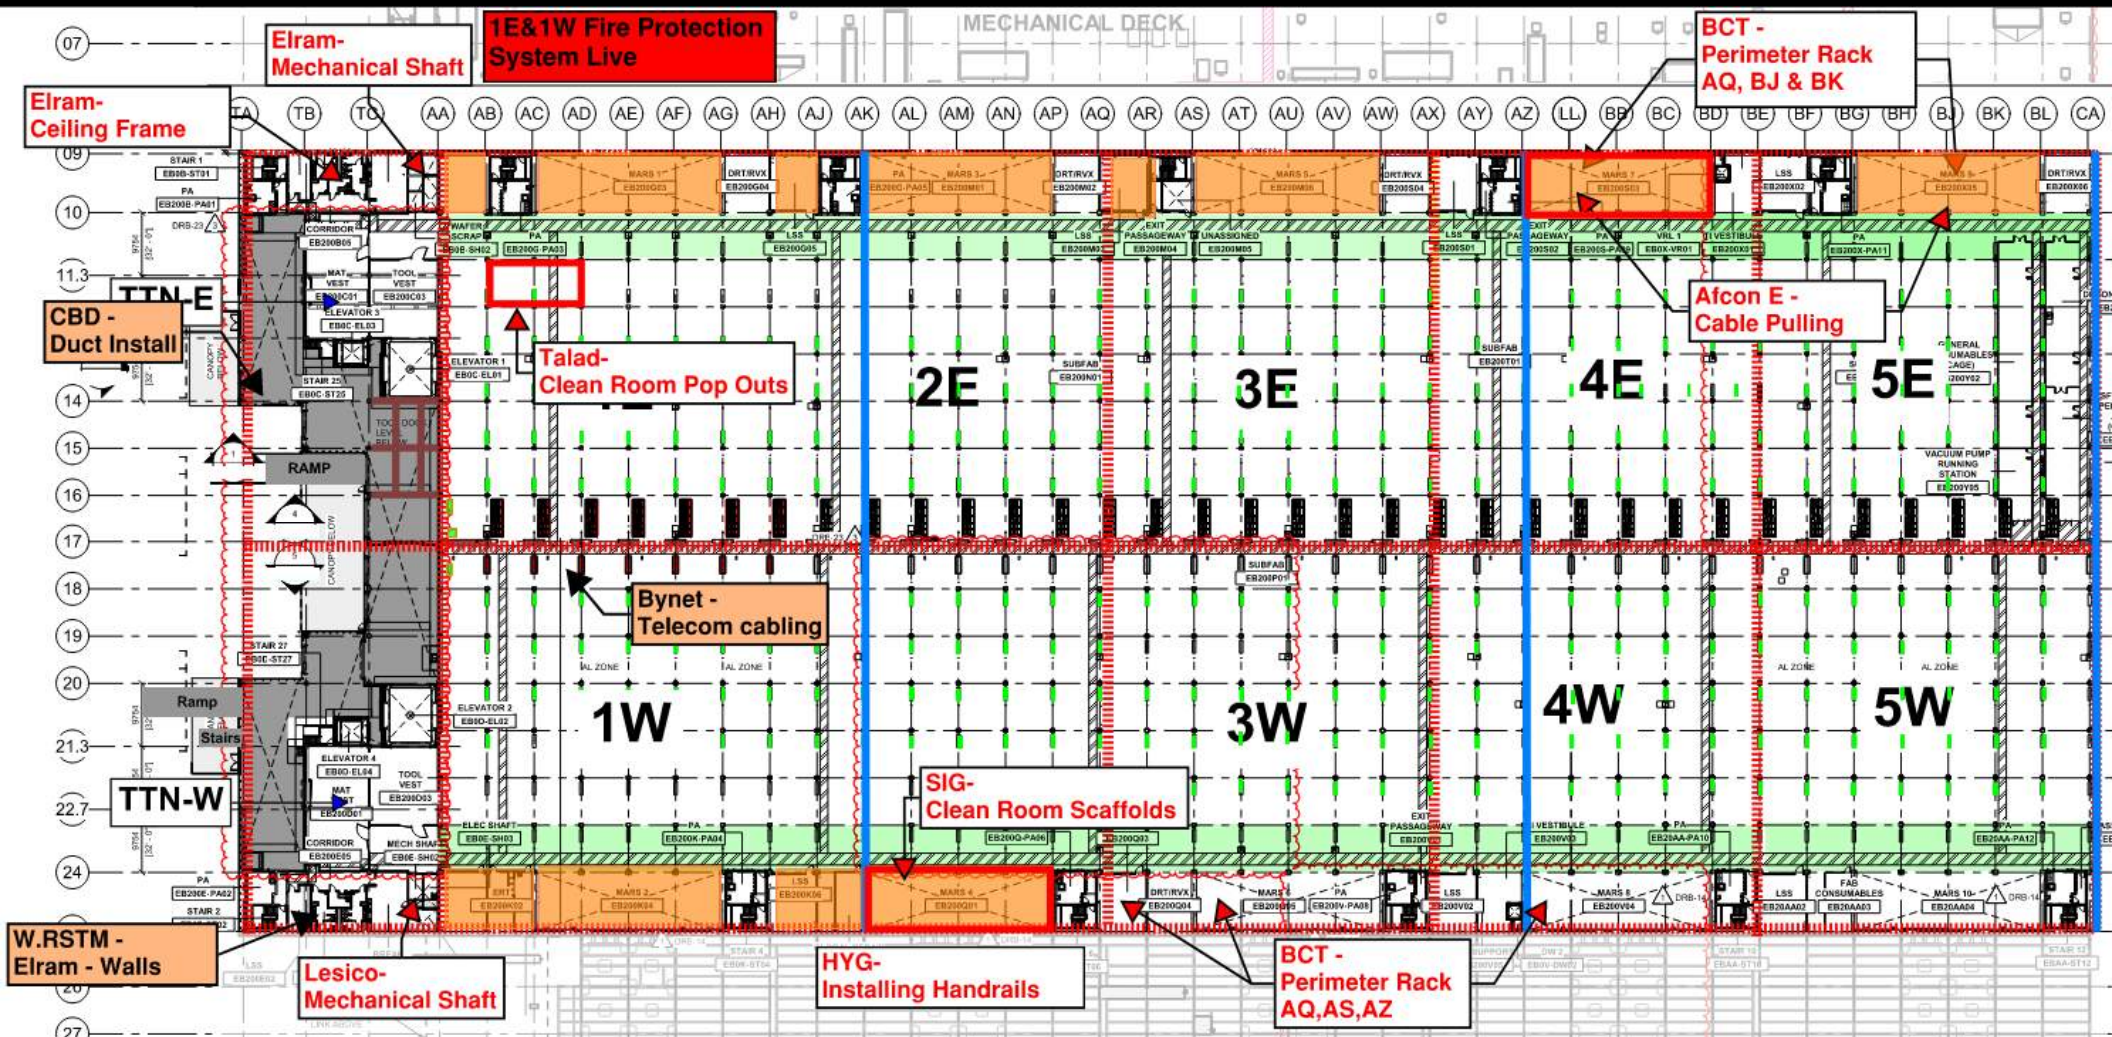


SUBFAB CRC TOPCOAT

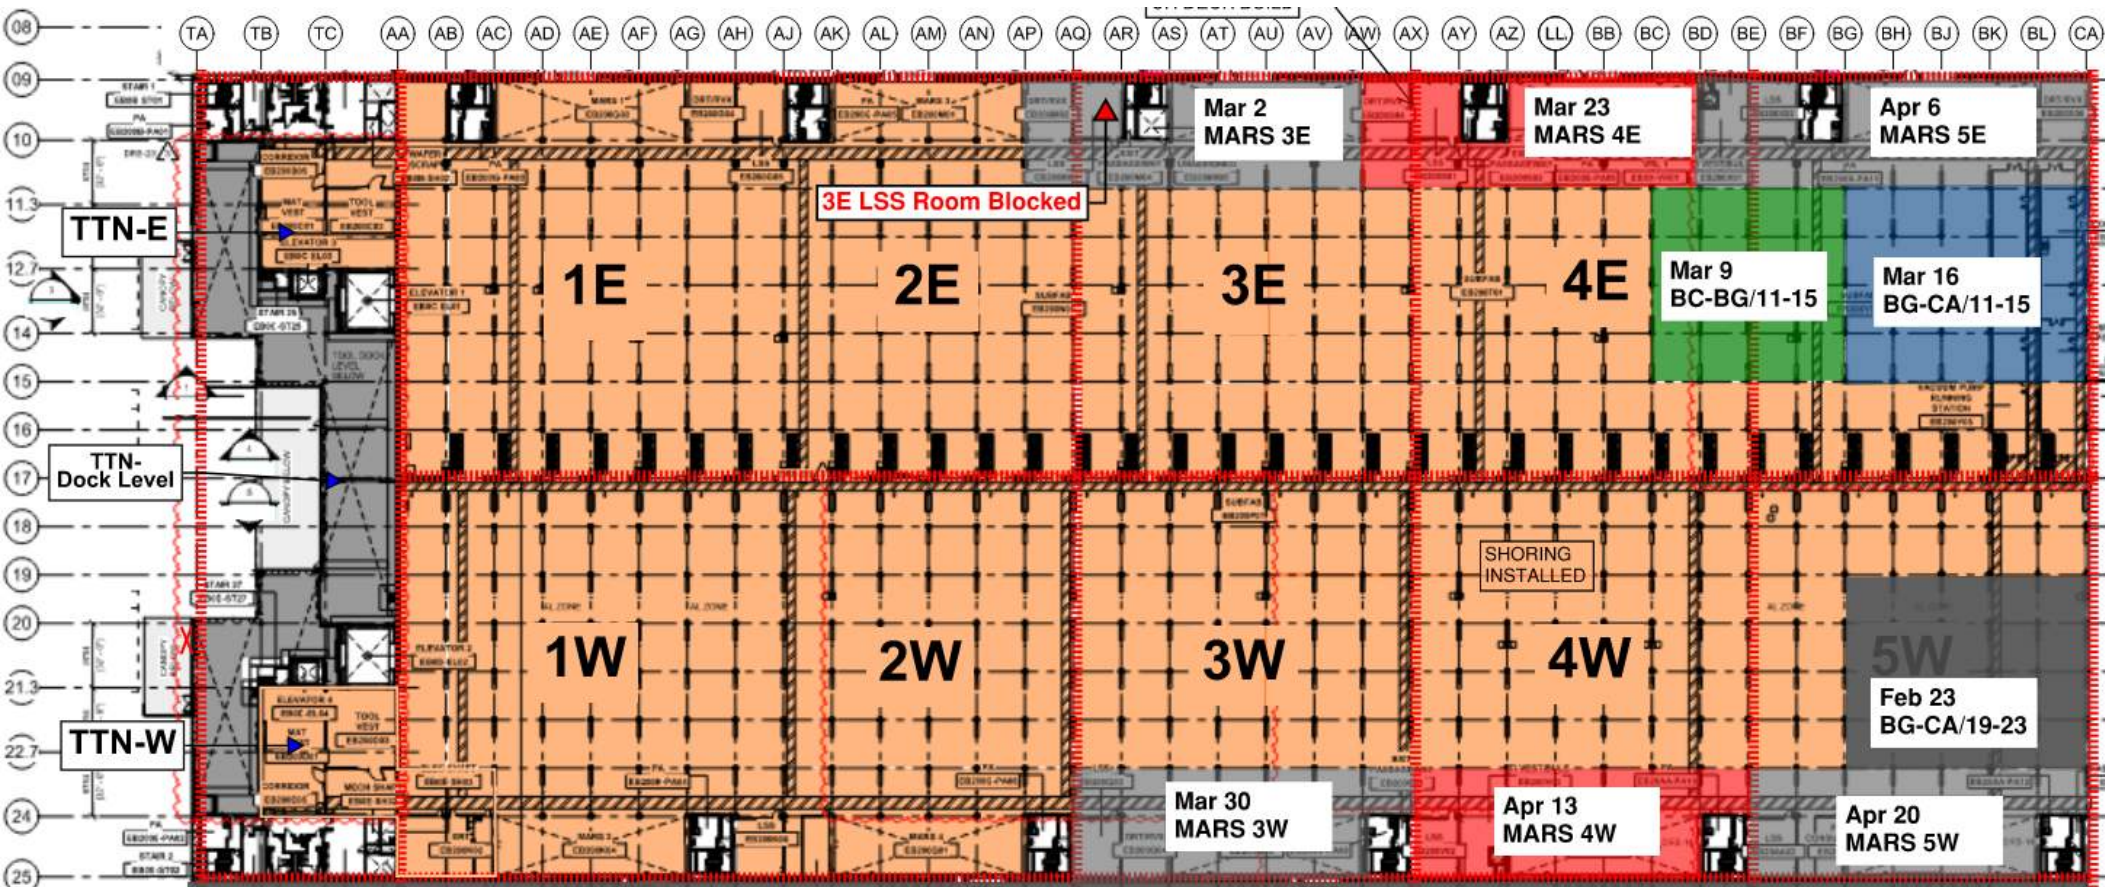


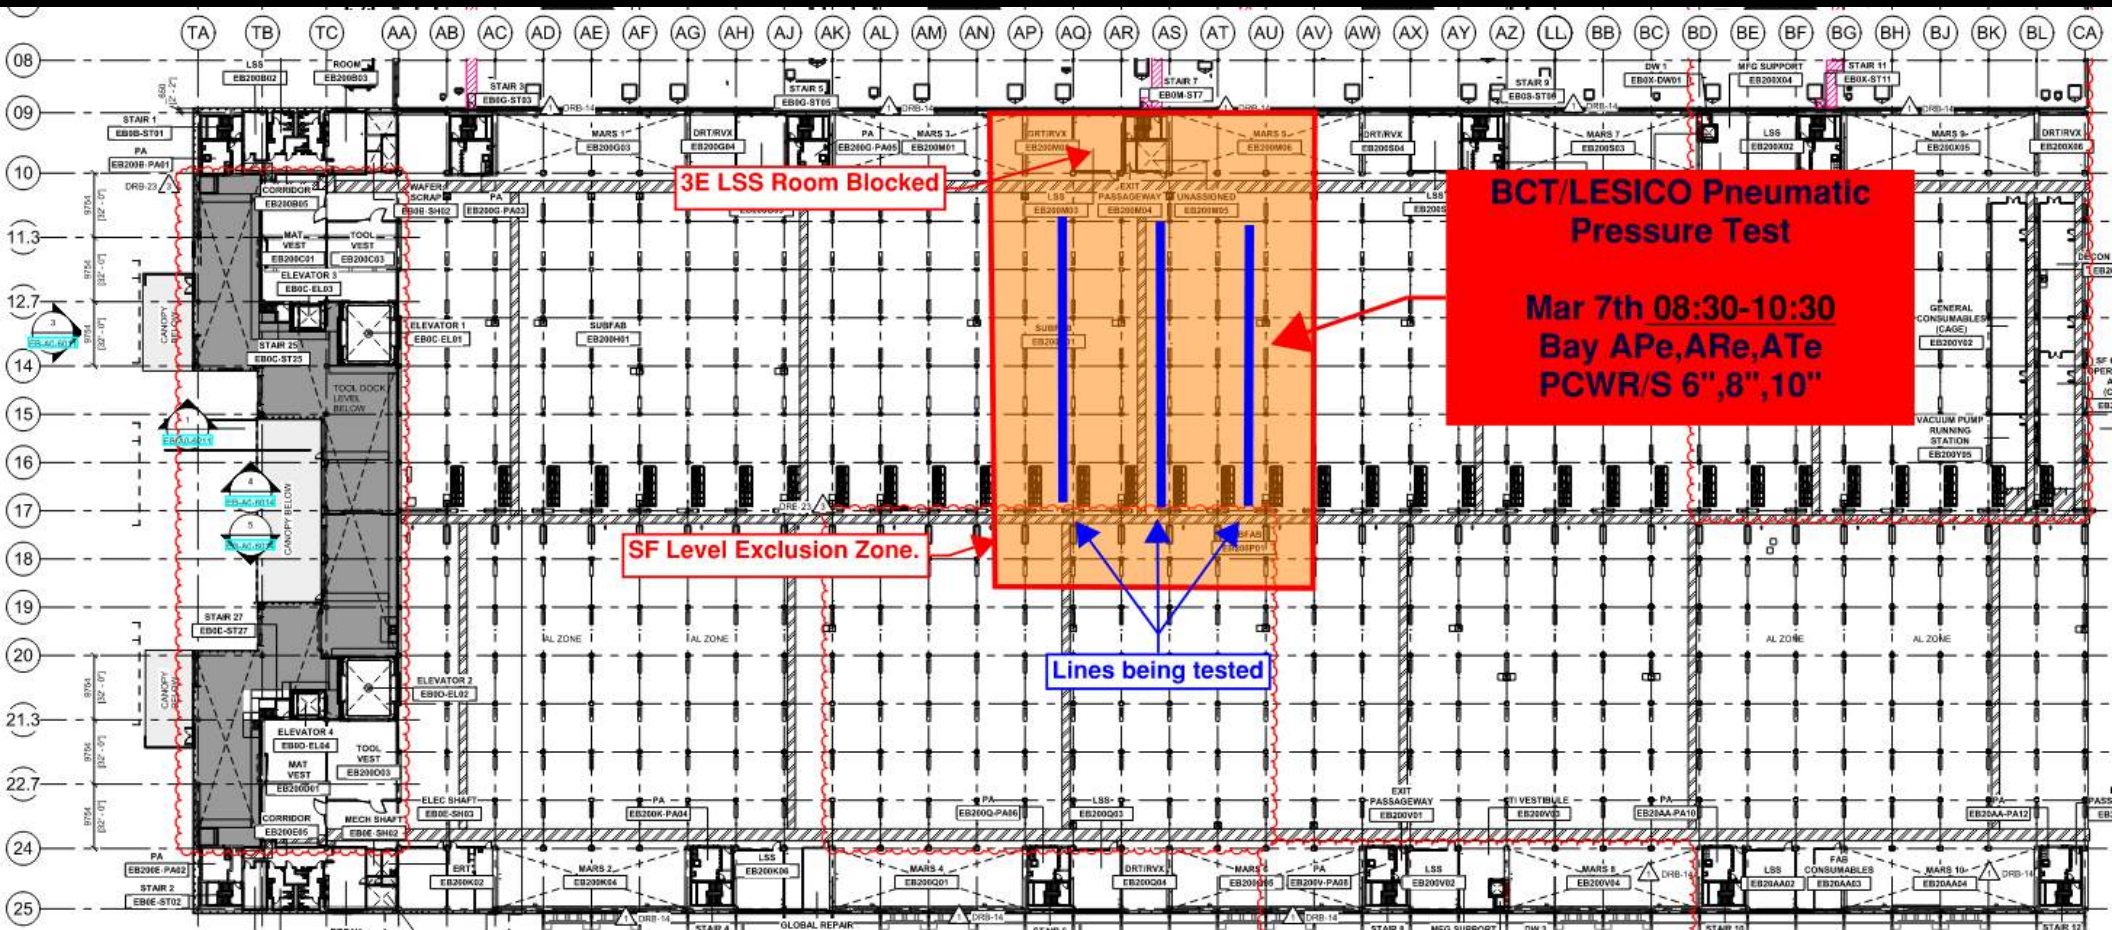




BCT Pressure Test

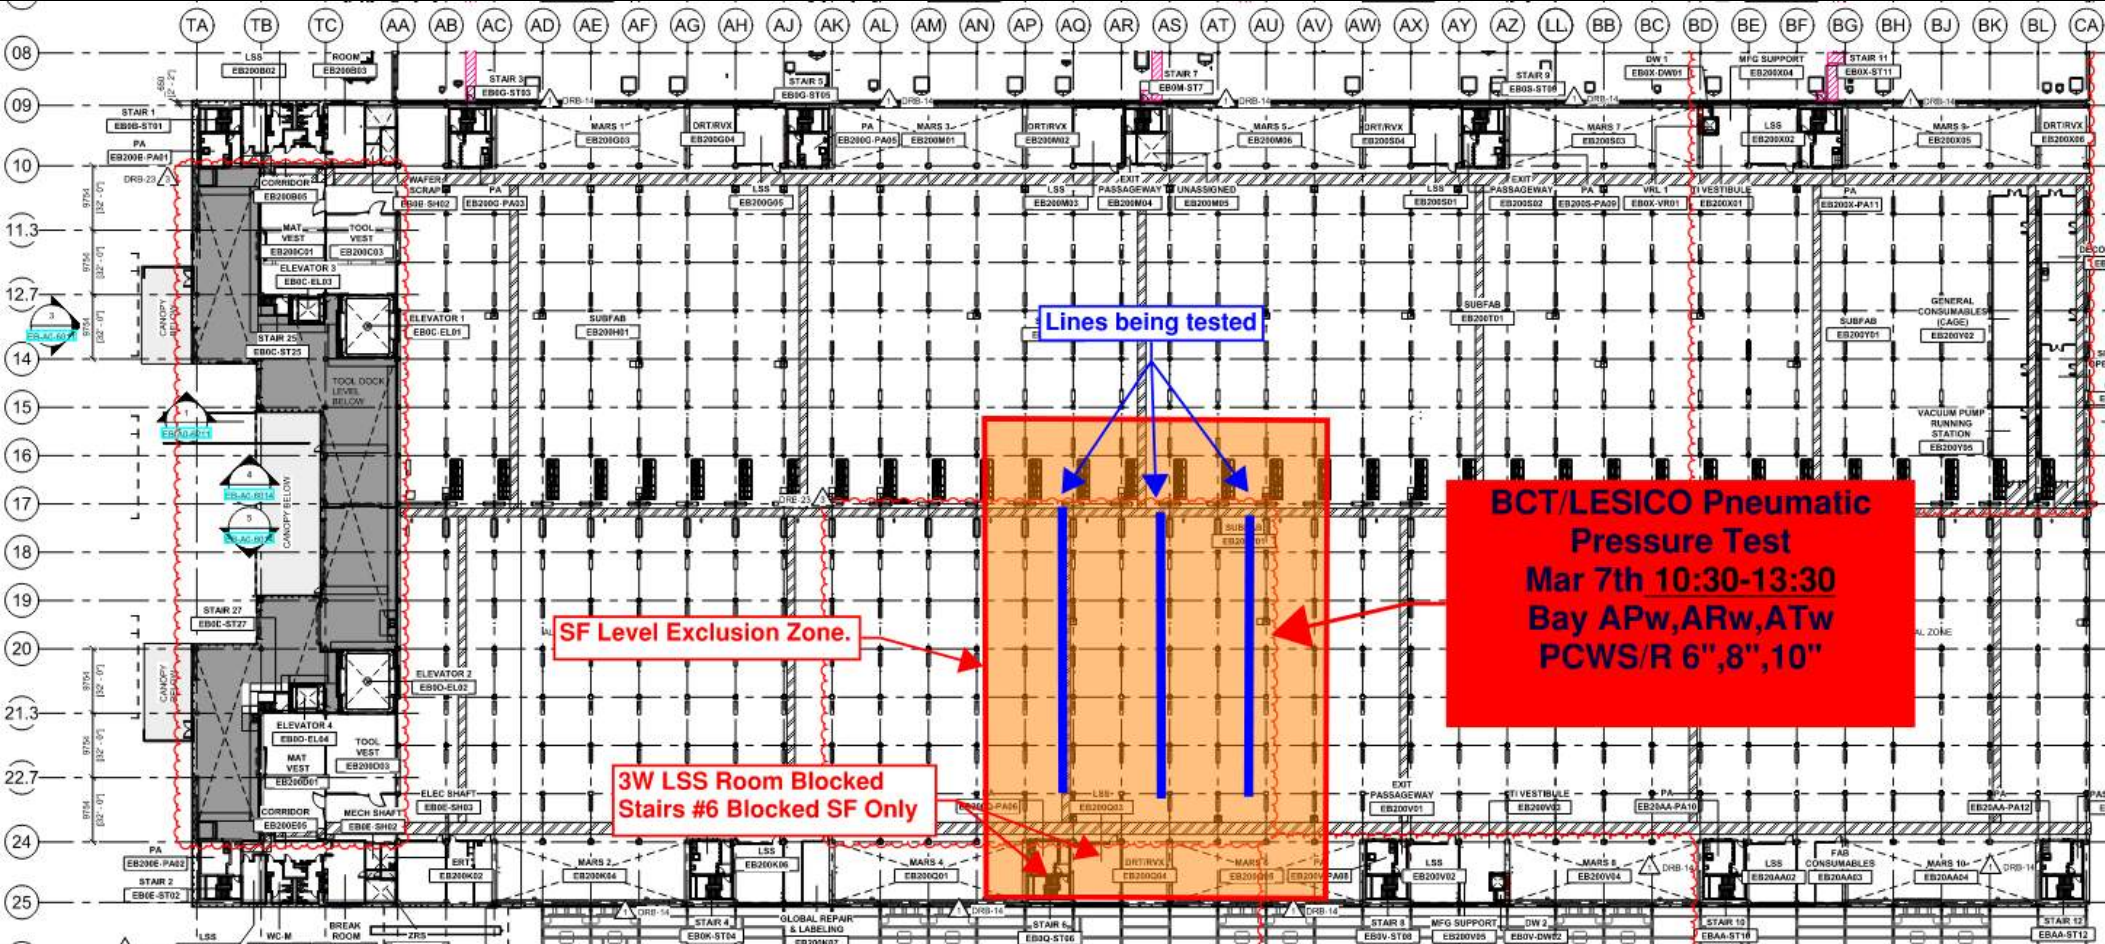


SUBFAB BUILDOUT MOD 2

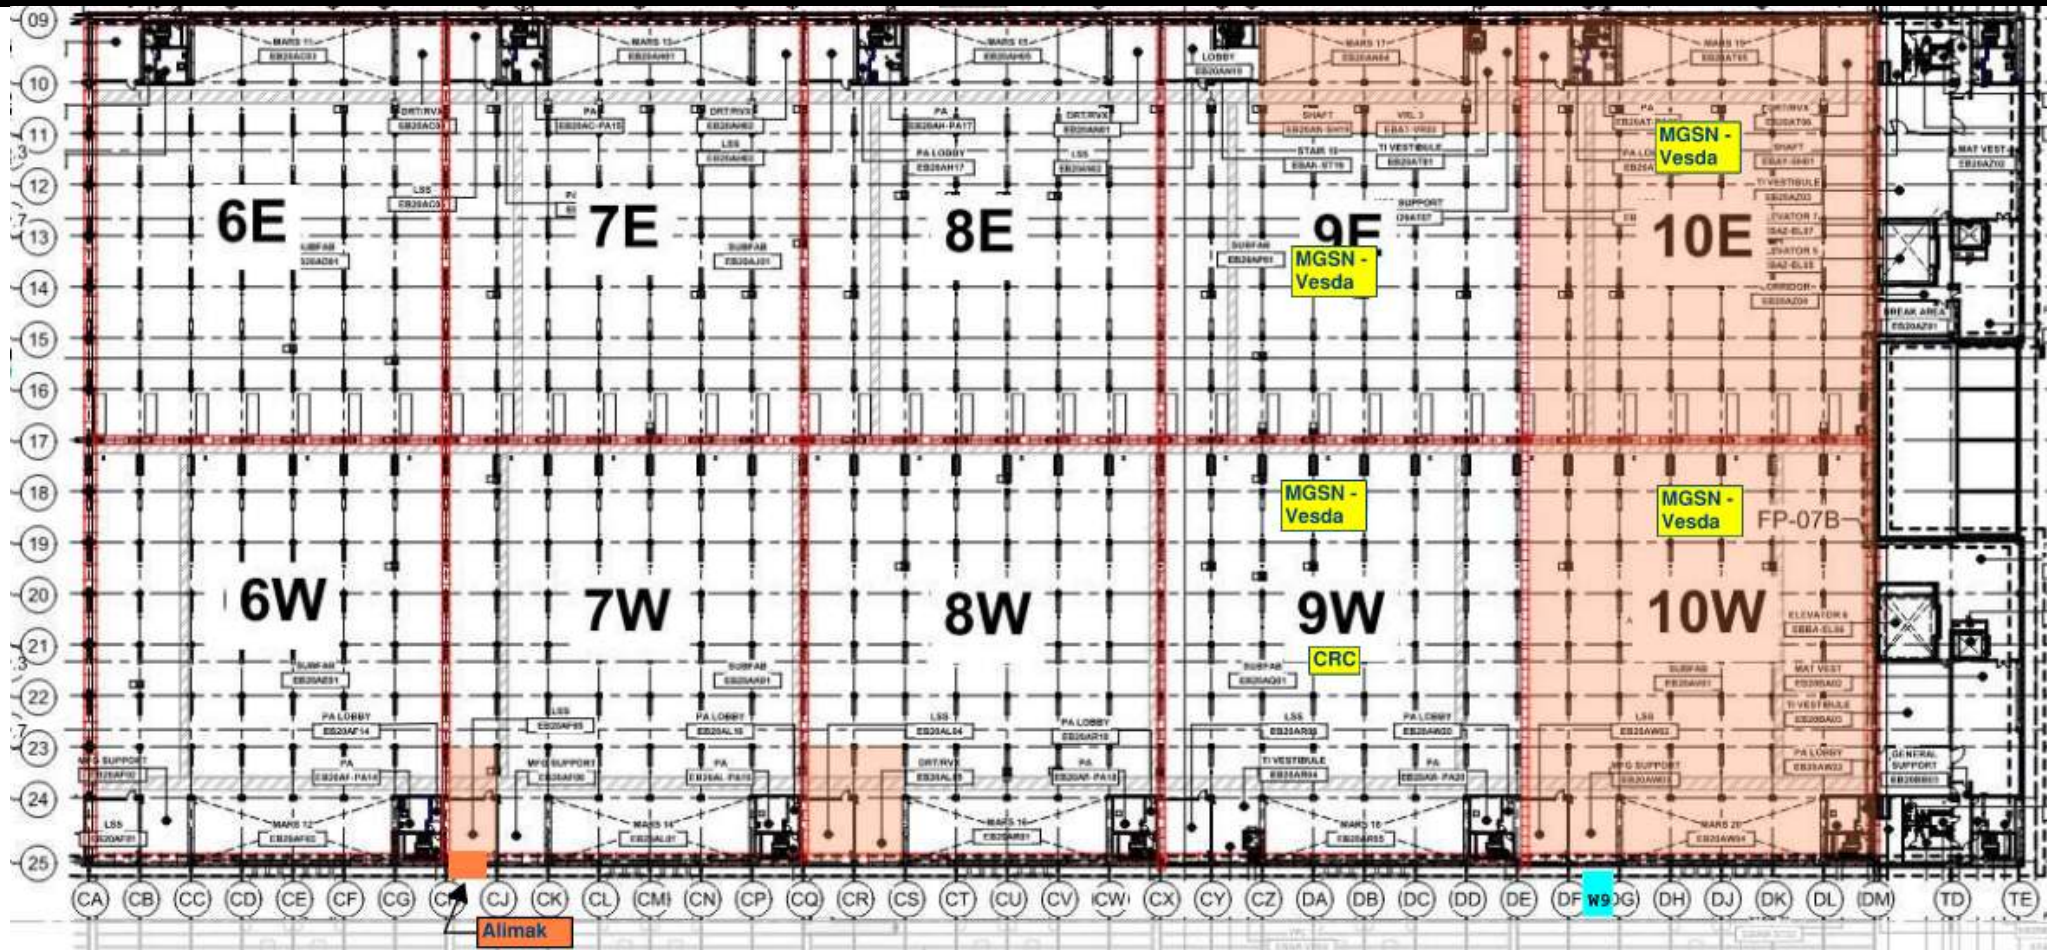


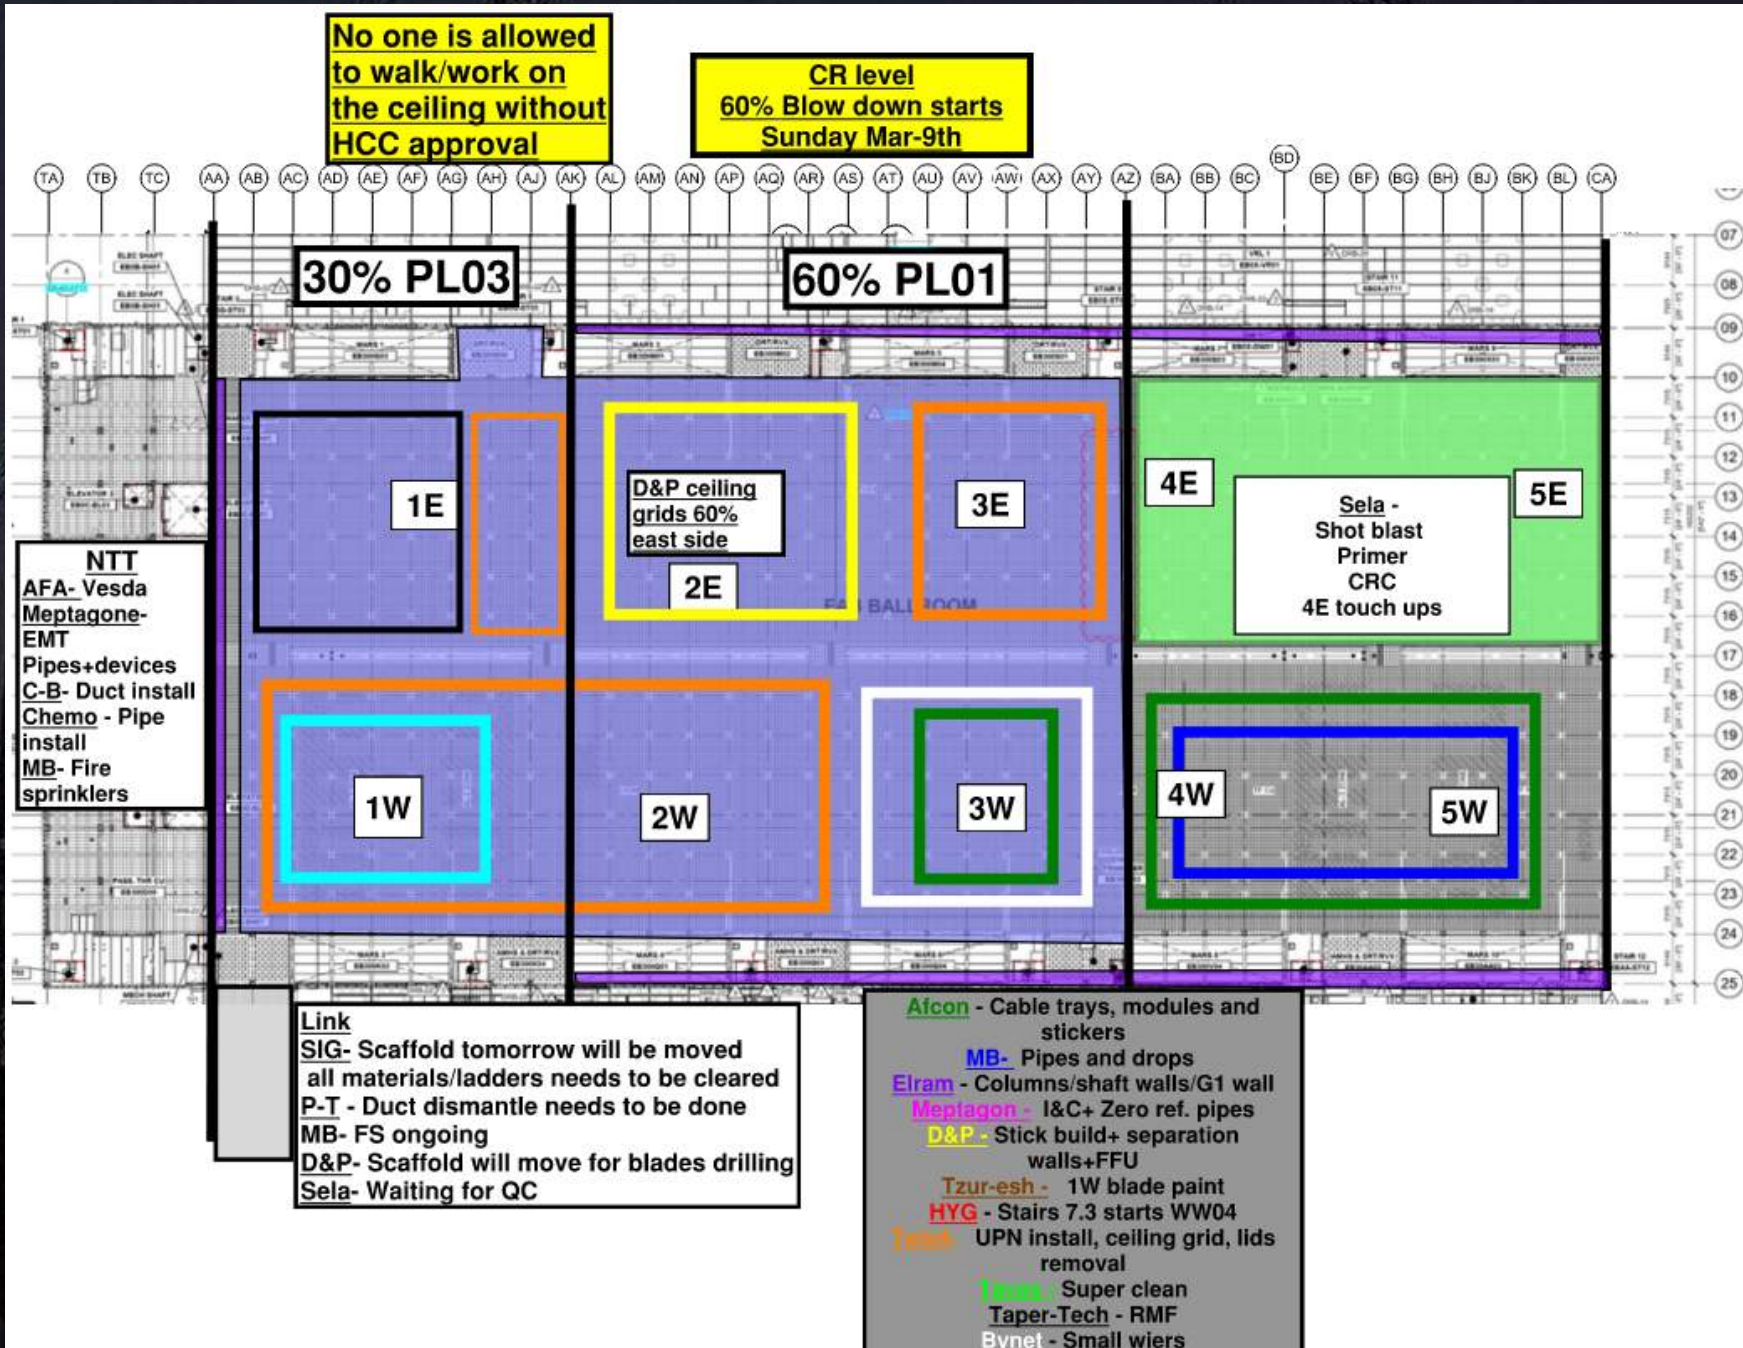

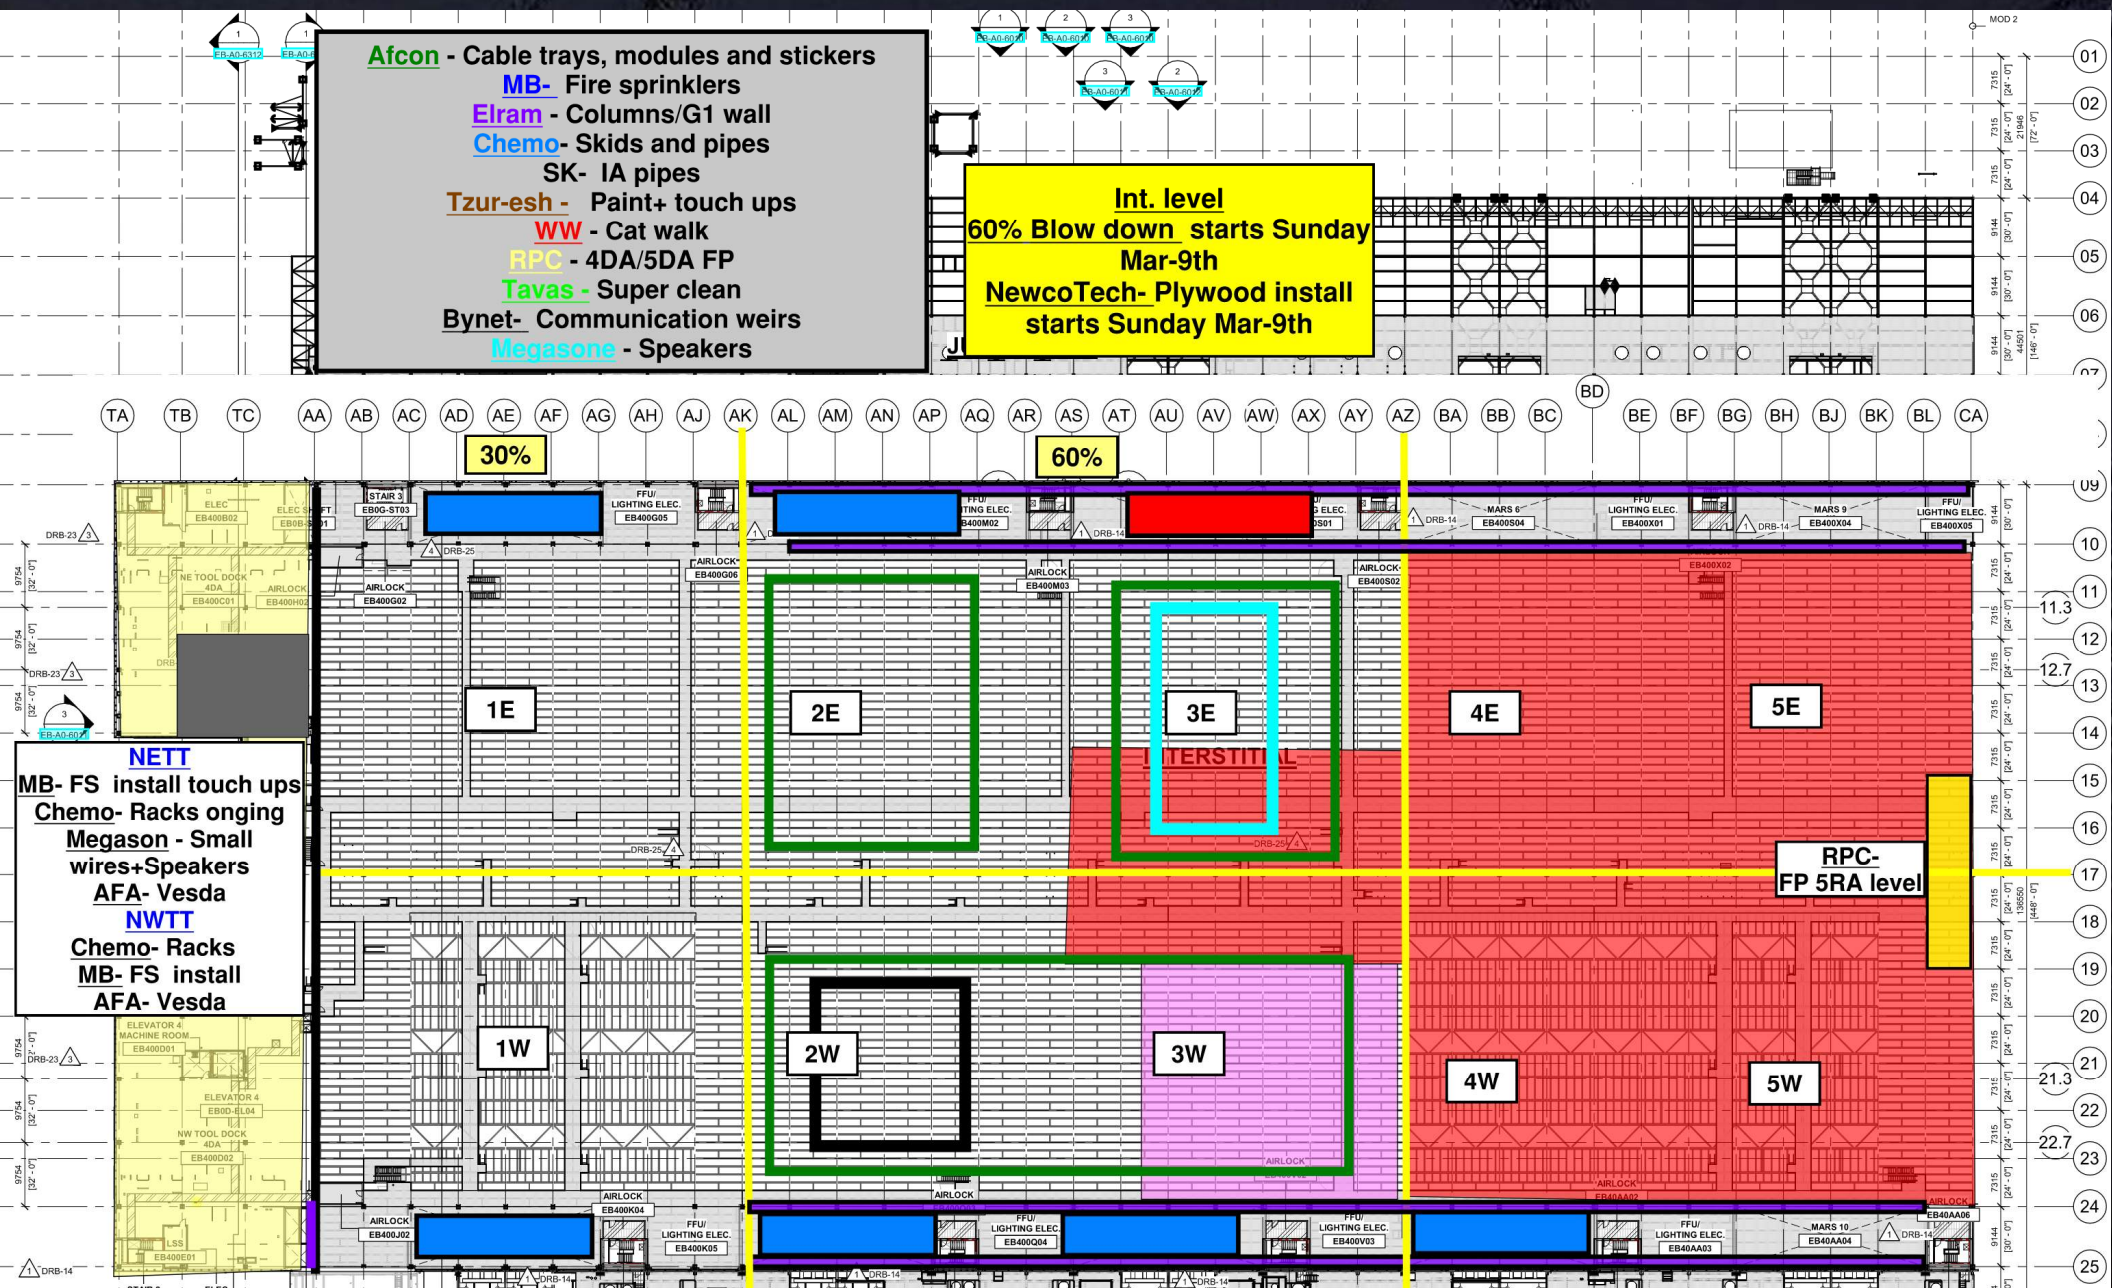


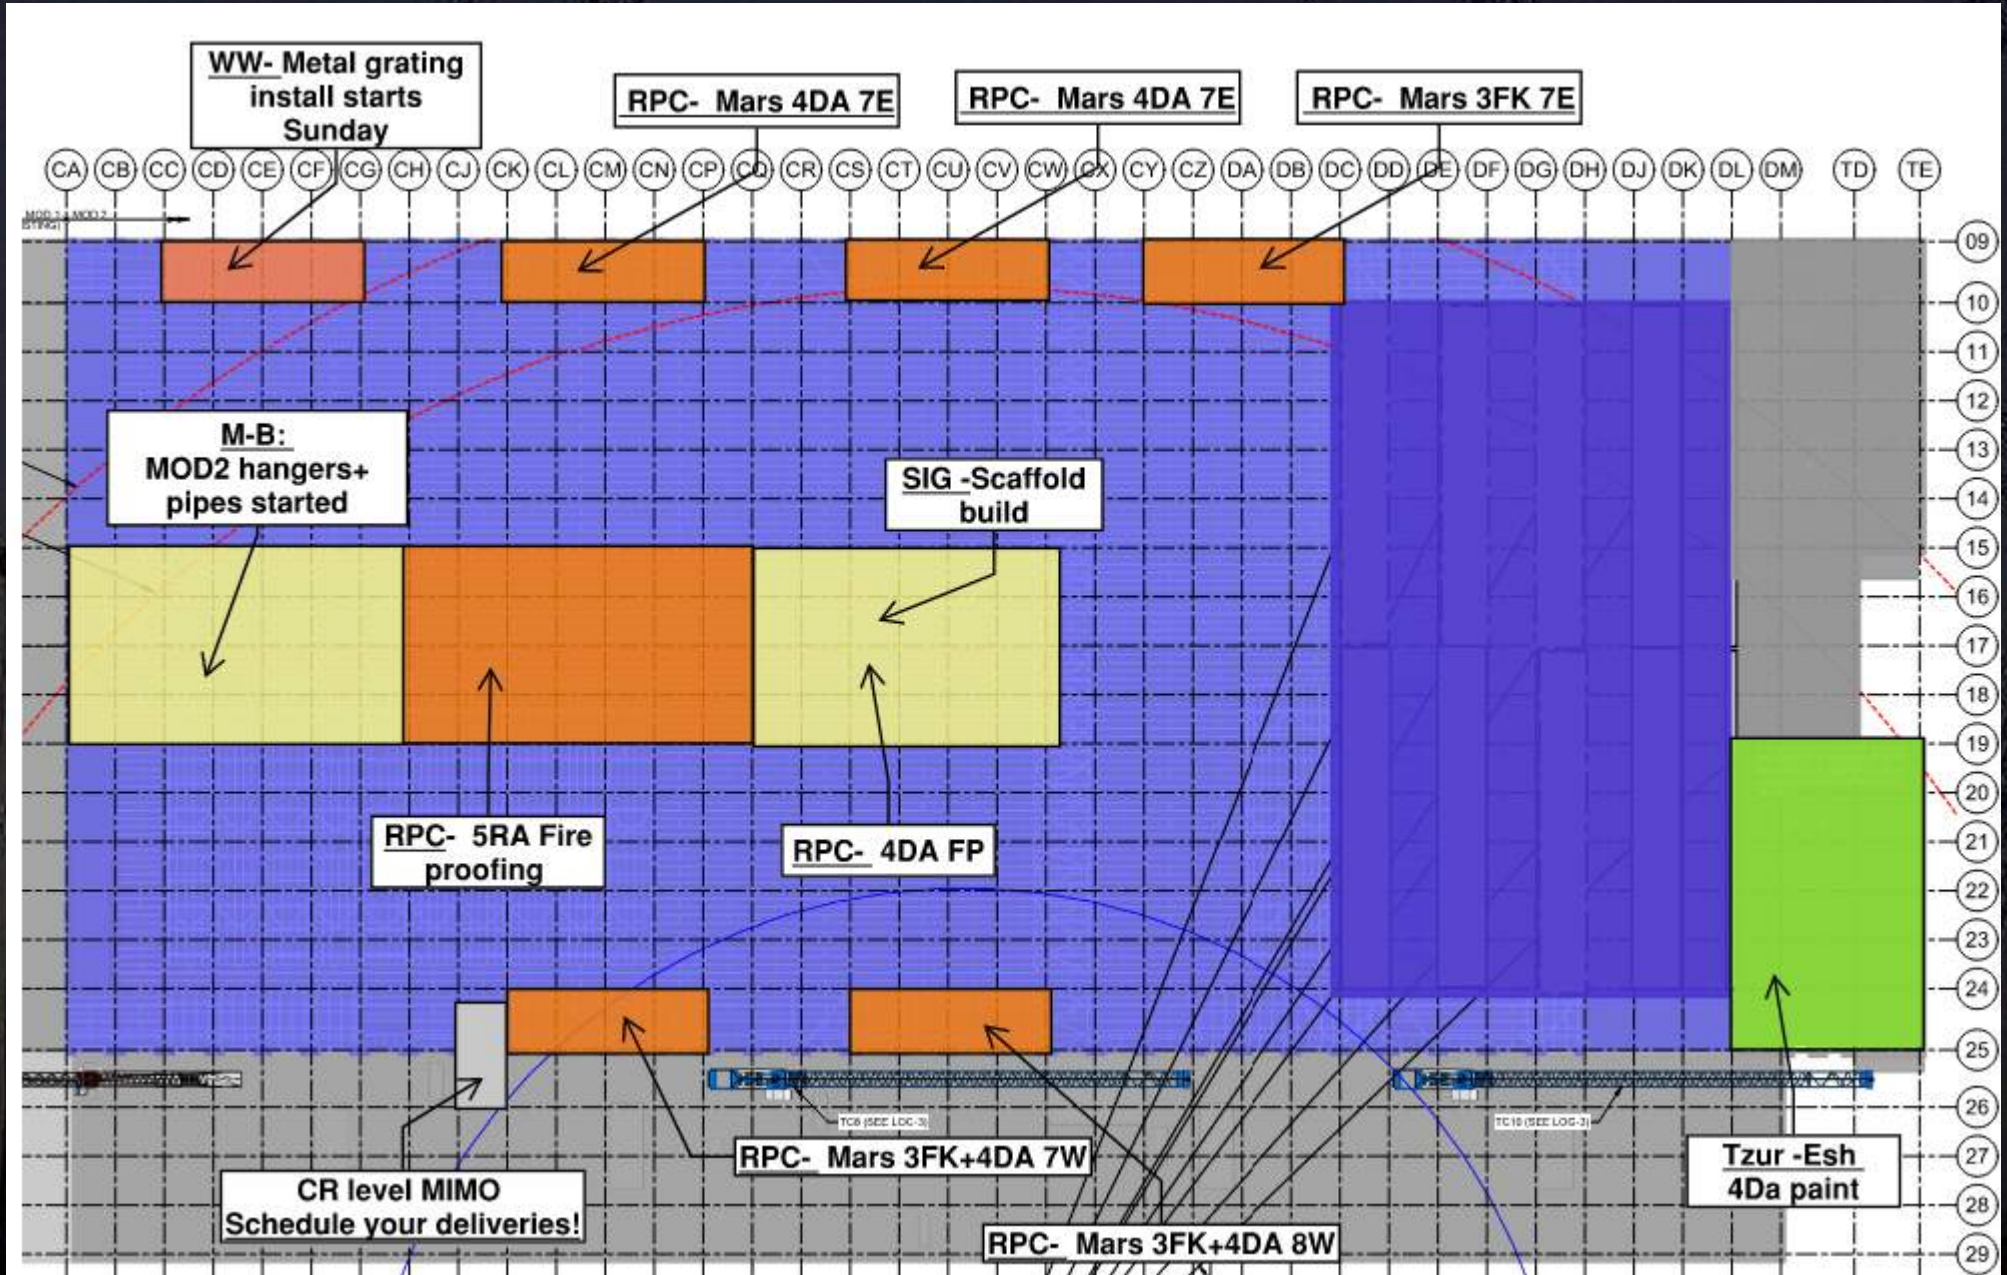

Siding Penetration Request Form

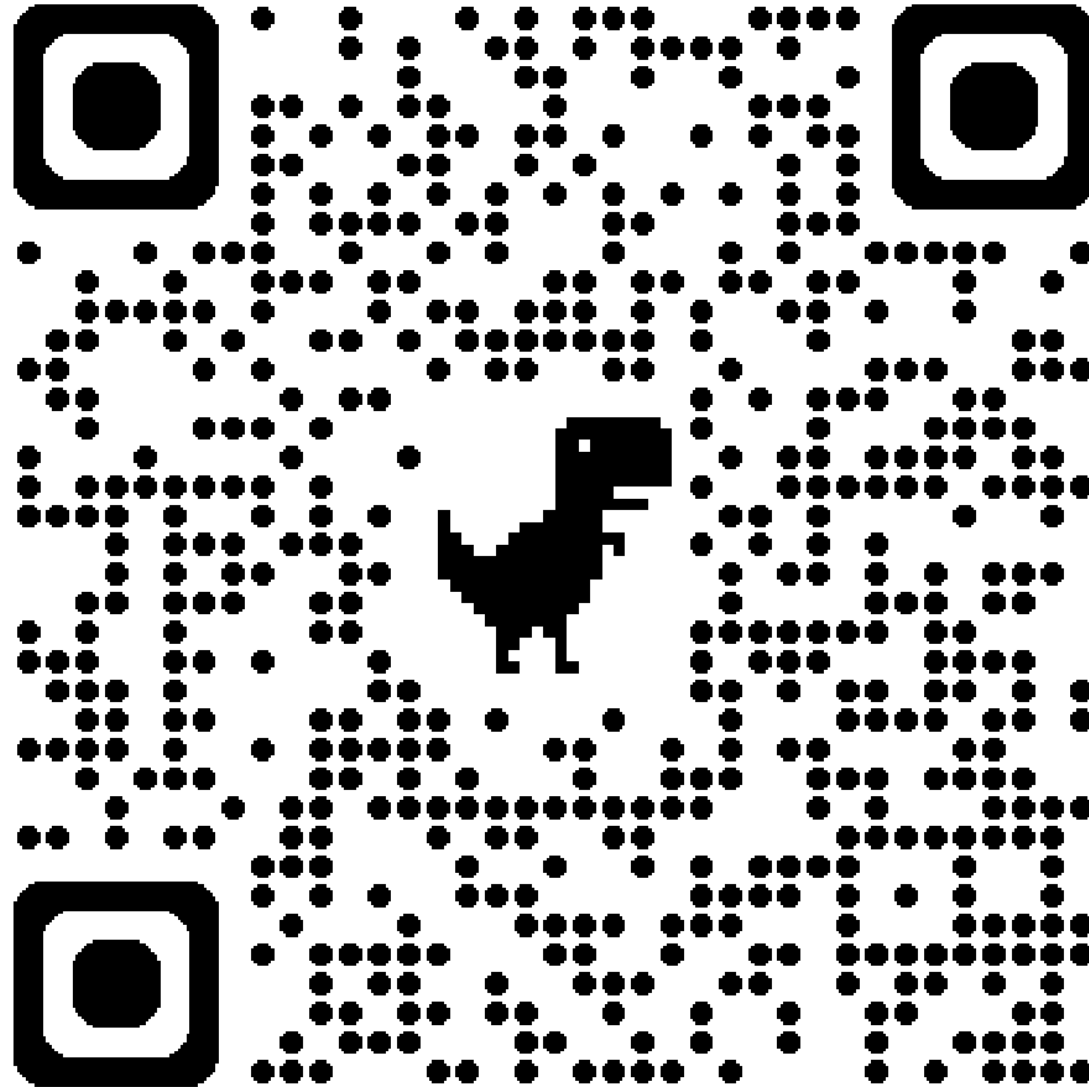

Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

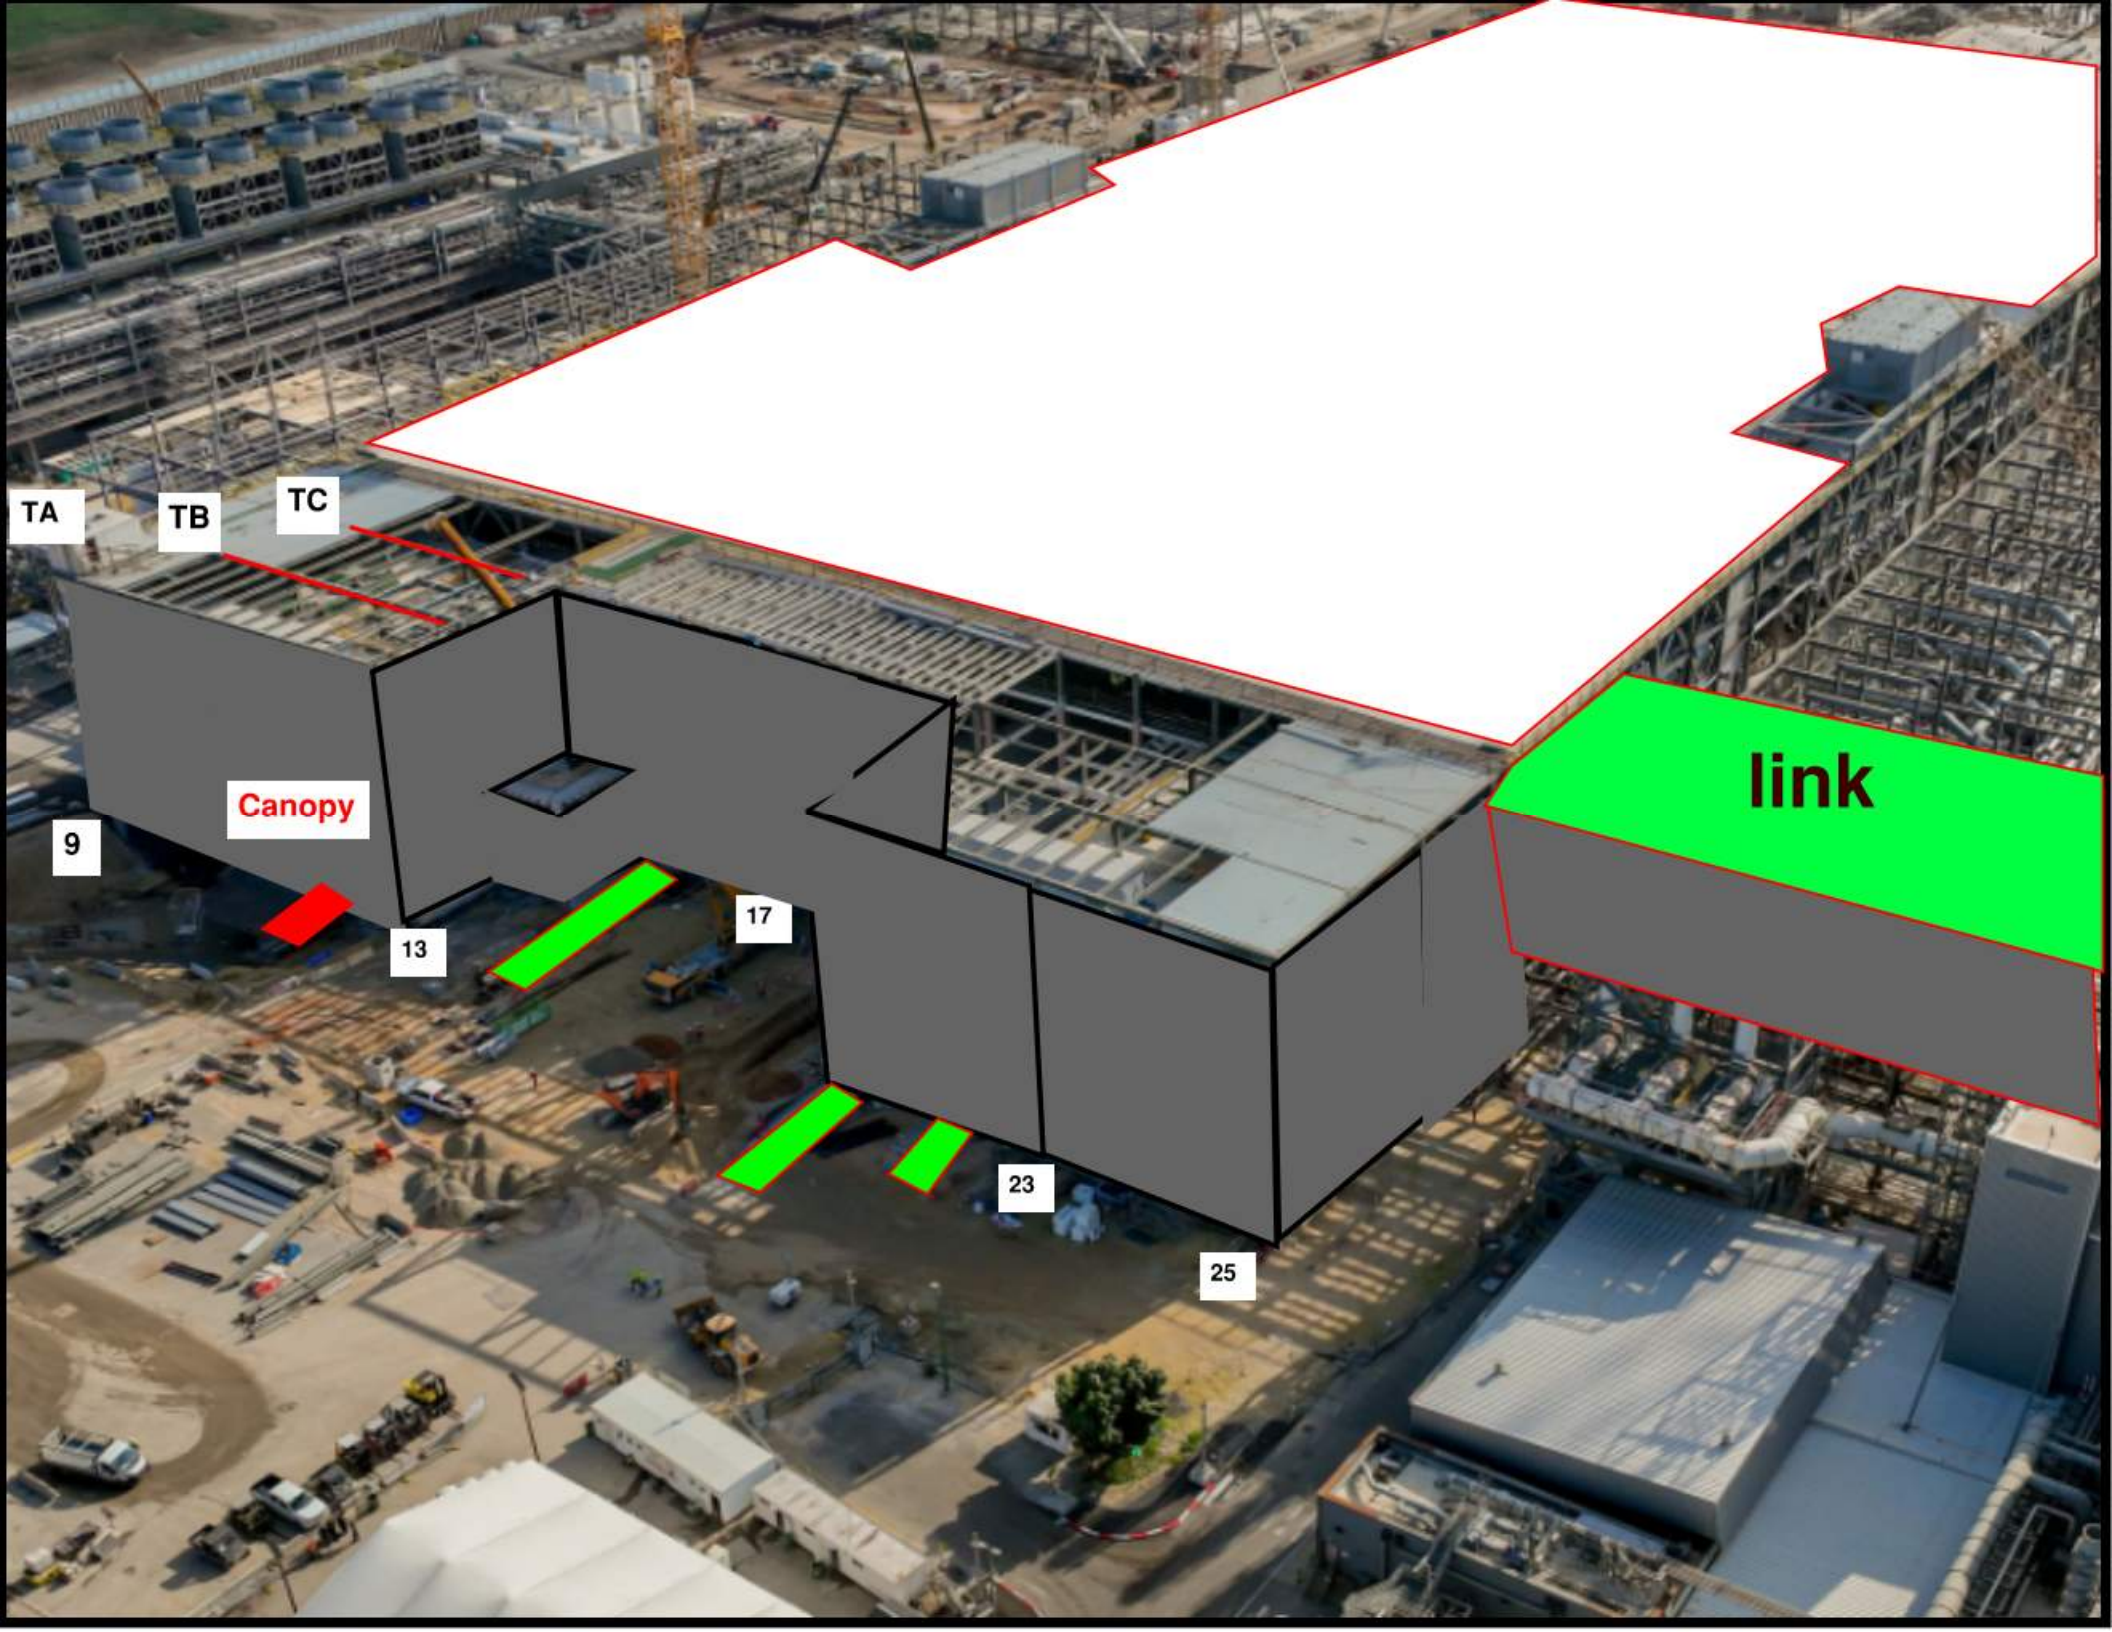

TA

TB

TC

Canopy

9

13

17

23

25

link



MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 


PANELS INSTALLED 



PSSS.1

Utility Level
1YA


PSSS Roof
2SA

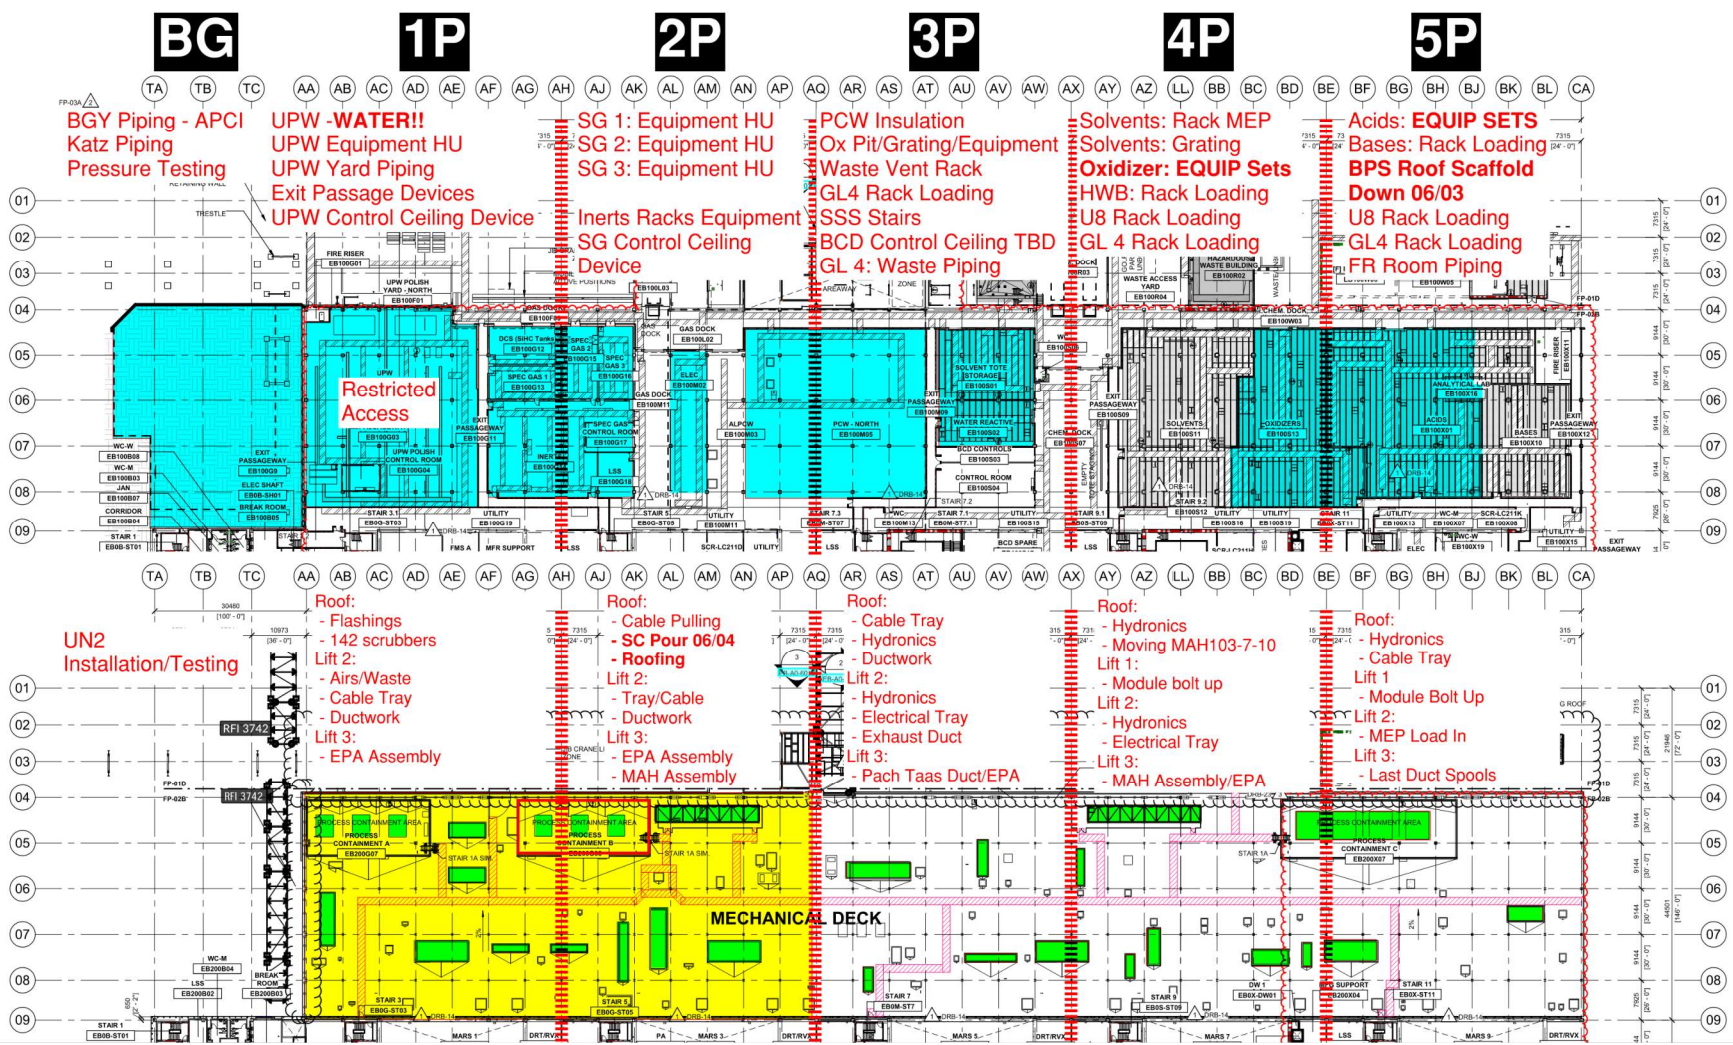

PSSS.2


Utility Level
1YA

PSSS Roof
2SA

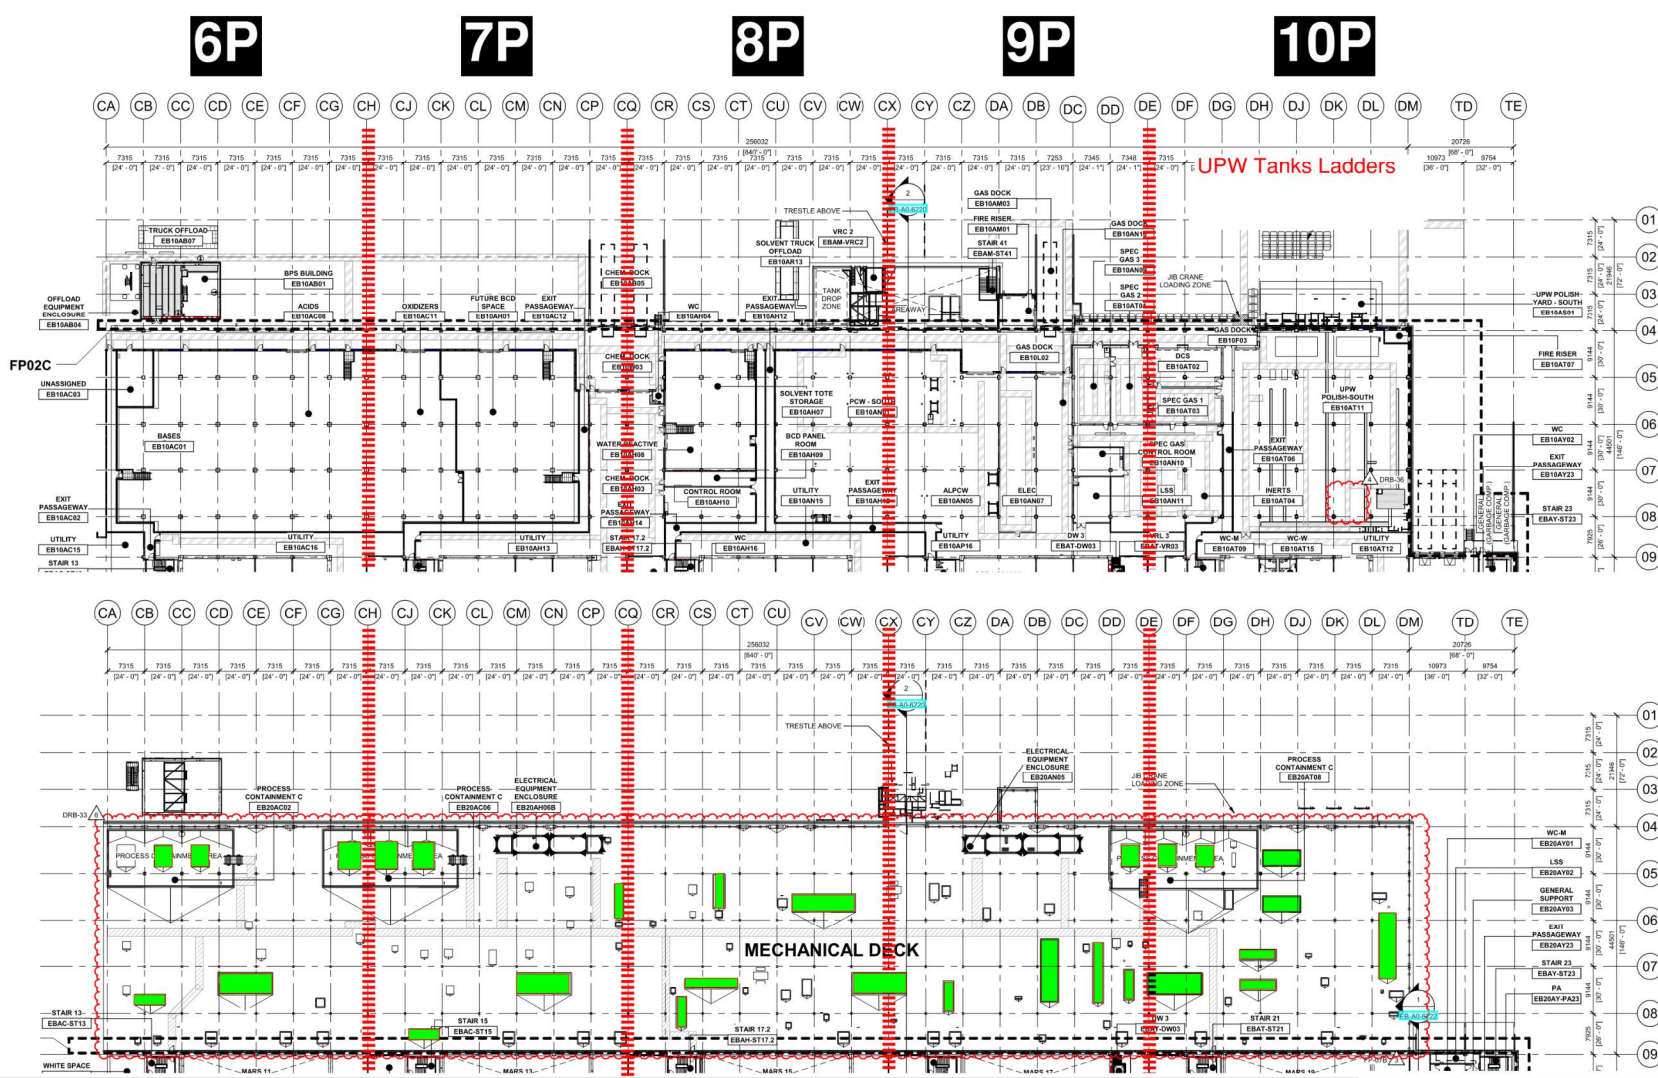


PSSS Pressure Testing

Utility Level
1YA

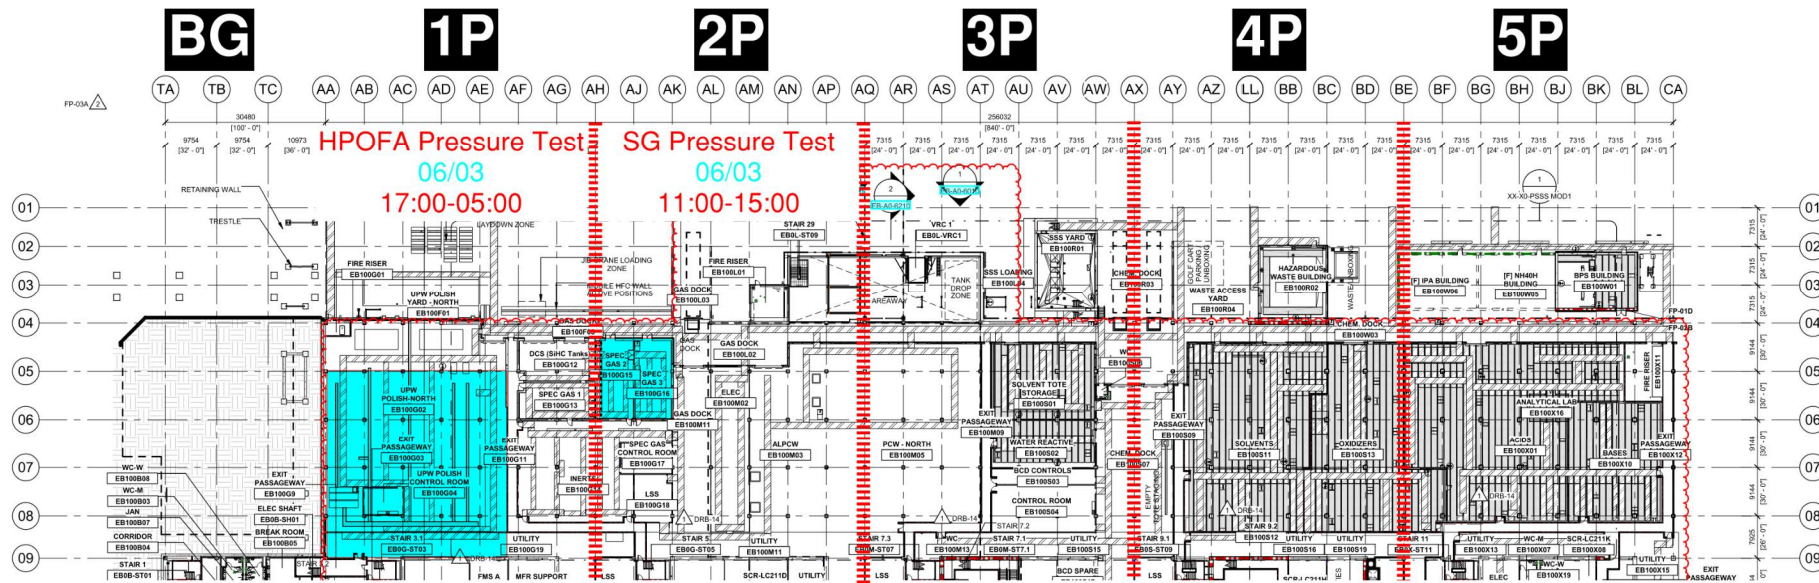

3800 Dismantle WW10

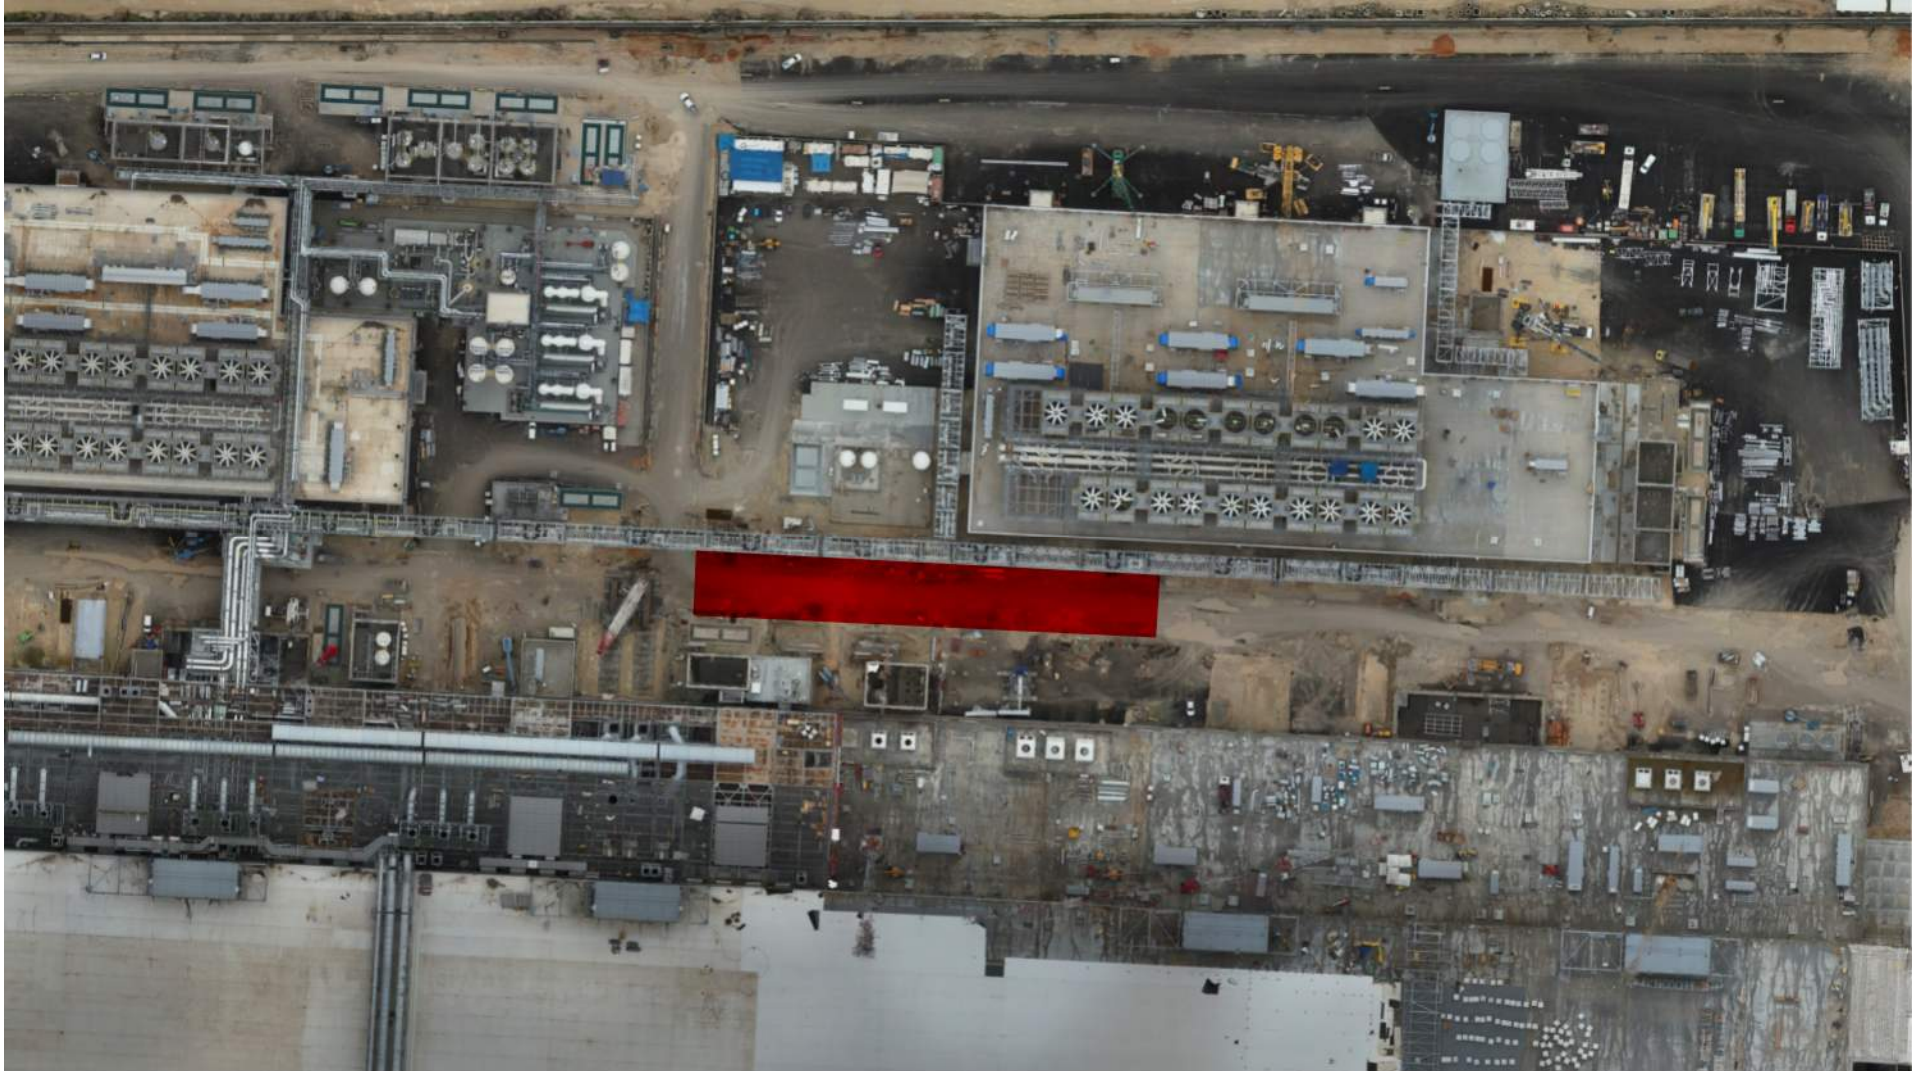

BGY Closed WW11 For UN2 Blowdown




WJG – UL

* Carmel Bidud - installation of ducts from small AH to FAB

* Pach Taas - installation of modules in west SUT.
* Pach Taas - new scaffold waiting for green tag for installation of spools to wall panels

* SK - installation of 3" cooper pipe
* W&W - welding of shims for outriggers

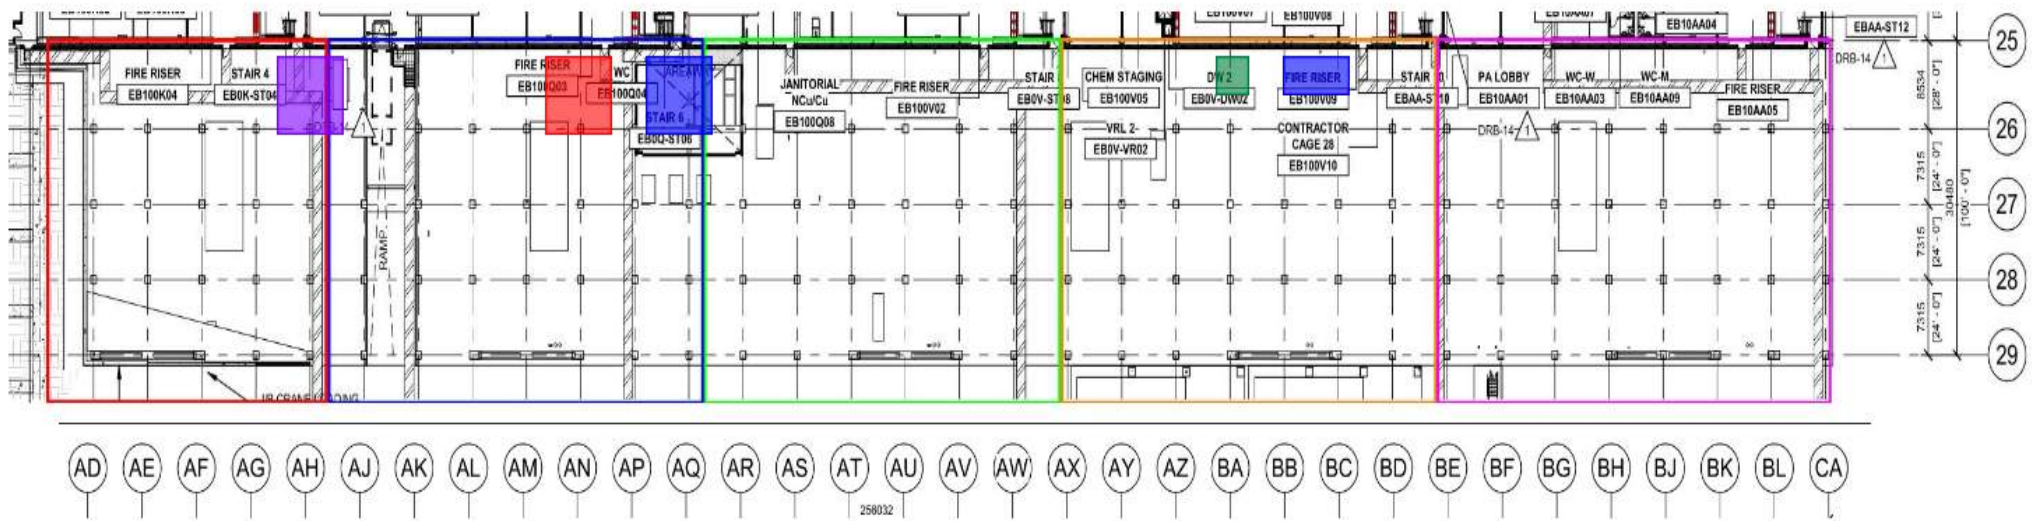


WJG – Lift 2

* Chemo - moving Nalco skid south for flushing of UPN 113

* Pach Taas -connection to single stack to exhaust fans

* Carmel Bidud - dismantling MAH scaffold

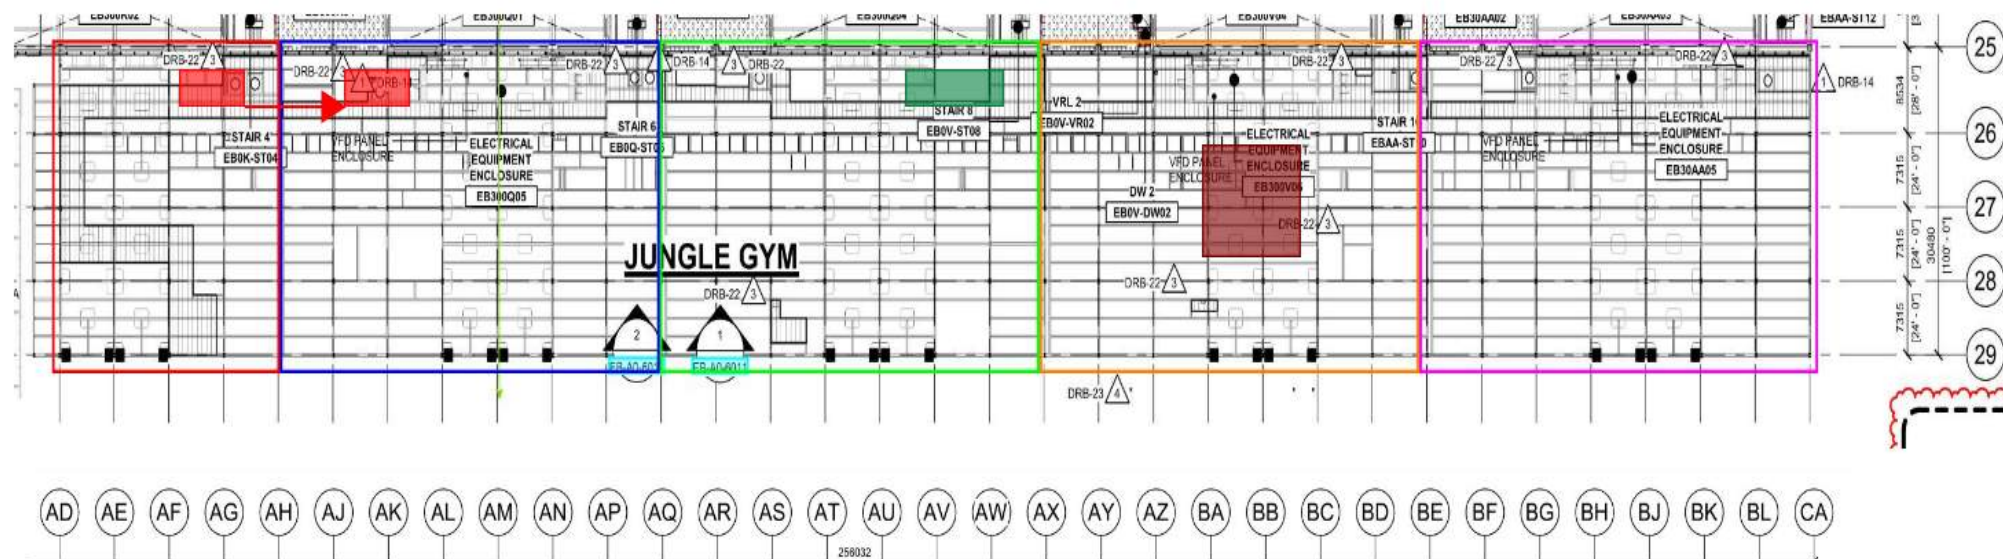

WJG – Lift 3

W&W - welding supports for gratings		* Pach Taas - hoisting and installing roof crossover ductwork	* SN -preparations for removing grating for Pach Taas equipment set	
-------------------------------------	--	---	---	--




Crane logistics

Crane: 750 ton crane
located at AV-AW.






CUB 1

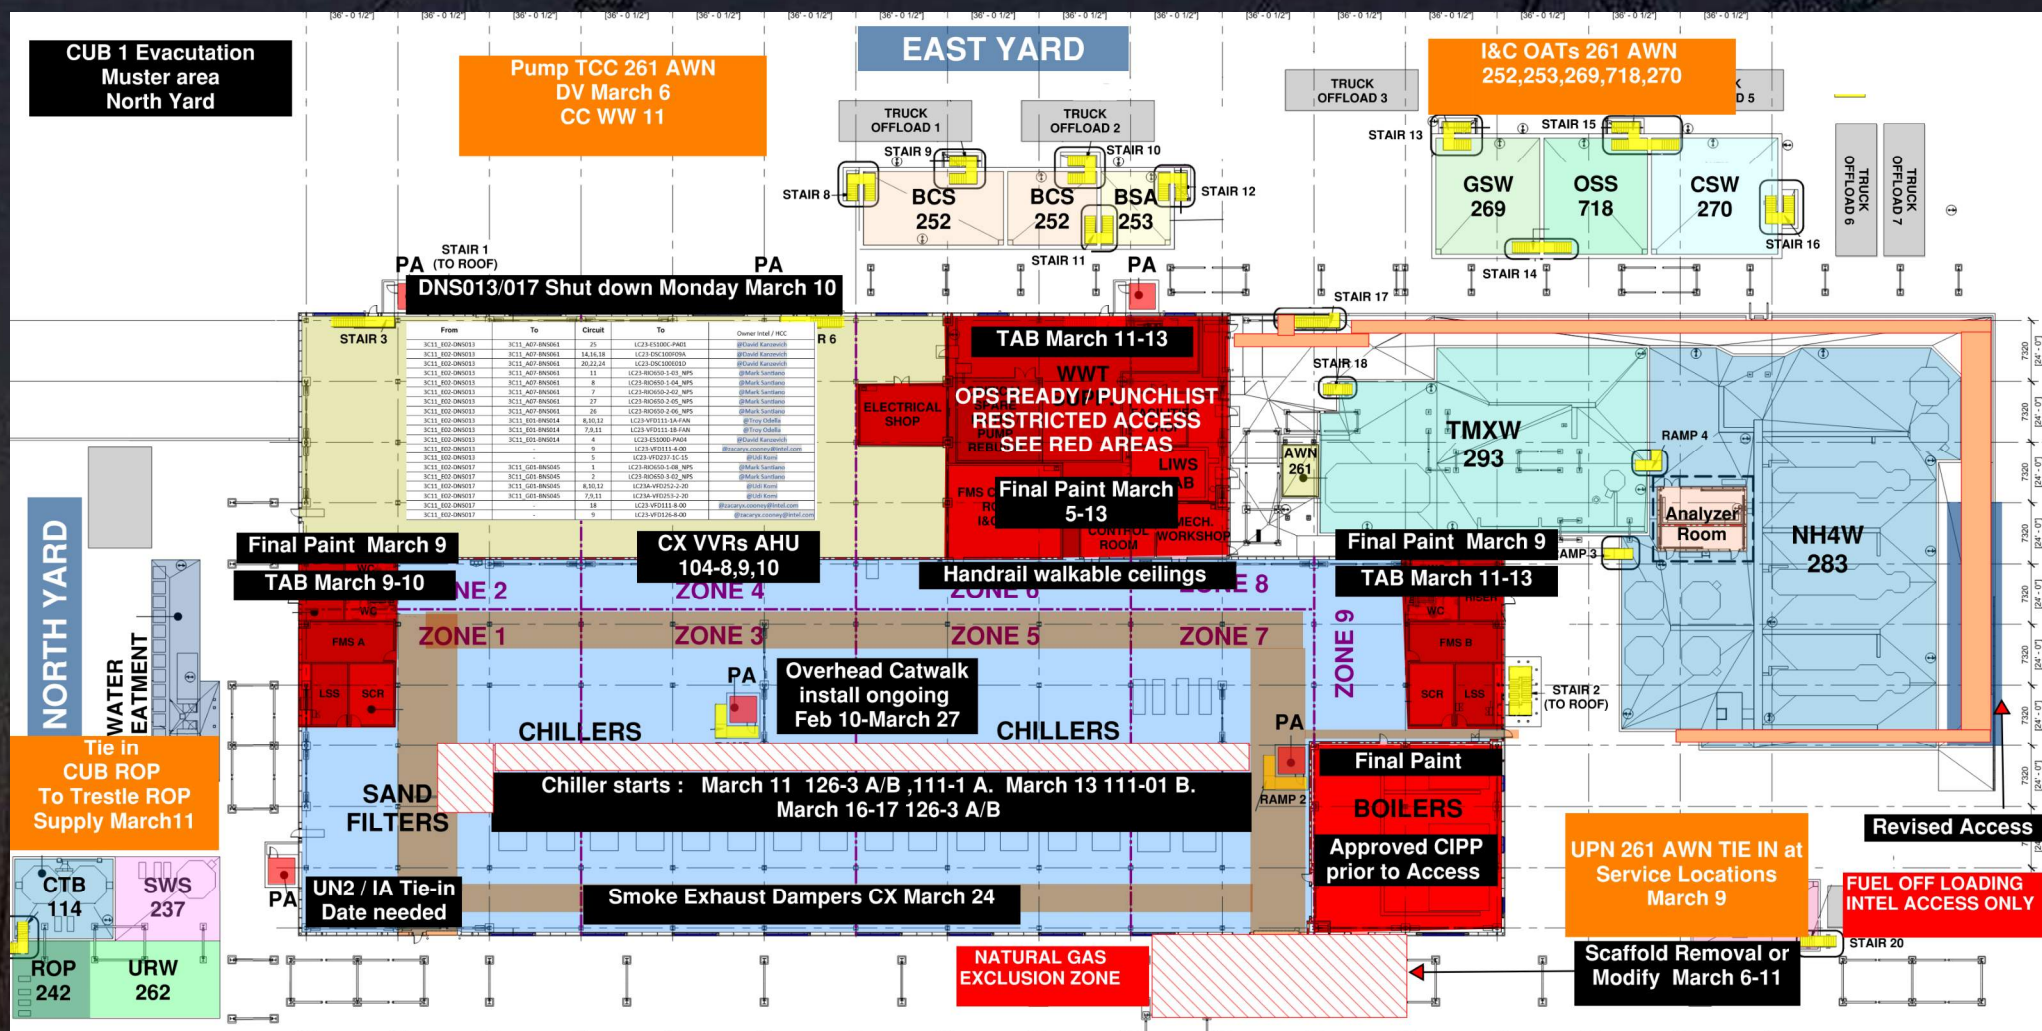


Architectural elevation drawing of the West Elevation of the ES-10A building. The drawing shows a long, low structure with a flat roof and a series of vertical supports. The elevation is divided into sections by vertical grid lines labeled A through P. Key features include a large central section labeled "RFI 10751" and a smaller section labeled "RFI 10752". The drawing includes various annotations such as "Pending UN2", "Pricing & Funding needed NLT VVW8", and "Need funding". Red callout numbers 34, 35, 36, 37, 38, 39, 40, and 4 are placed around the drawing, corresponding to specific areas of interest. The drawing also includes dimensions and material specifications.

- Waste Systems Pressure Testing Wrap up 3d March 4-5
- Trestle Scaffold removal 5d March 6-11
- Metal flashings and Panel work Man Door 5-7d March 12-20
- Claim Envelope ready for DVs March 20
- DV acceptance list and corrections 7d April 2
- Ops Ready April 3
- Concrete removal Site Grading Form rebar pour concrete 5-7 d March 23-March 31
- Bullards 2d April 1-2


CUB 1 – EXTERIOR/ROOF

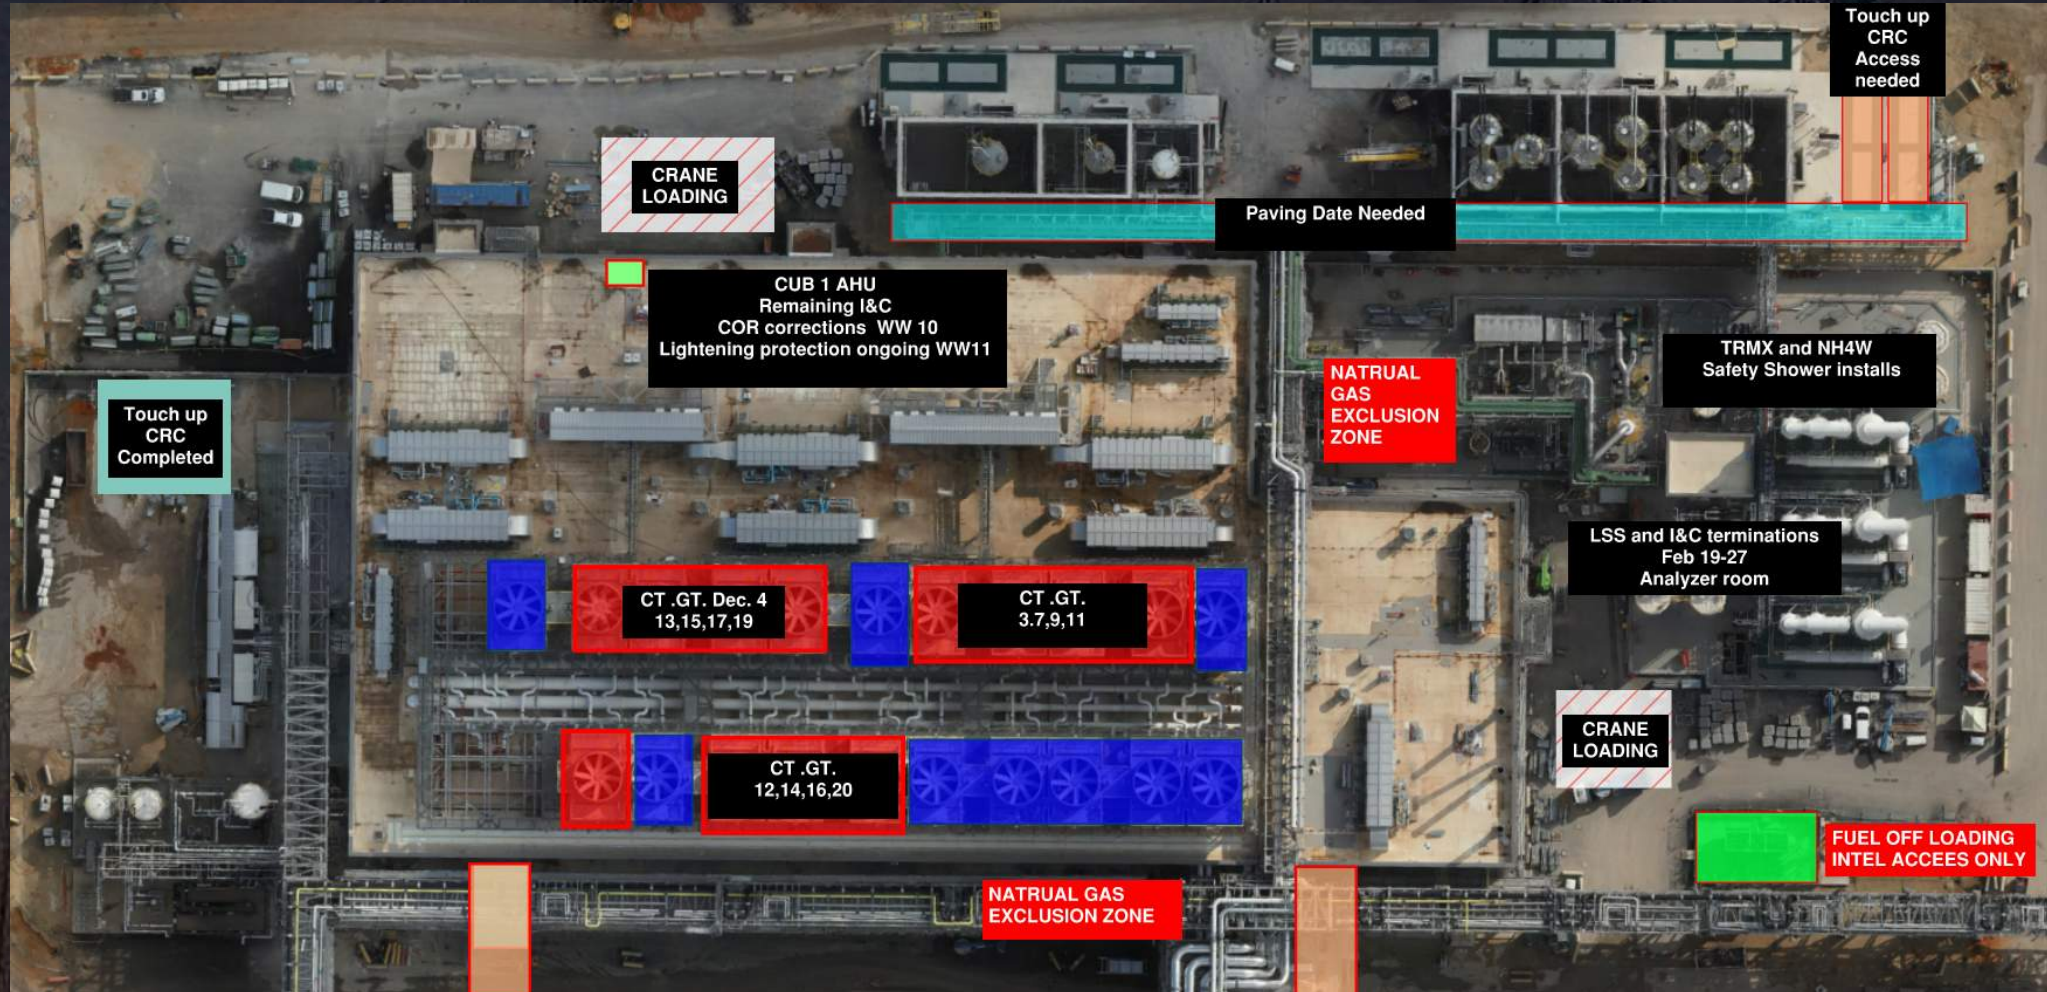


CUB 2- Load in ,H&T, Framing and Sheetrock

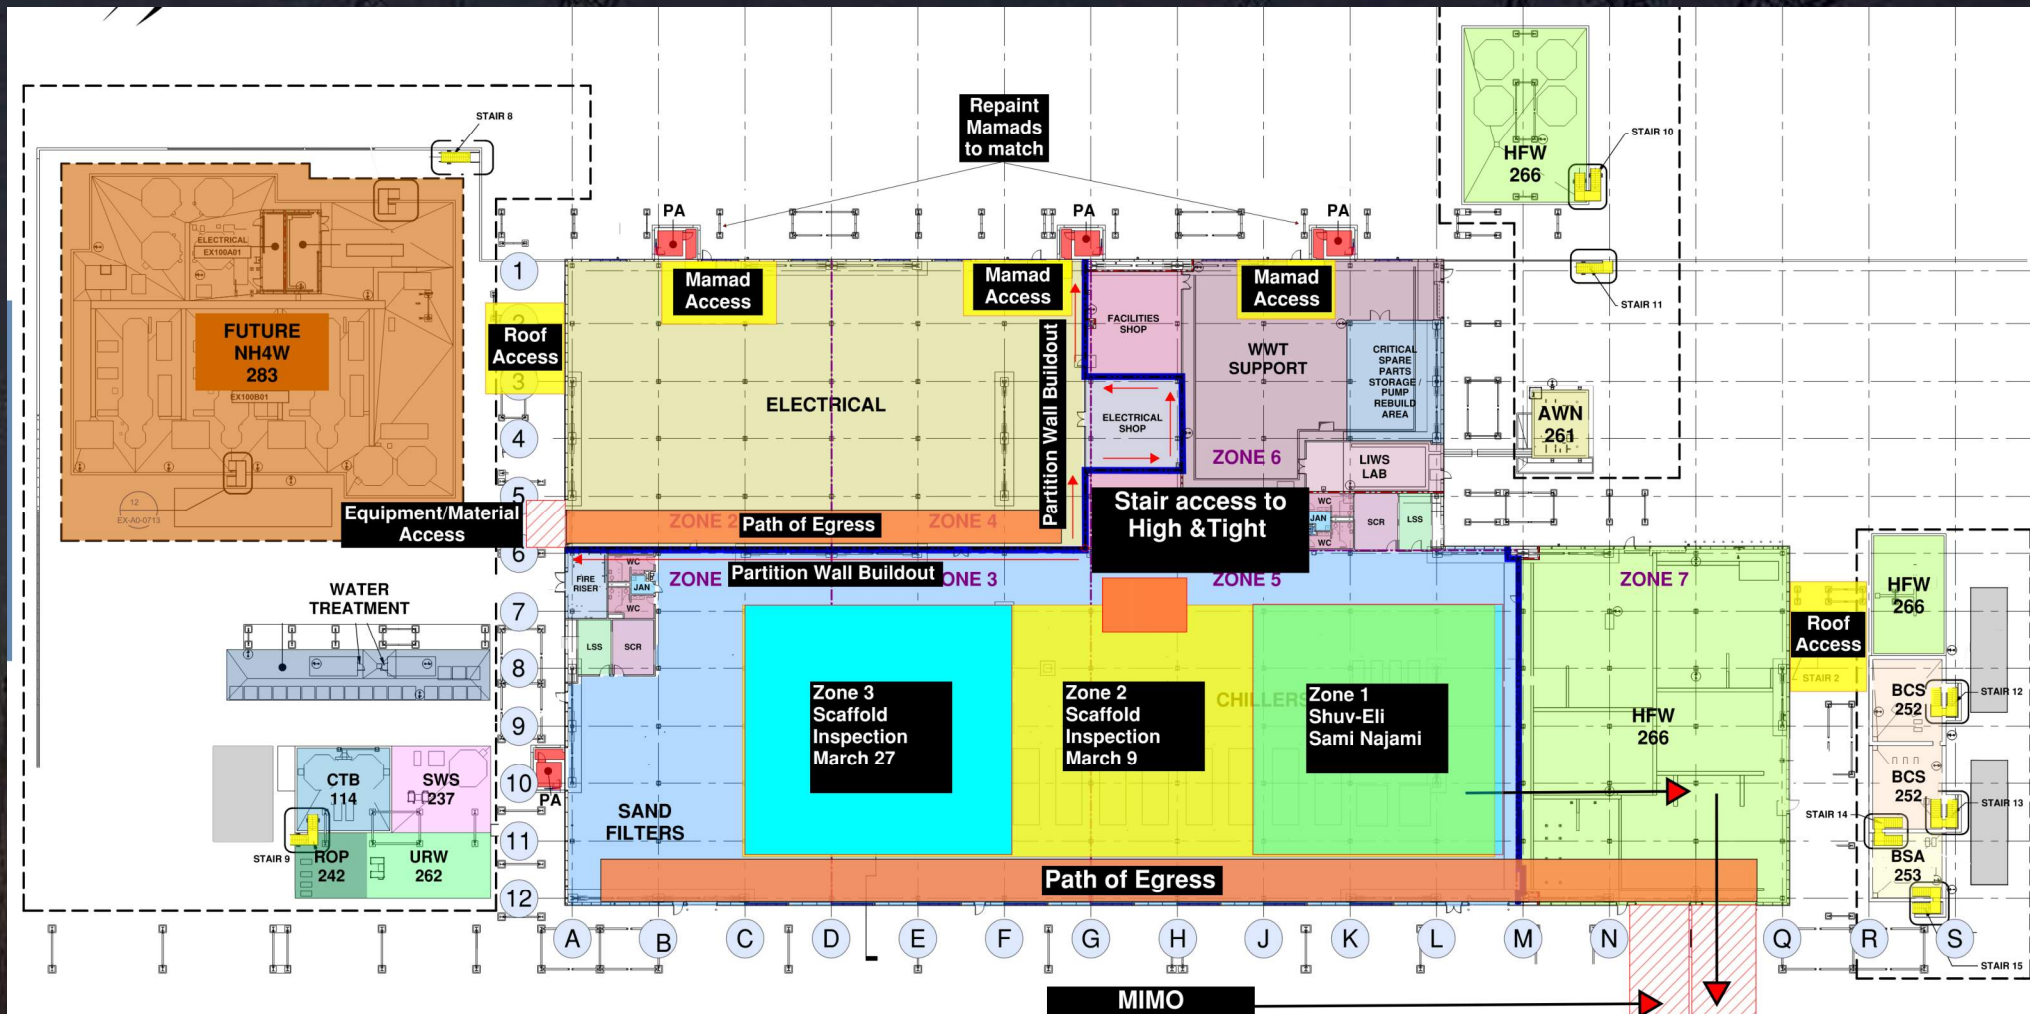




CUB 2 – EXTERIOR/ROOF

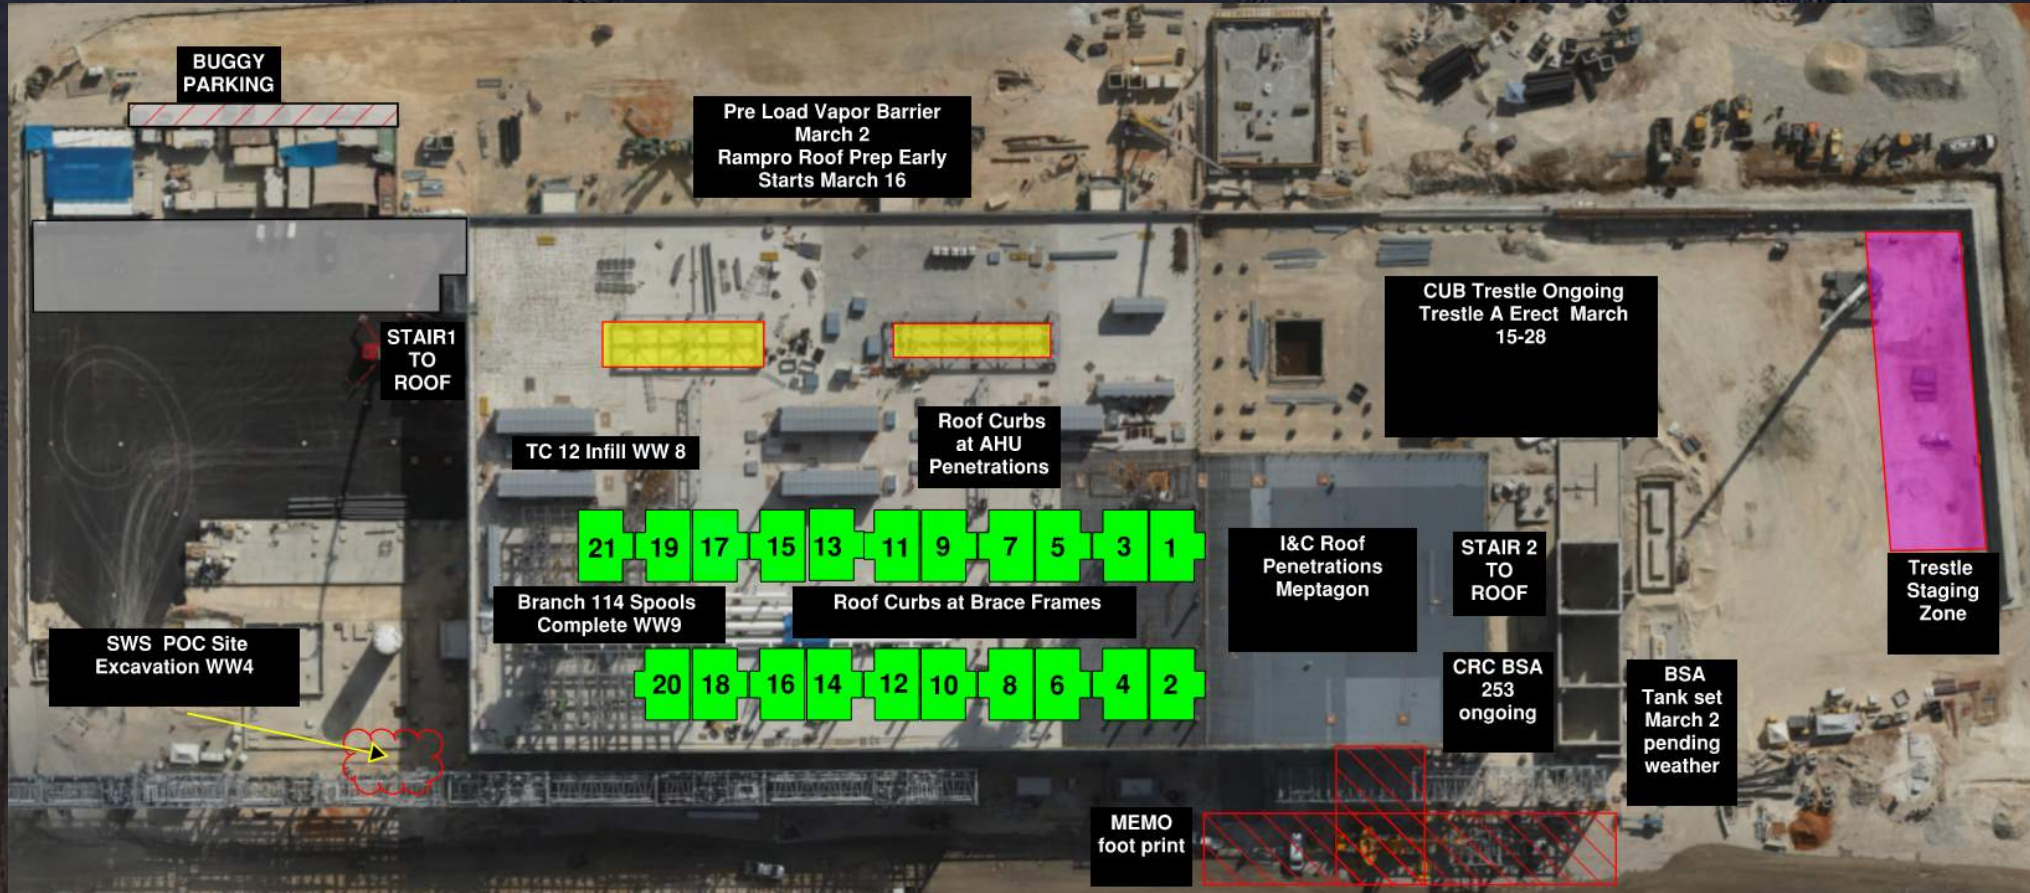



HOFFMAN CONSTRUCTION COMPANY

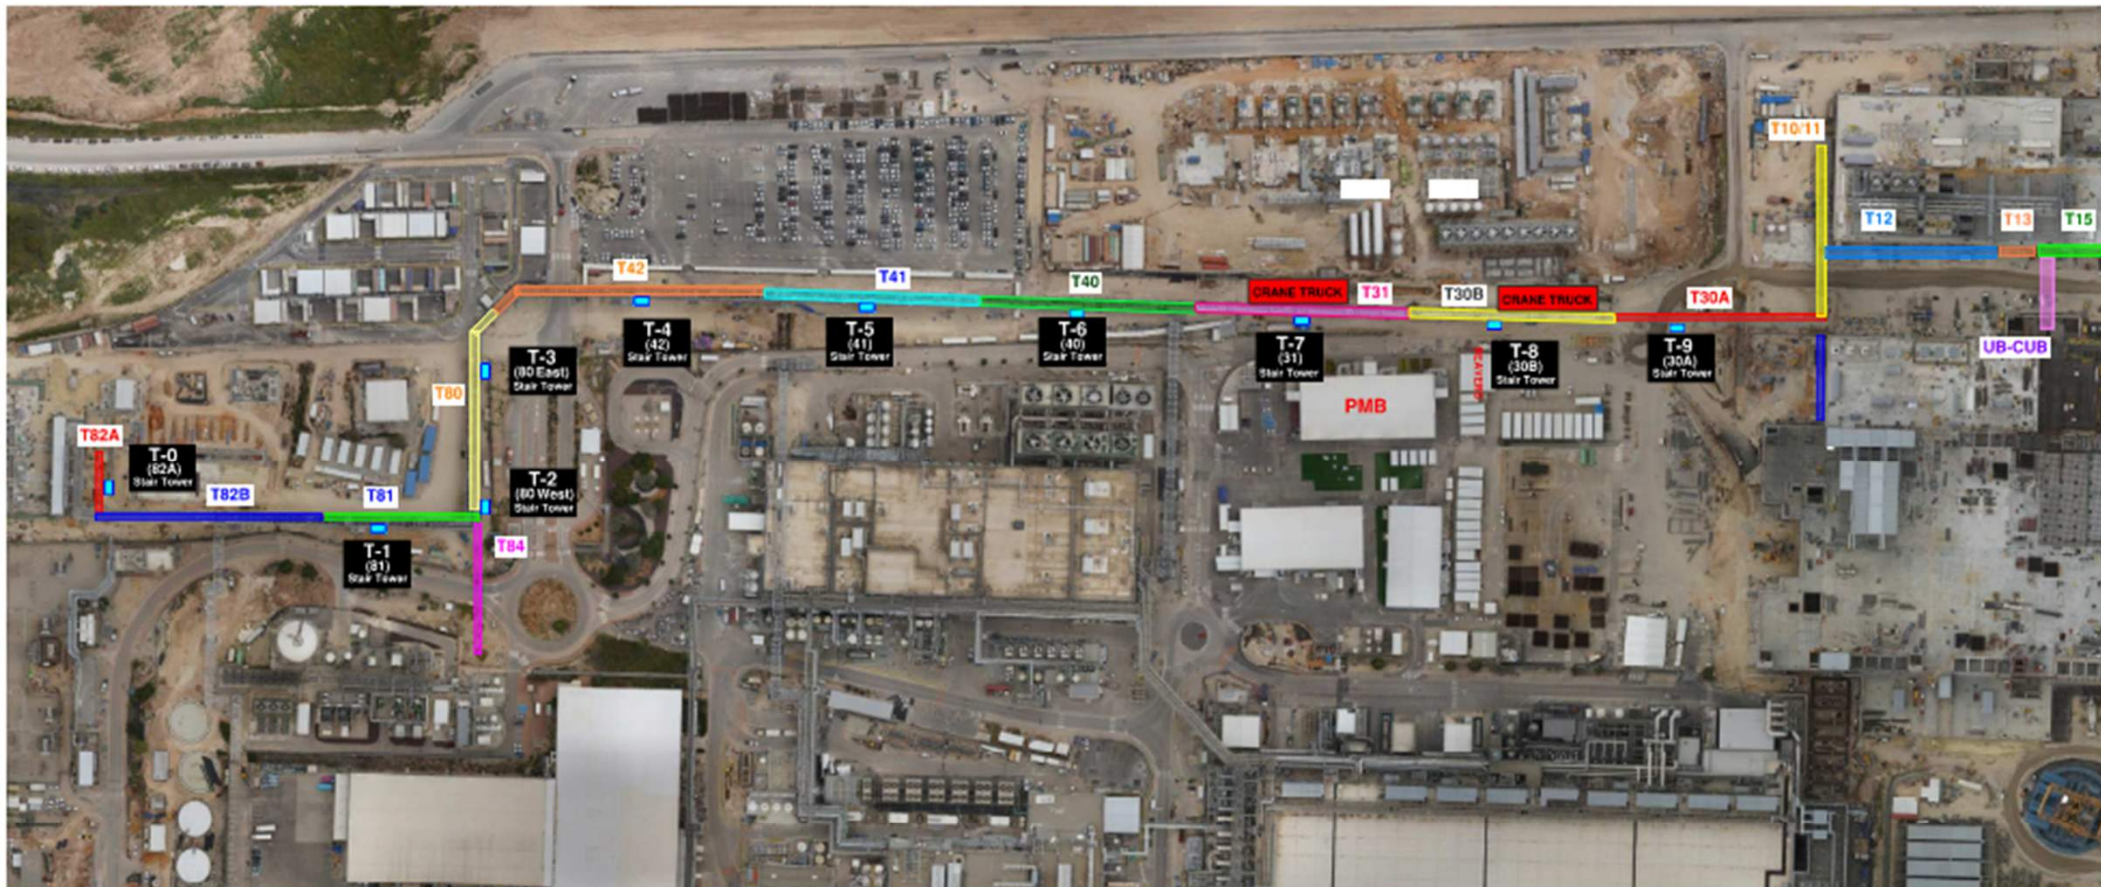

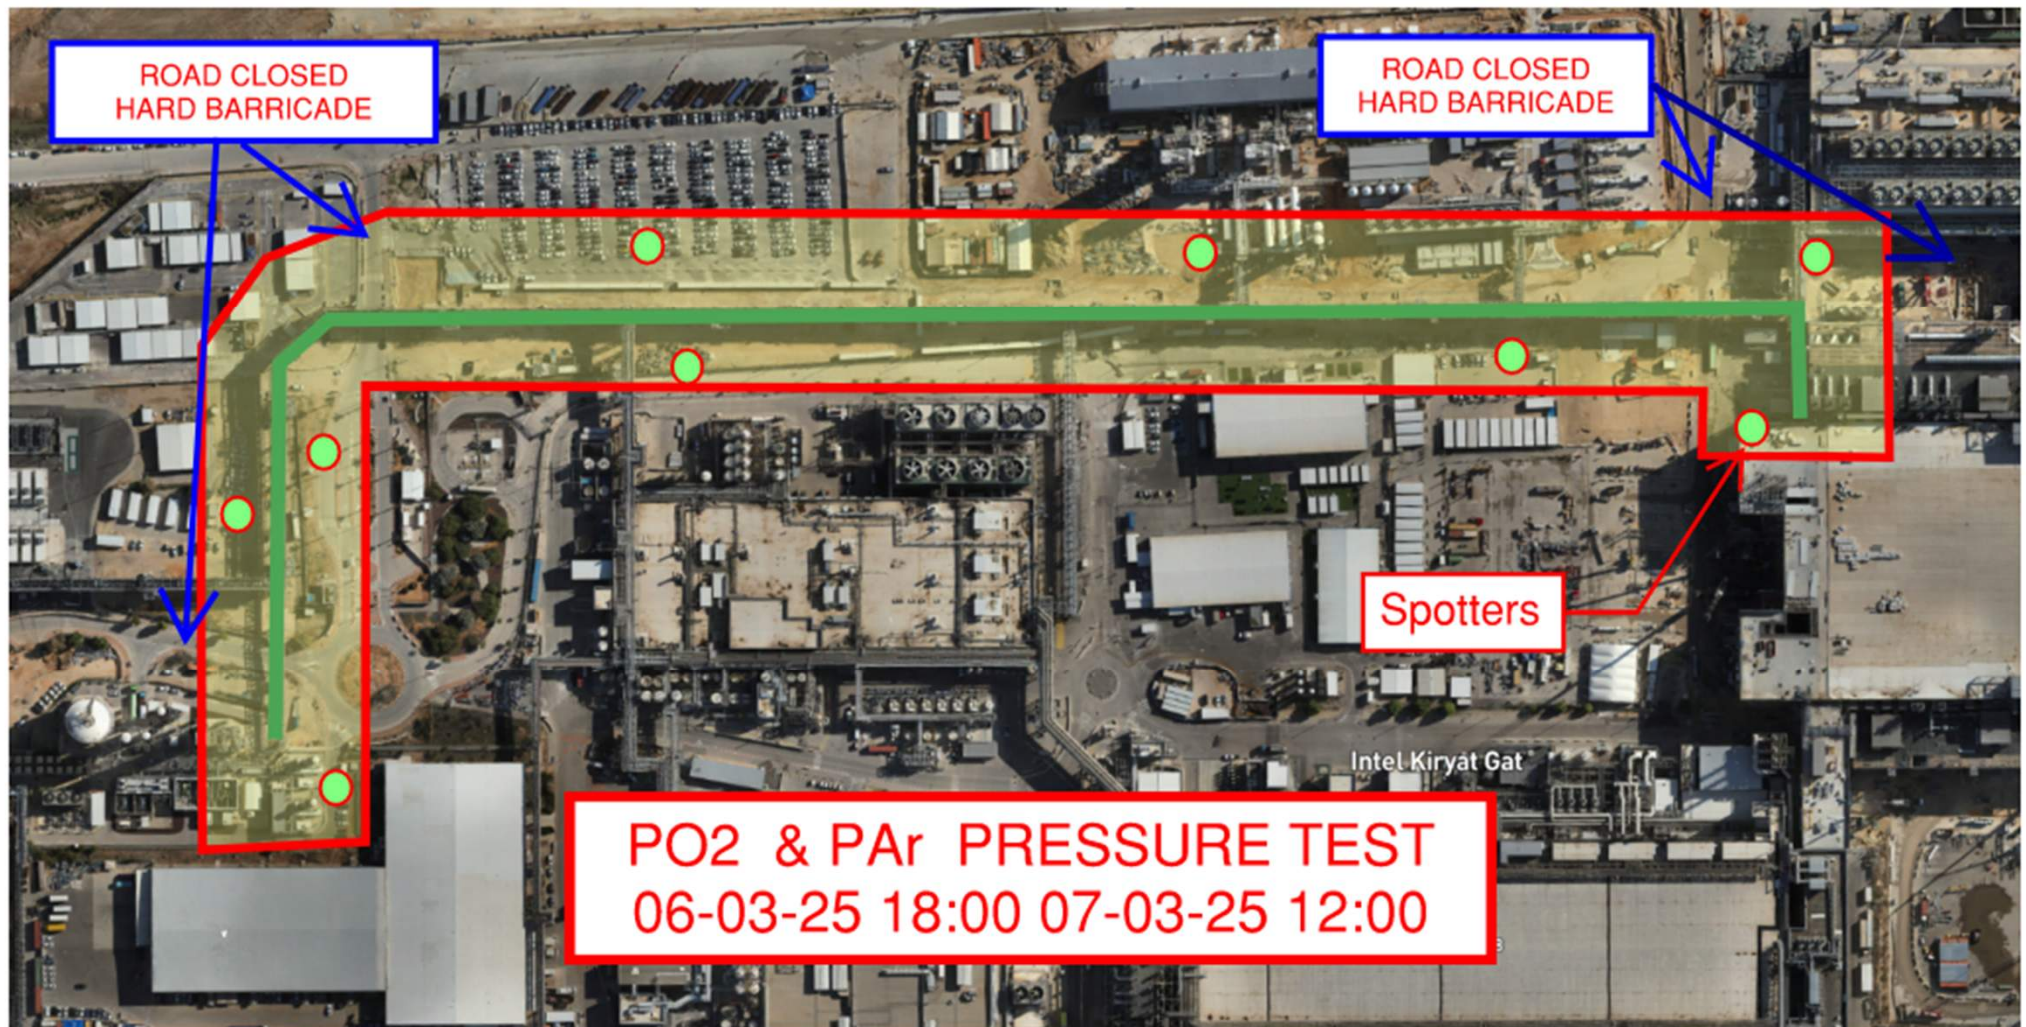


EXCLUSION ZONE FOLLOWING ASME PCC-2 APPENDIX 501-II AND 501-III



PO2 & PAr LINES UNDER TEST



SPOTTERS



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

INTEL- blue fence


OFA PRESSURE TEST
06-03-25 18:00 07-03-25 12:00



Daily Coordination Meeting

Site Logistics

North

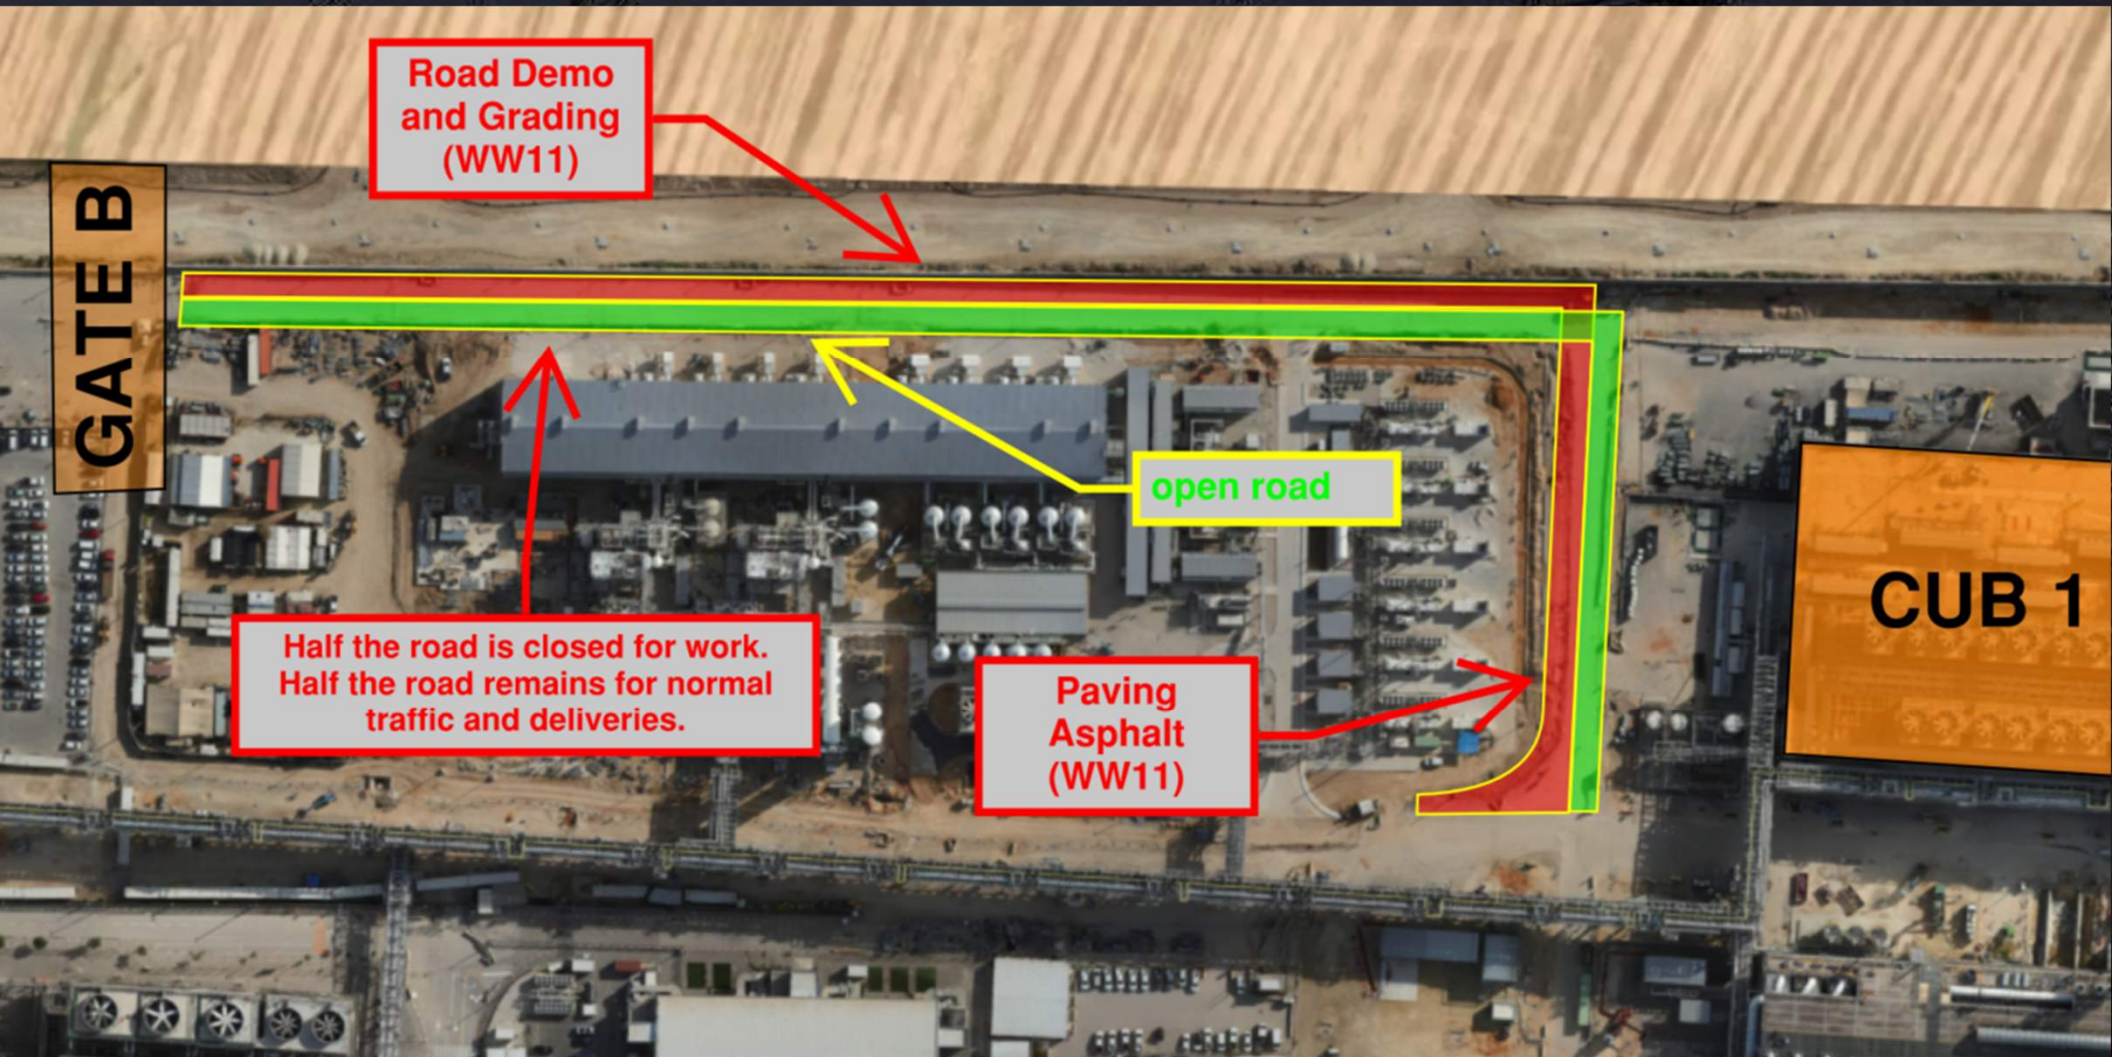




Daily Coordination Meeting

Site Logistics

North

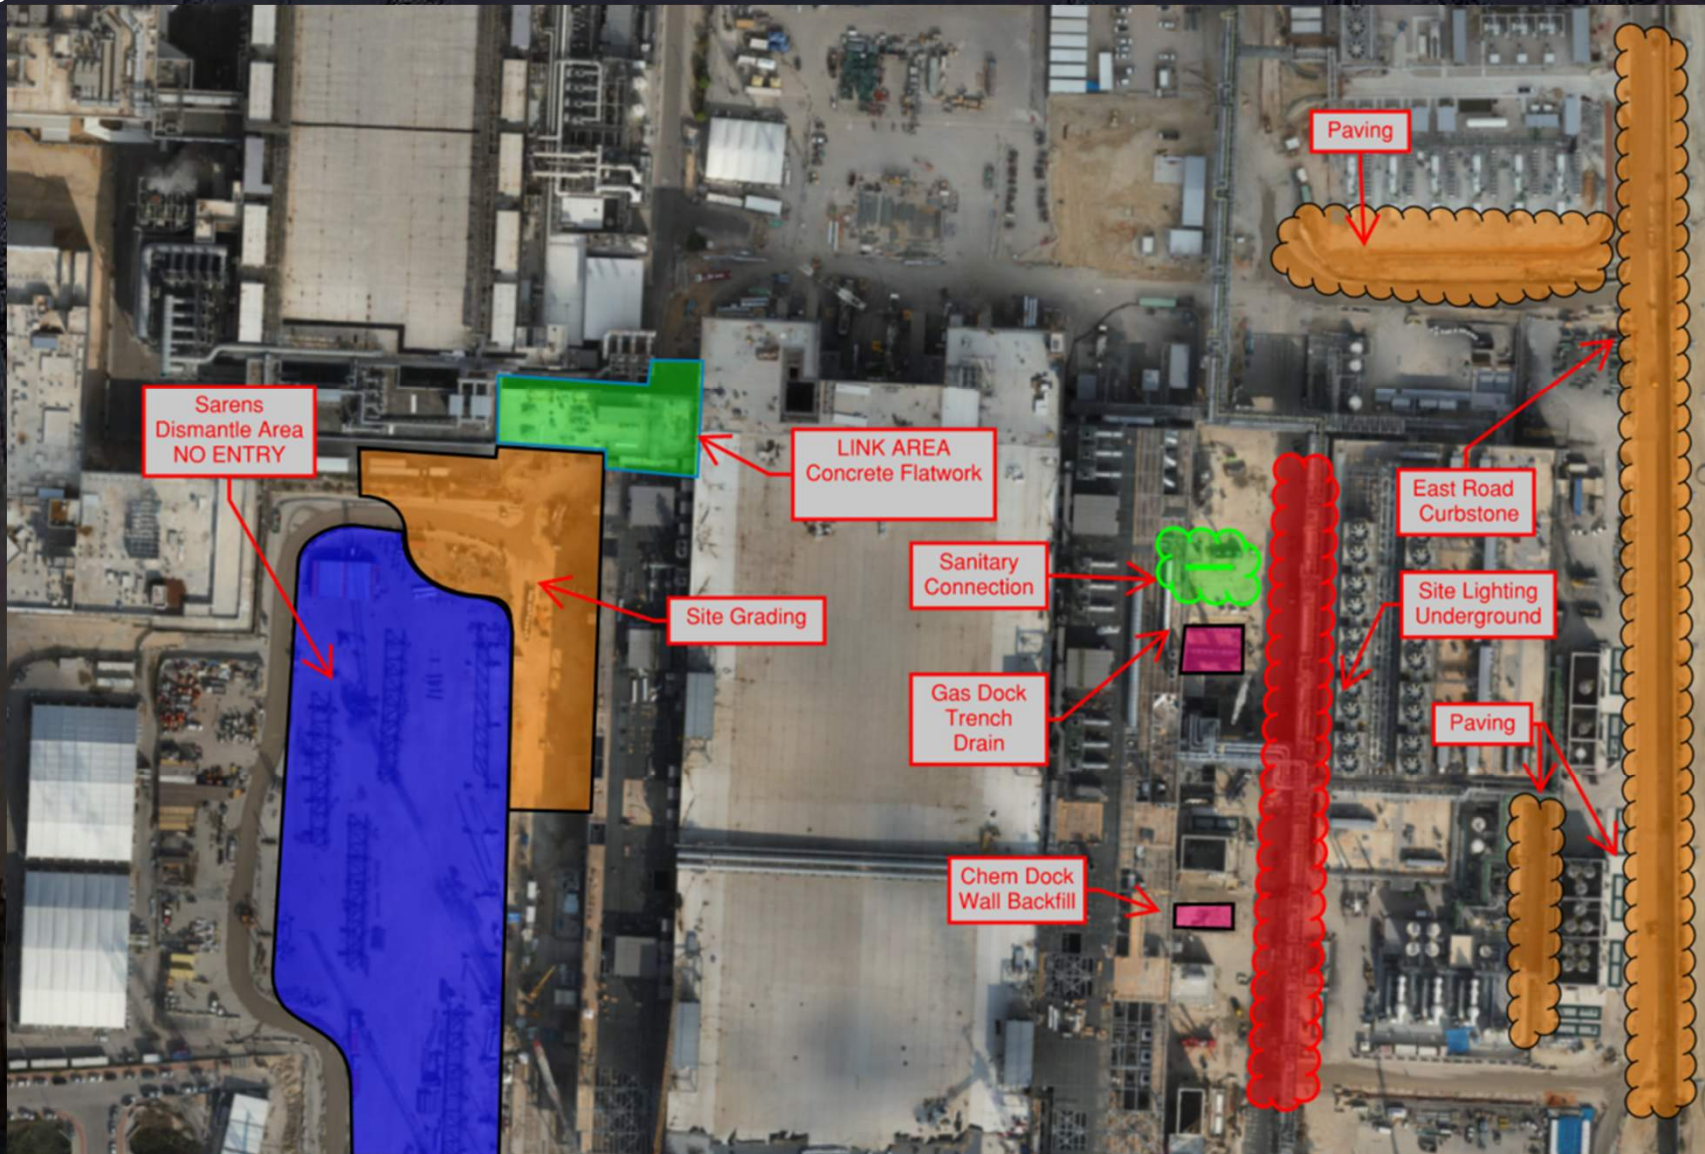



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South





Storage of gases or other materials

- When storing materials like gas cylinders and chemicals on a construction site, they must be kept in designated, well-ventilated areas, away from direct sunlight, heat, or ignition sources.
- Gas cylinders should be stored upright and securely fastened.
- Chemicals must remain in their original containers with clear labeling and be kept away from incompatible materials.
- Proper signage should indicate the presence of hazardous substances, and access should be restricted to authorized personnel only.
- Storage areas should be equipped with firefighting equipment, spill containment measures, and safety data sheets (SDS).
- Regular inspections are necessary to ensure compliance with safety standards and regulations.

HCC/EHS Weekend Work- 07.03.2025

White Board Meeting in Beavers at 06:30

Superintendents

Carter Miles - 052-3376046

Roi Zaidin - 052-2146194

Leslie Kelly - 052-6391546

CSA CM

Ran-Shwartz - 052-8766701

Tarek Nairoukh - 052-6636782

David-William - 052-3470794

Maor-Tzuri - 050-6558817

Raymond-Griffin - 052-6941063

Patrick k

Crane

Maksym Panov – 055-9181086

Cx

Safety

- Safety Foreman- Hay Halfon- 052-8049342 Hay-Halfon@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Khaled Delky- 052-3551385 Khaled-Delky@Hoffmancorp.com

Subcontractor Weekend Work- 07.03.2025

FAB

SNJ - Liron – 052-8939558

Utility level/ SUT

Malhimim Badarom

Forman: Aviran 0528636833

Ehs: Matan 0525506596

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Combe waste

Foreman: Denis 0525238504

Michael 0525506596

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- Pach Taas
 - 3W 4W MARS
 - Ilya: 0505771907
- Afcon E
 - All Over SF
 - Avi Eli: 0526008487
- Lesico
 - 3W,3E PT
 - Gabriel 0549892929

Clean Room

- Talad – 30 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Igor 0523540242)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Topaz 0532400158, 0542496363)
- Sig – 19 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Oleg 0542689370, EHS Ovidiu 0546993648)
- Afcon – 10 guys CR – Cable tags, INT Cable puling , cable tags (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Sela – 2E CRC 1E(Supervisor yoav 0548076339 , EHS SERGEY 0526650046)
- W&W (Sami) – Handrail on 4DA level, PSSS, WJG (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

- Sami is working on Handrail on 4DA level of FAB
- Sami will be performing grating work at PSSS and WJG

Subcontractor Weekend Work- 07.03.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/SSS Building
- Foreman – Chaim – 054-5210133
- Safety – Marzuke – 054-447-7112
- Lesico – Low Point Drains on PSSS Roof/OFA in Solvents
- Foreman – Suju Pally – 052-7755967
- Safety – Tal Madar – 052-8229109
- Combe UPW – BCD/UPW Rooms
- Foreman – Boris – 054-8346412
- Safety – Shimon – 054-5348843
- SK Engineering – Lift 2 MAH 4P/DW Punchlist
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- Carmel Scaffolding – H2 Vent Scaffold Removal
- Foreman –
- Safety –
- Talad – Water Reactive Fencing
- Foreman –
- Safety –
- W&W – Grating Cutting Lift 2 5P
- Foreman –
- Safety –

WJG

Afcon:

Foreman: Mantu Singh - 0559116973

Safety: Steven Shartho – 0559129333

Pach Taas:

Foreman: Ilya – 0505771907

Safety: Ofek Ben Harush – 0507838486

Chemo:

Foreman: Maor – 0509889071

Safety: Rotem – 0544477112

Sami Najami:

Foreman: Yosef Nahum – 0525166140

Safety: Amir Okev – 0502942941

SK:

Foreman: Marcelo – 0542072784

Safety: Majdi

Subcontractor Weekend Work- 07.03.2025

CUB

Chemo Aharon CUB 2:
Dudu - 0509808846
Arie - 0504244707

S.K Engineering CUB 2:
Mario - 0548991051
Marzuk - 0548830263

A.S Barzel CUB 1:
Dimitri - 0523800269
Yuri - 0522827211

Sela CUB 1:
Yoav - 054-8076339
Sergey - 052-6650046

Site

- Derech Afar – Shotcrete wall
 - Supervision = Raed: 054-244203
 - EHS = Alex: 054-5403849
- Olizki – Truck offload 10, Truck offload 13, Link concrete flatwork & BGC east road
 - Supervision = Or: 052-4917313
 - EHS = Ben: 052-4033565

Trestle

Piping:
19 People- pressure tests

FORMAN:
Misha avramov -052 6066163

Safety:
WISAM EL ATAMIN- 050-9828381

Daily Coordination Meeting



14:00 Sign In
