

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- See something, say something, do something.




HOFFMAN CONSTRUCTION COMPANY

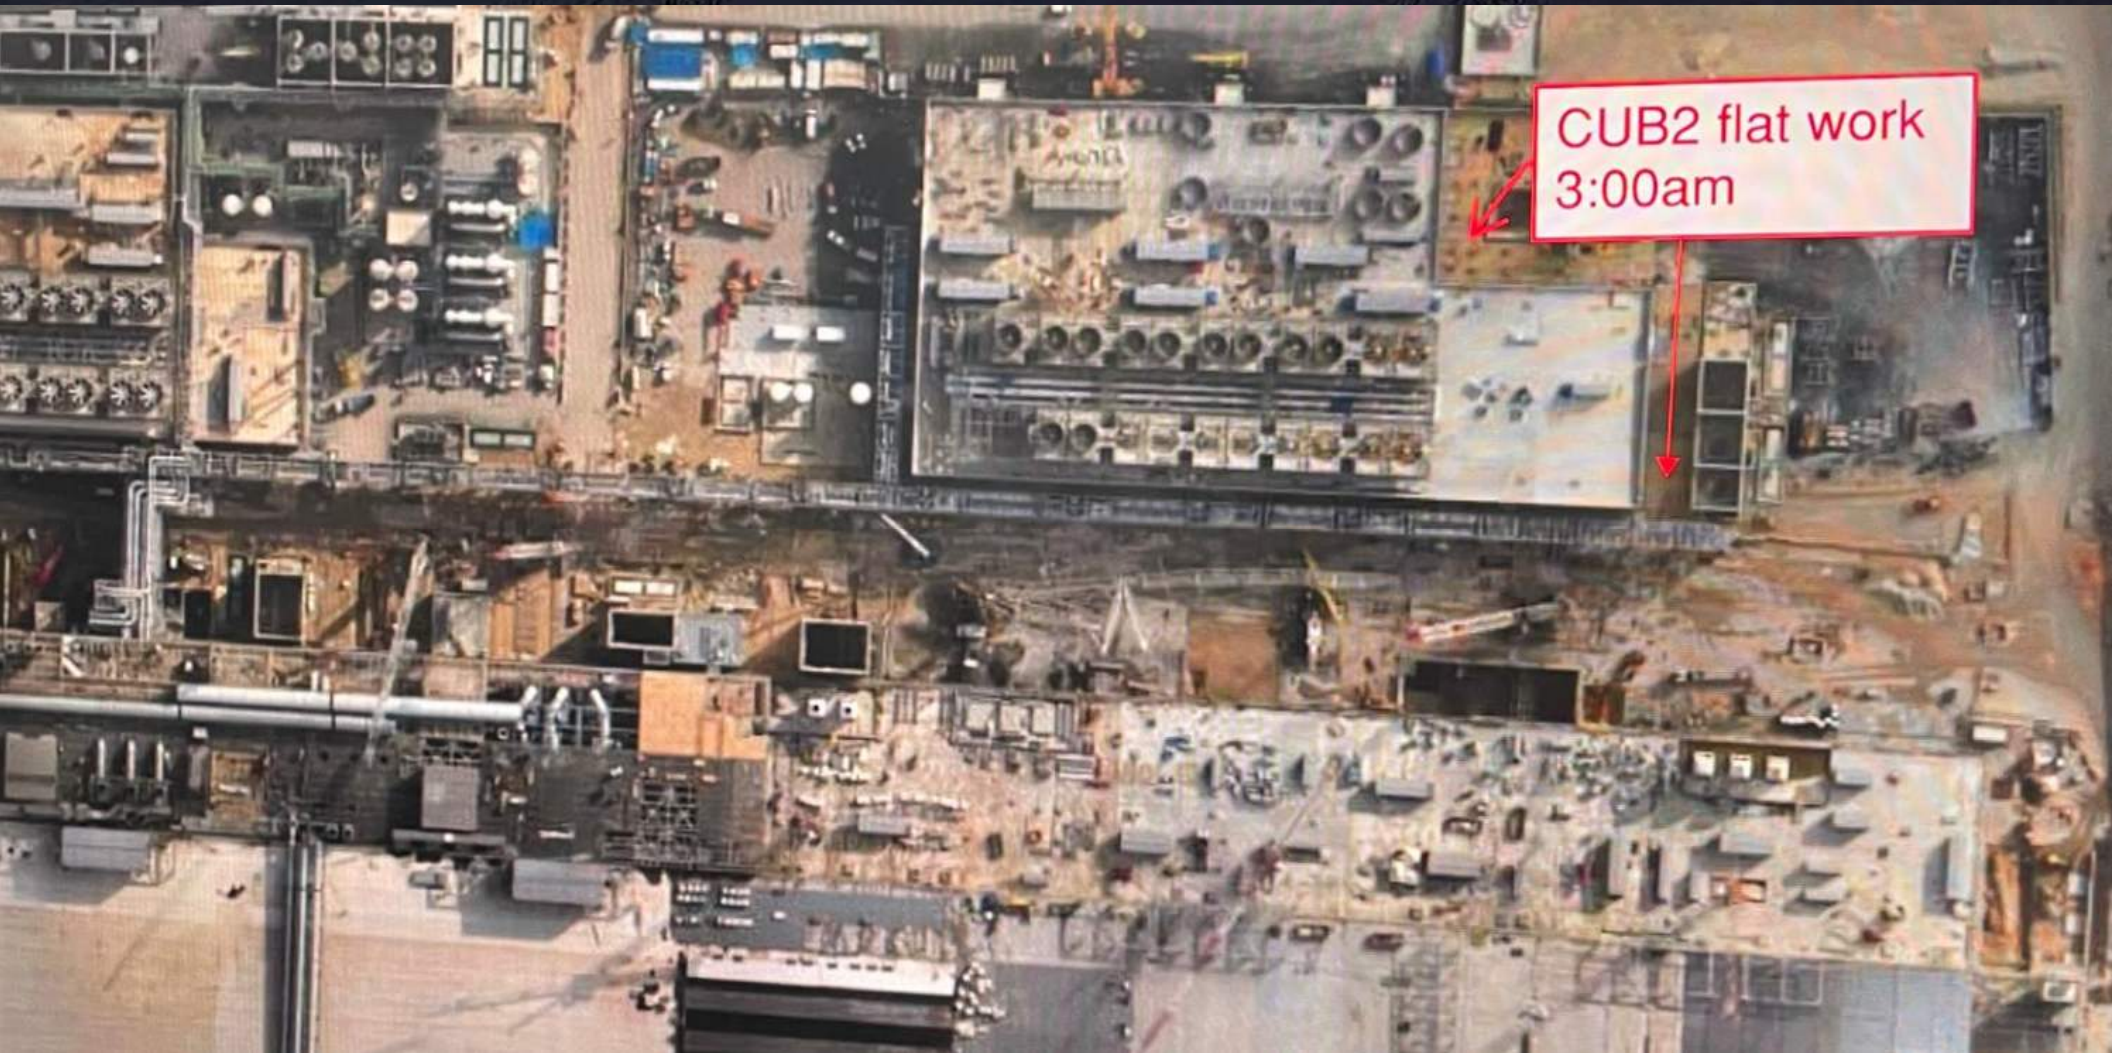




UTILITY LEVEL MOD1

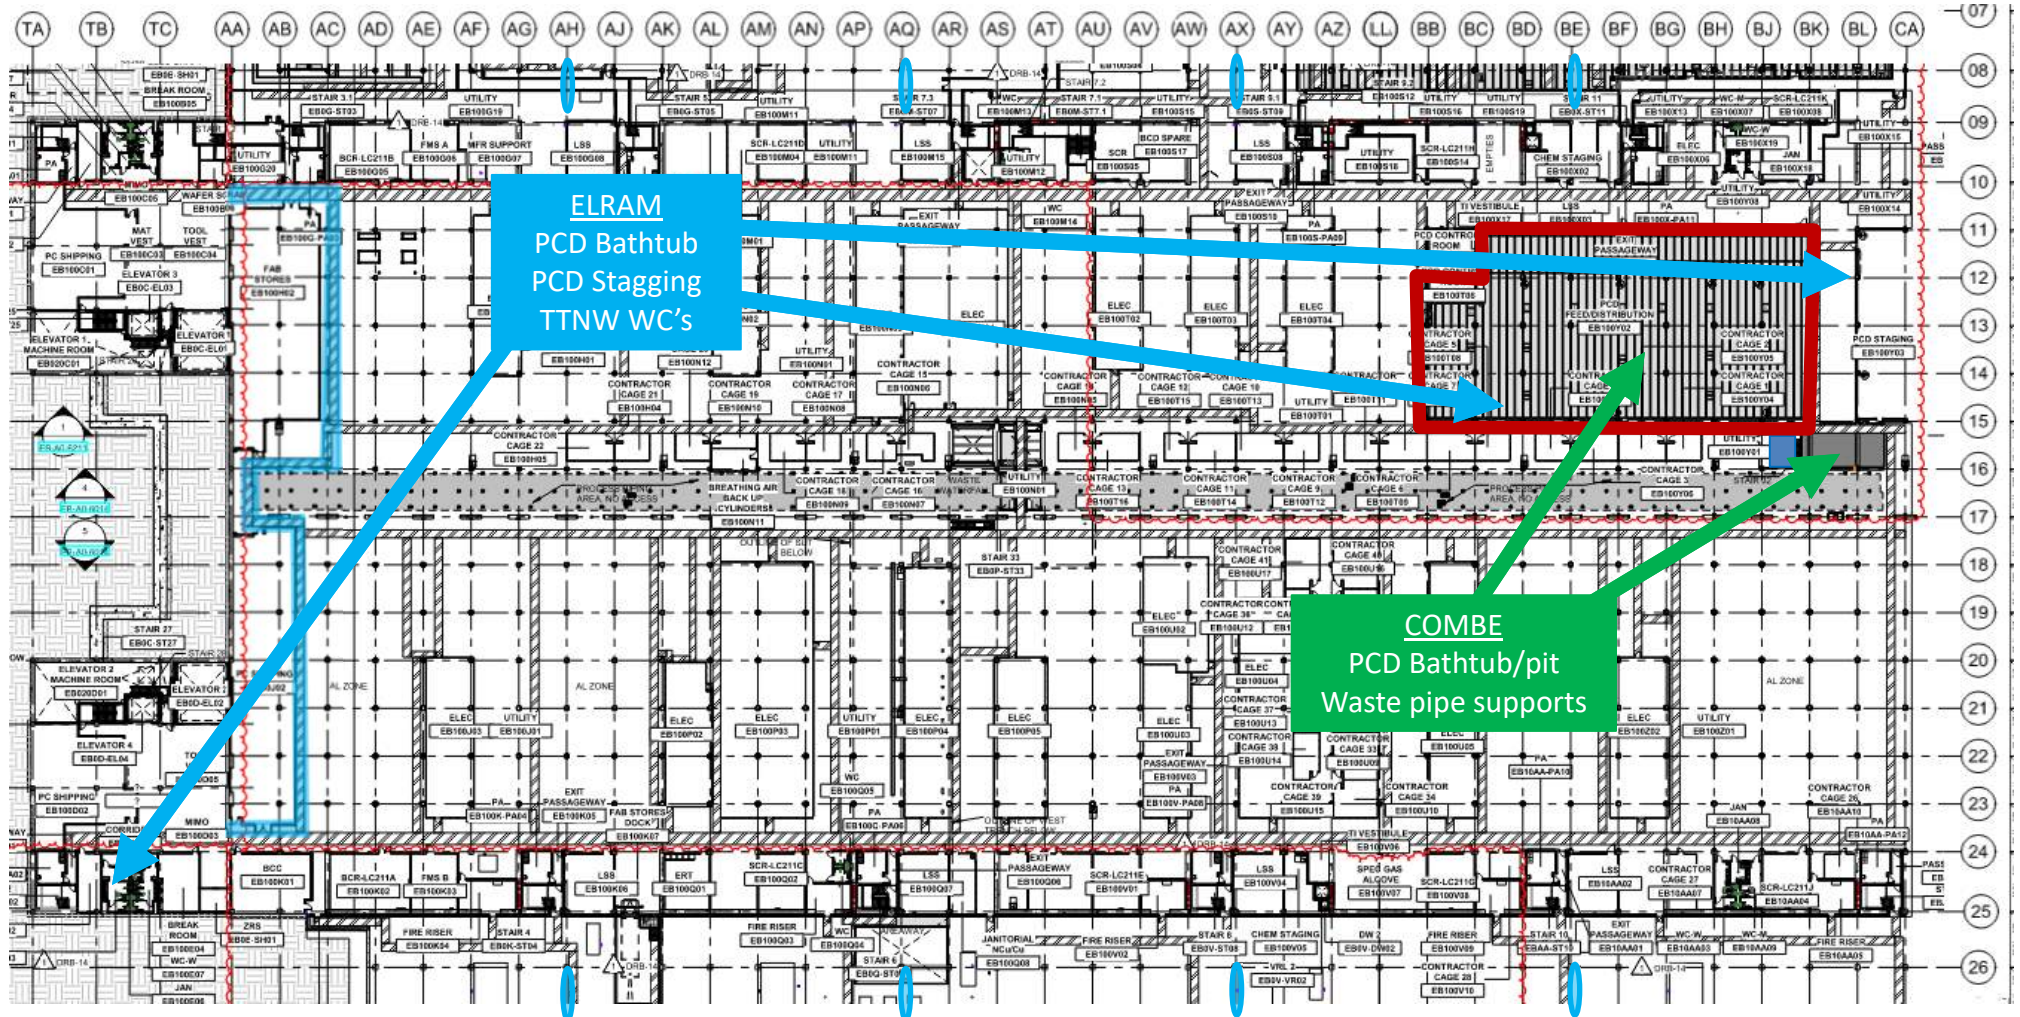

SUT 38.1 LEVEL

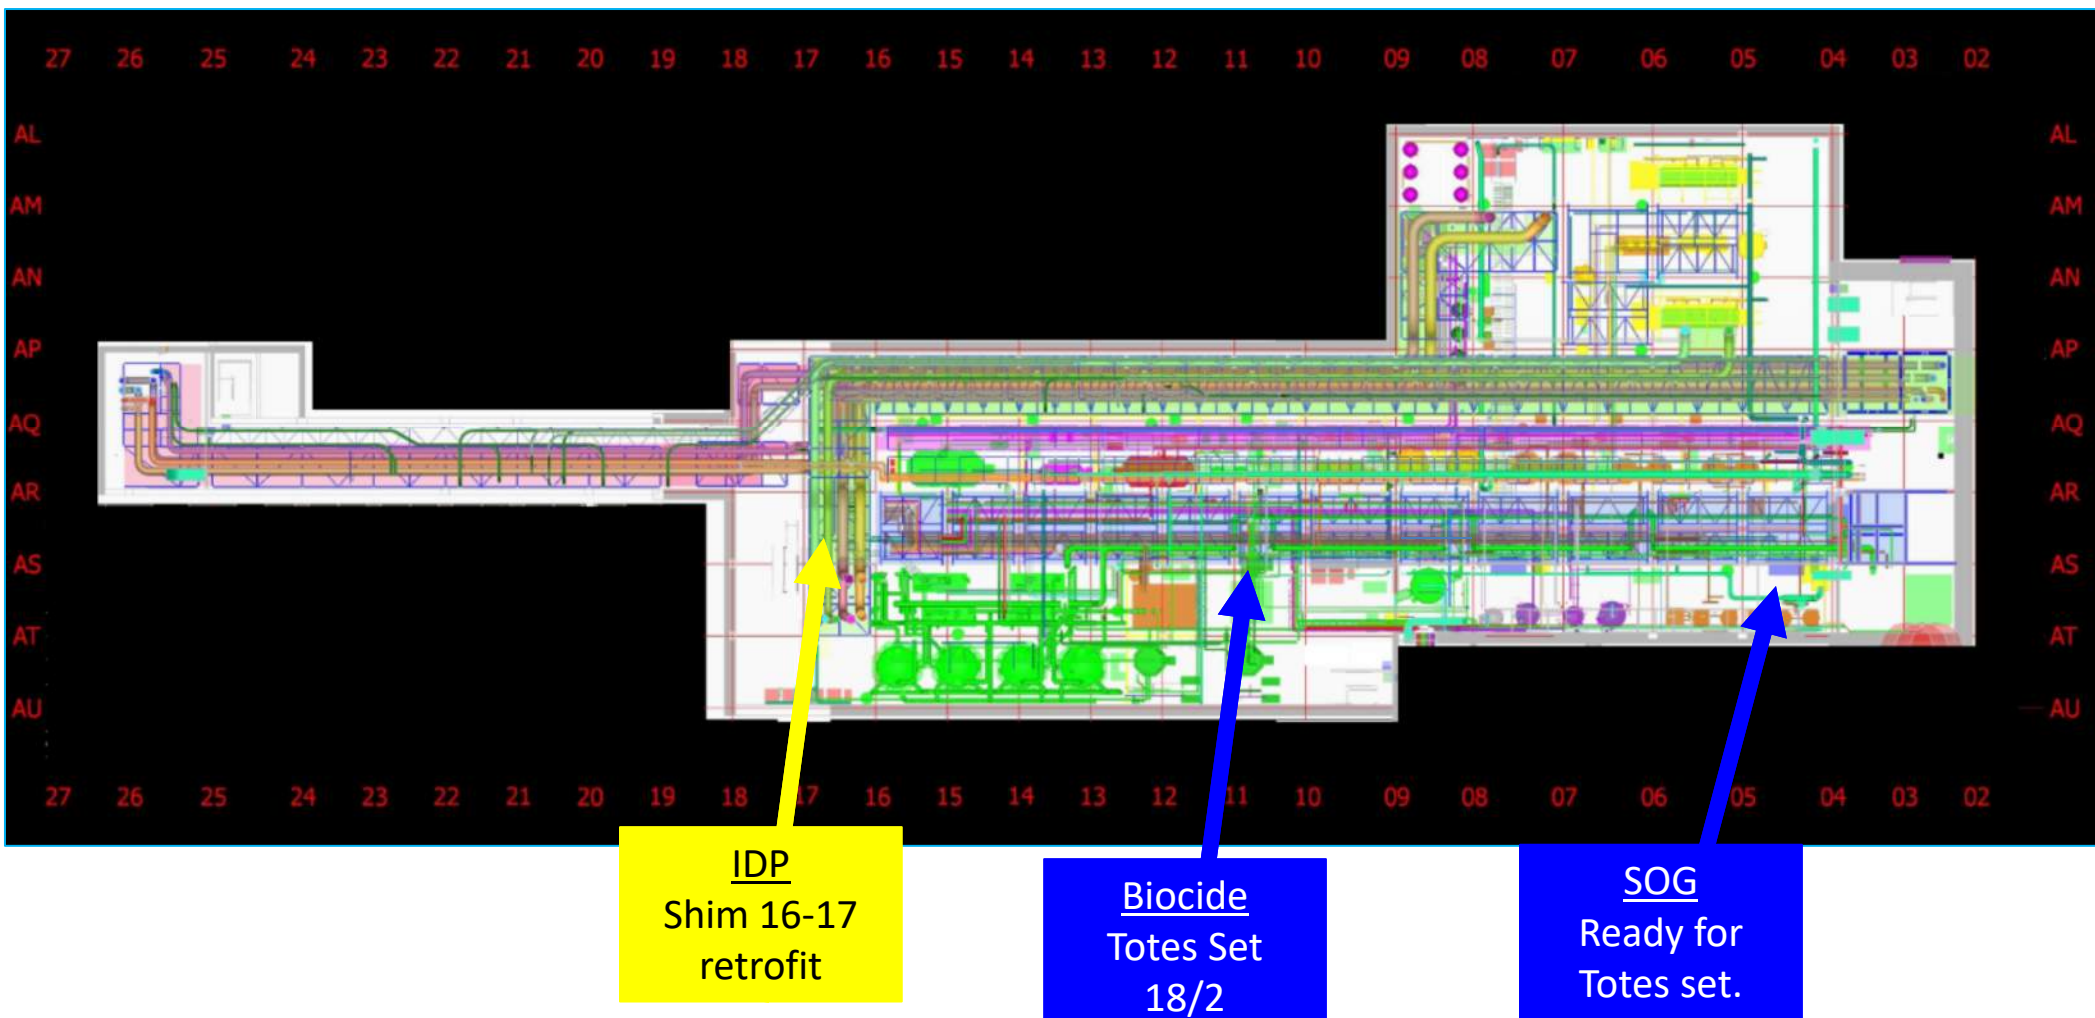




HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL


Rack 4b
Inter
Connection's

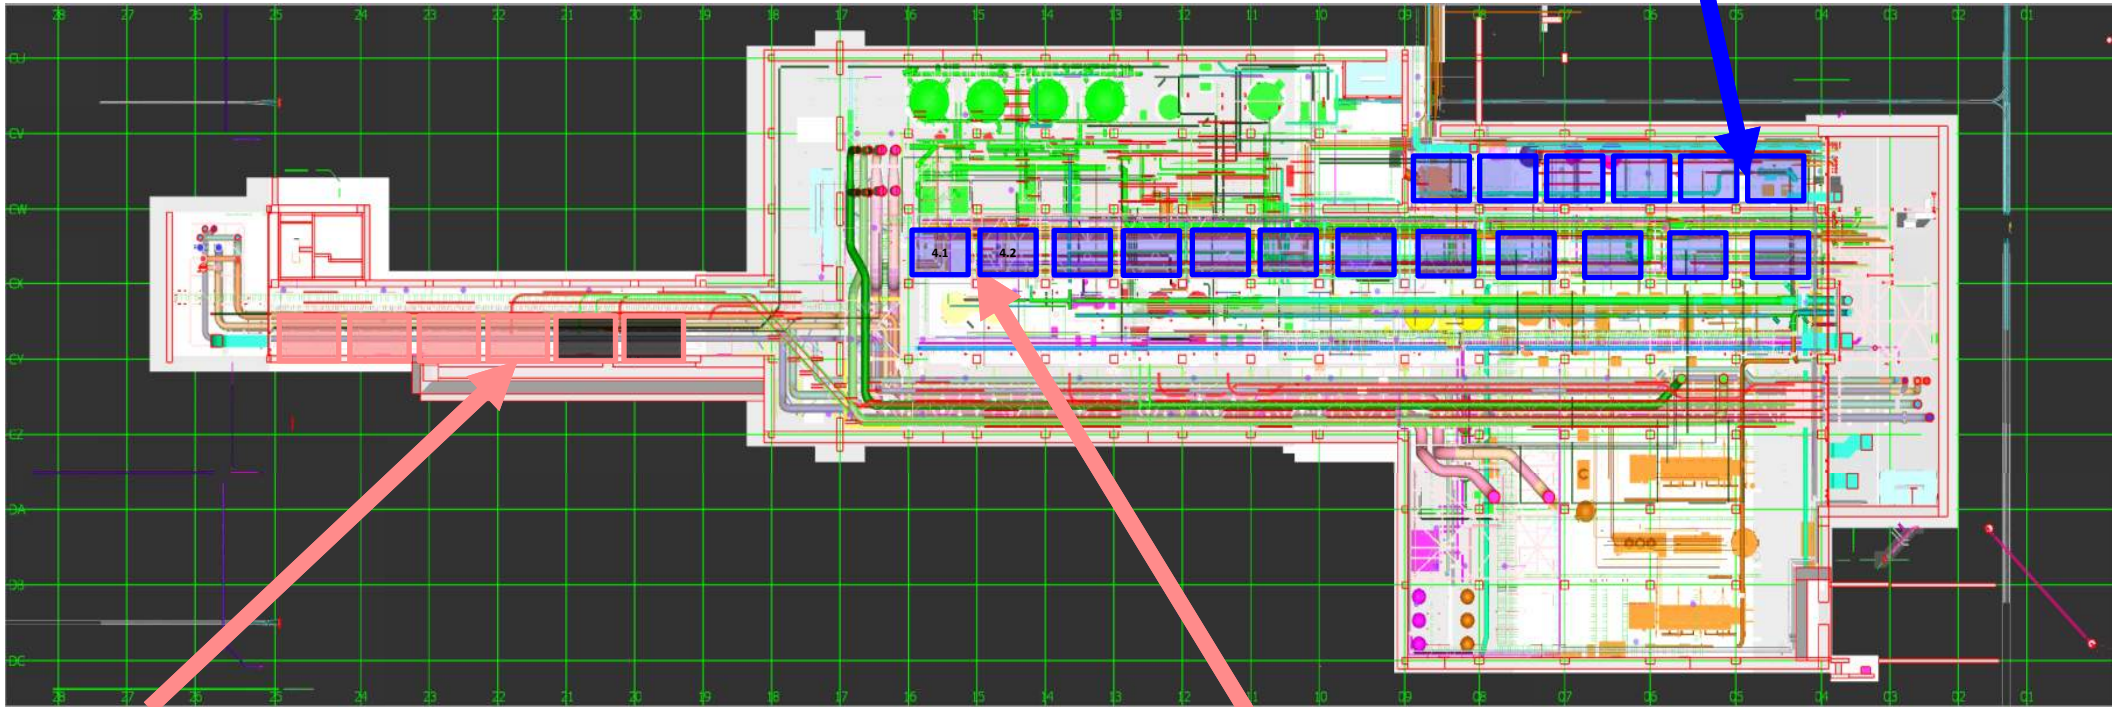


16/02/2025	Module 1
20/02/2025	Module 2
23/02/2025	Module 3
26/02/2025	Module 4
02/03/2025	Module 5
04/03/2025	Module 6

Temp stairs
relocation


SUBFAB BUILDOUT MOD 1

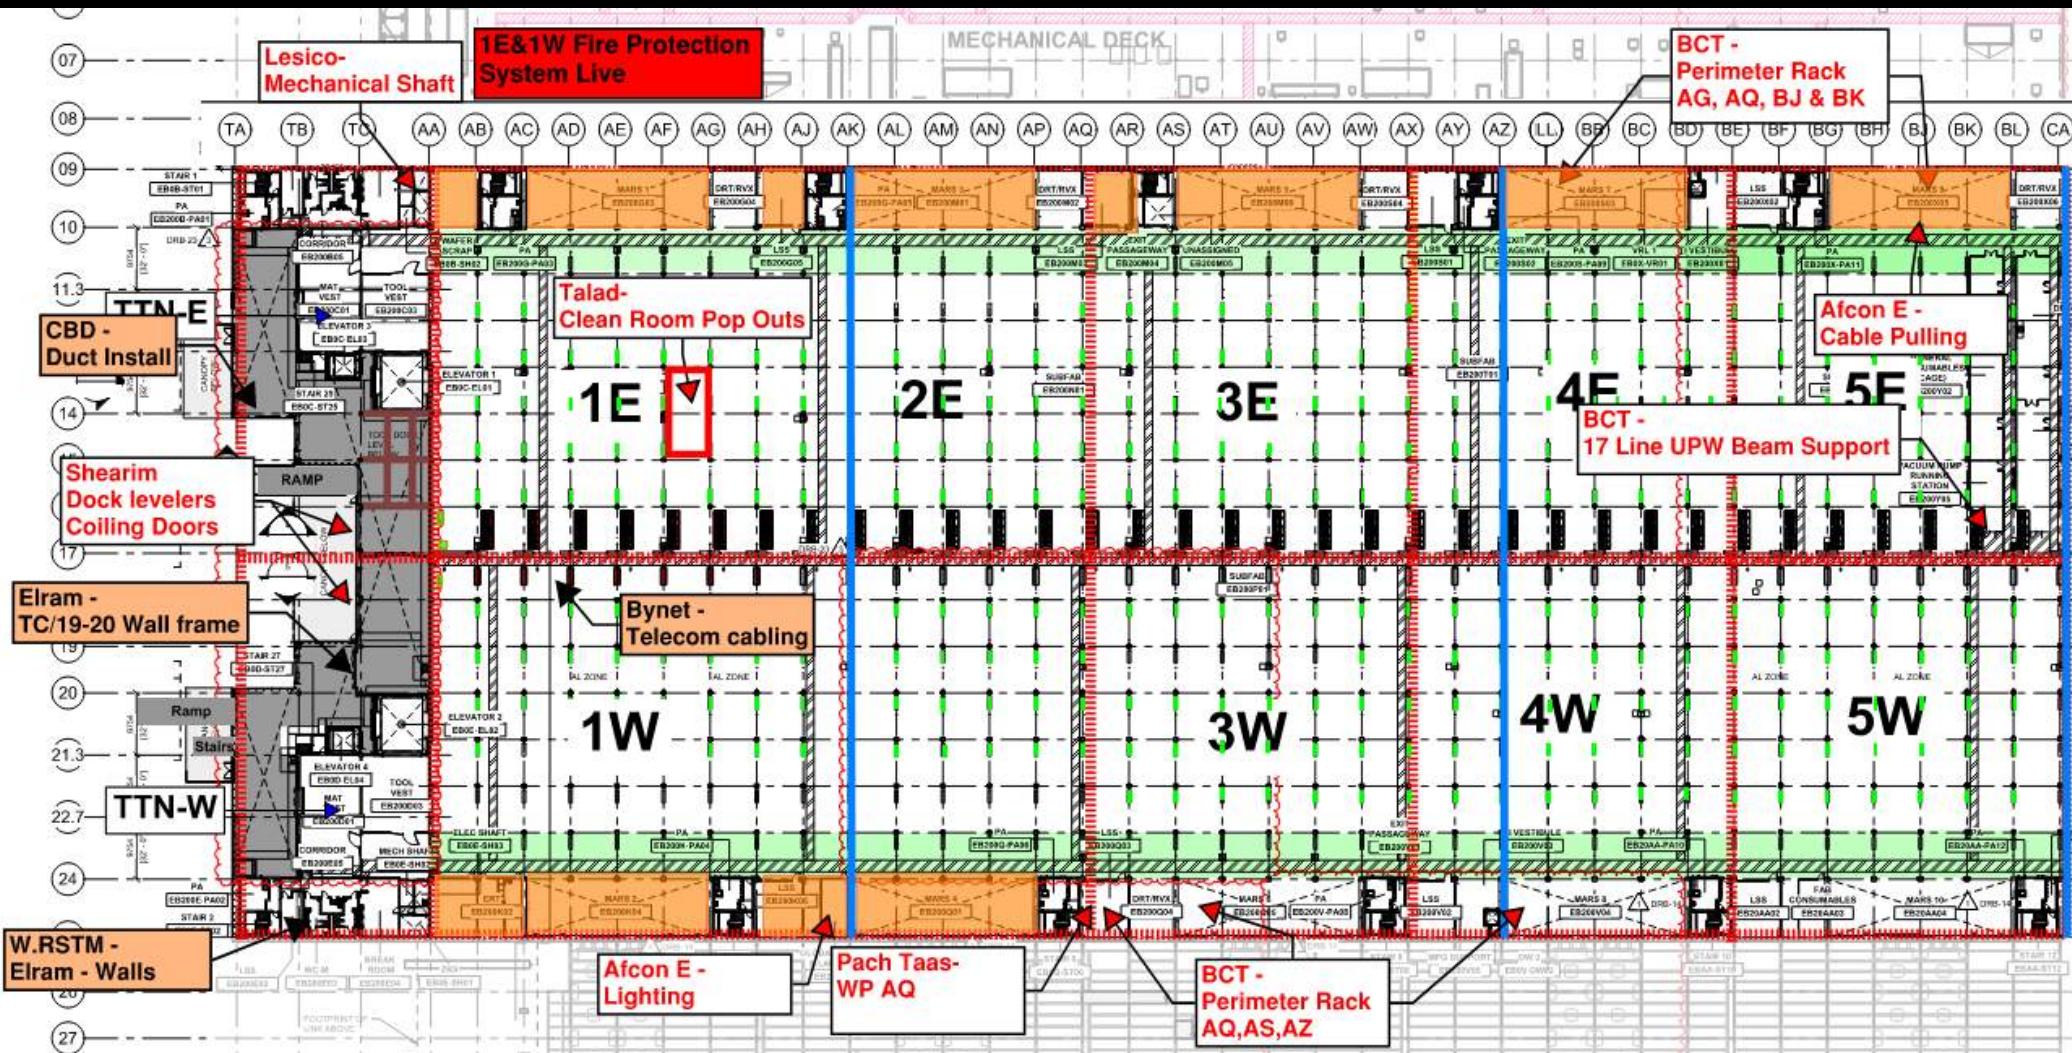


SUBFAB CRC TOPCOAT

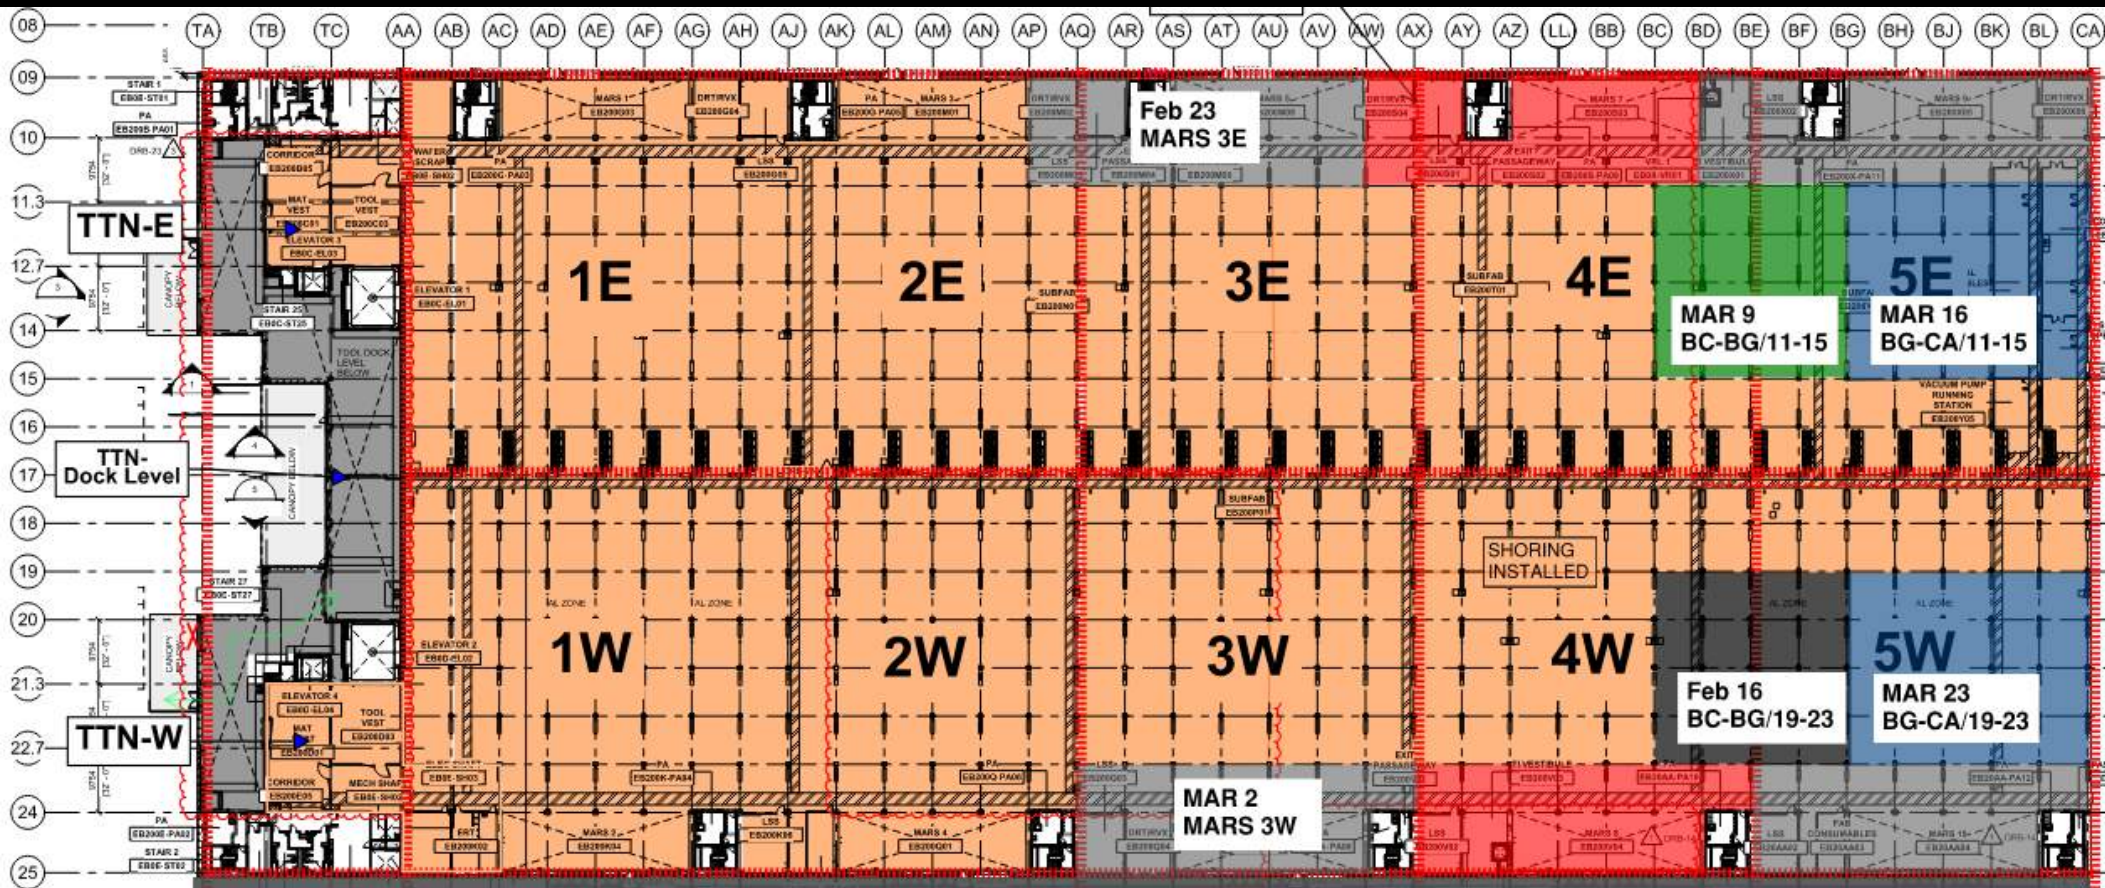


BCT Pressure Tests Today

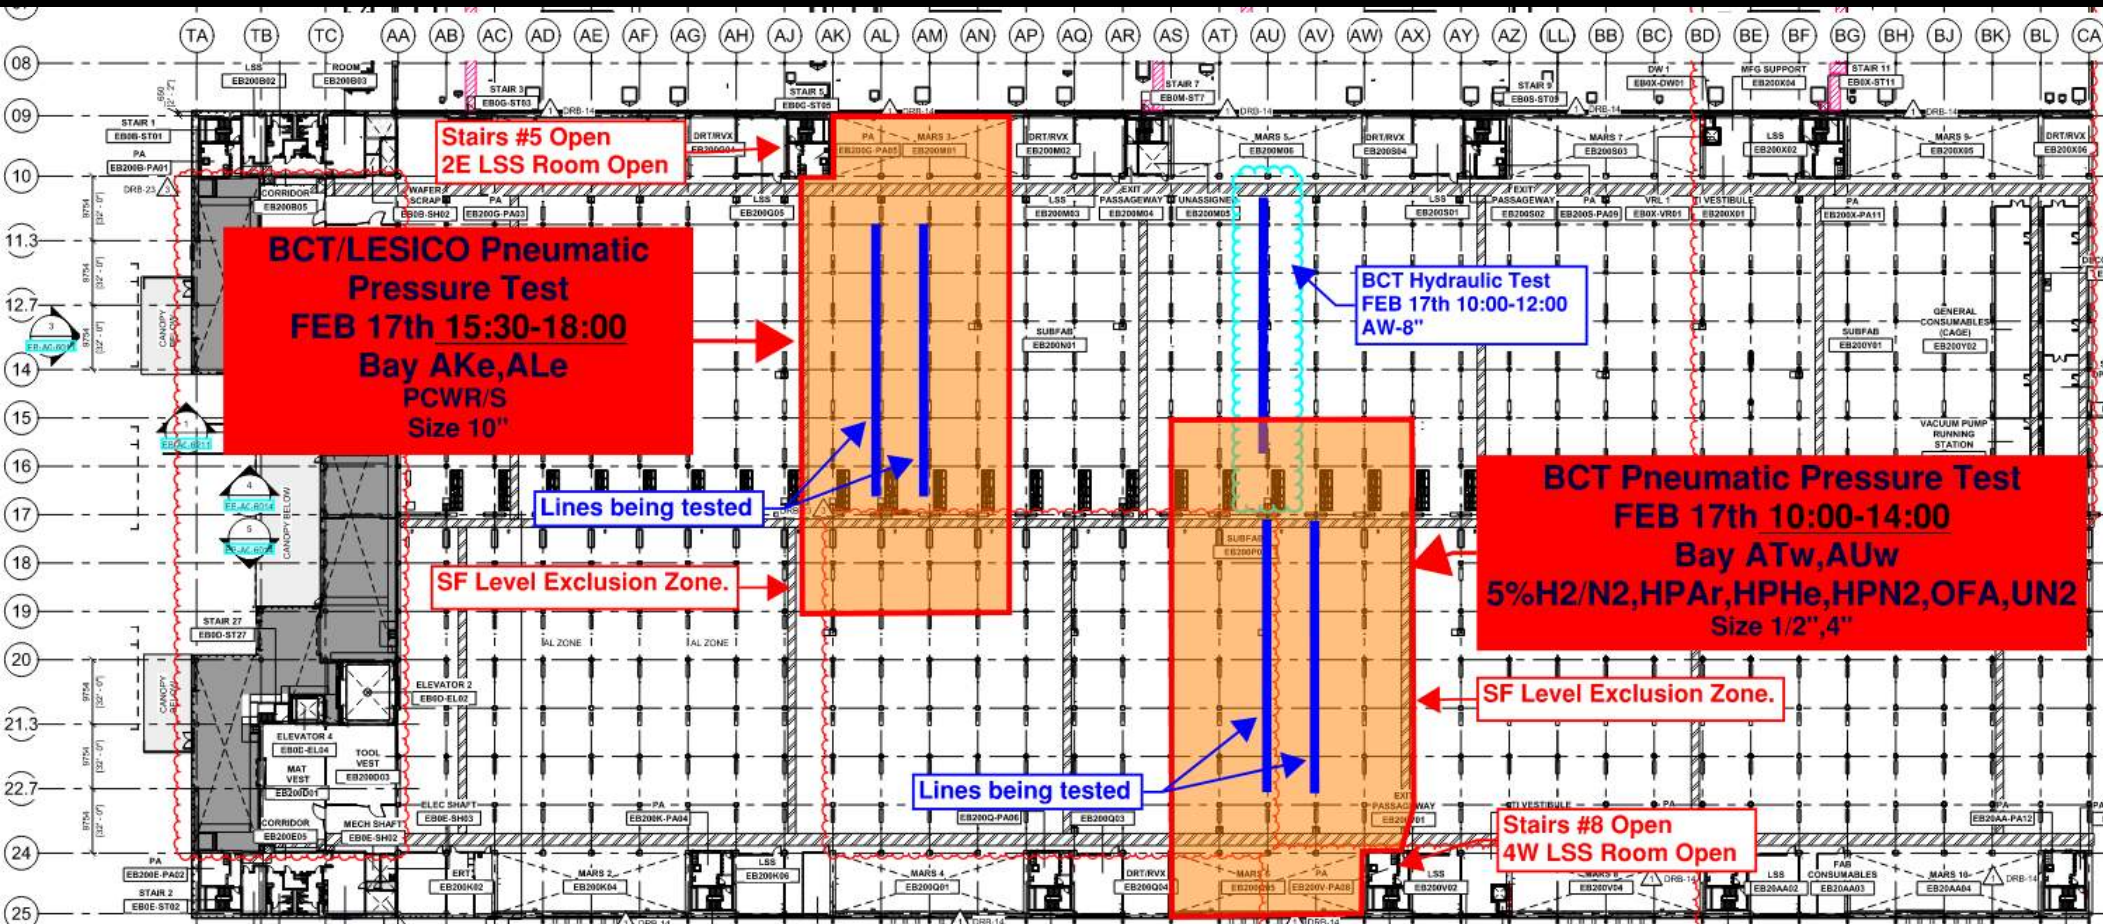



BCT Pressure Tests Tomorrow

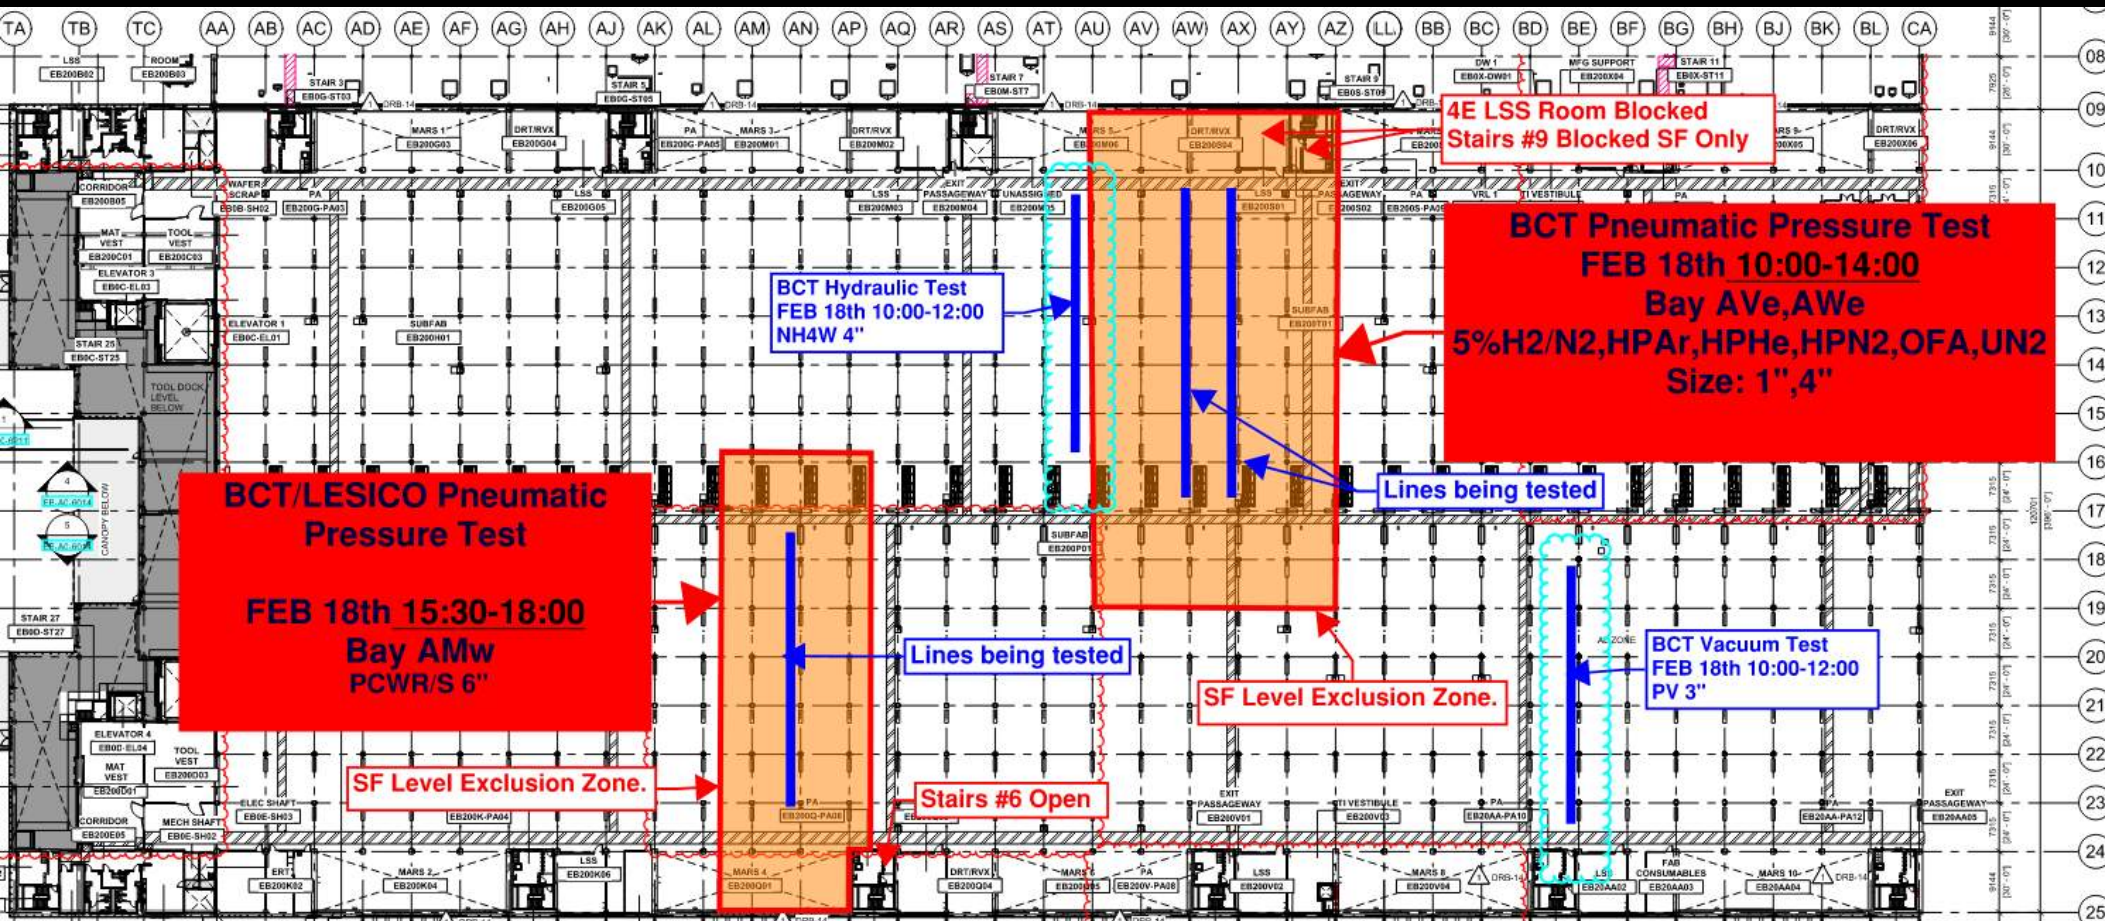



SUBFAB BUILDOUT MOD 2

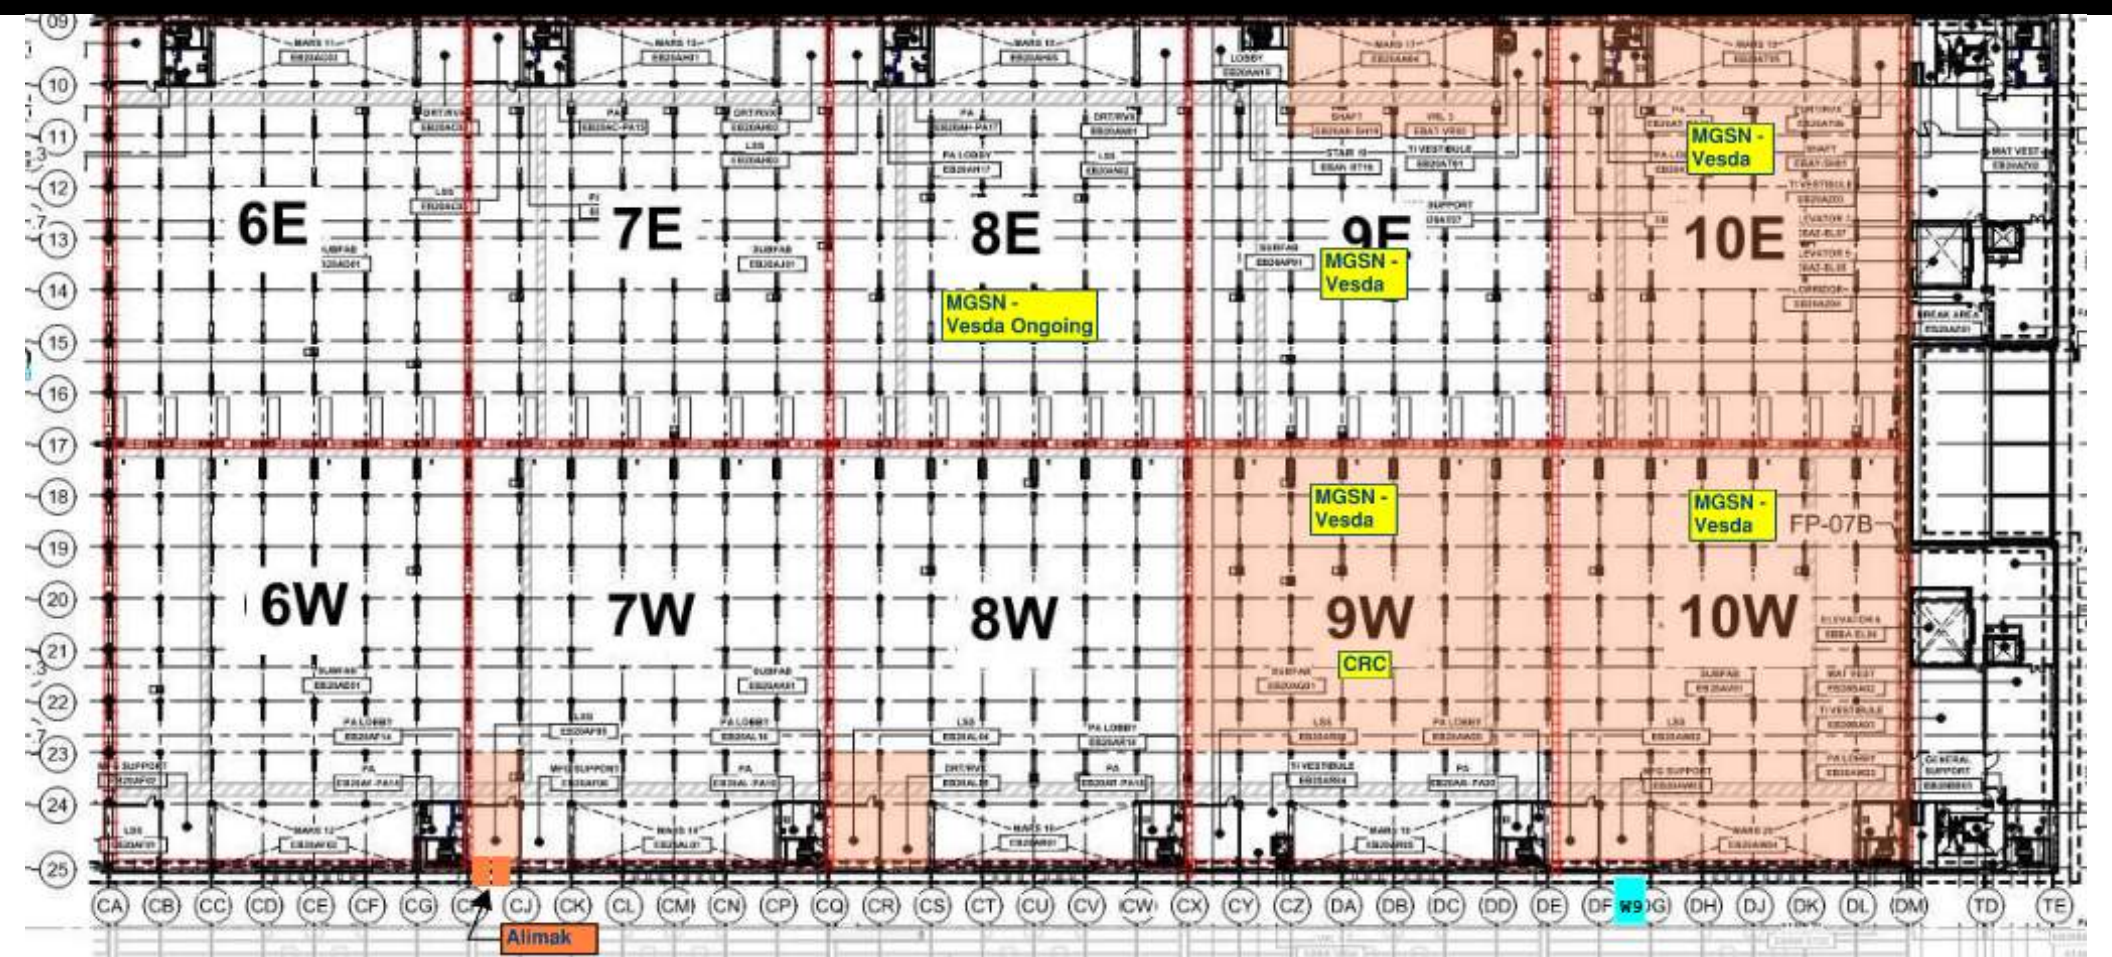

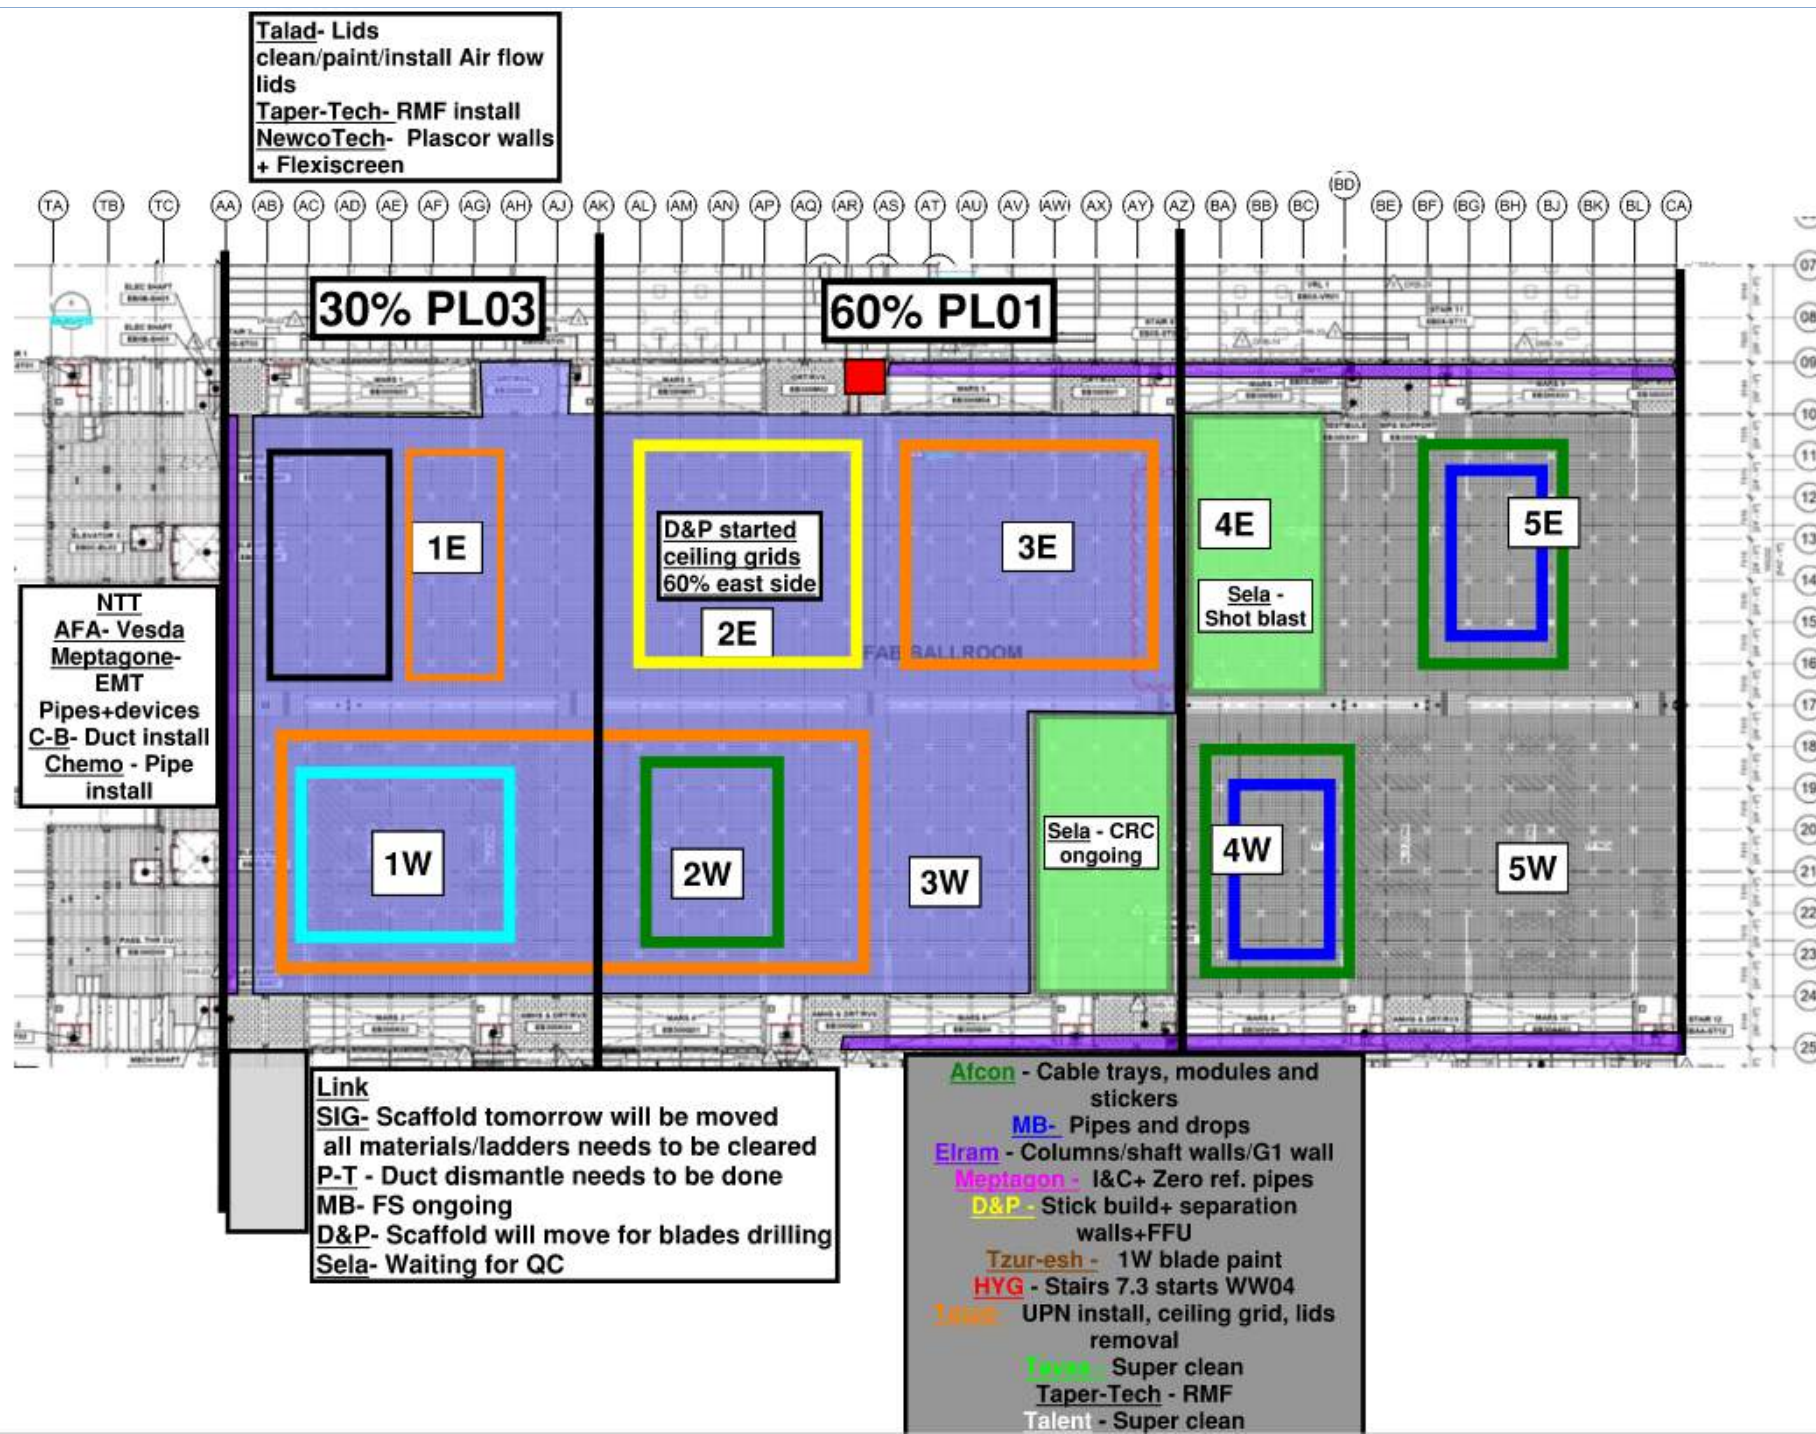


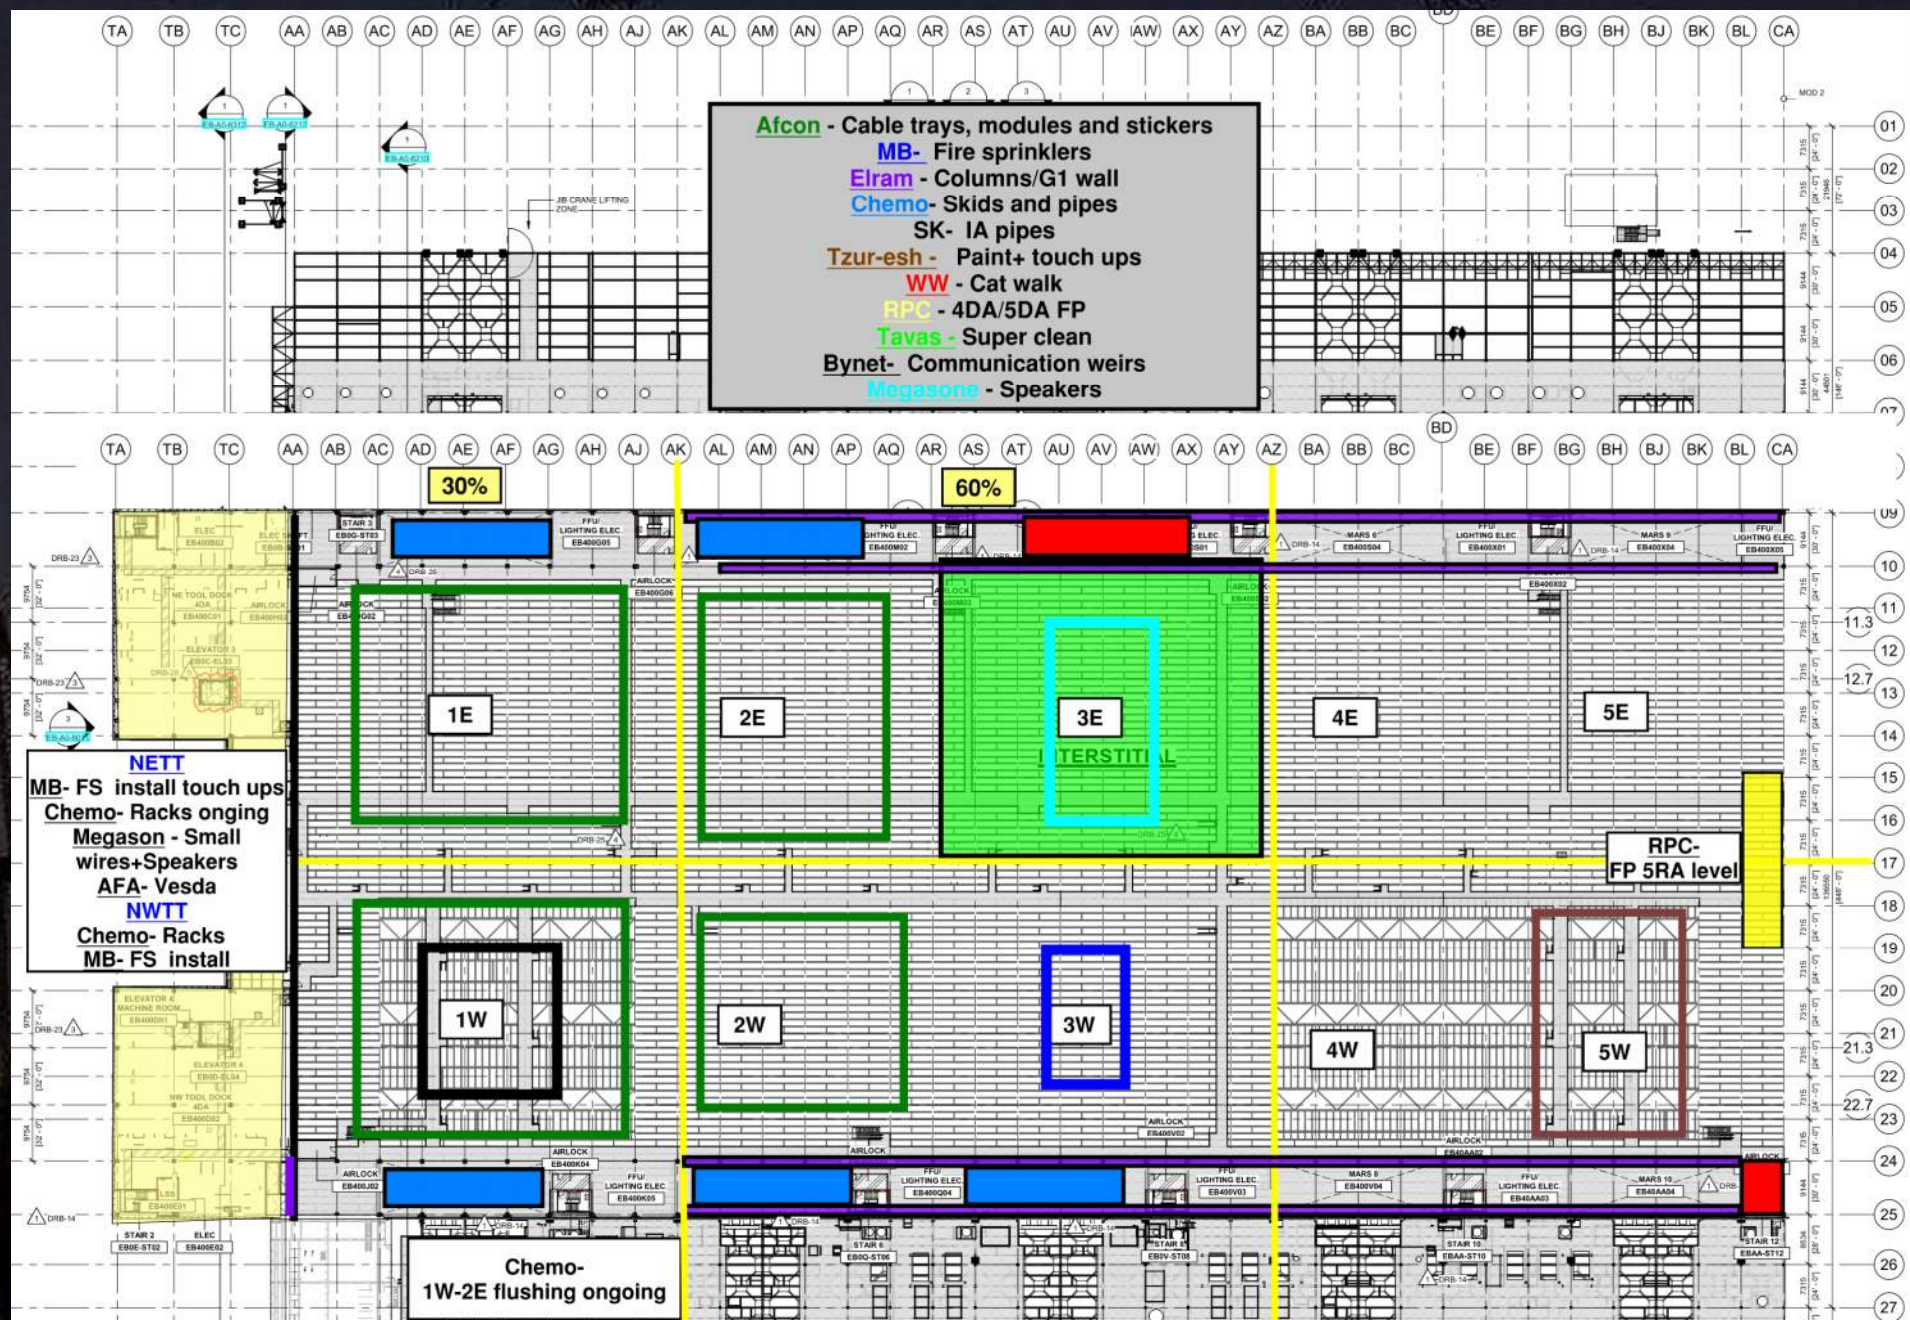

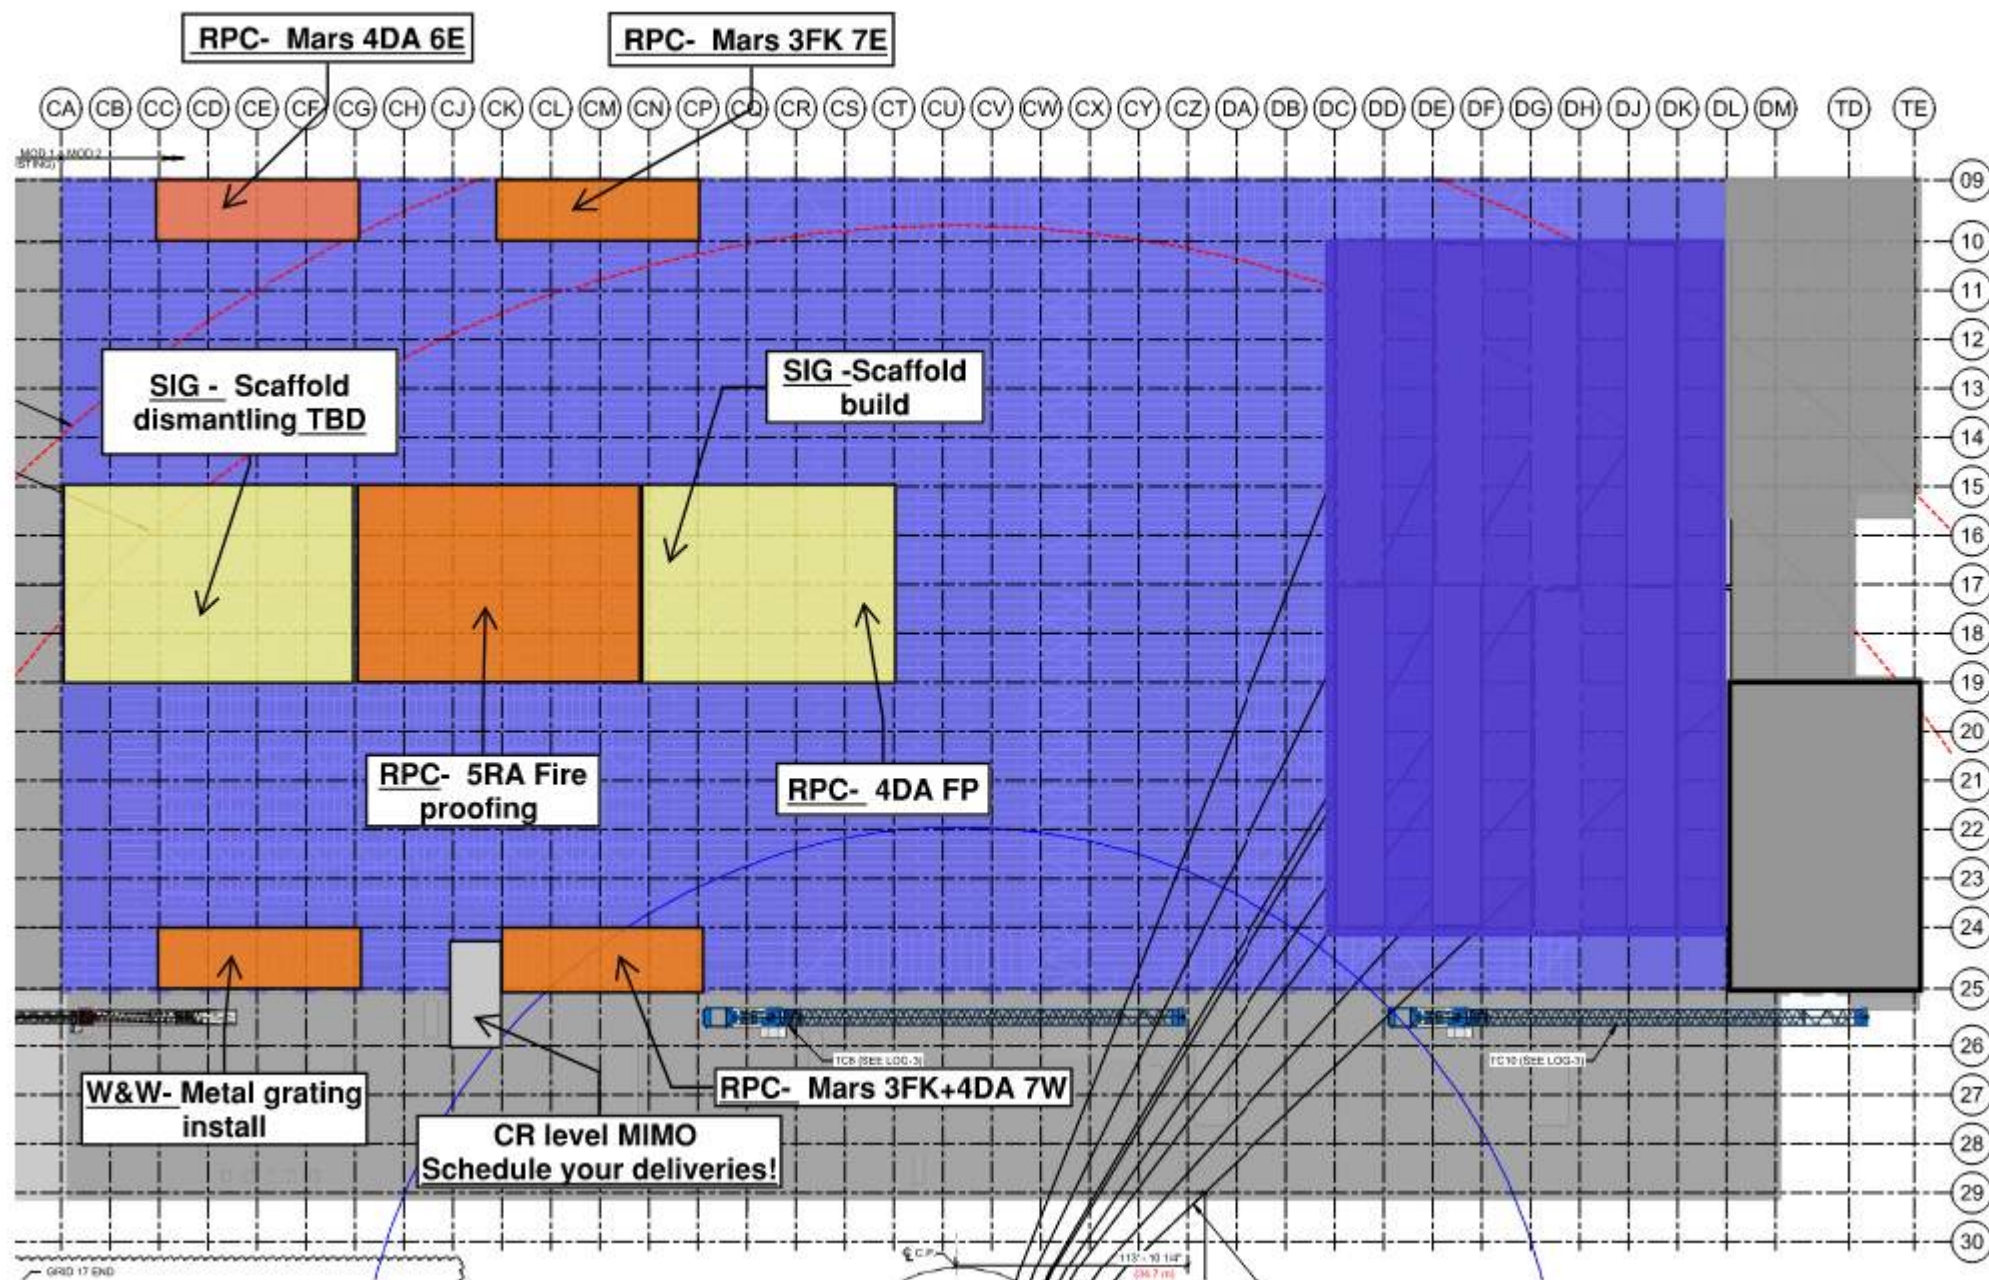


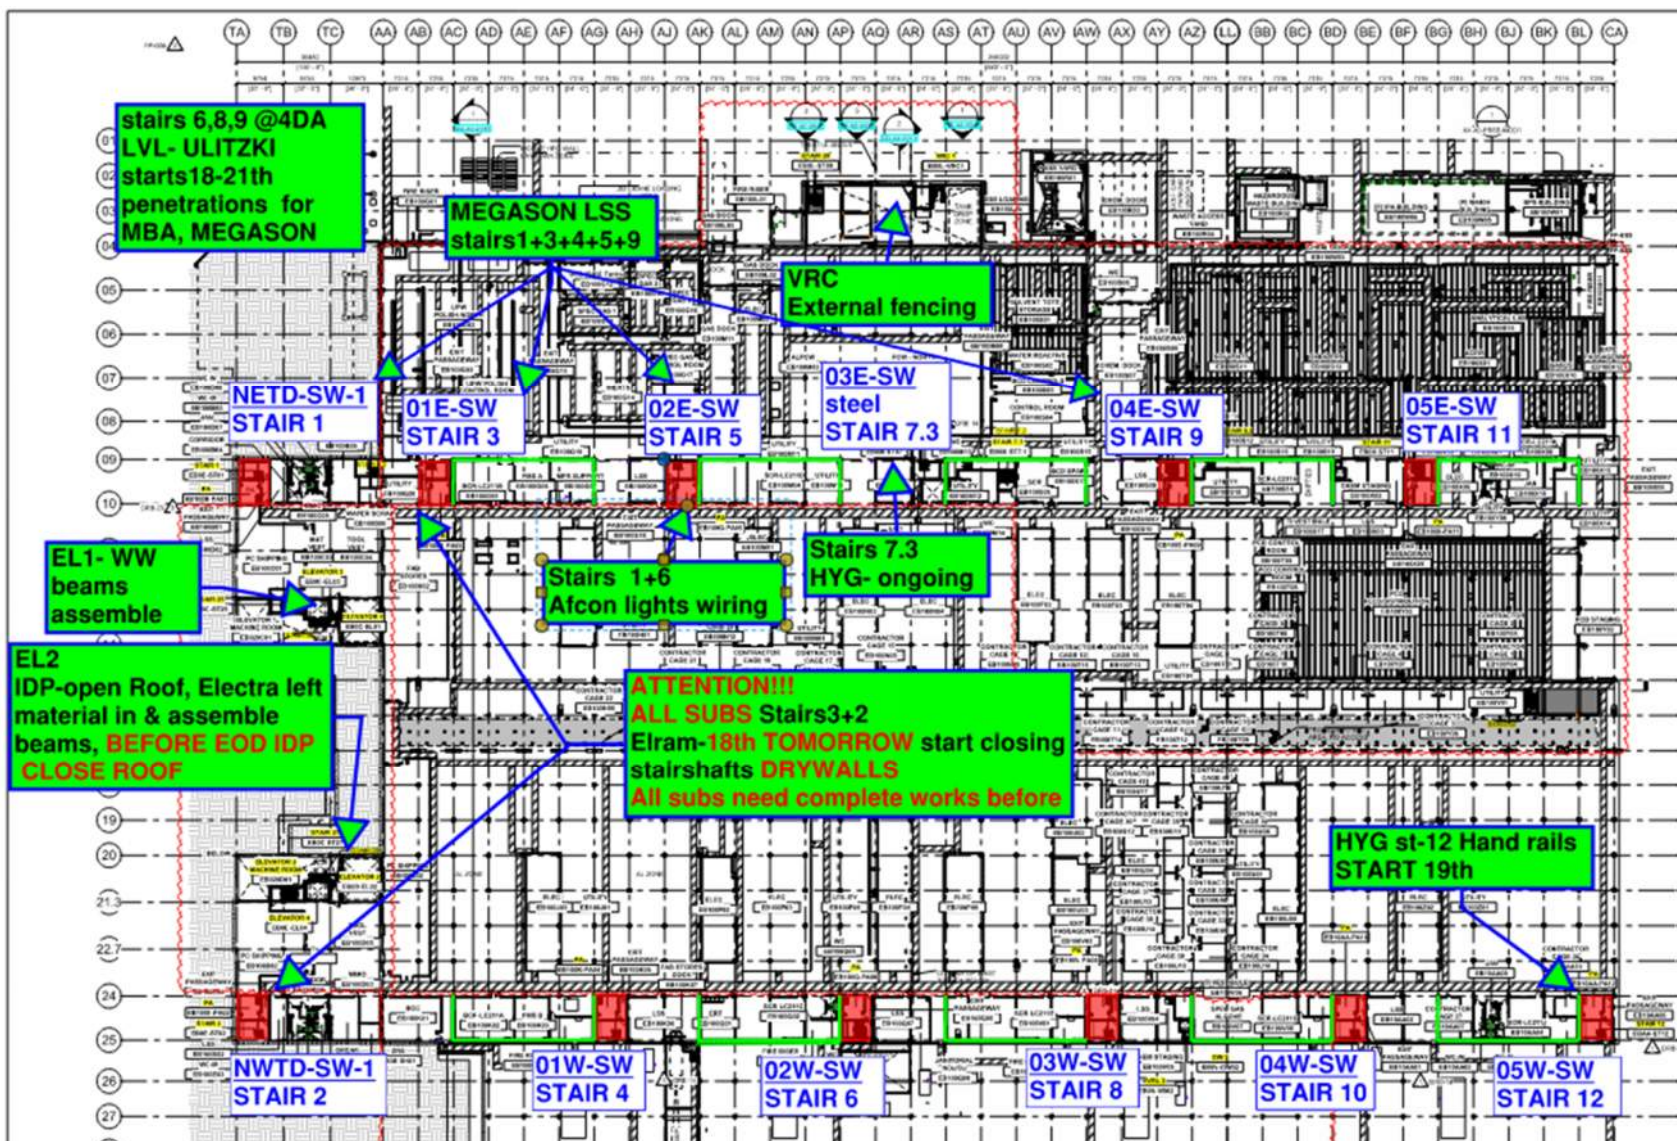


Siding Penetration Request Form

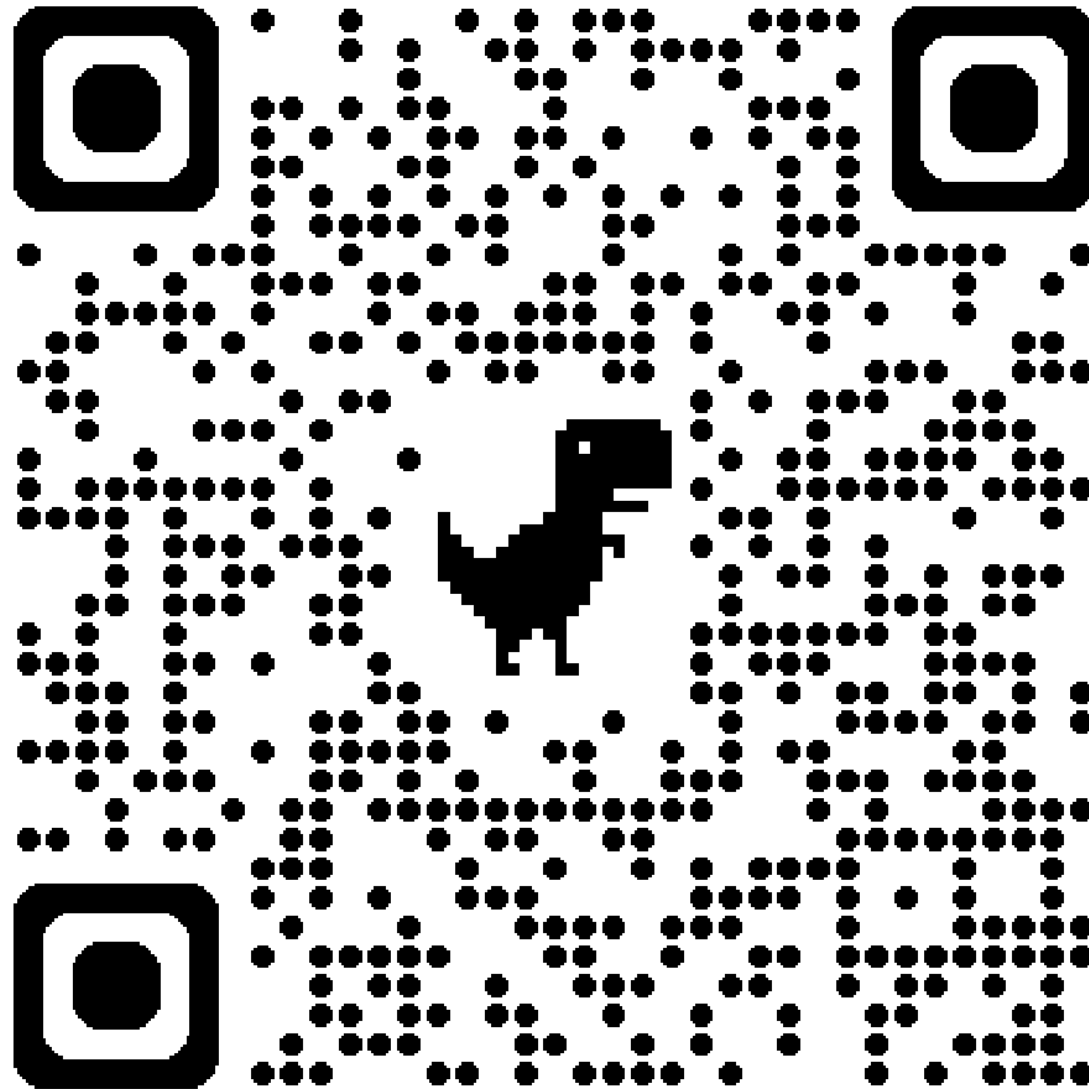

Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

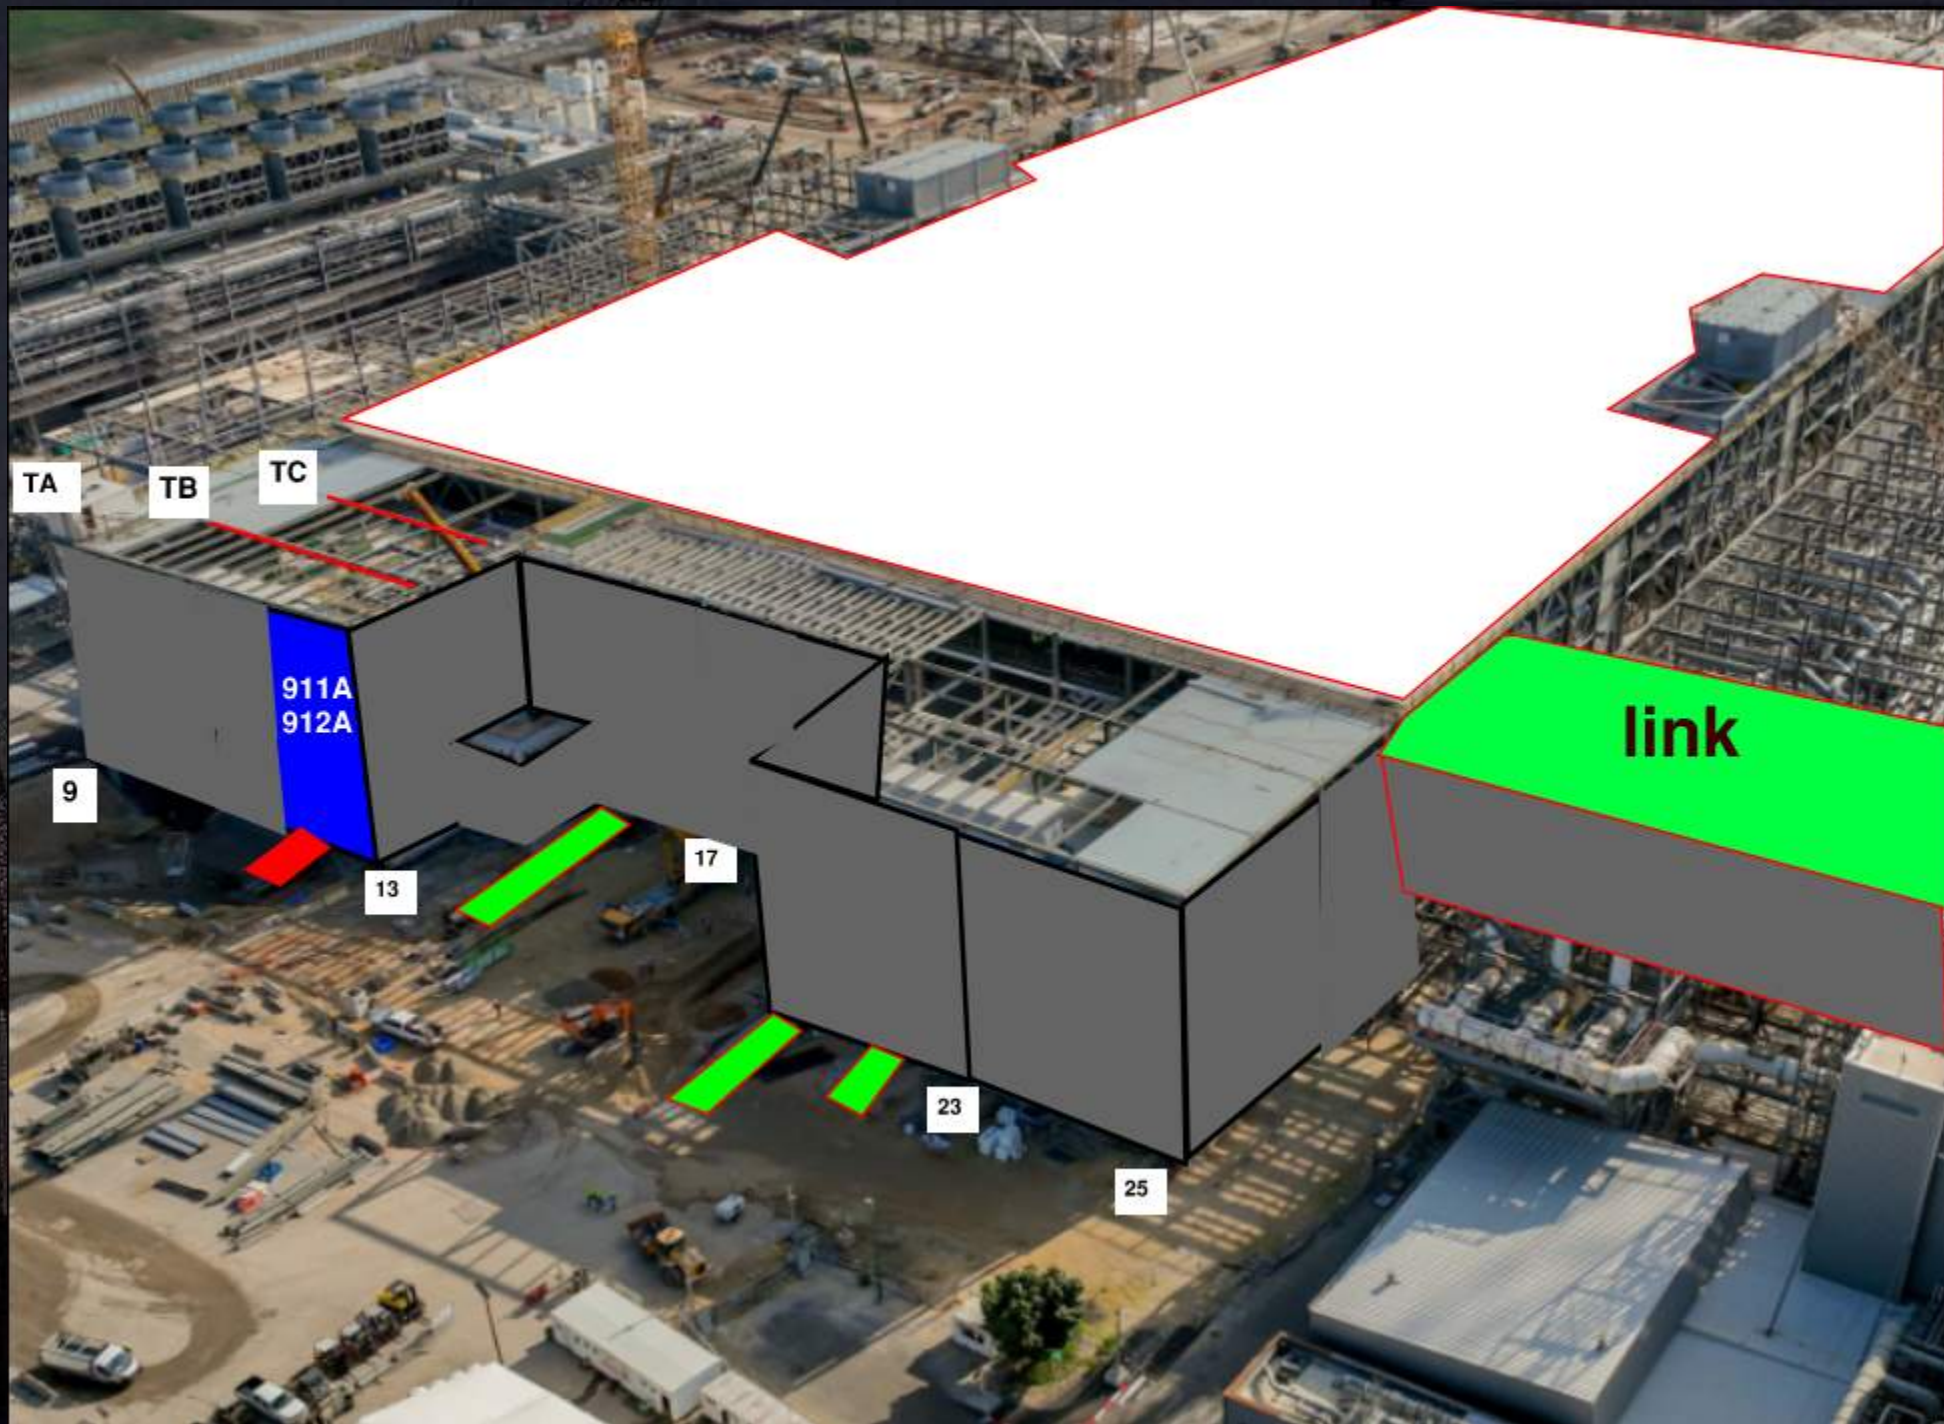

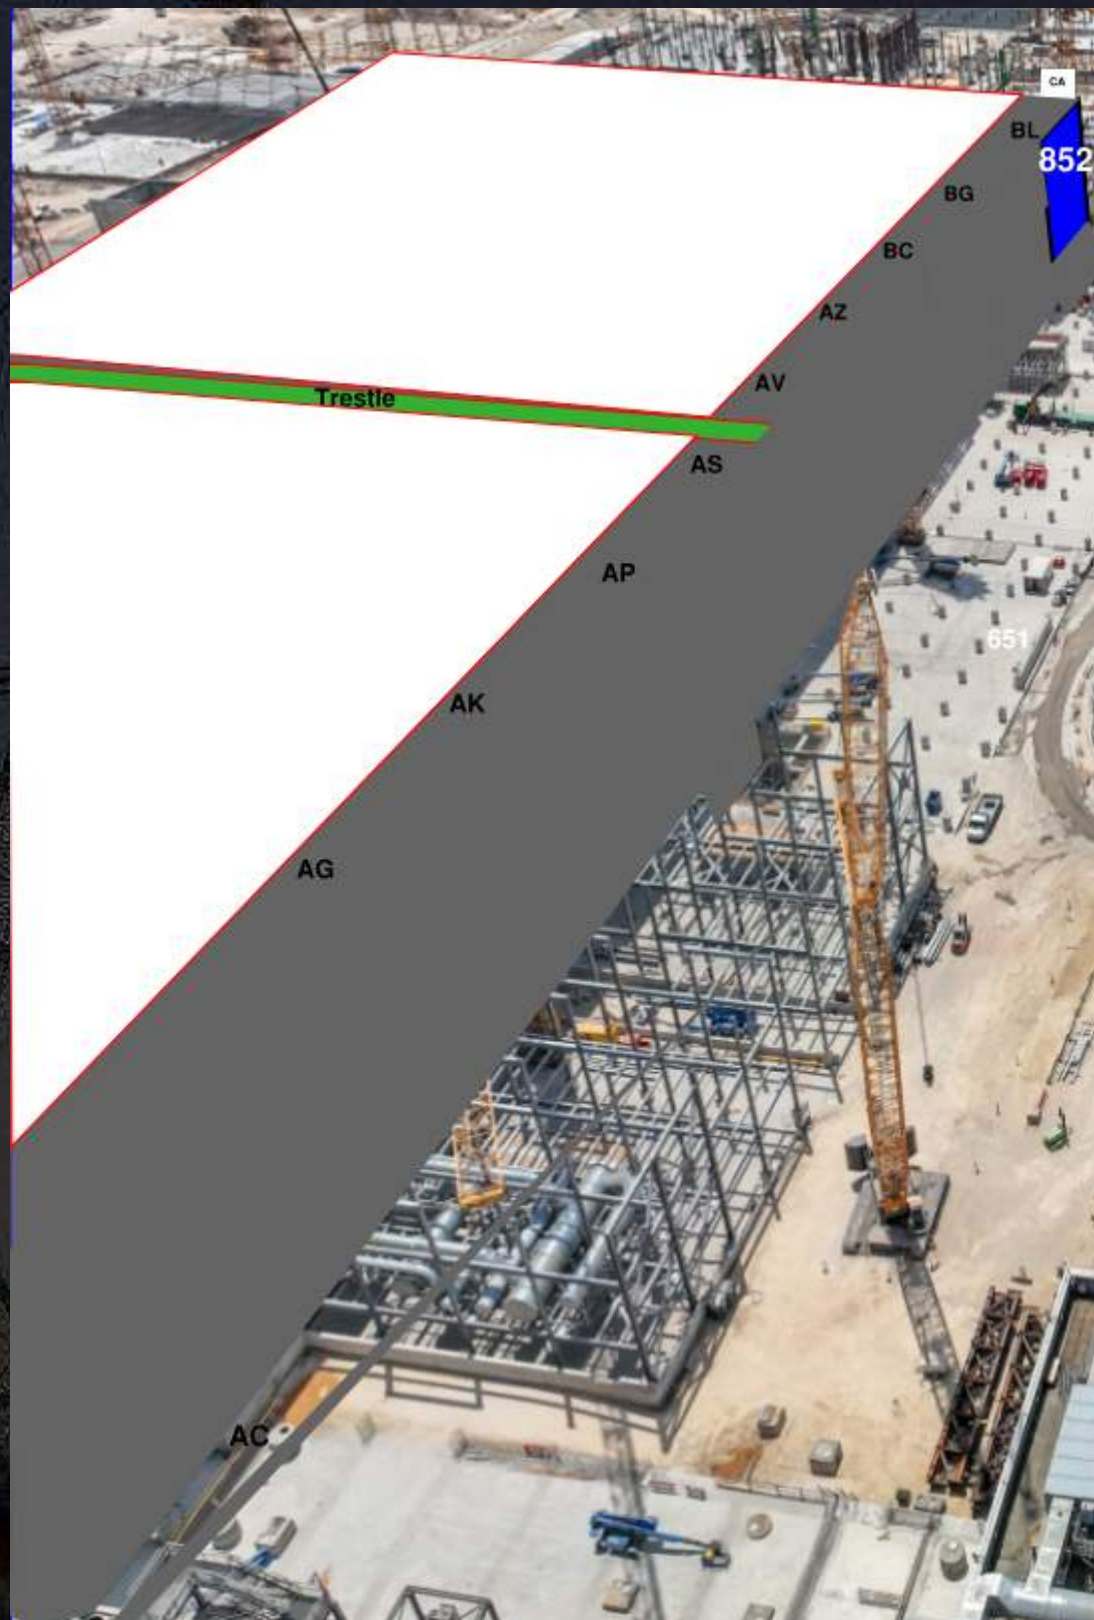




MOBILE EAST SIDE CITY SIDING



2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------



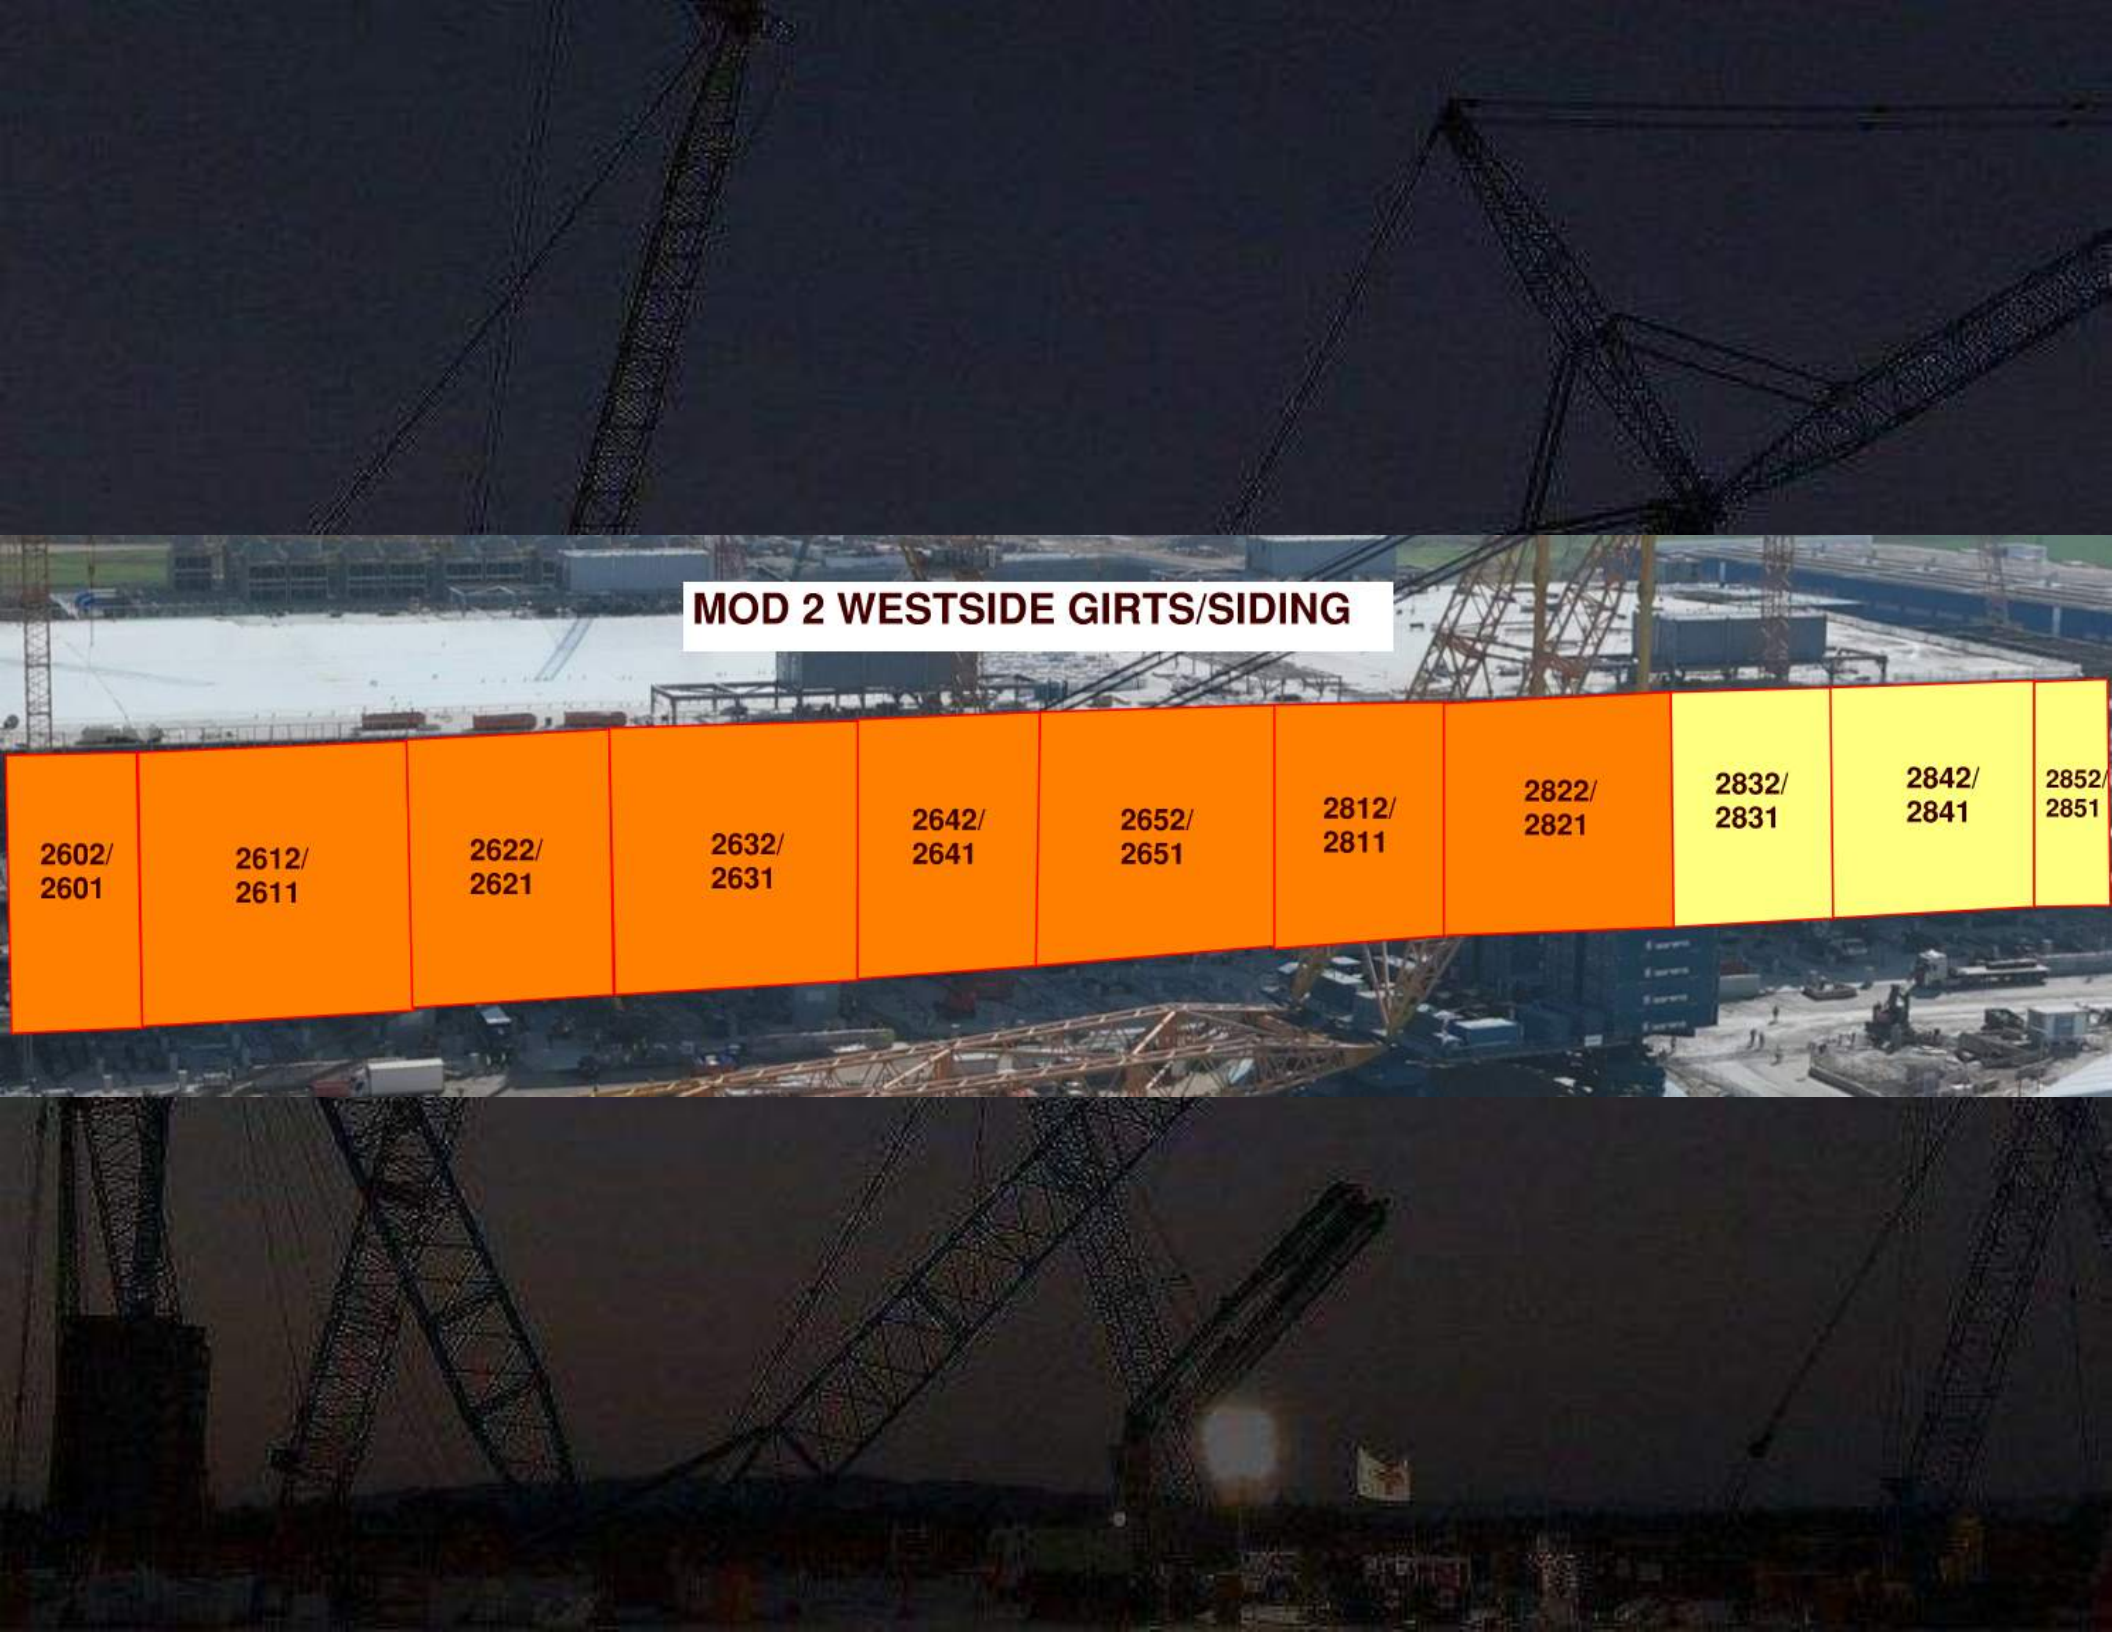

MOD 2 WESTSIDE GIRTS/SIDING

2602/
2601

2612/
2611

2622/
2621

2632/
2631

2642/
2641

2652/
2651

2812/
2811

2822/
2821


2832/
2831

2842/
2841


2852/
2851

PSSS.1

Utility Level
1YA

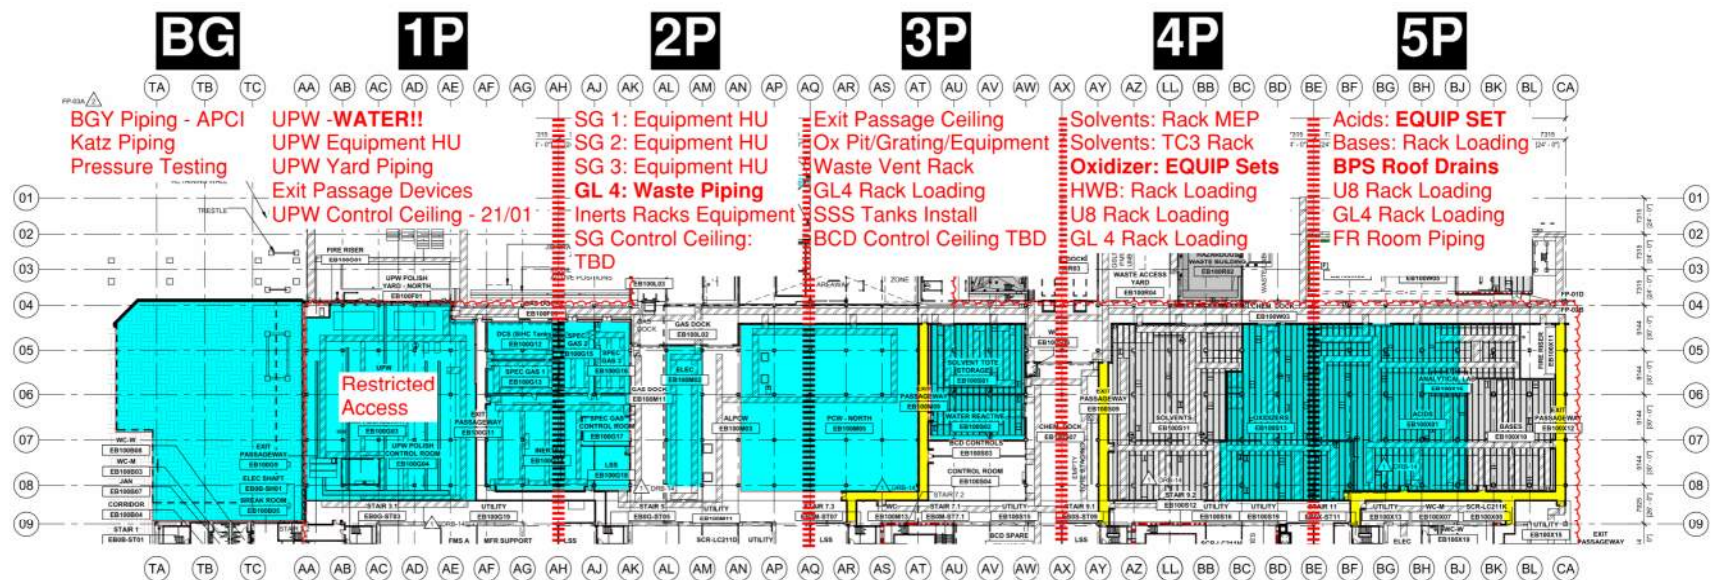


PSSS Roof
2SA

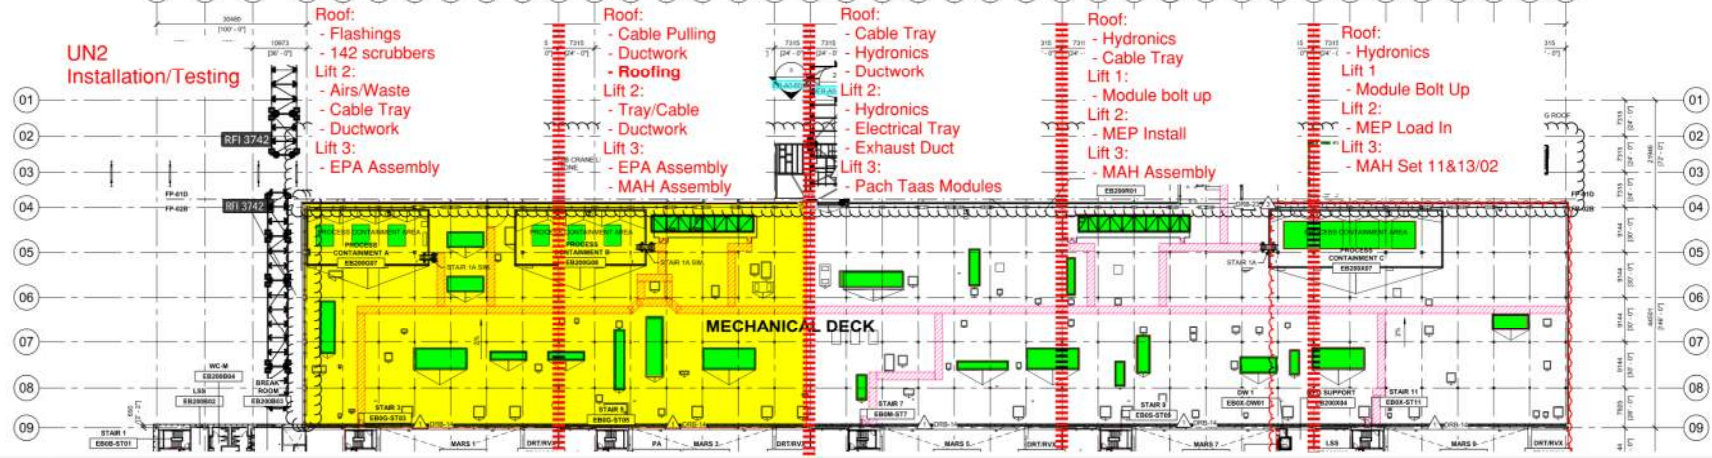

PSSS.2


Utility Level 1YA

PSSS Roof
2SA

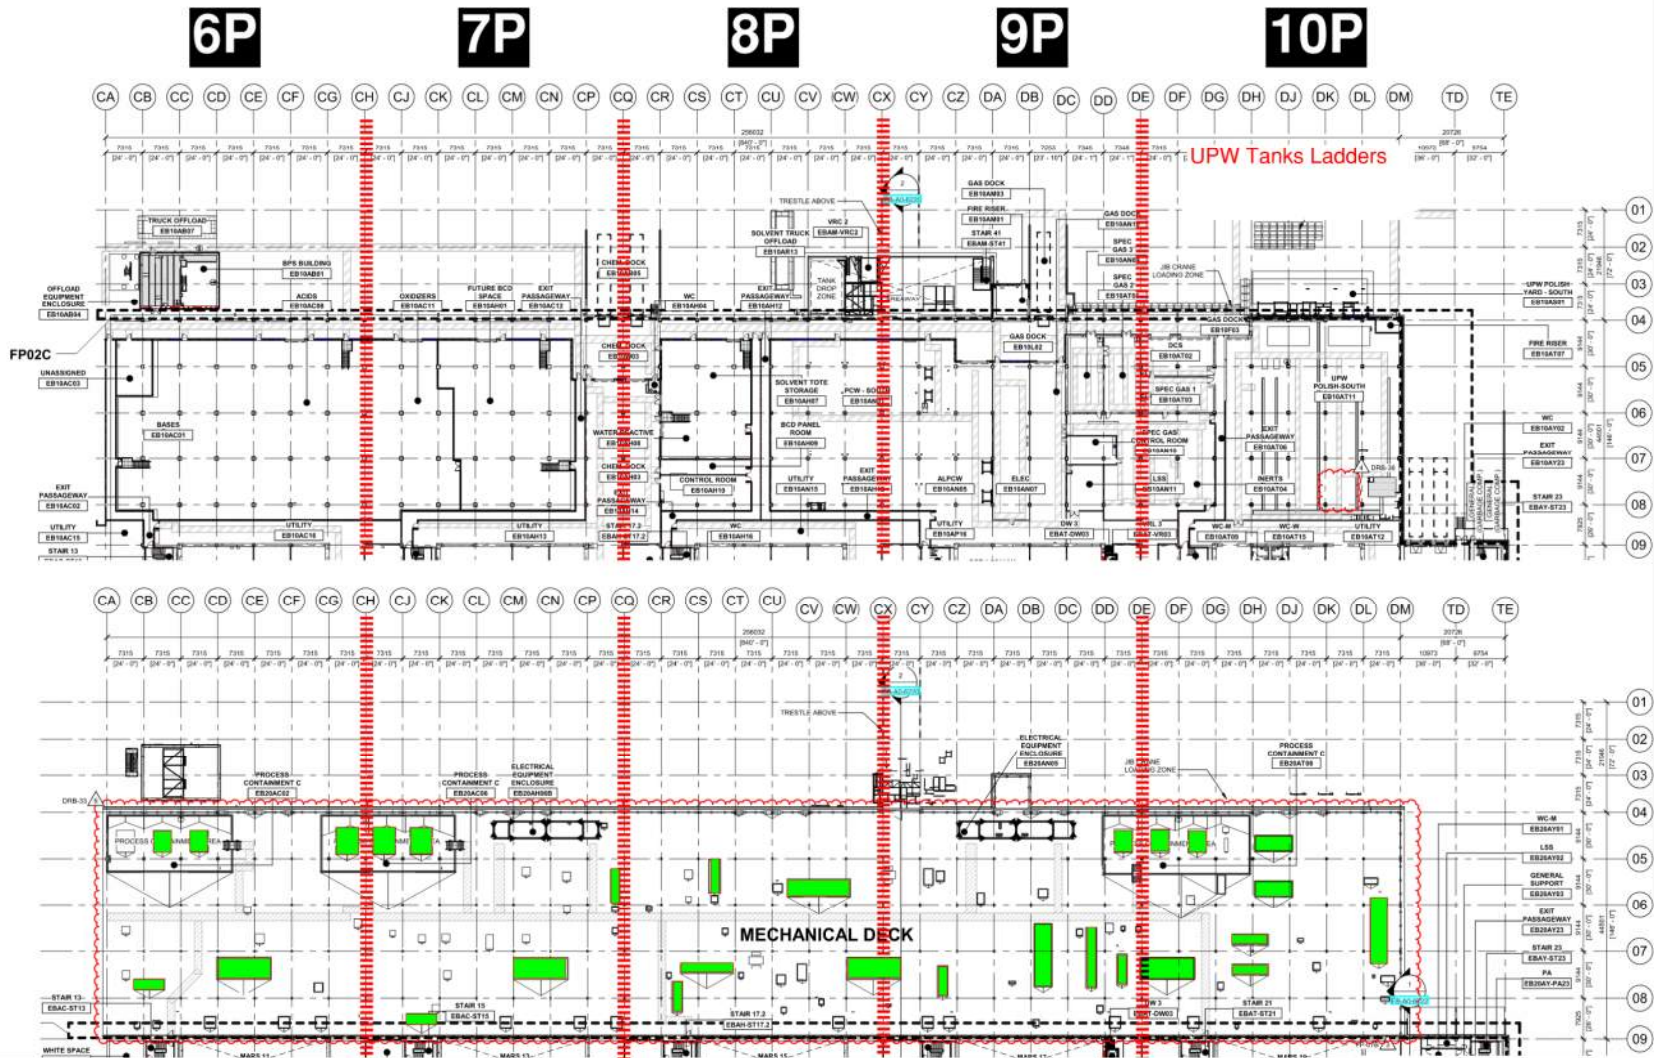


PSSS Pressure Tests

Utility Level
1YA

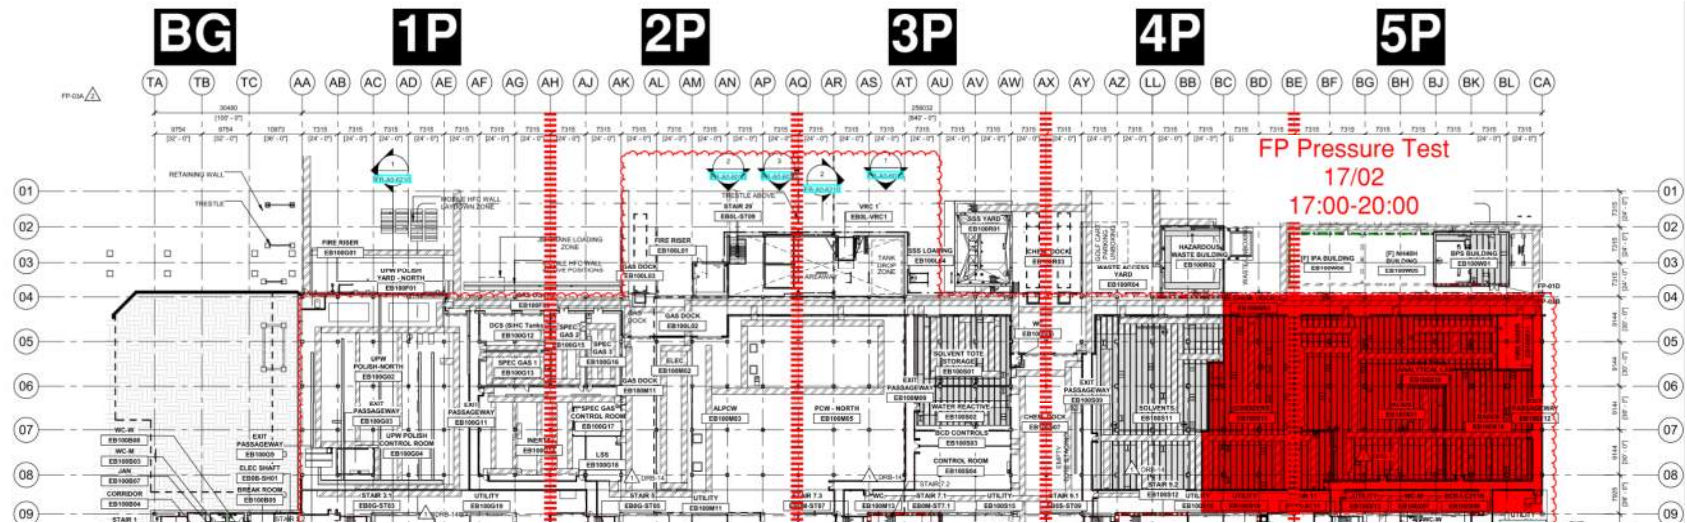

Utility Level
1YA

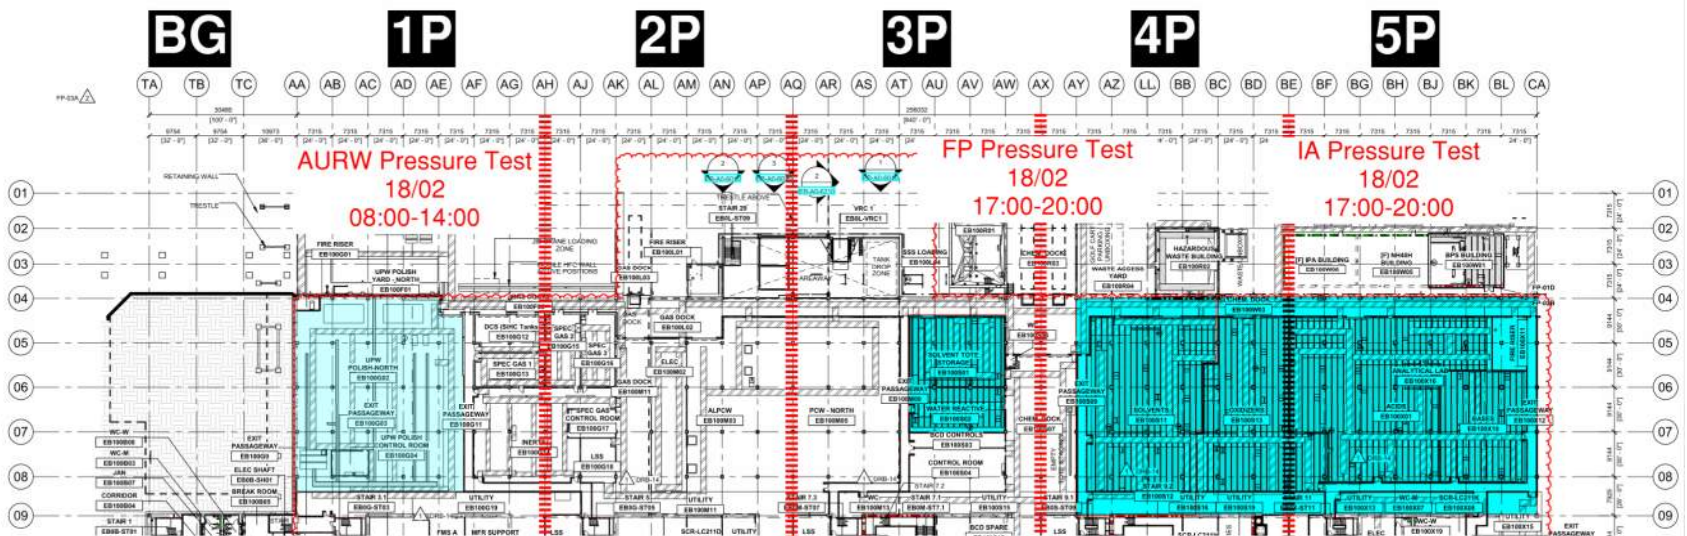

500T Dismantle 18th-20th






WJG UTILITY LEVEL BUILD OUT

WJG – UL

* Megason - working on fire detection and alarm	* Afcon - installation of permanent lighting and cable pulling. * Pach Taas - installation of modules in UL of west SUT.	* Afcon - installation of permanent lighting and cable pulling to the fixtures. * Pach Taas - installation of wall panels. * MB- dismantle of FP pipes and supports for installation of WP	* SK - installation of 3" cooper pipe	
---	---	--	---------------------------------------	--

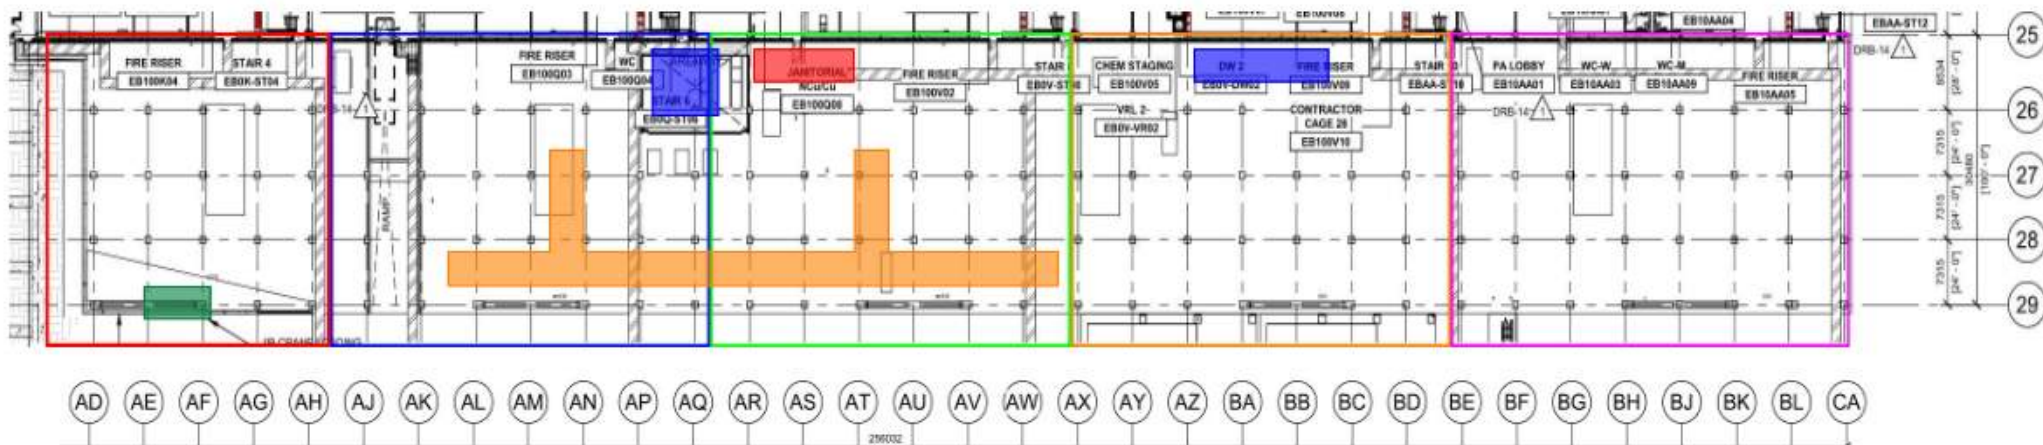

WJG – Lift 2

* W&W - working on Jib crane supports. * SIG - erecting a scaffold for SN gutter pipes works	* Afcon - pulling cables from the roof	* Pach Taas - installation of 1800 mm module and WP.	* SK - installation of CRW pipes to MAH. * Afcon - installation of cable trays and connections to MAH.	* Chemo Aharon - Insulation of UPN 117.
--	---	---	--	--



W&W - fixing of gratings.

- * Sami Najami - cutting grating penetrations.
- * W&W -welding supports for Jib crane.

Sami Najami - cutting grating penetrations.



Crane logistics

Crane: 220 ton
location: AF on west
road

Crane: 500 ton
location: AQ on west
road



EAST YARD

BCS/BSA-JEA Pressure Test Jan.27 -Feb12

CUB 1 Evacuation Muster area North Yard

Paving North Yard WW 7

NORTH YARD

Water Treatment

IW Blend Station Pipe support adjustments Feb. 2-6

CTB 114

SWS 237

ROP 242

URW 262

STAIR 1 (TO ROOF)

PA

LVSS Shut down for Com cable pull Feb 17 0900-1200 Brand Rextec Firestopping ongoing

STAIR 3

STAIR 6

ELECTRICAL

From	Circuit Number	To	To	Owner
3C12_G03-ONS094	6	3C12_G03-ENS099	GENERAL RCPT_2H02	@Omni Tupper
3C12_G03-ONS094	6	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper
3C12_G03-ONS094	6	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper
3C12_G03-ONS094	6	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper
3C12_G03-ONS094	6	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper
3C12_G03-ONS094	6	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper
3C12_G03-ONS094	16	3C12_G03-ENS099	SERVICE RCPT_2H10	@Omni Tupper
3C12_G03-ONS094	7	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper
3C12_G03-ONS094	8	3C12_G03-ENS099	EC25-AH104-S-1H6	@Omni Tupper

STAIR 7

WWT

OPS READY / PUNCHLIST RESTRICTED ACCESS SEE RED AREAS

FMS CONTROL ROOM & LAB

MECH CONTROL ROOM

MECH WORKSHOP

LIWS LAB

TRUCK OFFLOAD 1

TRUCK OFFLOAD 2

STAIR 9

STAIR 10

STAIR 12

BCS

BCS

BSA

Insulation, Labeling Feb 5 QC walk DV Feb 10

TRUCK OFFLOAD 3

TRUCK OFFLOAD 4

STAIR 13

STAIR 15

STAIR 16

GSW

OSS

CSW

Insulation, Labeling Feb 12 QC walk DV Feb 17

Evoqua onsite Feb 20 Vendor runs

TRUCK OFFLOAD 6

TRUCK OFFLOAD 7

TRUCK OFFLOAD 8

TMWX to Roof Trestle Pressure Tests Jan 26 RE Test ongoing

NATURAL GAS EXCLUSION ZONE

TMWX 293

Analyzer Room

NH4W 283

NH4W to Roof Trestle Pressure Tests Inner pipe Jan 23 RE Test ongoing

STAIR 2 (TO ROOF)

PA

Overhead Catwalk install ongoing Feb 10-March 27

CHILLERS

CHILLERS

Trane/Rockwell Cx AFDs Chiller start dates: 126-1-10 Jan 23-29 111-1-10 Jan 30- TBD 126-3-10 TBD

SAND FILTERS

UN2 / IA Tie-in Feb.12

PA

Purge Lines and Charge Natural Gas To Site Feb.18

NATURAL GAS EXCLUSION ZONE

BOILERS

Natural Gas to Boiler Feb.19

OIL FUEL TANK

Revised Access

FUEL OFF LOADING INTEL ACCESS ONLY

Scaffold Removal or Modify March 6

STAIR 20

STAIR 17

STAIR 18

STAIR 19

STAIR 21

STAIR 22

STAIR 23

STAIR 24

STAIR 25

STAIR 26

STAIR 27

STAIR 28

STAIR 29

STAIR 30

STAIR 31

STAIR 32

STAIR 33

STAIR 34

STAIR 35

STAIR 36

STAIR 37

STAIR 38

STAIR 39

STAIR 40

STAIR 41

STAIR 42

STAIR 43

STAIR 44

STAIR 45

STAIR 46

STAIR 47

STAIR 48

STAIR 49

STAIR 50

STAIR 51

STAIR 52

STAIR 53

STAIR 54

STAIR 55

STAIR 56

STAIR 57

STAIR 58

STAIR 59

STAIR 60

STAIR 61

STAIR 62

STAIR 63

STAIR 64

STAIR 65

STAIR 66

STAIR 67

STAIR 68

STAIR 69

STAIR 70

STAIR 71

STAIR 72

STAIR 73

STAIR 74

STAIR 75

STAIR 76

STAIR 77

STAIR 78

STAIR 79

STAIR 80

STAIR 81

STAIR 82

STAIR 83

STAIR 84

STAIR 85

STAIR 86

STAIR 87

STAIR 88

STAIR 89

STAIR 90

STAIR 91

STAIR 92

STAIR 93

STAIR 94

STAIR 95

STAIR 96

STAIR 97

STAIR 98

STAIR 99

STAIR 100

STAIR 101

STAIR 102

STAIR 103

STAIR 104

STAIR 105

STAIR 106

STAIR 107

STAIR 108

STAIR 109

STAIR 110

STAIR 111

STAIR 112

STAIR 113

STAIR 114

STAIR 115

STAIR 116

STAIR 117

STAIR 118

STAIR 119

STAIR 120

STAIR 121

STAIR 122

STAIR 123

STAIR 124

STAIR 125

STAIR 126

STAIR 127

STAIR 128

STAIR 129

STAIR 130

STAIR 131

STAIR 132

STAIR 133

STAIR 134

STAIR 135

STAIR 136

STAIR 137

STAIR 138

STAIR 139

STAIR 140


STAIR 141

STAIR 142


STAIR 143




CUB 1 Exterior Pre-Punch Status

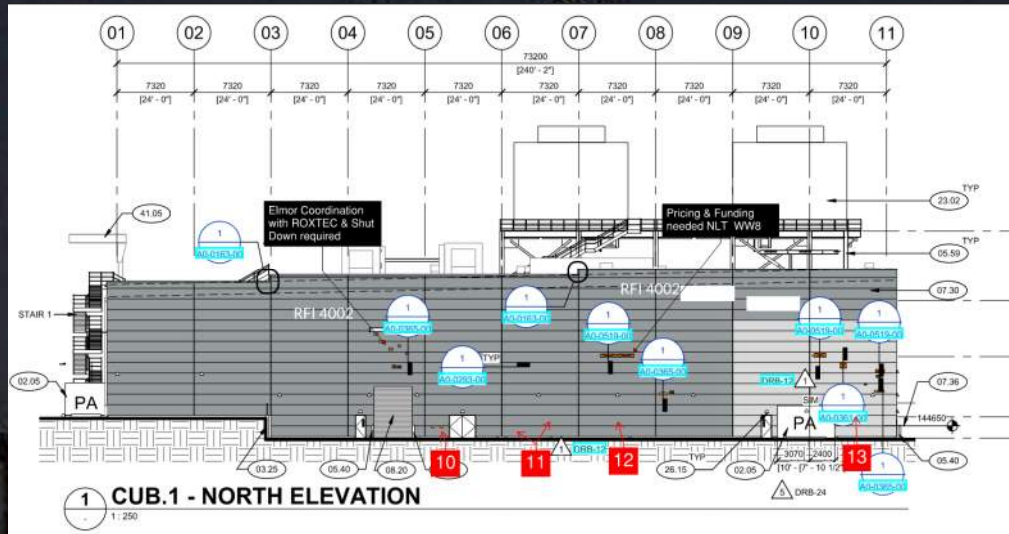

1. North Elevation ROXTEC Electrical in Coordination with Elmor WW 8
2. West Elevation pending UN2 tie in, Blank out Conditioned water to CUB 2
3. Set Final Man door complete Access Controls March 6- 20

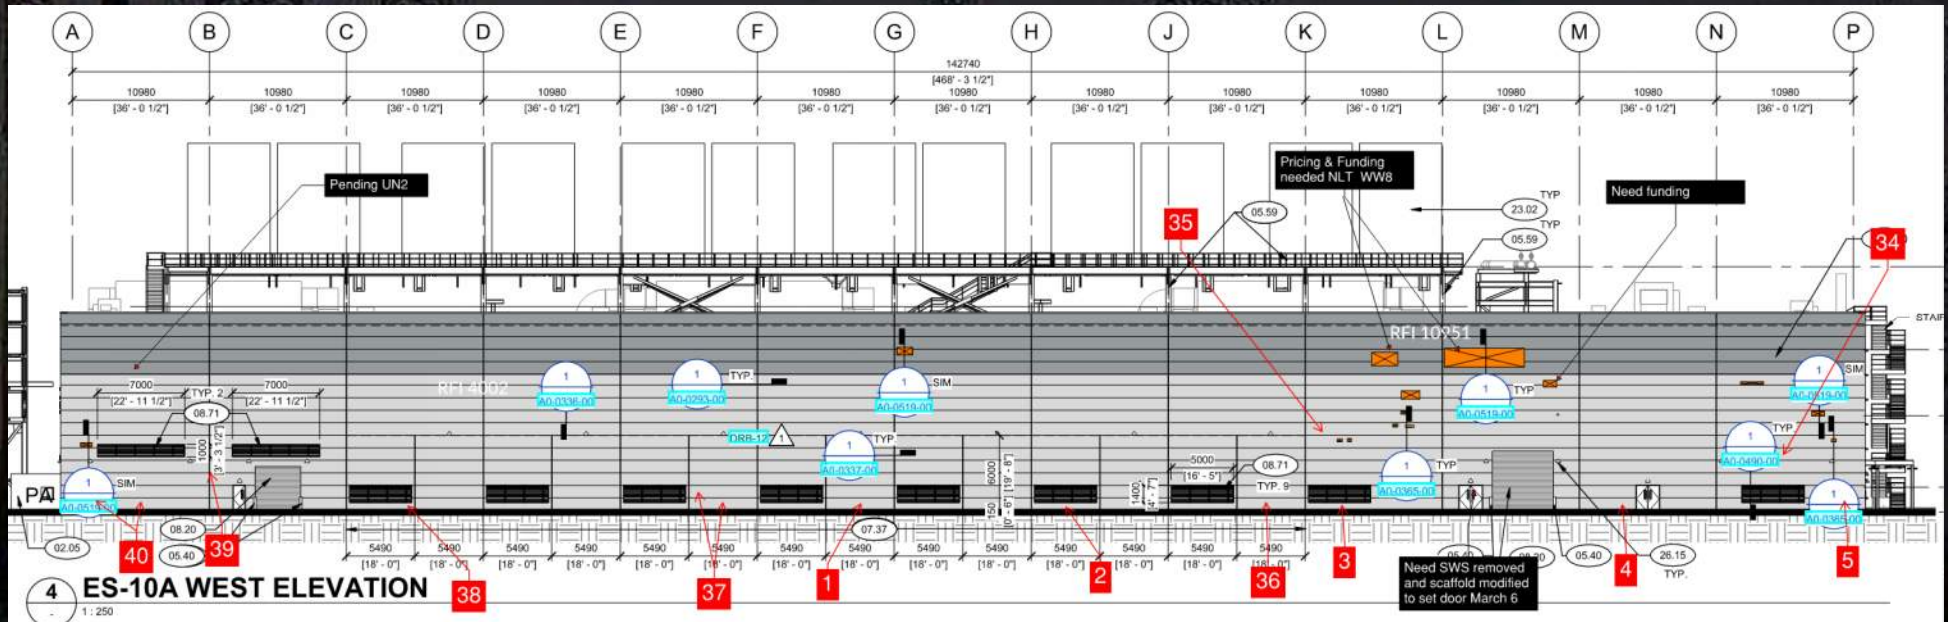


CUB 1 – EXTERIOR/ROOF

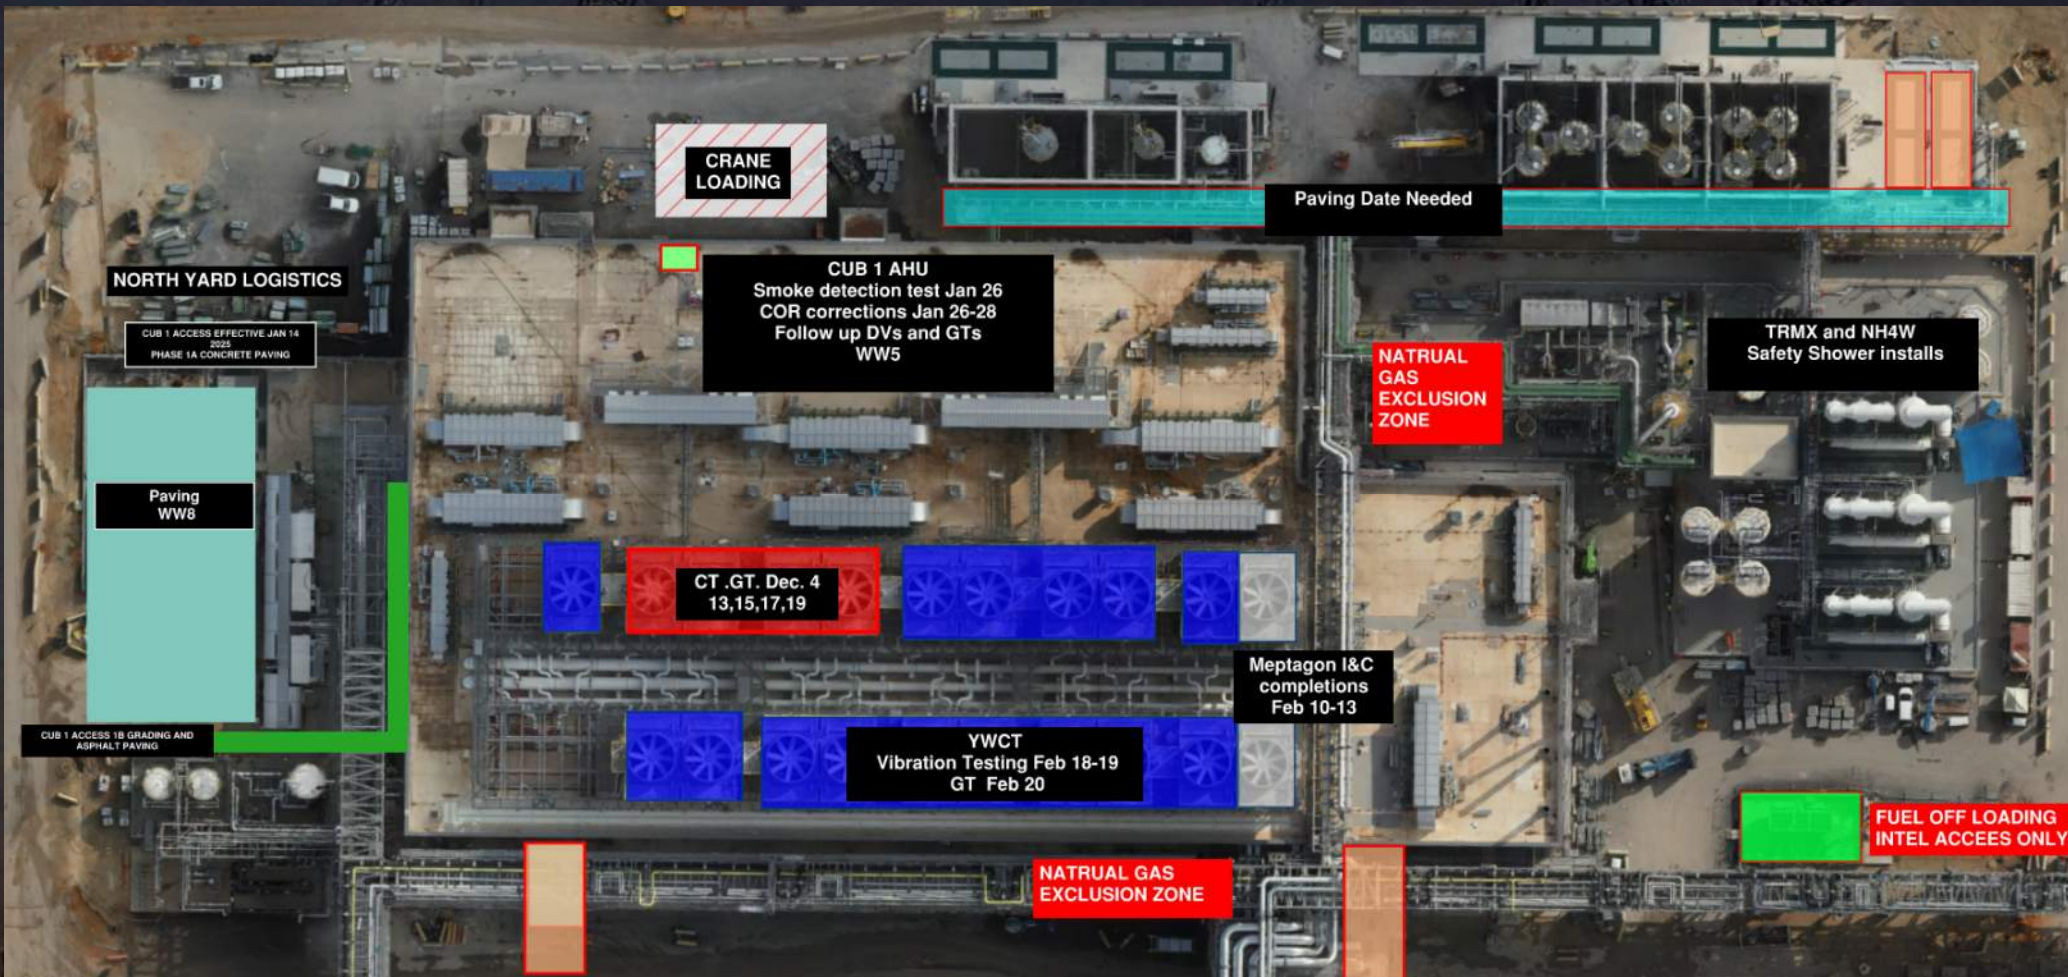


CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

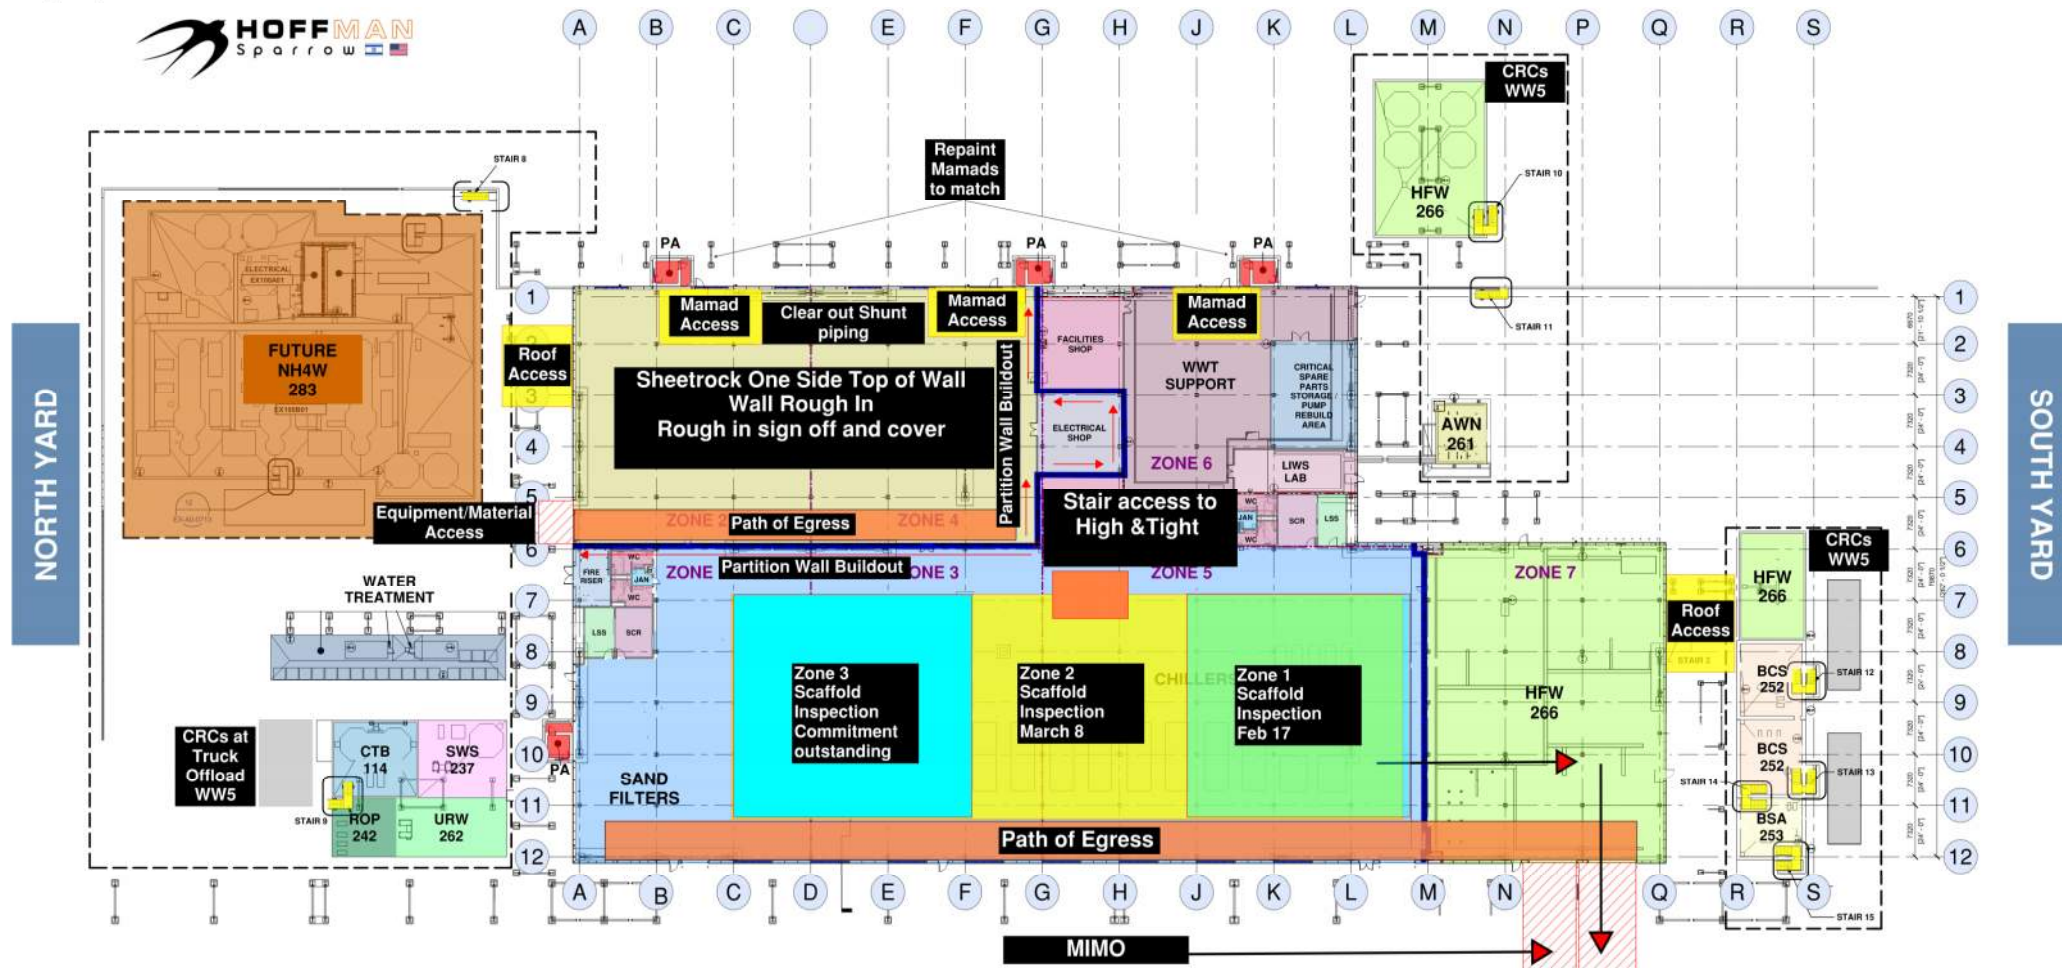

CUB 2 – EXTERIOR/ROOF

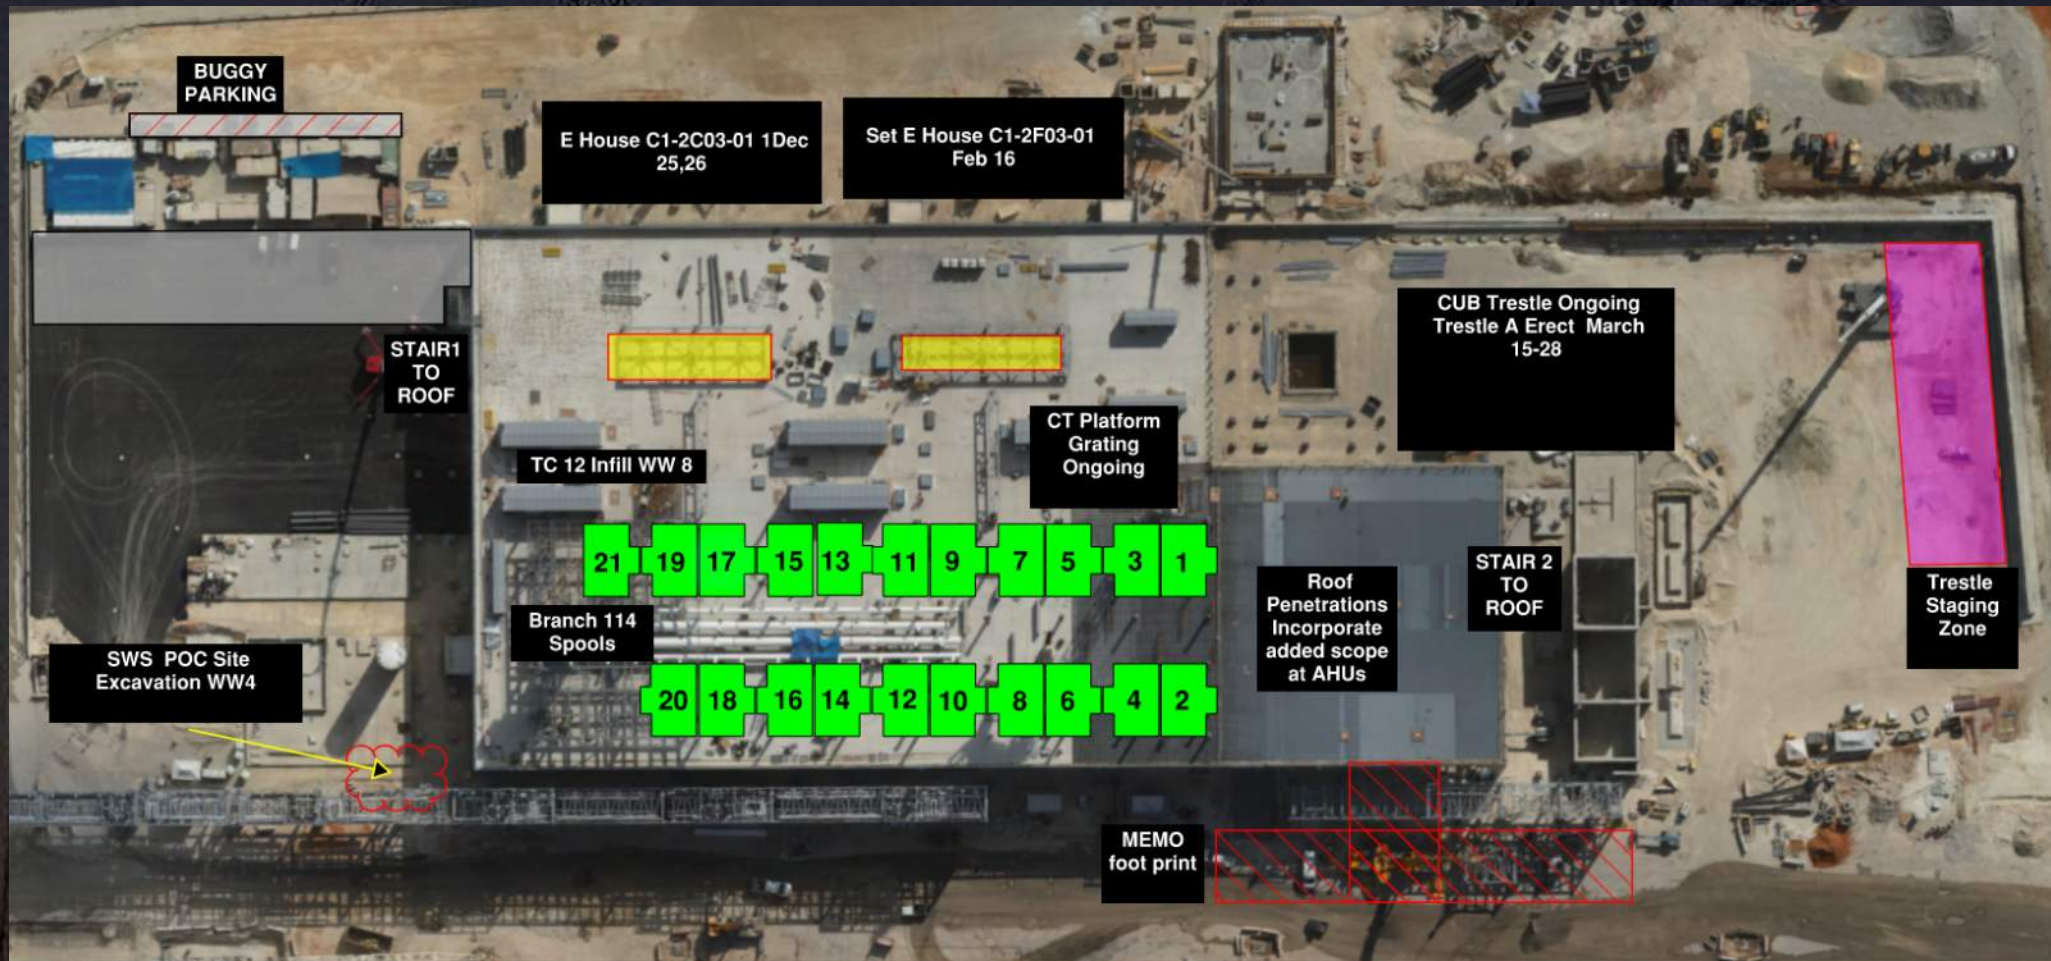



HOFFMAN CONSTRUCTION COMPANY






Daily Coordination Meeting

Site Logistics


North

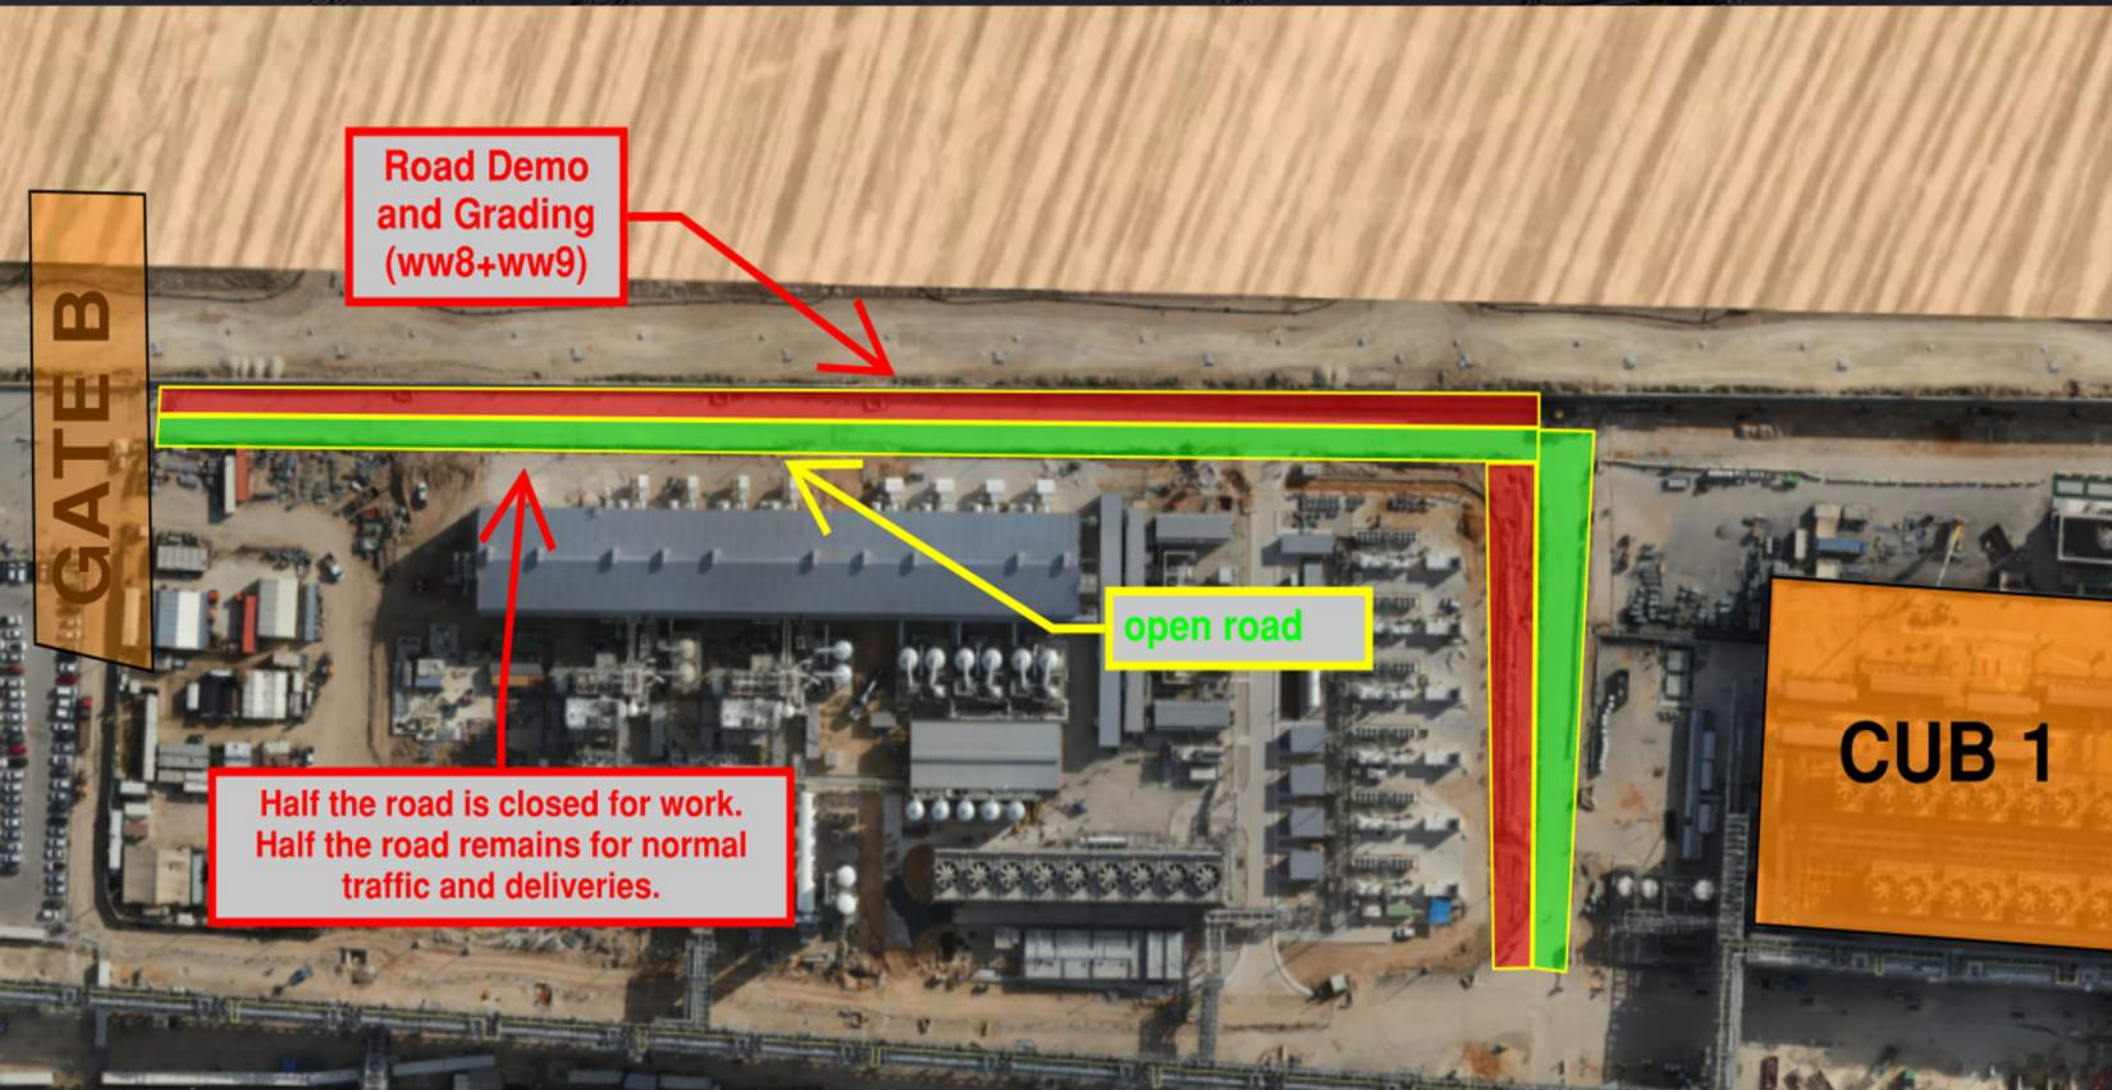



Daily Coordination Meeting


Site Logistics North

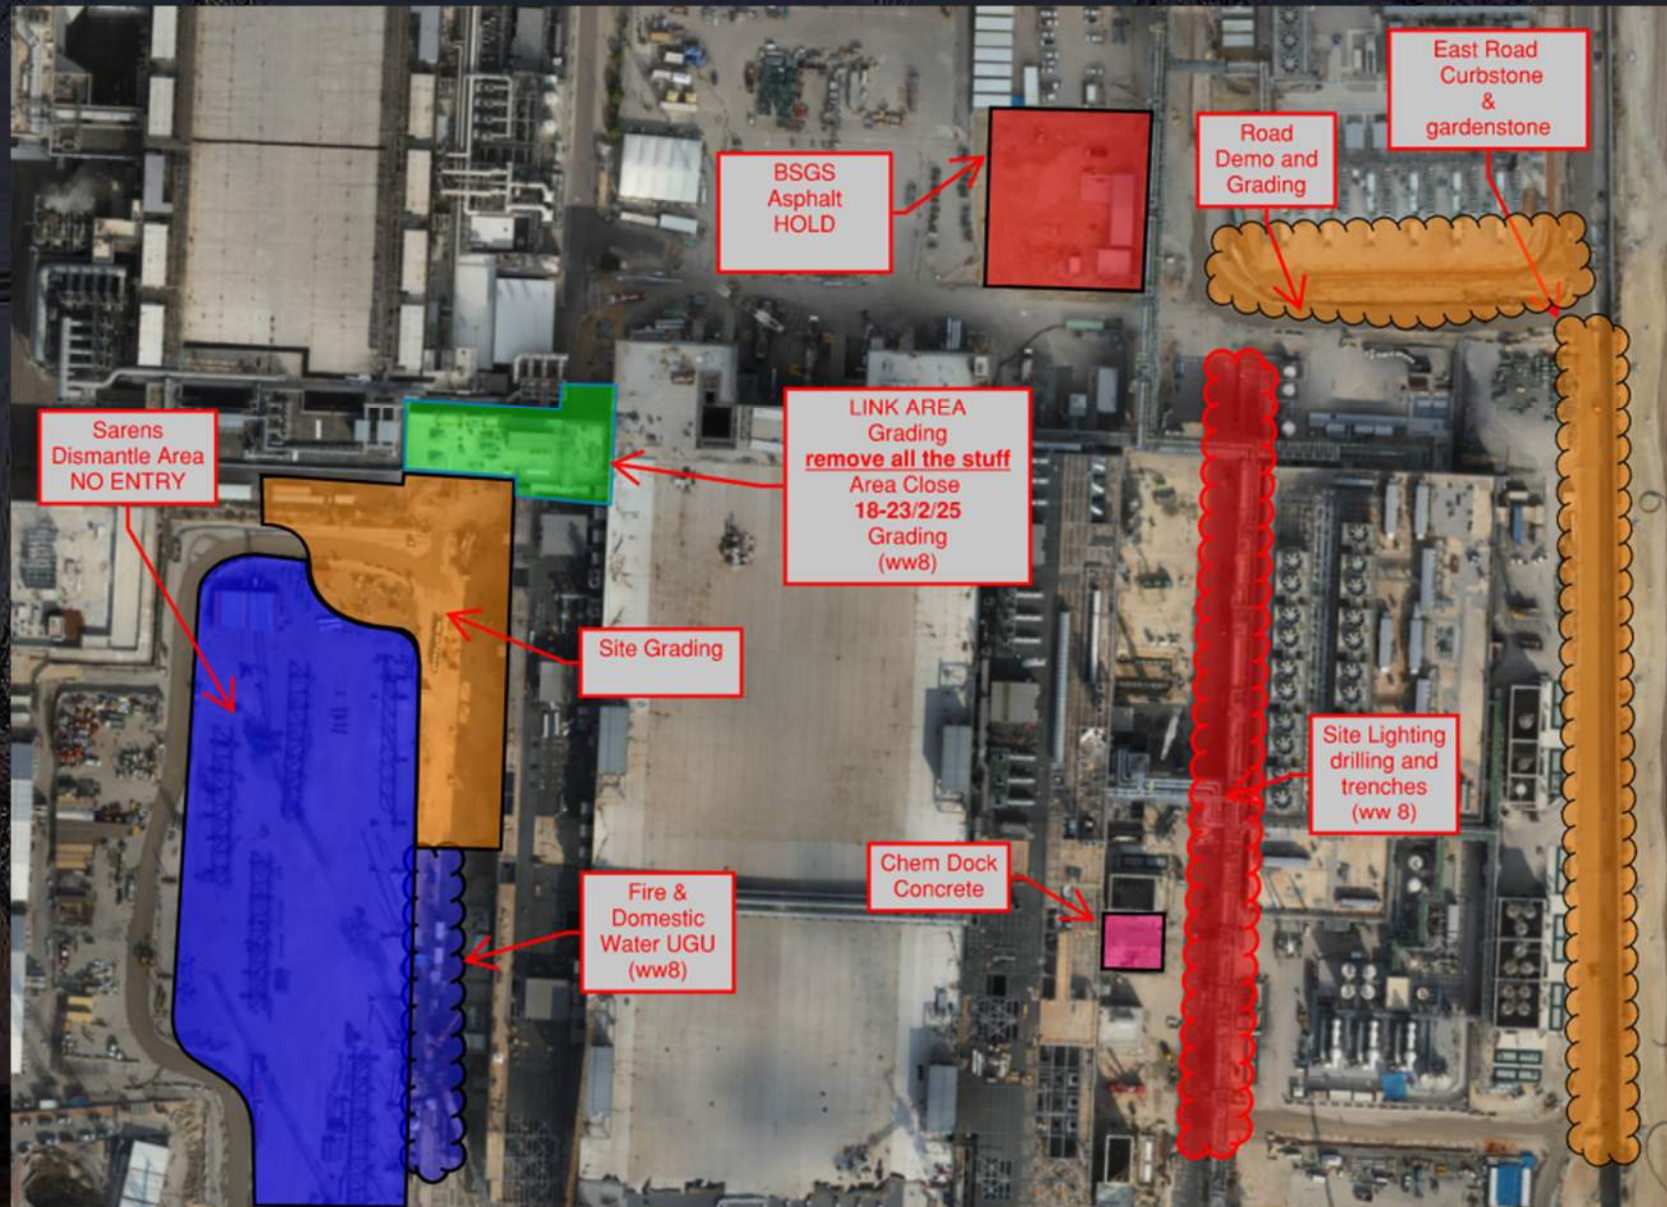



Daily Coordination Meeting


Site Logistics South

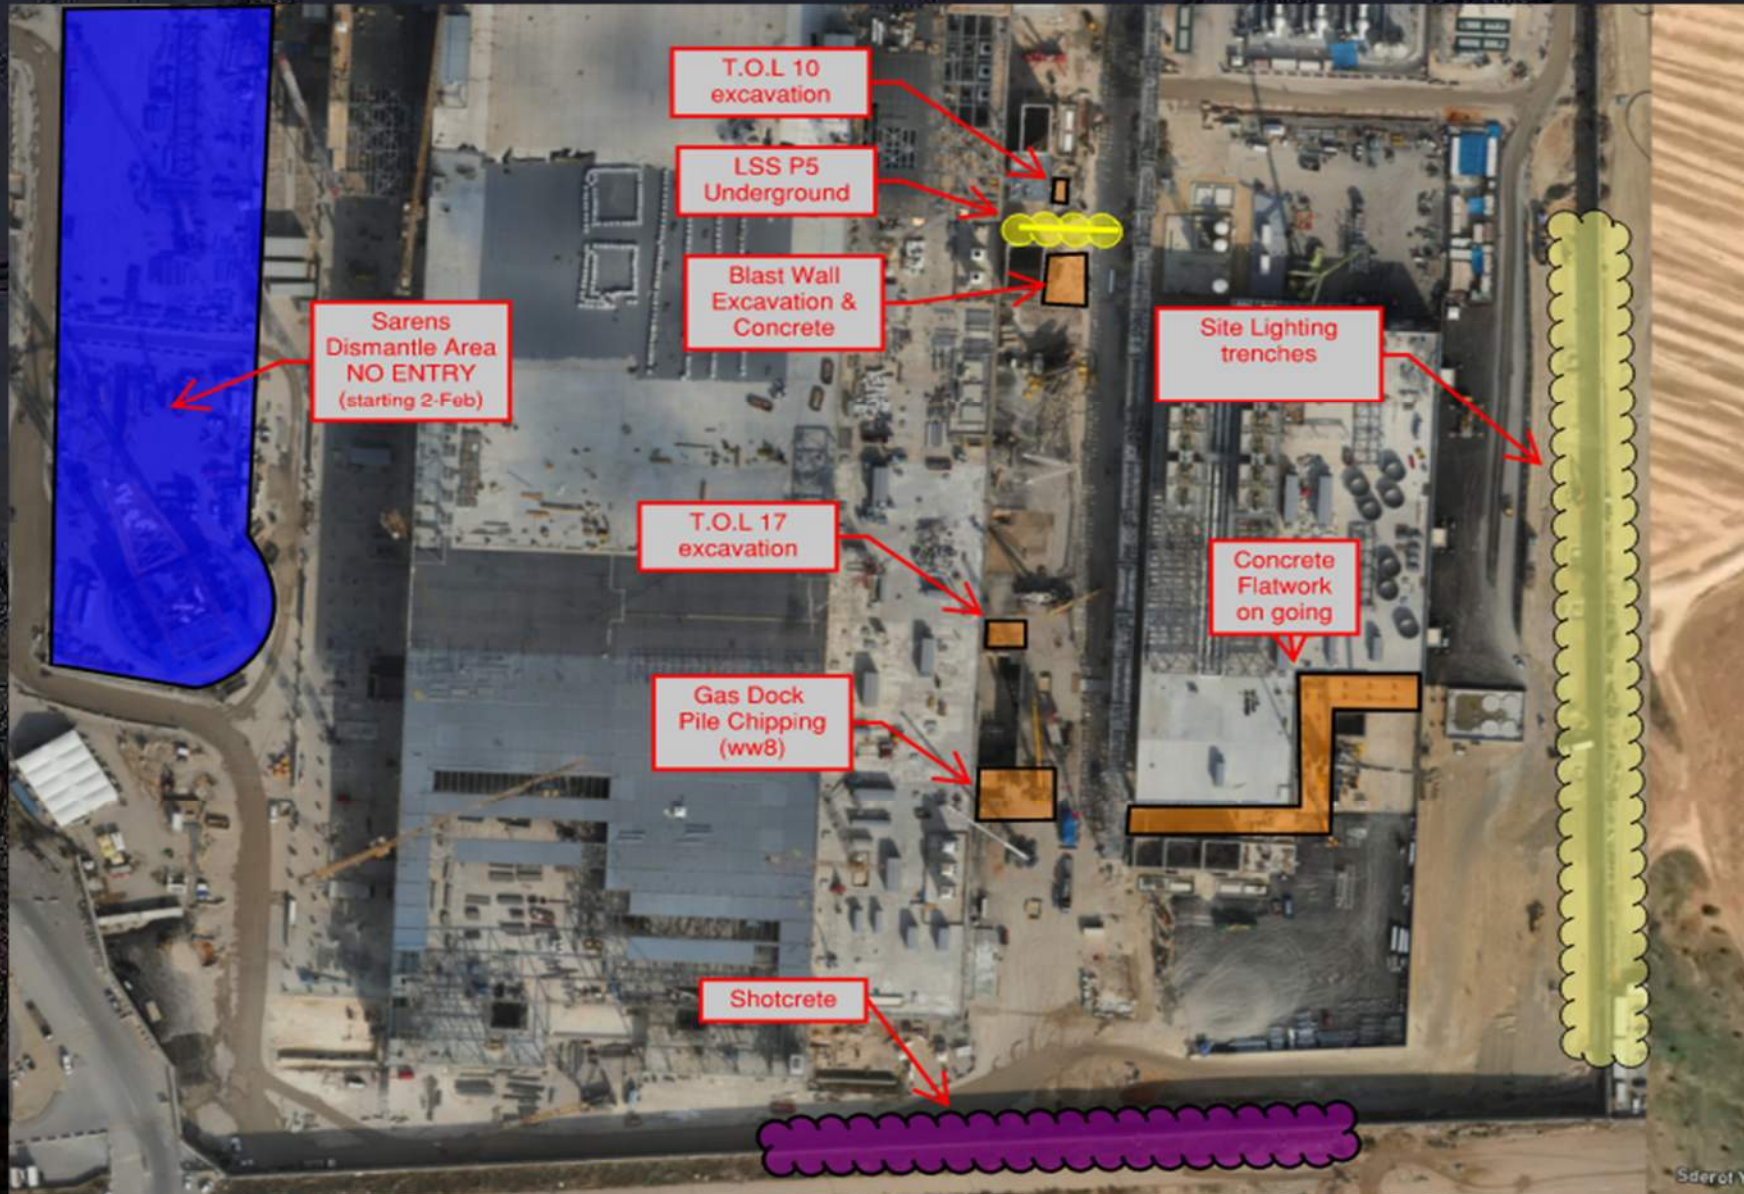

Rigging Plans

Rigging Plan Level Evaluation Form

Please use this flowchart to determine what rigging plans you need for your hoisting activity.

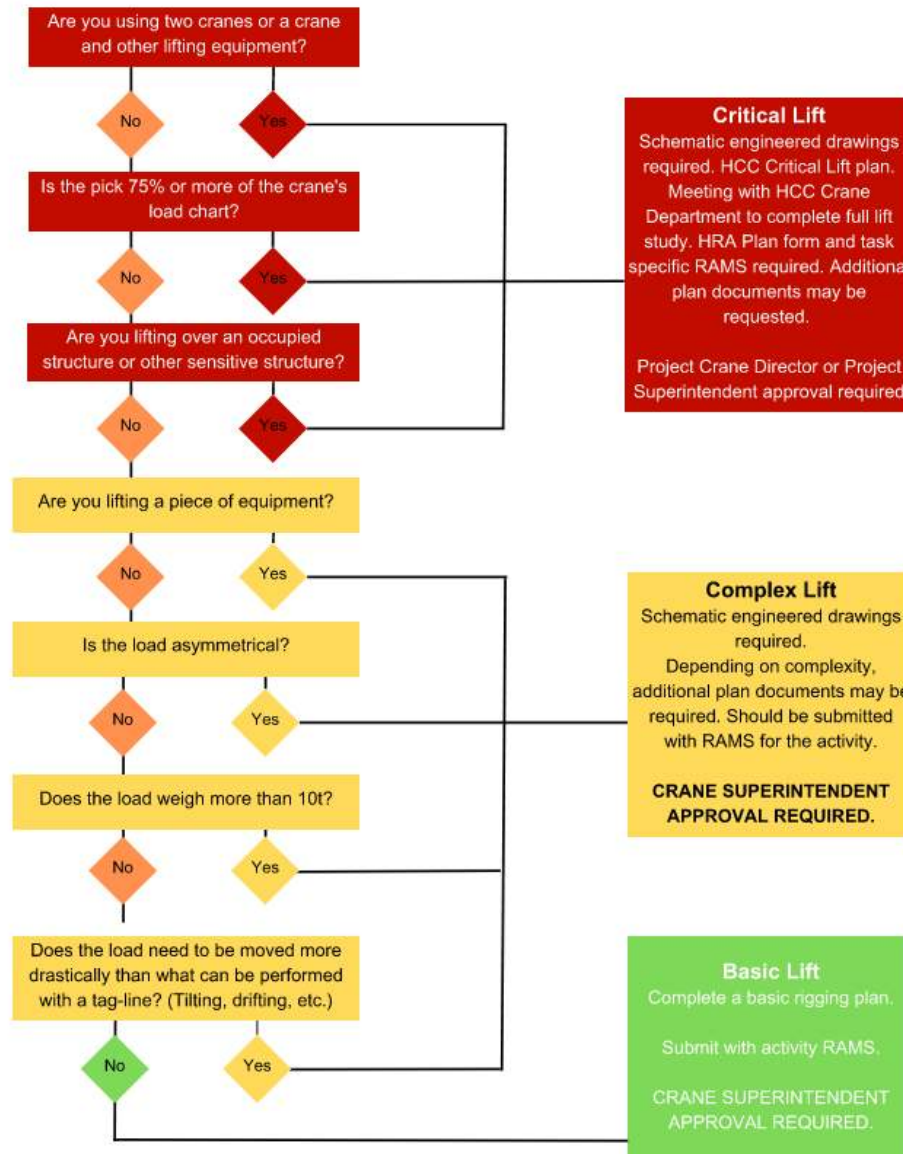

Rigging Plans


BASIC RIGGING PLAN			
Please note: this is not a full lifting plan. This plan only covers from the "hook down"			
Contractor:		Preparer:	
Information on object to be lifted:			
Object to be lifted:		Total weight:	
	Length	Width	Height
Dimensions of object:			
Information on rigging to be used			
	Member 1	Member 2	Member 3
Rigging type (wire rope chokers, endless nylon slings, chains, etc.) to be used:			
Number of rigging members:			
Capacity of each rigging member:			
	Accessory 1	Accessory 2	Accessory 3
Other lifting accessories (shackles, spreader bar, etc.) to be used:			
Number of lifting accessories:			
Capacity of each lifting accessory:			
Total weight of all lifting accessories:			
Information on Location of Lift			
Pick location:			
Set location:			



Rigging Plans

Rigging Diagram

(include the configuration of the rigging, angles of the slings, the attachment points, center of gravity etc. this can be a separate document as well)



Rigging Plans

COMPLEX RIGGING PLAN COVER SHEET			
Please note: this is not a full lifting plan. This plan only covers from the "hook down"			
Contractor:		Preparer:	
Information on object to be lifted:			
Object to be lifted:		Total weight:	
Is this a piece of equipment?		Yes	▼
Is the load asymmetrical?		Yes	▼
Does the load need to be shifted drastically while on the hook?		Yes	▼
Does the load weigh more than 10t?		Yes	▼
Plan Documents Needed:			
Schematic engineered rigging drawings (must detail all lifting accessories and capacities, COG, weights, dimensions, attachment points, etc.)		☐	
Method statement		☐	
Risk assessment		☐	

Rigging Plans

CRITICAL RIGGING PLAN COVER SHEET			
Please note: this is not a full lifting plan. This plan only covers from the "hook down"			
Contractor:		Preparer:	
Information on object to be lifted:			
Object to be lifted:		Total weight:	
Are two cranes, or a crane and other lifting equipment, being used for this lift?		Yes	▼
Is the load more than 75% of the crane's load chart?		Yes	▼
Will it be lifted over an occupied, or otherwise sensitive structure?		Yes	▼
Plan Documents Needed:			
Schematic engineered rigging drawings (must detail all lifting accessories and capacities, COG, weights, dimensions, attachment points, etc.)		☐	
Task specific method statement		☐	
Task specific risk assessment		☐	
HRA Plan form		☐	

HCC/EHS Weekend Work- 14.02.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jeff Bowen – 052-3787746
Gad Yaacov - 052-3784838
Pini Kahlon - 052-7343004
Brian Smith - 052-2181361
Asher Amar - 052-8801316
David Jollands - 052-3961675

CSA CM

Nikol – Loboda - 052-3124965
Ben Tauar - 052-3173040
David McBride - 052-5379828
Shir A
Hadar S

MEP

Cx

Cranes

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 14.02.2025

FAB

Utility level/ SUT

Subfab

- Pach Taas
 - Wall Penetration
 - Tomer: 0507670585
 - Ofik: 0507838486
- Afcon E
 - All over SF
 - Raz: 0546838626
- MEGASON
 - MOD 2,LSS Rooms
 - Israel: 0526869393
- SELA
 - 2E MARS
 - Yuvel: 0502649246
- Afcon-Telecom
 - 5E,5W
 - Anish: 0559537332
- Elram
 - TTNE
 - Eliezer: 0544236899
- Lesico
 - 17 Line
 - Gabriel 0549892929

Clean Room

- Talad – 25 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Elad 0546654473)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Roni 0542496363, Elisha 0587963704)
- Talent solution 8 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Super Yosi 0526557130)
- W&W 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Sig – 17 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Codrin 0546594273, EHS Ovidiu 0546993648)

Subcontractor Weekend Work- 14.02.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- Lesico – H2 Vent/SUT East Area Way Rack
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109
- Combe UPW – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- HSAI – Chem Dock Retaining Wall
 - Foreman – Dave – 052-4121028
 - Safety – Hiam
- SK Engineering – 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112

WJG

Pach Taas

Foreman: Tomer Sasi – 0507670585

Safety: Eran Tzadok - 0547706233

Afcon

Foreman: Montu - 0559116973

Safety: Stiven – 0552742935

Chemo Aharon

Foreman: Shai Adi – 0524801180

Safety: Erez Megidish - 0549716840

Subcontractor Weekend Work- 14.02.2025

CUB

Chemo Aharon CUB 2:
Dudu - 0509808846
Alberto - 0508573970

SKE CUB 2:
Mario - 0548991051
Marzuk - 0548830263

Sami Najami CUB 2:
Husein - 052-6917461
Aviram - 050-9059920

HSAI CUB 1&2:
Sergey - 0552728807
Haim - 054-8038554

Meptagon I&C CUB 1:
Sergey - 0537981592
Itzik - 0587441140

Pach Taas CUB 1 Roof:
Tomer - 050-767-0585
Eran - 054-7706233

Trestle

SNJ:

Piping:
17 People
Steal:
15 People

Superintendent
Mahmoud Ayub 054-4915889

Safety:
Aviram Shriki / 050-9059920

Site

- D.A. - shotcrete south wall
- Olizki - Cub 1 east, north,
- Afkon - BGY

Daily Coordination Meeting



14:00 Sign In
