


Daily Coordination Meeting

General Topics:


- Winds this weekend - secure material/equipment
- Vehicle passes - pick up your passes from safety trailer #12 by end of day today
- Weekend work



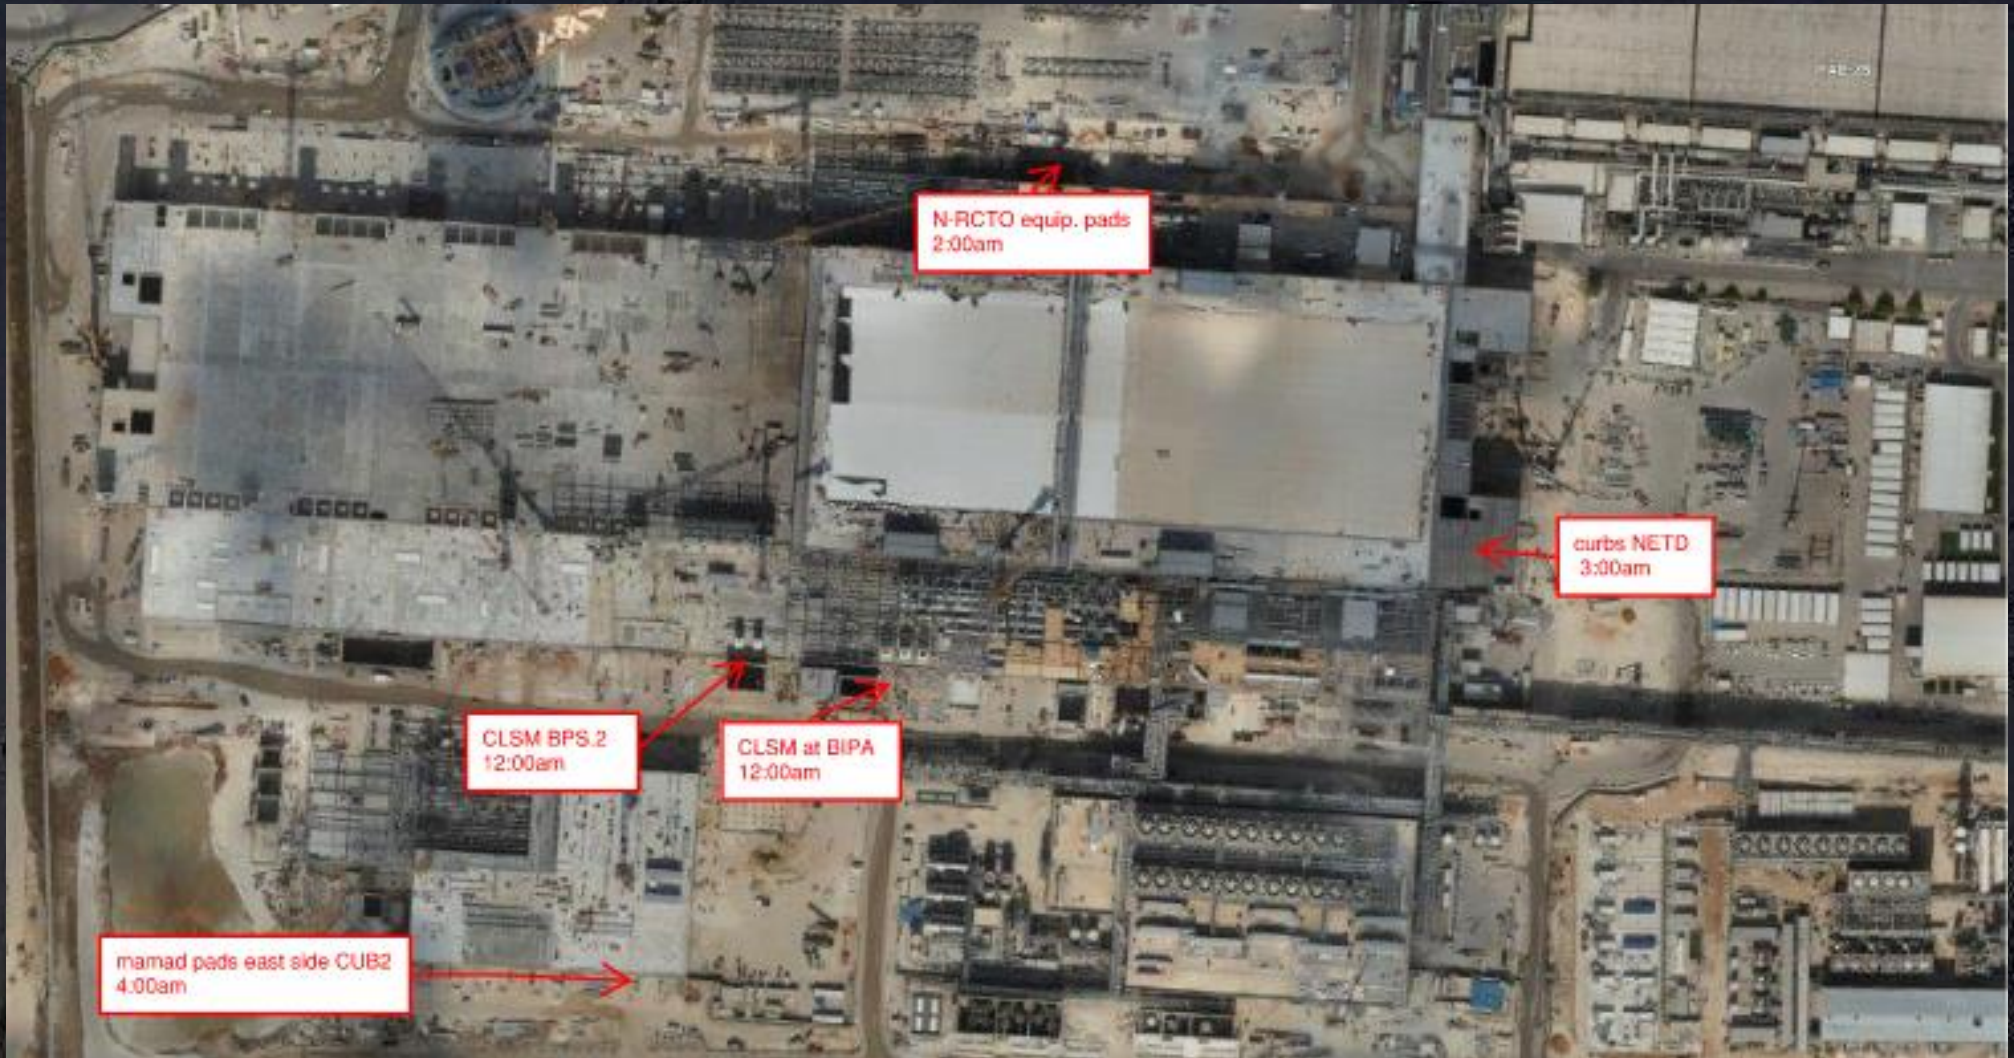

Concrete pours for Sunday morning. Please have the gates open at 11:00pm on the 27th for the guys and pump to get set up for the pour.

UTILITY LEVEL MOD1

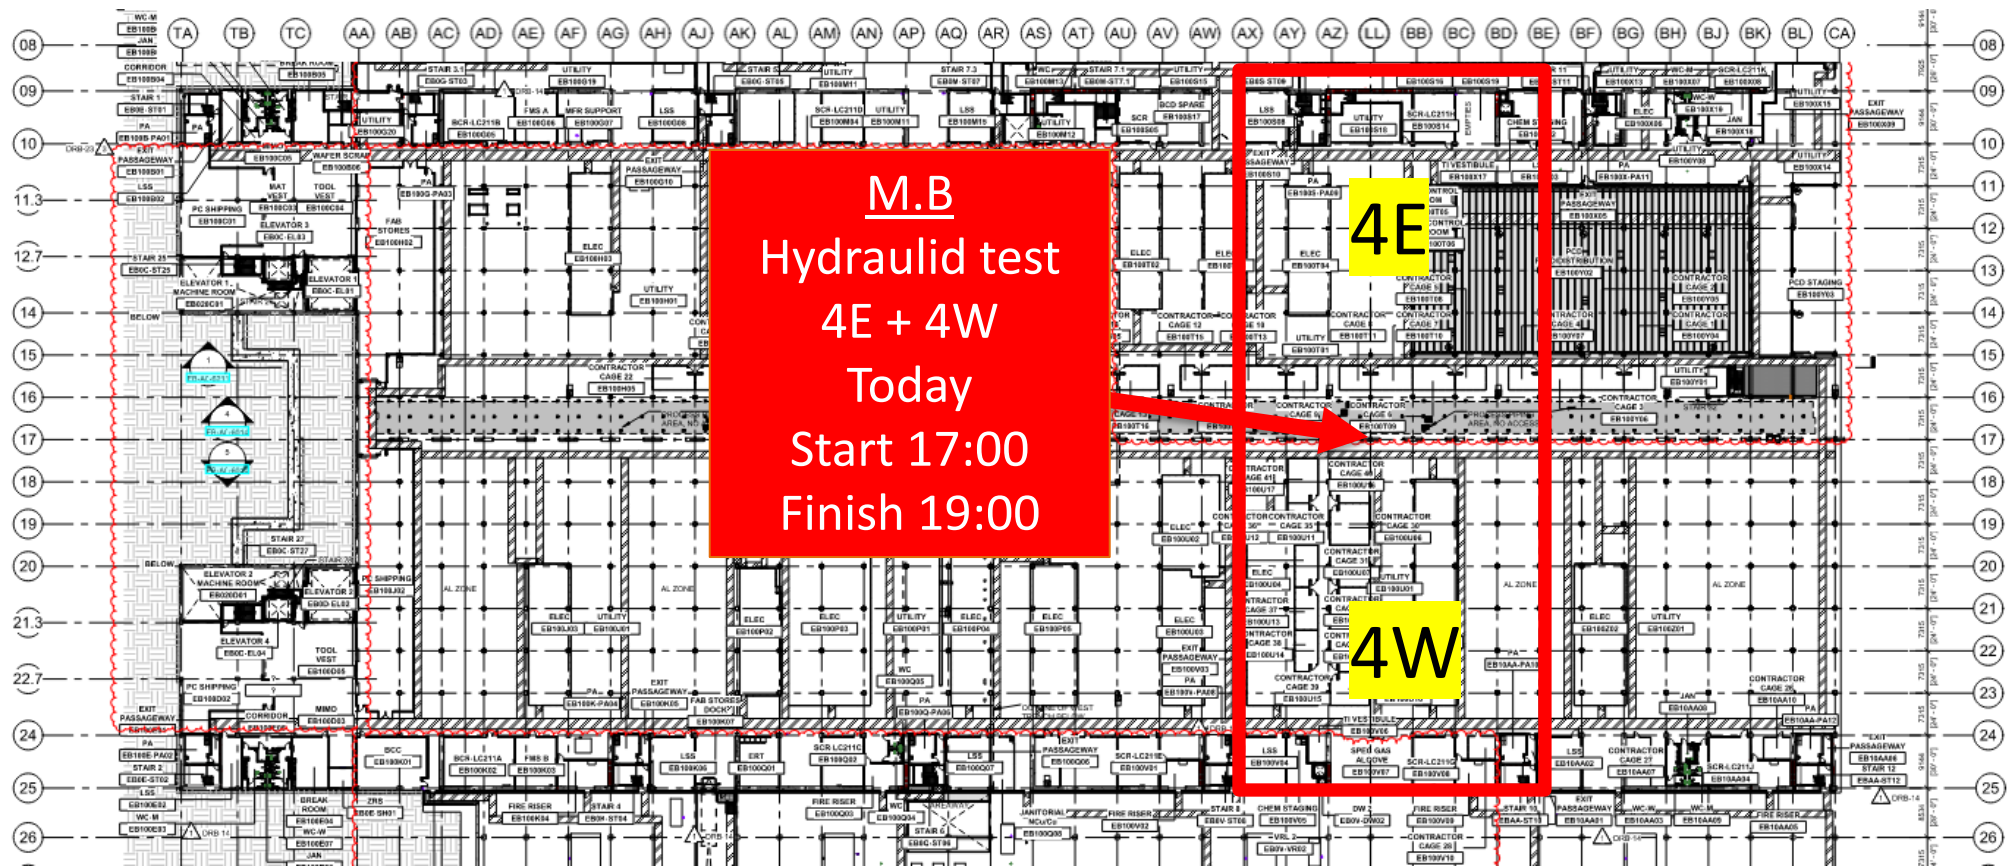




MEPTAGON
9W Bridge strut install
8E Start 7/30

Malhimim
8E 10W
Sprinklers install




SUT 38.1 LEVEL

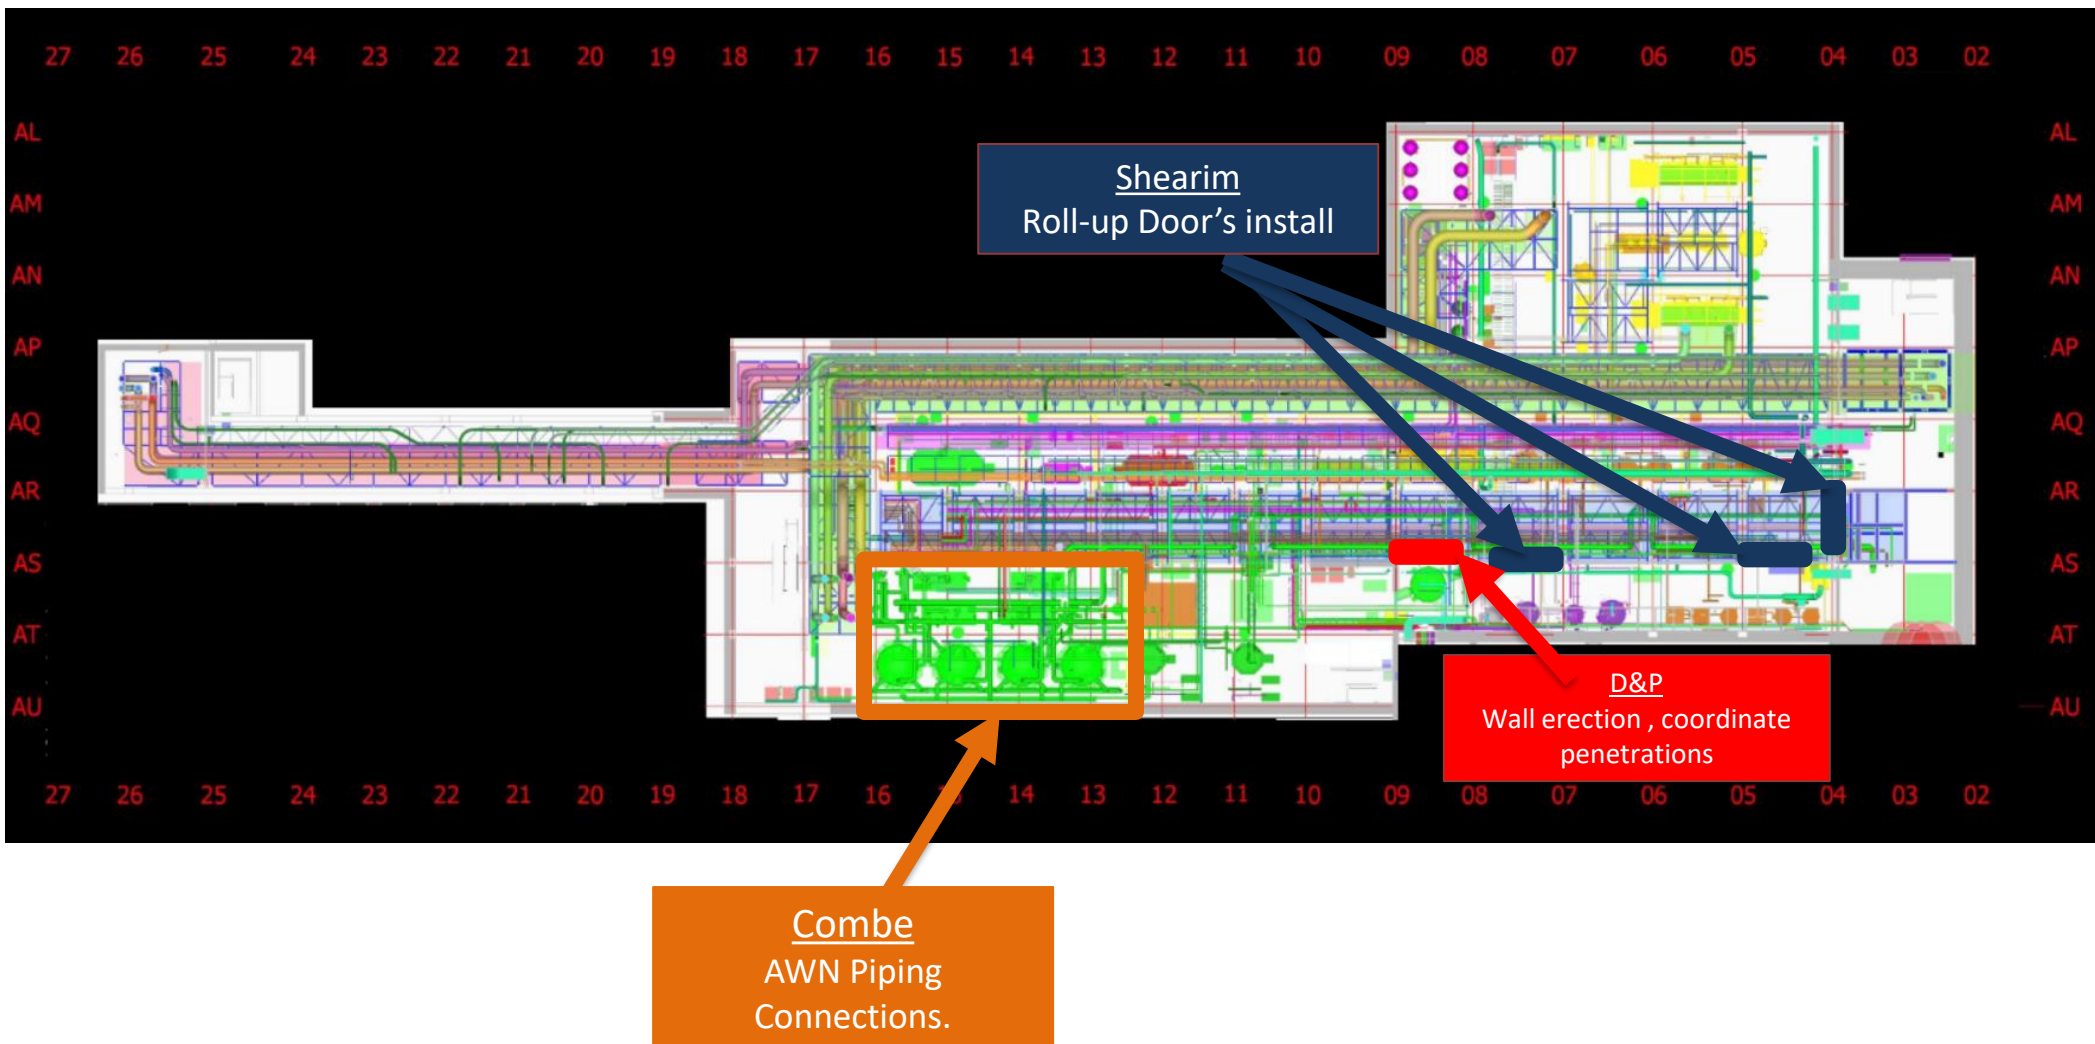





SUT 38.2 LEVEL

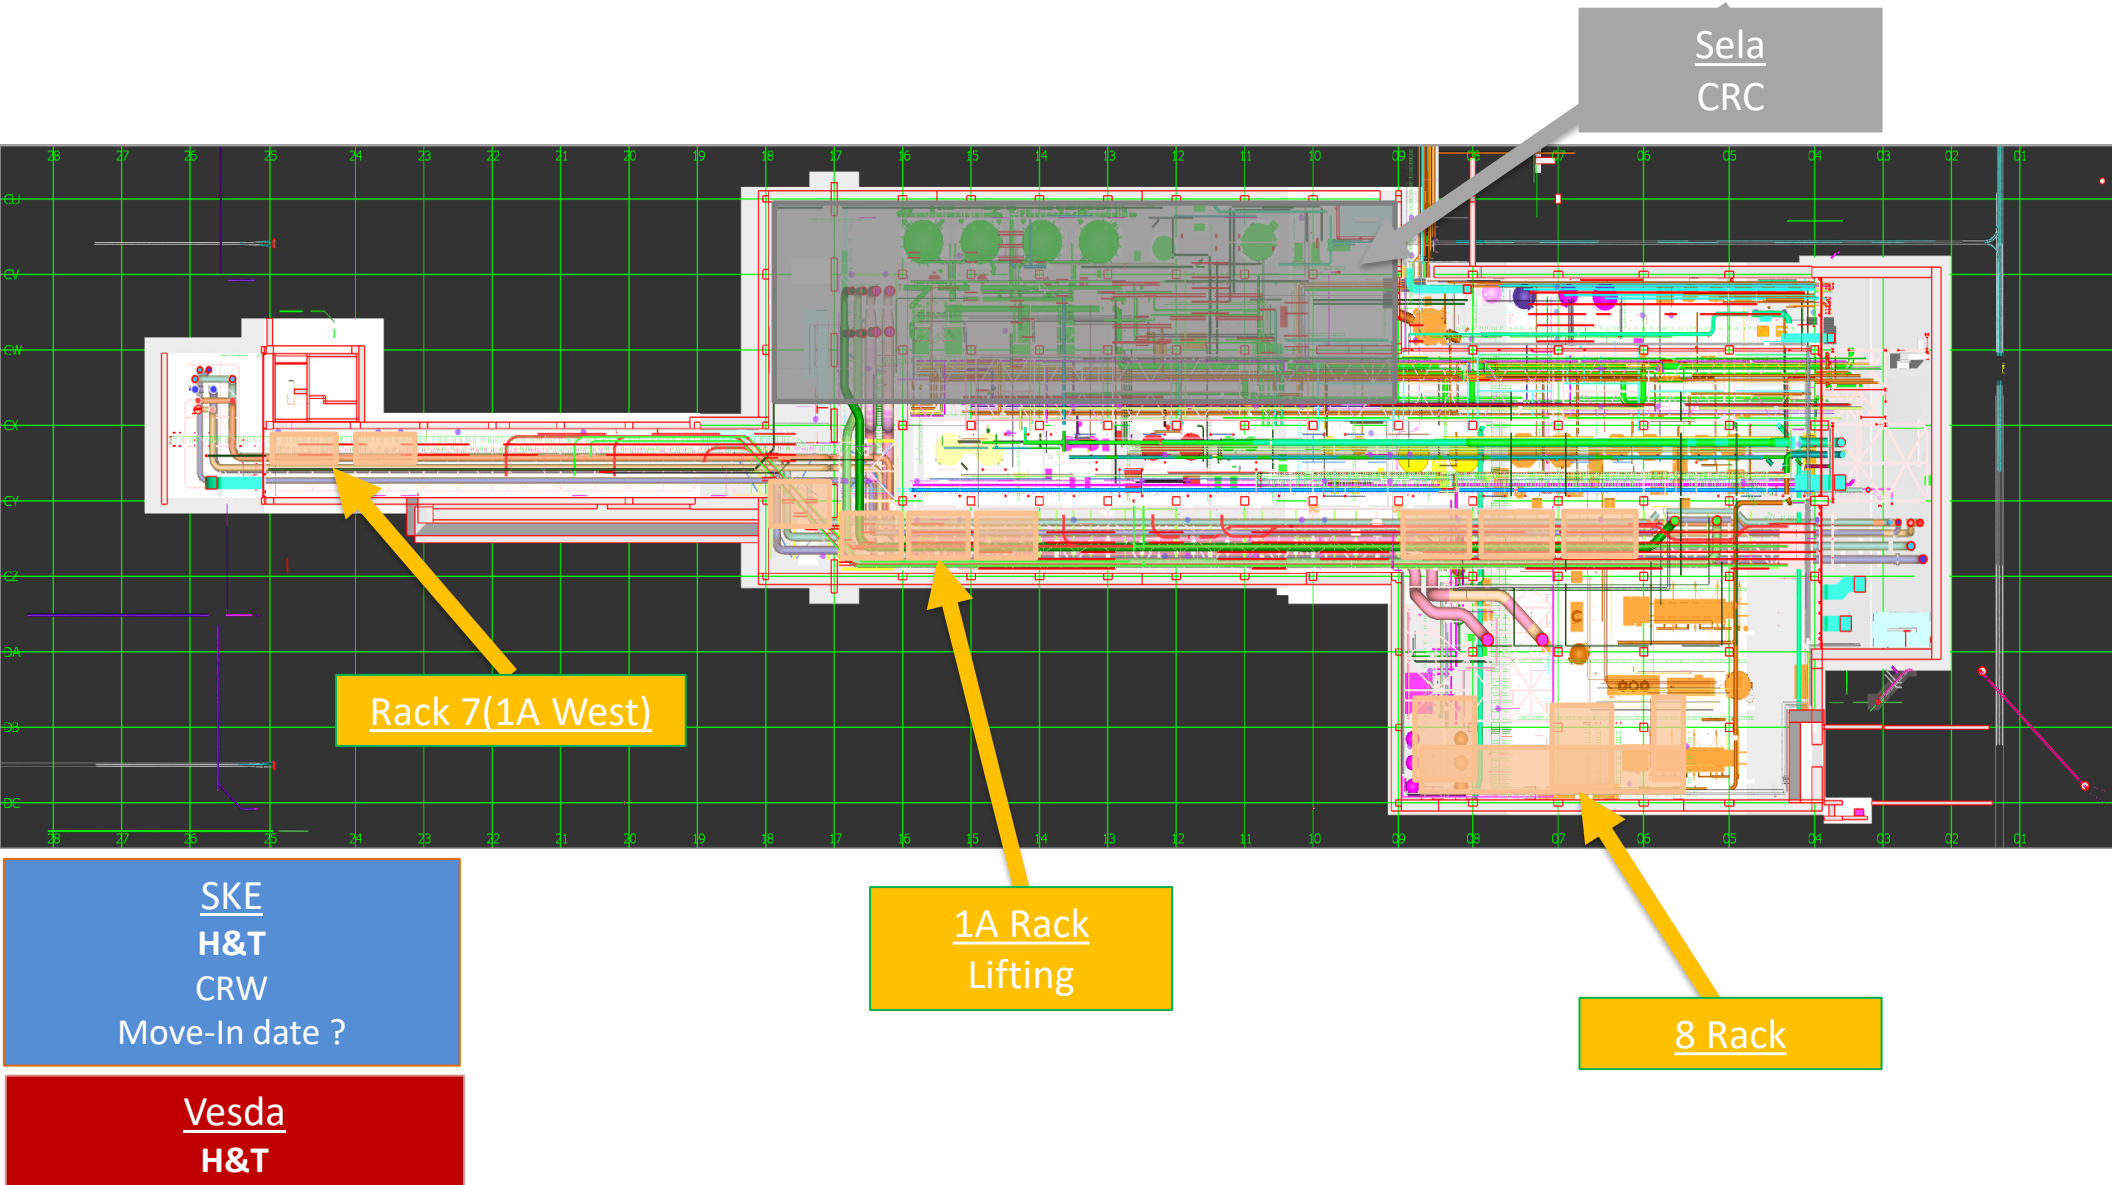


SUBFAB BUILDOUT MOD 1

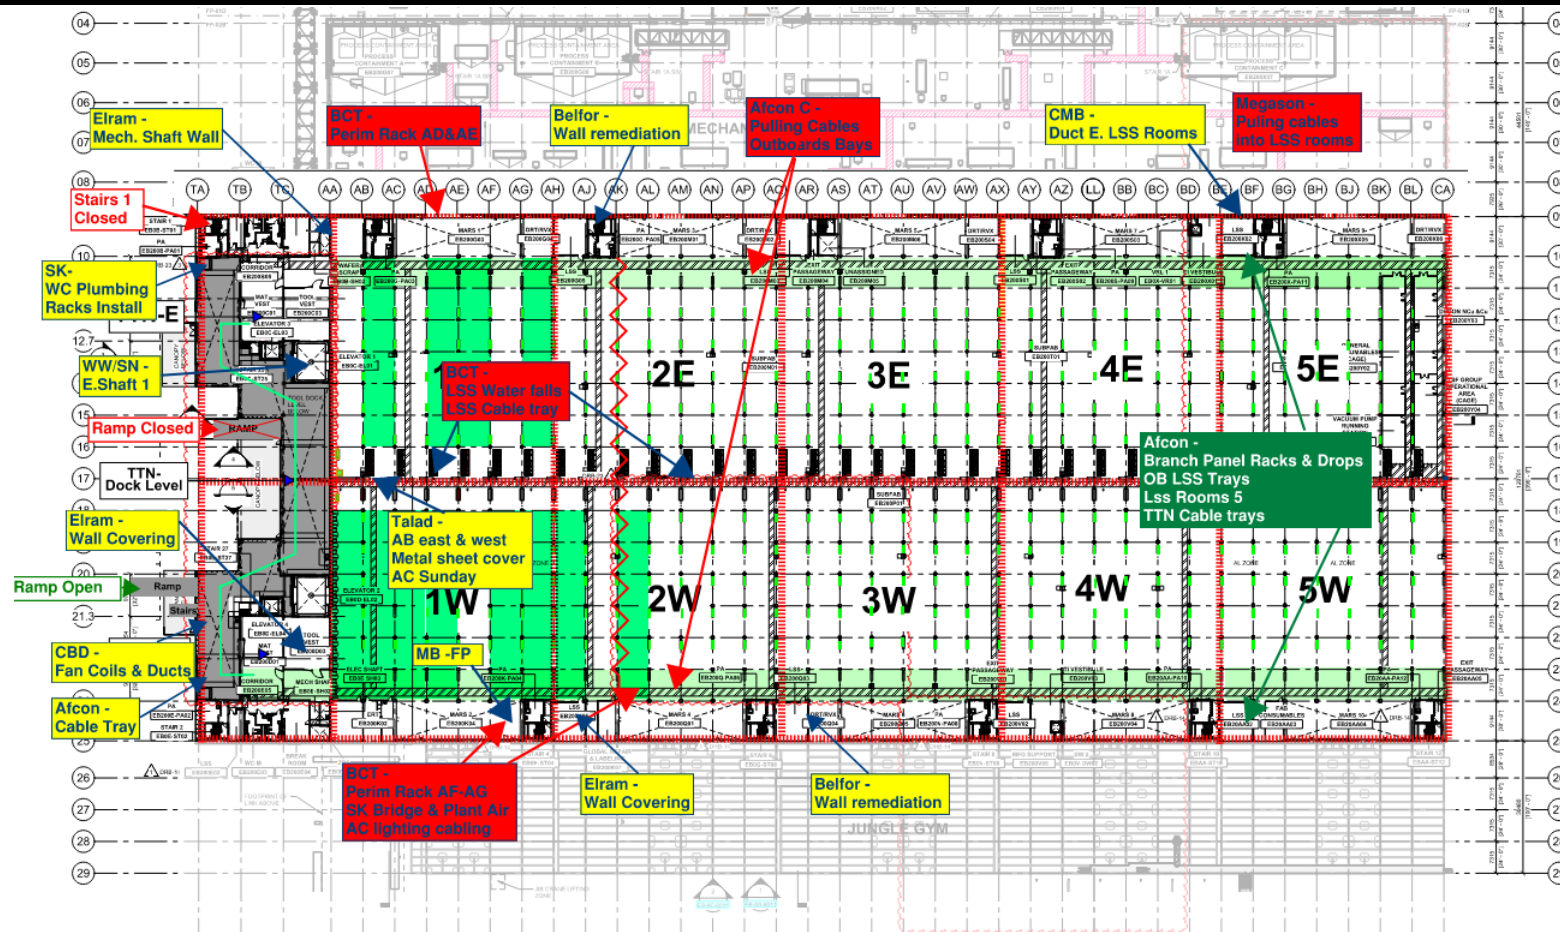


GBD - 3FK Platform-Jul 23 (Swing)
Tzur Esh - Steel paint Jul 24 (Day)
Pach Ta'as - Coils set Jul 25 (Swing)

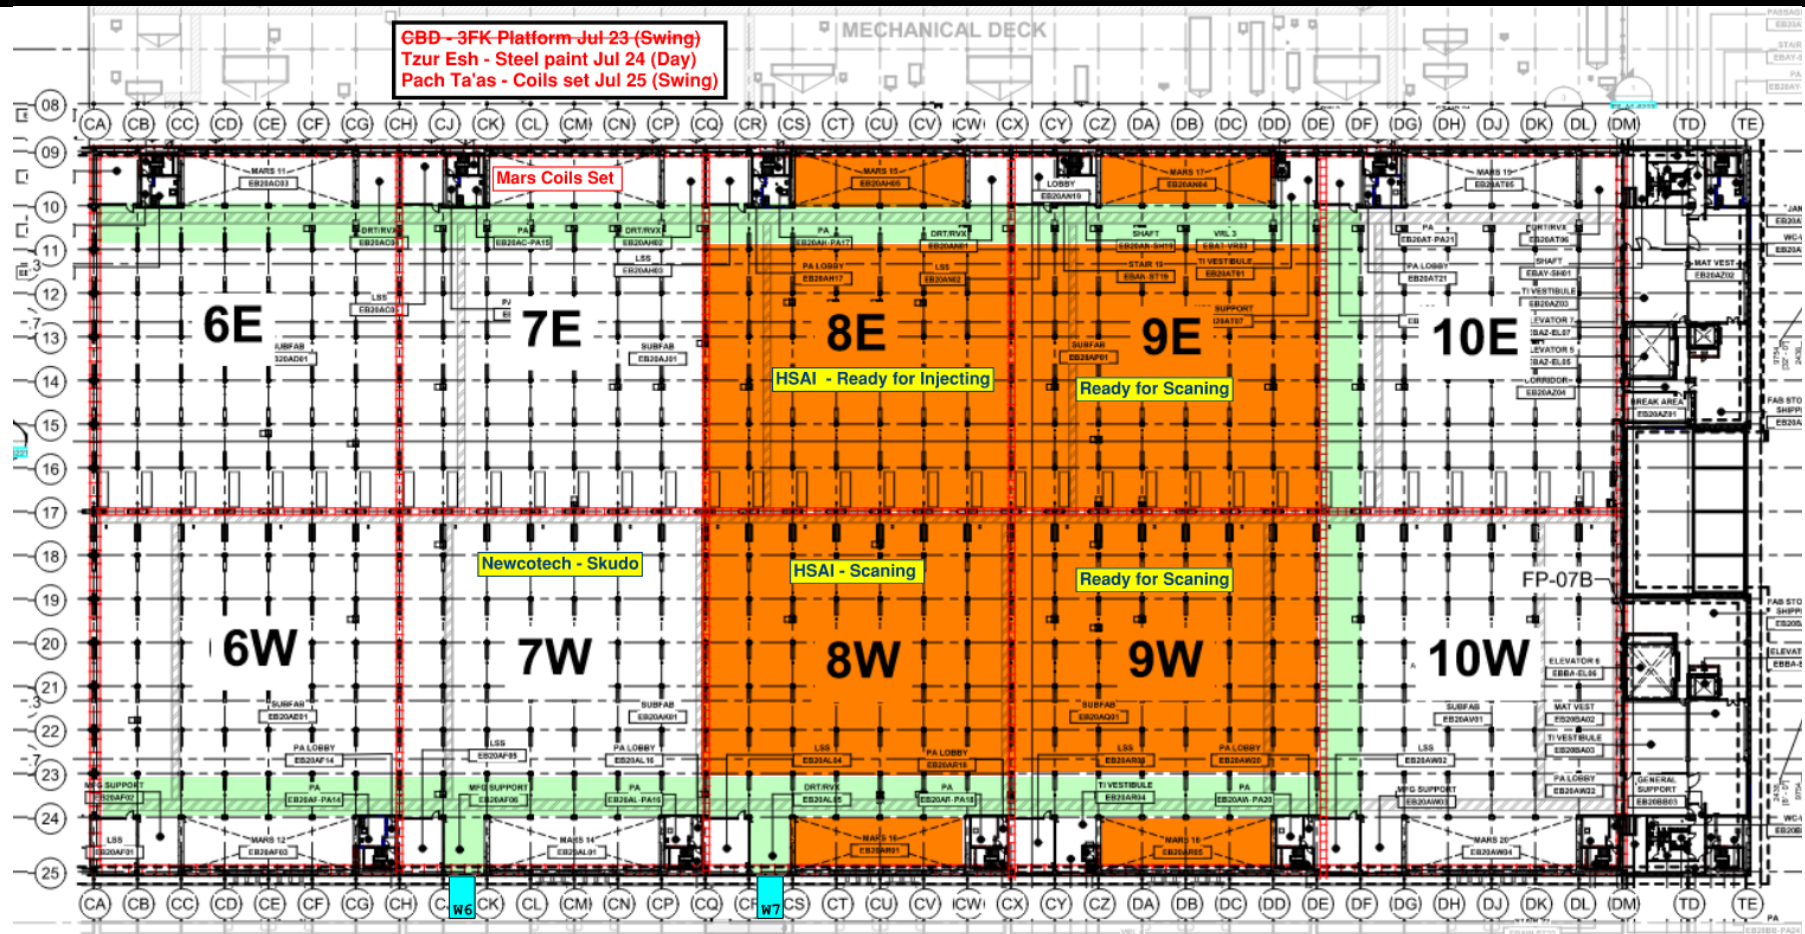

SUBFAB BUILDOUT MOD 1

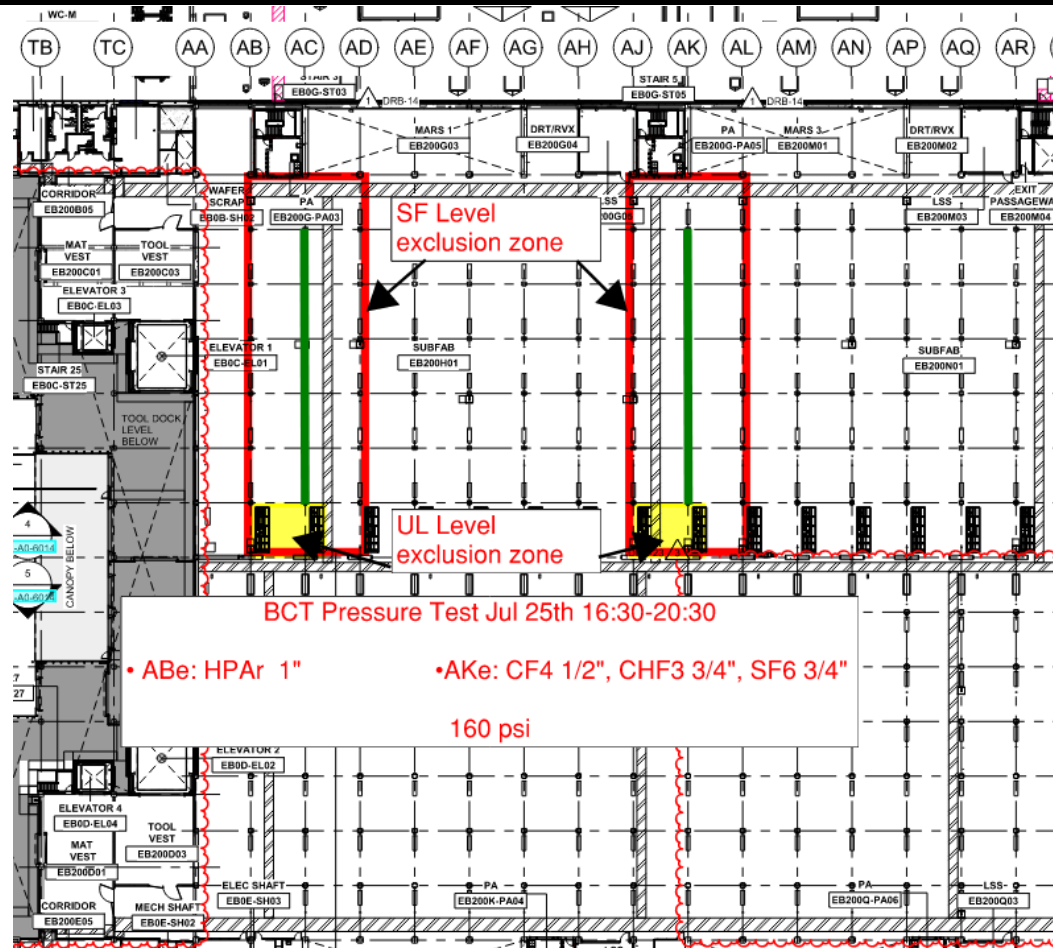



- CR level:**
- Afcon** - Cable trays, modules and stickers 1W, 2E, 2W
 - MB** - 1E drops, 1W drops. 2E-2W IFF approved
 - Elram** - 10, 24 columns fix/wrap.
9,25 line columns wrapping
 - Meplagon** - Zero tolerance pipes 5E-5W. I&C preparations
 - D&P** - Ceiling rods 1E, 5E blades install.
 - Tzur-esh** - 24-25 lines. 4E-4W
 - HYG** - 1W Litho crane plates install, 5W Litho crane steel
 - PT** - Duct prep for test AA-AH east
 - Talad** - Seismic cables 1W.


Belfore - 1W 25 line QC papers
1E 9 Line Ongoing


NTTE/W

W/W/SN - west side
welding tabs and
replacing beams
Elram - East/West floor
done QA/QC
SK - east side pipes
needs to be completed
HYG - East to finish steel.
West receiving material



Link
RP - Fire proofing
D&P - Bolts torque

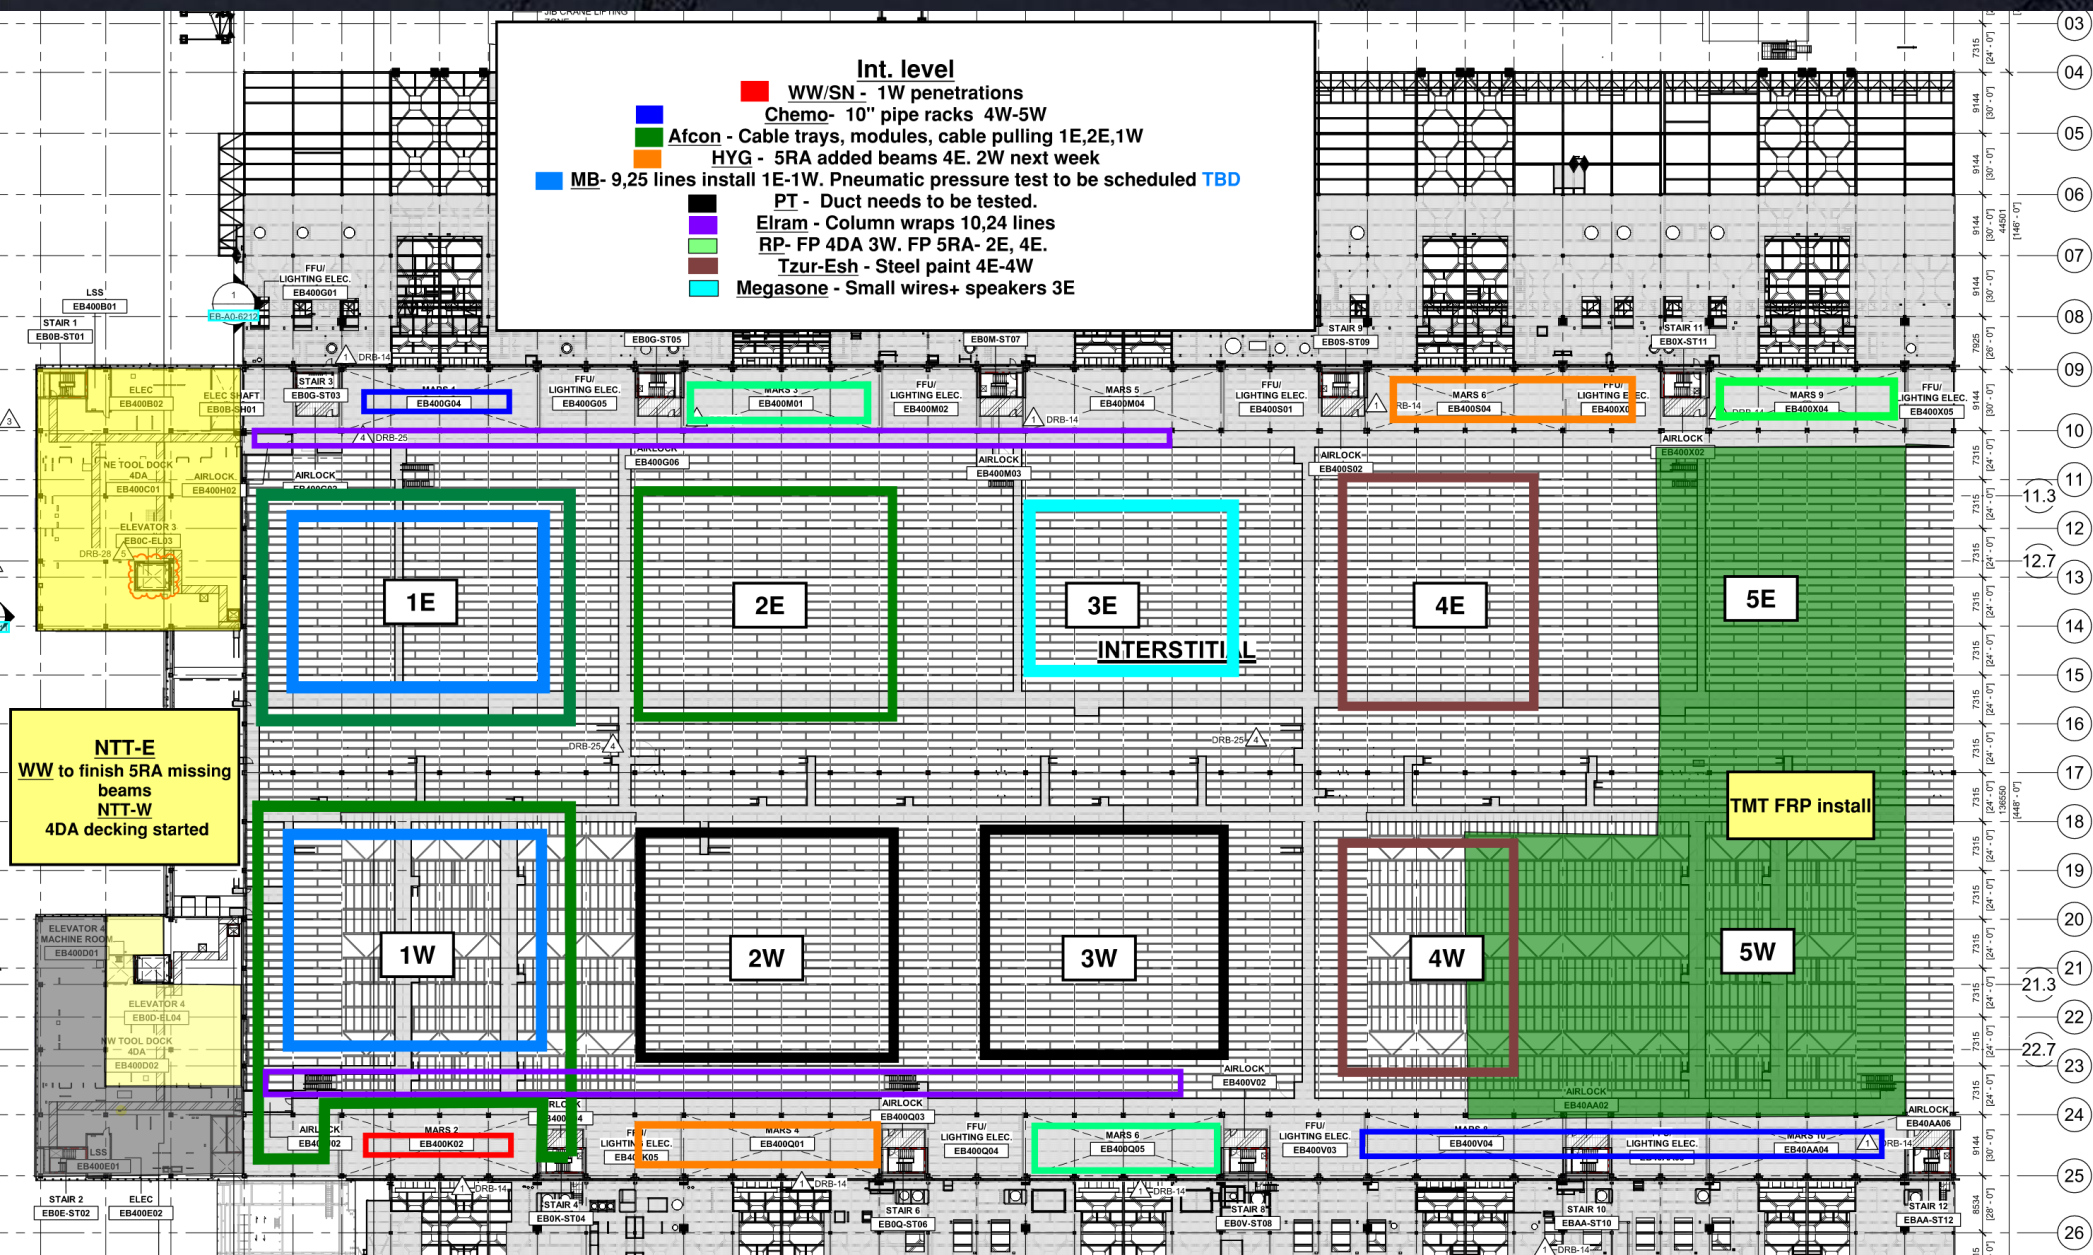

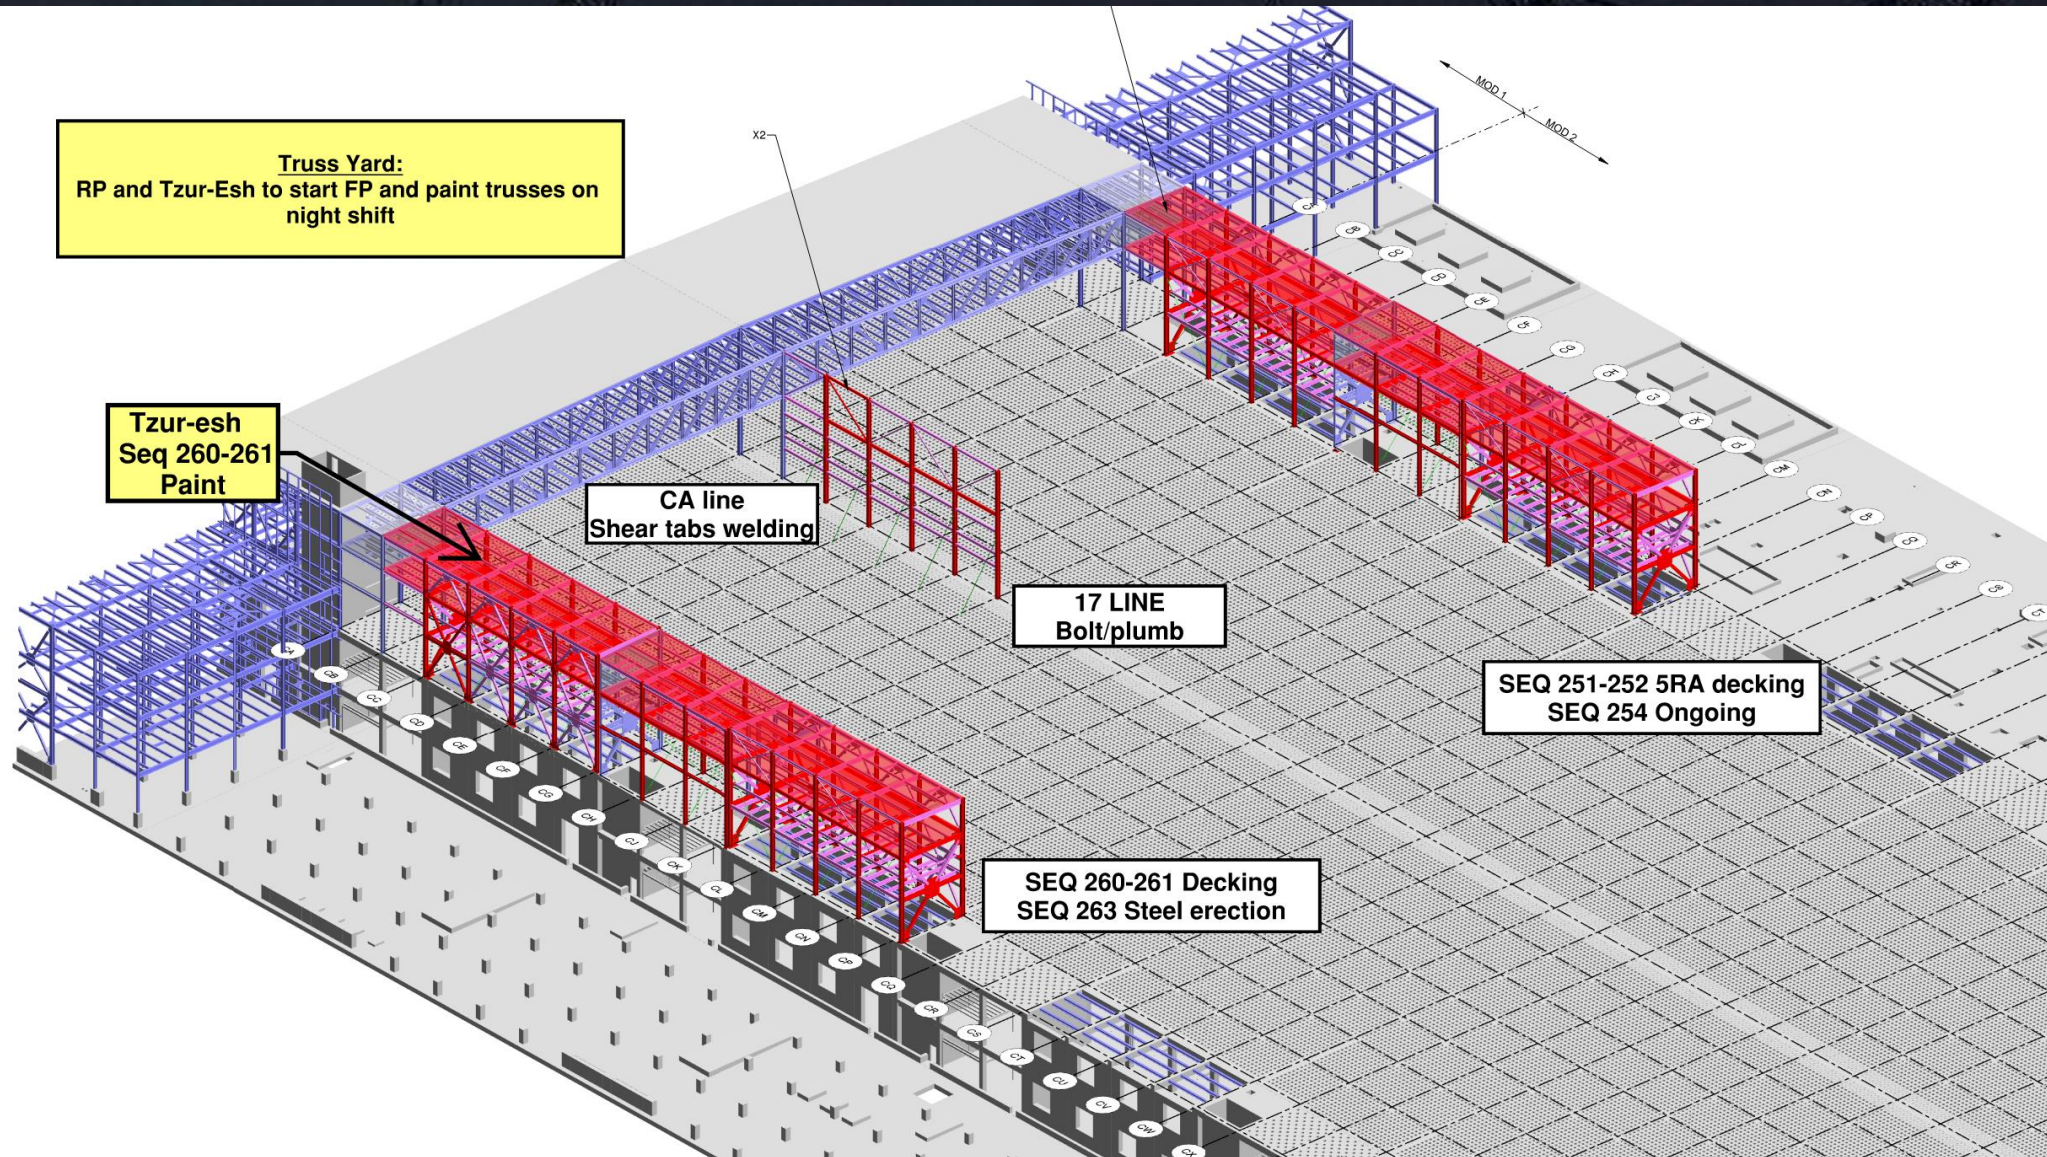

Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift


Tzur-esh
Seq 260-261
Paint


CA line
Shear tabs welding


17 LINE
Bolt/plumb


SEQ 251-252 5RA decking
SEQ 254 Ongoing

SEQ 260-261 Decking
SEQ 263 Steel erection

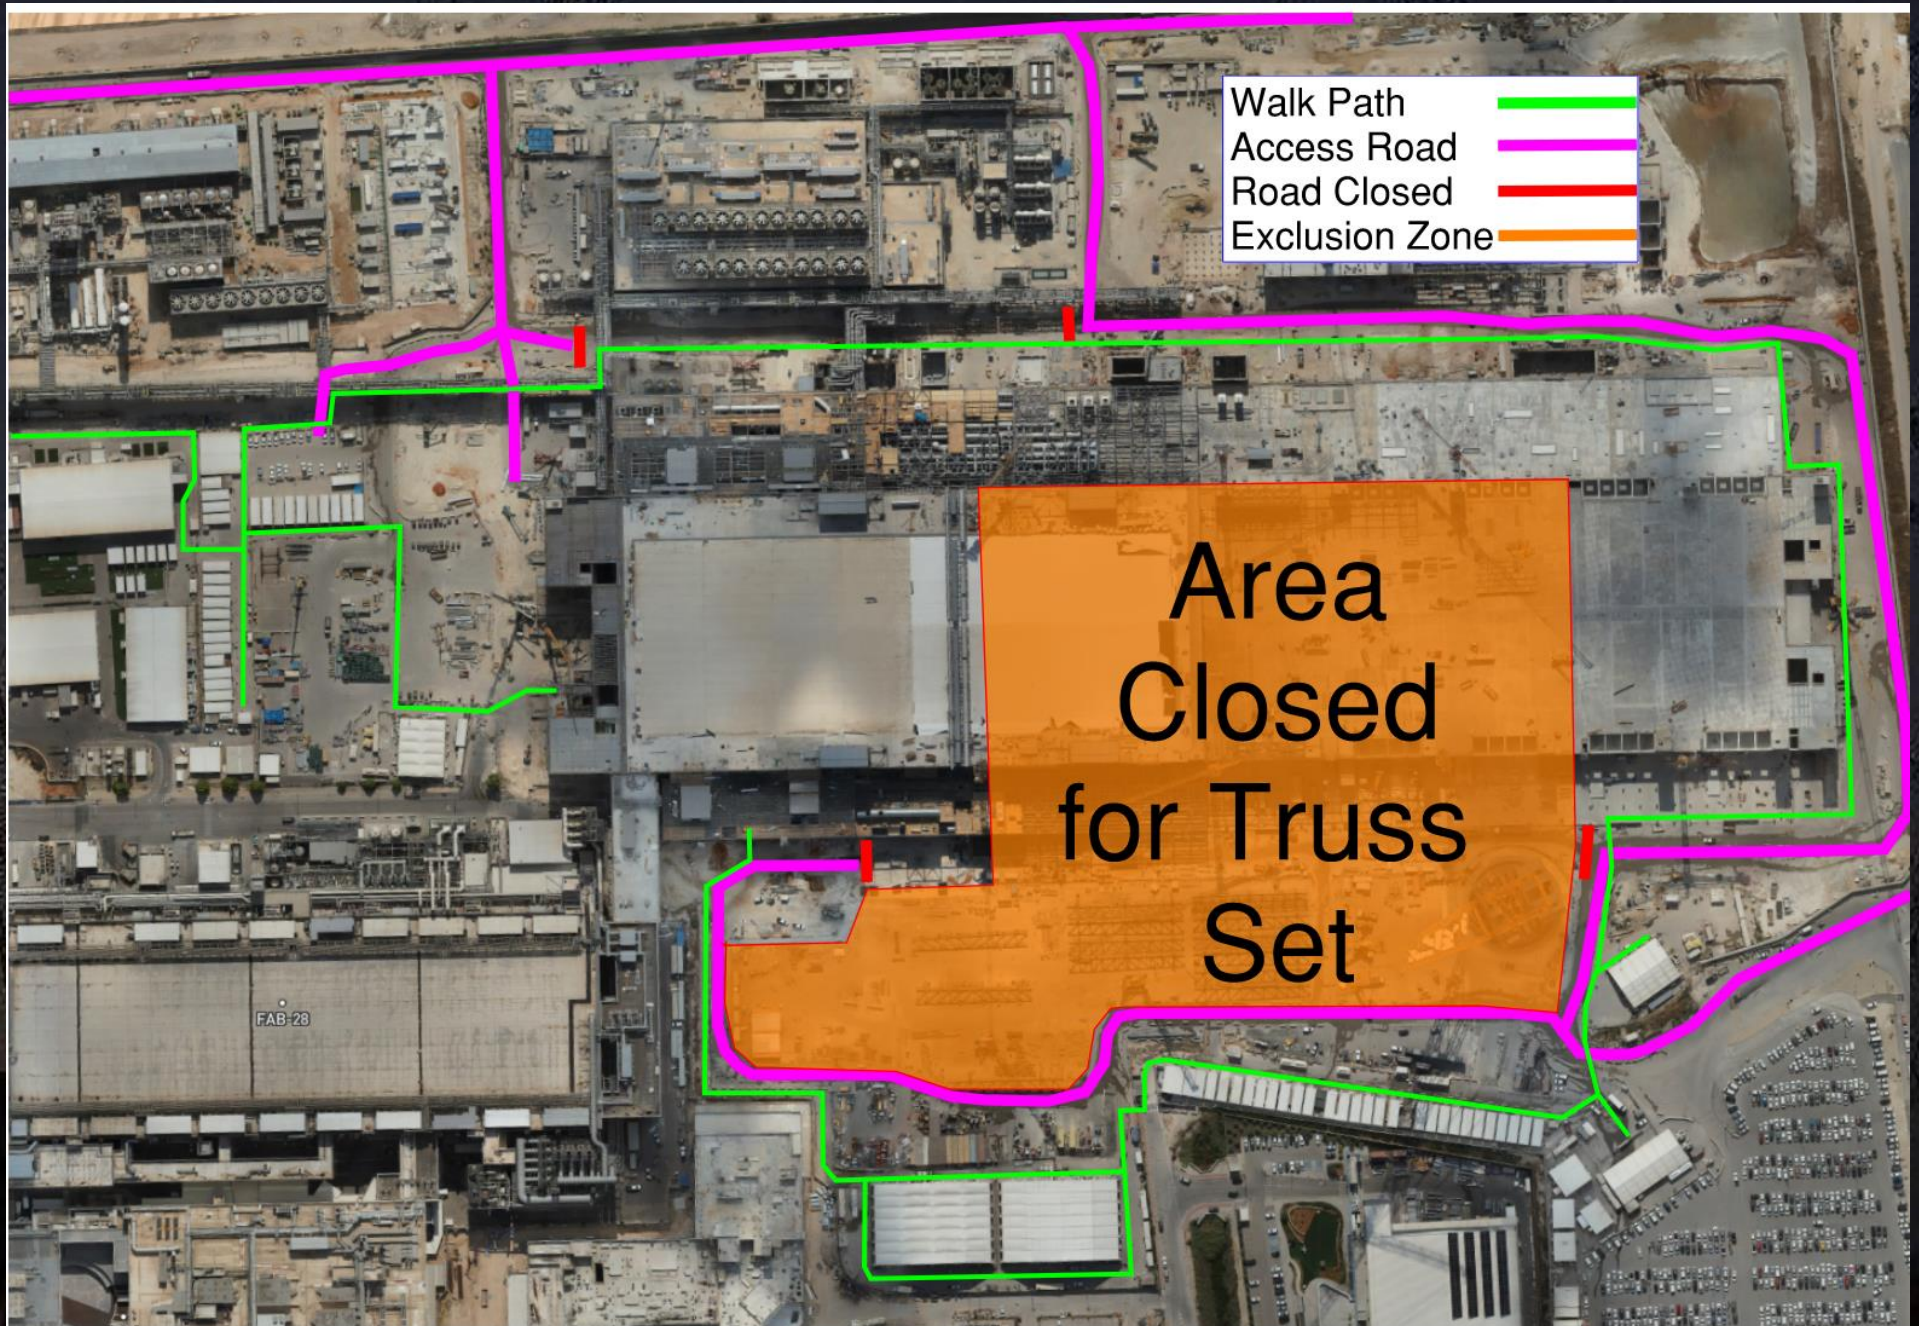

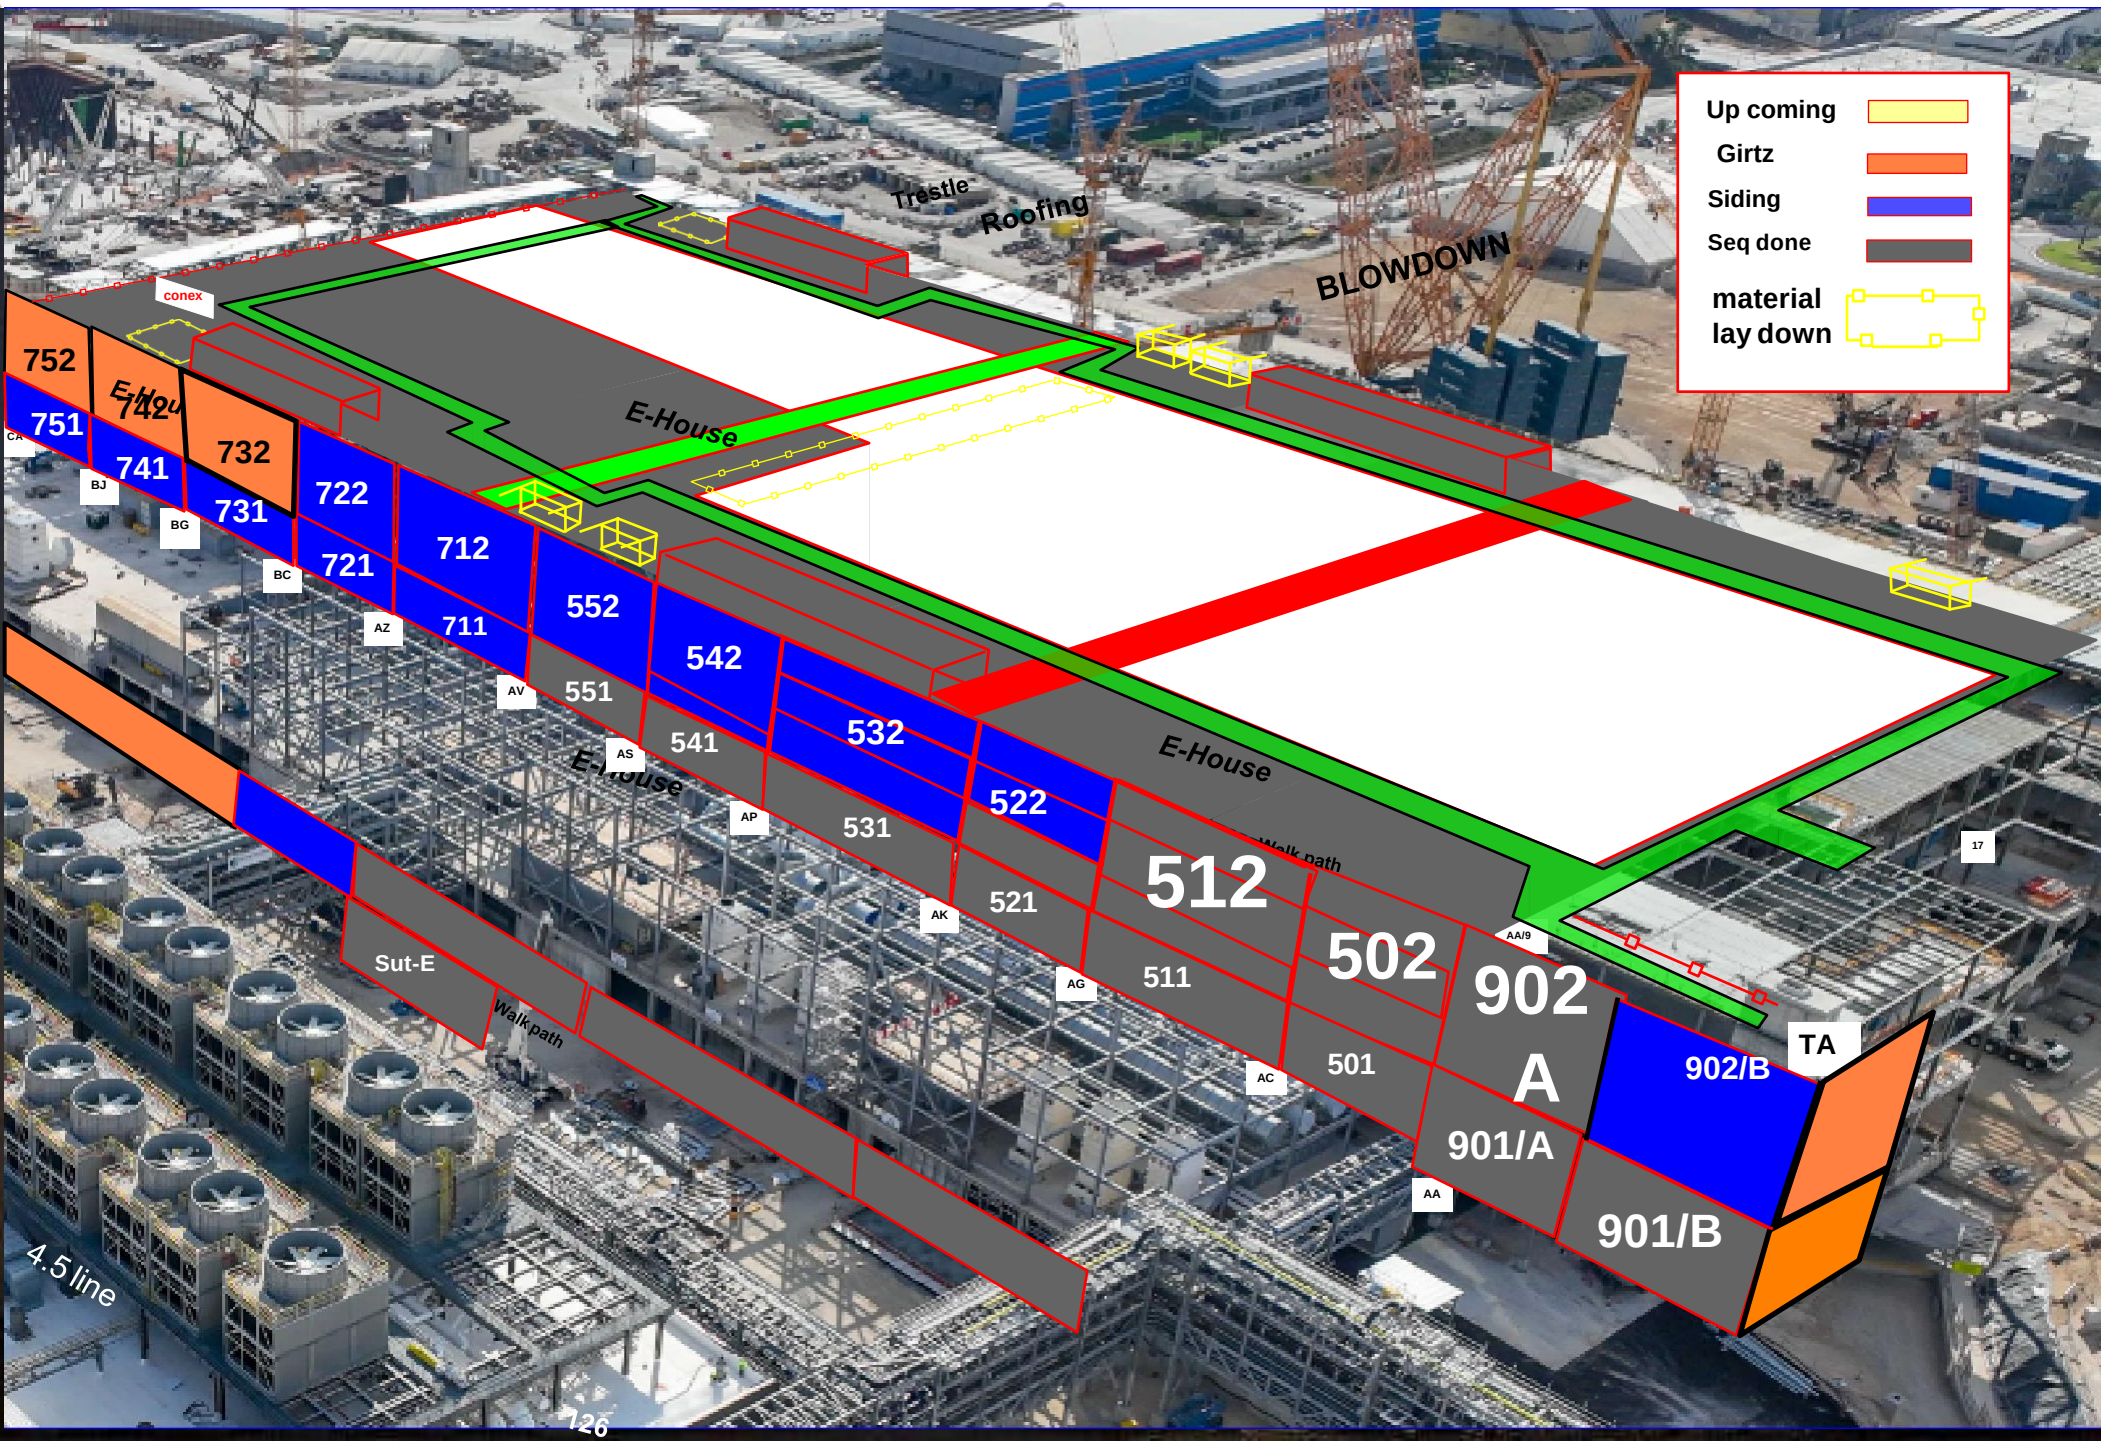

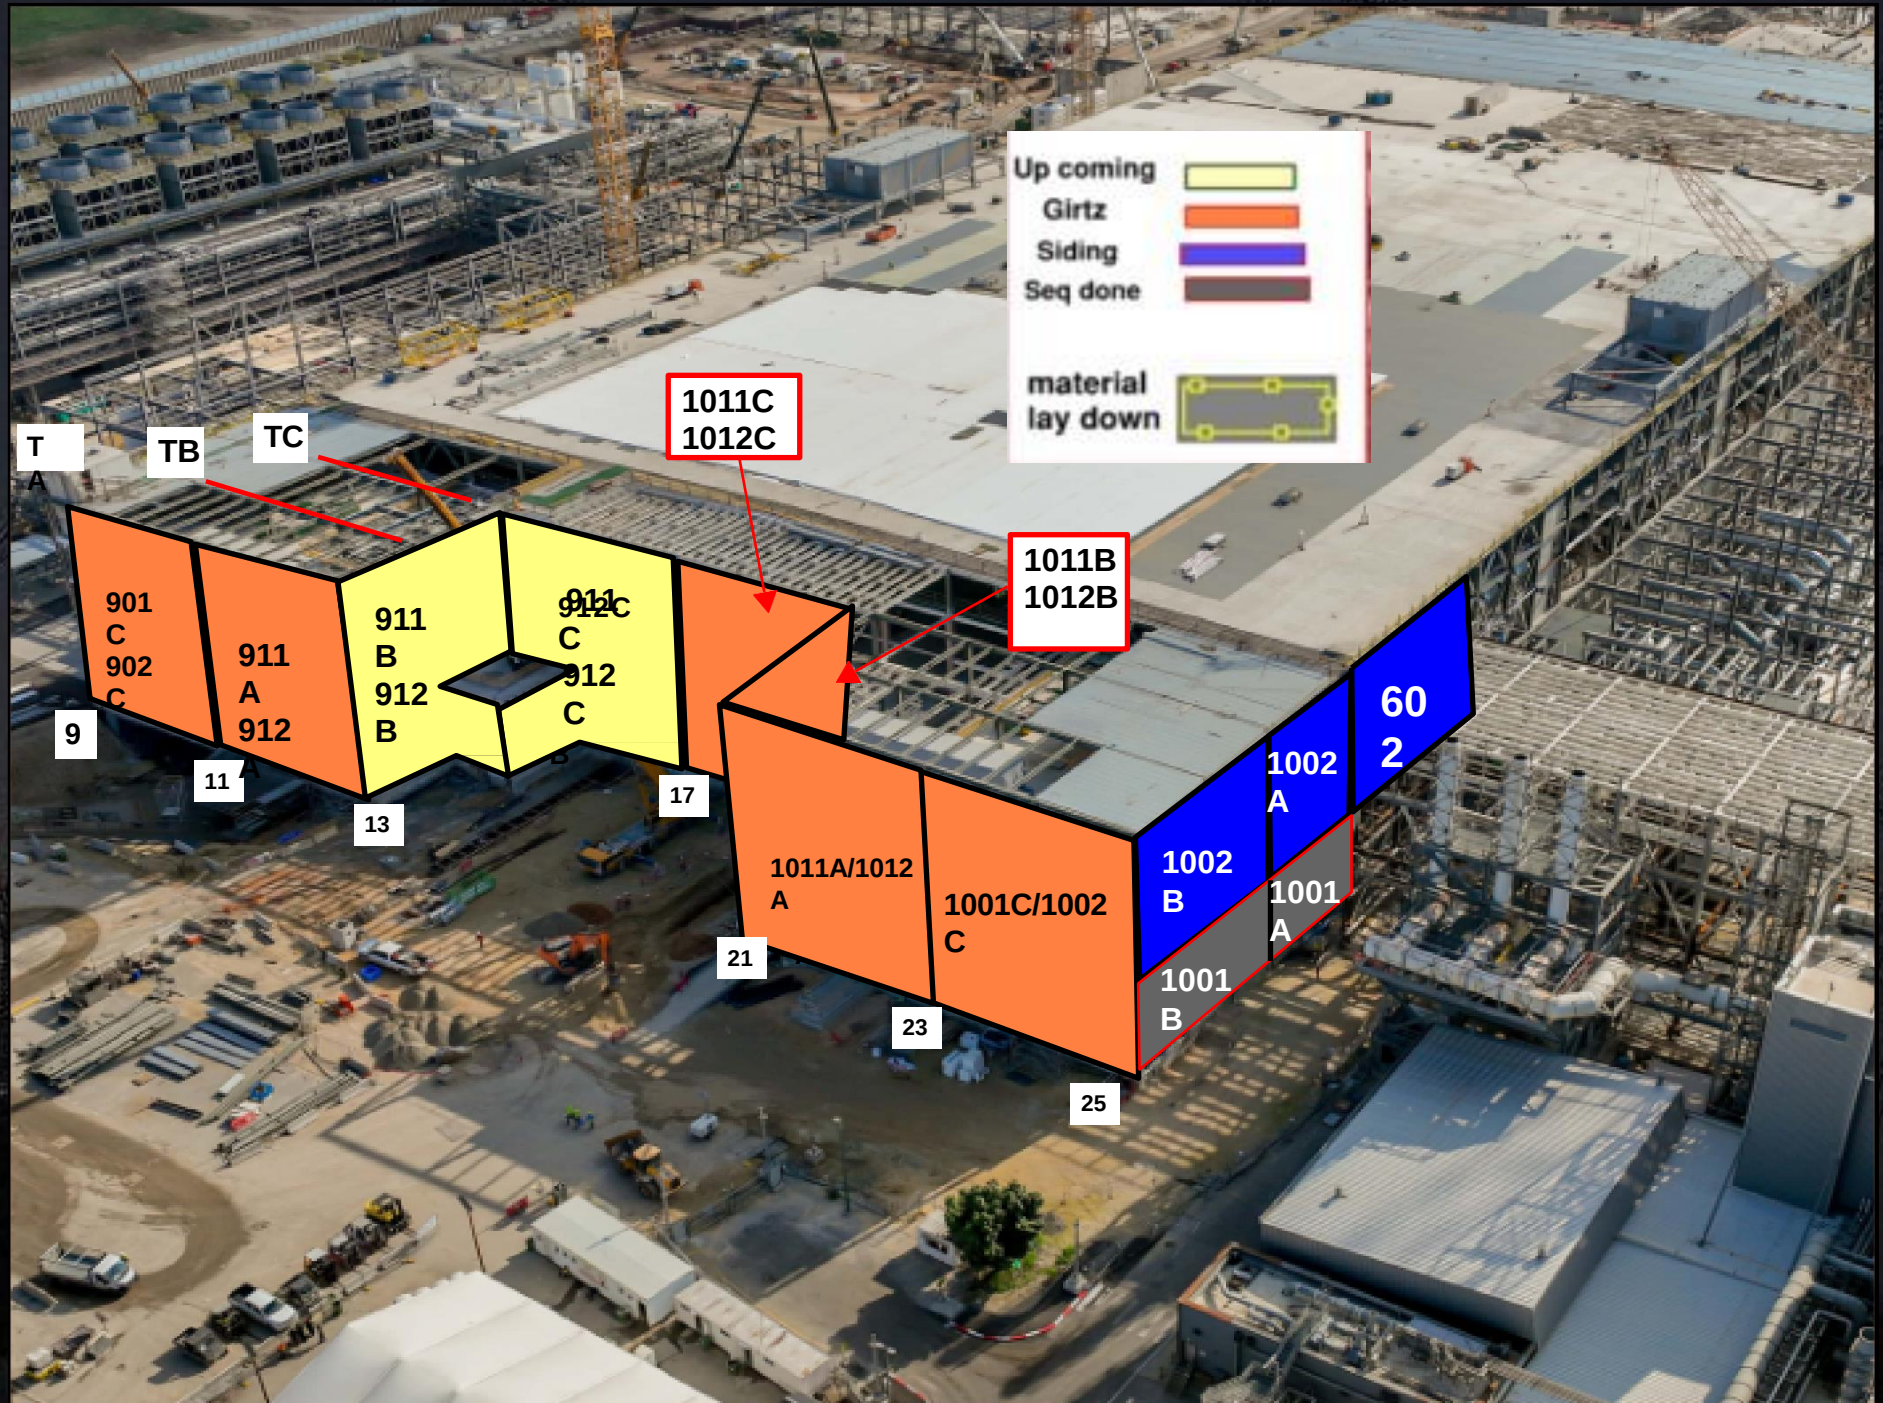


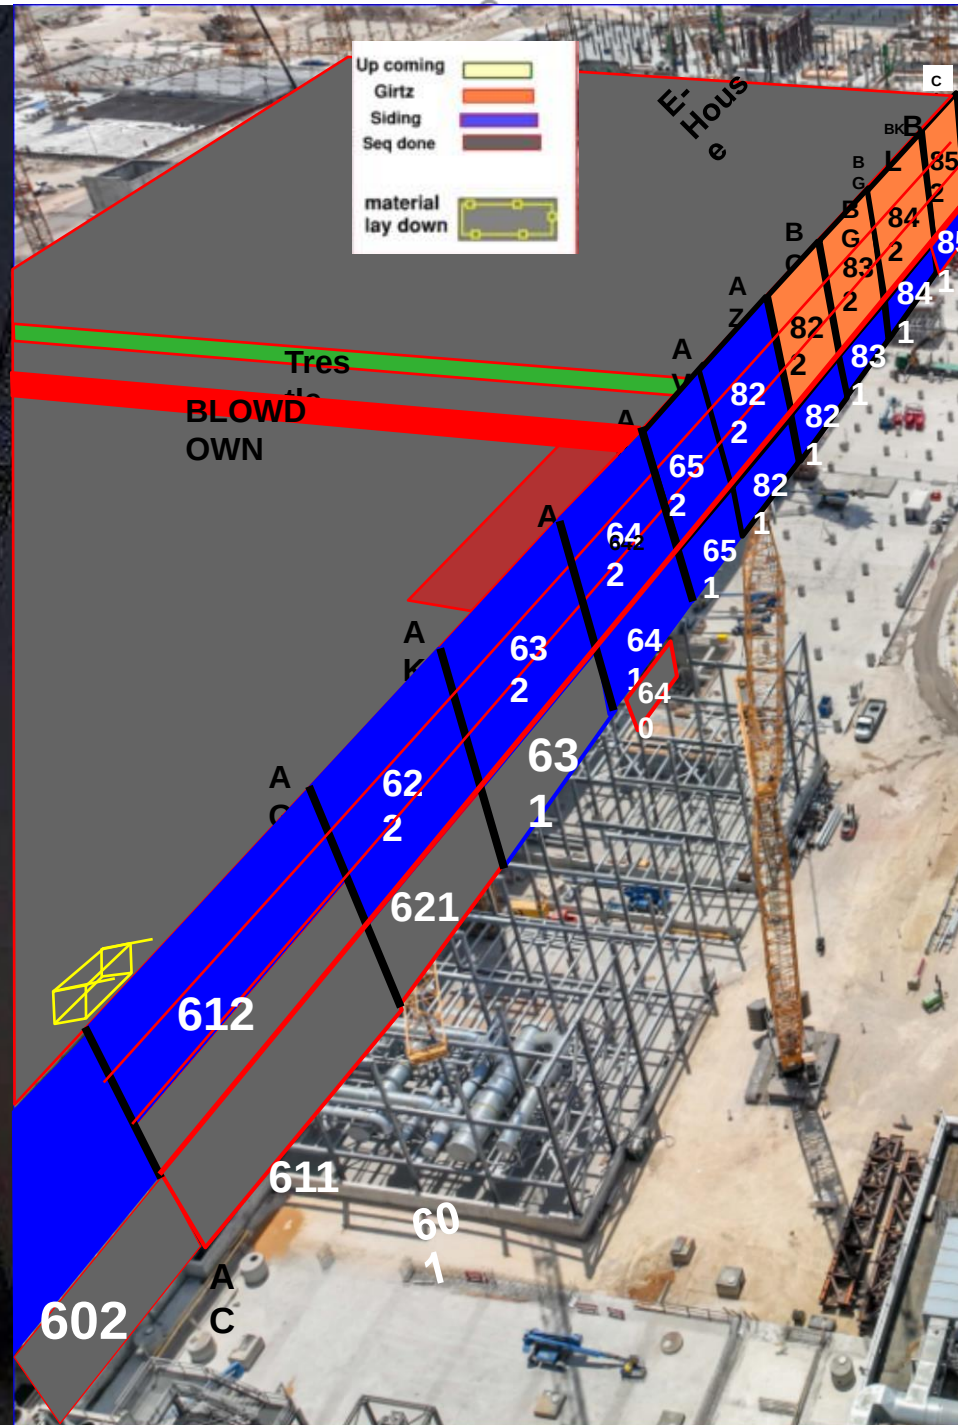

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

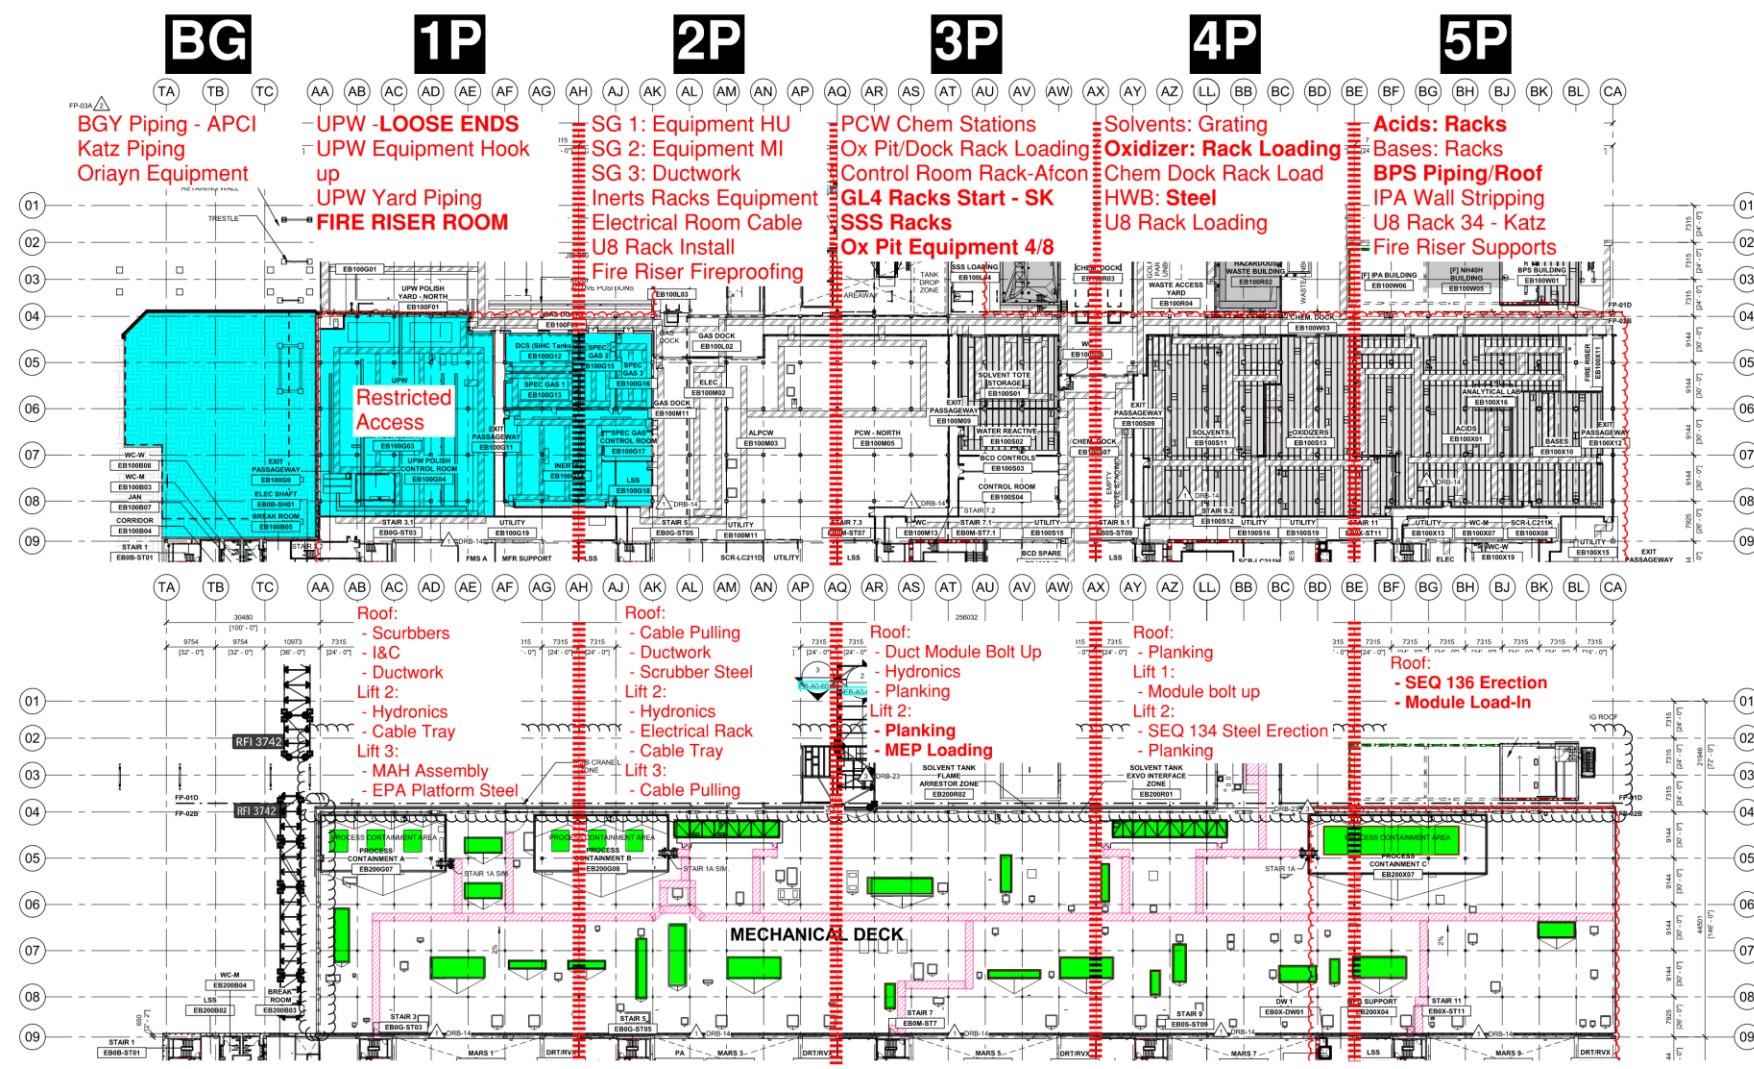

PSSS.2

Utility Level 1YA

PSSS Roof 2SA

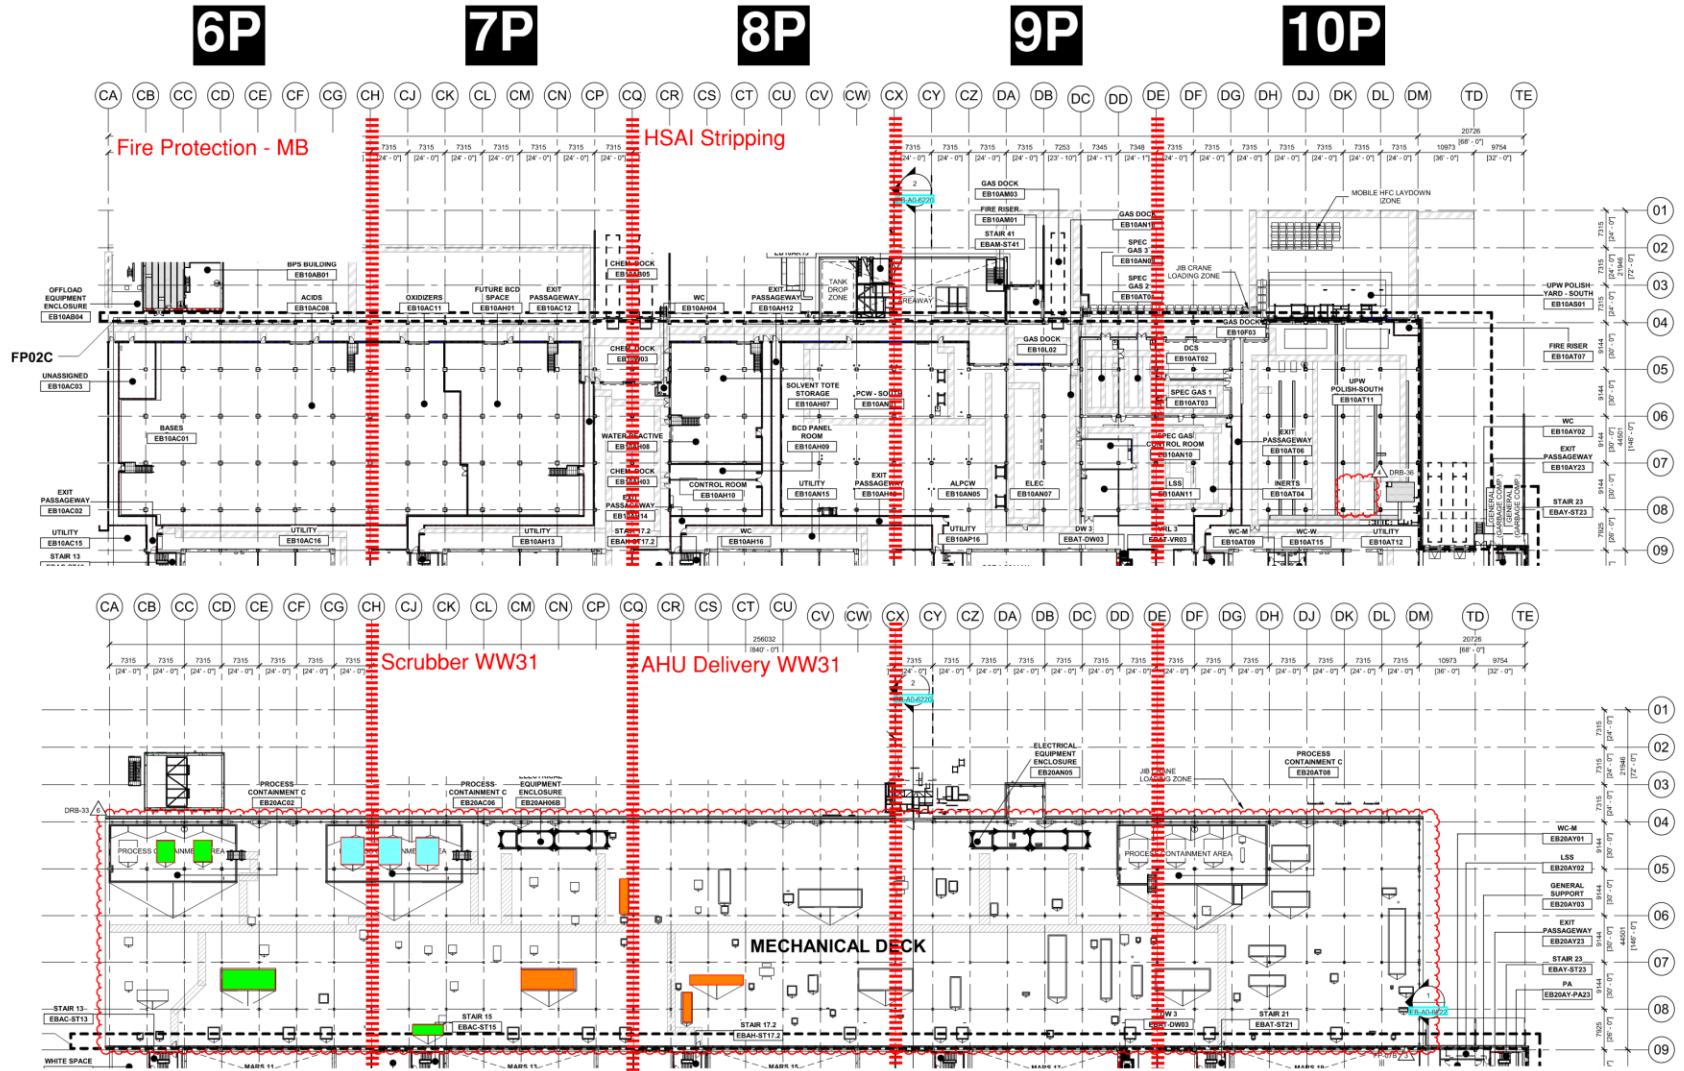



WJG 01J, 02J LIFT 2 & 3



WJG 03J, 04J, 05J LIFT 2 & 3



1J 2J 3J 4J 5J

Need Scaffold Removal Sun/Mon


CLOSED FOR STEEL ERECTION


Carmel Bidud - Ductwork
Pach Taas - Ductwork (UPN138)
SKE - DW/ CD Install


Carmel Bidud - Ductwork
Pach Taas - Module
Meptagon - Conduit Install


Carmel Bidud - Ductwork
Lesico NG Pipe Install (Fit Up +Welding)
Afcon Cable Tray Install
MB - FP Riser (DRB31)

Chemo - Pipe Install

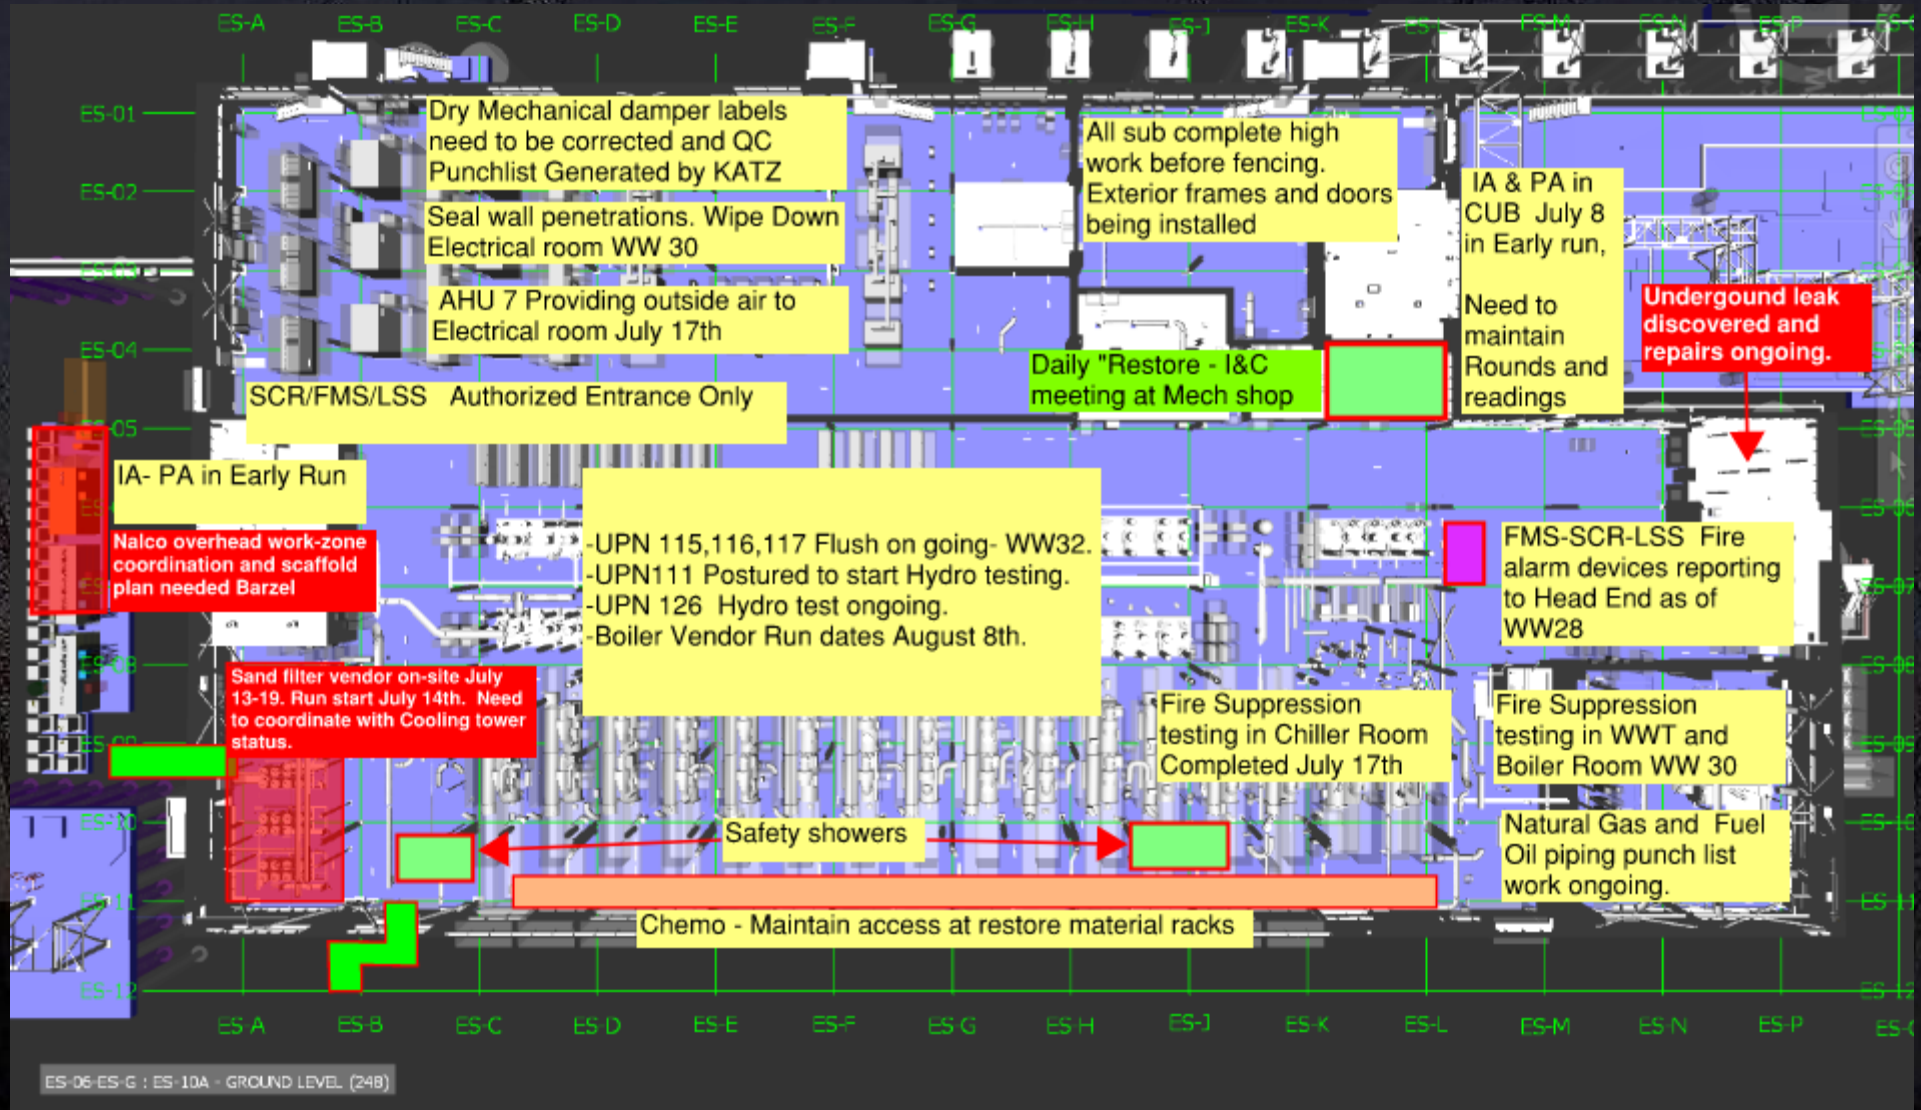

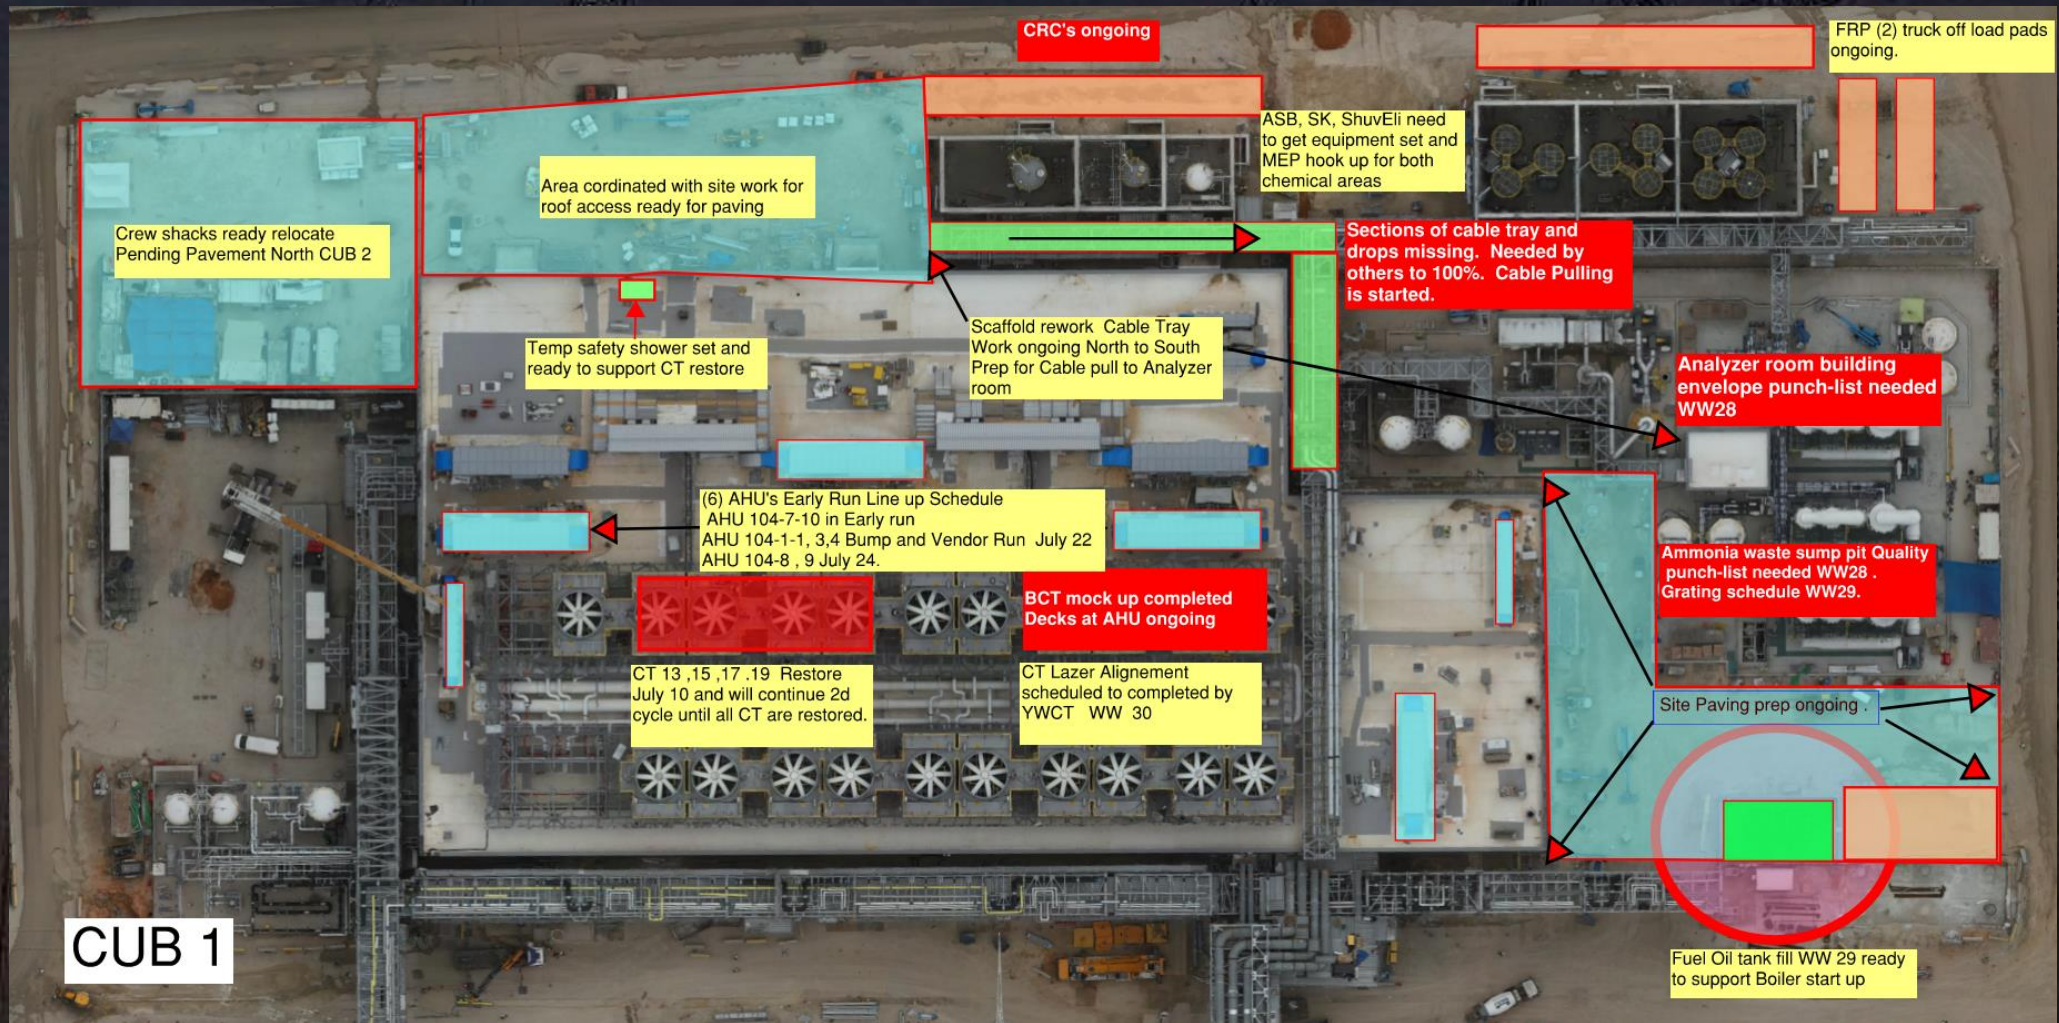

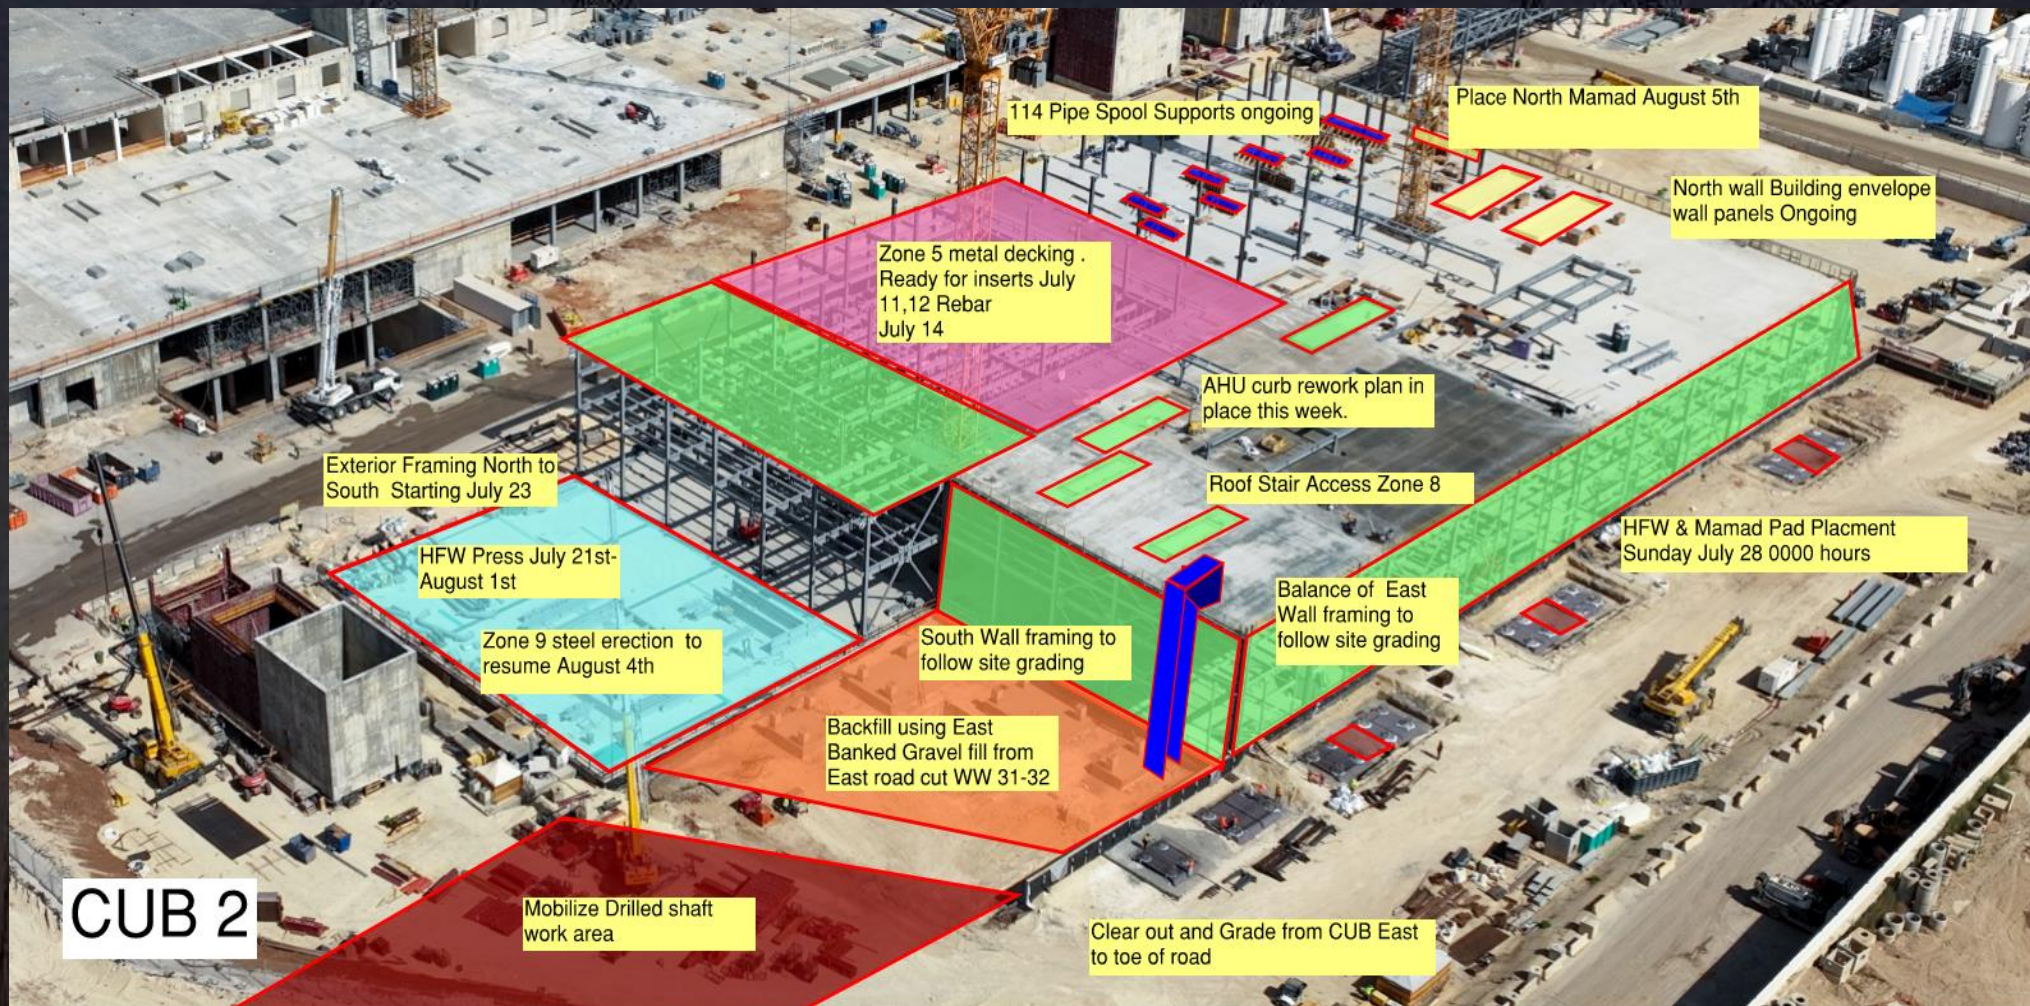

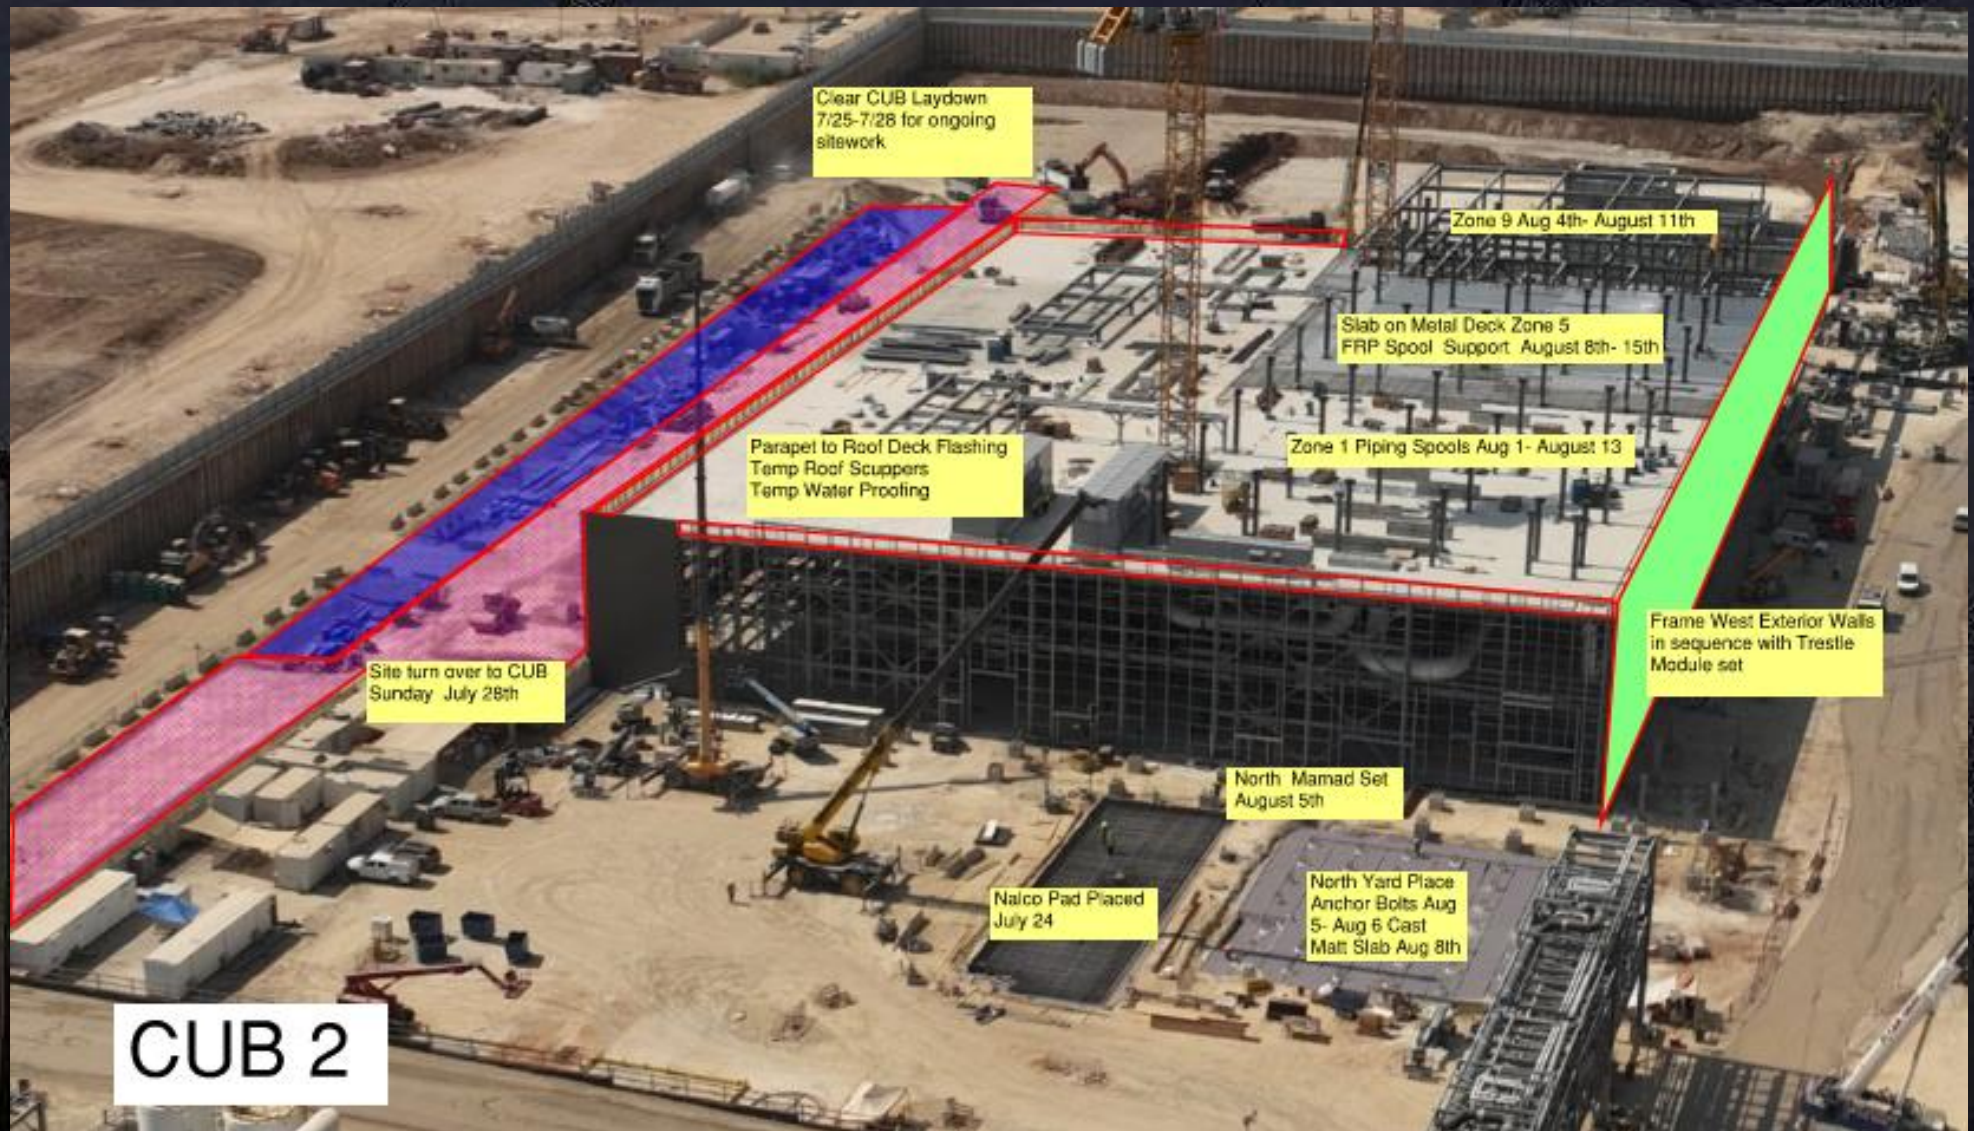



Trench lids will be instal 5/9/24
complete your sow before.


crane
locati
on

HRA AREA

Planning machinery-
truck, boom lift, fork
... etc work- requires
coordination in
advance Hcc Sup &
meet the requirement
before starting work
to insure not damage
facilities

For all subs
for compeleting SOW to submit microshedule till
25.07.24 for each sow , including disconnect &
evacuate trailers & material & must comply with
P6 SCHEDULE 100%
after NEY area turned to intel need sipp all NEY





HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

T-17

Trestle - MOD 2 Steel erection

6-7 August

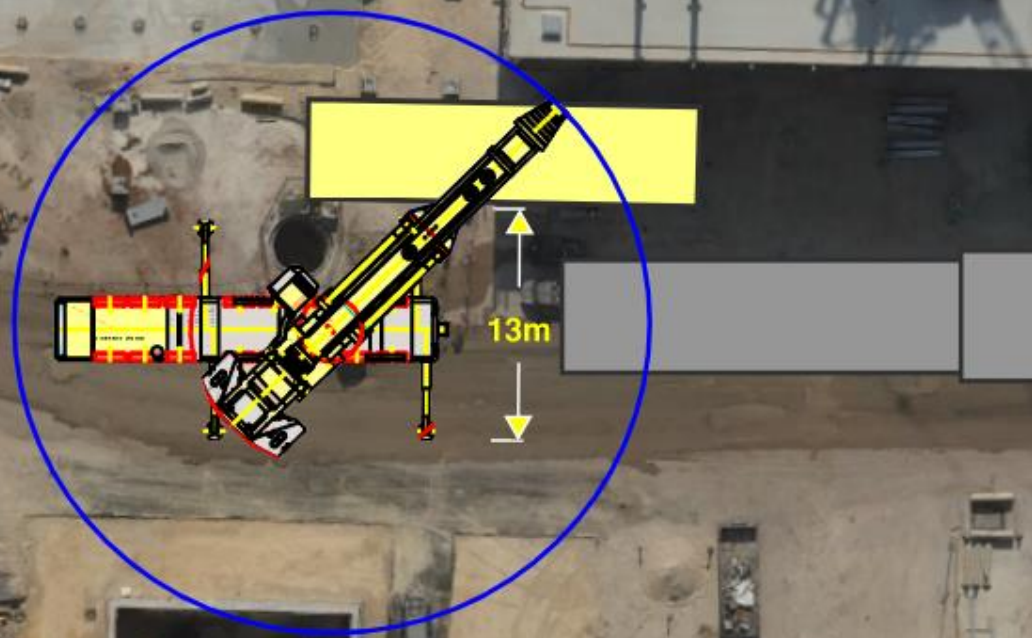




NDT radiography test at BGC vacuum tanks area

Spoter

Spoter


**Wednesday night July 28rd at
22:00 To
July 29th at 05:00 am.**

Daily Coordination Meeting

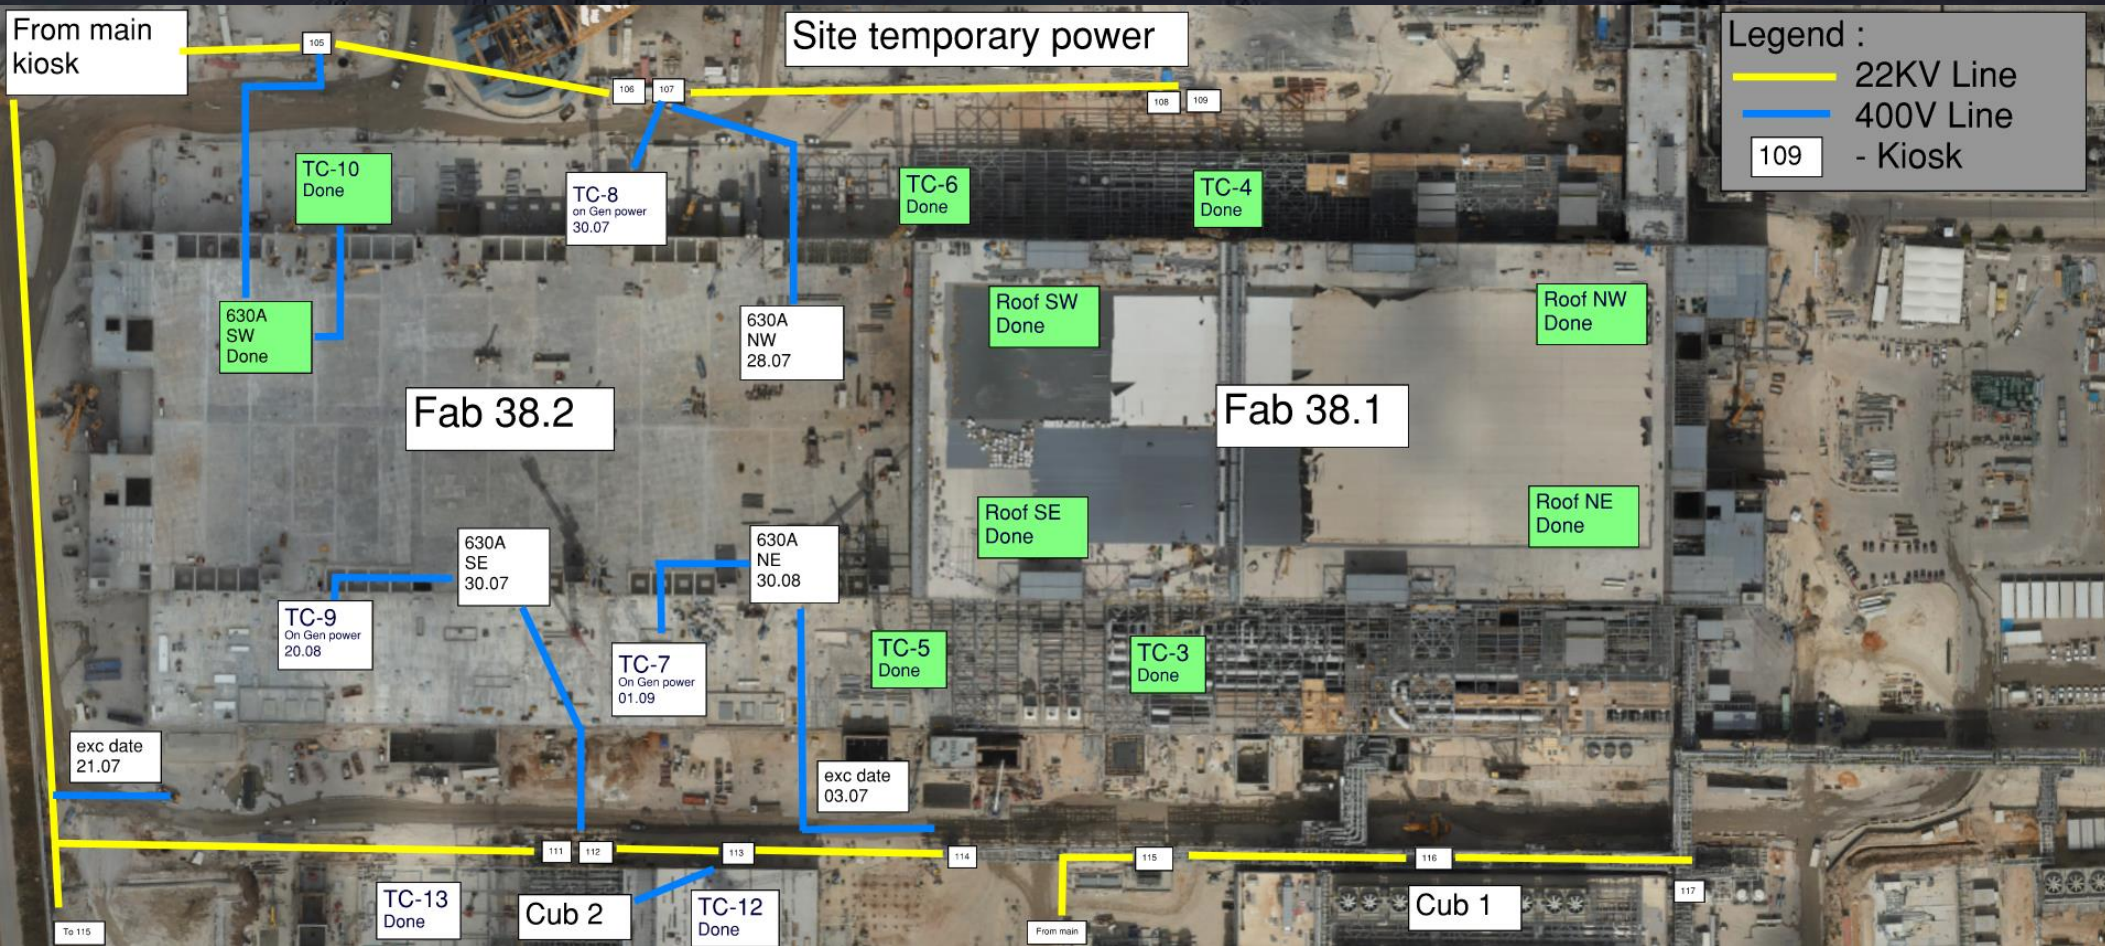

Daily Coordination Meeting


Site Logistics
North Gate B

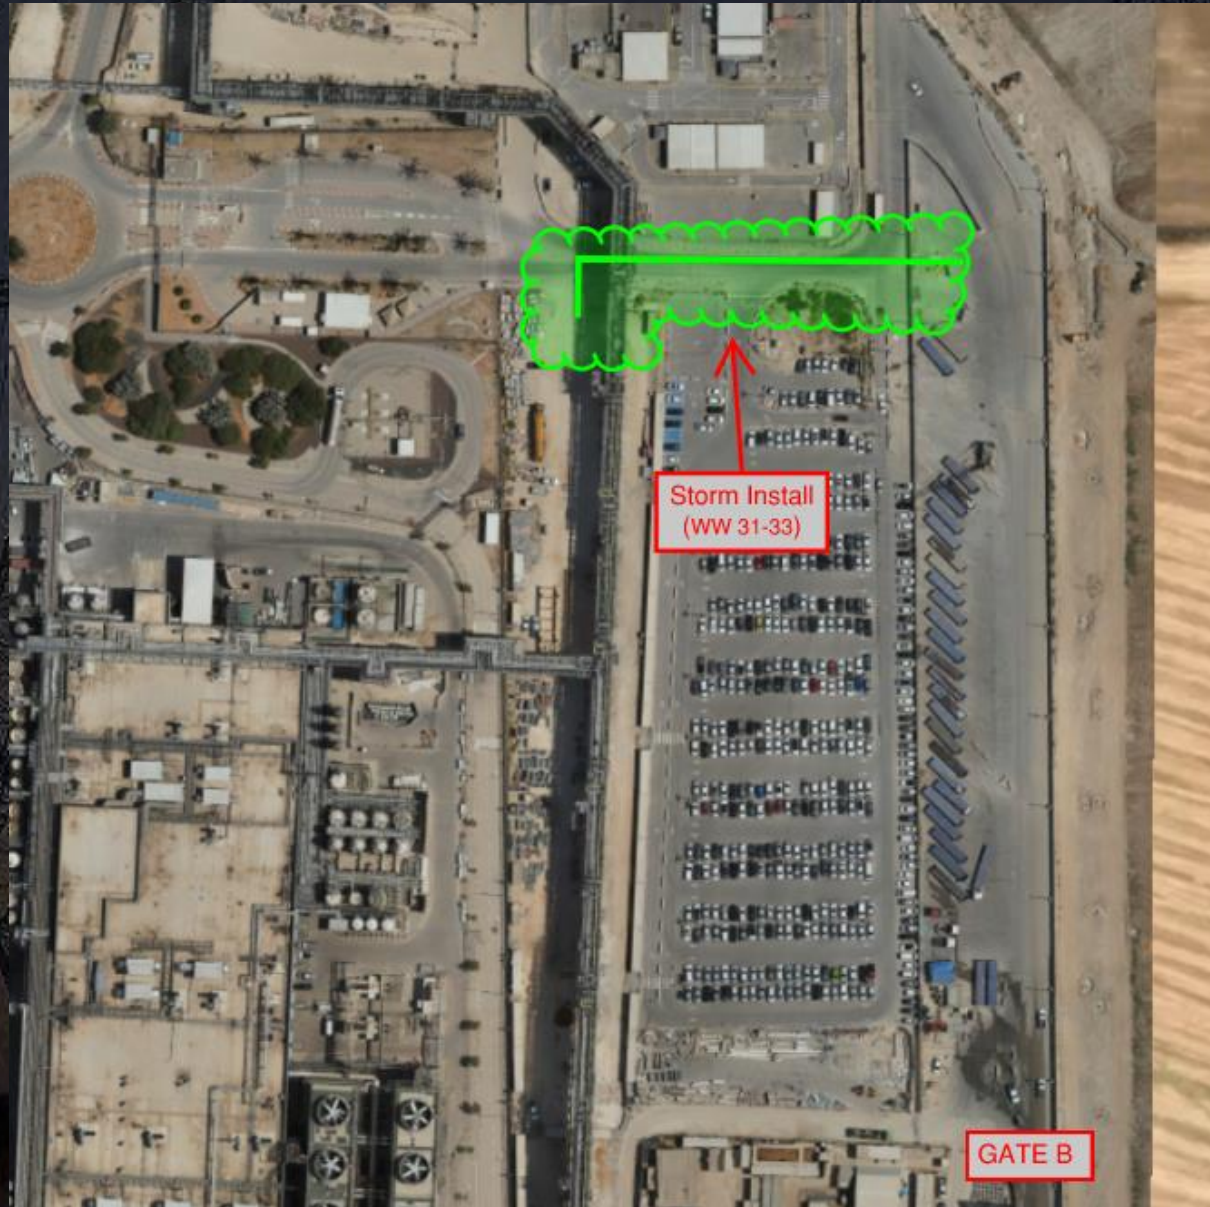

Daily Coordination Meeting

Site Logistics


Traffic Plan

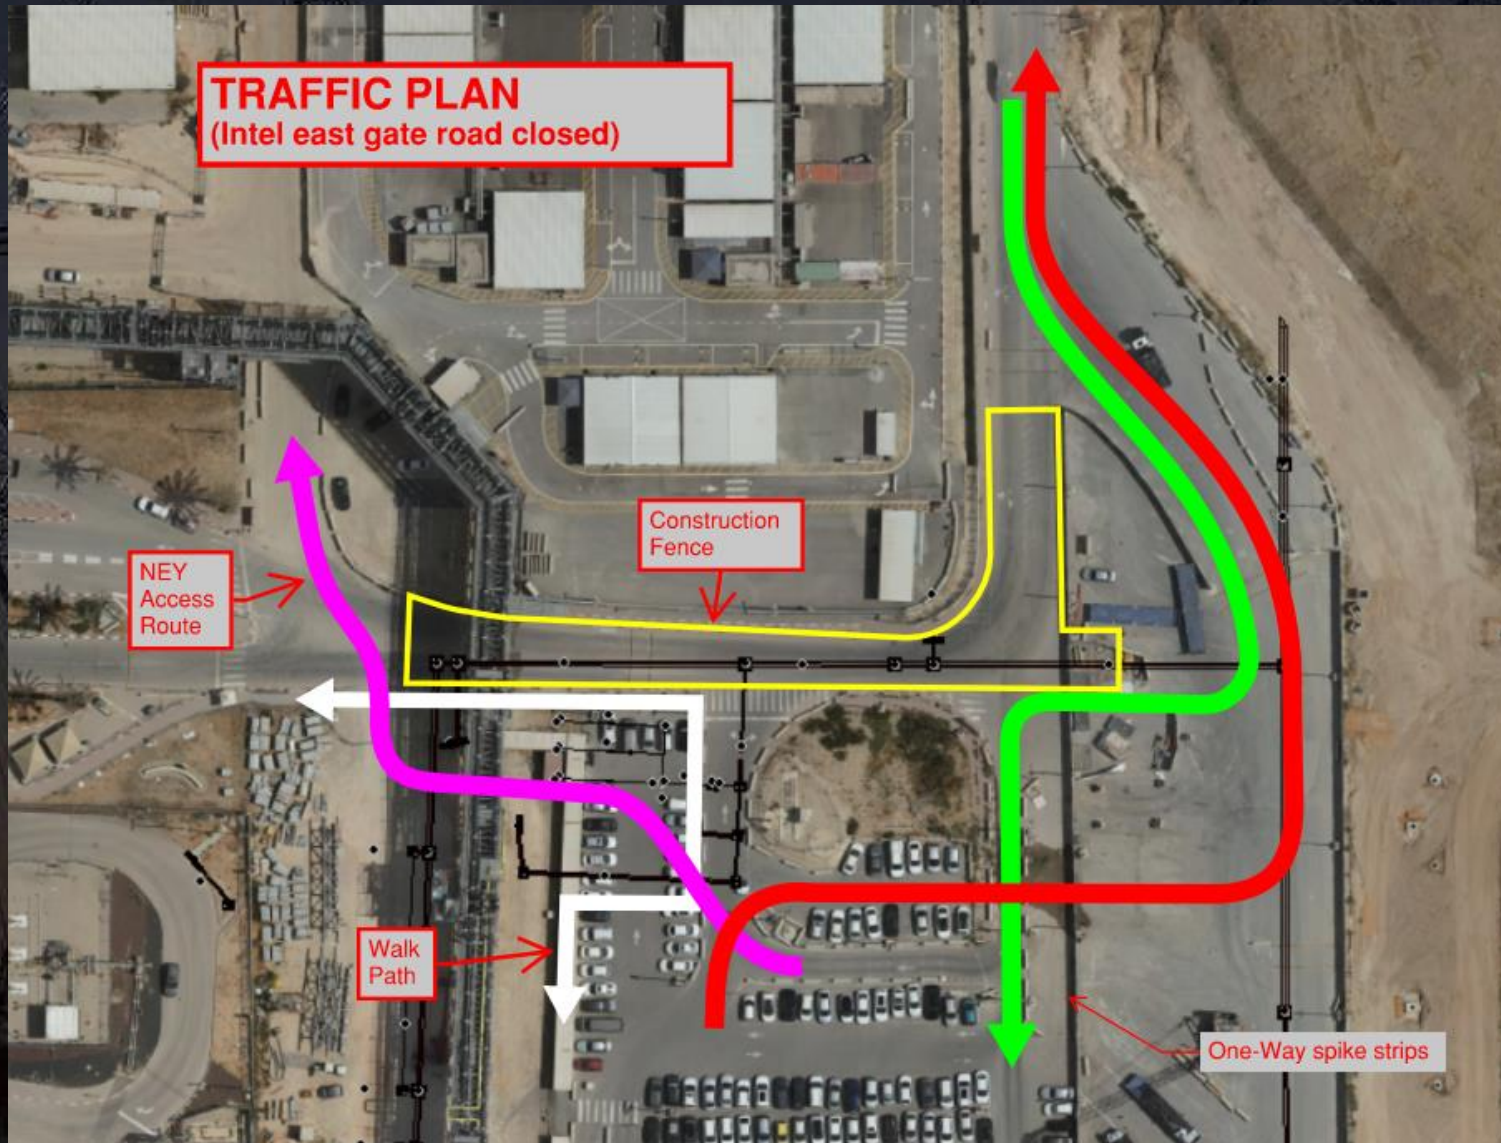

Daily Coordination Meeting

Site Logistics

North

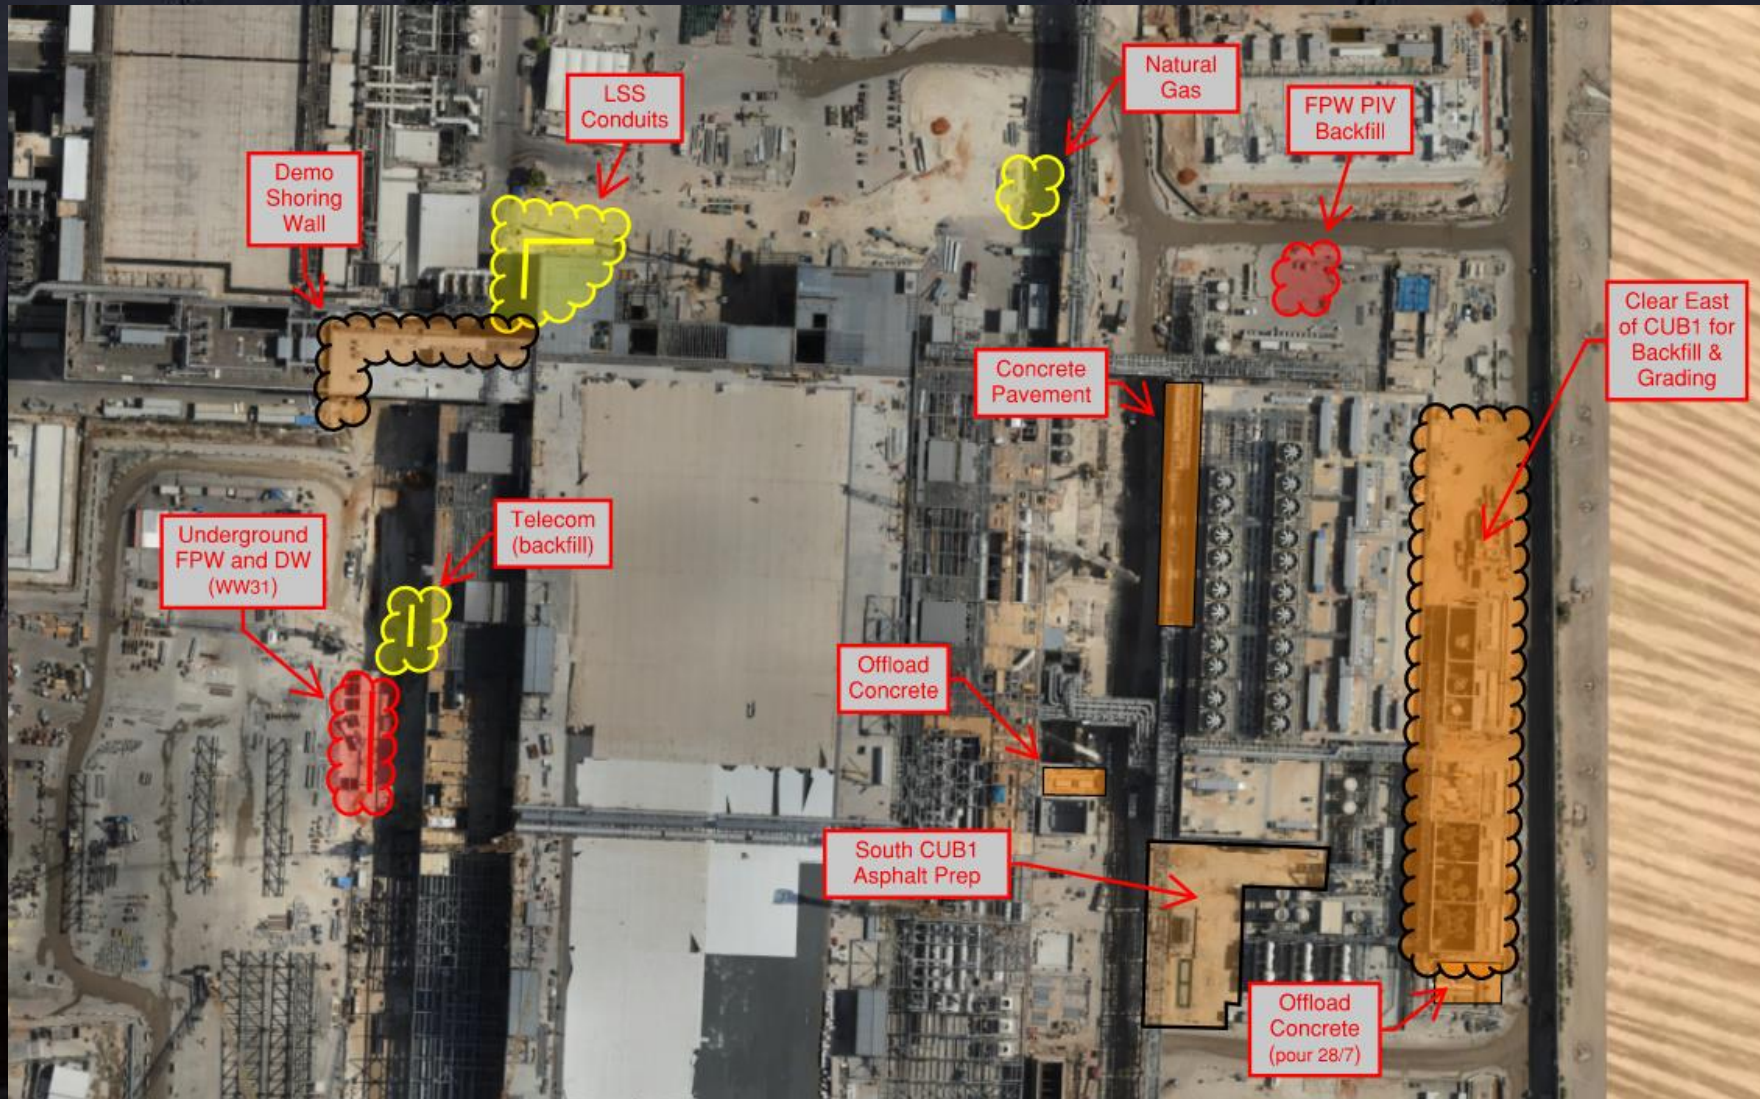

Daily Coordination Meeting

Site Logistics

South



Daily Coordination Meeting


Site Logistics
SW Parking
Sanitary



Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS


BF (1) AT GIS

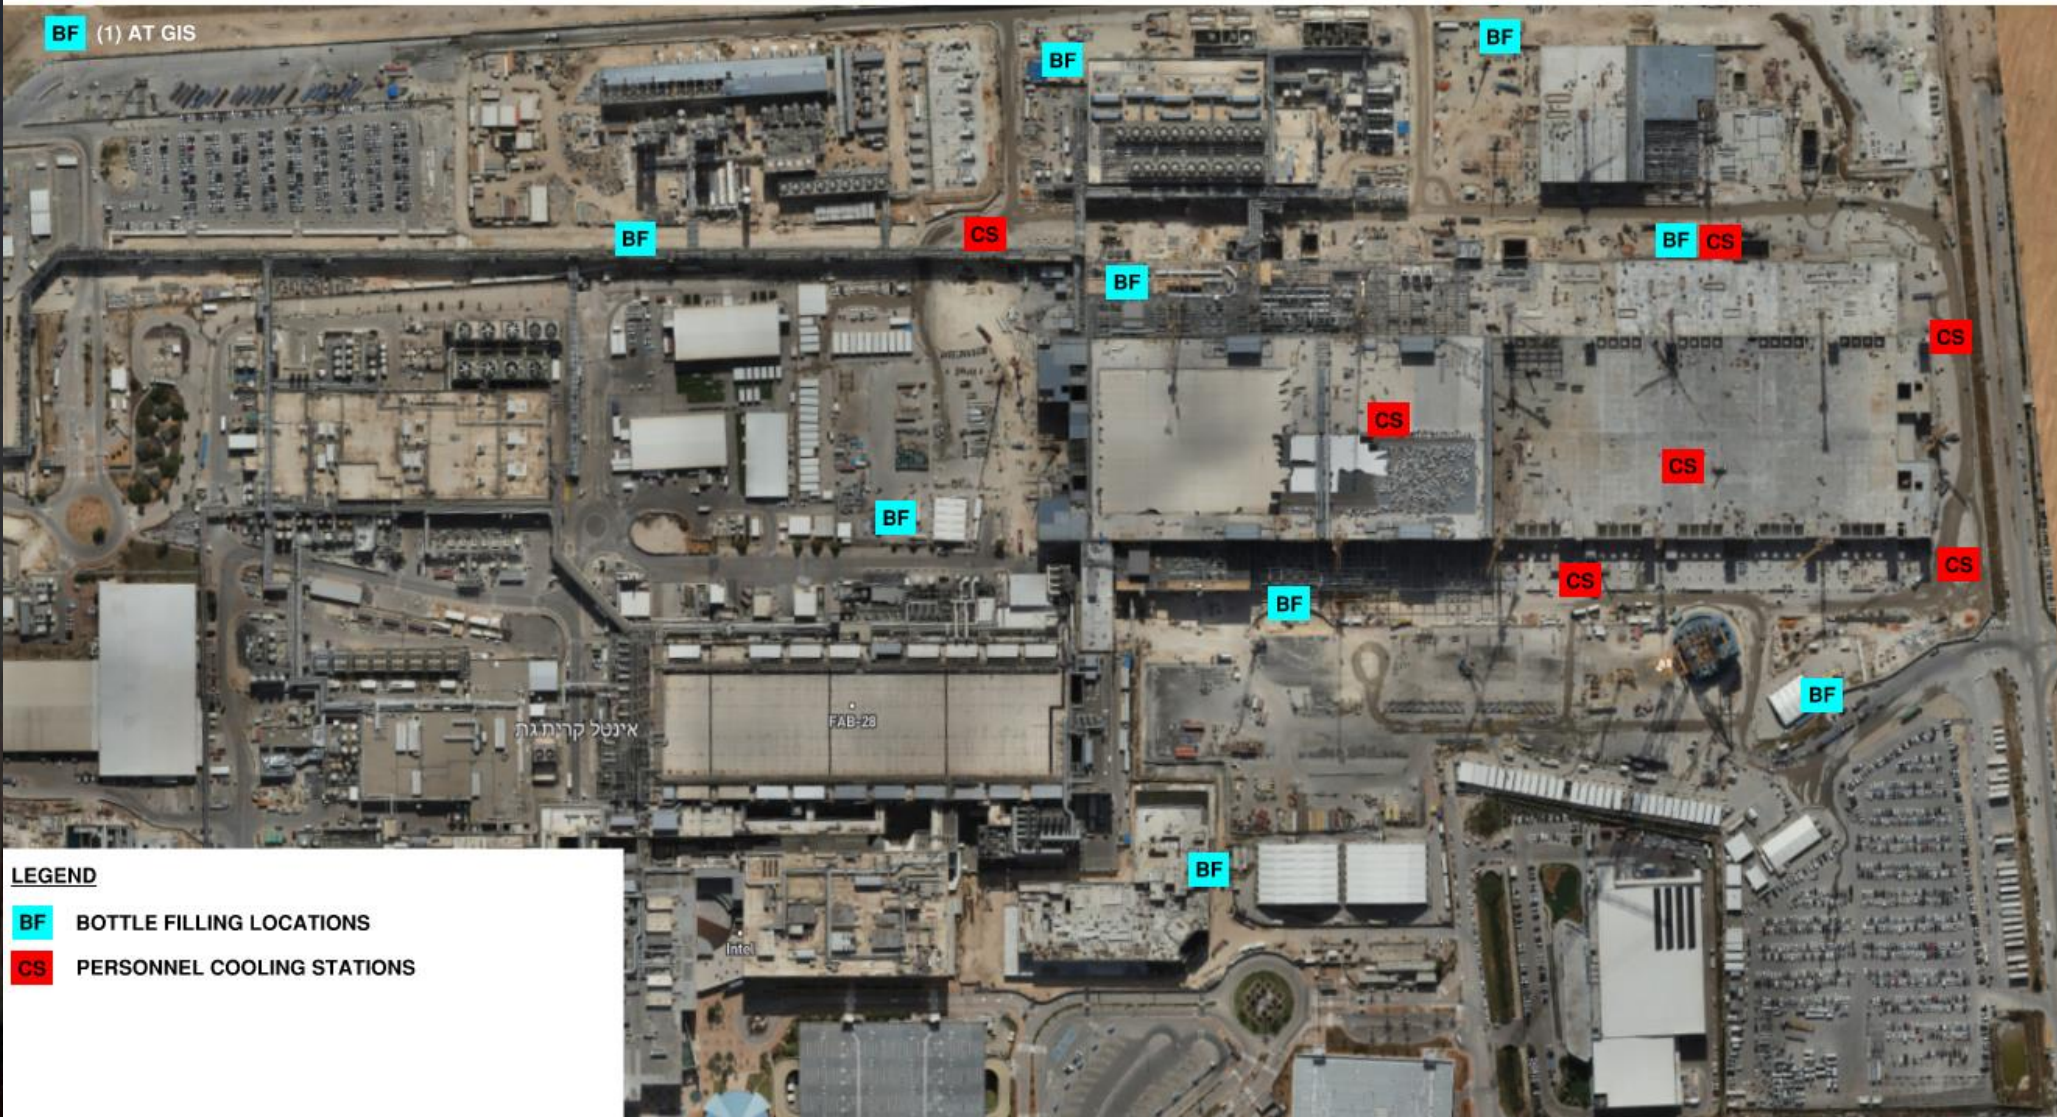

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

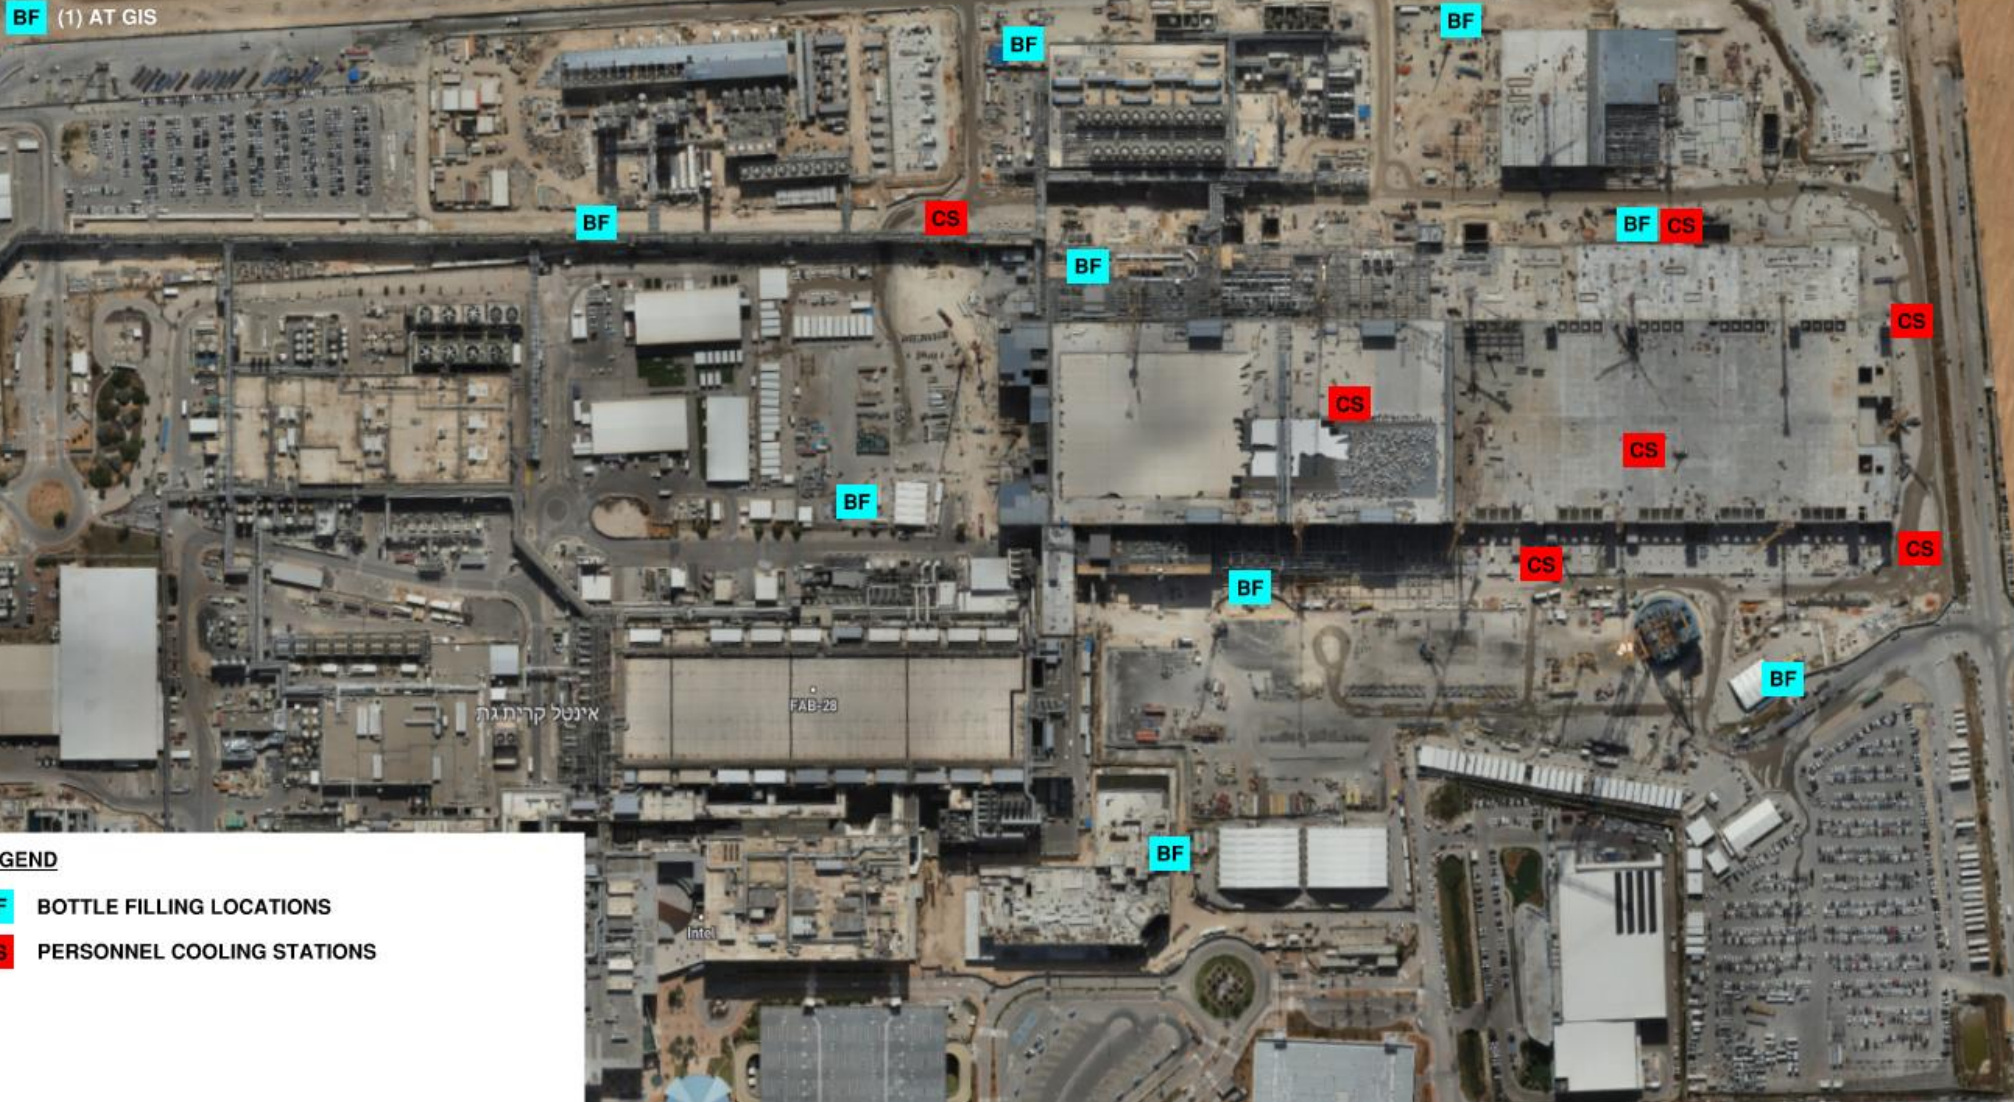


Line of Fire

- Line of fire is where part of our body is positioned where it is exposed to danger.
- Today, we had an employee lose the tip of their thumb due to positioning their hand in the line of fire.
- When we are setting up our work areas- especially small fabrication, cutting, drilling, etc. stations- we need to have the tools in place to allow employees to secure their material they are working on WITHOUT putting their hands in the line of fire.
- When using any tool, we need to ensure that our employees have received OTJ training about best practices for use, and that must include where to put our bodies to be out of the line of fire.

DON'T USE YOUR HANDS WHEN A TOOL WILL DO!

DON'T USE YOUR HANDS WHEN A TOOL WILL DO!

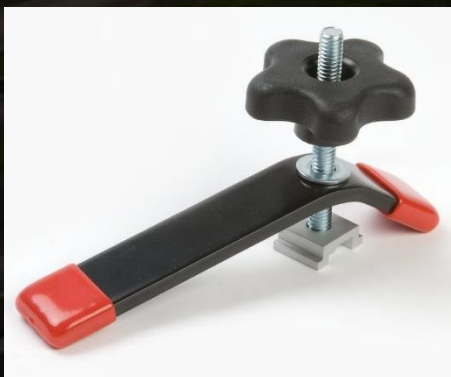

DON'T USE YOUR HANDS WHEN A TOOL WILL DO!



[Types of Clamps and When to Use Them | Dimide](#)

Heat Index- July 28th

	temperature (°F)															
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
45	80	82	84	87	89	93	96	99	104	109	114	119	124	130	137	
50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
55	81	84	86	89	93	97	101	106	112	117	124	130	137			
60	82	84	88	91	95	100	105	110	116	123	129	137				
65	82	85	89	93	98	103	108	114	121	128	136					
70	83	86	90	95	100	105	112	119	126	134						
75	84	88	92	97	103	109	116	124	132							
80	84	89	94	100	106	113	121	129								
85	85	90	96	102	110	117	126	135								
90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127										
100	87	95	103	112	121	132										

Caution

 Extreme Caution Danger Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

HCC/EHS Weekend Work- 26.07.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Ethan Wolery 052-6041765
- Gilad Haziza 052-5984370

CSA CM

- Idan Dahan 052-5949702
- Nikol Loboda 052-3124965
- Andy Jollands 052-9659290

MEP

- Michael Ohehir 052-4168879
- Leslie Kelly 052-6391546
- Hillel Mashiah 052-6175084
- David Young 052-2241683

QA/Cx

Cranes

- Hadar Shem Tov 054-6693626

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Professional – Anan Ragbe-058-7708886

Subcontractor Weekend Work- 26.07.2024

FAB

Utility Level

- Carmel raks
Foreman; Lucy 0506552488
Ehs; Michel 0542634700
- Combe upw
Foreman; Edward 0526419894
Ehs; Michael 0525506596
- Elram
Foreman: Shlomo 0545551702
Ehs: shy 0523632132
- Combe waste
Foreman: Denis 0525238504
Ehs: Michael 0525506596
- Chemo
Ehs lilach 0547886704
Forman sergey 0544659688
- Carmel duct
- Afcon electrical
- HYG

Clean Room

Subfab

- Carmel Bidud – AA scaffold removal
Ibrahim – 052-951-9833
- Afcon E – SF LSS Rooms. Avieli – 052-600-8487
- WW – Elev. Shaft 1

PSSS

- Pach Taas – Module bolting PSSS Roof and Lift 2
Foreman – Vadim – 052-6229005
Safety – Offek – 050-7838486
- W&W – SEQ 131,134,136, and 2P Scrubber Grating
Foreman – Willie – 052-6145521
Safety – Gary Lambert – 1-405-833-8910
- Katz – U8 Rack 7 Plate Install
Foreman - Polishchuk - 054-750-1845.
Safety – Ofer Ilisar - 054-675-6690
- Katz Piping – UPW Room
Foreman – Konstantin Tsib – 054-7861613
Safety – Ofer Ilisar - 054-675-6690
- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2
Foreman – Charles – 055-2740190
Safety – Stevan – 055-9129333
- Combe UPW – UPW Room, UPW Yard, and Water Reactive Piping
Foreman – Eduard – 052-6419894
Safety – Michael – 052-6419894
- Chemo A. – PSSS Roof and Lift 2
Foreman – Maor – 050-955-9071
Safety – Rotem – 054-447-7112
- HSAI – BIPA & MOD2 Stripping
Foreman – Dave – 052-4121028
Safety – Sam – 052-5259268
- Carmel Bidud – 5P/U8 Rack 7 Ductwork & Roof Ductwork
Foreman – Hitim – 052-7053353
Safety – Michael – 054-2634700

Girts

Subcontractor Weekend Work- 26.07.2024

WJG

- Afcon
- W&W
- Pach Taas
- Chemo Aharon

Site

- **Derech Afar** – Sanitary lift station & sanitary underground install
Supervision = Raed: 054-2442030
EHS = Alex: 054-5403849
- **Olizki** – Sweepers and water trucks, truck offloads, concrete flatwork (PCC) & excavation
Supervision = Yossi: 052-2180485
EHS = Ben: 052-4033565

Trestle

- SN- Piping

CUB

- H.s.a.i
- Chemo
- Saminajami cub 2

GIS/NEY

TMT: •

Zone 8 Welding of fire fighting piping with the help of a crane

Zone 7+8+warehouse general cleaning and hot work in favor of a concrete floor 1*1

Manager - Ido Deus 050-866262
