

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- Weekend work




UTILITY LEVEL MOD1

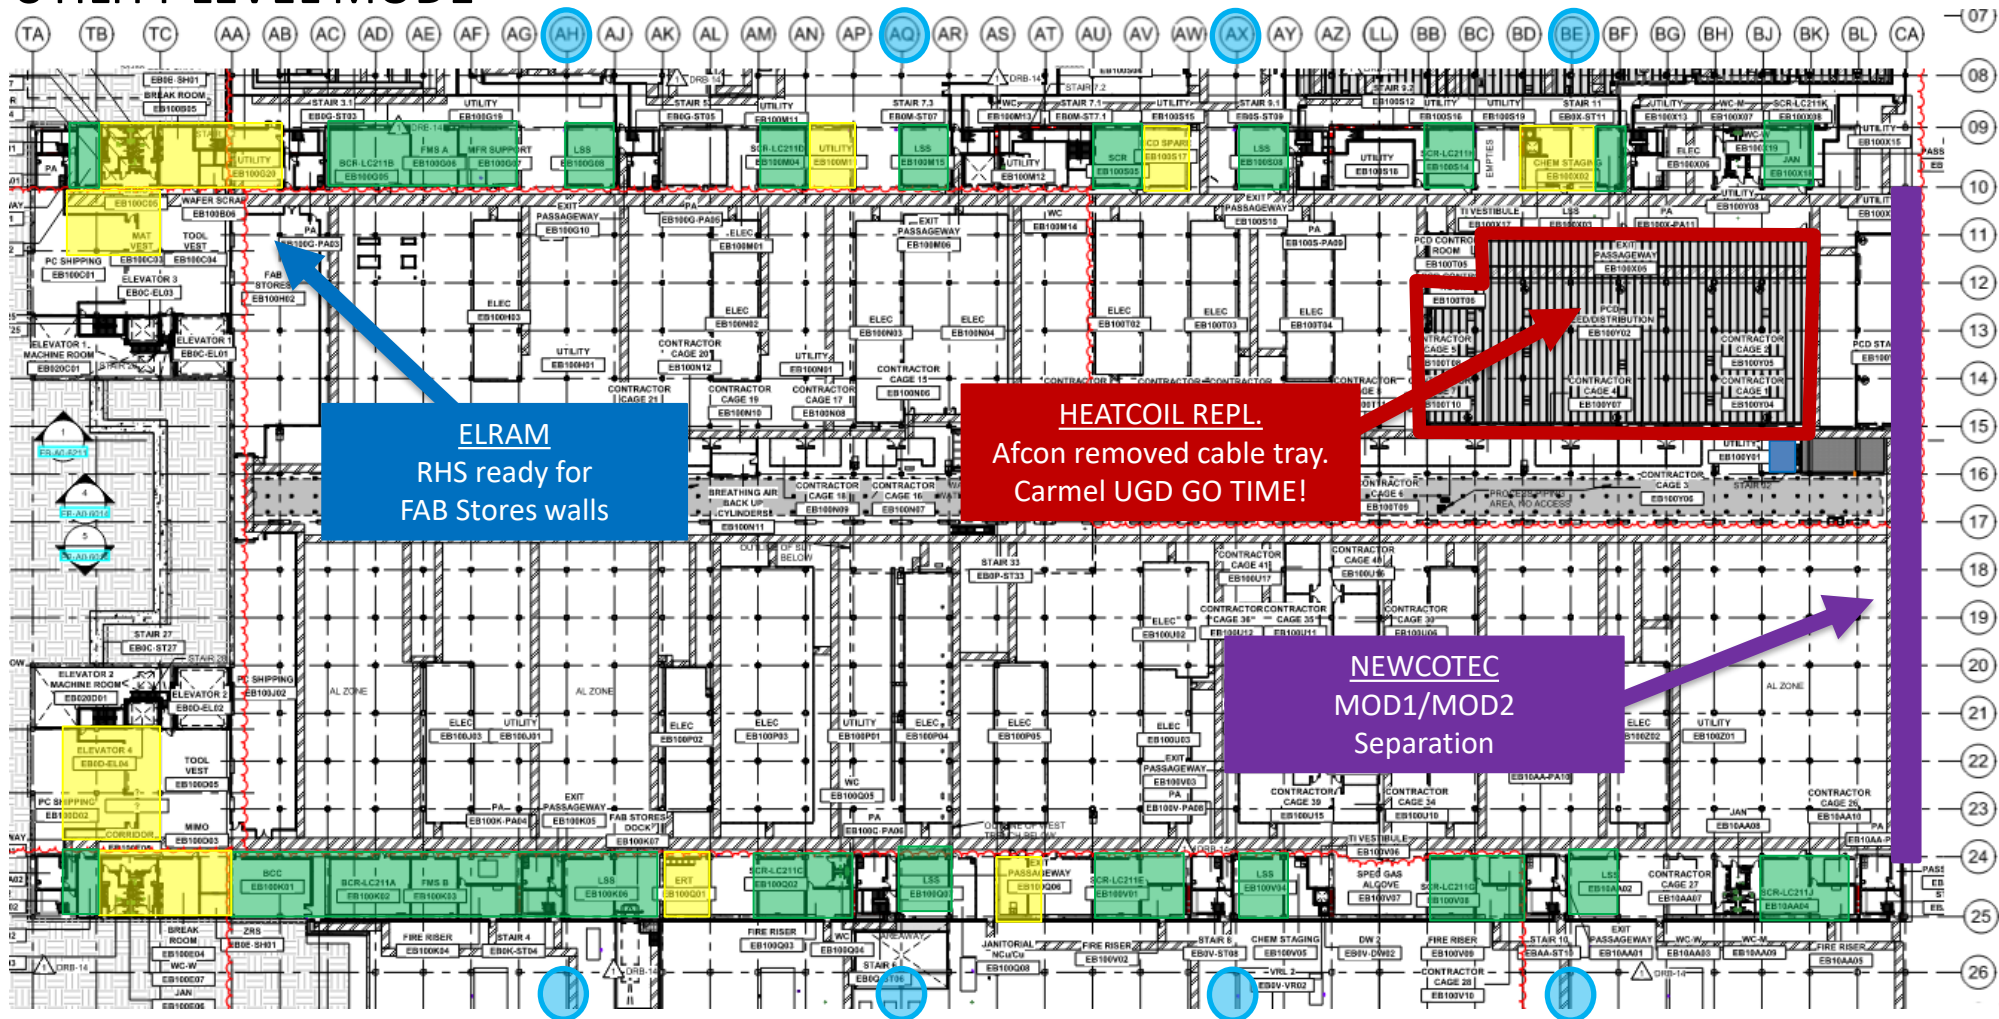

ELRAM
Drywall install

MEP+Electrical
Ready for re-install

UTILITY LEVEL MOD2

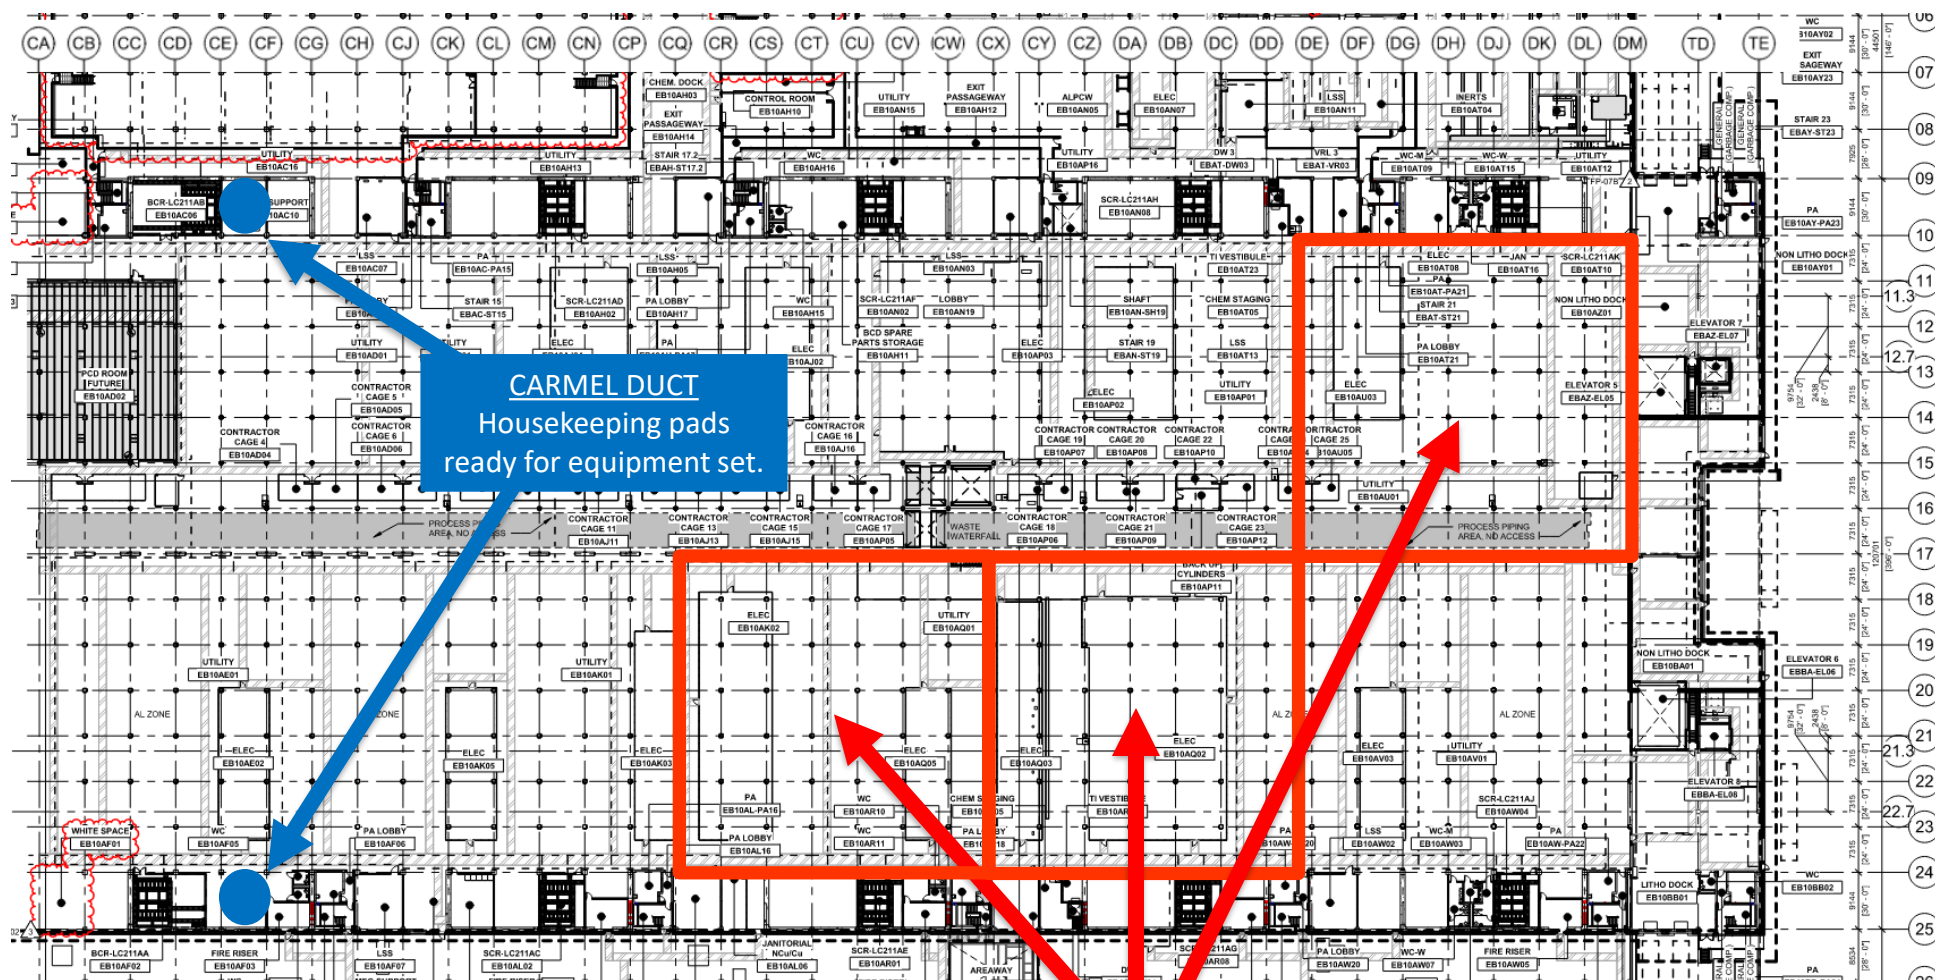

SUT 38.1 LEVEL




Solvent room.

CRC completion -
31/12

SUT 38.2 LEVEL

Rack 4b
Lifting
schedule
#6 –

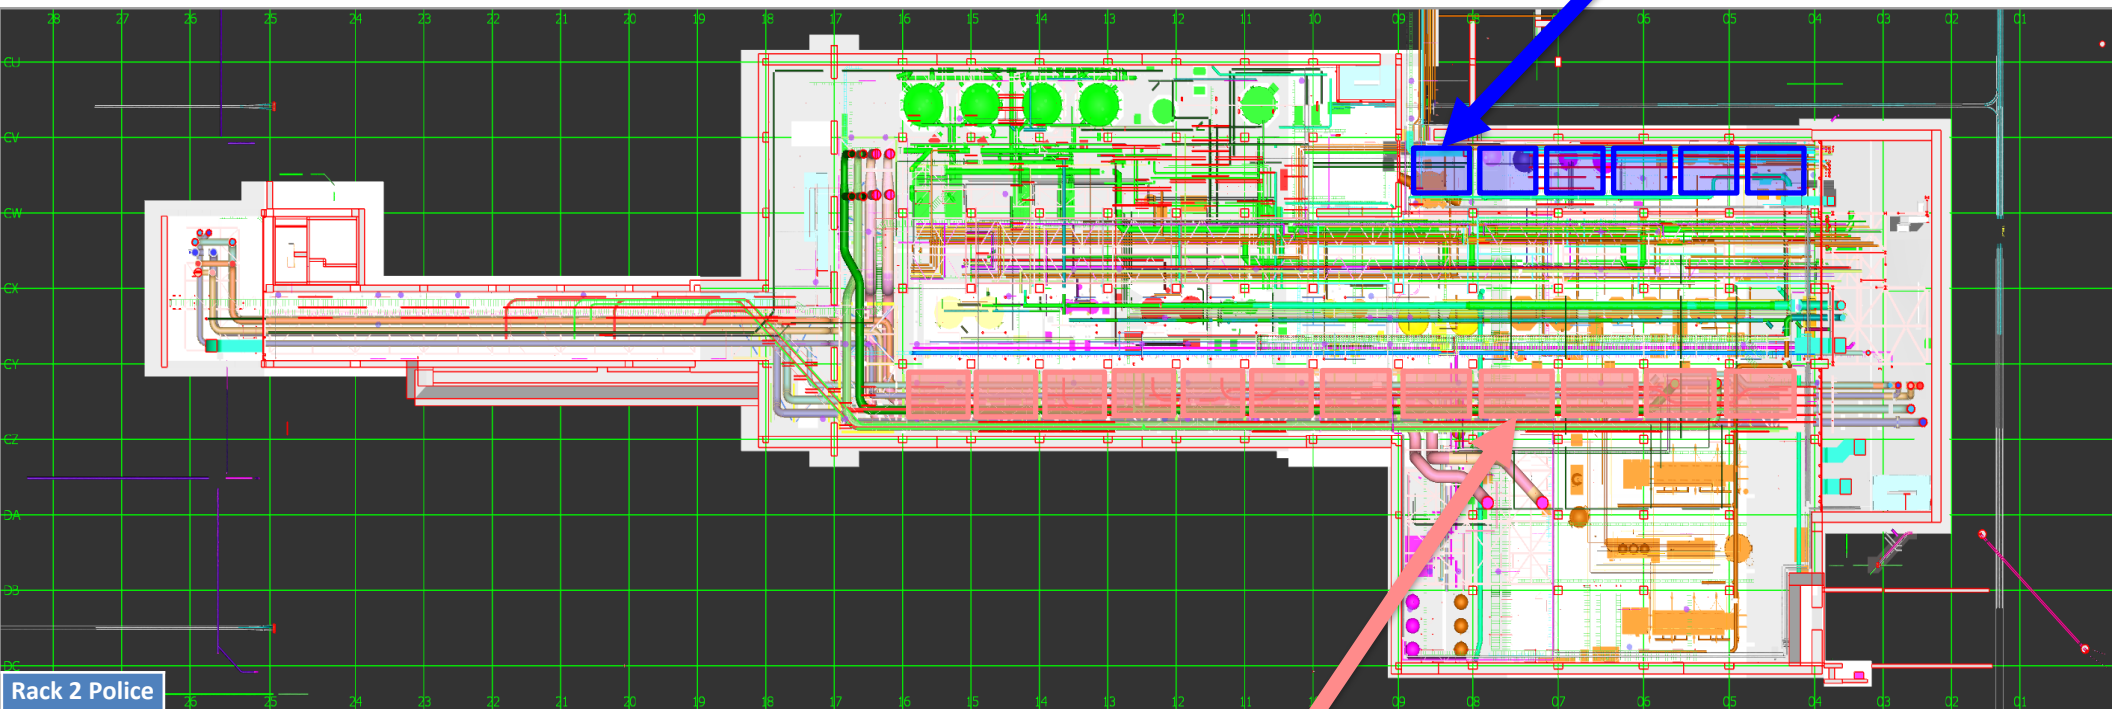


**Rack 2 Police
escort dates**


v24.11.24
v25.11.24
v3.12.24
v9.12.24
v12.12.24
v15.12.24
v17.12.24
v22.12.24
5.1.25
14.1.25
2.2.25
9.2.25

Rack 2
MIMO -
Module #9
5th of Jan


SUBFAB BUILDOUT MOD 1

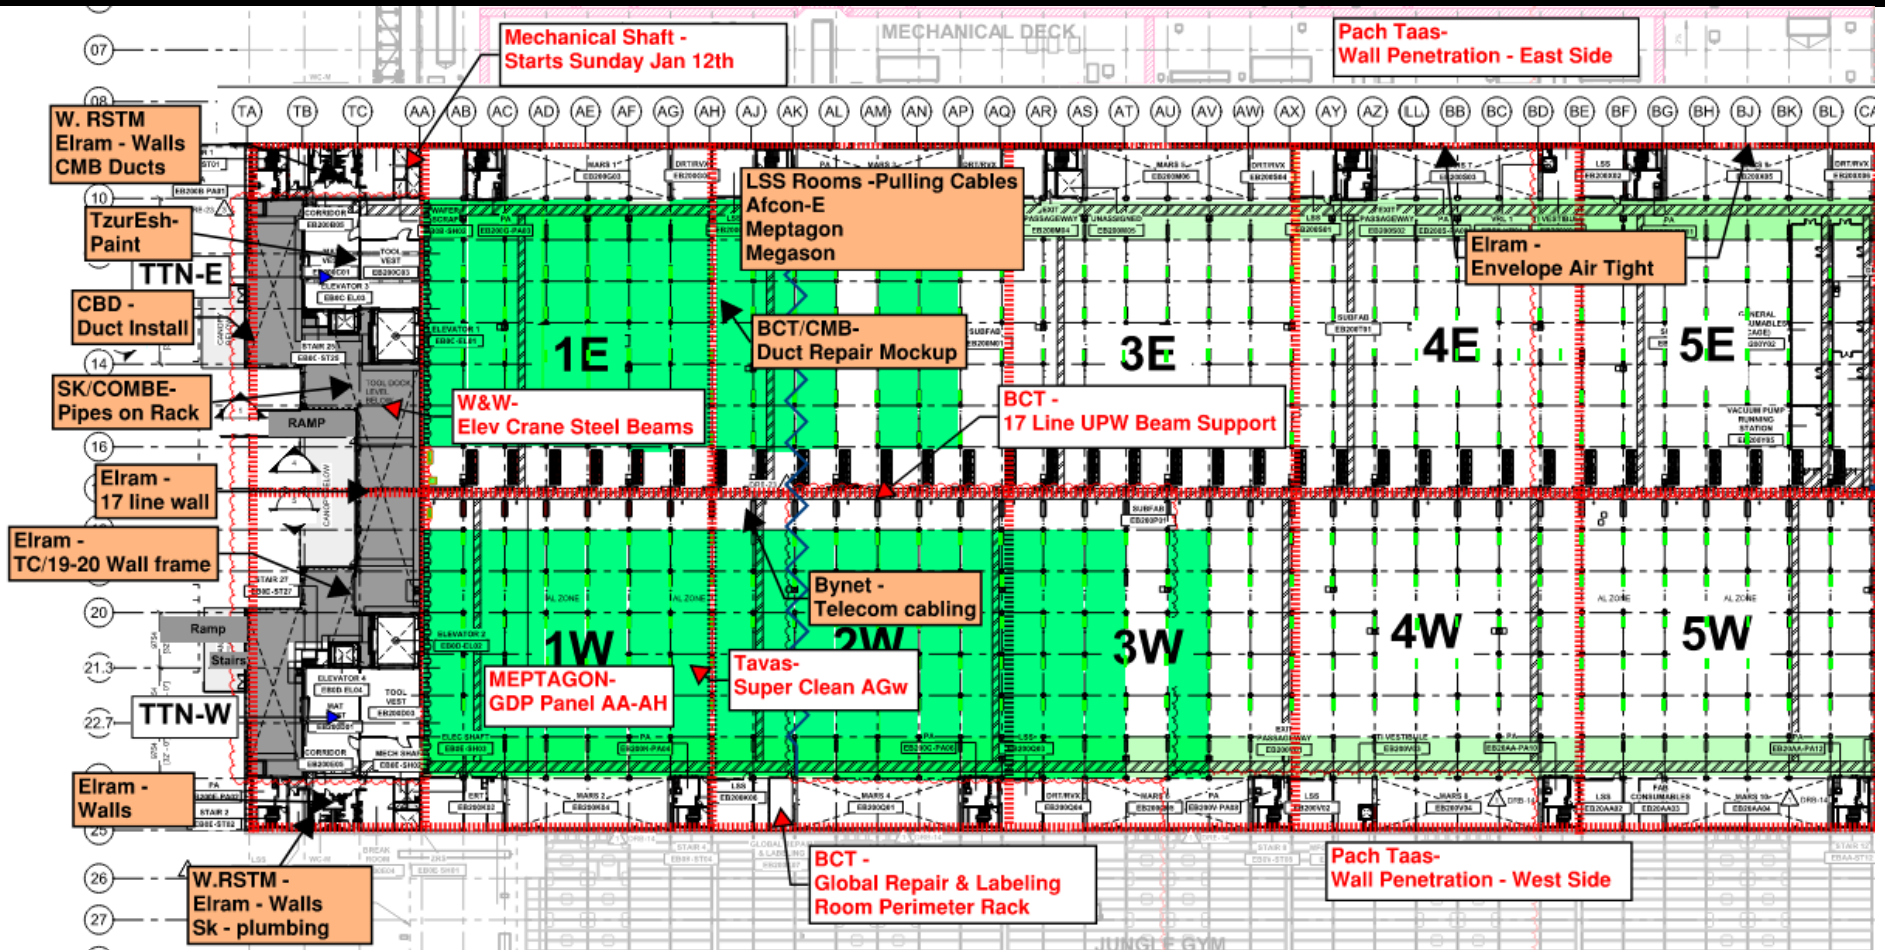


SUBFAB CRC TOPCOAT

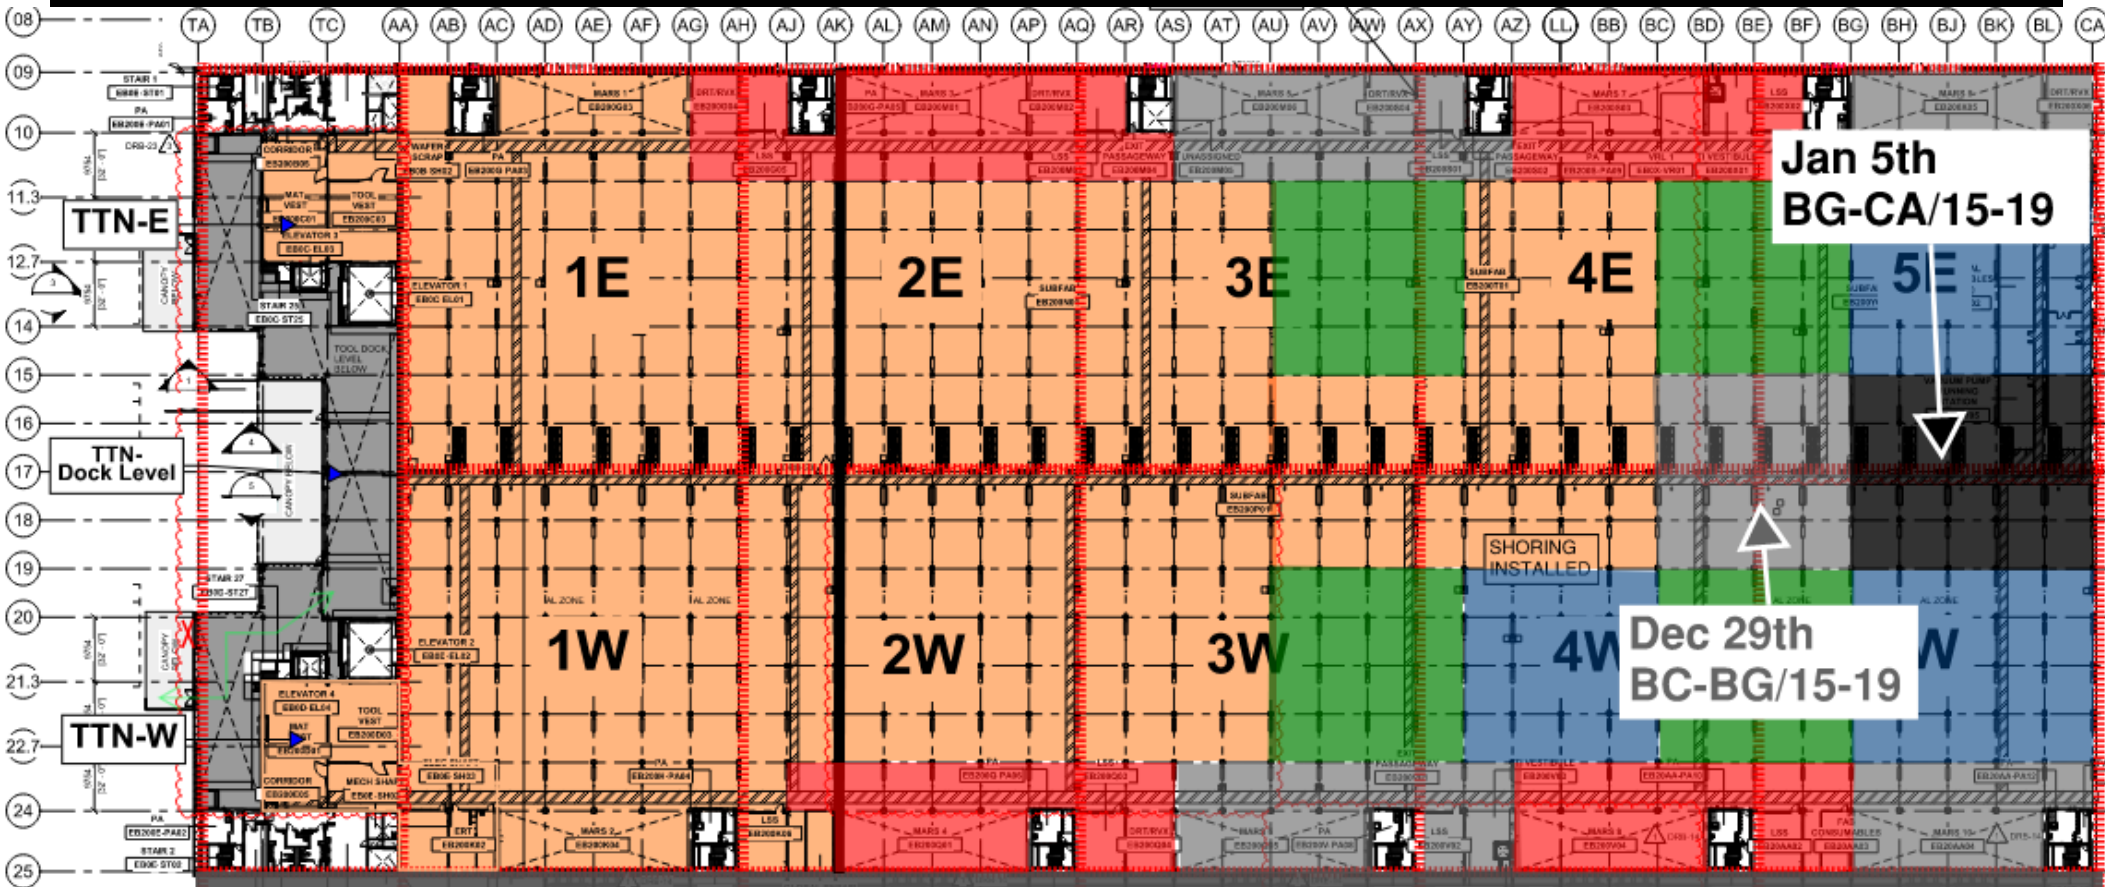


BCT Pressure Test Today


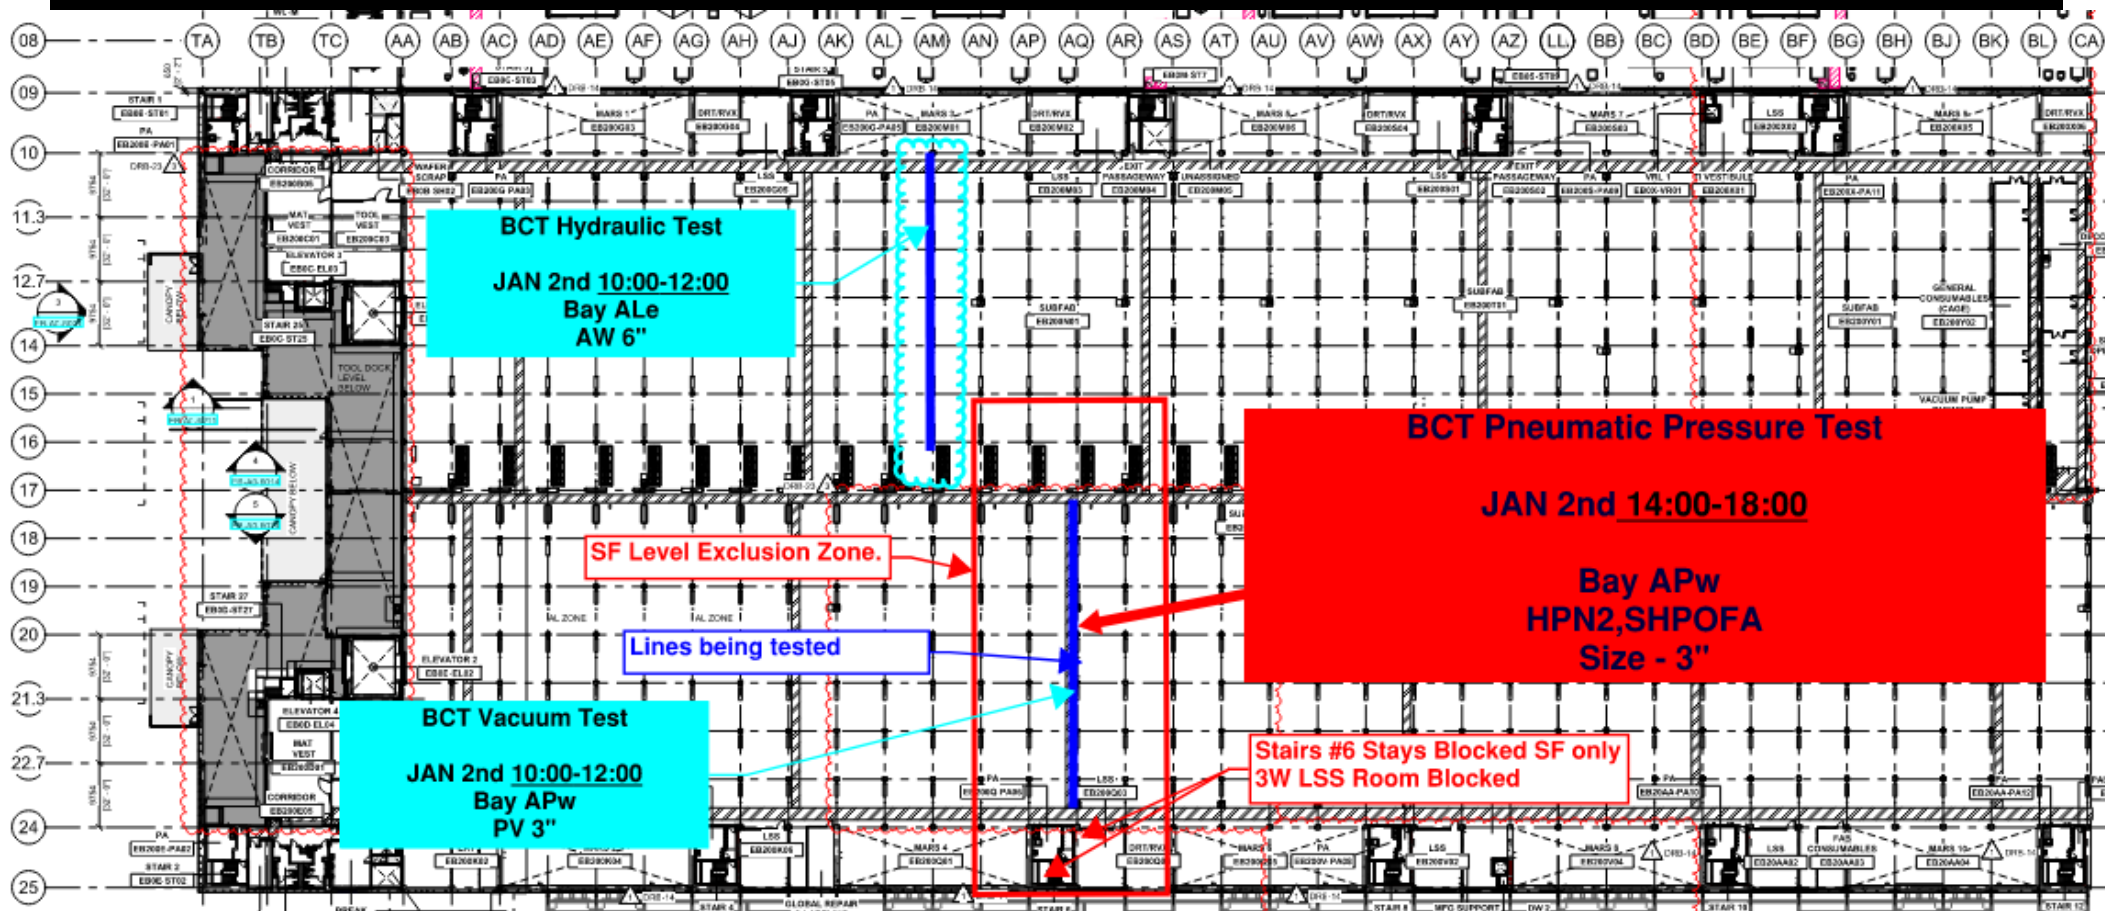



BCT Pressure Test Tomorrow

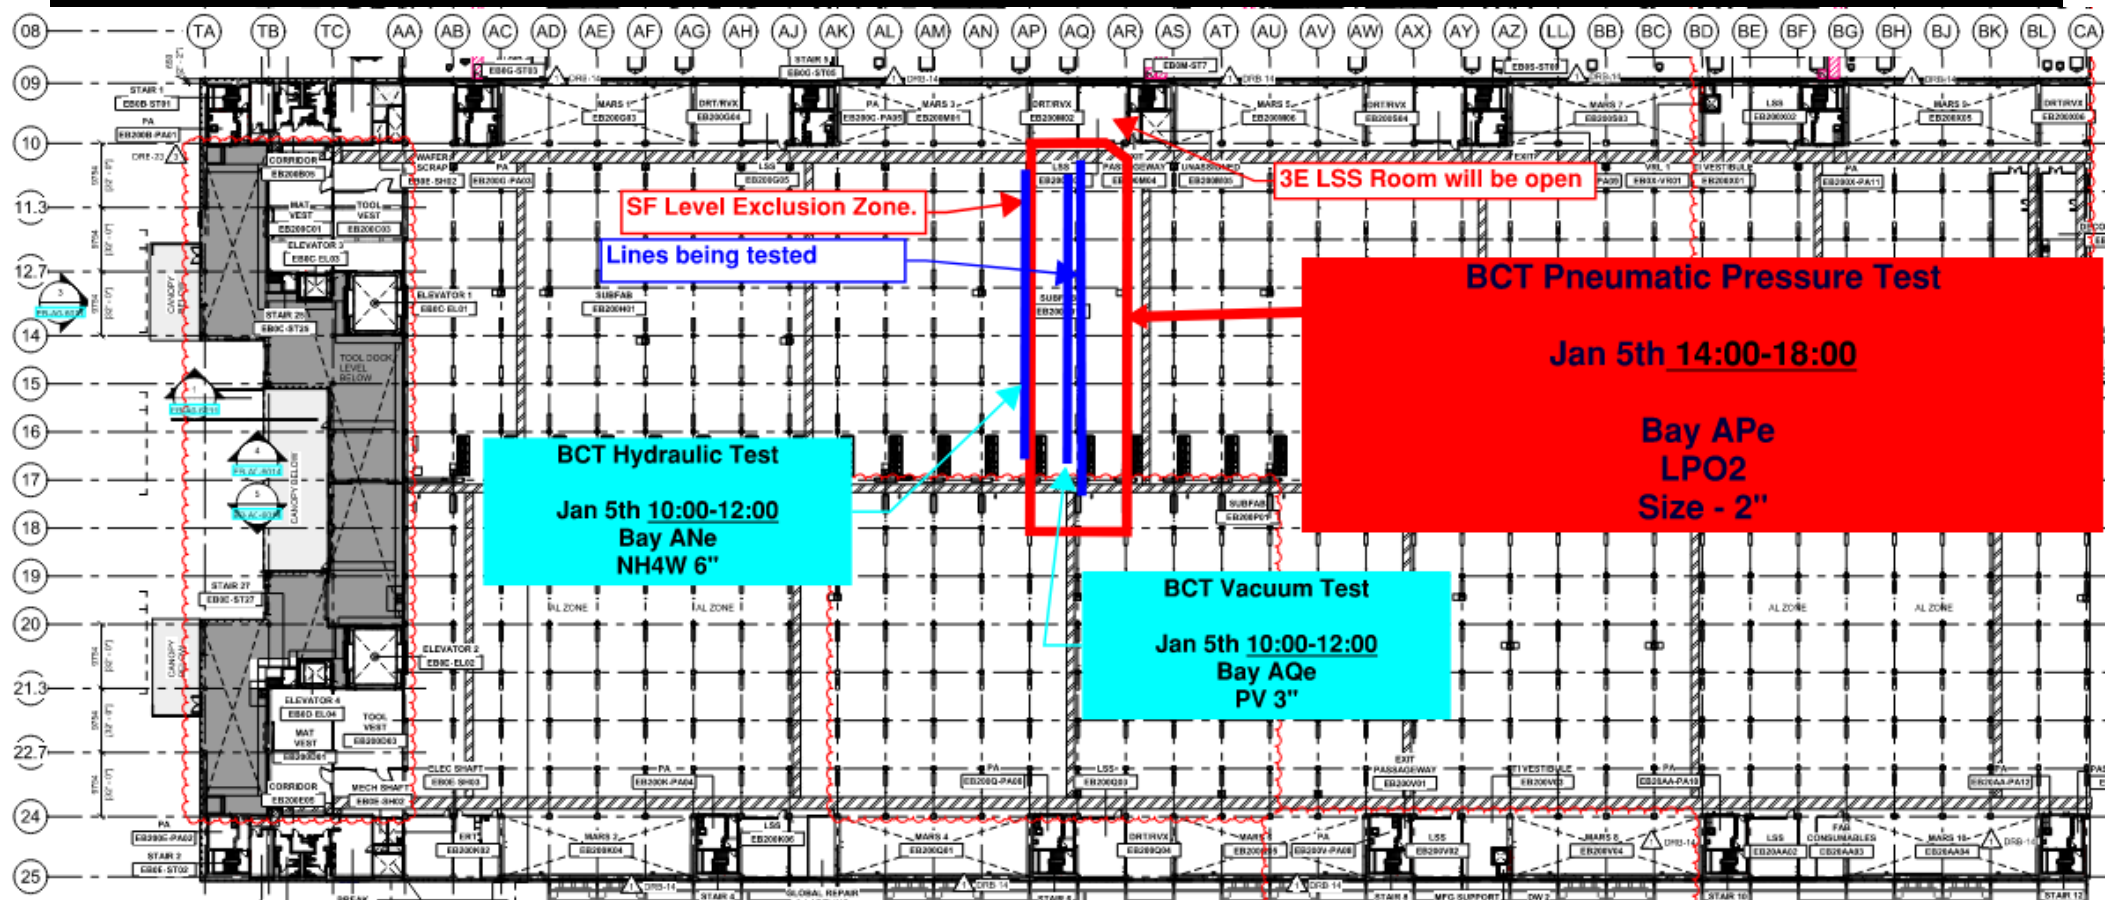



SUBFAB BUILDOUT MOD 2

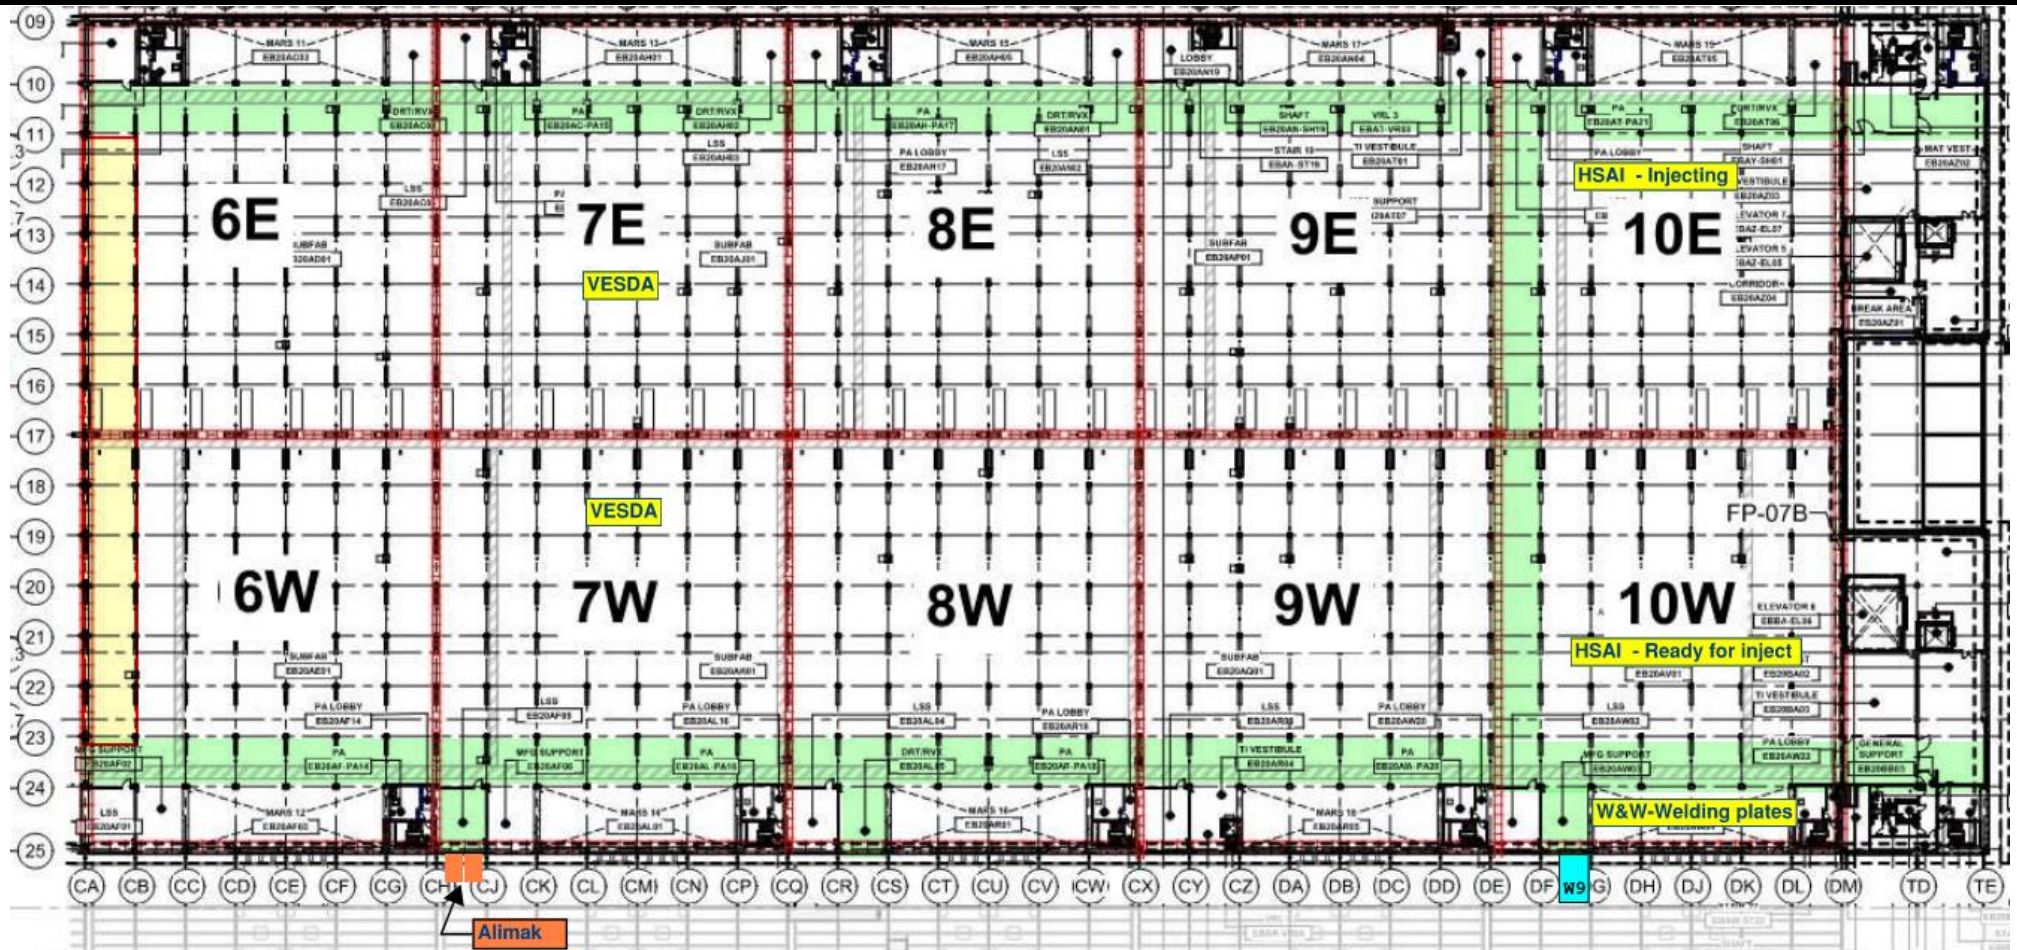

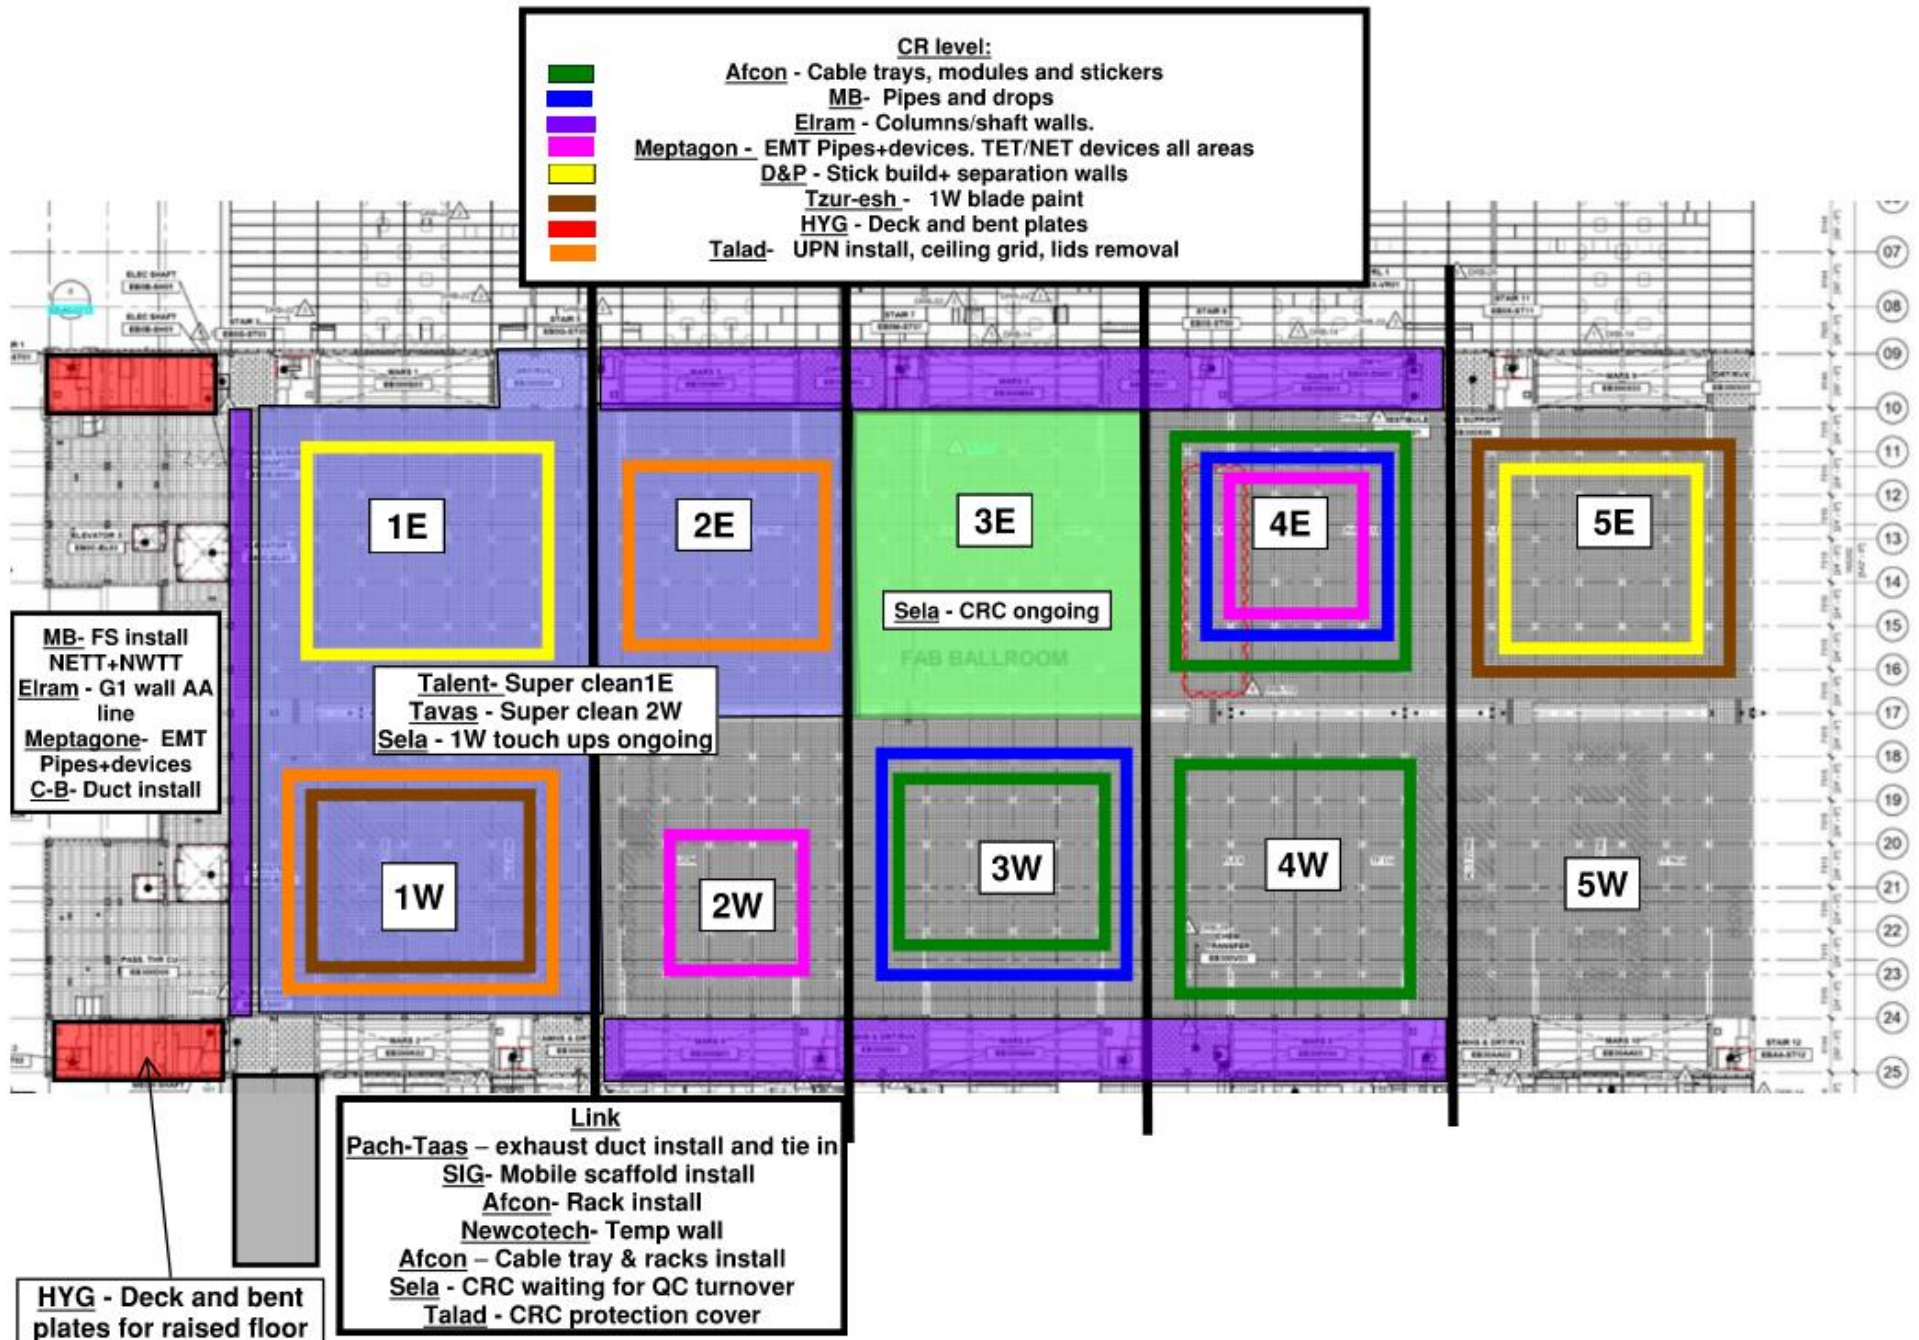

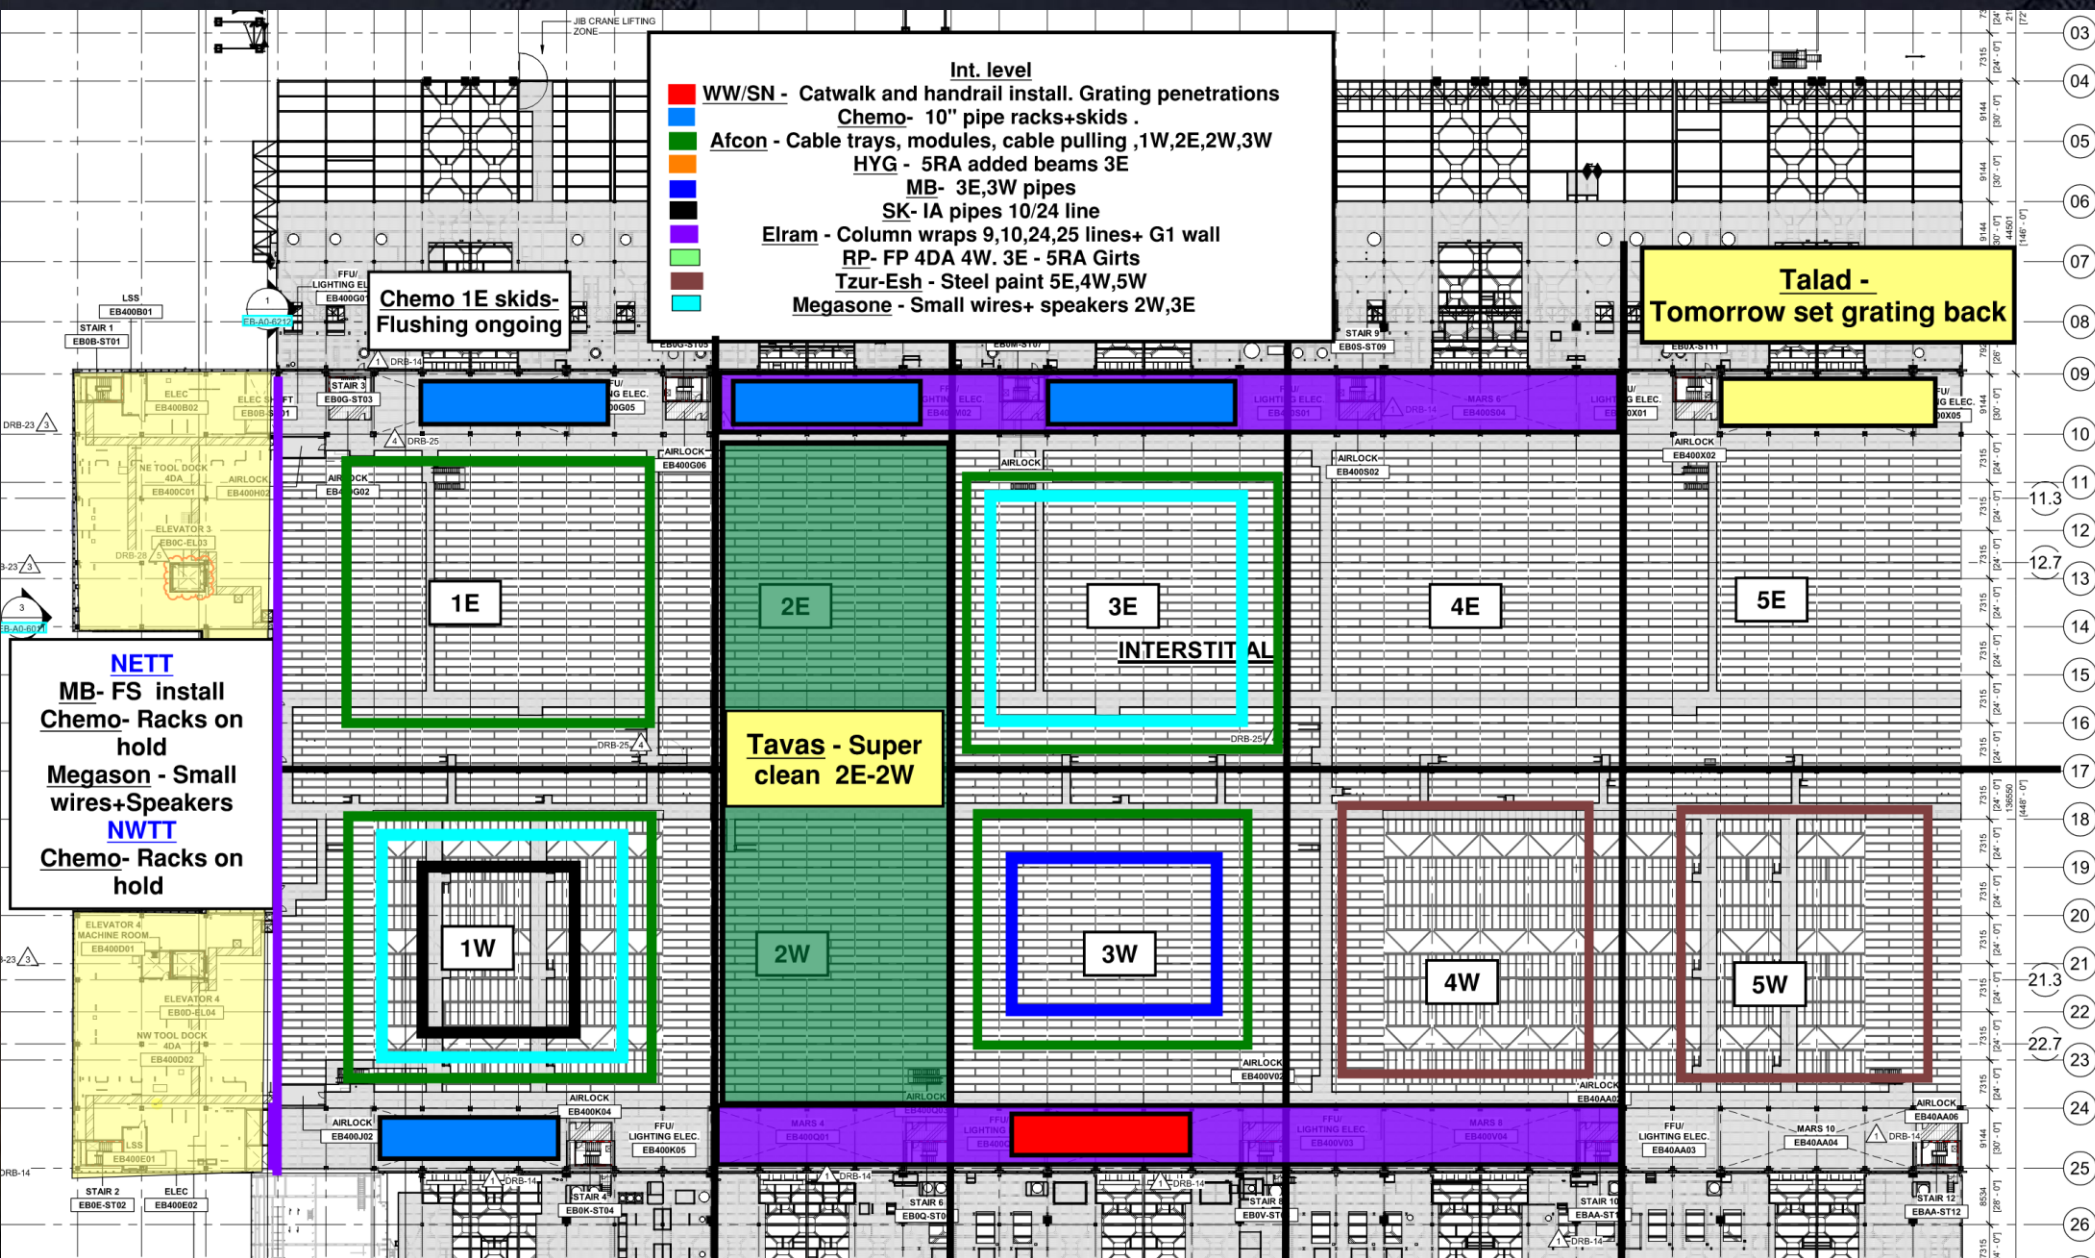

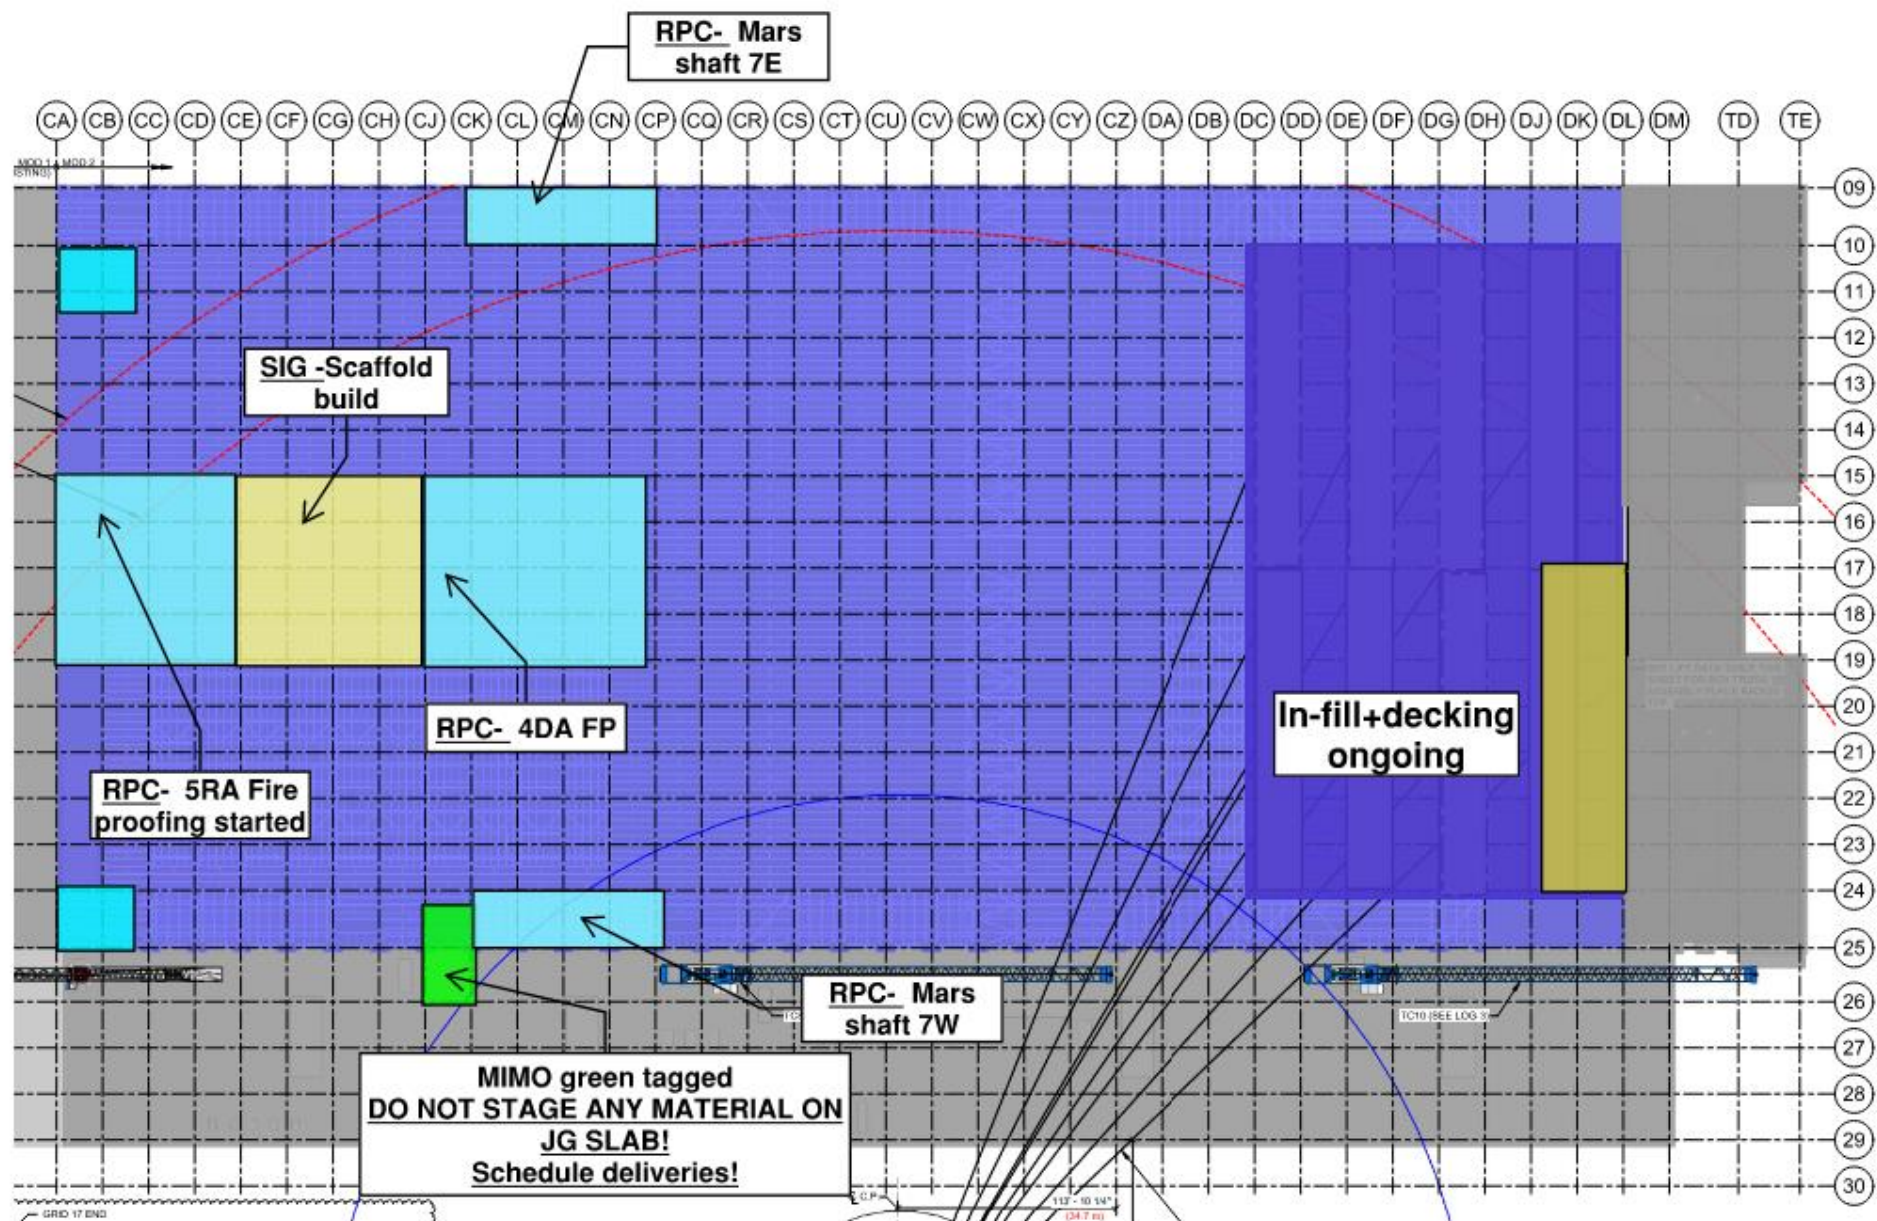

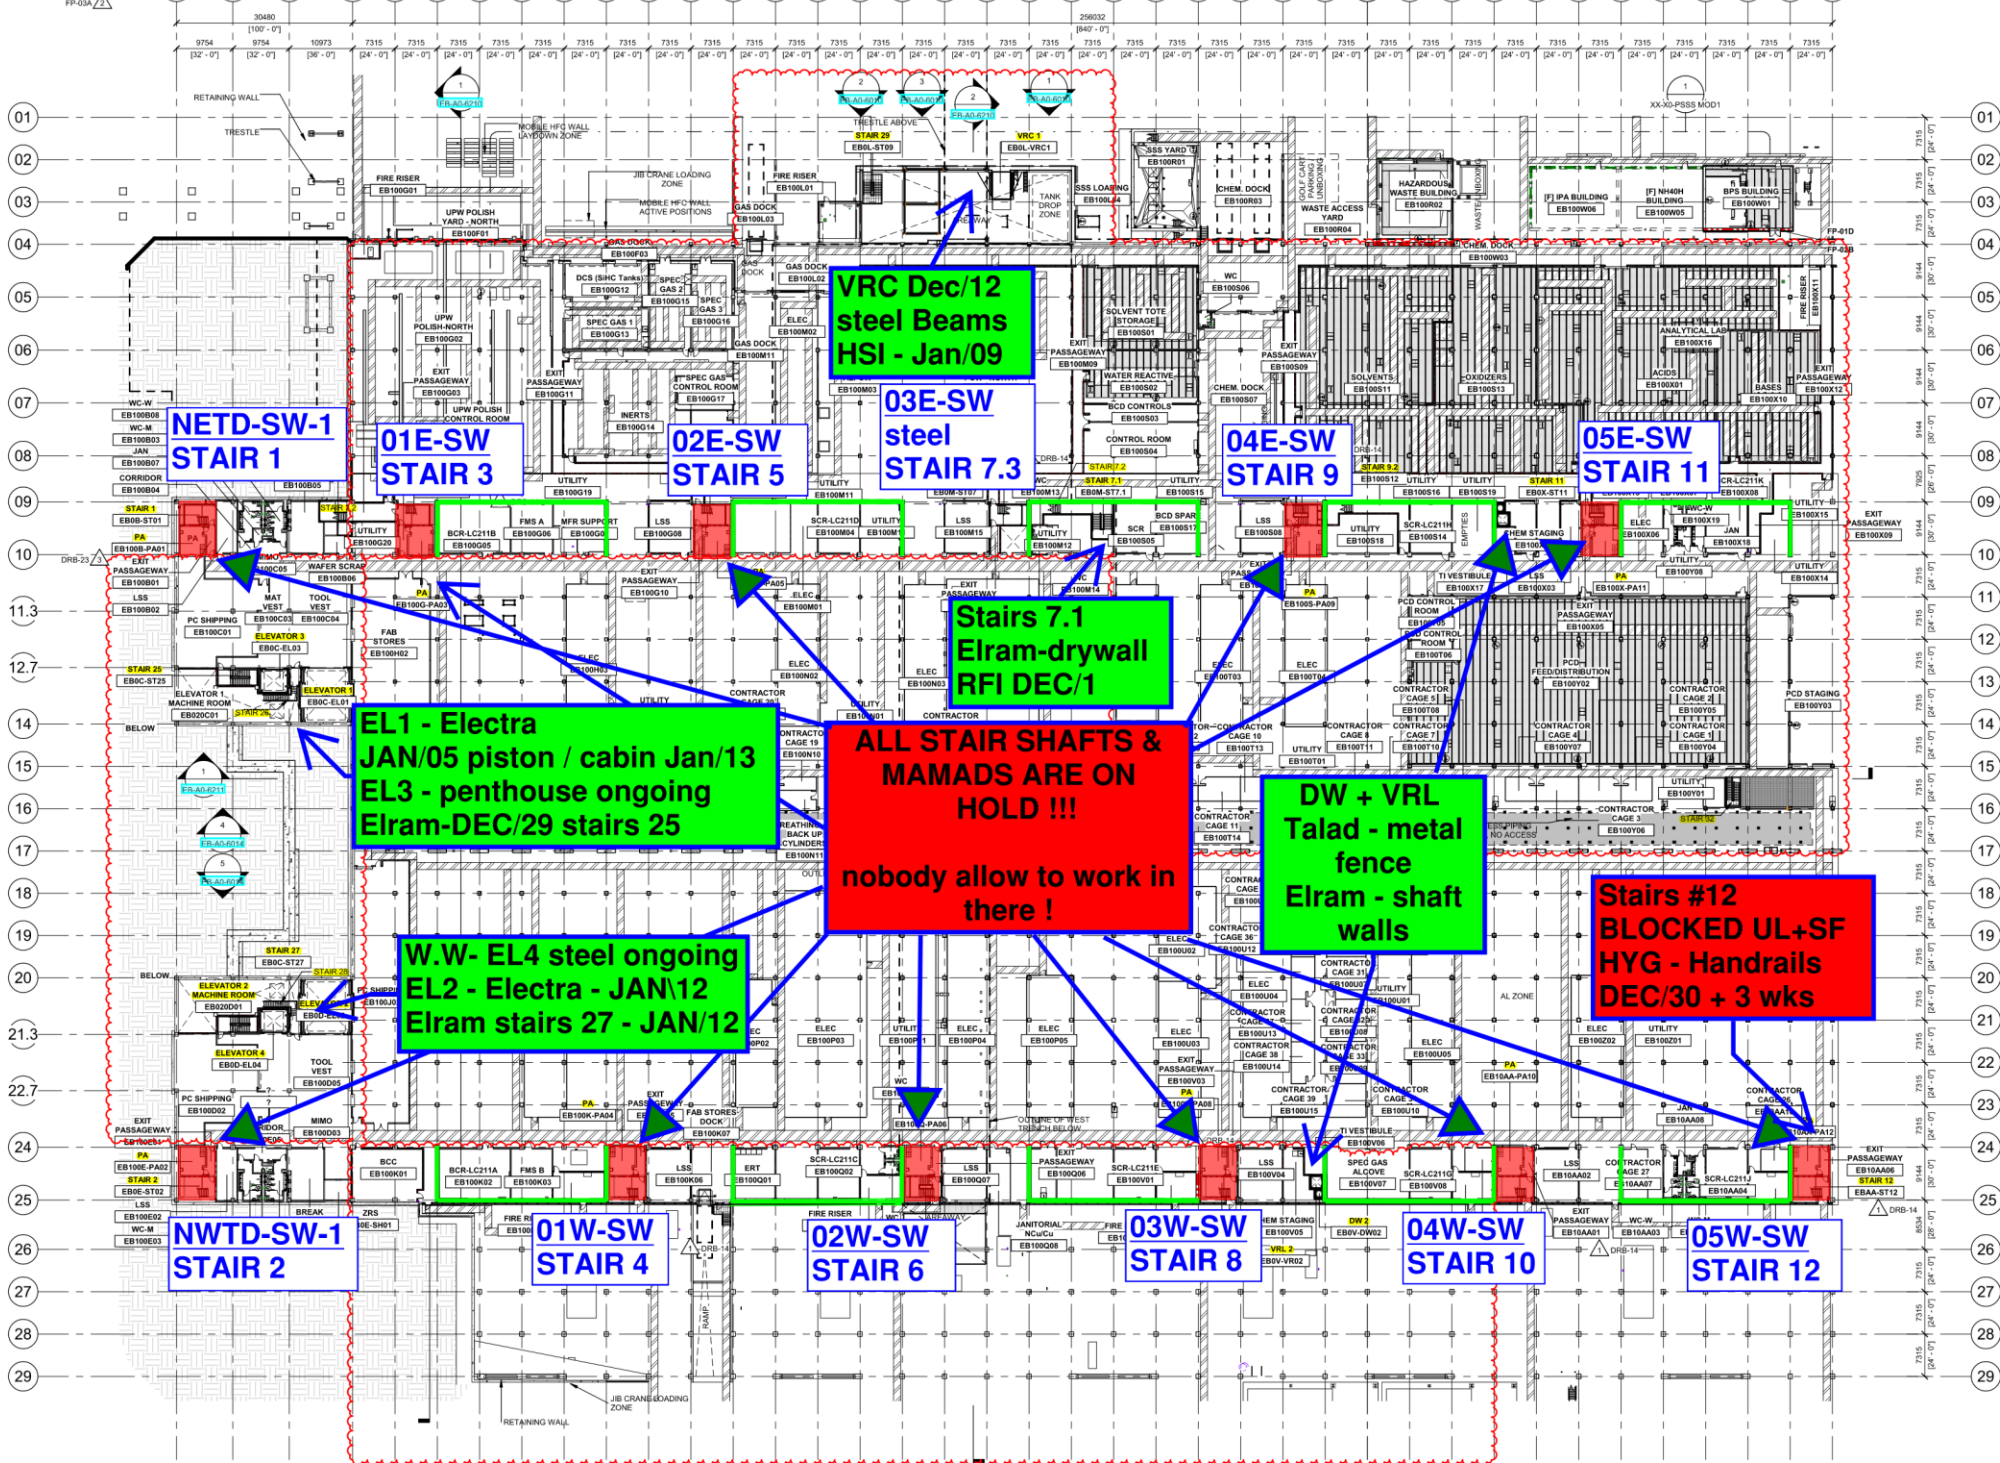

Siding - West FAB - JYG


BLOWDOWN 30%

	TA	TB	TC	TD	TE	TF	TG	TH	TI	TJ	TK	TL	TM	TN	TO	TP	TQ	TR	TS	TT	TU	TV	TW	TX	TY	TZ	TA	TB	TC	TD	TE	TF	TG	TH	TI	TJ	TK	TL	TM					
	1001 / 1002			601 / 602			611 / 612				621 / 622			631 / 632						641 / 642			651 / 652			611 / 612			621 / 622			631 / 632						641 / 642			651 / 652			
Total	28	28	28	15	15	31	31	31	31	31	31	31	36	31	31	31	31	31	31	31	31	31	31	31	31	31	25	25	25	31	31	31	31	31	31	31	31	31						
Inverted	28	28	27	15	15	31	31	31	31	31	31	31	36	28	28	28	28	28	28	28	28	28	28	28	28	28	25	25	25	31	31	31	31	31	31	31	31	31						
X	100%	100%	96%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	90%	90%	90%	90%	90%	90%	90%	90%	90%	90%	90%	90%	90%	87%	87%	87%	100%	100%	100%	87%	87%	87%	61%	61%	61%	100%	90%	74%	74%	74%	61%
SRA														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
4DA														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
3FC														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
3FA														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
2SA 2F														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	
UL														0	0	0				0	0	0	0			0	0	0	0										0	0	0	0	0	


Siding - East FAB - PSSS


BLOWDOWN 30%

[illegible]

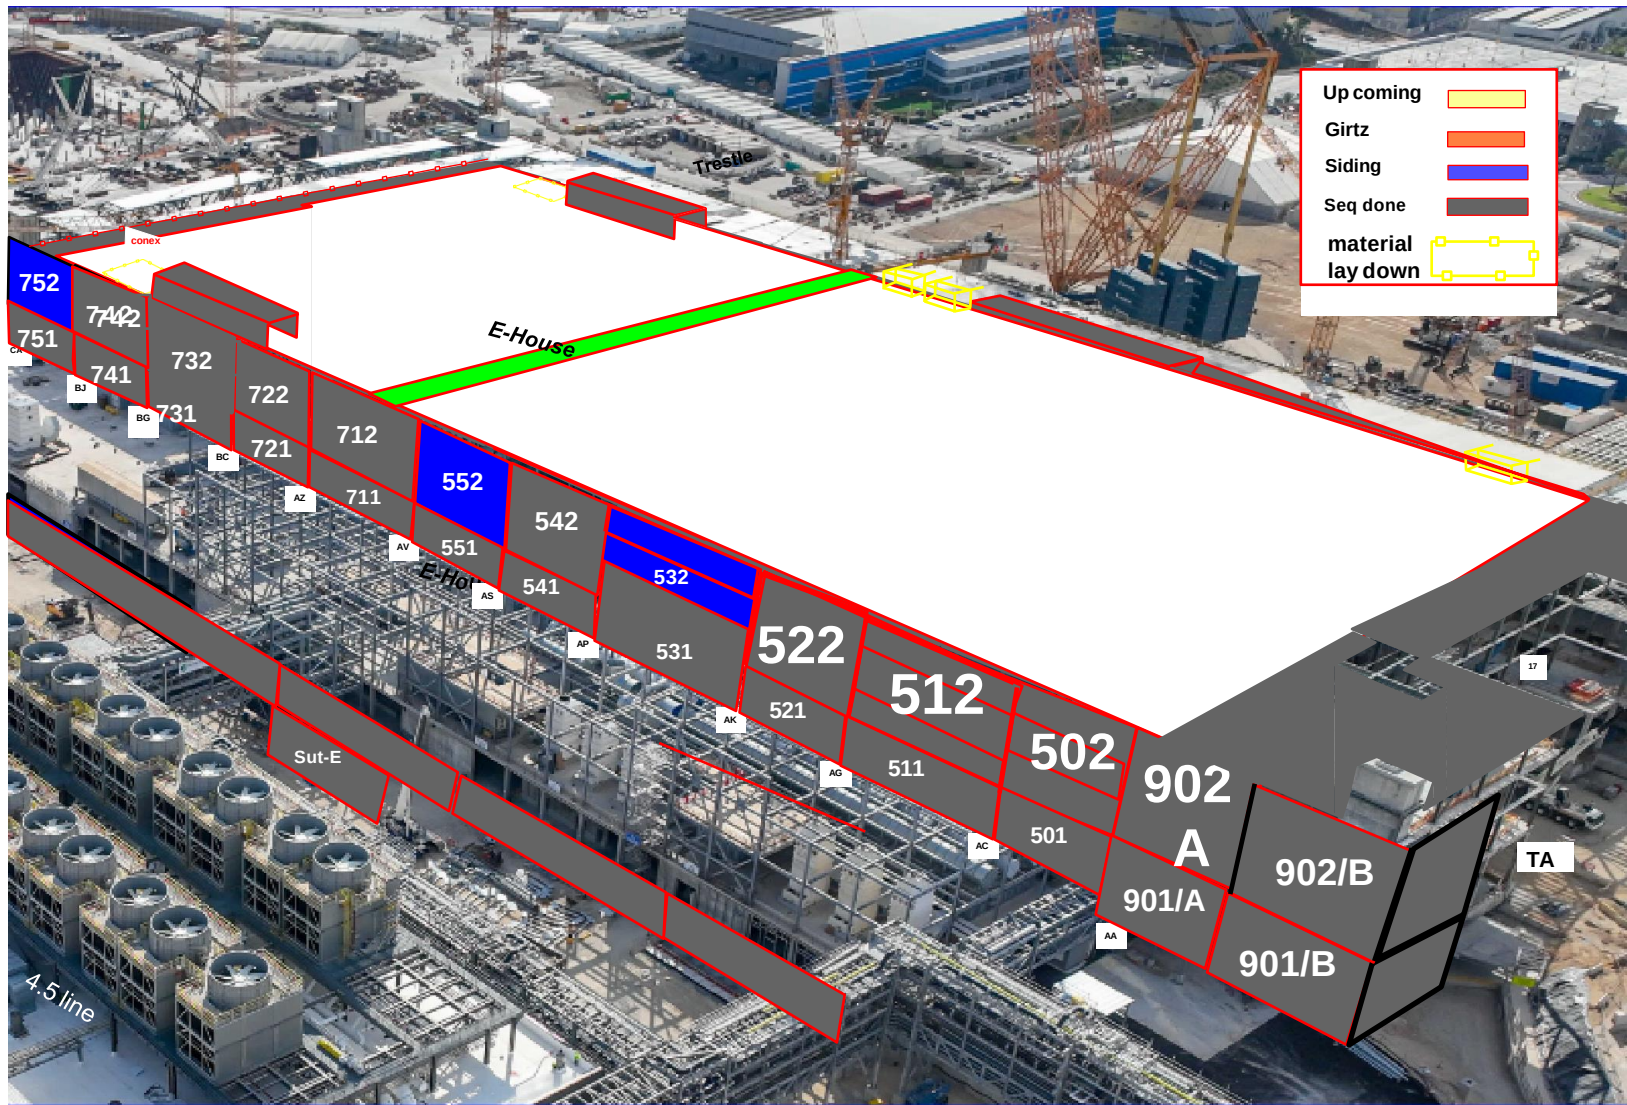

Walk path

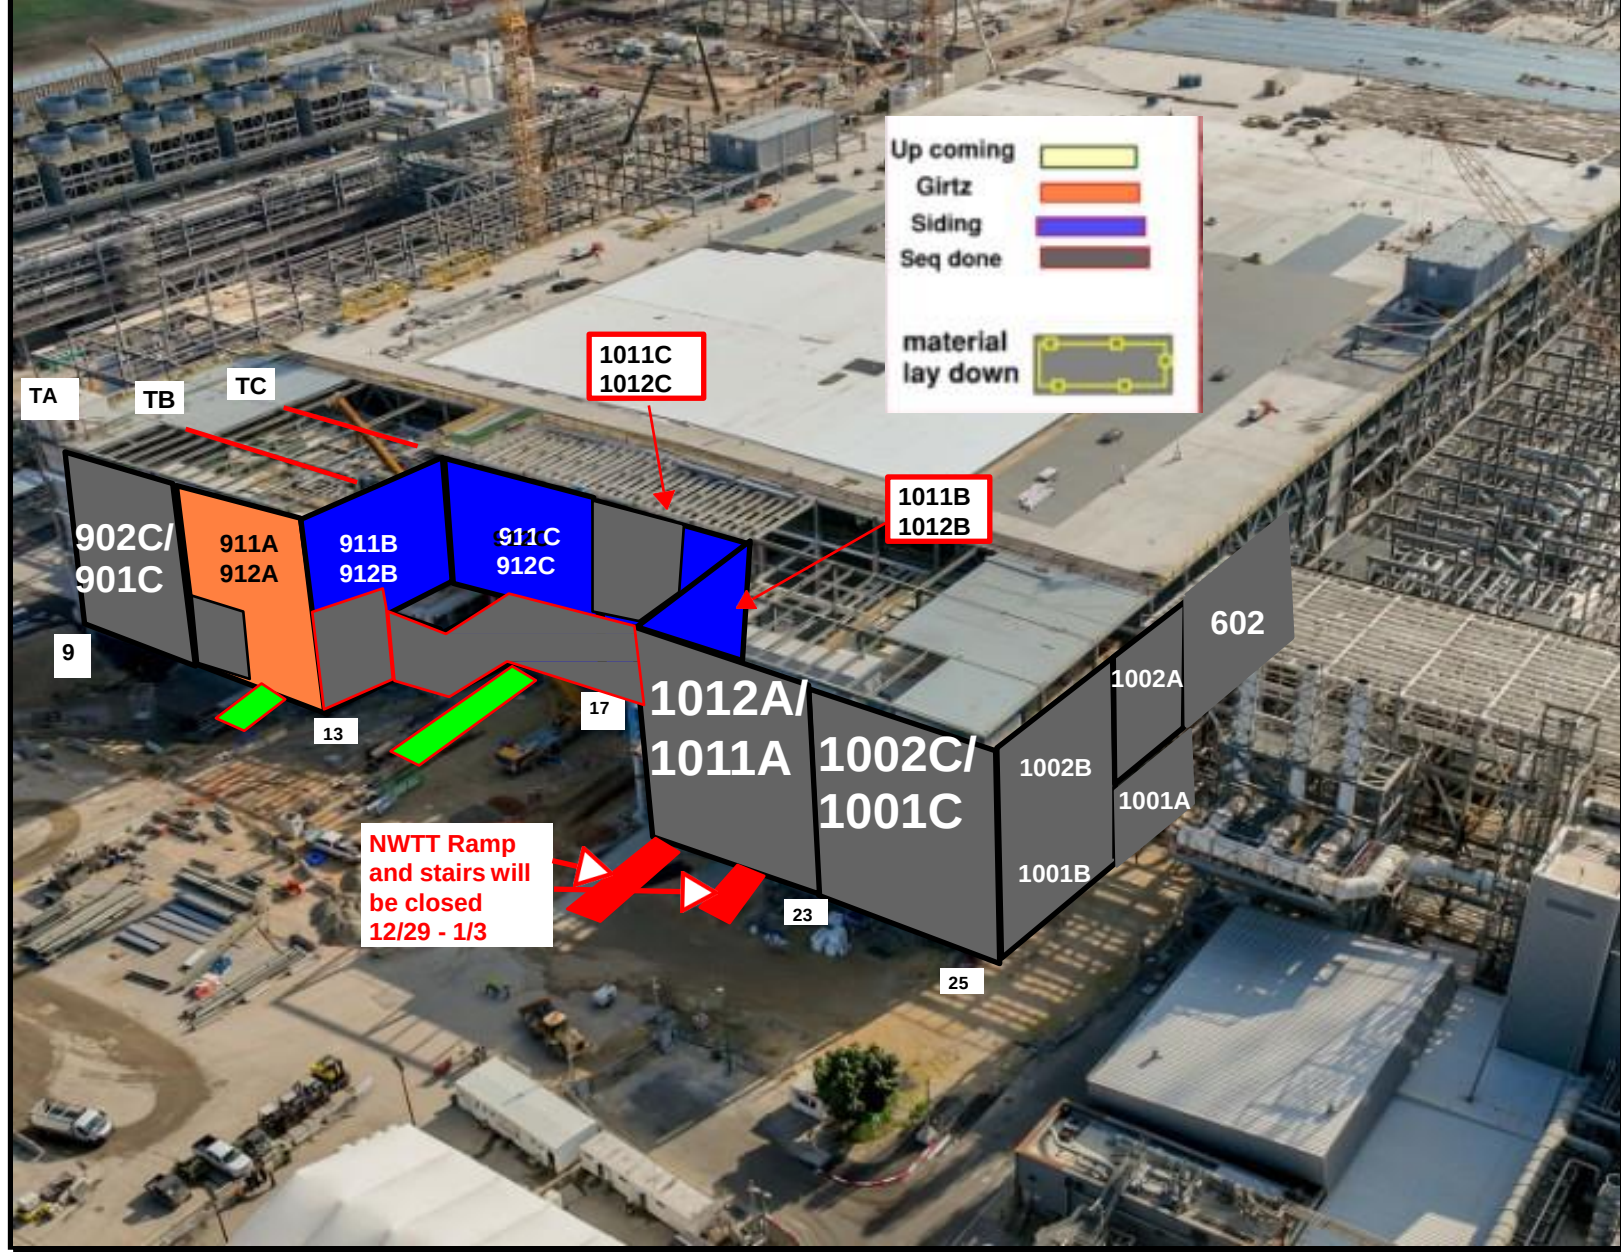

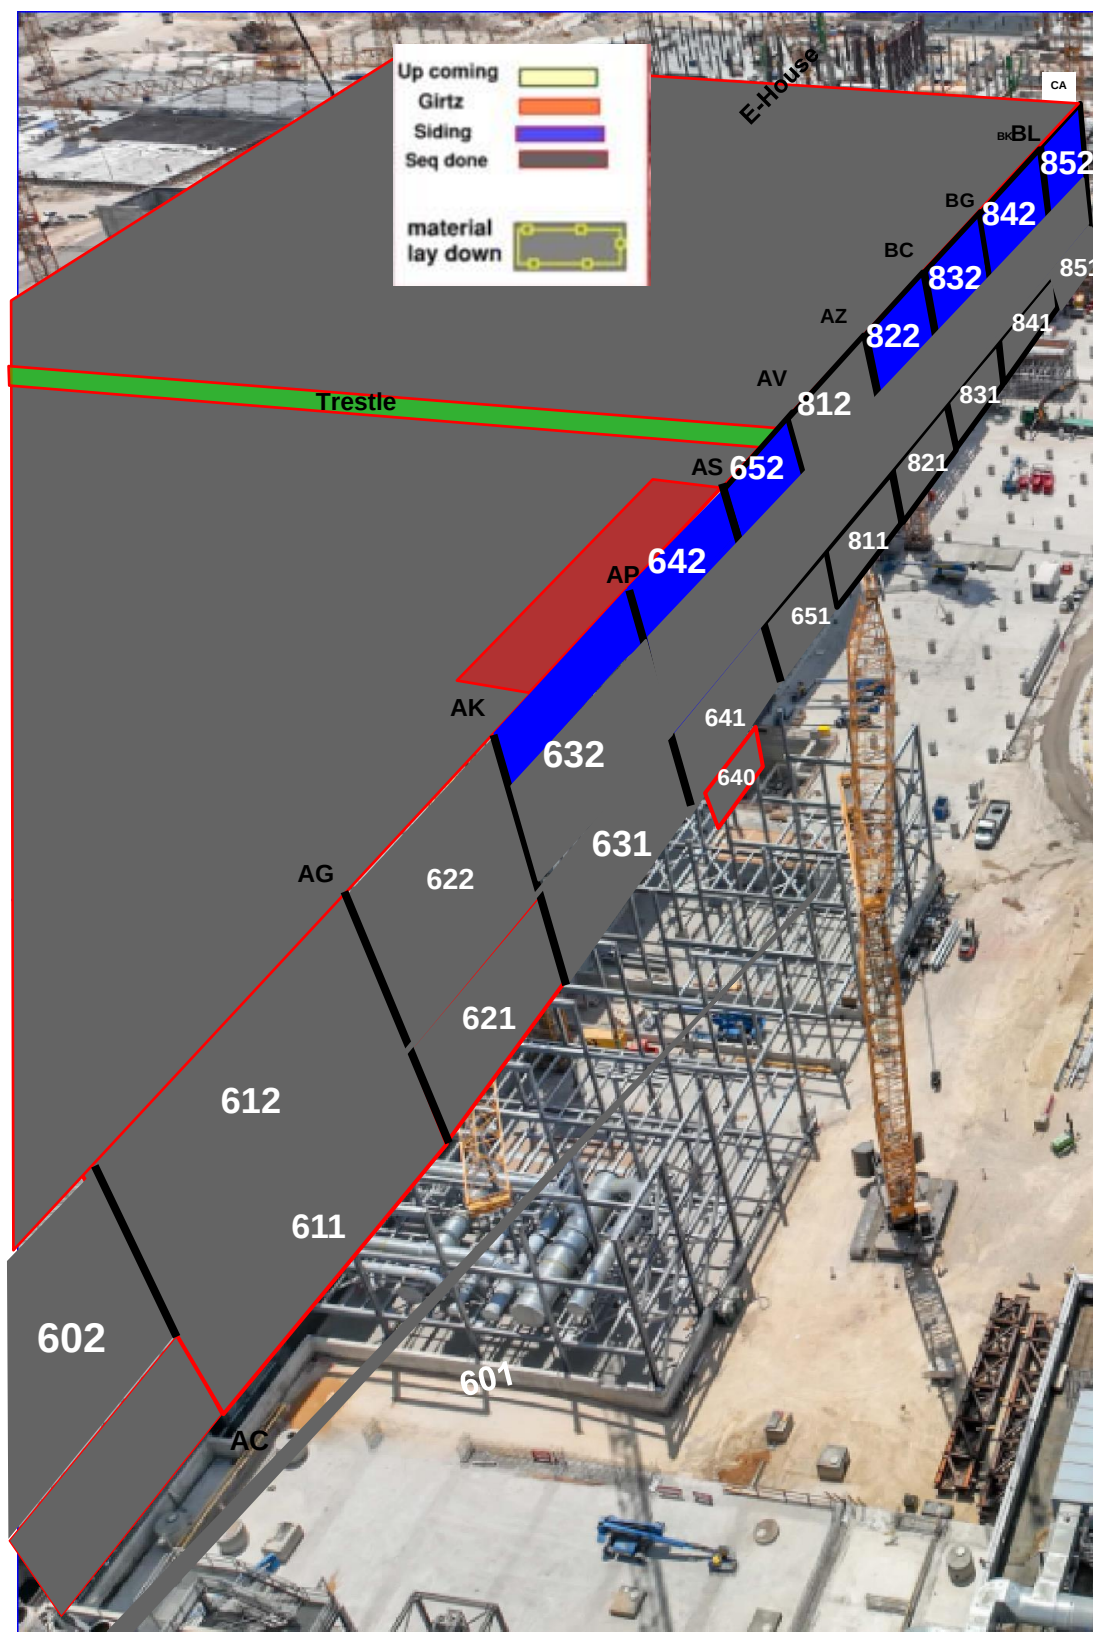


Jan 6th @ 4:00 AM
Jan 8th @ 4:00 AM

Condensed
Barricade
for Bolting.

PSSS.1

Utility Level
1YA

PSSS Roof
2SA

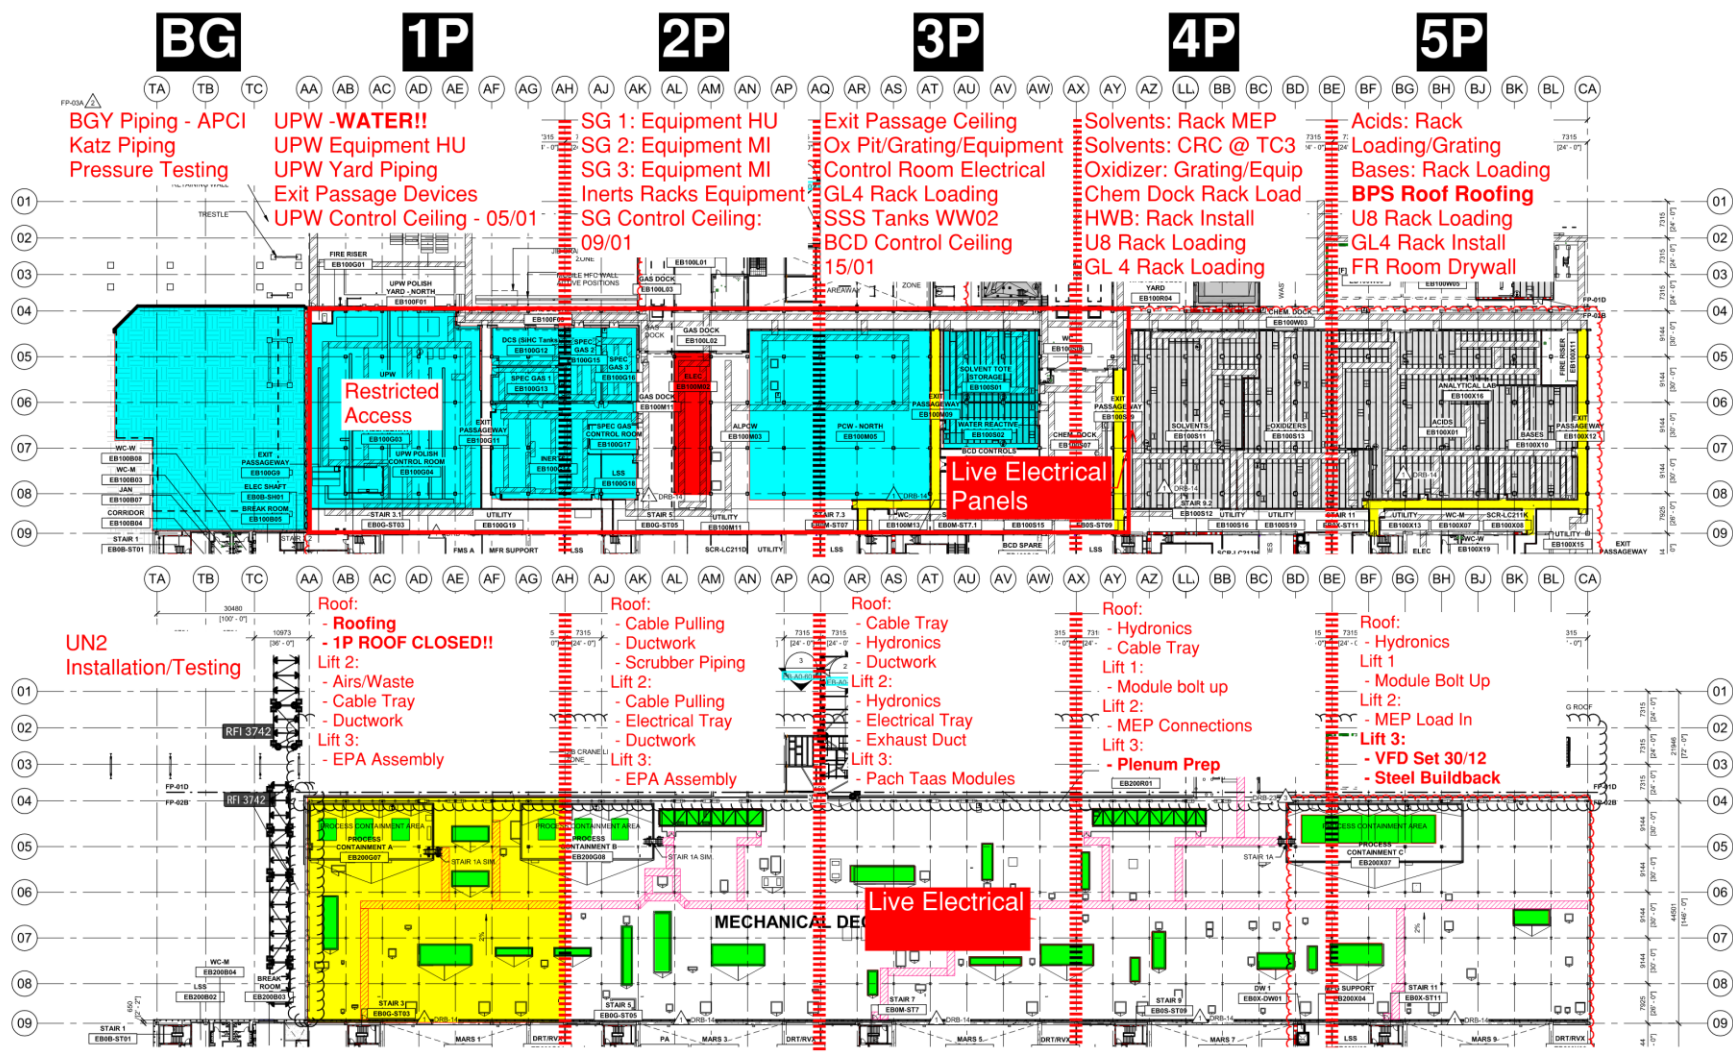

PSSS.2




PSSS Pressure Tests


5P

Utility Level 1YA

PSSS Roof 2SA

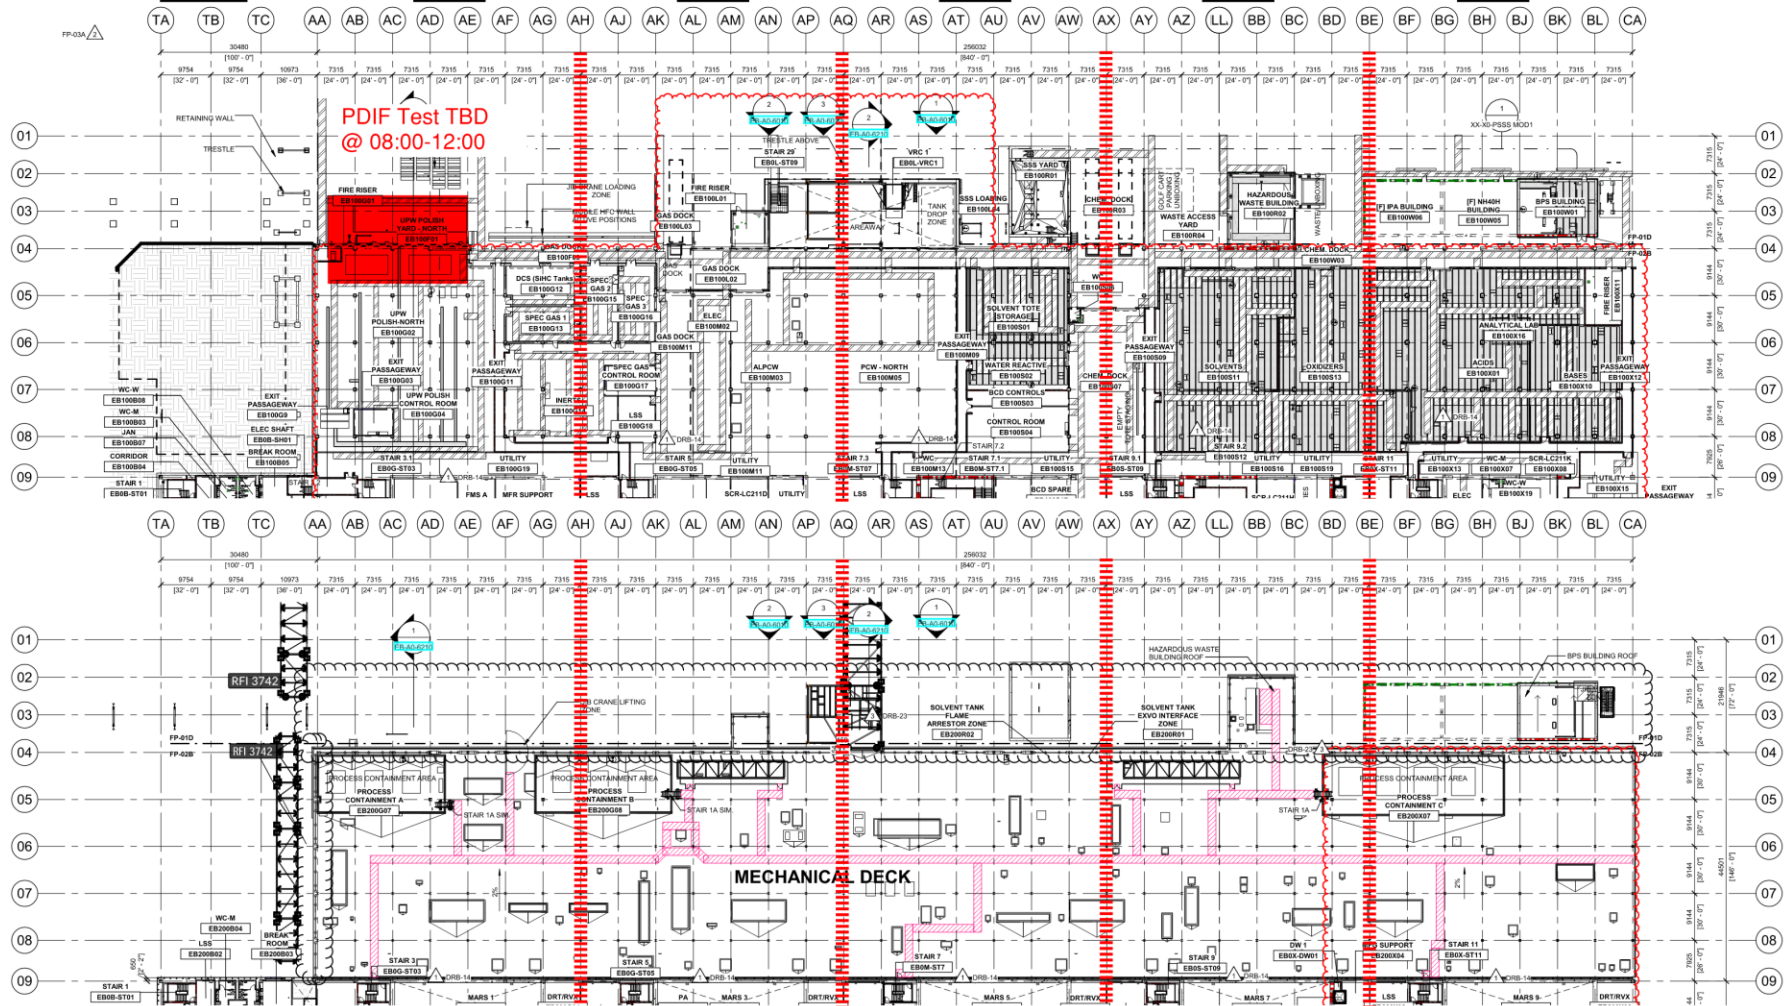


PSSS

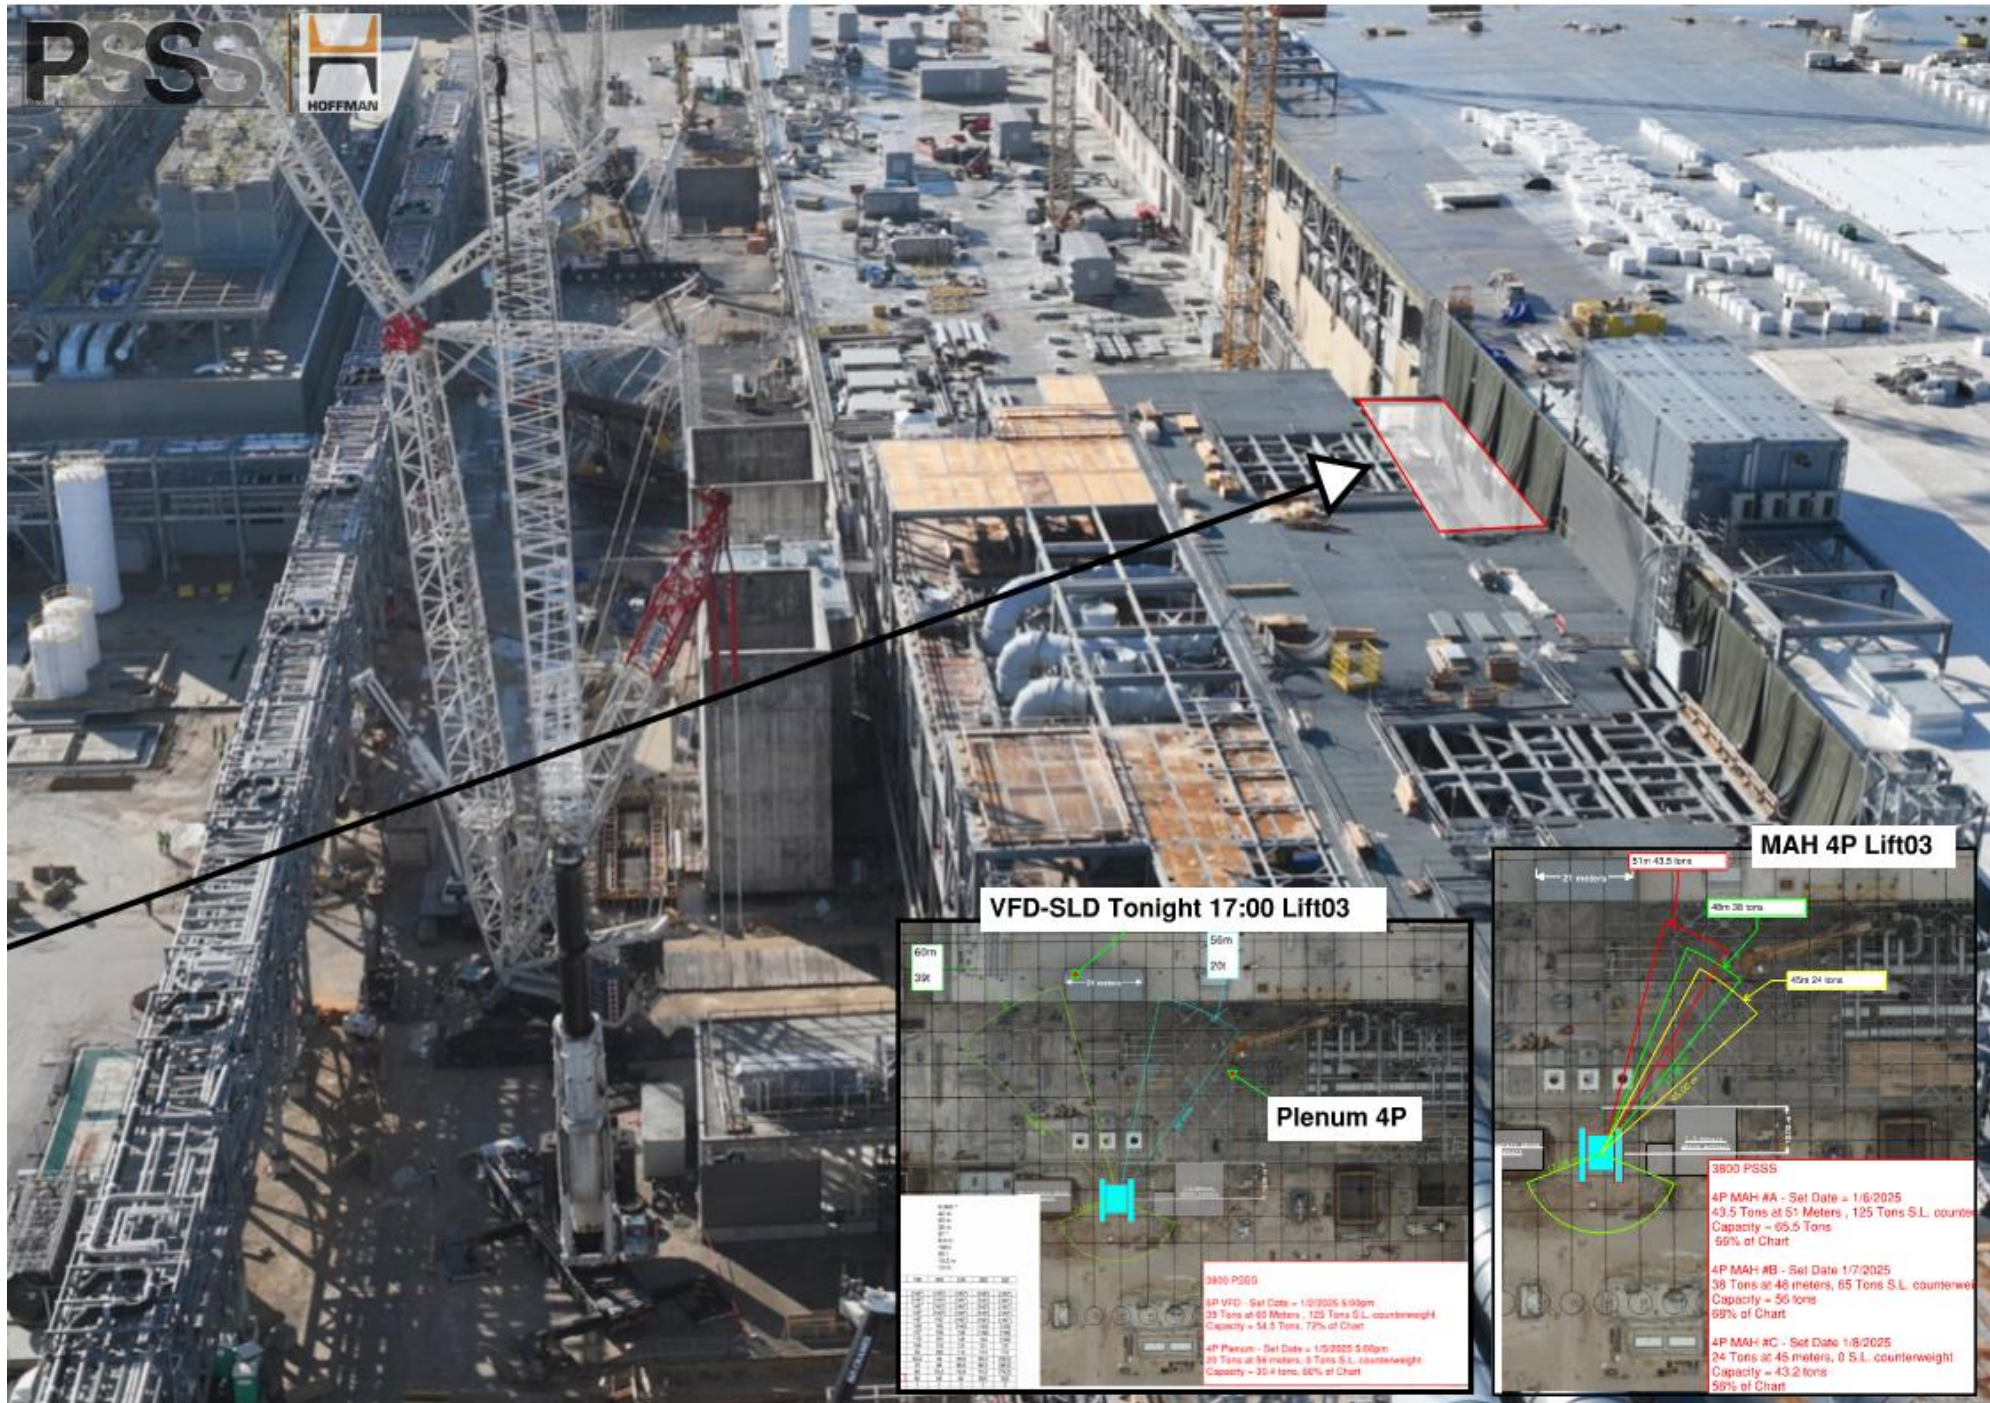

VFD-SLD Tonight 17:00 Lift03




MAH 4P Lift03

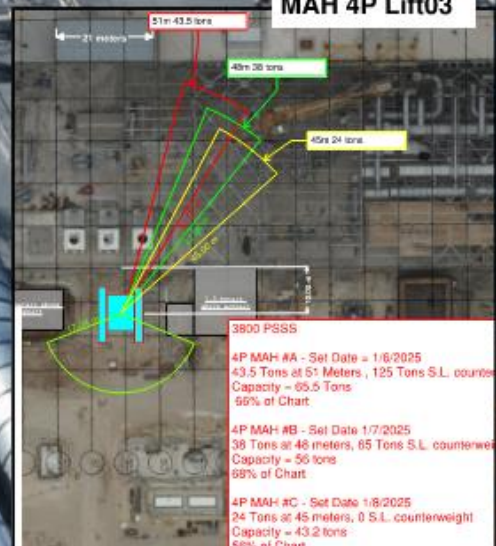




WJG 01J, 02J LIFT 2 & 3

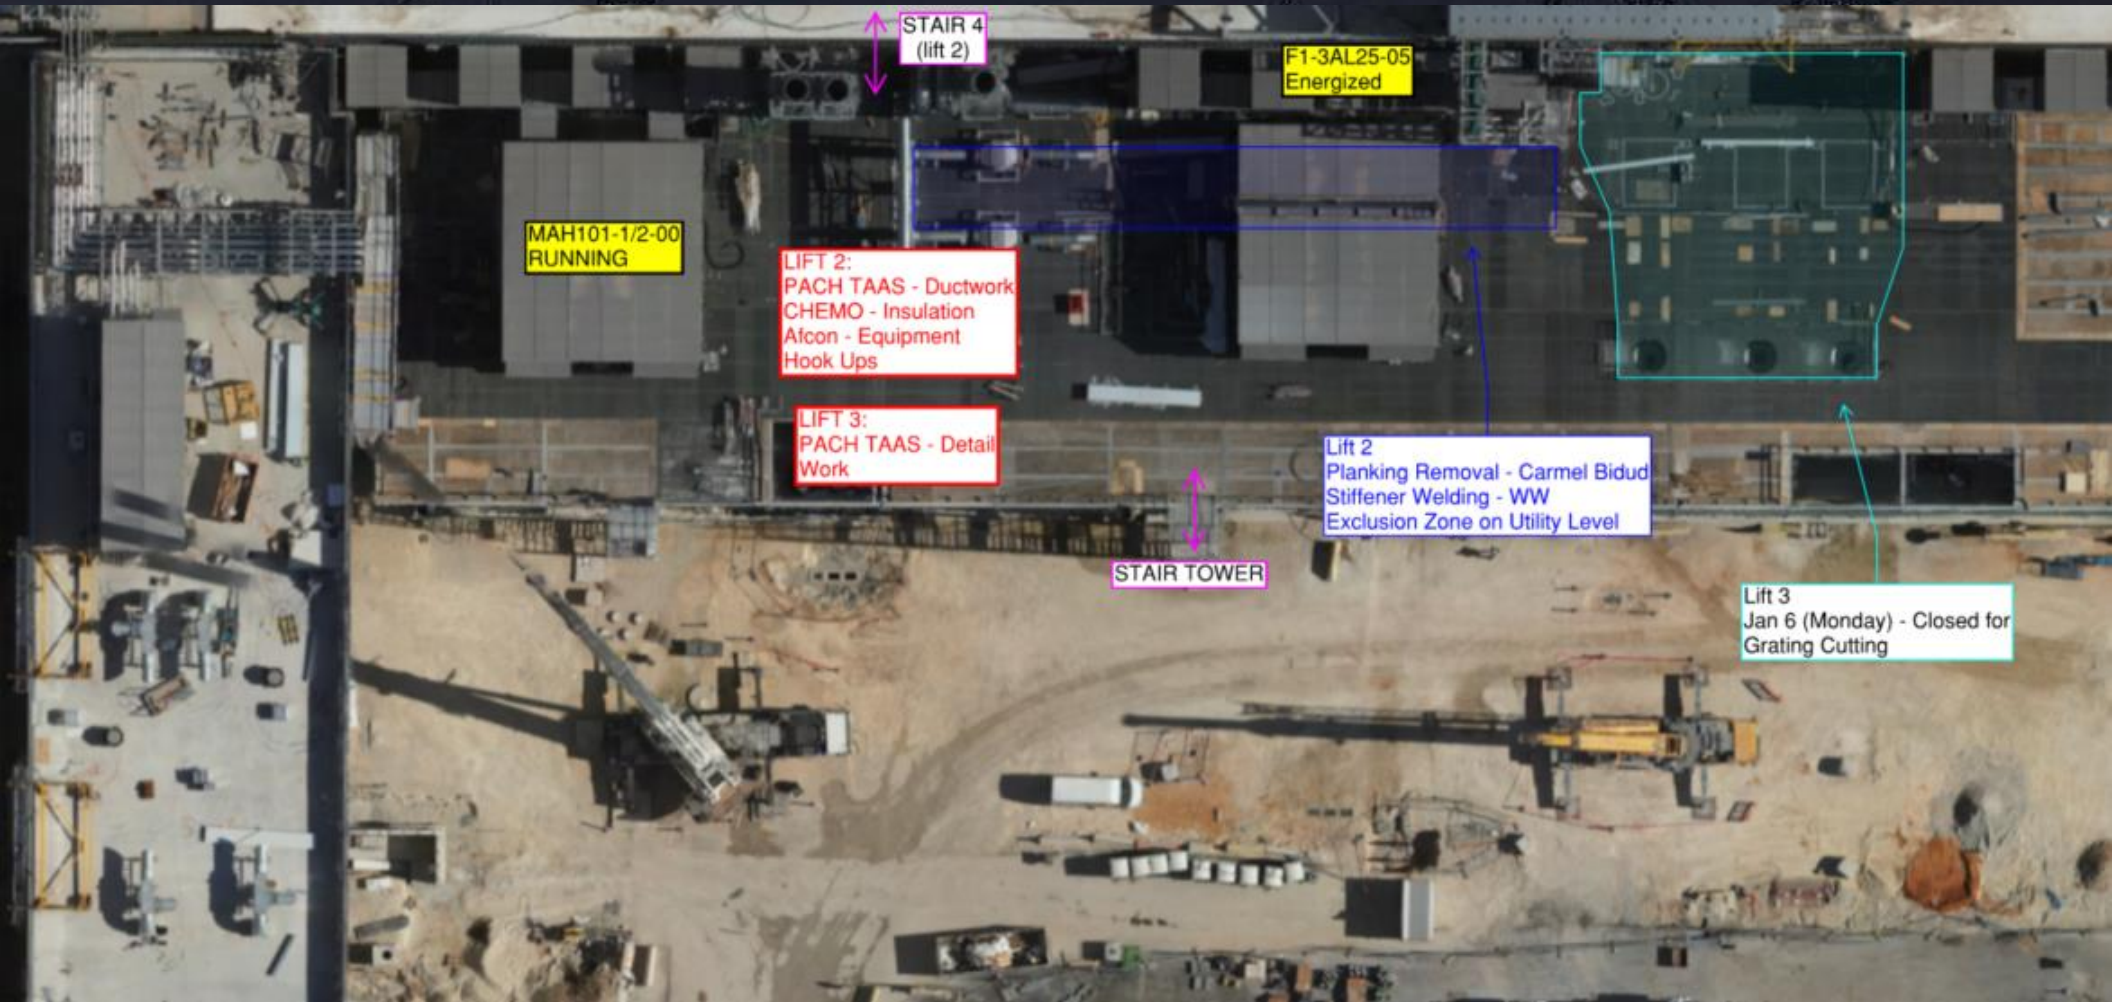




WJG 03J, 04J, 05J LIFT 2 & 3

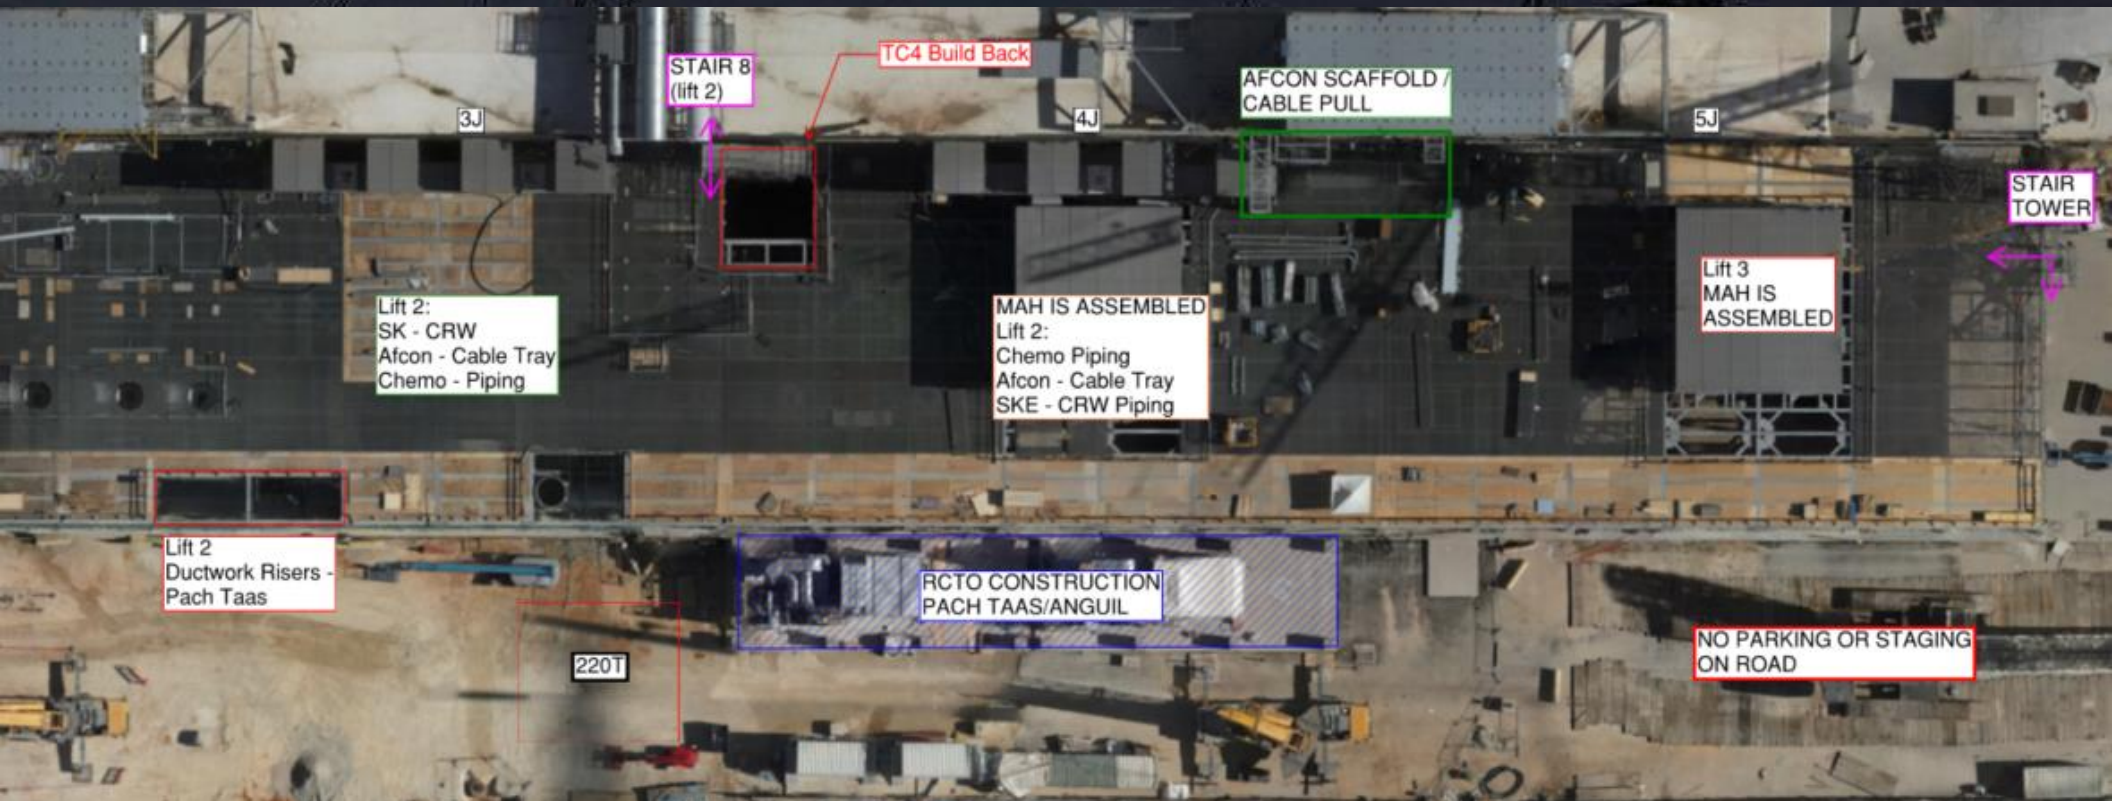



WJG UTILITY LEVEL BUILD OUT

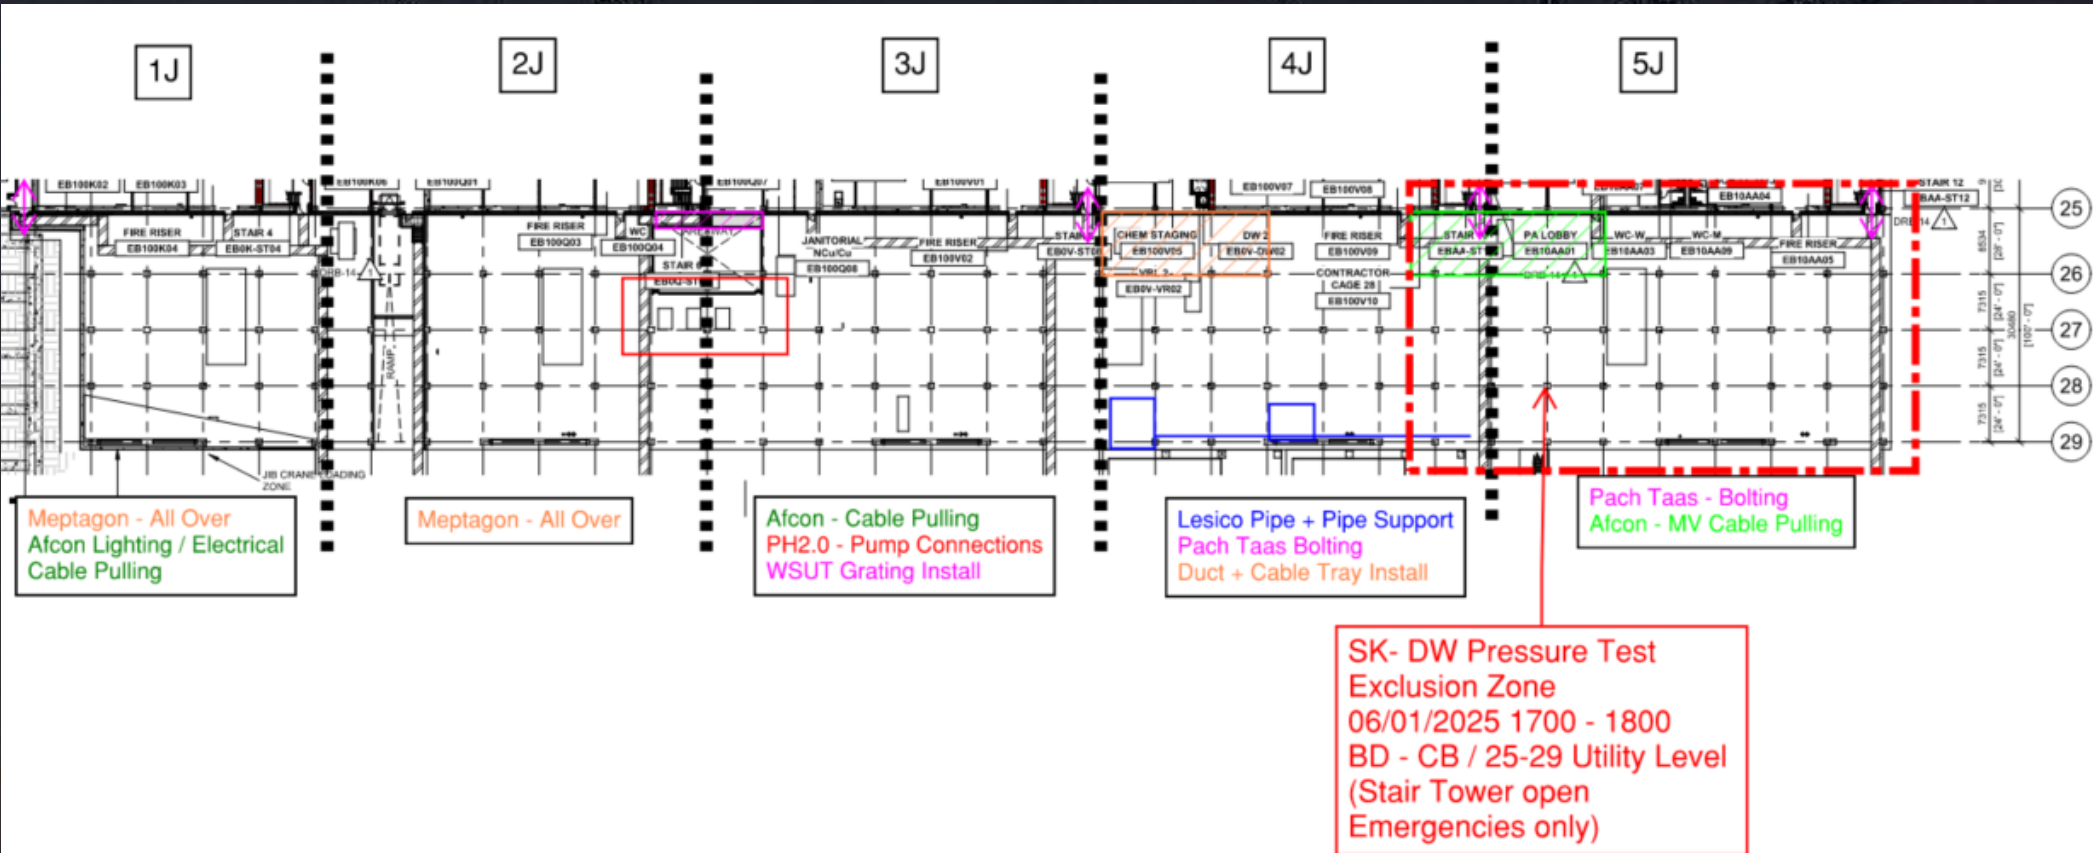


CUB 1 Ops ready 12 weeks to go Building Envelope
Trade Damage 40 documented Repairs Required







CUB 1

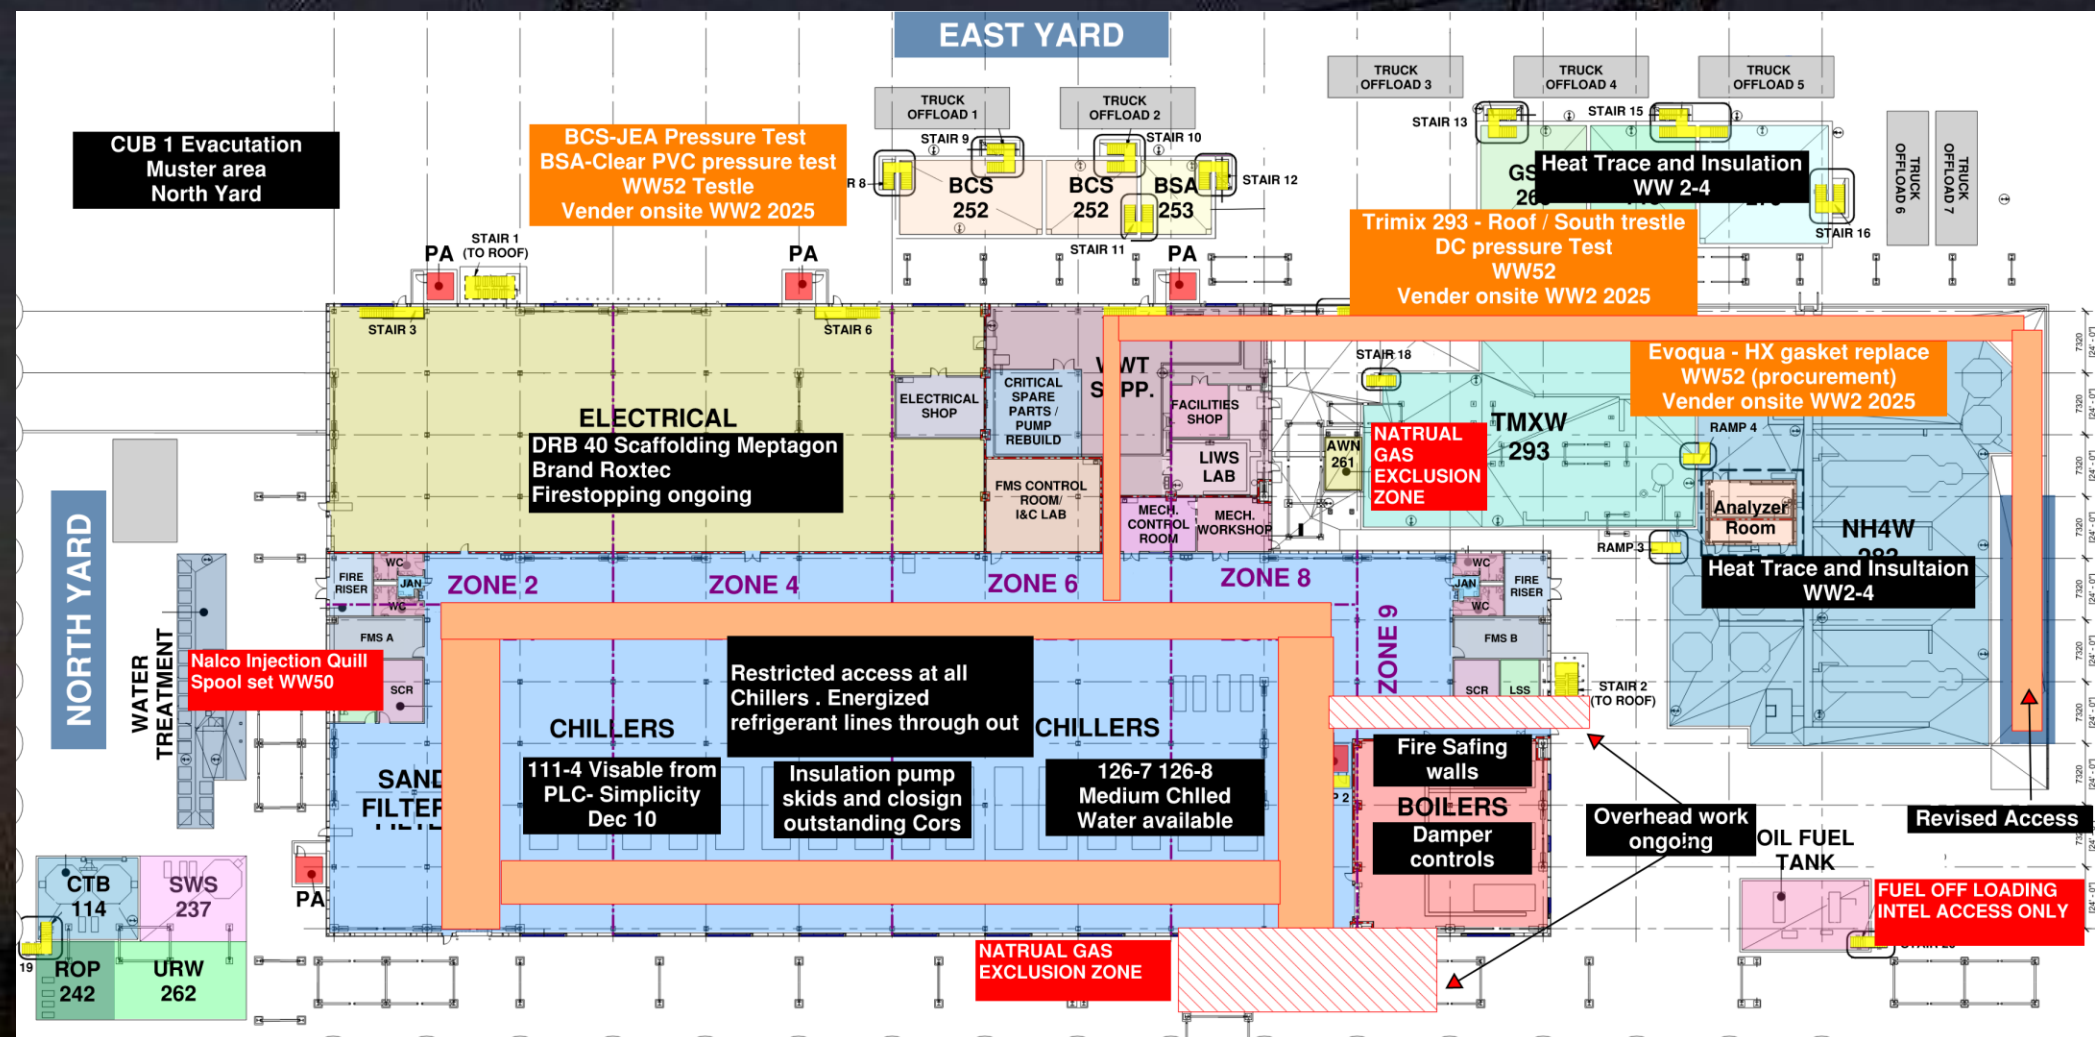

CUB 1 – EXTERIOR/ROOF

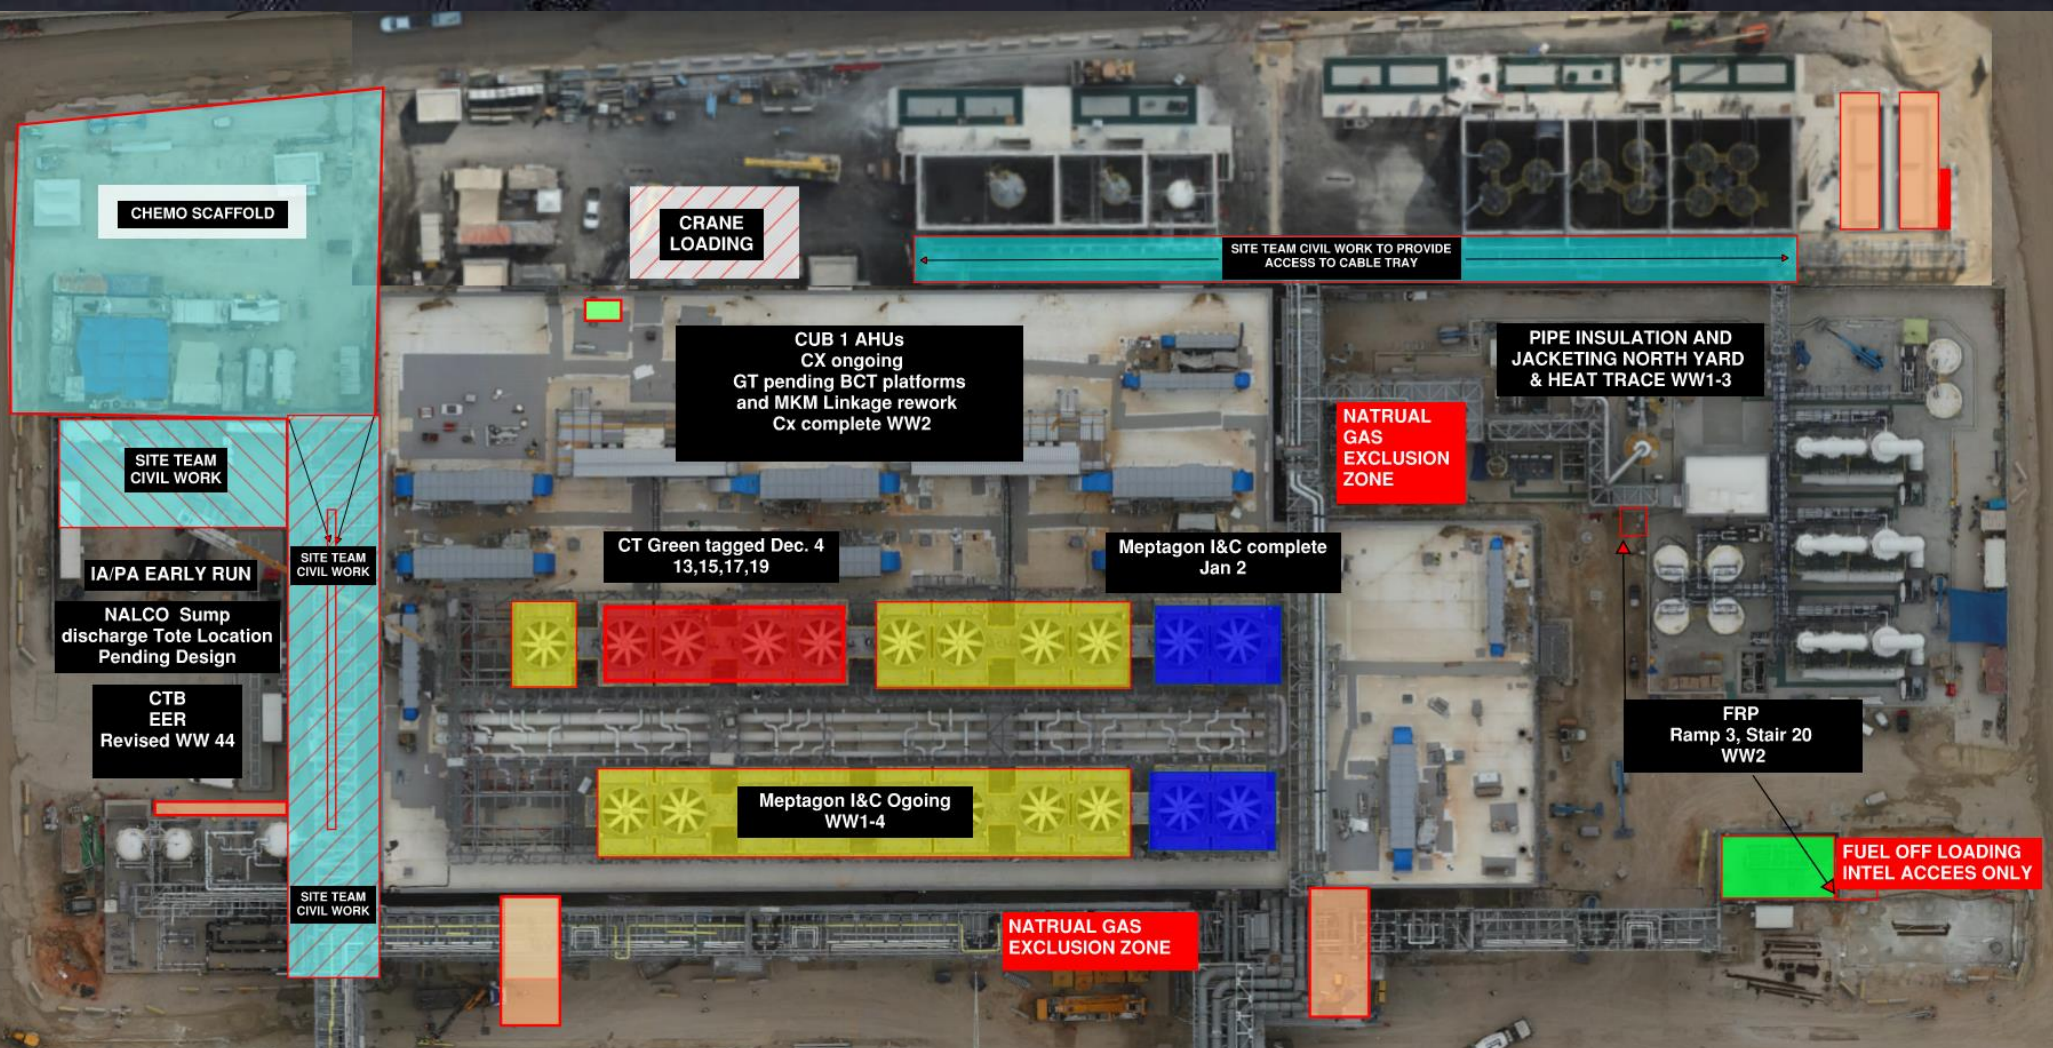


CUB 2- Load in and H&T

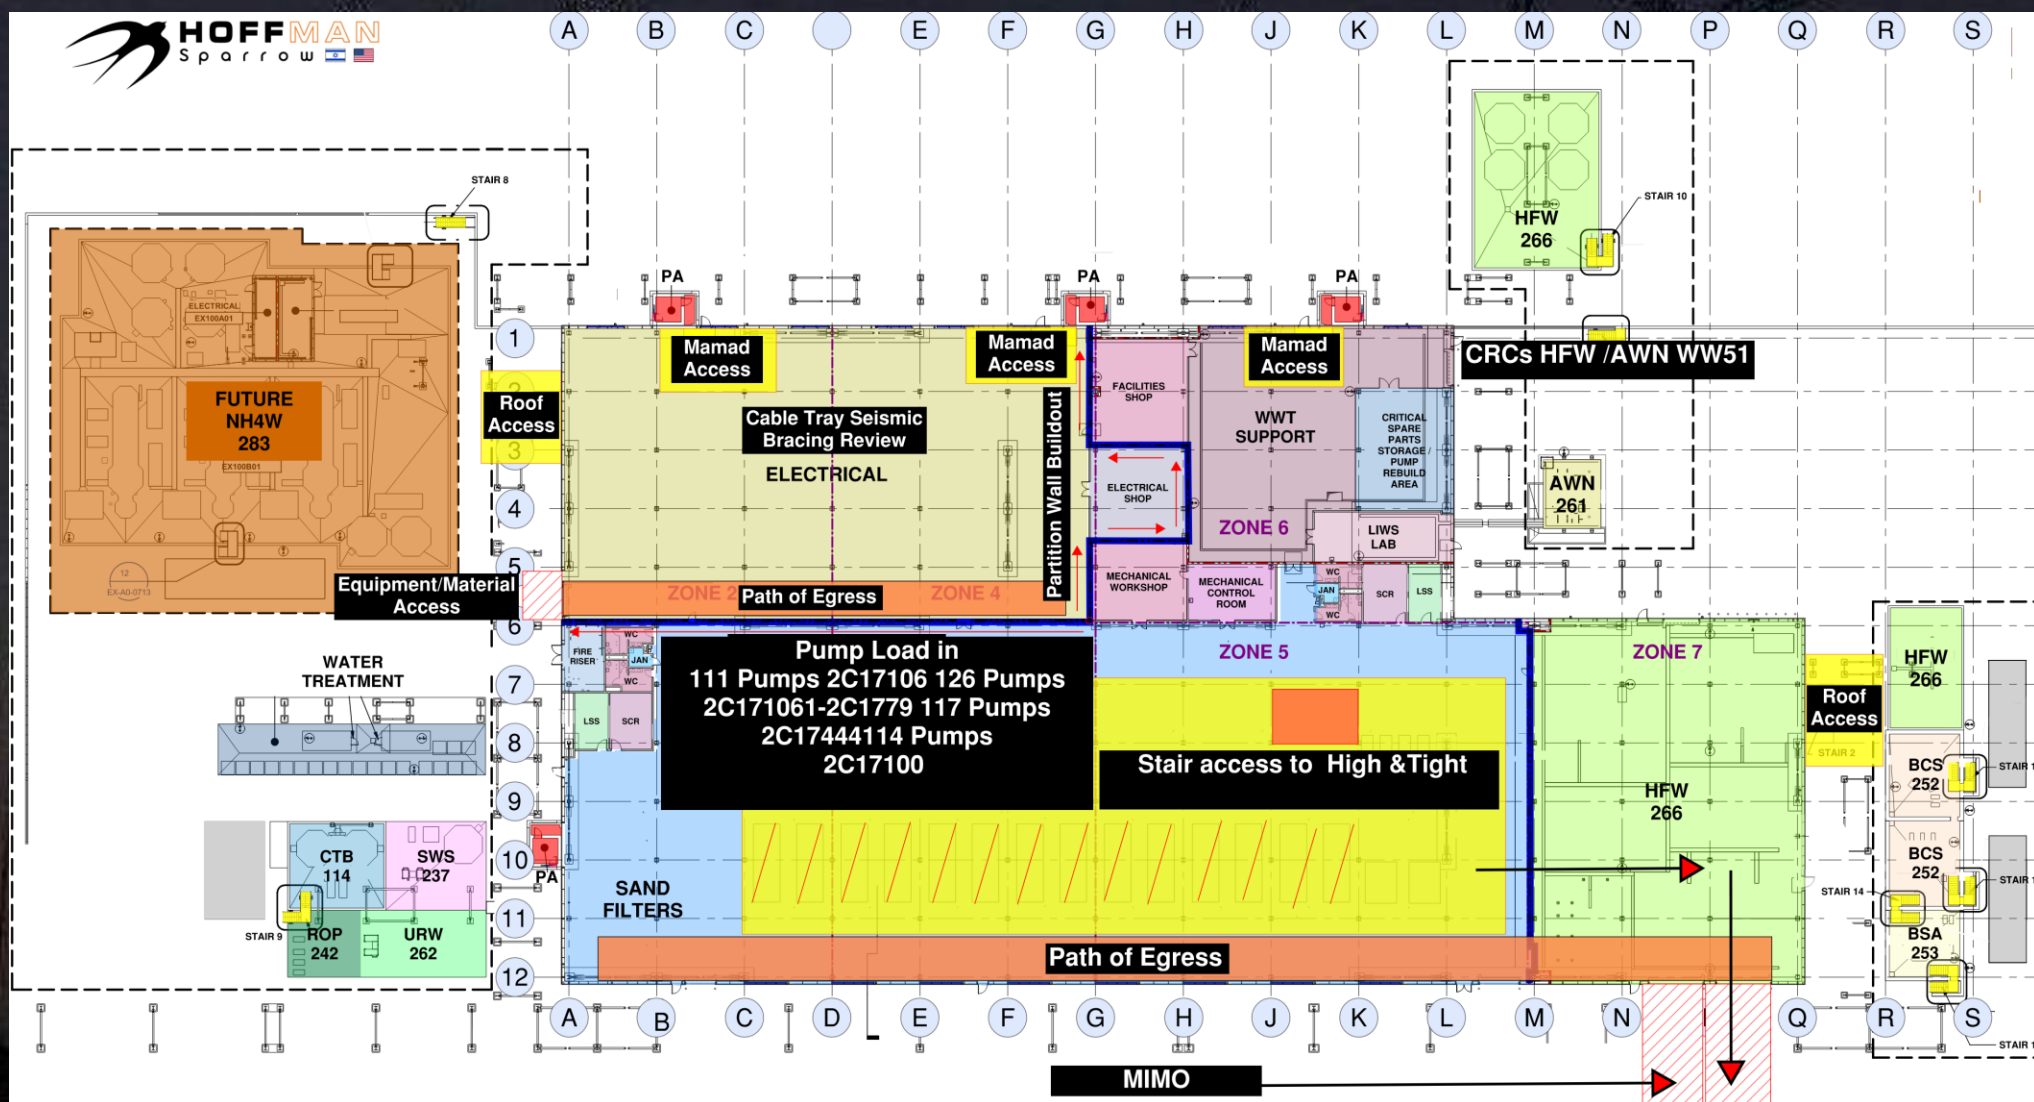

CUB 2 – EXTERIOR/ROOF







HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

BGC - NDT


Starting –Thursday January 2nd night at 19:00
Finish Friday January 3rd at 05:00am.


Safety spotter

No impact on PMB
entrance\Exit

Safety spotter

Safety spotter

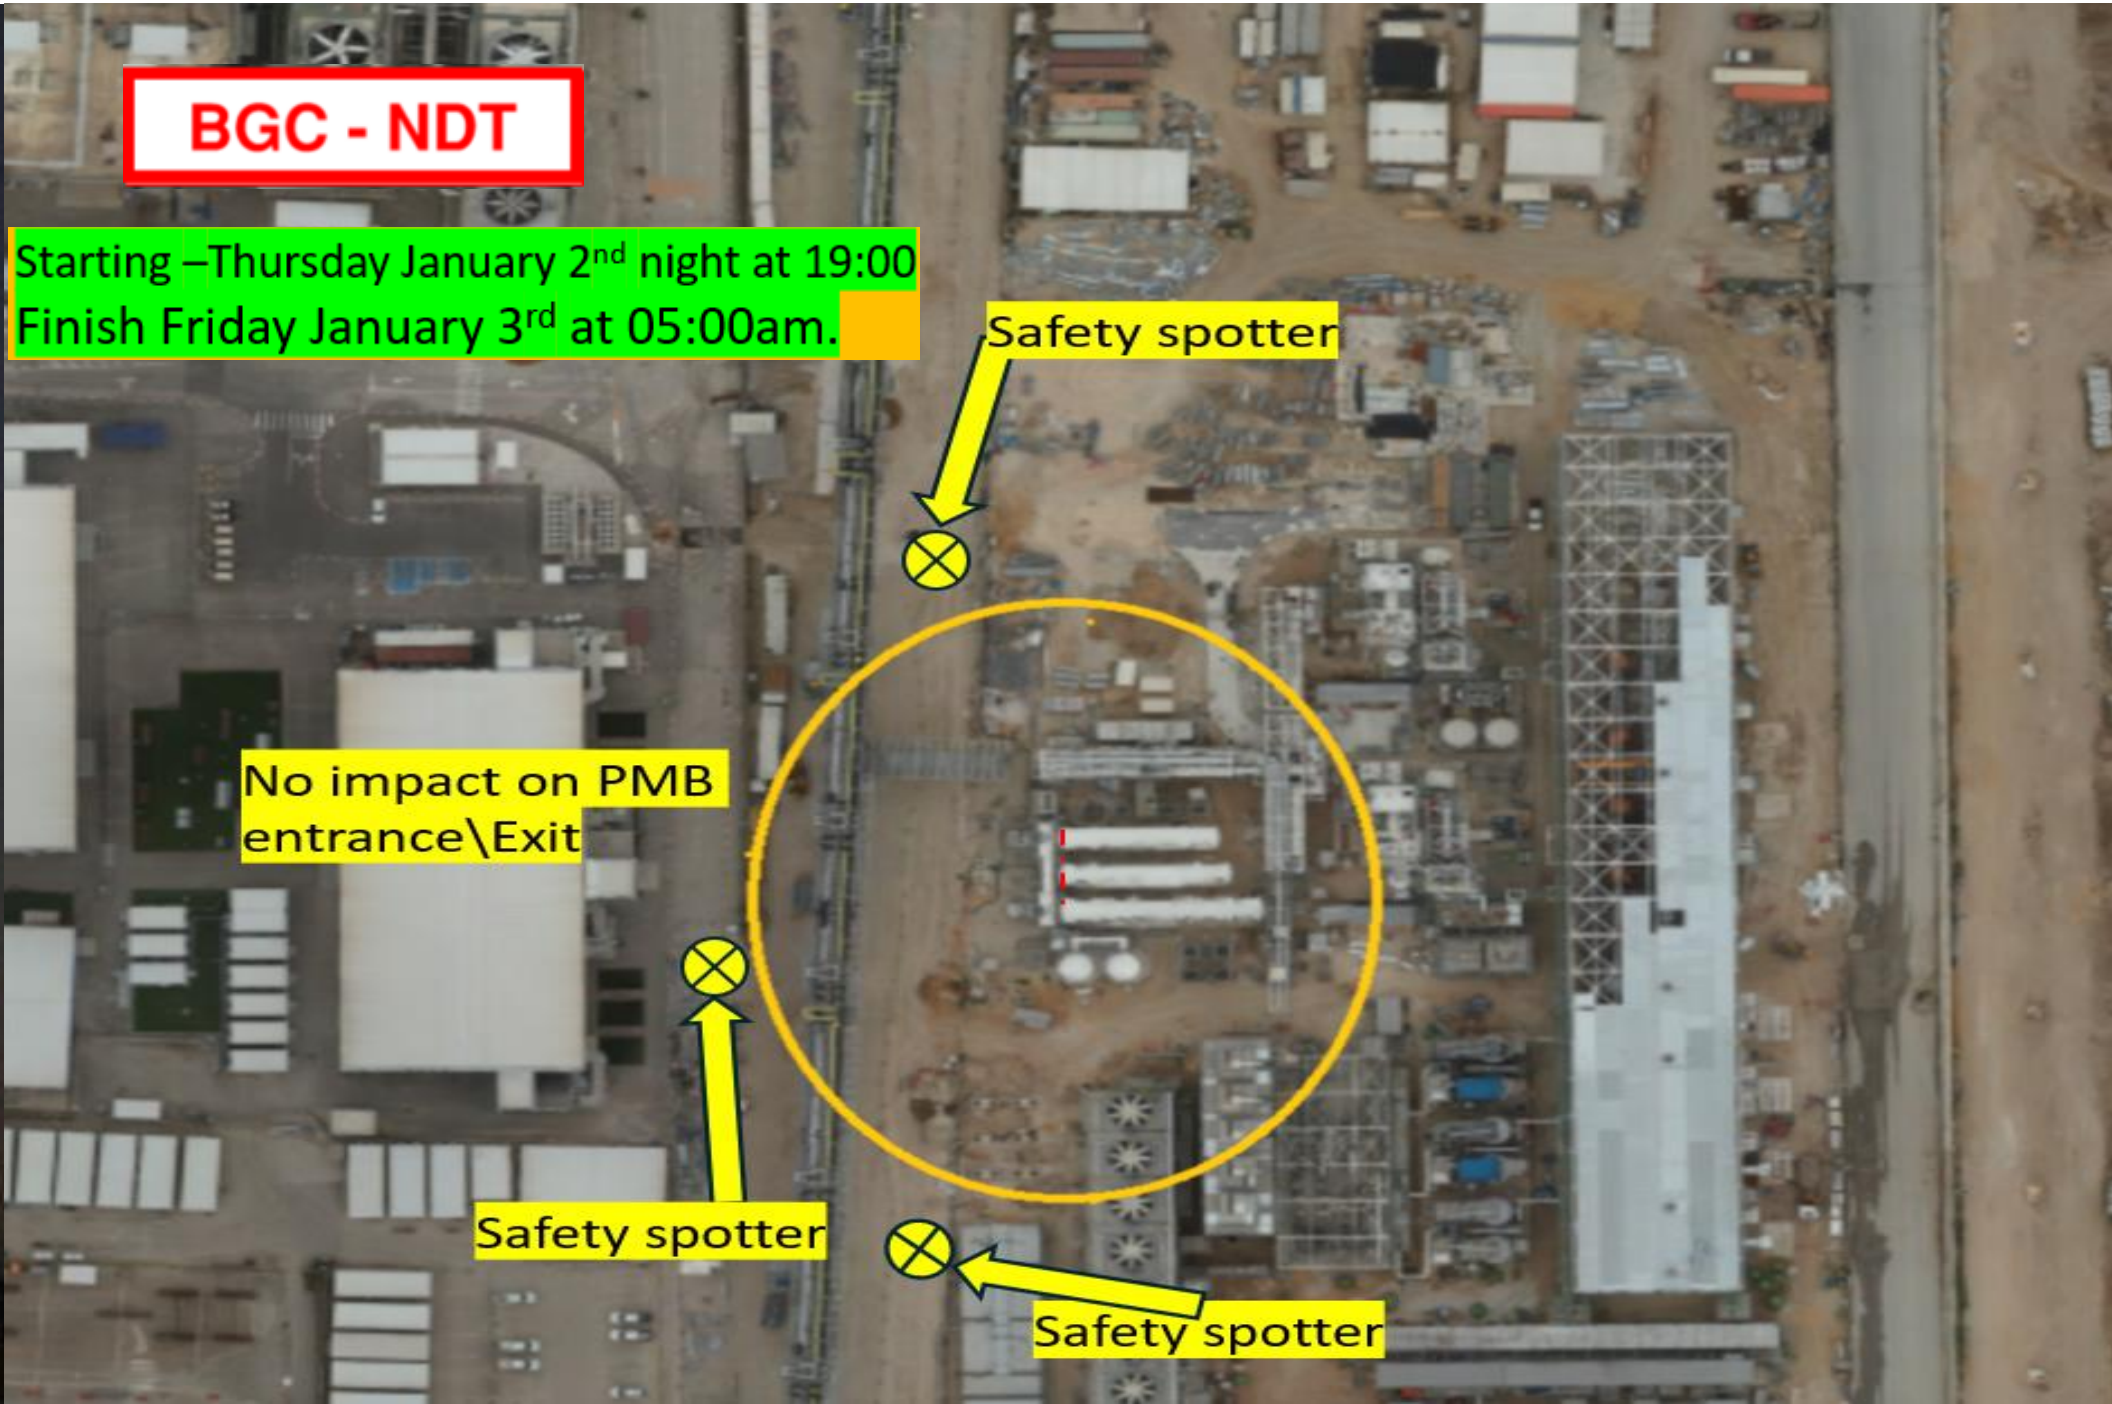

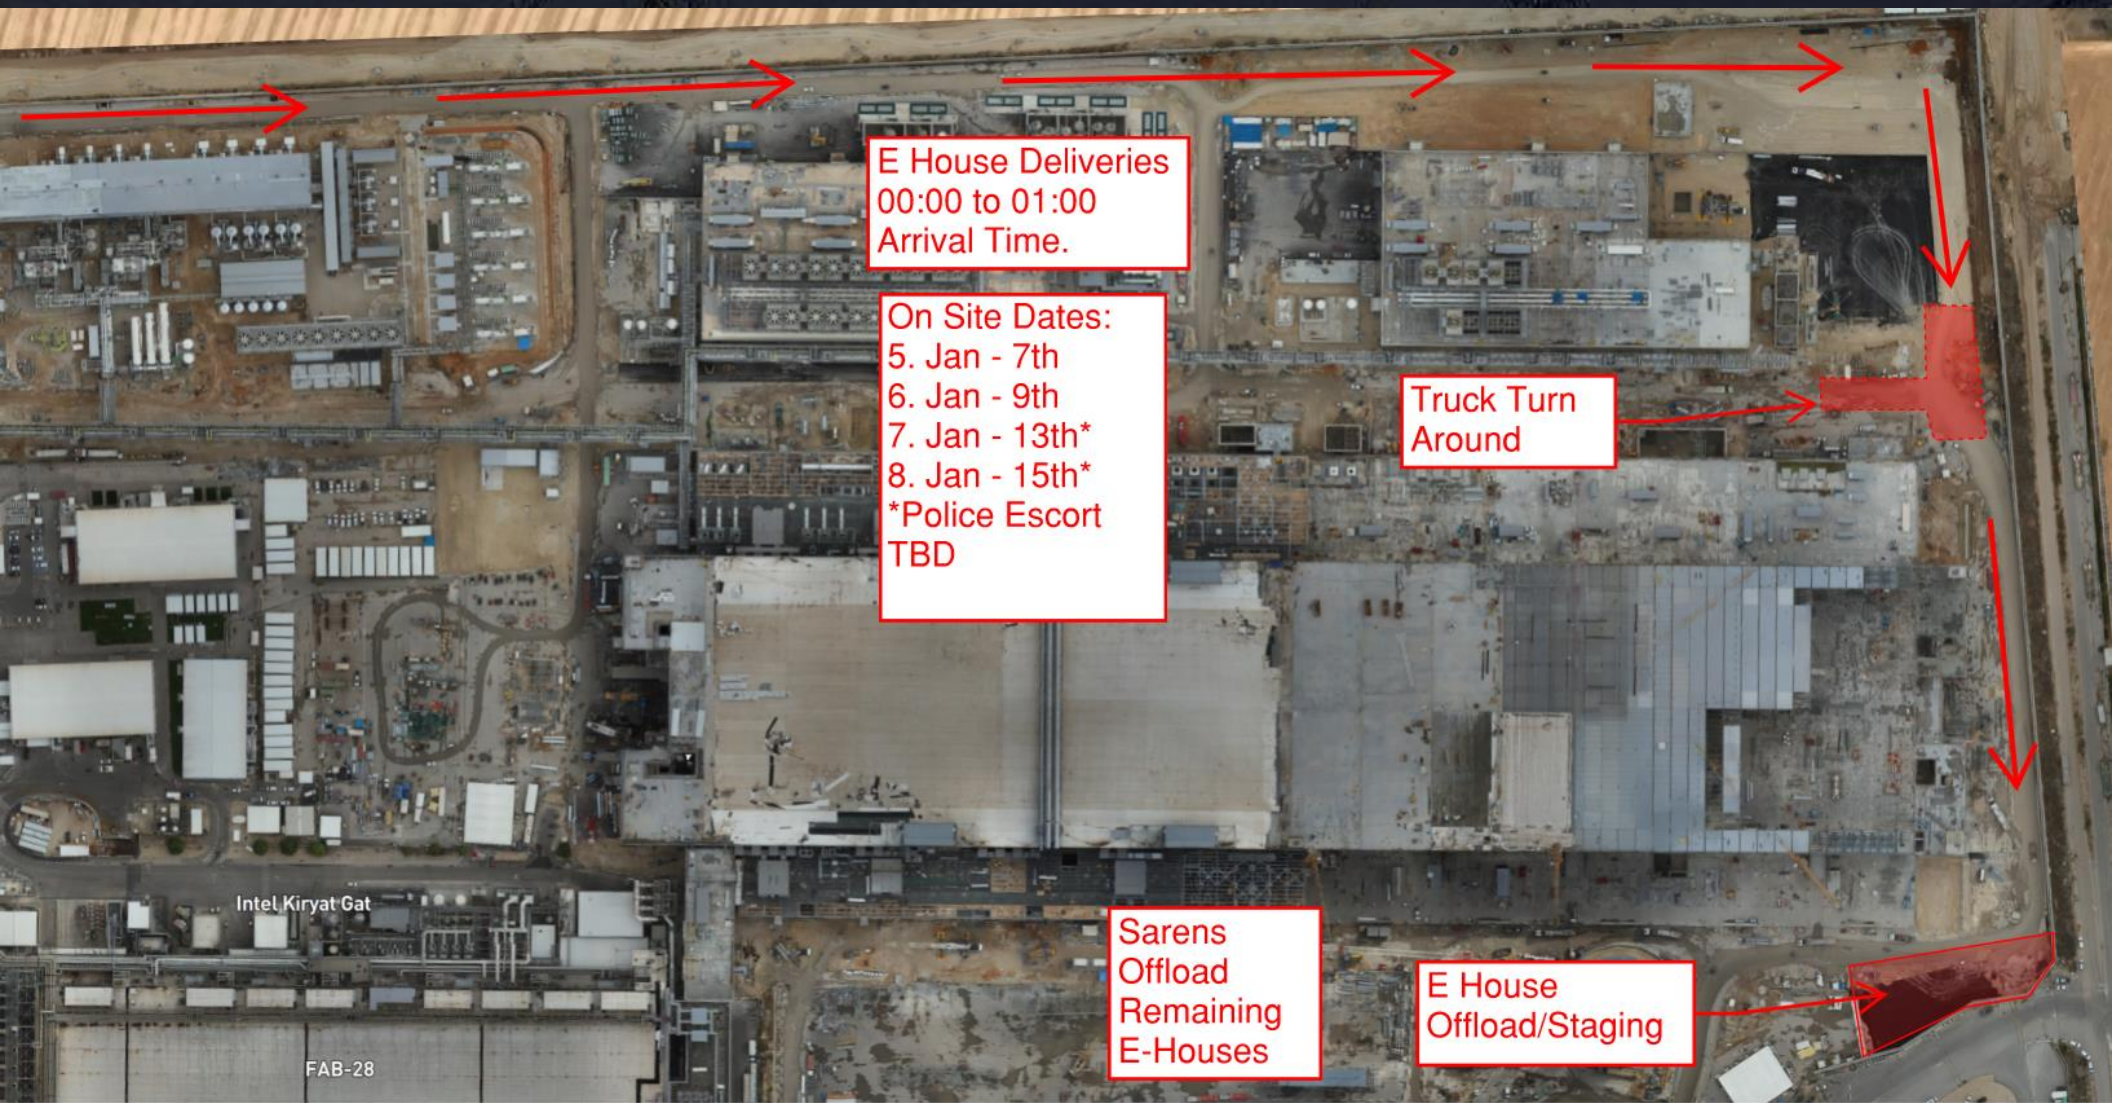

E House Deliveries
00:00 to 01:00
Arrival Time.

On Site Dates:
5. Jan - 7th
6. Jan - 9th
7. Jan - 13th*
8. Jan - 15th*
*Police Escort
TBD


Truck Turn
Around


Intel Kiryat Gat

FAB-28

Sarens
Offload
Remaining
E-Houses

E House
Offload/Staging

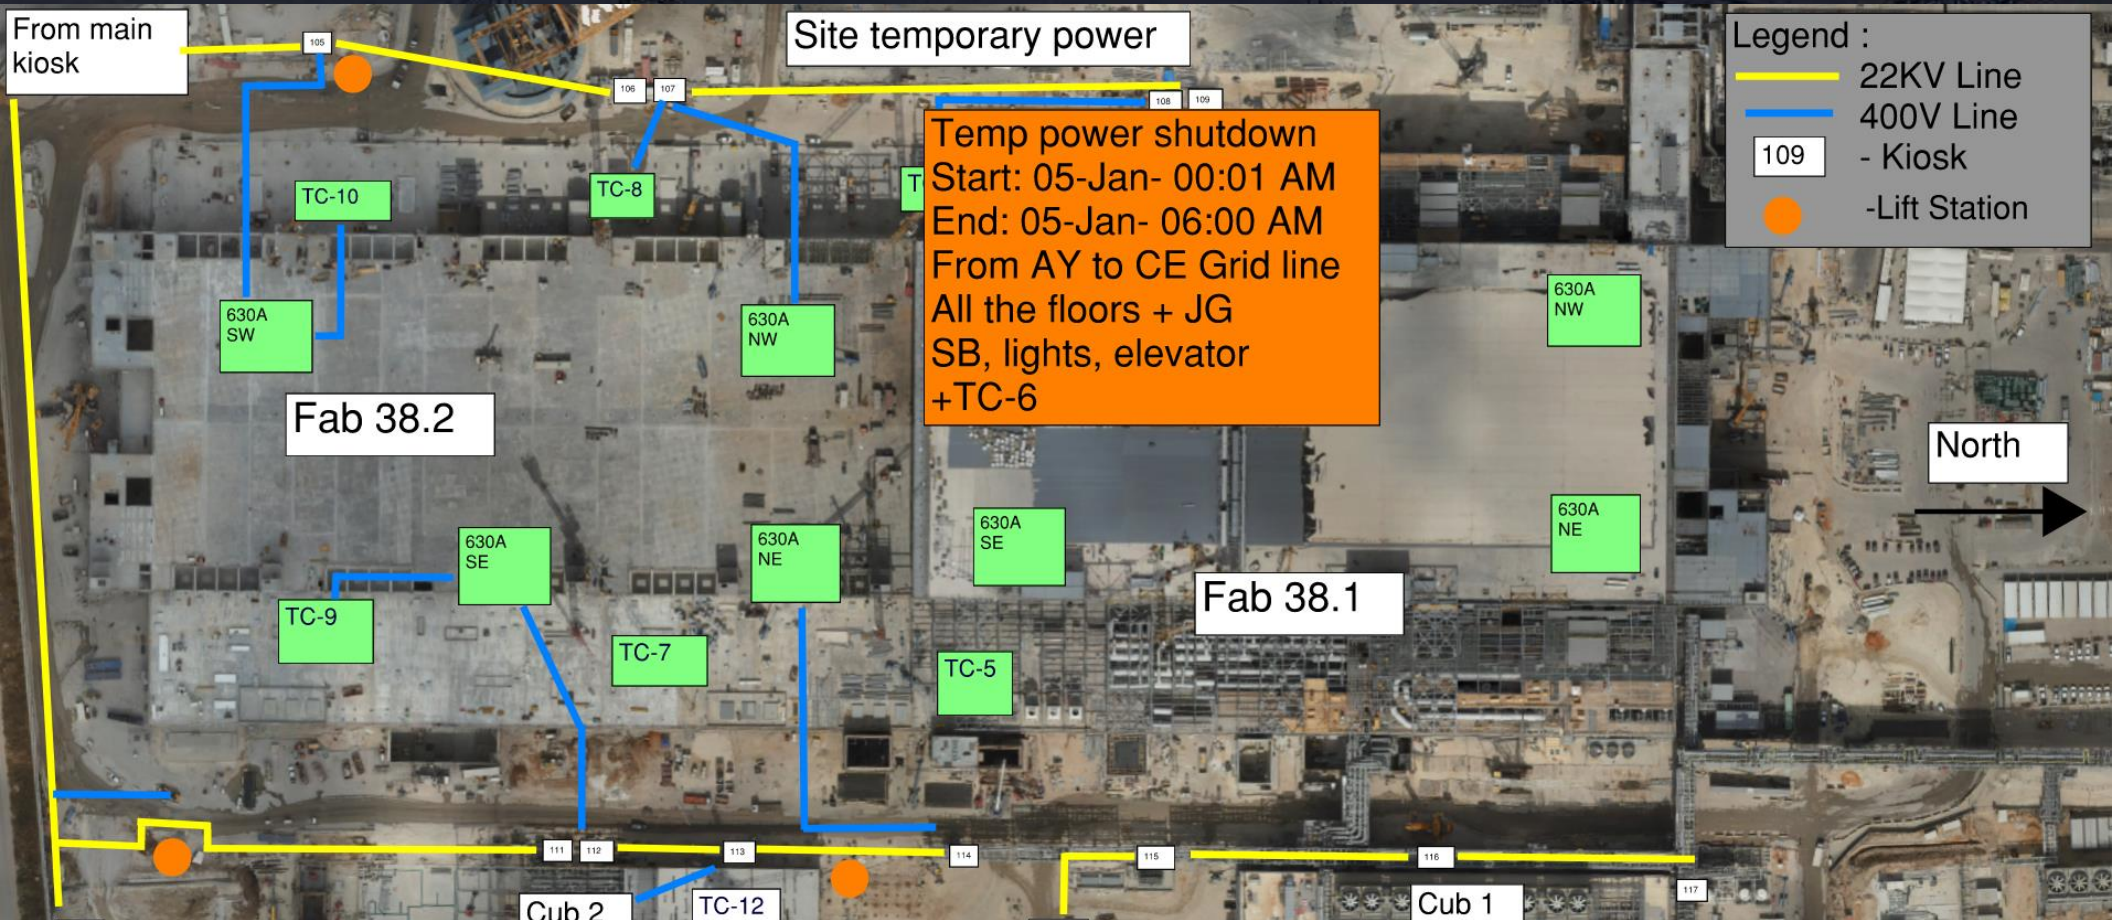

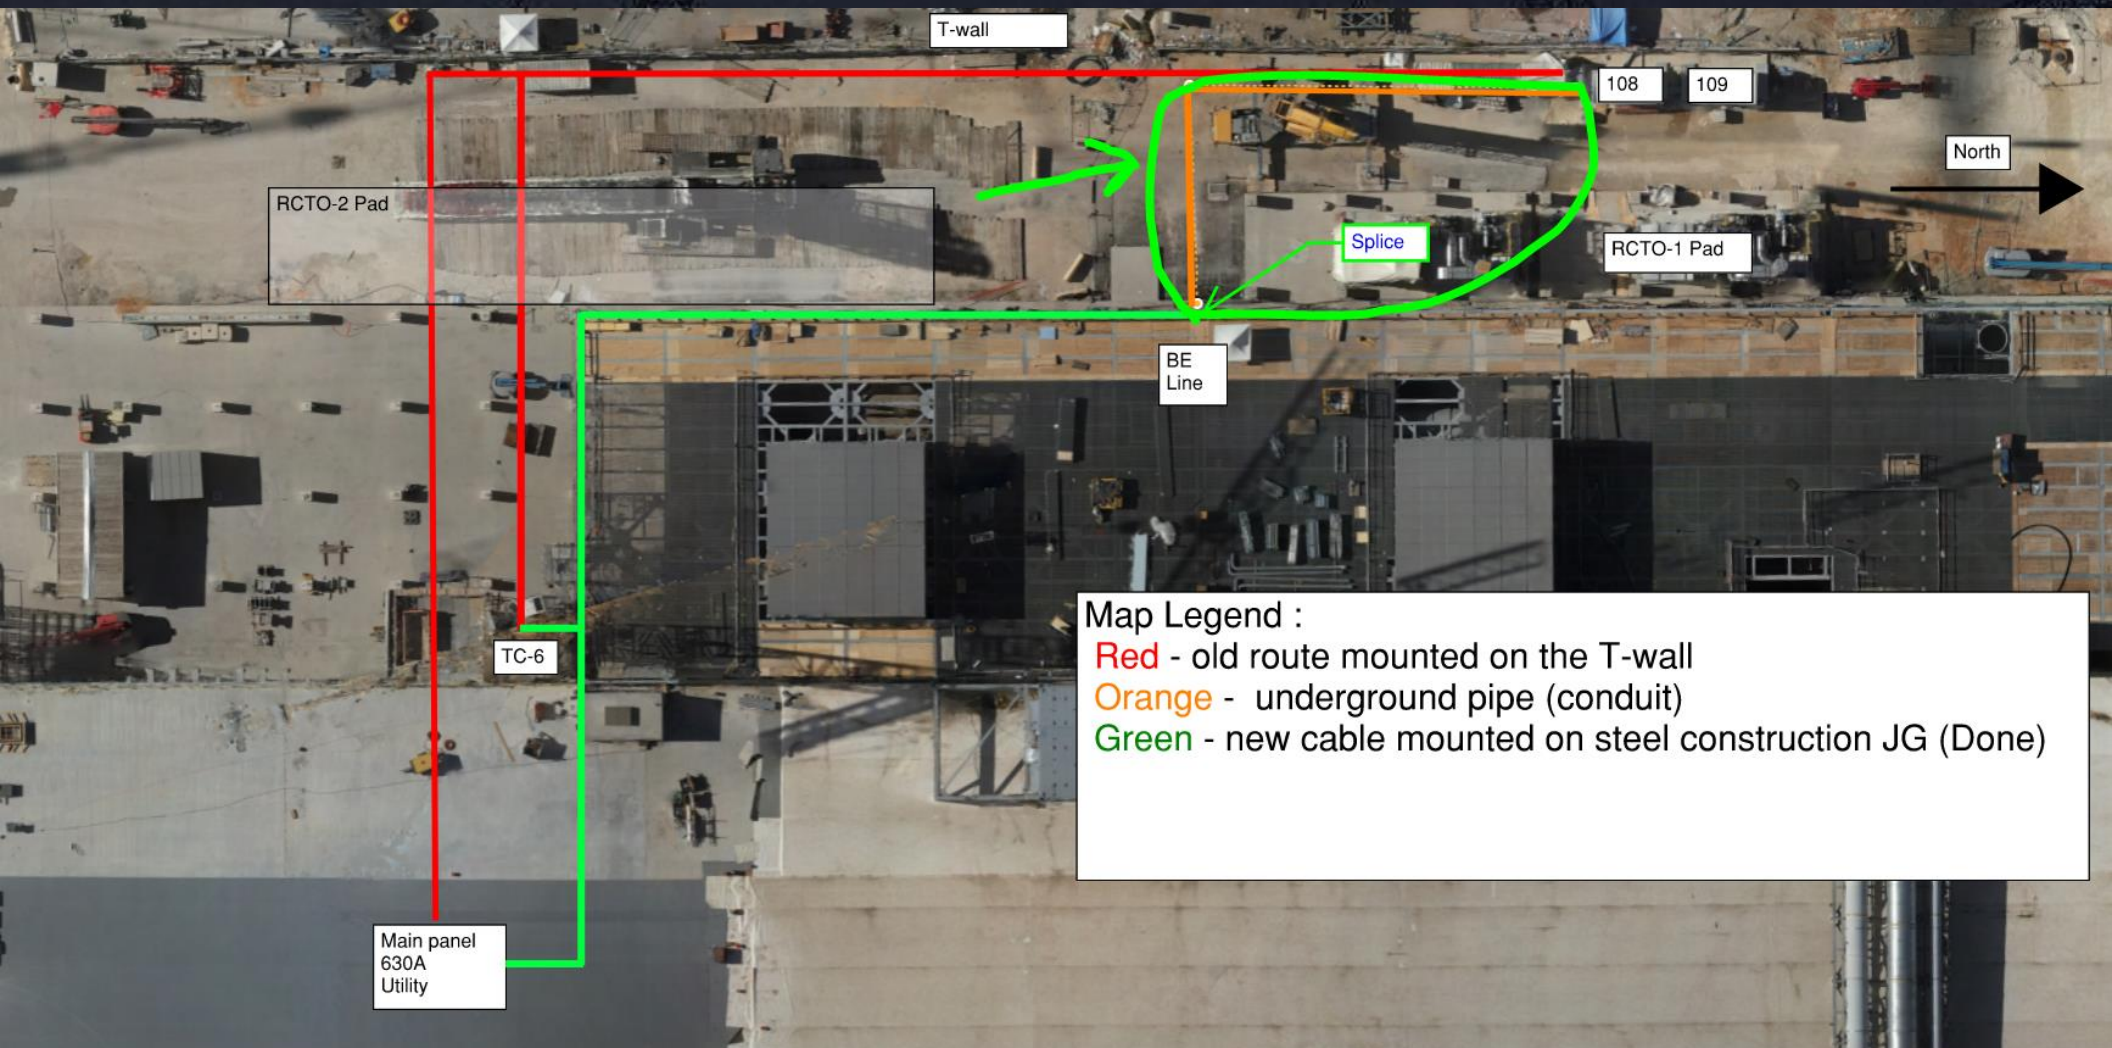

Map Legend :


- Red - old route mounted on the T-wall
- Orange - underground pipe (conduit)
- Green - new cable mounted on steel construction JG (Done)

Daily Coordination Meeting

Site Logistics

600 Car Park

Boring

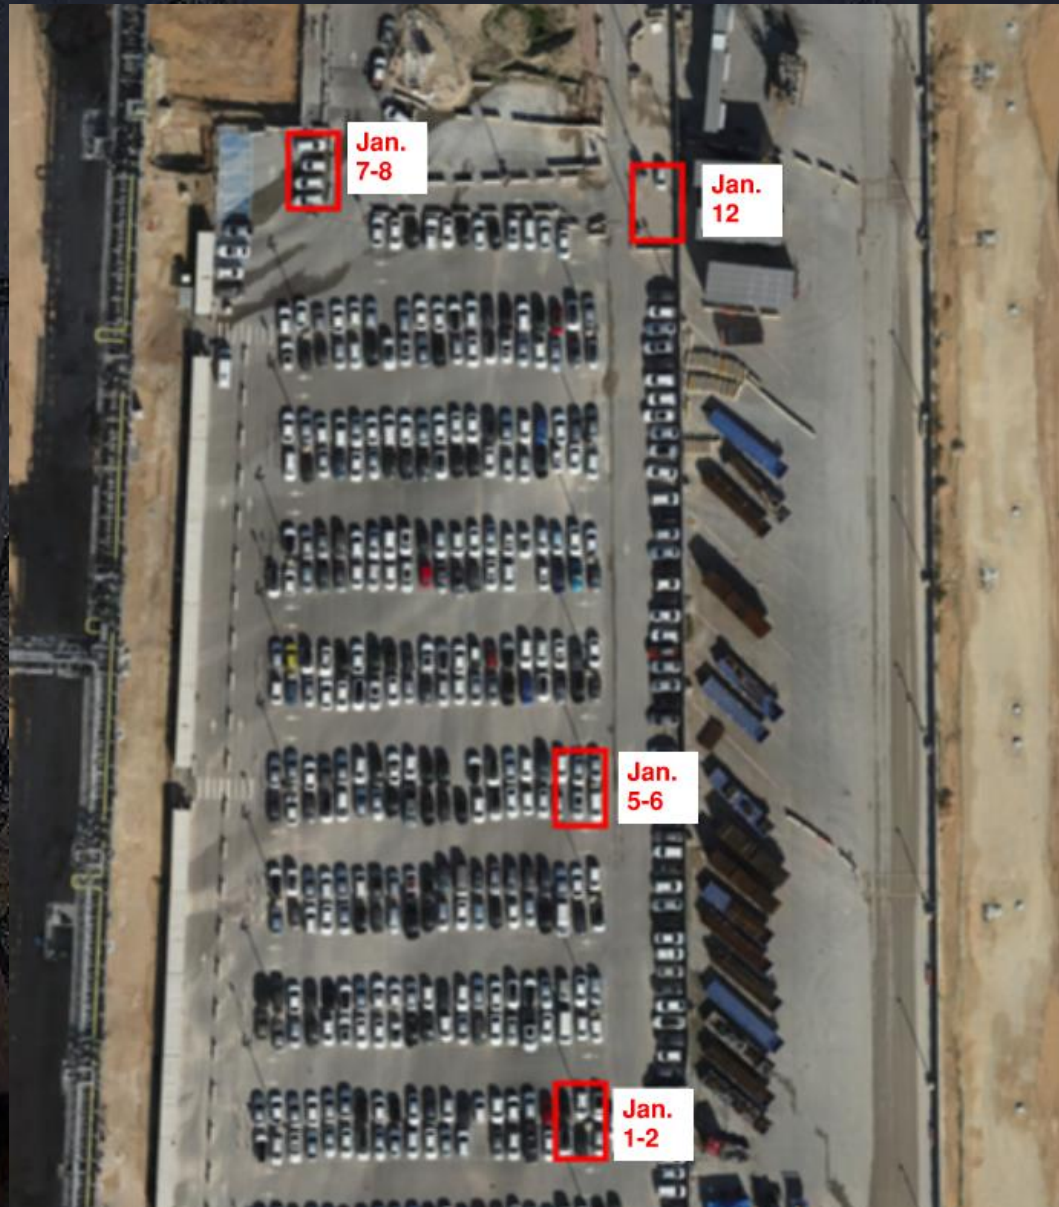

Daily Coordination Meeting

Site Logistics North



Daily Coordination Meeting

Site Logistics
South



Learn From Everything

- Following up on our presentation yesterday of the incident data from last year. Some of our key focus areas for preventing incidents are the following:
- Planning
 - Have complete plans
 - Follow or update plans
- Access
 - Assess and keep clear
- Attentiveness
 - Don't use your phone in an active construction area
 - Limit distractions, especially while walking
- Material Handling
 - Limit manual material handling
 - Keep secured at all times
- Falling Object Protection
 - All tools and materials must be secured at heights

HCC/EHS Weekend Work- 03.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Standefer 052-3440752

Yakov Malka 052-3459250

Yakov Alon 052-4671271

CSA CM

Charlie Aitken 052-6041443

Ilyssa Ingenthron 052-5732553

MEP

David Chavez 052-2756390

Denis Ryan 052-2962447

Pauric O'Reilly 052-3571665

Lara Salaymeh 052-2410953

Abhilash Parameswaran 052-6938827

Cranes

Craig Mowry 052-300-2769

Safety

Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com

Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com

Safety Professional- Nassim Yones- [052-2208434](tel:052-2208434) Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 03.01.2025

FAB

Utility Level / Roof / Stair Shaft

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Megason

Subfab

Pach Taas

BAe Wall Penetration

Itamar 0509301917

Afcon E

MARSes, E LSS Rooms

Avi Eli: 0526008487

Chemo

TTNW

Tomi: 0523759408

SELA

AY-BC 15-19

Avihen 0548155302

MEGASON

LSS Rooms

Israel 0526869393

Clean Room

Talad – CR 2 E – UPN Install, 4E Grating (EHS Marcelo 0523540242, Super Igor 0544509386)

Sig – 10 GUYS 5W INT 4W, 3E Handrails (EHS Beni 0506232032, Super Shmulik 0549205966)

Afcon – CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)

Chemo –30 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)

Megason - 16 GUYS INT LEVEL + 7 GUYS ON UTILITY LEVEL FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Sela – 2E CRC (Supervisor yoav 0548076339 , EHS SERGEY 0526650046)

Protocol - aa+ak lines.

Talent solution 1w_+ 1e + interstitial.

Subcontractor Weekend Work- 03.01.2025

PSSS

Pach Taas – Module bolting PSSS Roof, Lift 2 1-3P

Foreman – Itamar – 050-9301917

Safety – Offek – 050-2161429

Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2

Foreman – Pradeep - 055-2742935

Safety – Stevan – 055-9129333

Chemo A. – PSSS Roof and Lift 2 1-5P

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

SK Engineering – GL4 Rack UL, Lift 2 2P Piping

Foreman – Marcelo – 054-5210133

Safety – Majdi – 054-6192581

WJG

Afcon – Lift 2 and Utility Level Cable Tray

Foreman: Montu 055 911 6973

Safety: Pradeep 055 274 2935

Chemo: 4J/5J Lift 2 Piping & Link Roof

Foreman: Maor 050 988 9071

Safety: Erez 054 971 6840

Pach Taas: All over

Foreman: Tomer 050 767 0585

Safety: Jad 050 5405016

Subcontractor Weekend Work- 03.01.2025

CUB

S.K.E - CUB 1:

Renato - 0548991623

Marzuk - 0548830263

Chemo Aharon - CUB 1:

Dudu - 0509808846

Leonid - 0548883878

D&P - CUB 2:

Constantino - 0545501602

David - 0548894447

Sami Najami - CUB 1 test + CUB 2:

Husein - 0526917461

Faiz - 0502227962

Alon - 0509895008

HSAI:

Sergey - 0552728807

Trestle

Siding

Sami Najami

Forman- Abed Kilani 054-5501880

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Elmor – Site Lighting Underground

Supervision = Shlomi: 050-9182260

EHS = Daniel: 052-2584171

Olizki – Offload 18 & CUB1 trench drains, South GUT road excavation

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Daily Coordination Meeting



14:00 Sign In
