

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:


- Trestle Testing – be out of PMB parking lot by 18:15 on 23 Thursday and through 12:00 on 24 Friday .
- Safety Award – water bottles – get your dailies updated, will be distributed next week.
- The following is the list of subcontractors are delinquent on dailies:
 - **Chemo Aharon (Fab and CUB(s))**
 - **Olizki**
 - **Talad**
 - **El-Mor Electric**
 - **Siemens**




UTILITY LEVEL MOD1

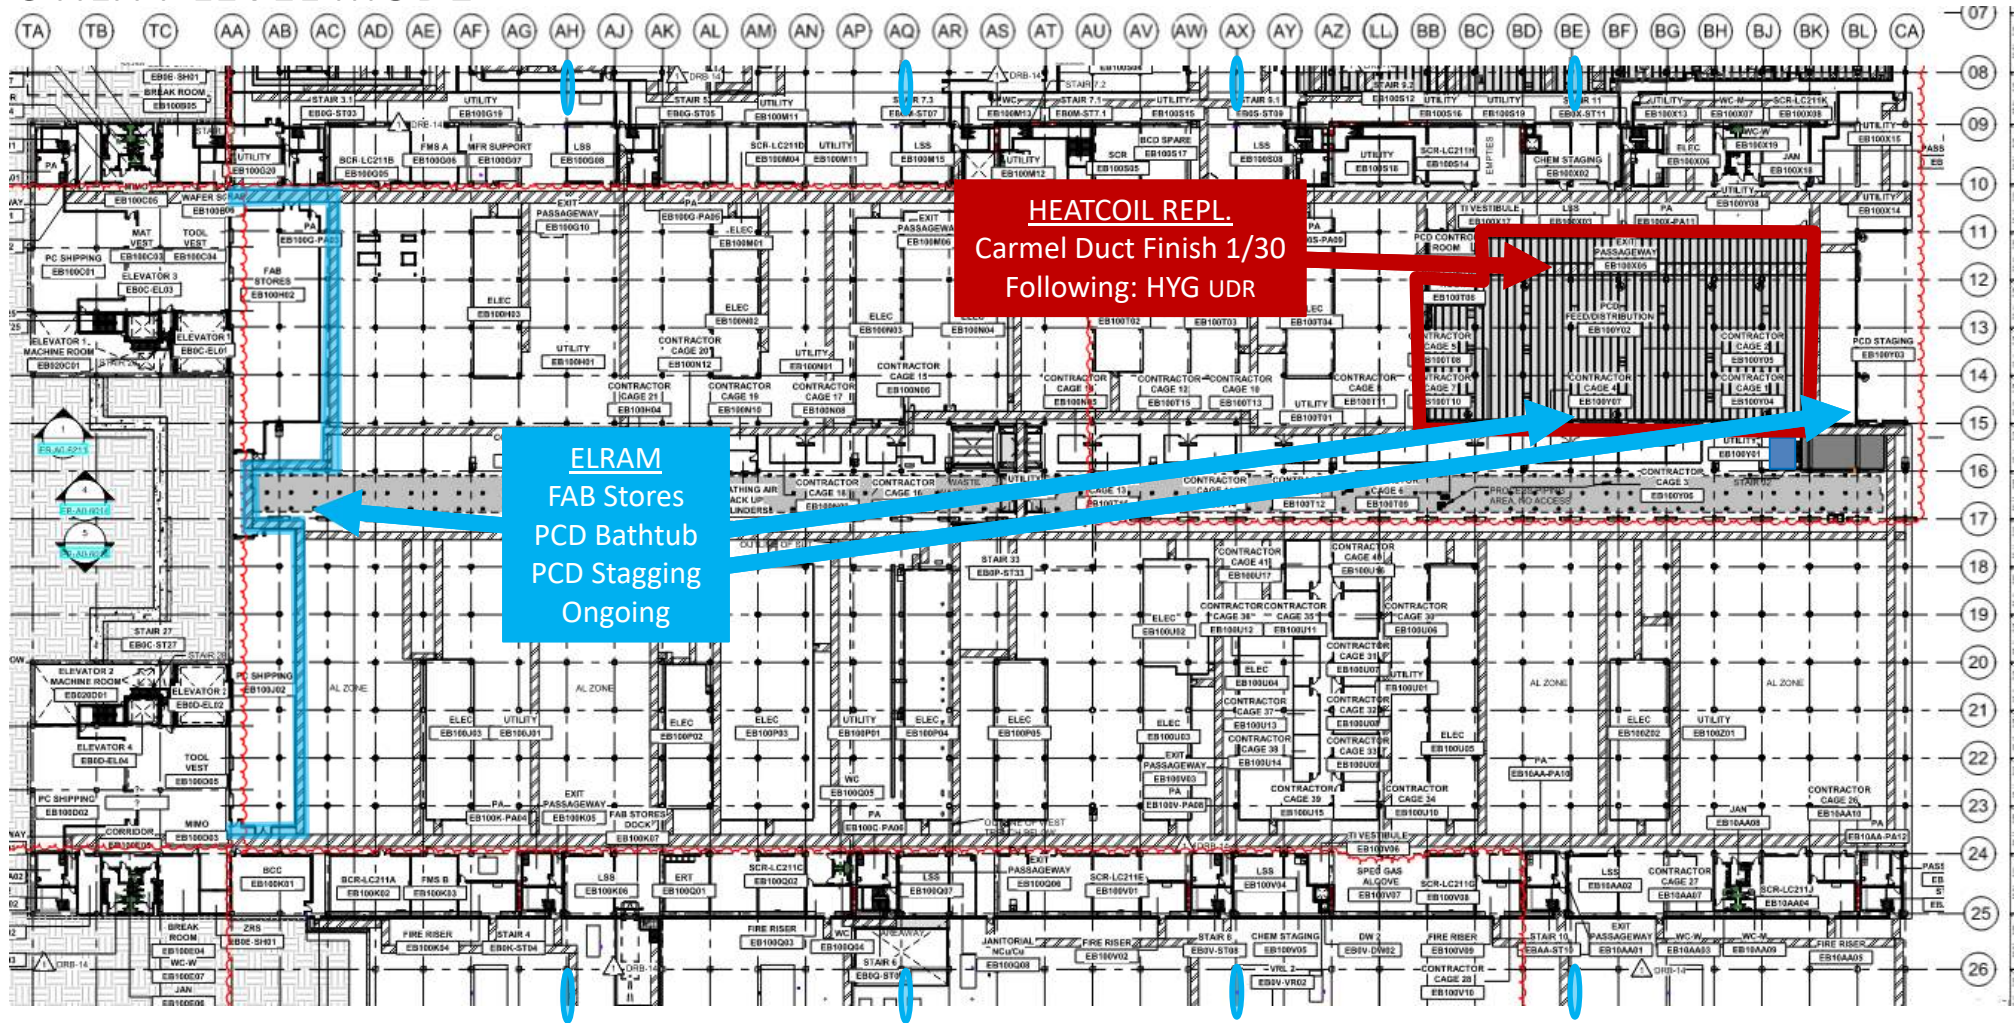


UTILITY LEVEL MOD2

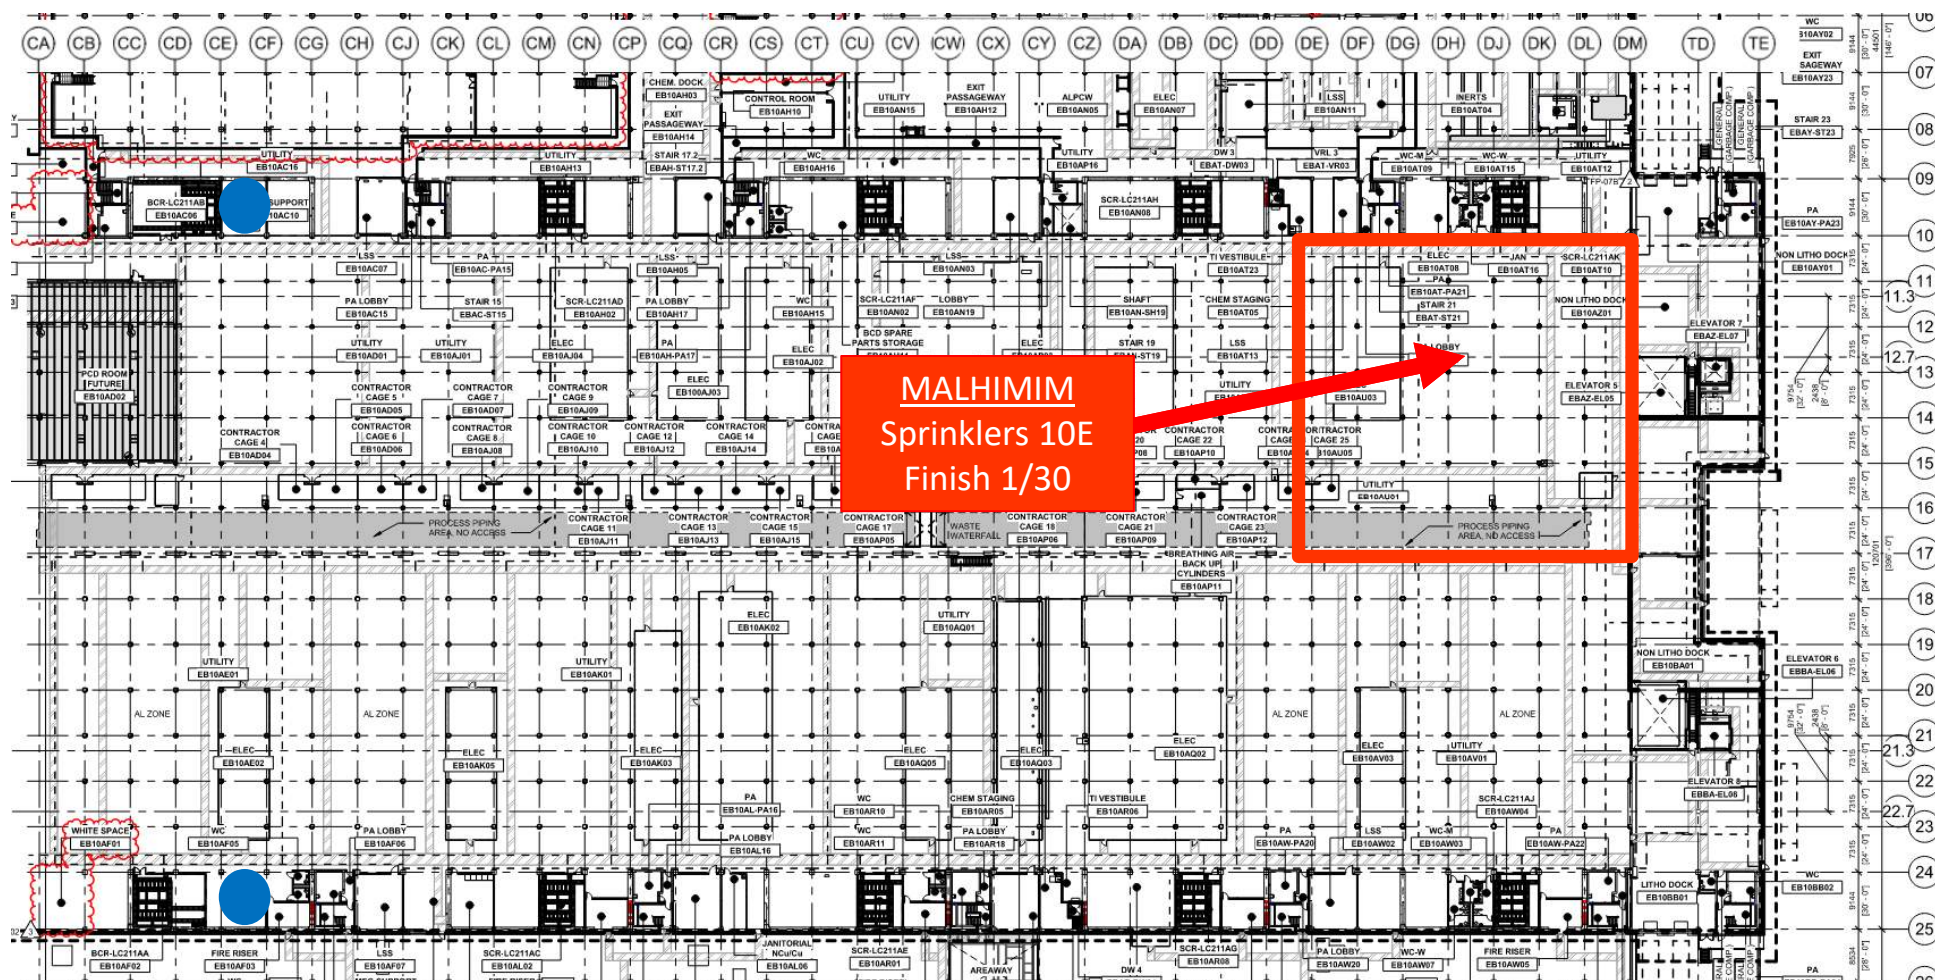

SUT +BCD
M.B pressure test
17:00- 2:00

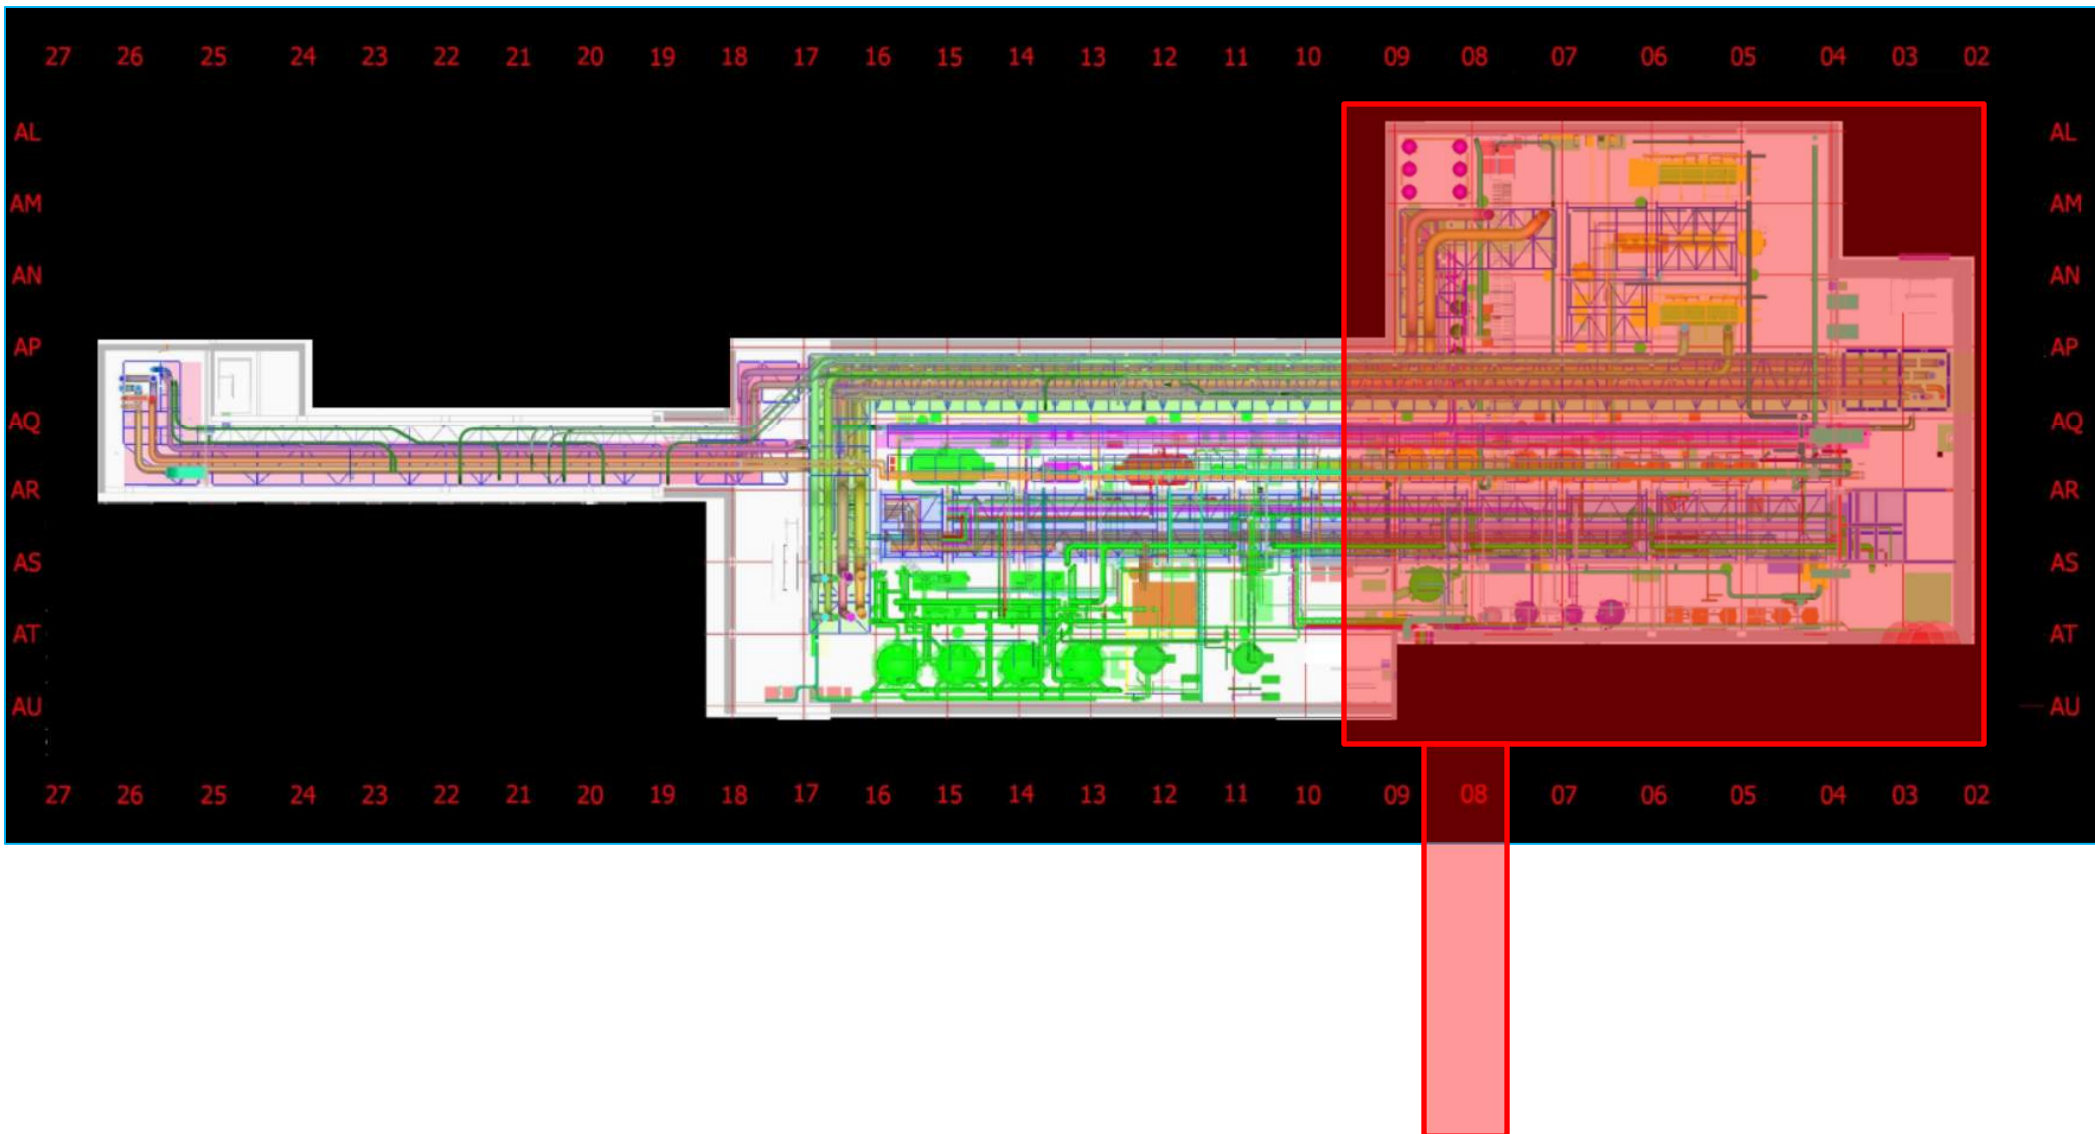

SUT 38.1 Accesses& Egress

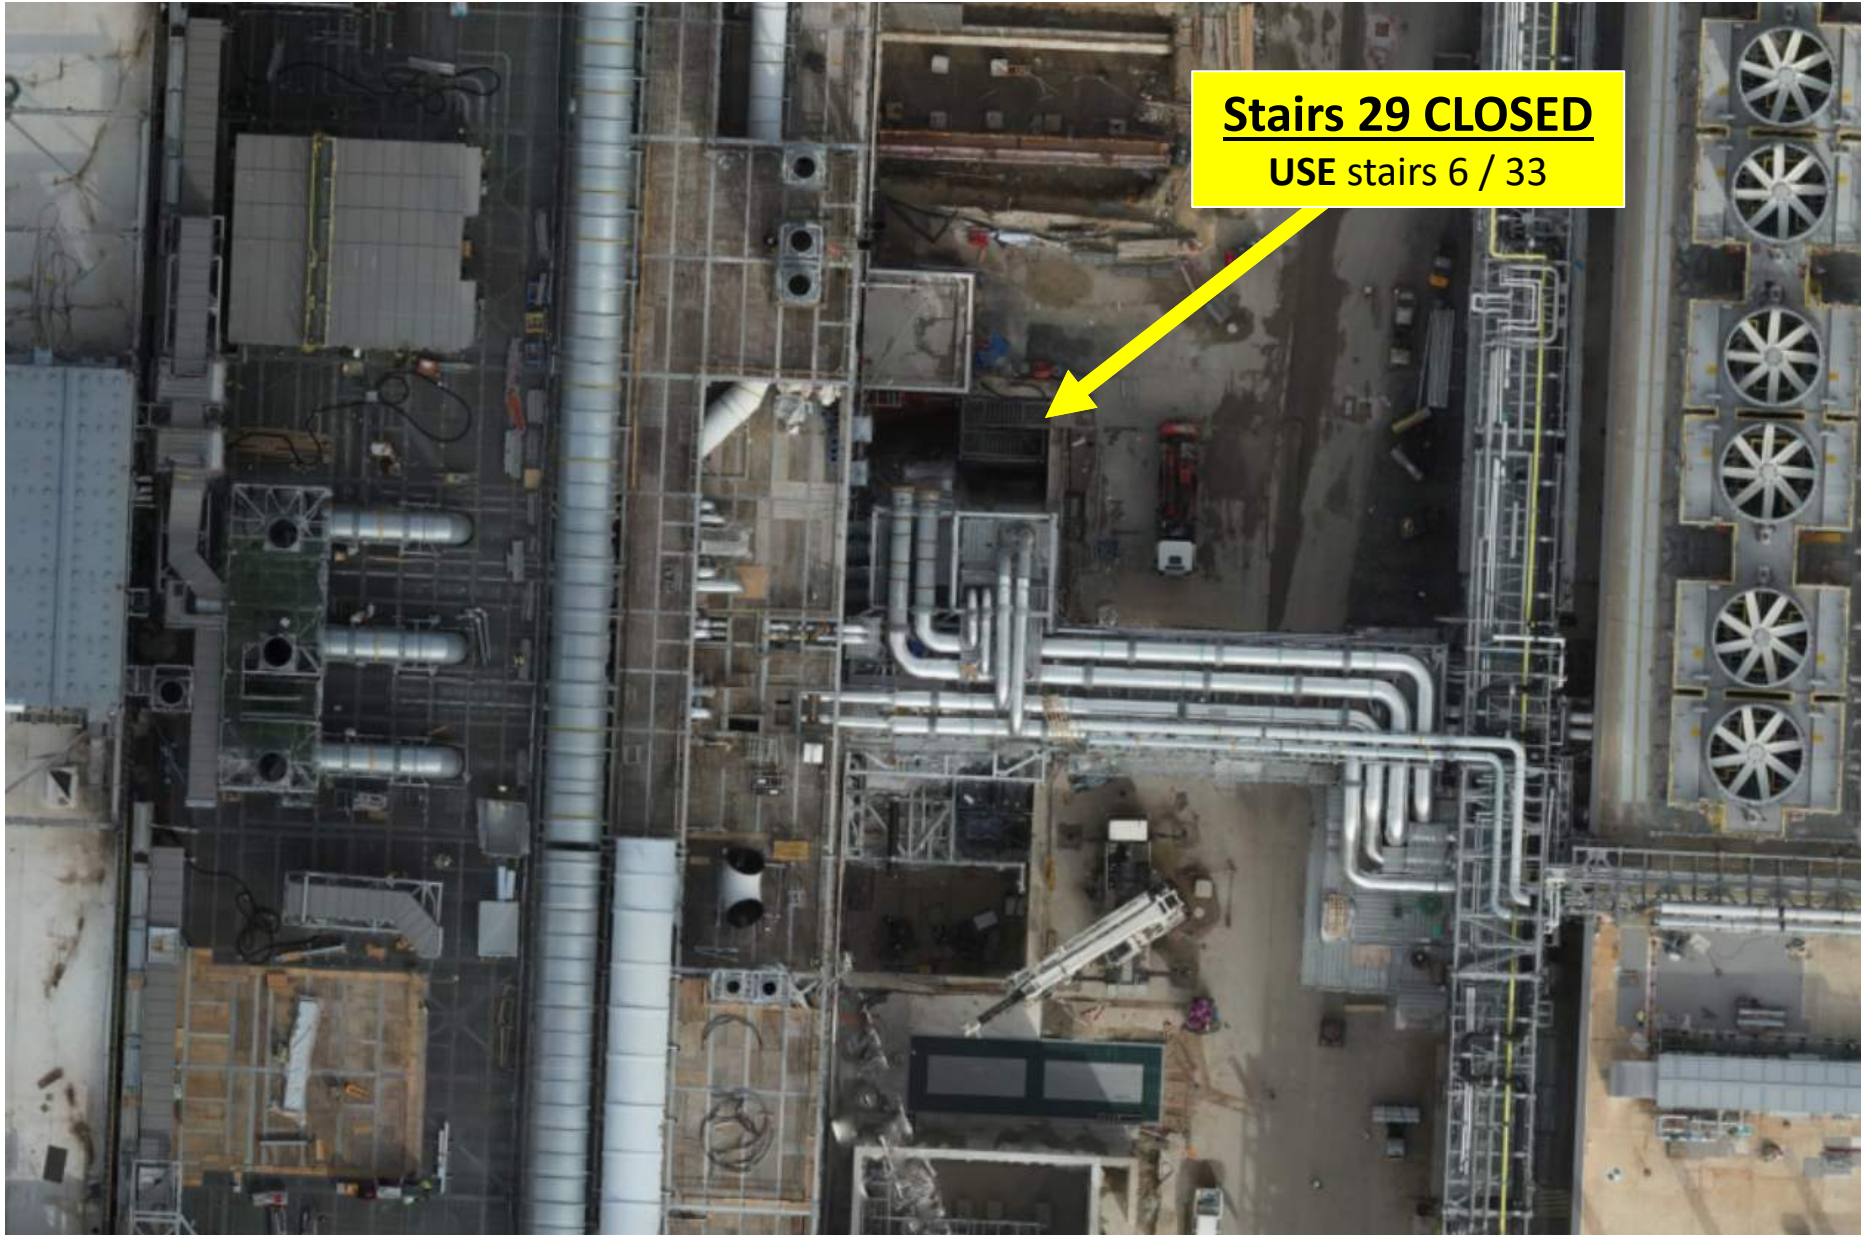




HOFFMAN CONSTRUCTION COMPANY



SUT 38.1 LEVEL

Stairs 29 CLOSED

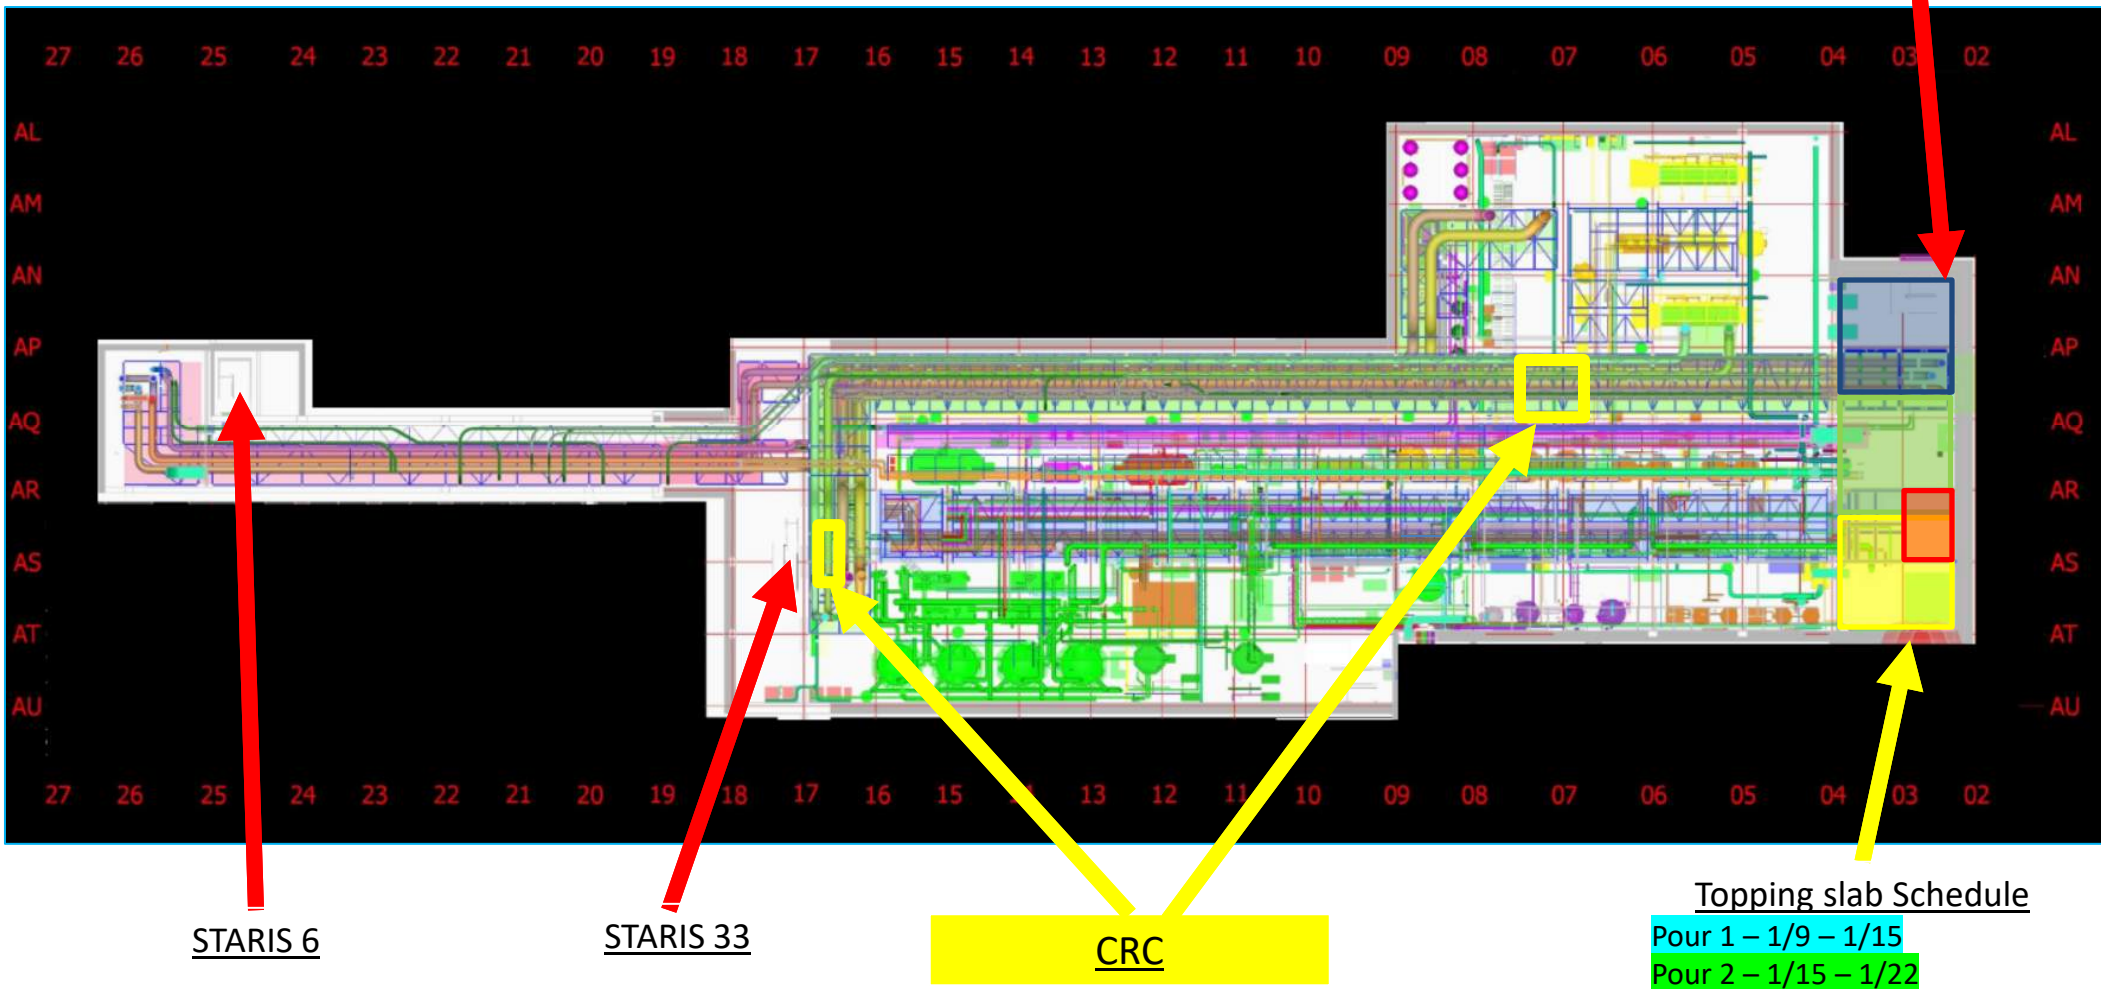

Topping slab Schedule


- Pour 1 – 1/9 – 1/15
- Pour 2 – 1/15 – 1/22
- Pour 3 – 1/22-1/27
- Pour 4 – 1/28-2/4




HOFFMAN CONSTRUCTION COMPANY




SUT 38.2 LEVEL

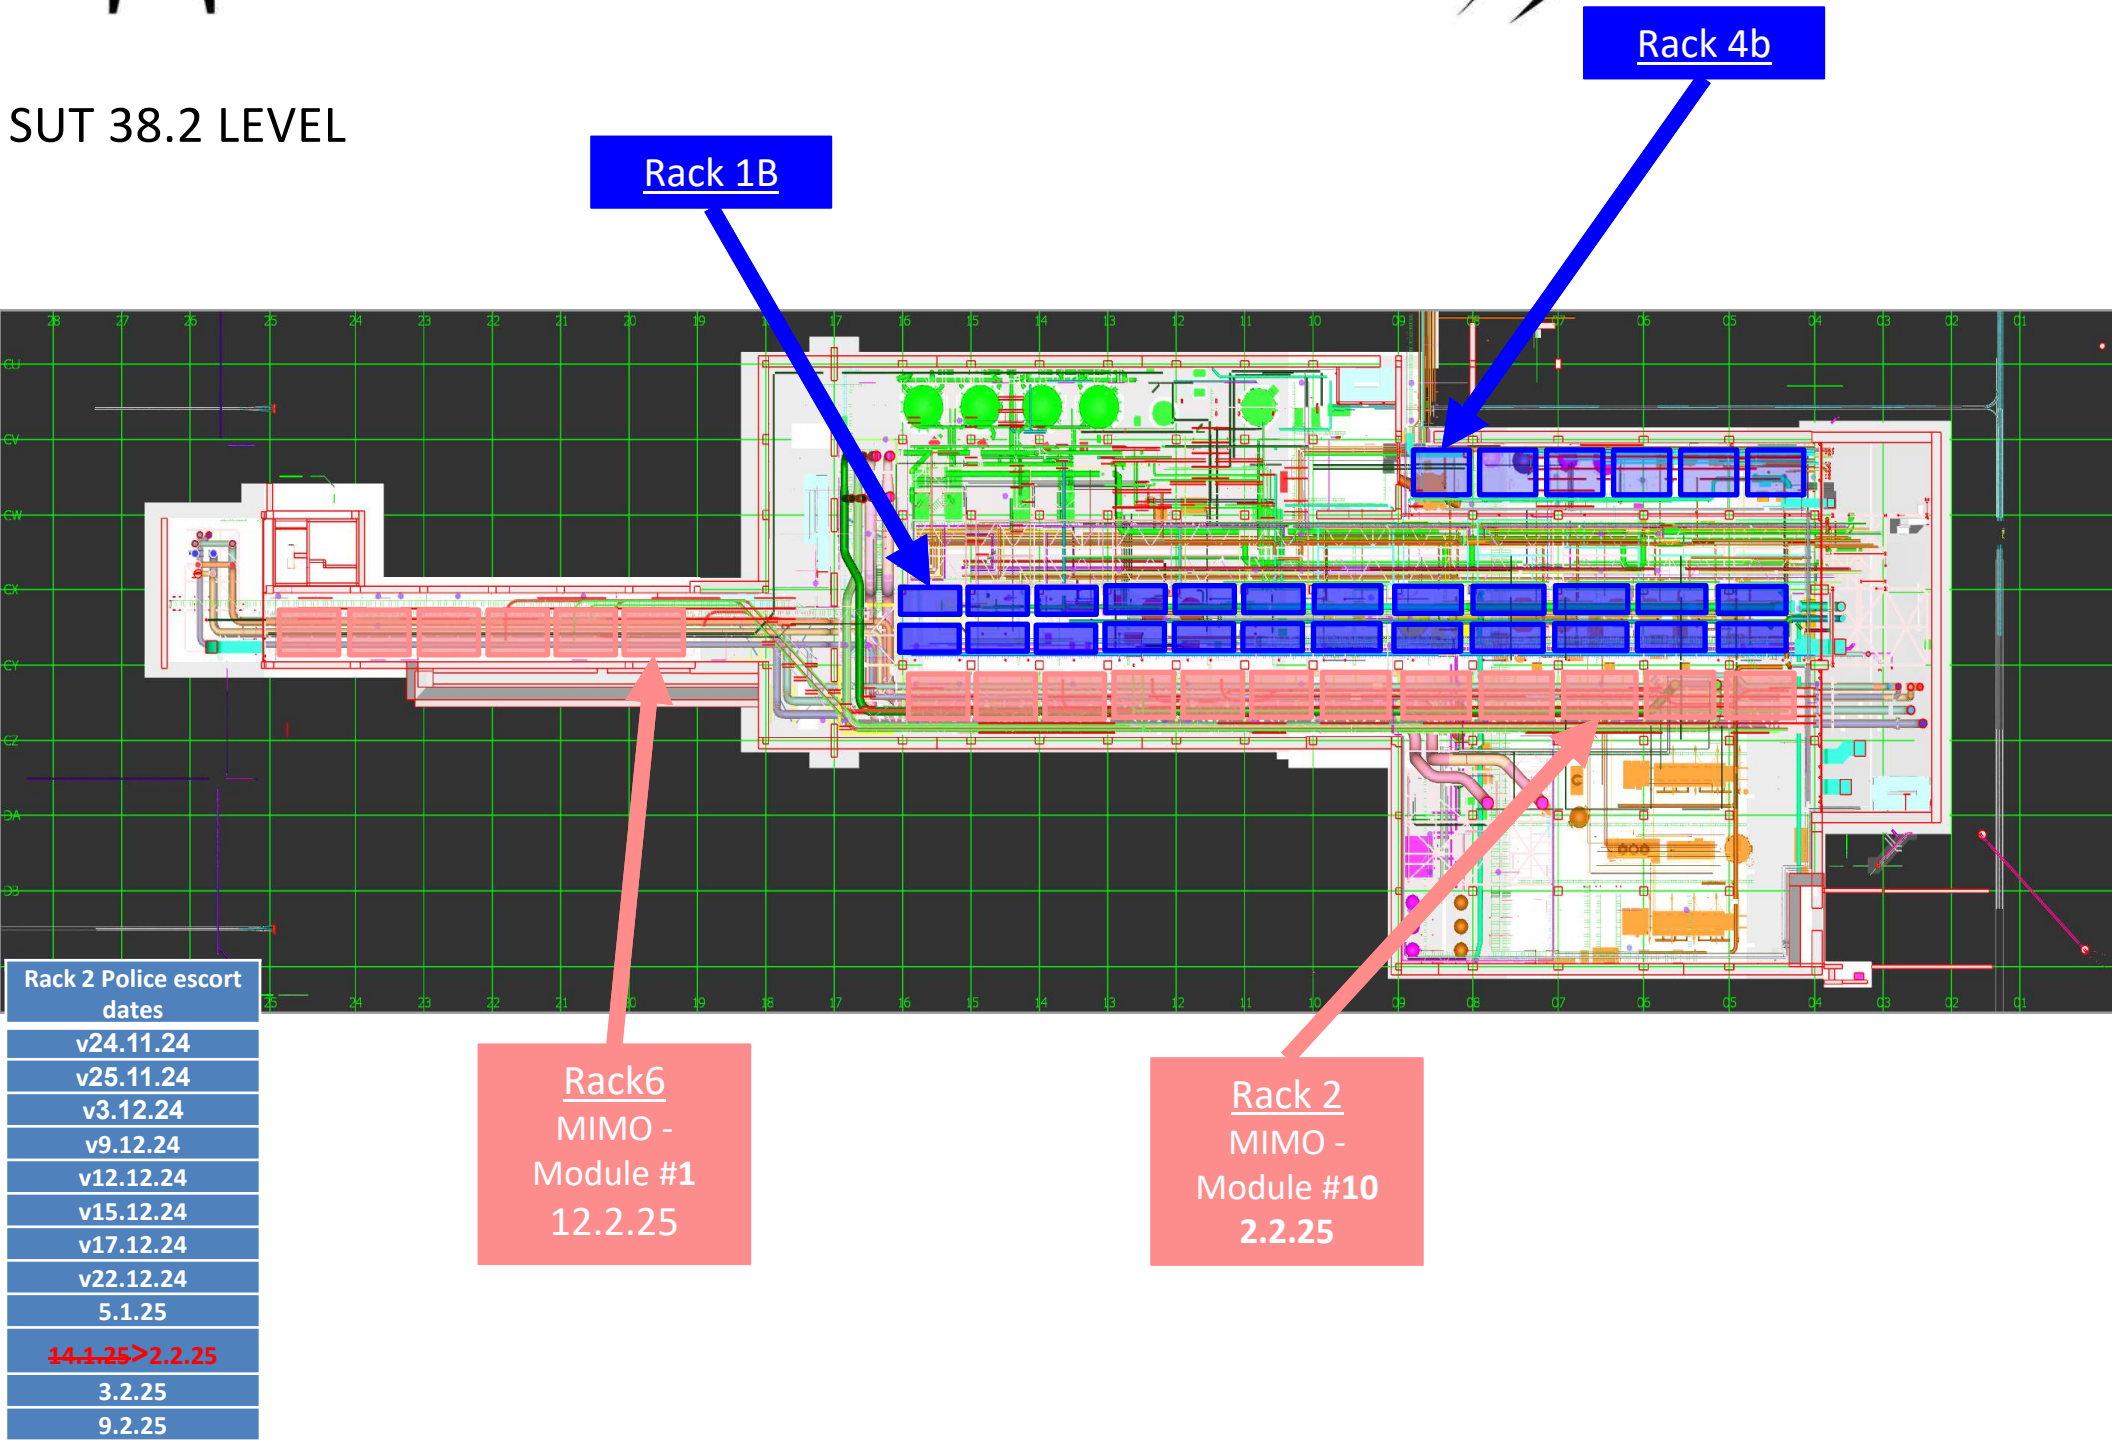


SUBFAB BUILDOUT MOD 1

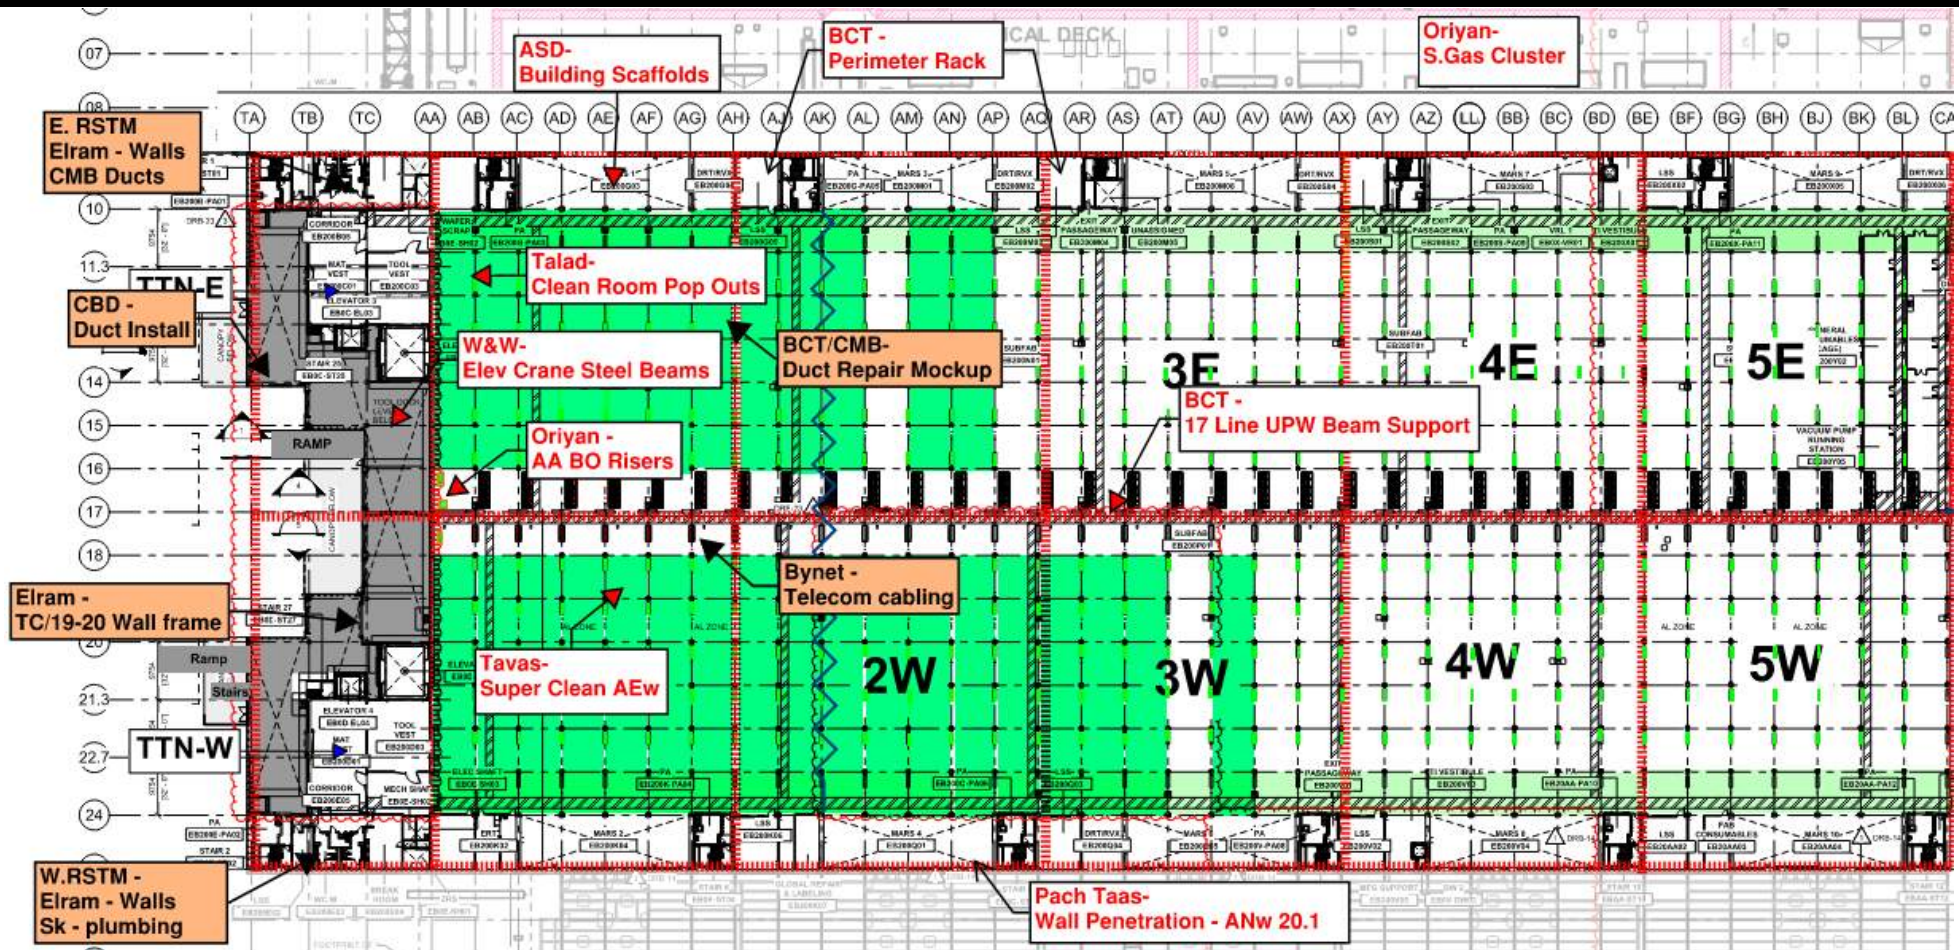


SUBFAB CRC TOPCOAT


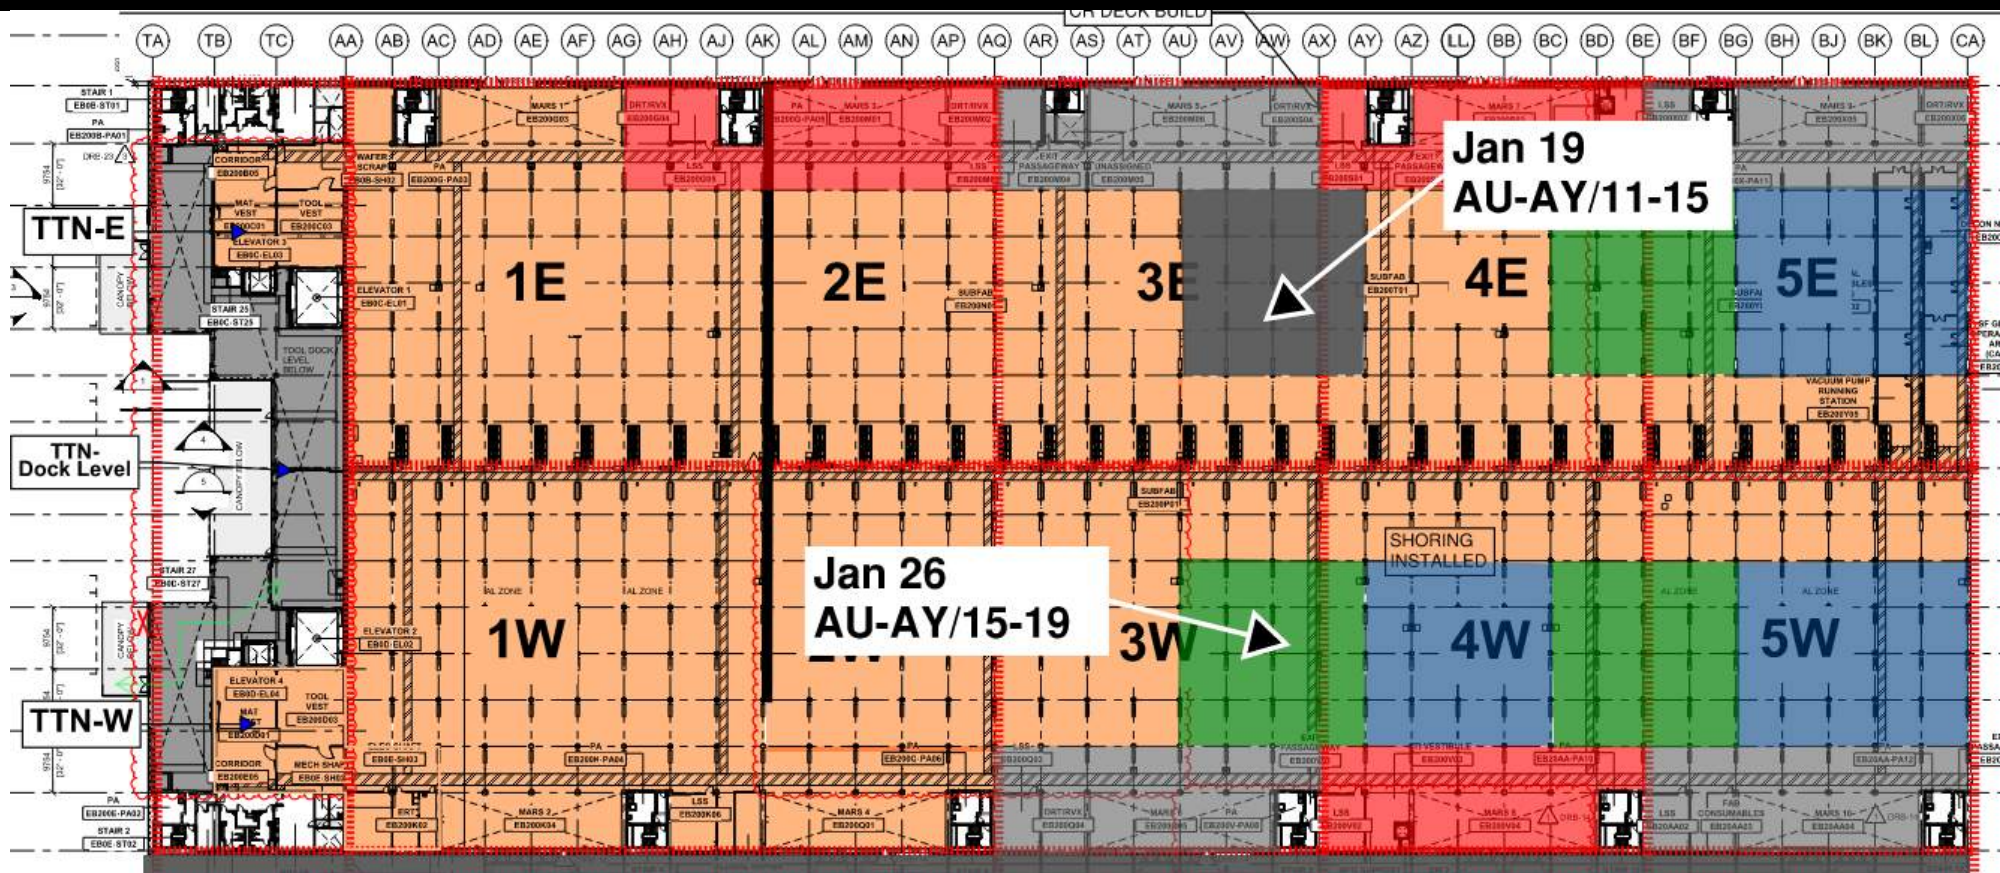



BCT Pressure Test Today


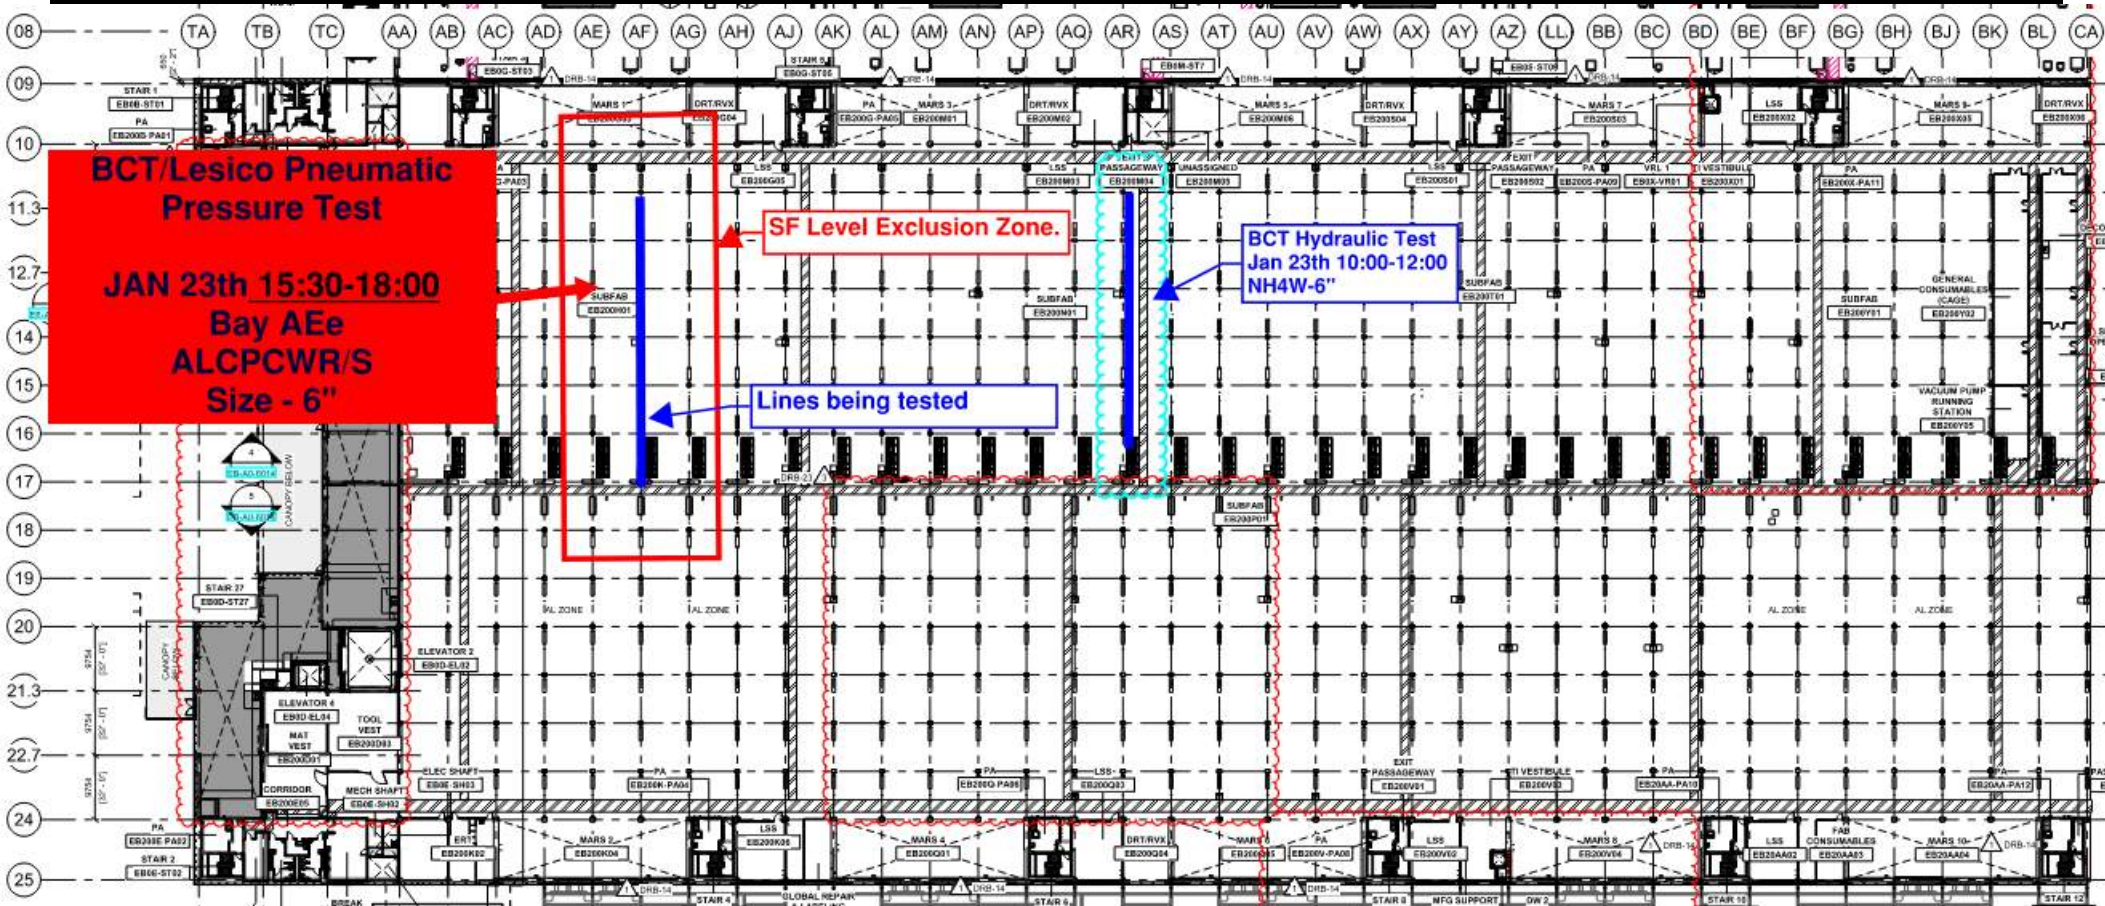




SUBFAB BUILDOUT MOD 2

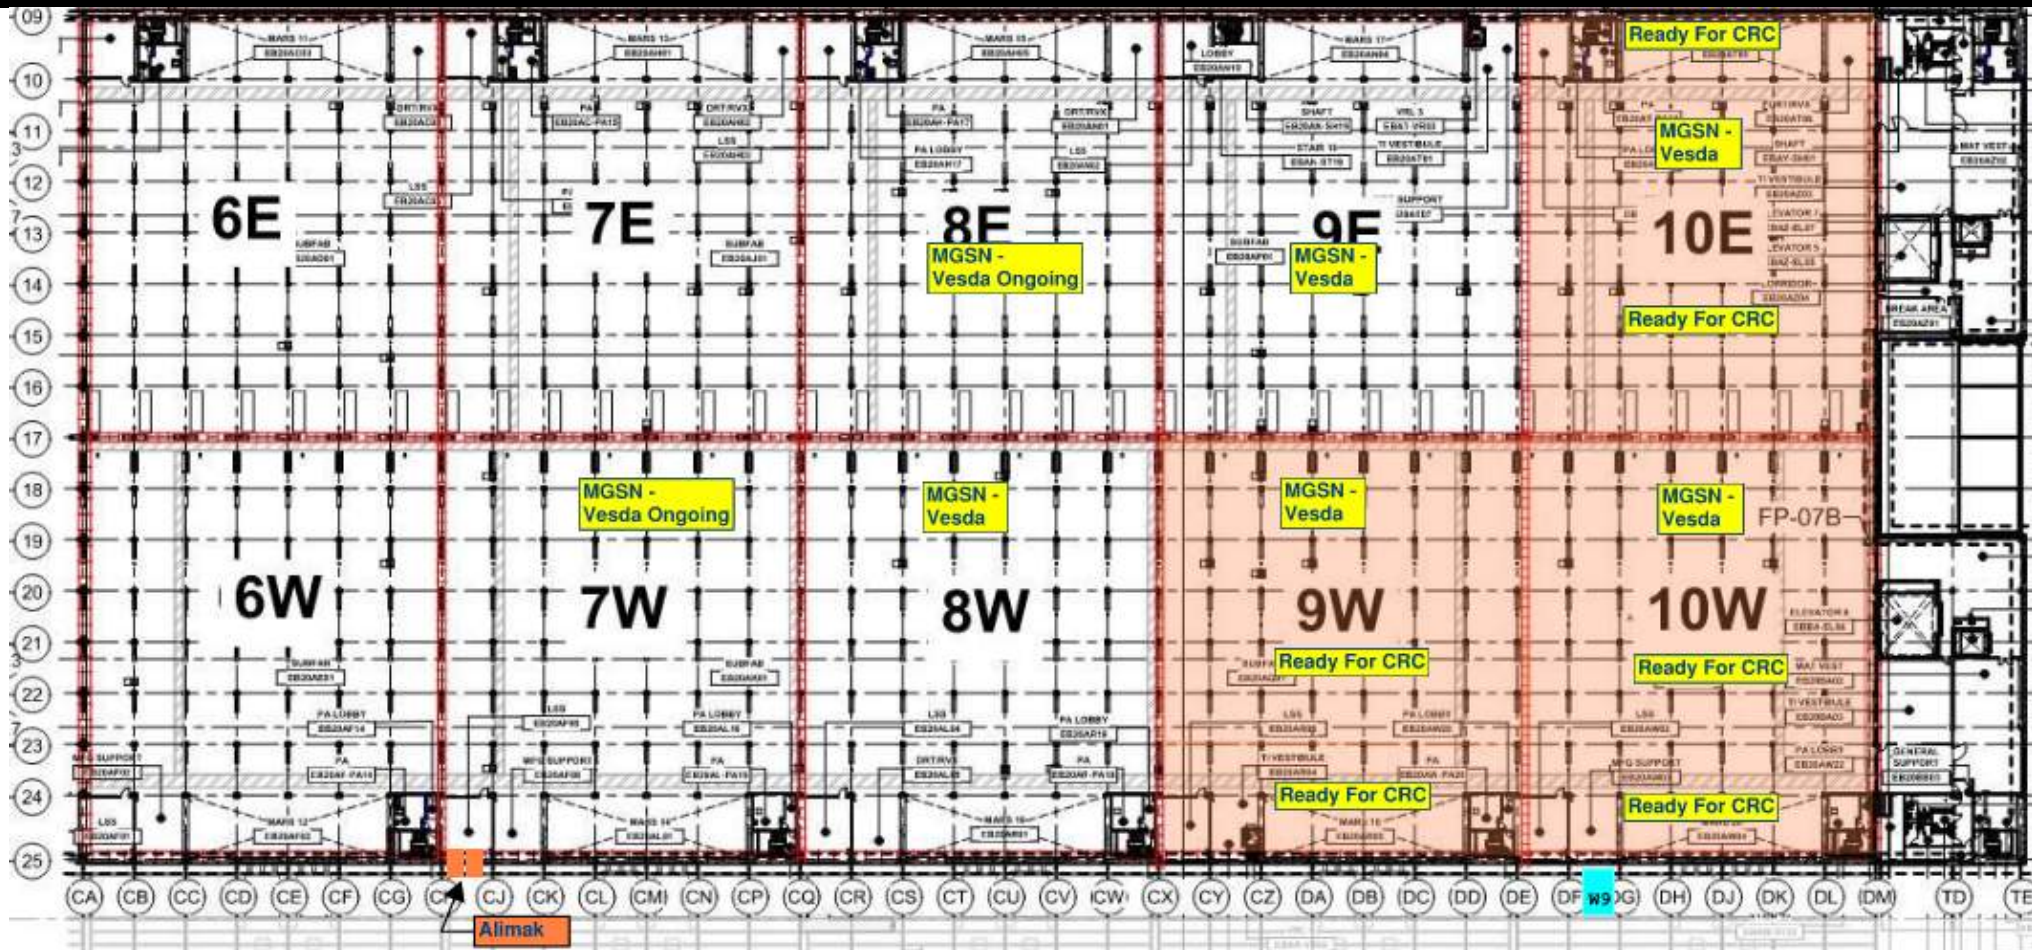

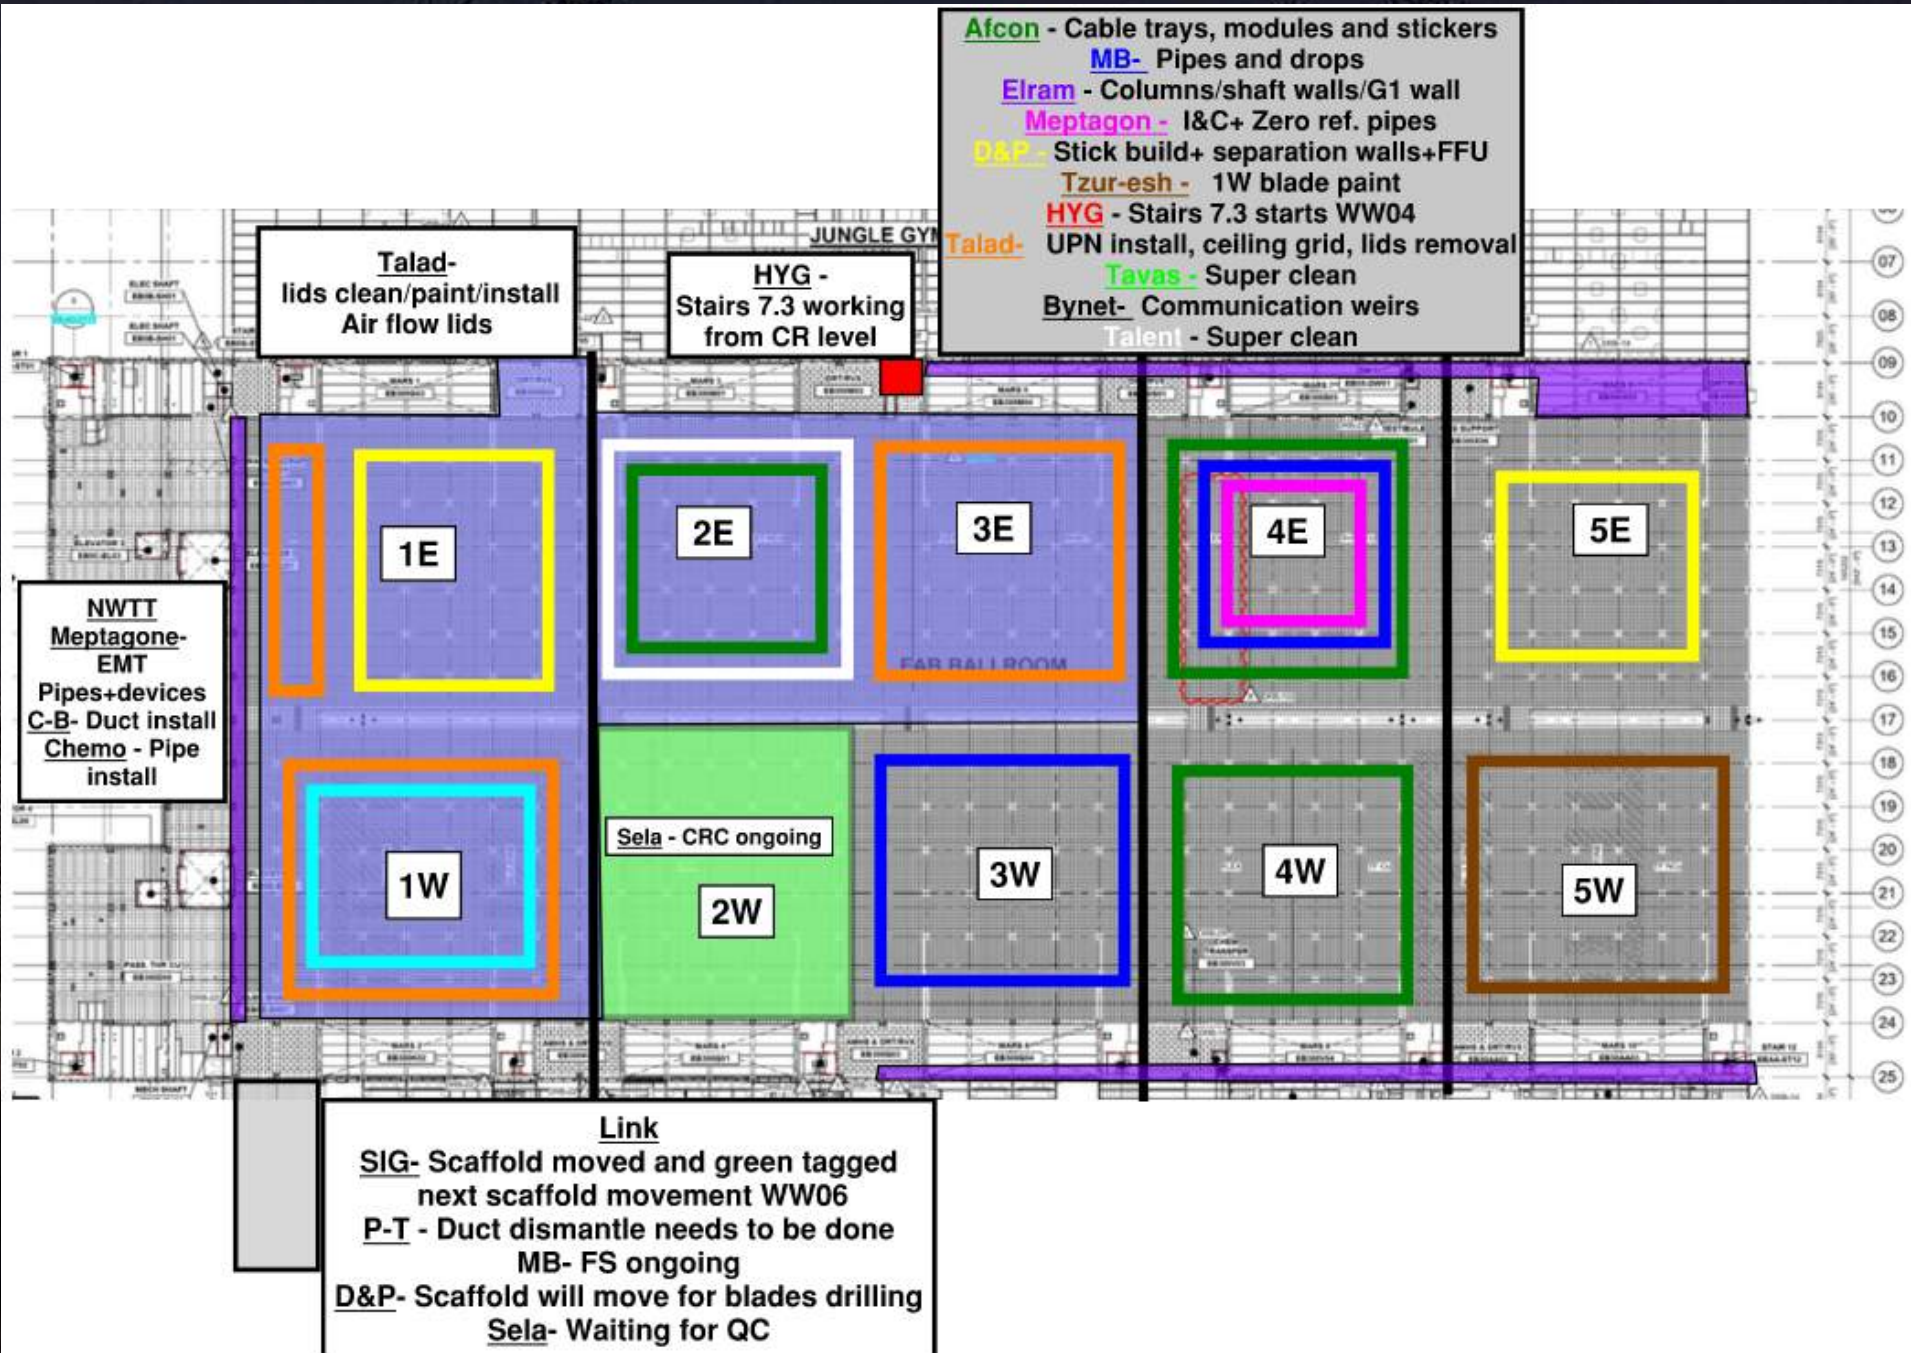

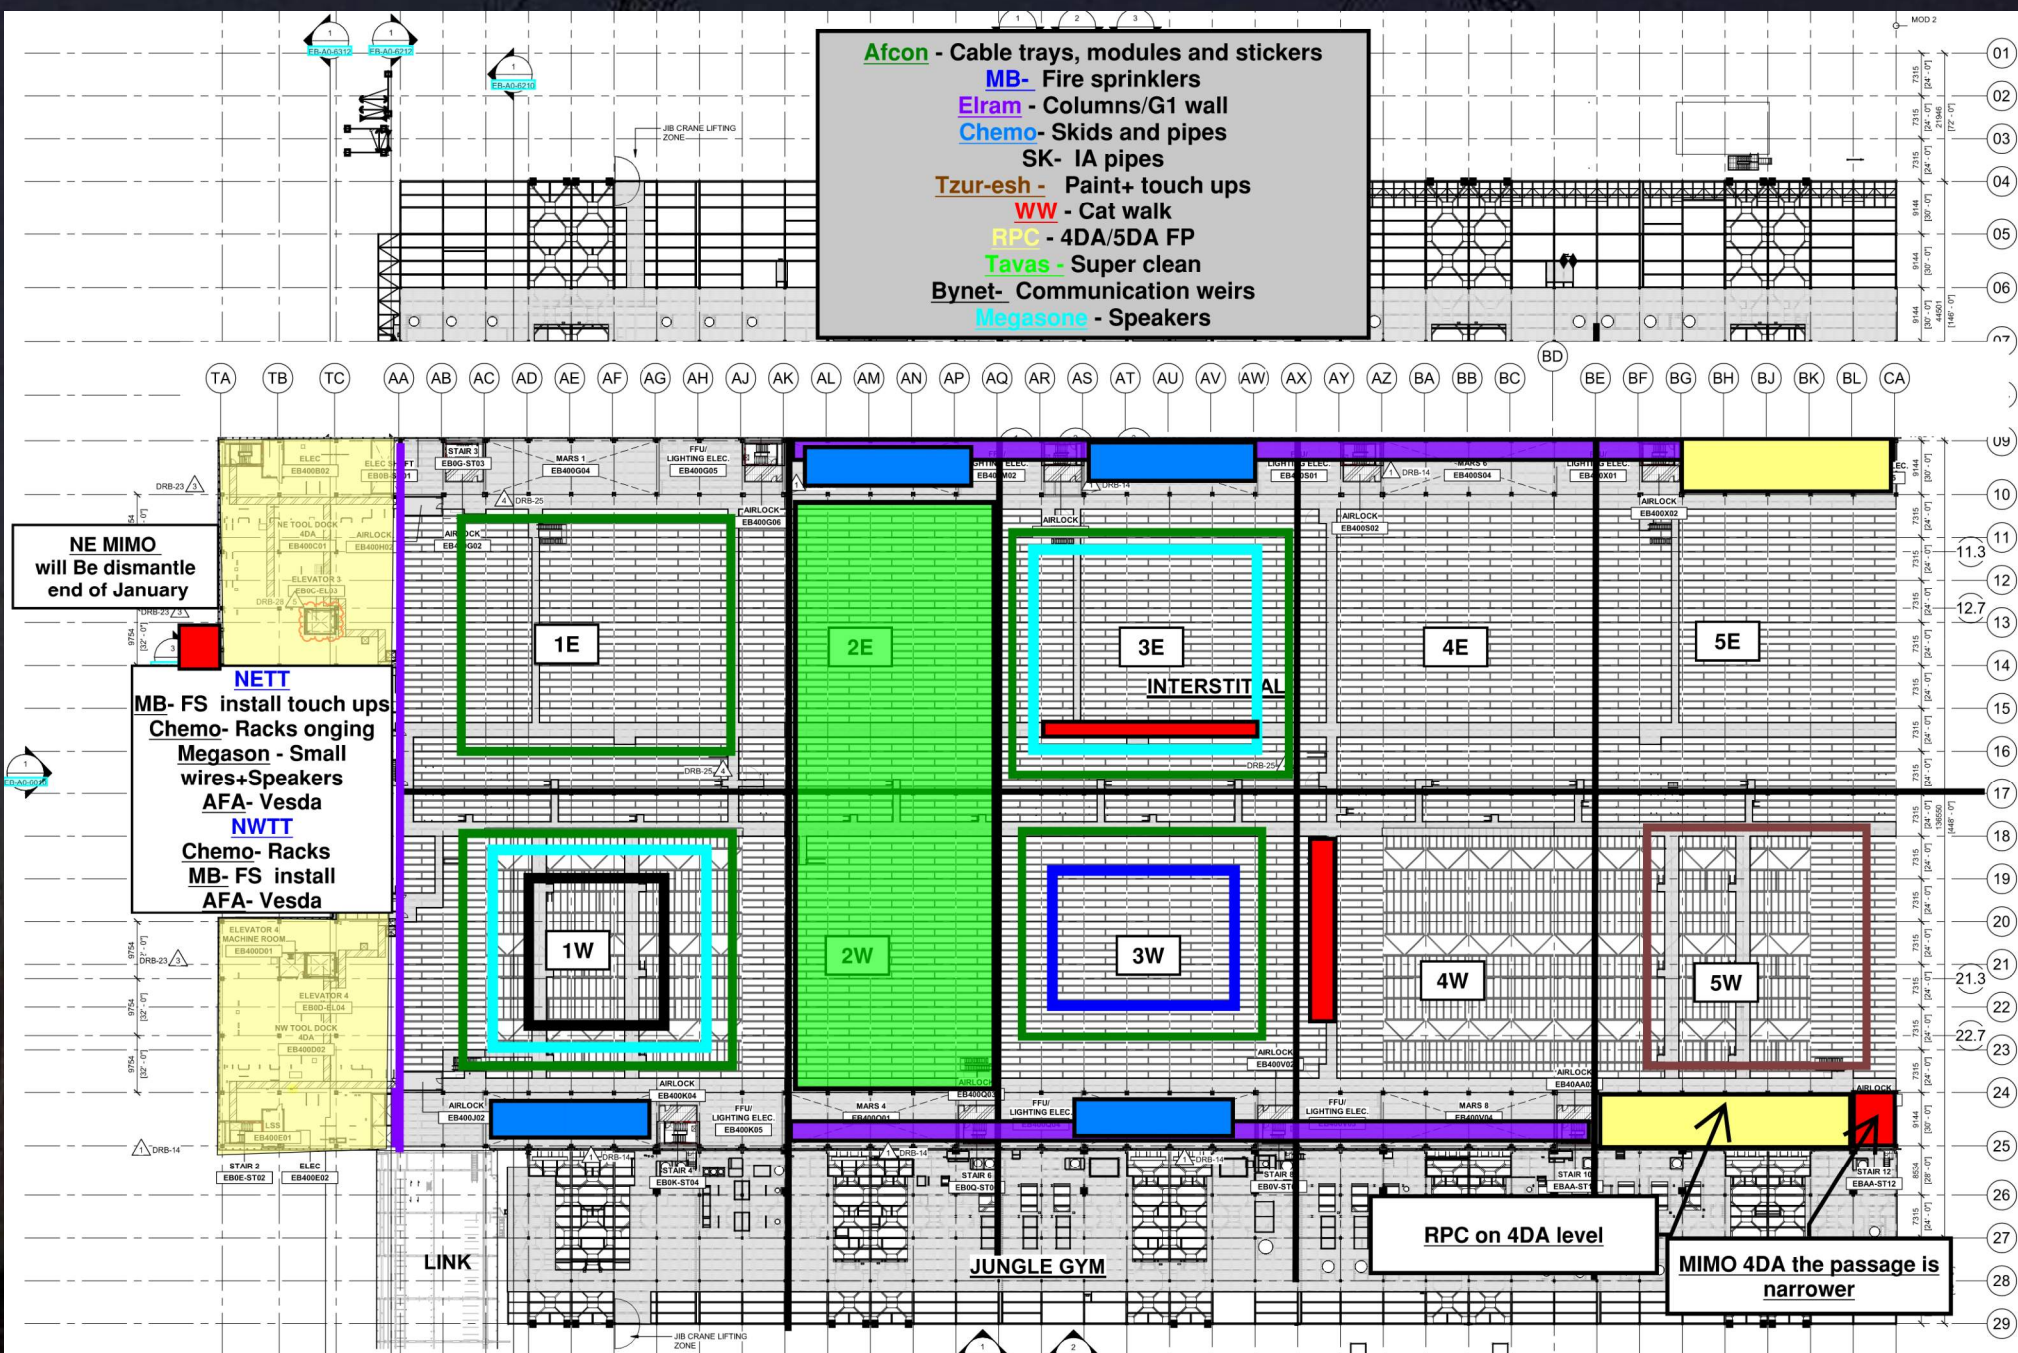

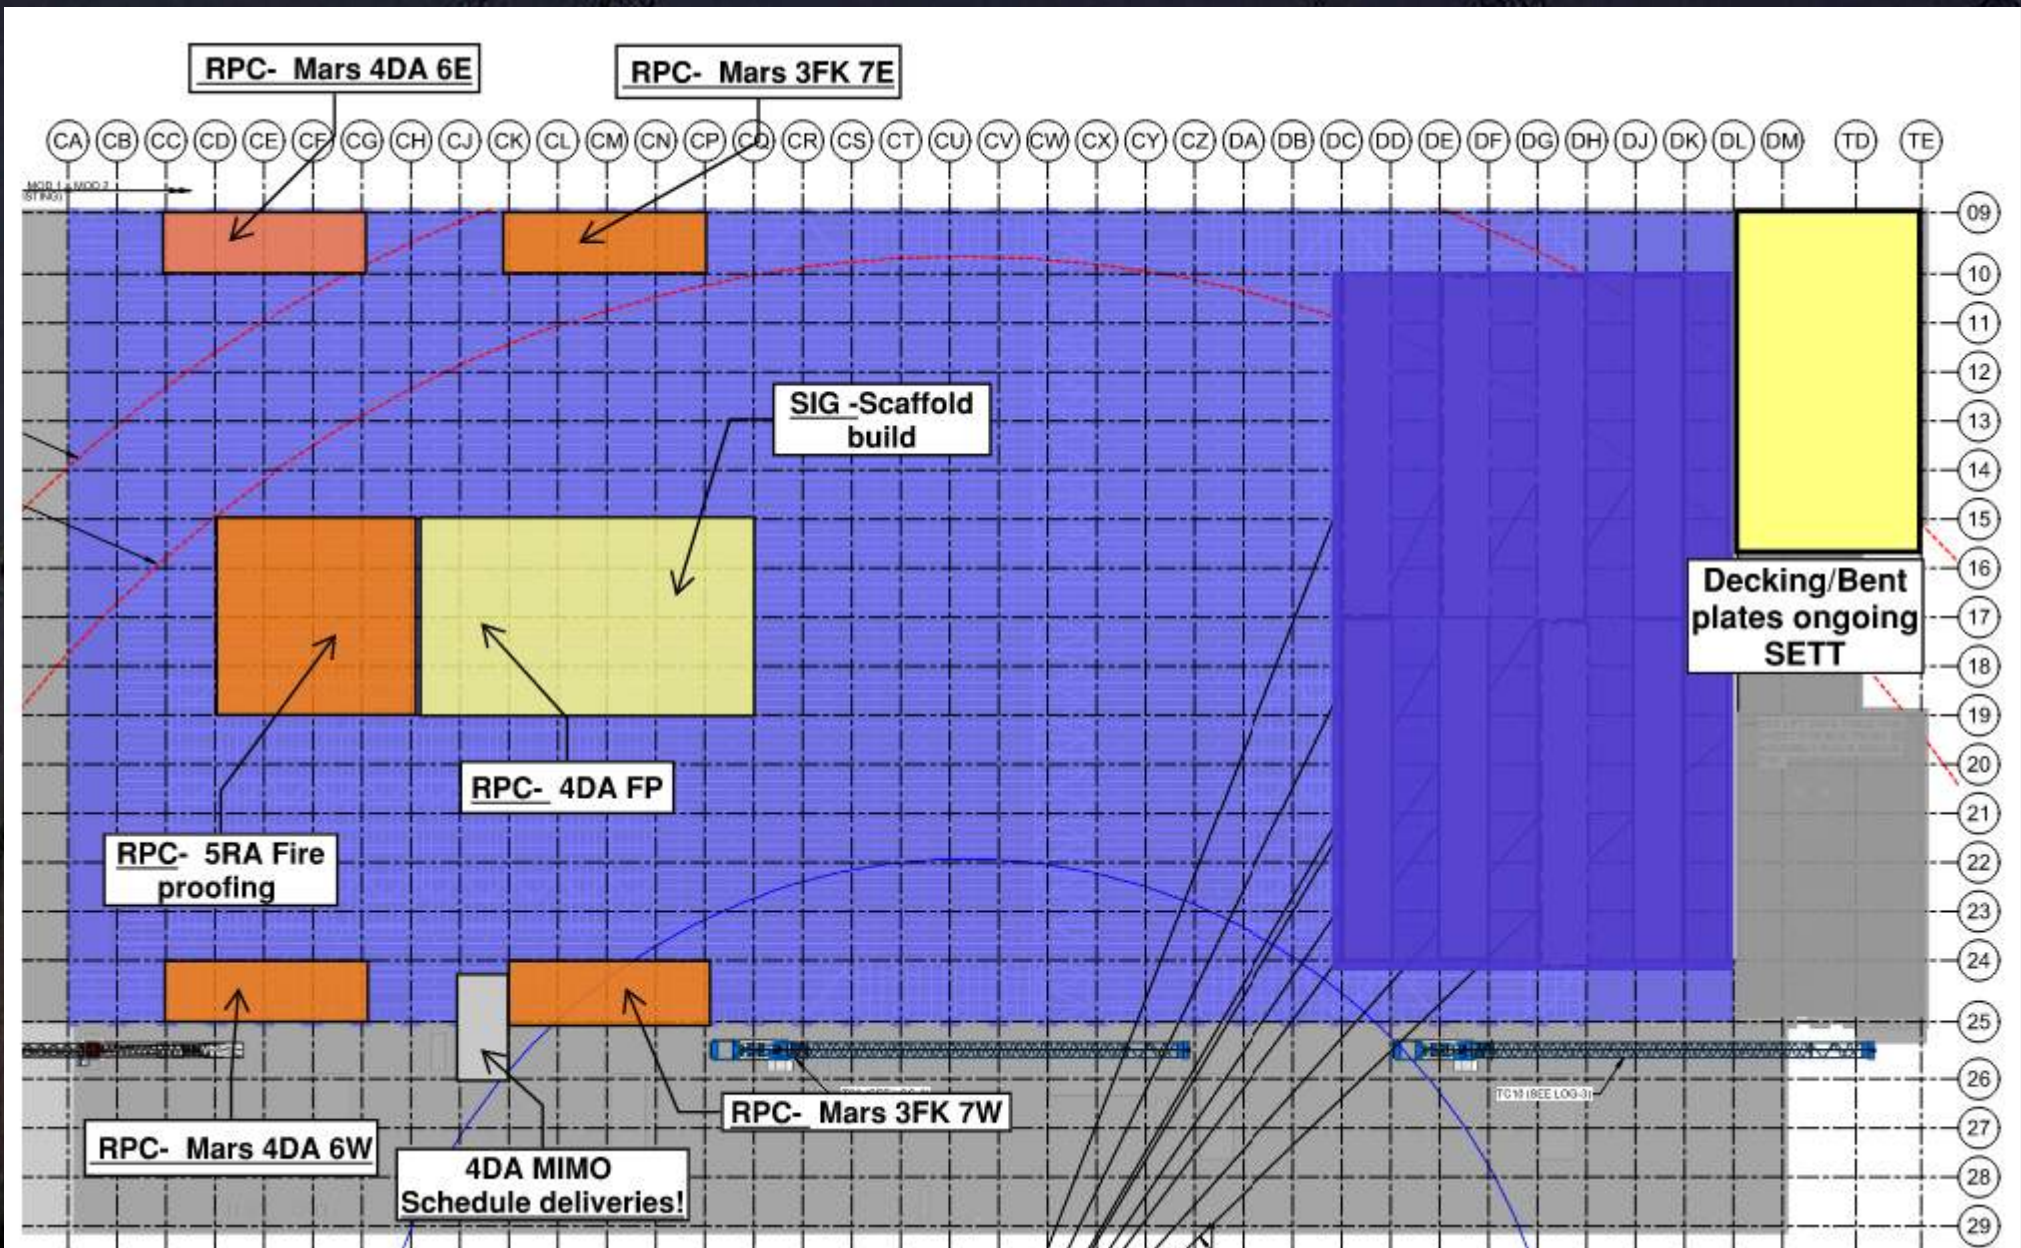

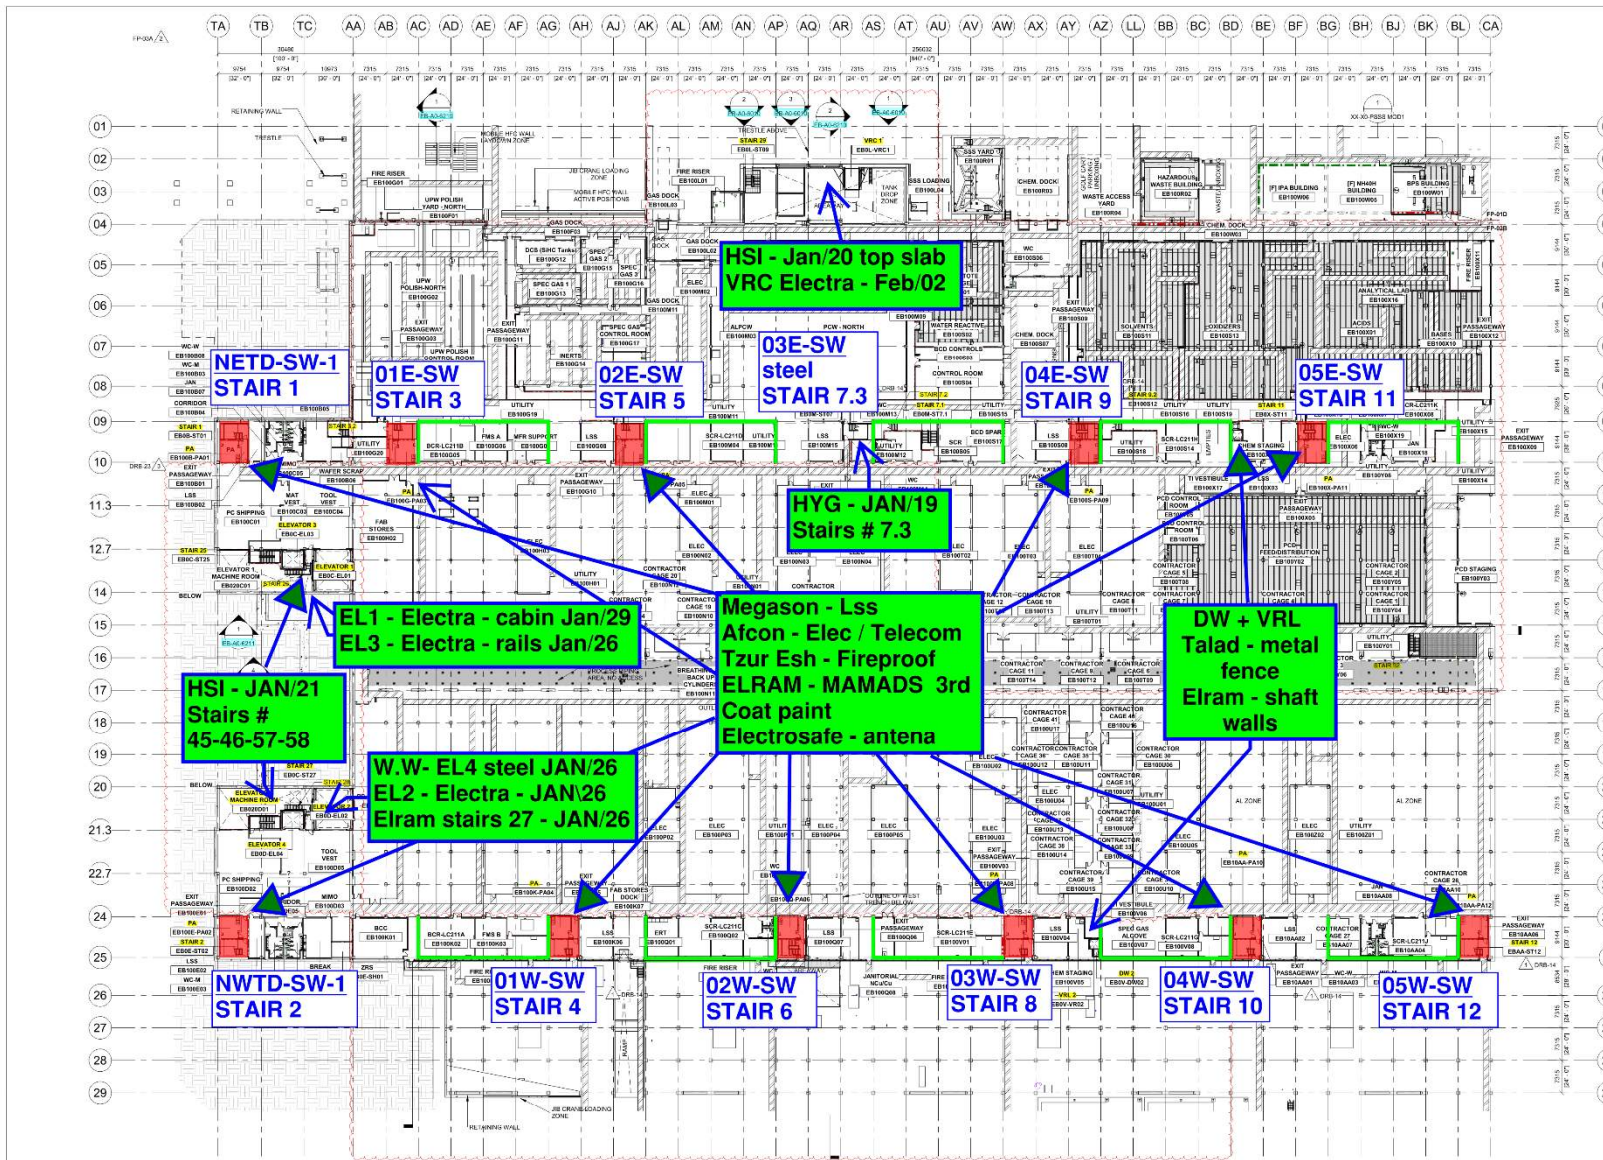

- GENERAL NOTES**
- FOR ARCHITECTURAL SYMBOLS, LEGENDS, AND ABBREVIATIONS, REFER TO DRAWING 00-00000.
 - REFER TO SPECIFICATION SECTION 01.11.10, SUMMARY OF WORK AND SCHEDULE, FOR A SUMMARY OF THE WORK AND SCHEDULE. THE SCHEDULE OF WORK IS SUBJECT TO CHANGE WITHOUT NOTICE. THE SCHEDULE OF WORK IS SUBJECT TO CHANGE WITHOUT NOTICE.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.
 - FOR EXISTING WALL, ROOF, AND FLOOR FINISHES, REFER TO DRAWING 00-00000.

KEYED NOTES:

- ROOM TAG**
- ROOM NAME
- ROOM NUMBER OR ST/EL/DW/VOL/PA NUMBER
- BUILDING SECTION
- STAIR/ELEVATOR/VOL/PA NUMBERING DOES NOT INCLUDE FLOOR COORDS.
- LEGEND**
- EXISTING WALL, ROOF, AND FLOOR FINISHES
- EXISTING WALL, ROOF, AND FLOOR FINISHES
- EXISTING WALL, ROOF, AND FLOOR FINISHES

ISSUE FOR CONSTRUCTION: DB-03	AV	12/05/22
ISSUE FOR CONSTRUCTION: DB-04	AV	06/01/22
ISSUE FOR CONSTRUCTION: DB-14	AV	06/01/22
ISSUE FOR CONSTRUCTION: DB-15	AV	06/01/22

Jacobs
2001 N.W. 4th Avenue, 3rd Floor
Portland, Oregon 97201

ISRAEL - FCE

intel

**LC21 - ARCHITECTURAL
UTILITY LEVEL - 1YA
OVERALL
FLOOR PLAN**

EB-A0-1YA-A0AA0

Siding - East FAB - PSSS

BLOWDOWN 30%

[illegible]


[illegible]

Siding - North FAB

100% - BLOWDOWN

	9	10	11	12	13	14	TA	TB	TC	14	14.5	15	15.5	16.5	17.5	18.5	19	19.5	20	TC	TB	TA	20	21	22	23	24	25
Total Installed %	901C / 901C			911A / 912A			911B / 912B			911C / 912C					1011C / 1012C					1011B / 1012B			1011A / 1012A			1001C / 1002C		
	29	29	29	29	0	0	29	29		27	18	9	27	27	27	27	9	18	0	29	29		29	29	29	29	29	
	100%	100%	45%	0%	0%		100%	100%		100%	100%	100%	100%	100%	100%	100%	30%	100%	0%	100%	100%		100%	100%	100%	100%	100%	
29	1	1	0				1	1												1	1		1	1	1	1	1	
28	1	1	0				1	1												1	1		1	1	1	1	1	
27	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
26	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
25	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
24	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
23	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
22	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
21	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
20	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
19	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
18	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
17	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
16	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
15	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
14	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
13	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
12	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
11	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
10	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
9	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
8	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
7	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
6	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
5	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
4	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
3	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
2	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	
1	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	



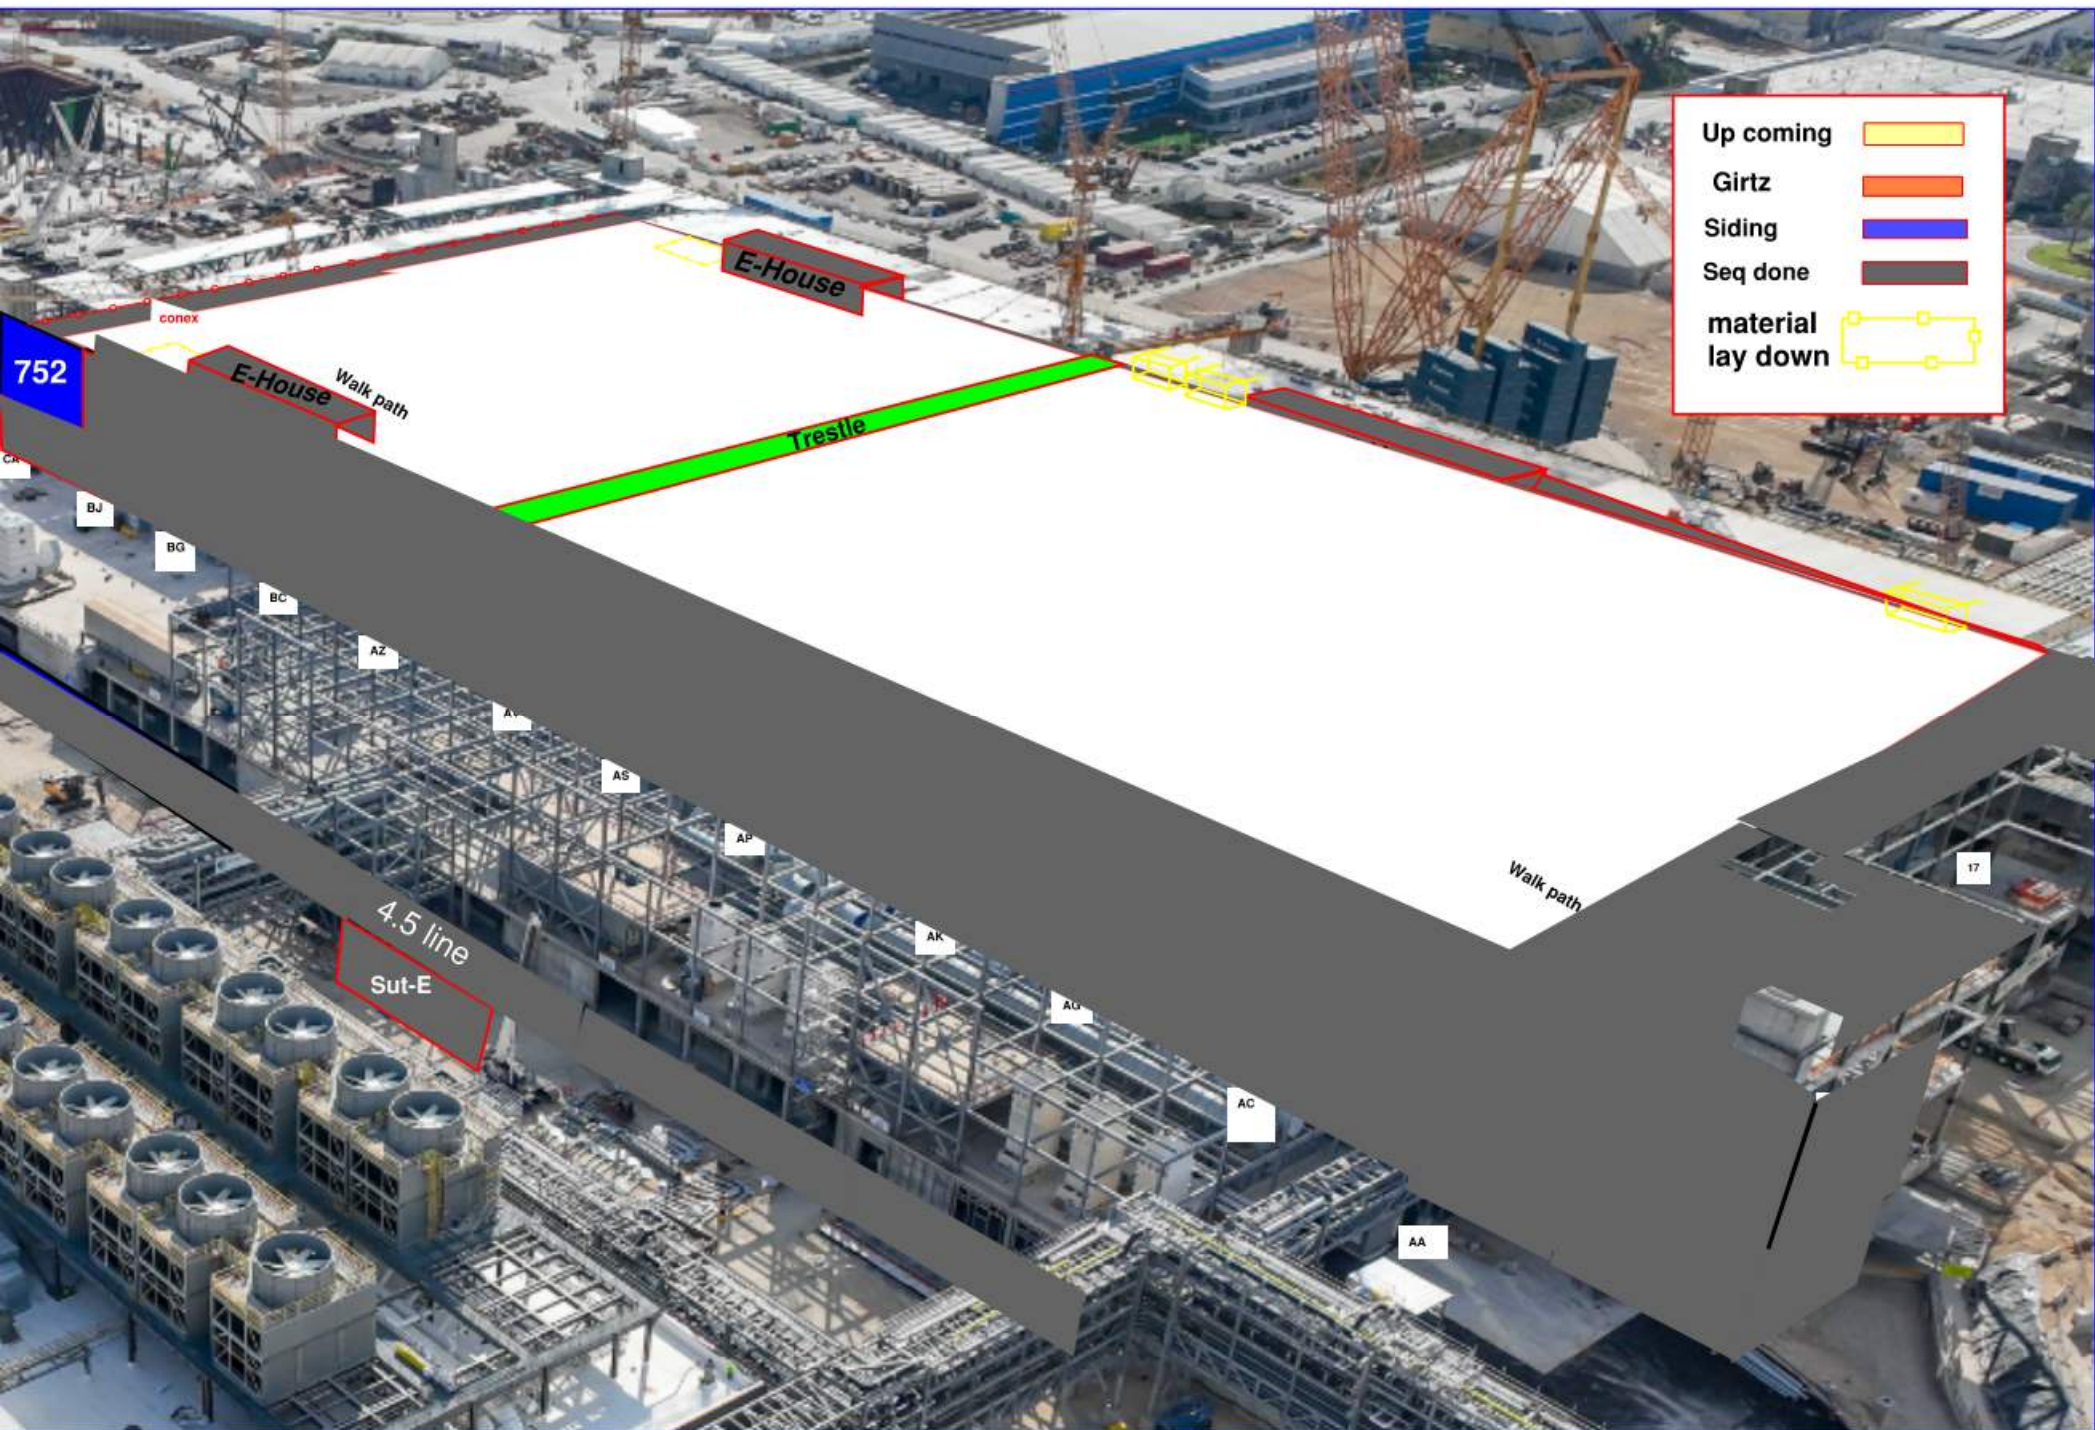


Up coming	
Girtz	
Siding	
Seq done	
material lay down	

PSSS.1

Utility Level 1YA

PSSS Roof 2SA

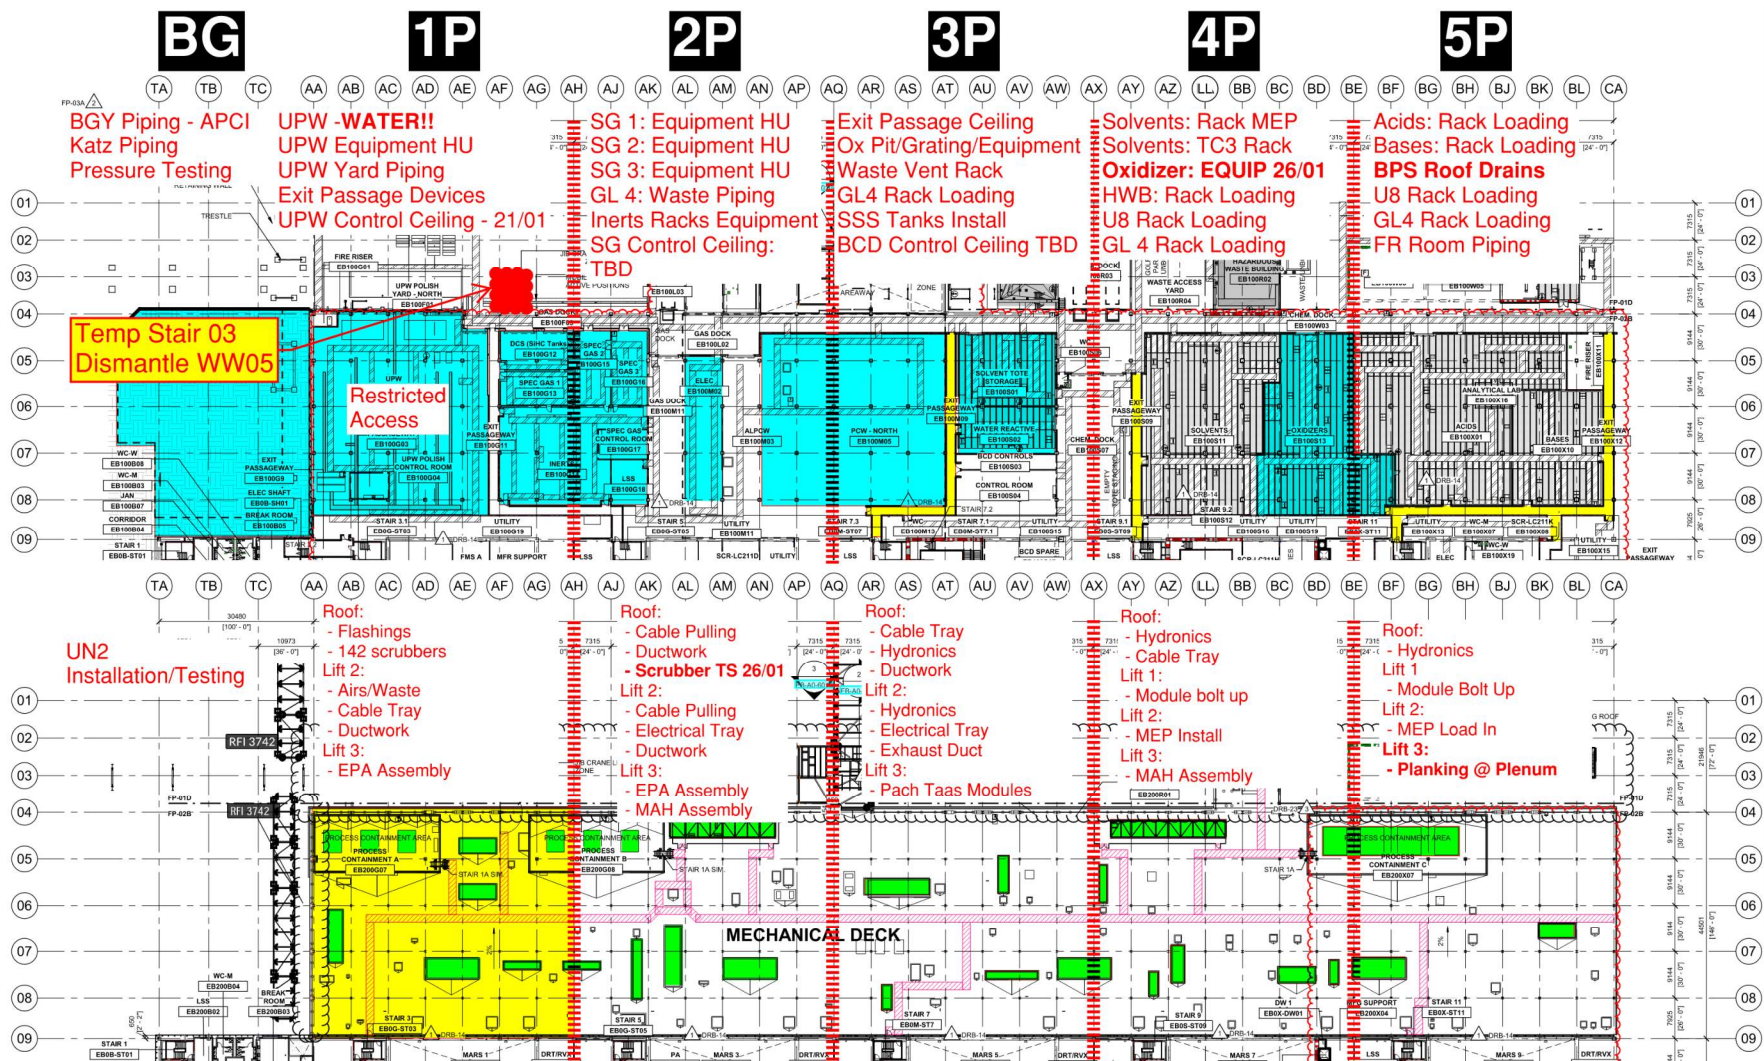

PSSS.2

6P


7P

8P


9P

10P


Utility Level
1YA

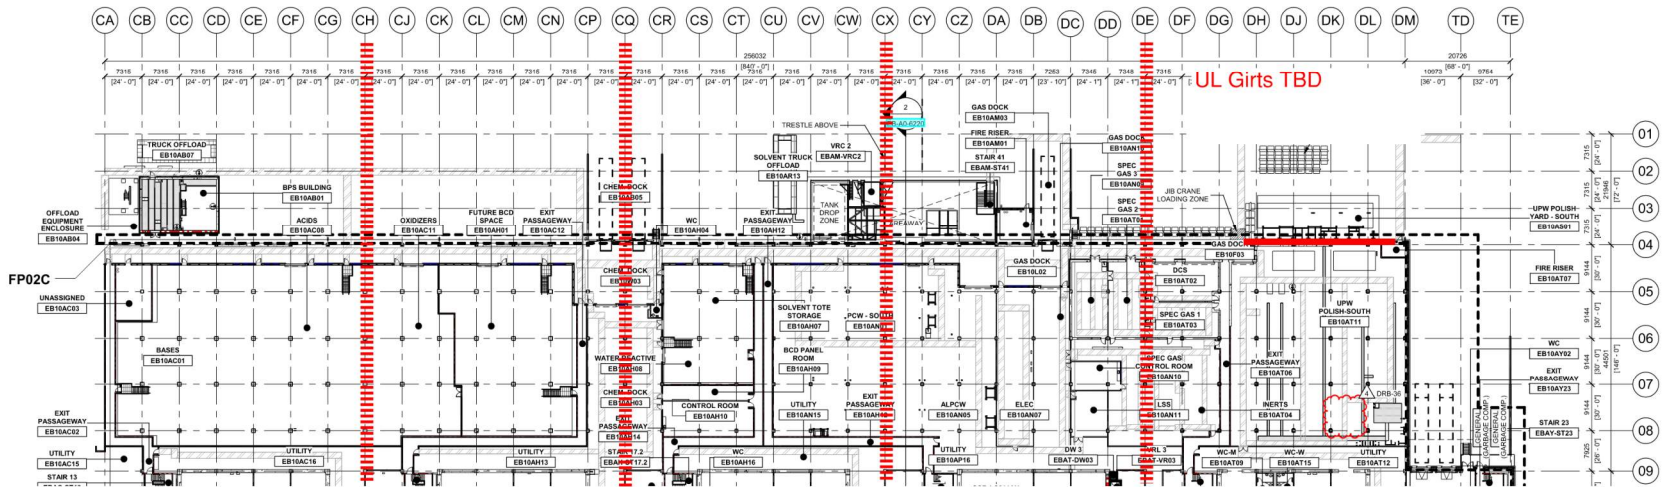


PSSS Roof
2SA

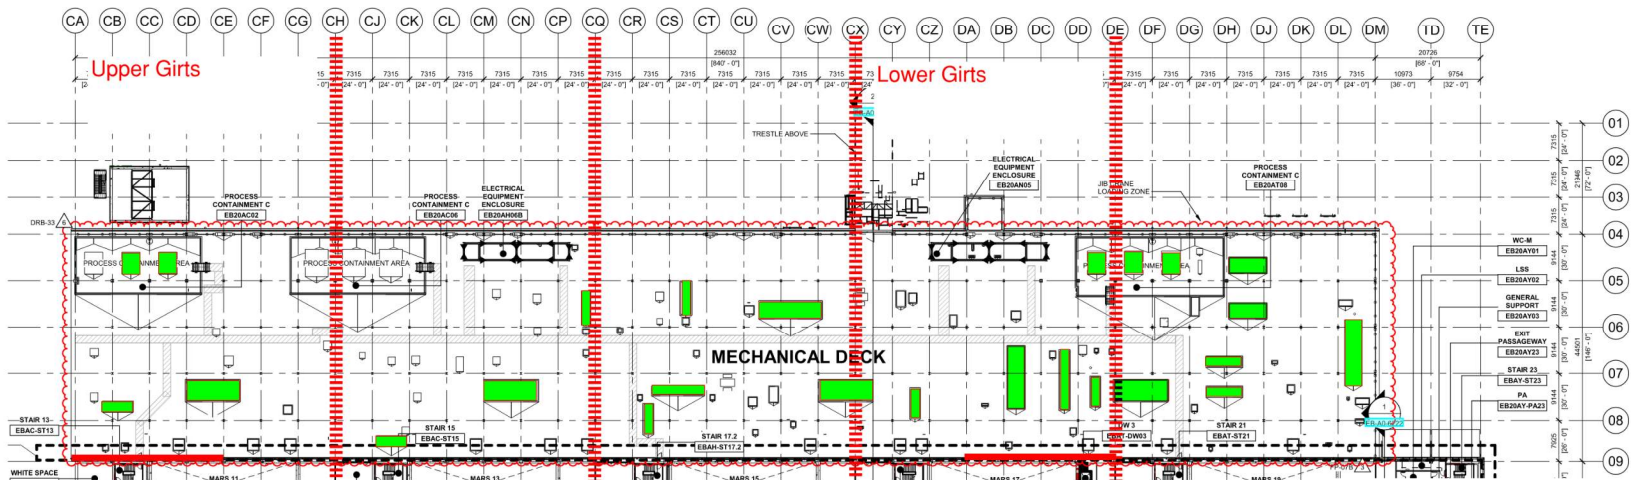



PSSS.1 Pressure Testing

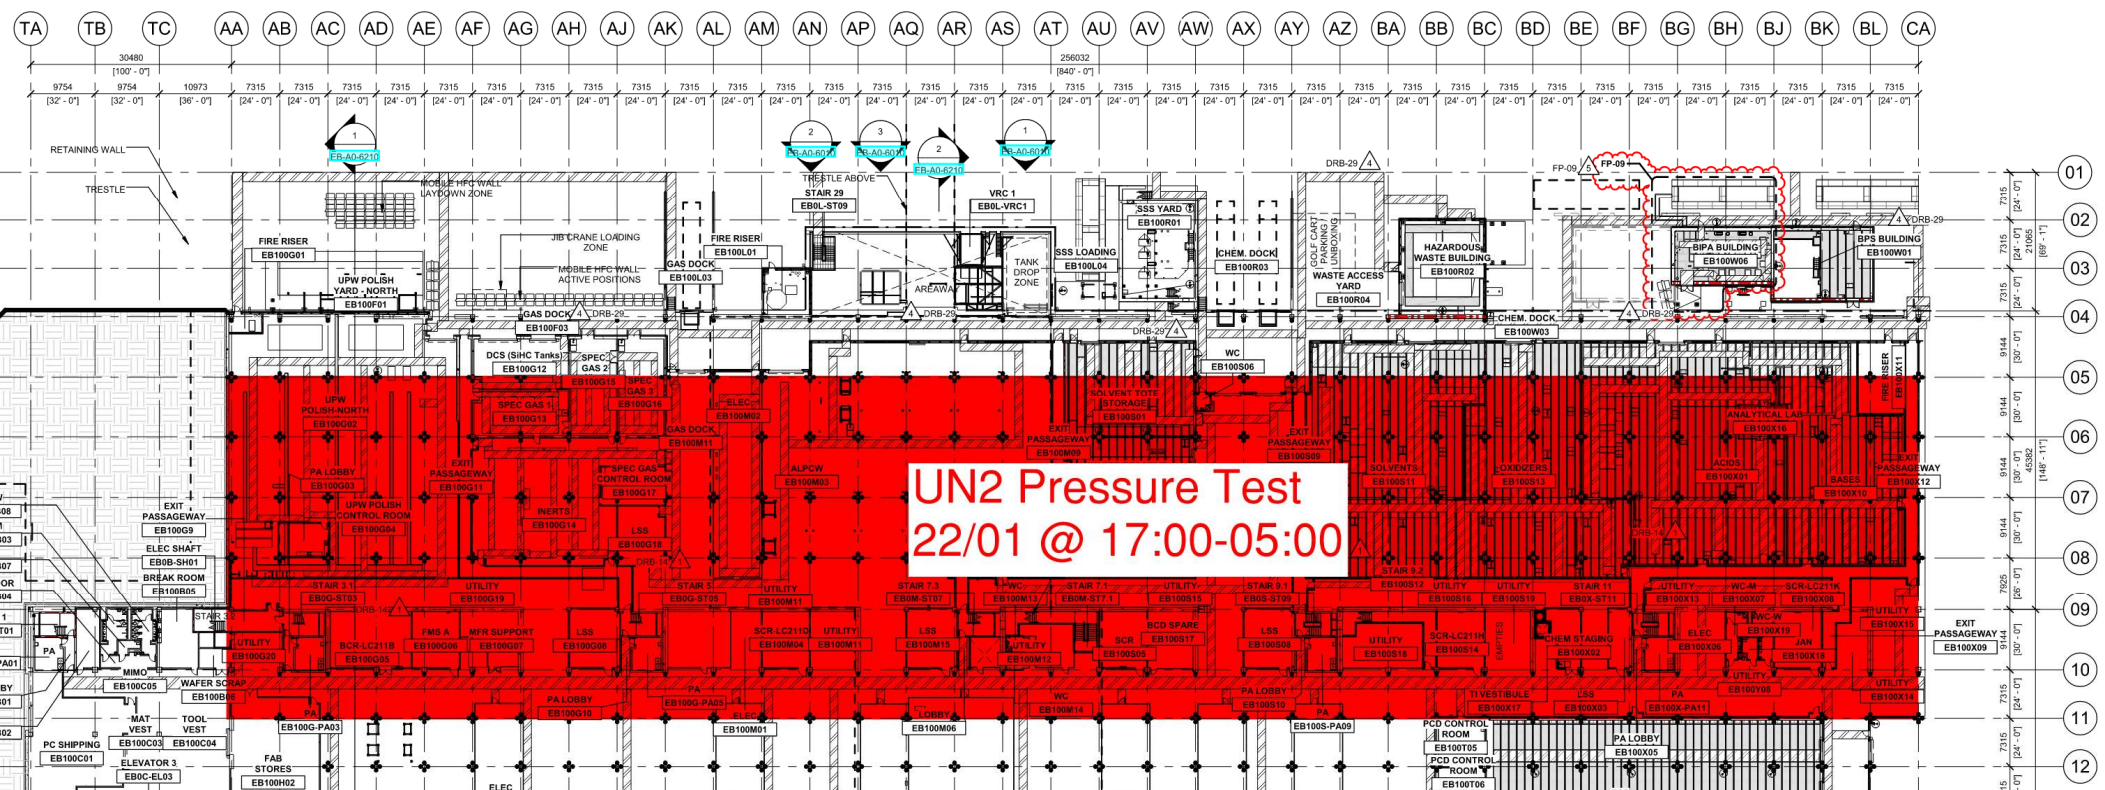





WJG 01J, 02J LIFT 2 & 3

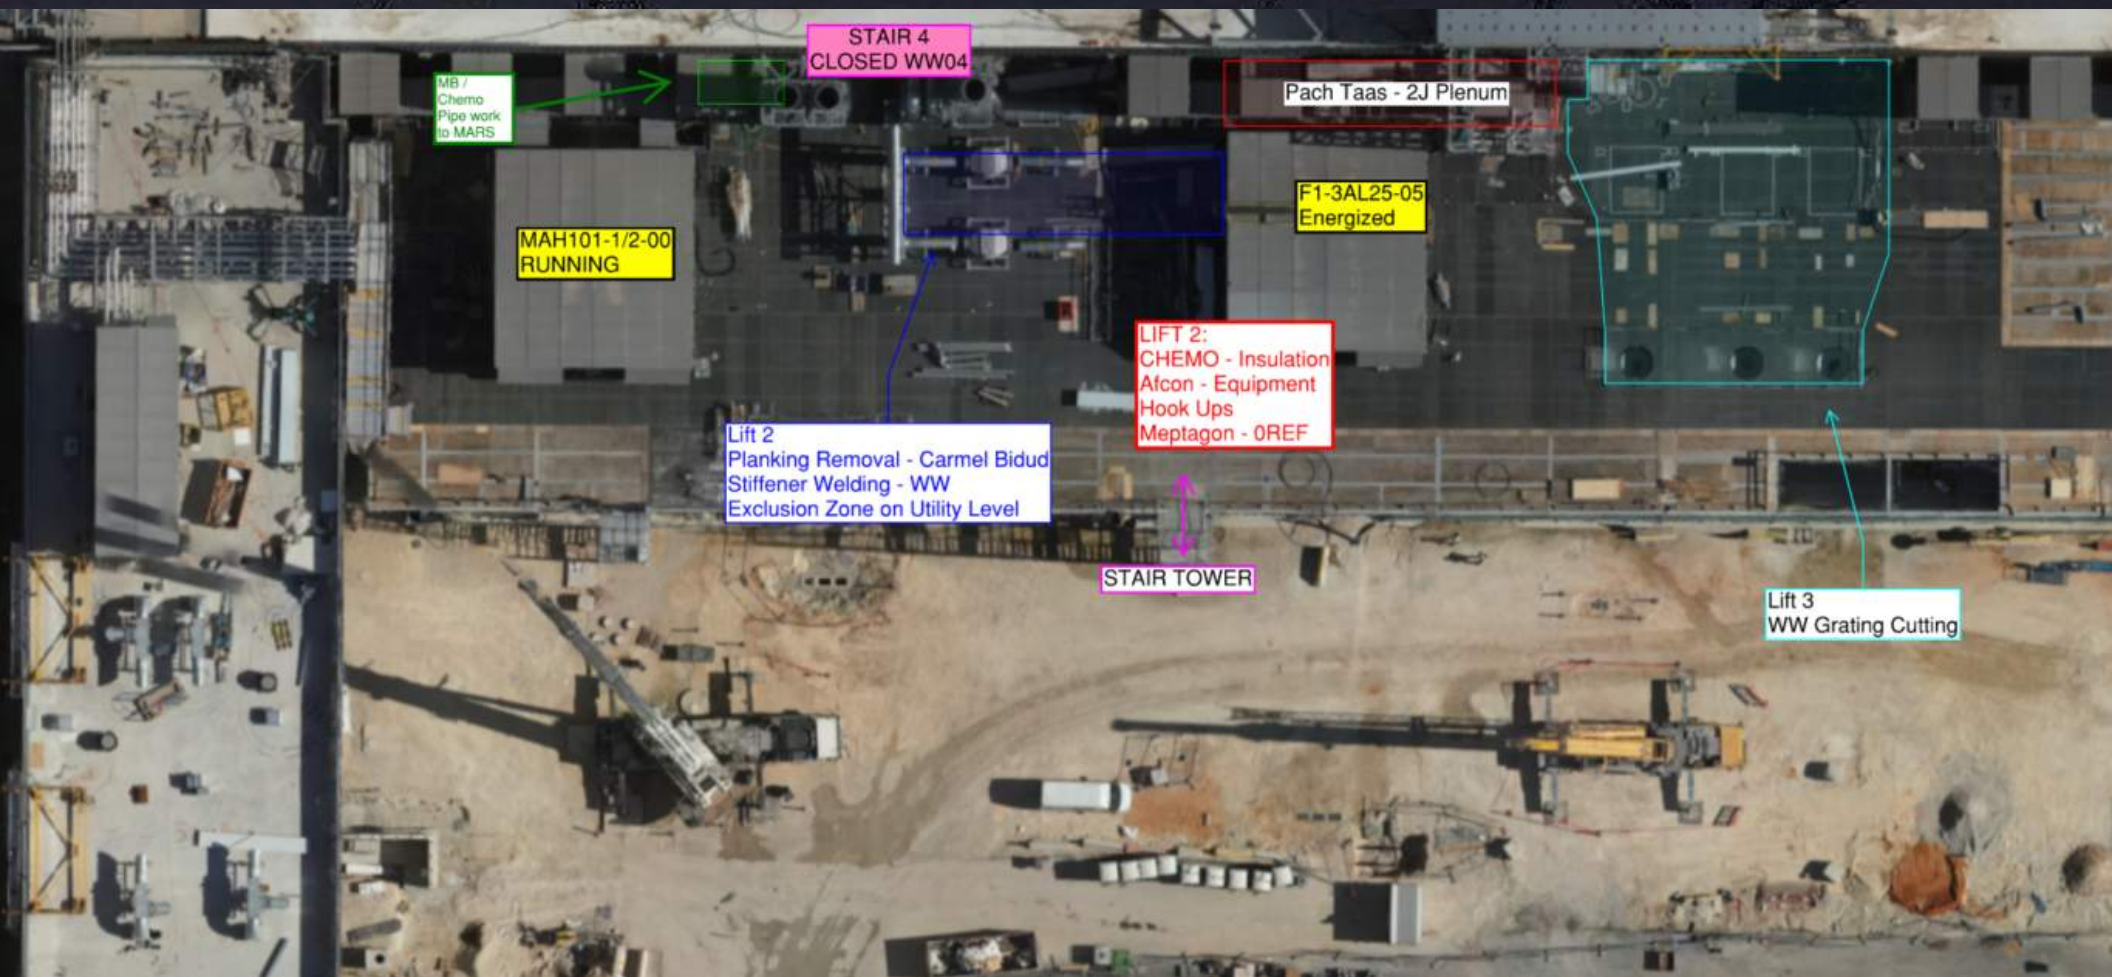




WJG 03J, 04J, 05J LIFT 2 & 3

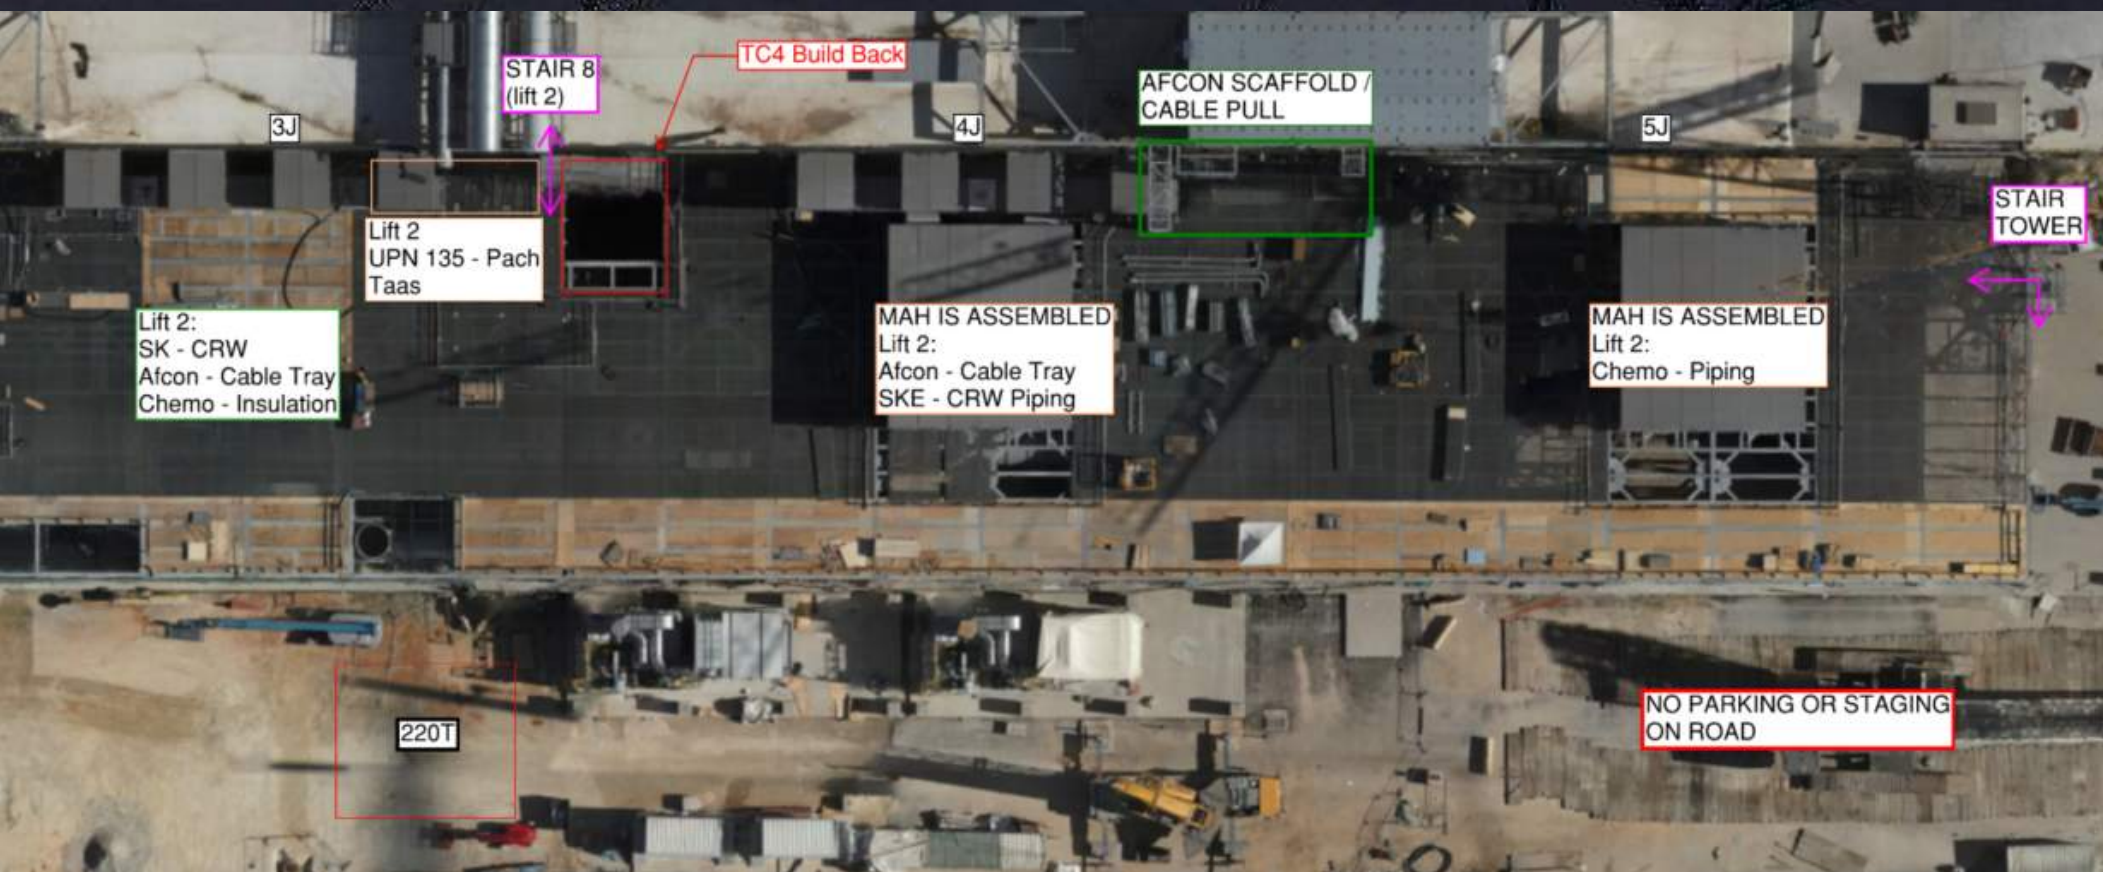





WJG UTILITY LEVEL BUILD OUT

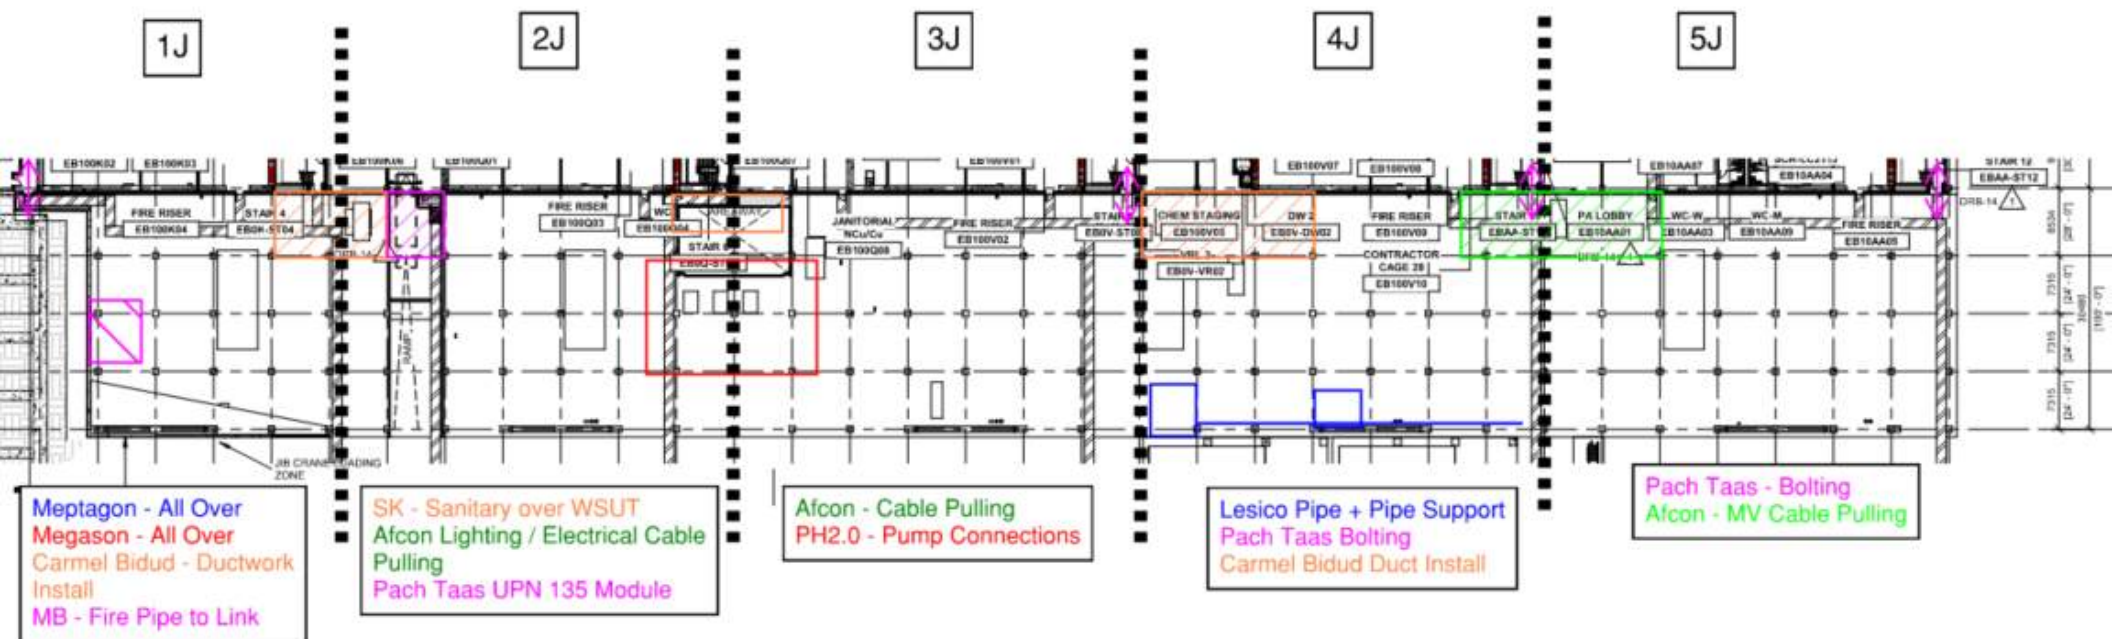

CUB 1

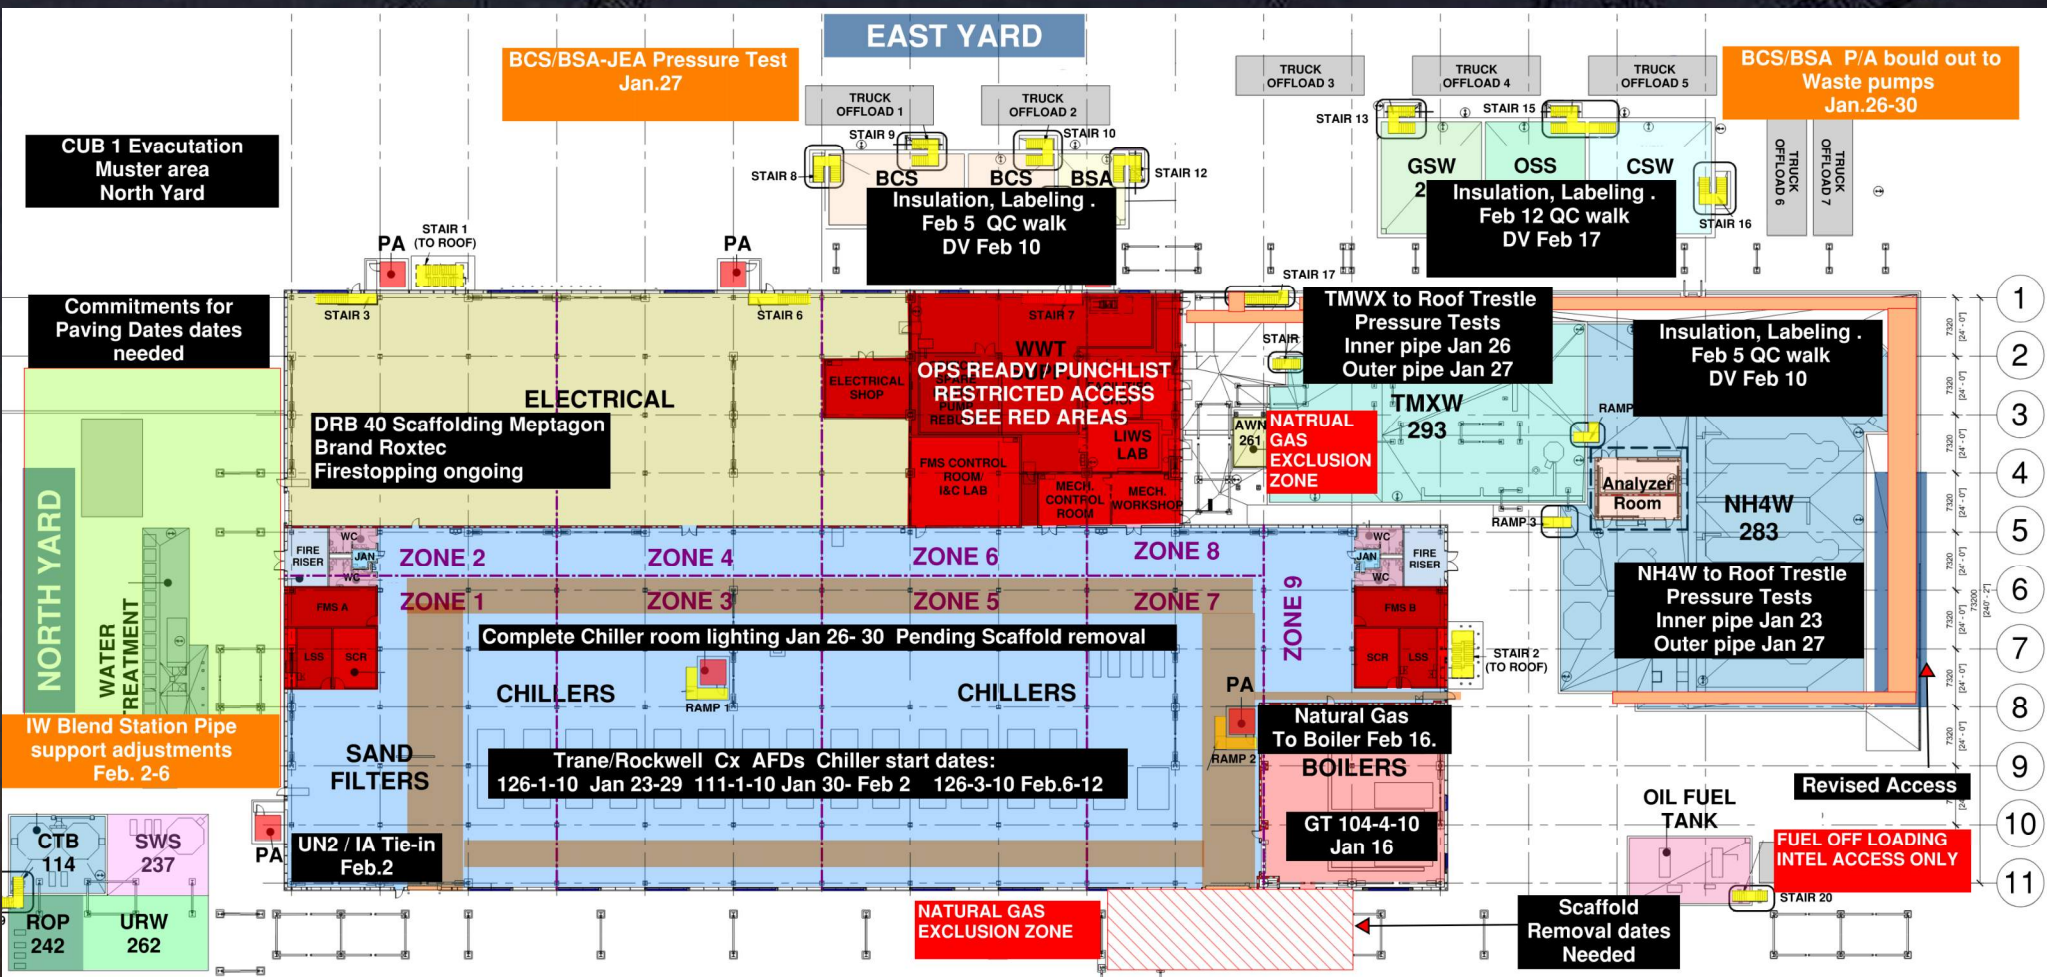


CUB 1 – EXTERIOR/ROOF

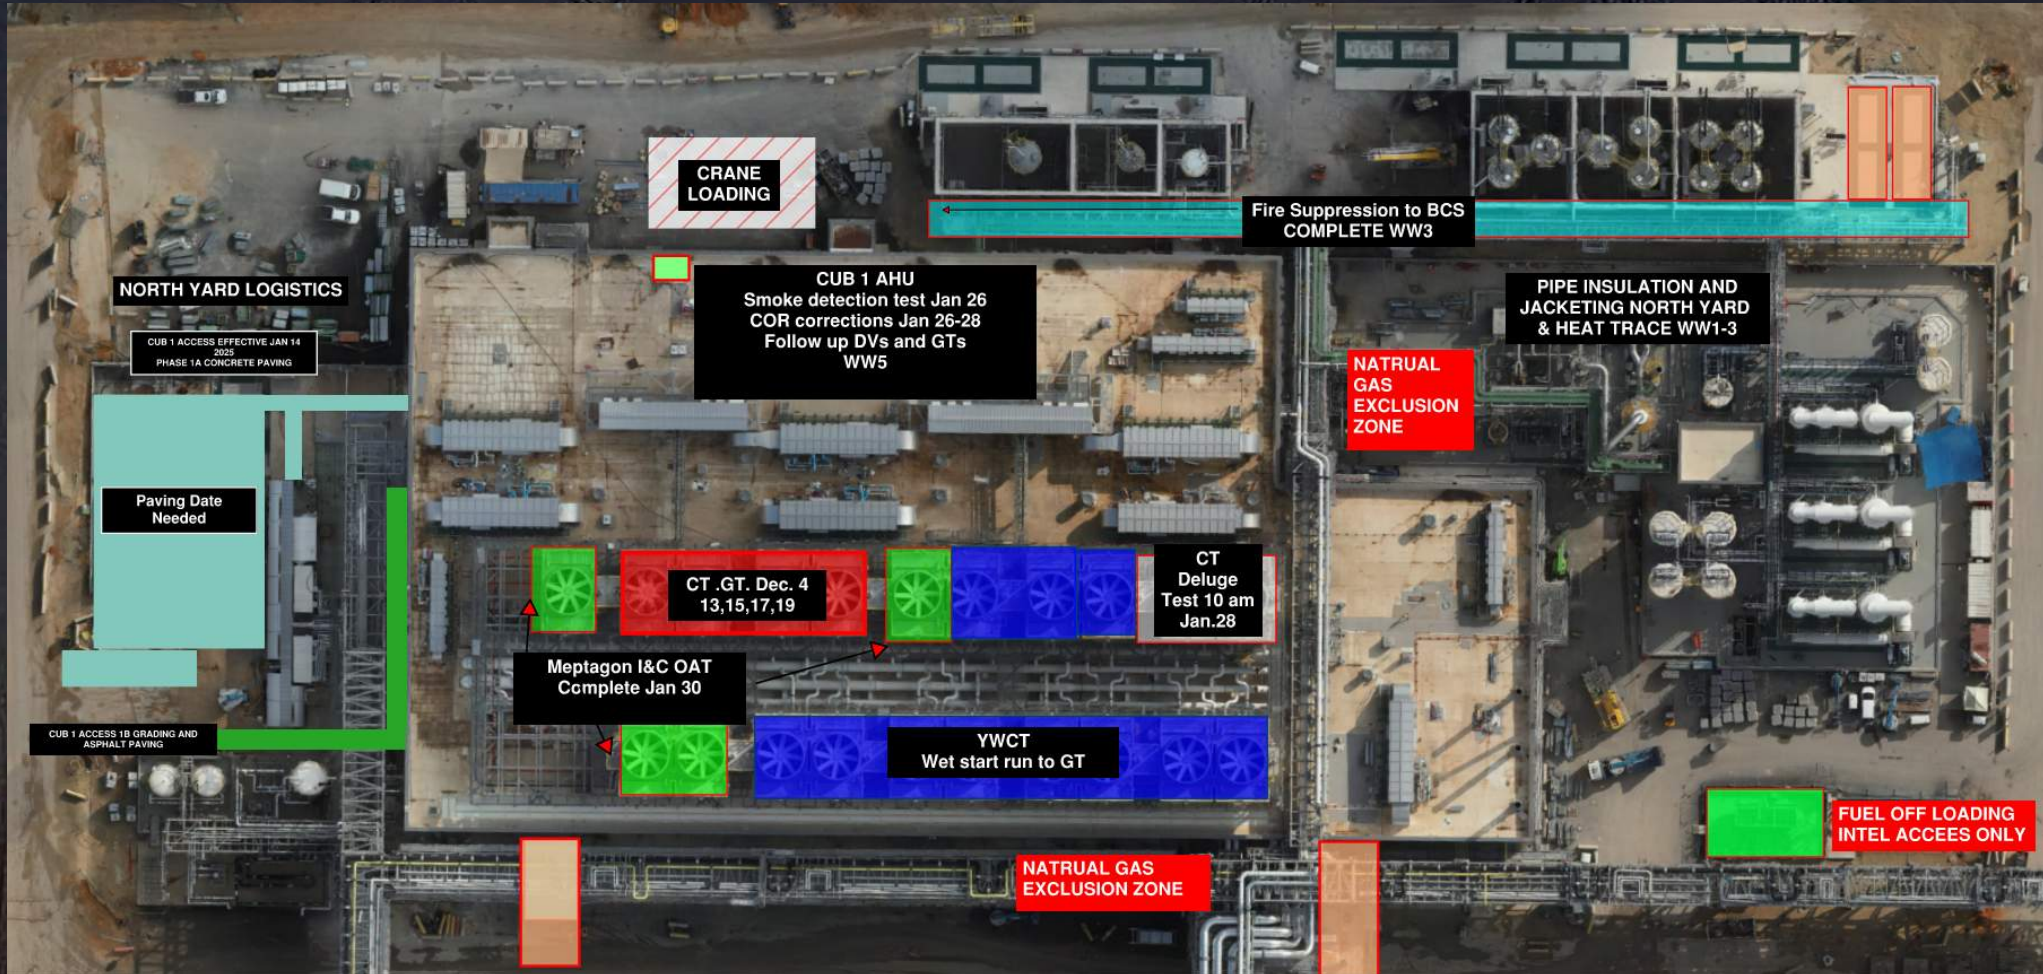


CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

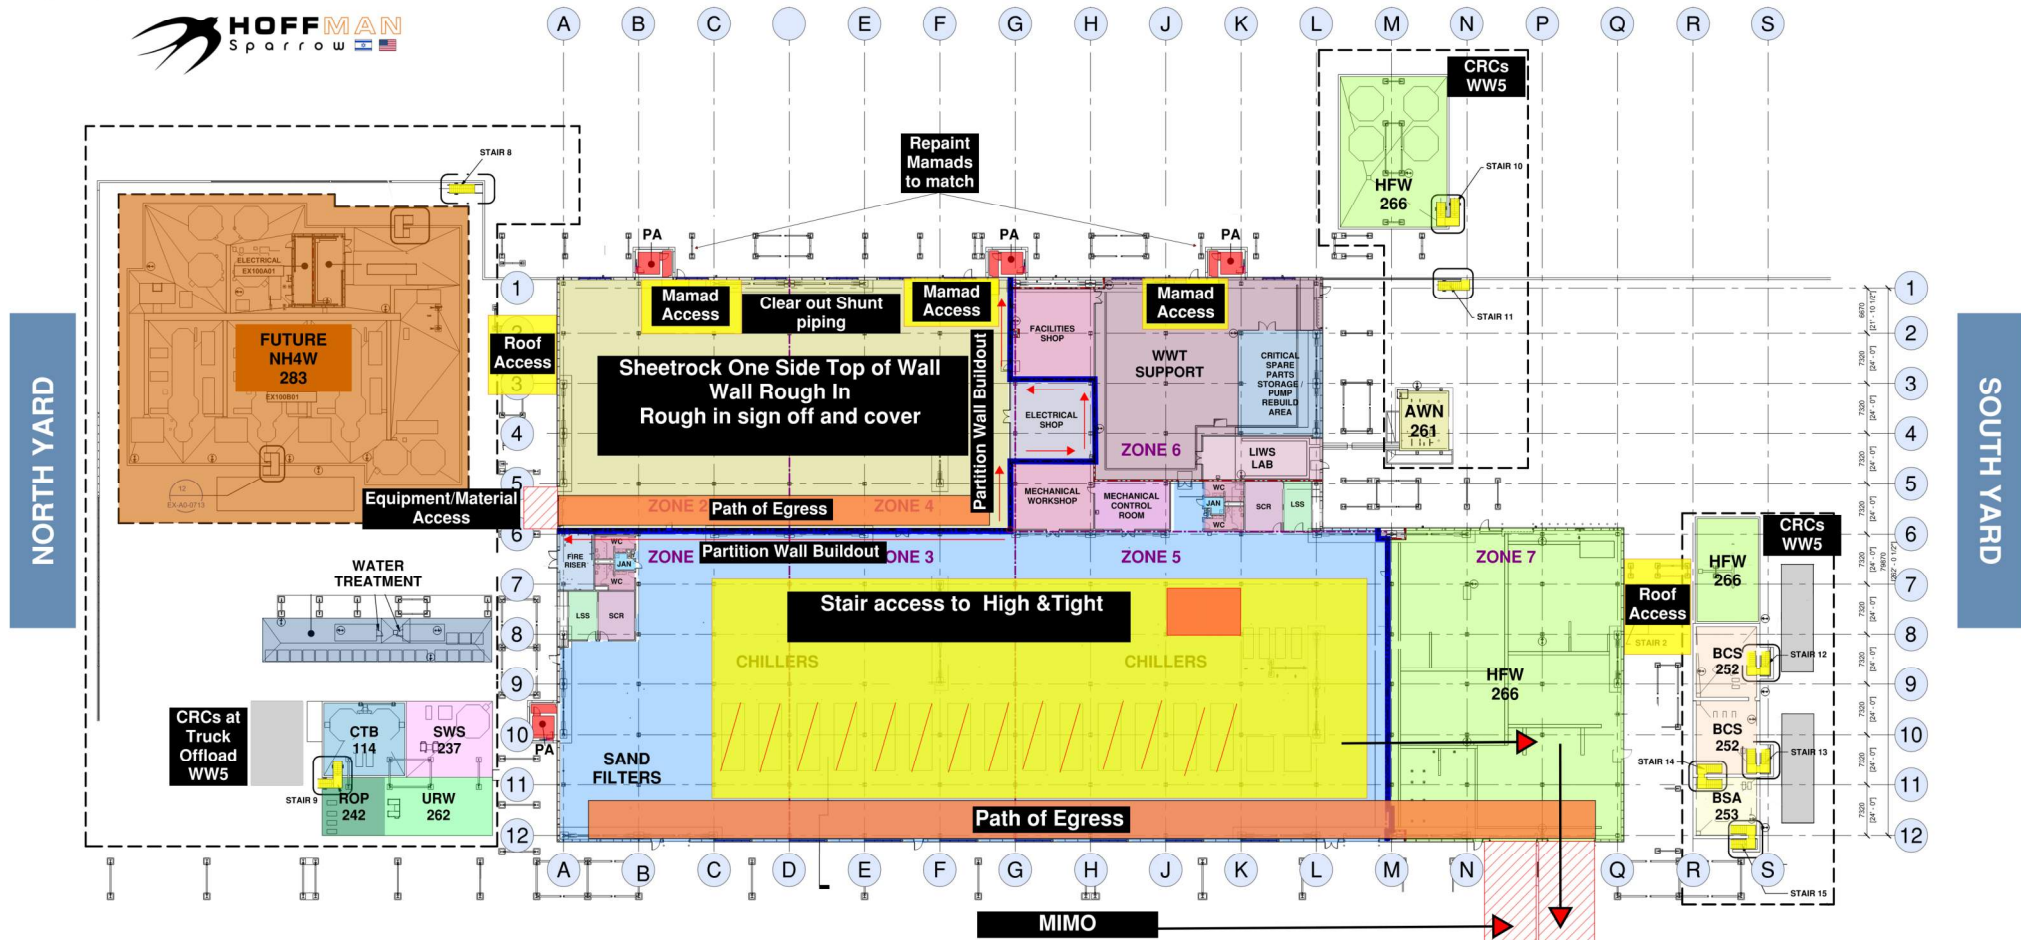



CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY

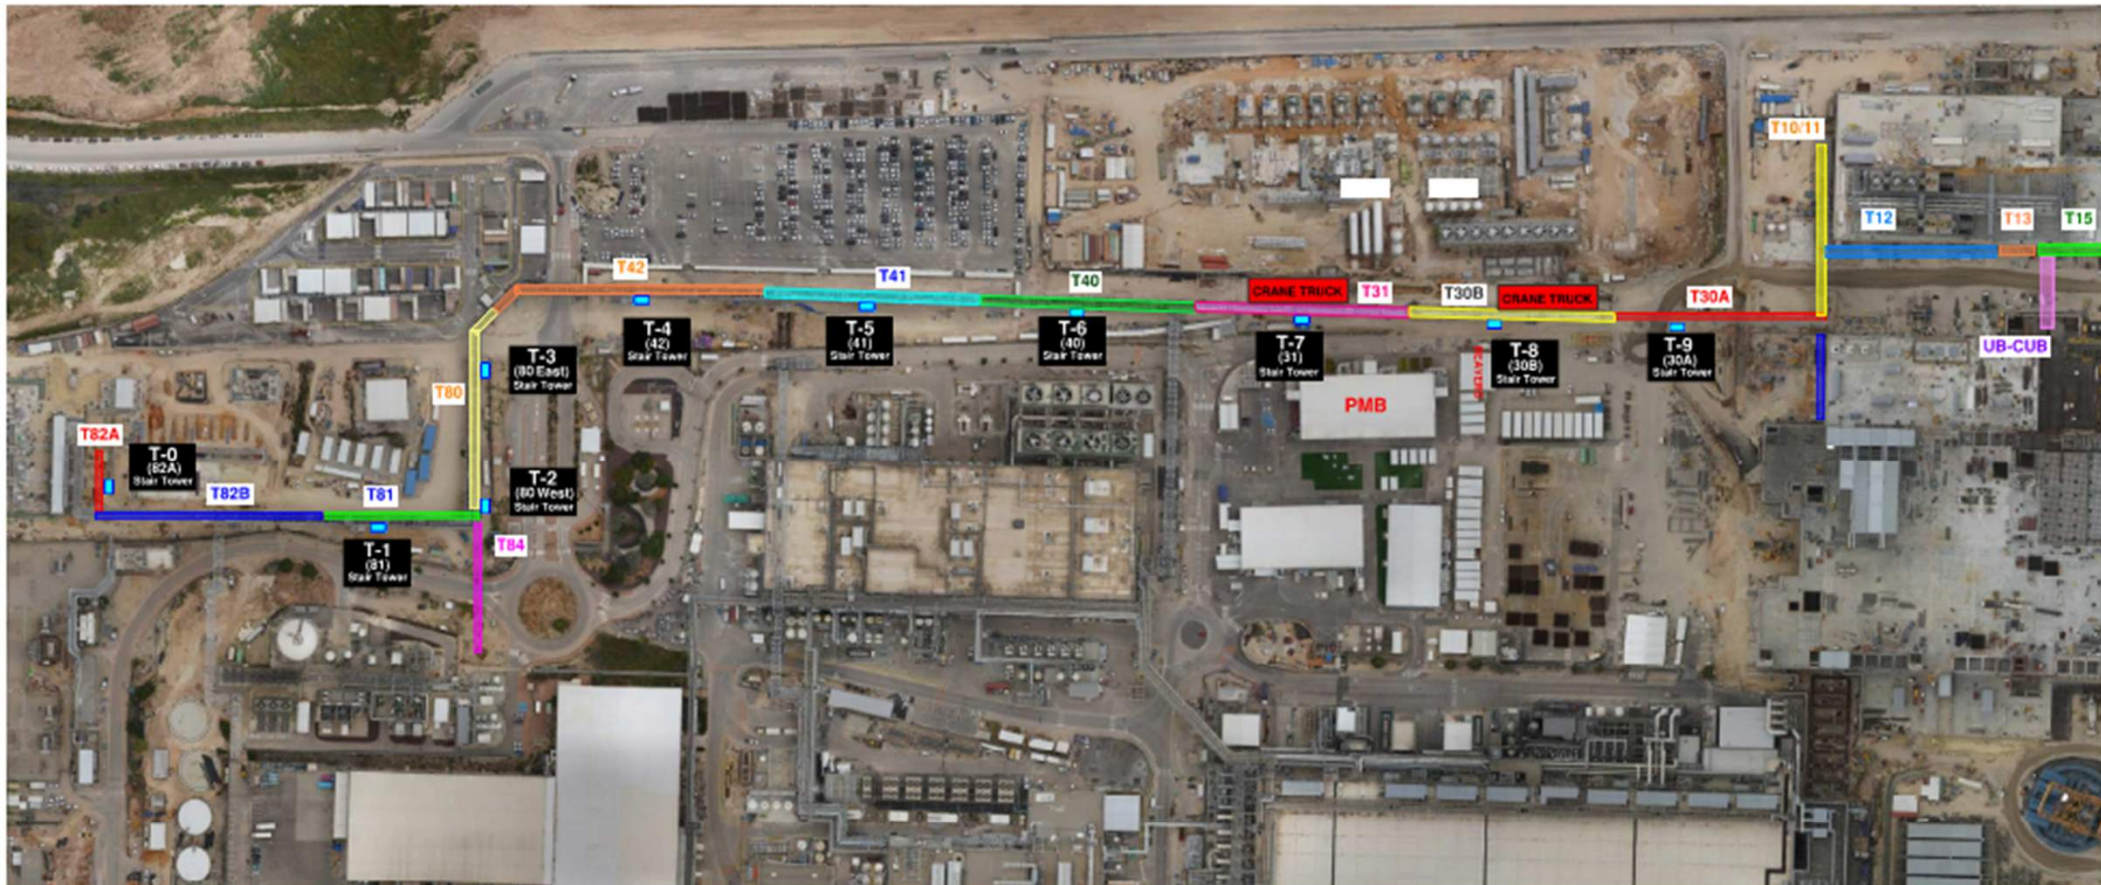





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow

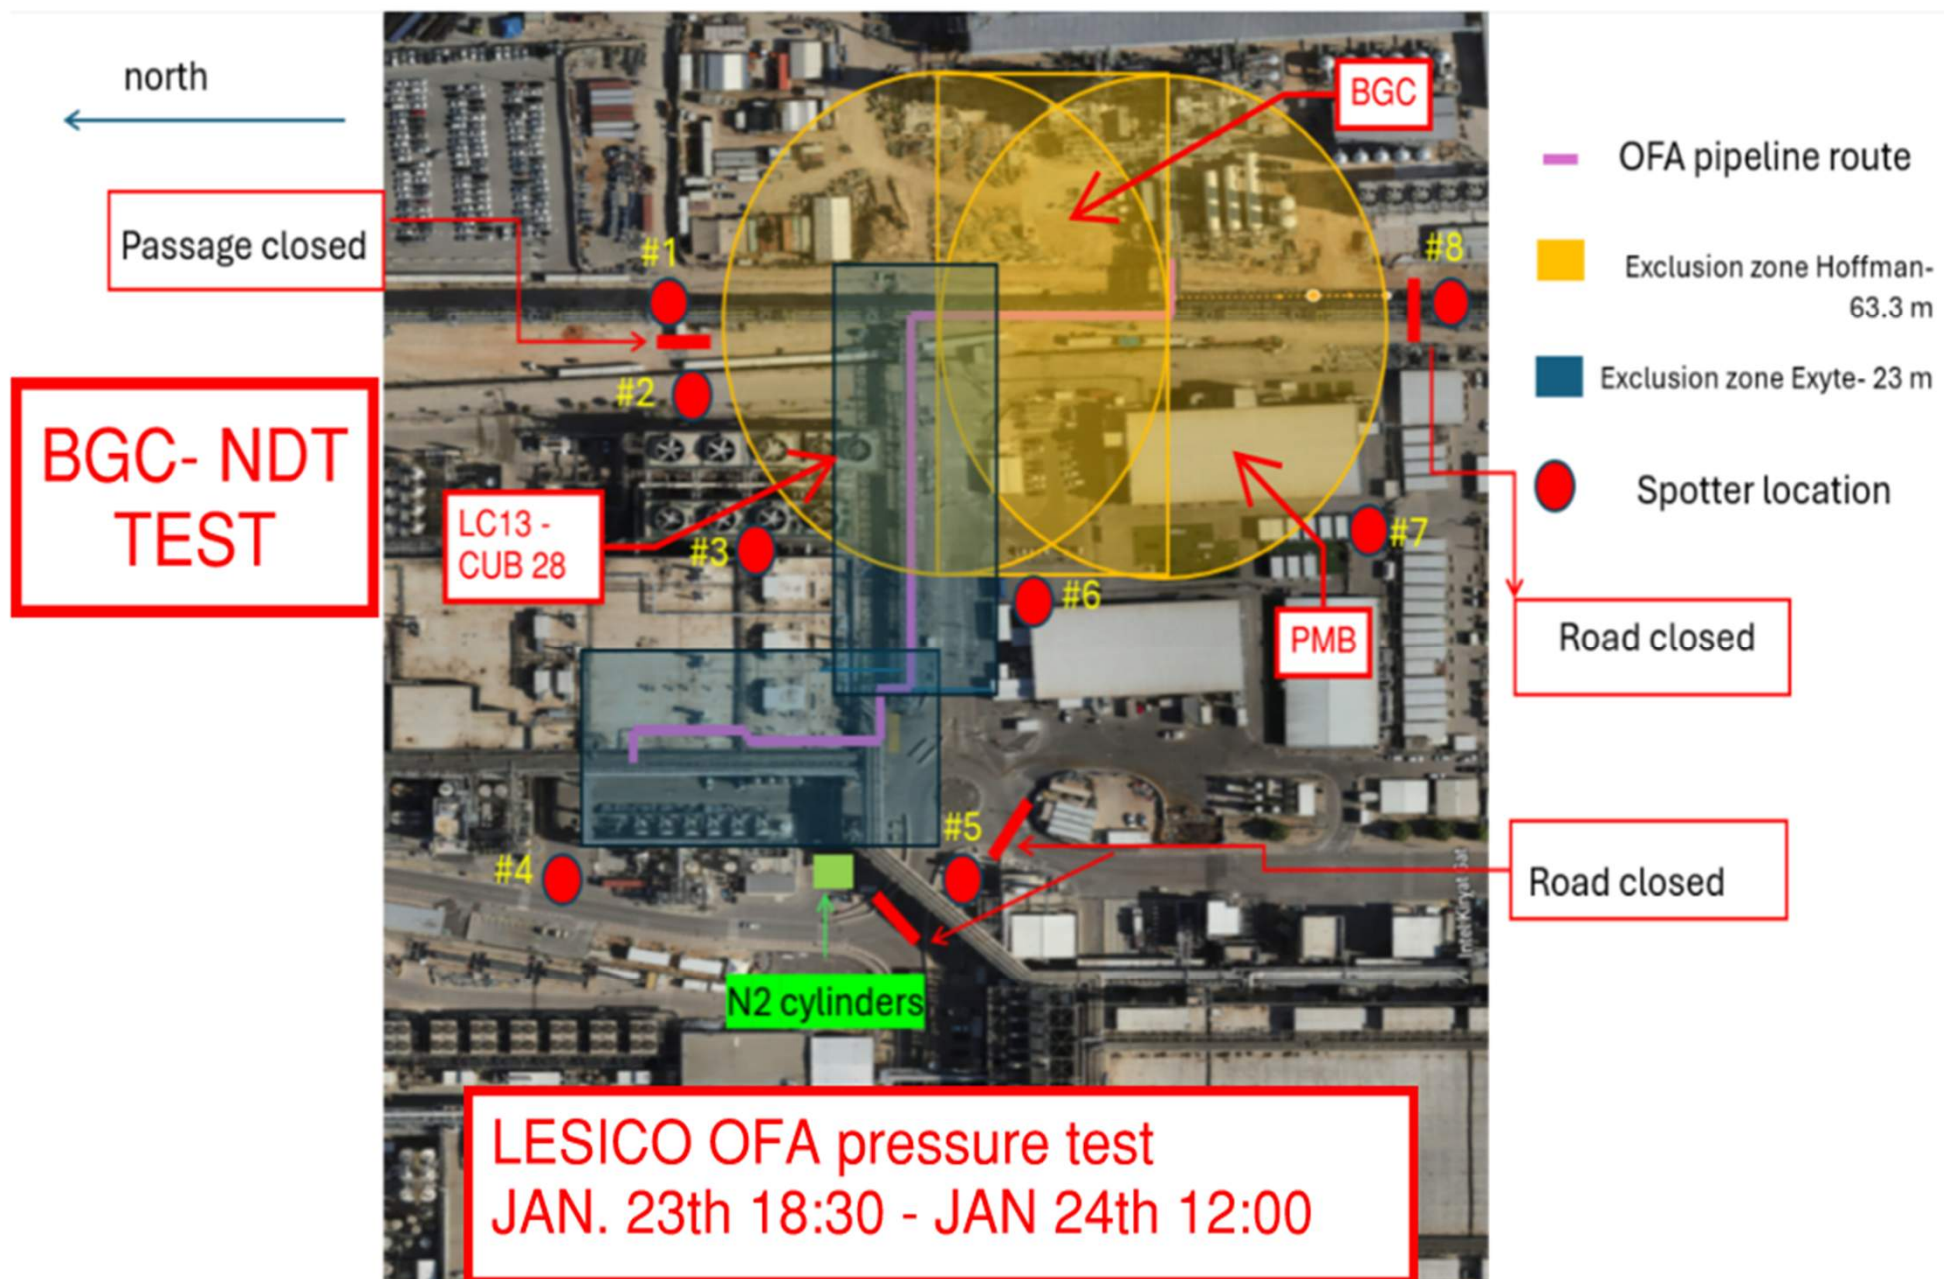



HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
S p a r r o w  

Lesico OFA Pressure Test

Thurs. 23/1 18:30-Fri. 24/1 12:00

PMB: Closed 17:45

Access to car parking: Closed 18:15



HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow



I.A pipe pressure test -
23/01/2025- 15:00- 18:30





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

MODULES IN FOR STORAGE

1 unit-Tue 21/1+1 unit-Wed 22/1
1 unit-sun 26/1+1 unit-Mon 27/1

GATE A

CUB 2

MODULES STORAGE AREA

Trucks maneuver area

Module access route

Keep a 10-meter-wide passage open



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
North






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South

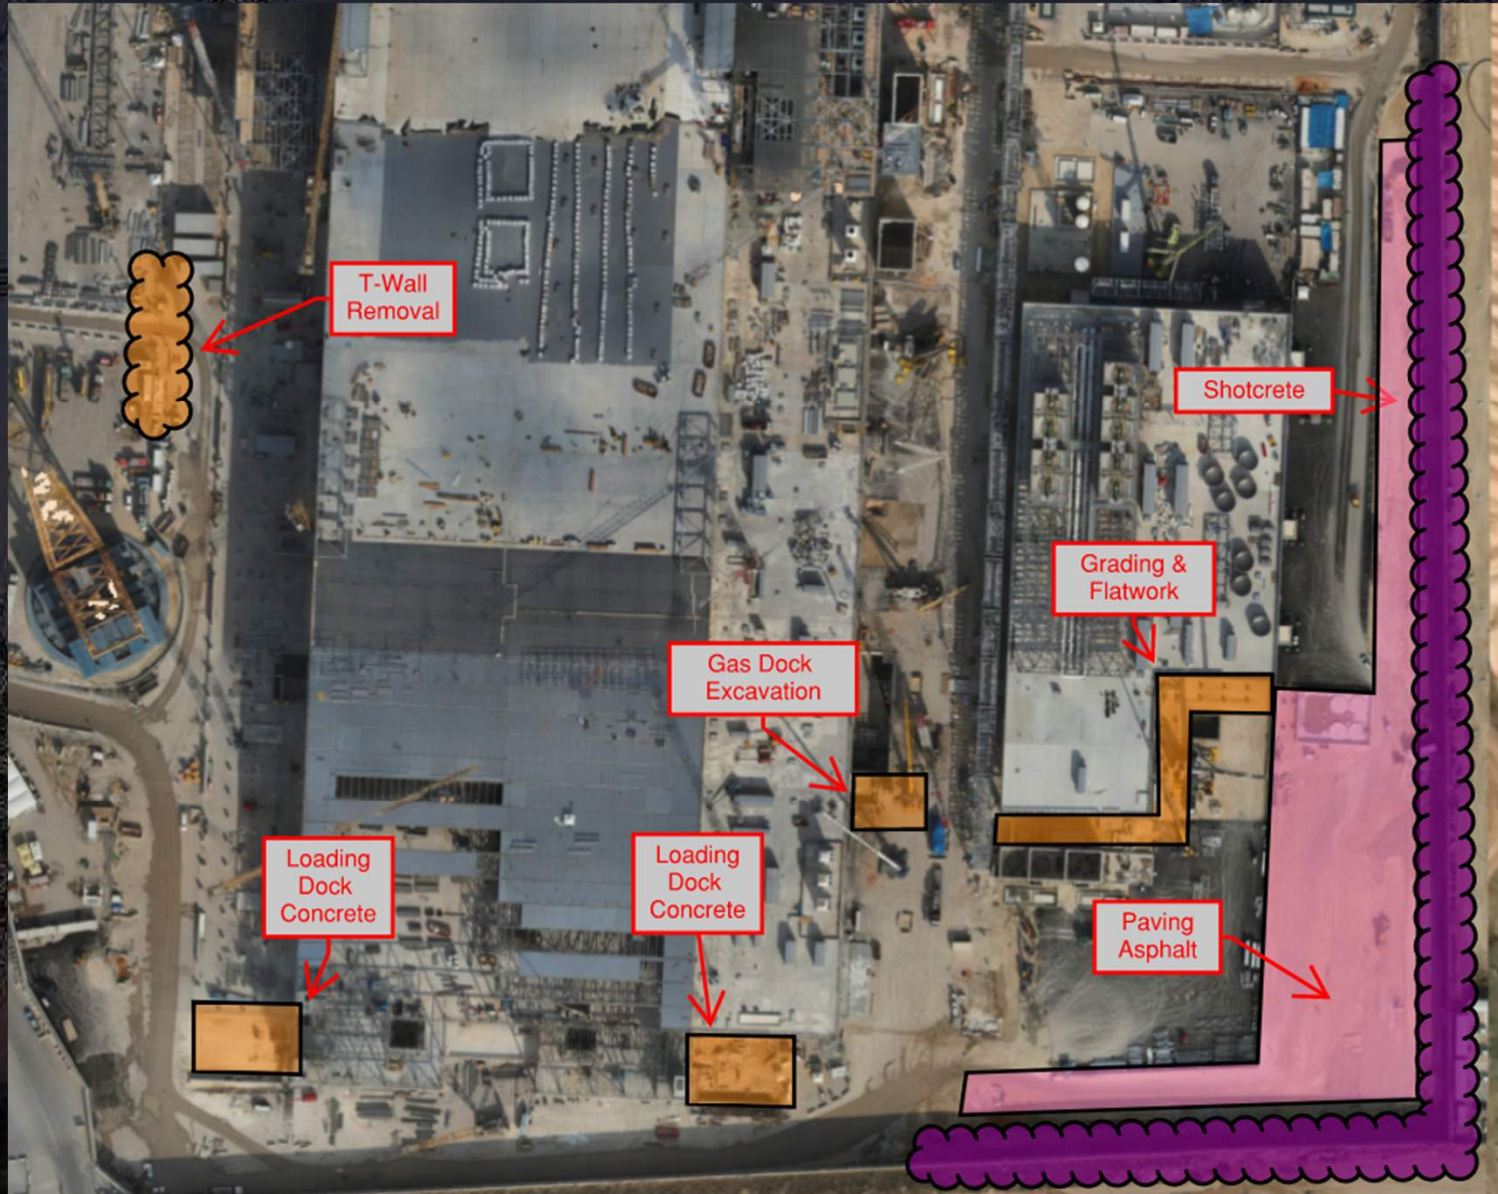



Daily Coordination Meeting

Site Logistics - Cleanup







HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

Site Cleanup

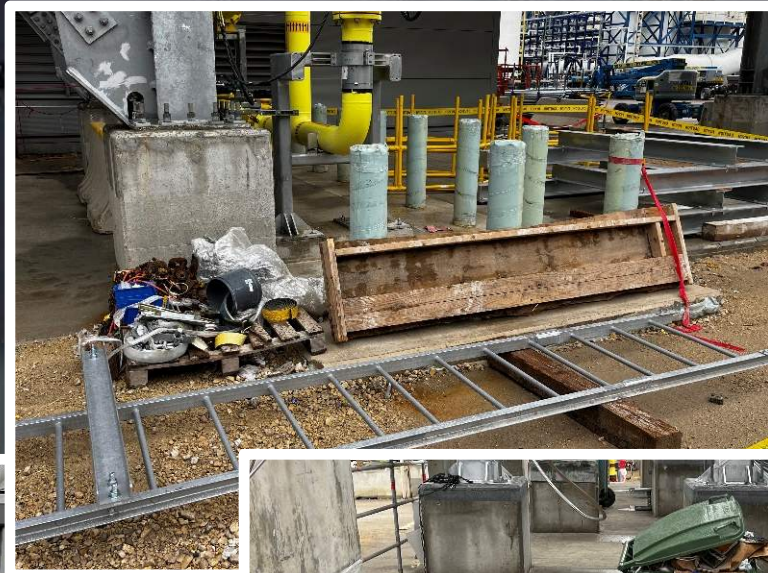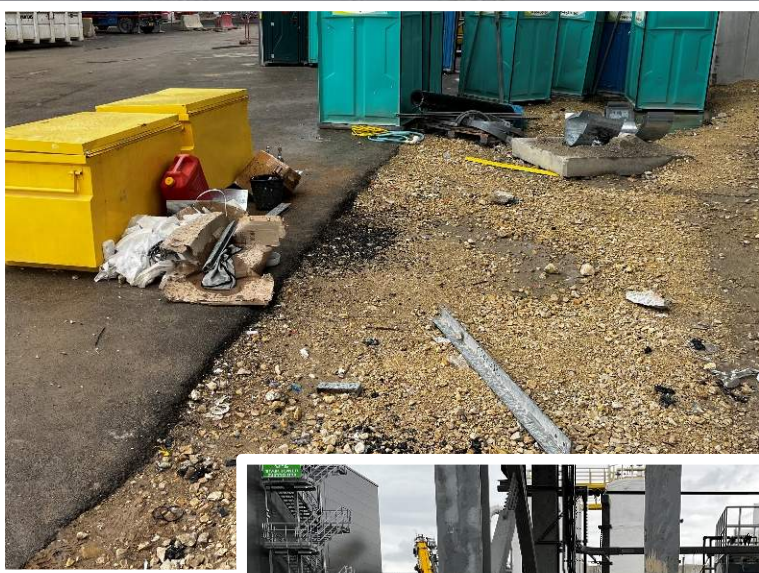

Basic Forklift Safety

- **INSPECT** prior to use.
- **KNOW** the weight of your load prior to attempting to pick it.
- **KNOW** the capacity of the forklift at the distance your load will be from the forklift at its maximum.
- **Plan** and **ASSESS** your travel path before utilizing it.
- Loads must be **SECURED** (either strapped or by utilizing the fork pockets) at all times.
- Slings cannot be slung over the forks, a **PICKING** device must be used.
- **SPOTTERS** are required and must be positioned where they are effective and safe. This means that they cannot always spot from the front when the forklift is backing up.
- **SEAT BELTS** must be worn.
- Indoor/warehouse forklifts are not to be used off road. They are not designed to be able to go over speed bumps or rough conditions.

HCC/EHS Weekend Work- 24.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jesse Fritch - 052-3697329

Ibrahim A

Or Yaakov - 052-4268250

CSA CM

Cody Baumann - 052-7582613

Eyal Ben Shabat - 052-2239767

Brandon Feerer - 052-878-4285

Mark Santiano - 052-6937203

Shmuel Rosenberg - 052-3878052

Abhilash Parameswaran - 052-6938827

Eden I

Max P

MEP

Cx

Cranes

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional - Or Pitusi- 054-812-4788 Or-Pitusi@Hoffmancorp.com

Subcontractor Weekend Work- 24.01.2025

FAB

Utility Level / Roof / Stair Shaft

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

HYG

Ehs Salah 0507773119

Foreman Avishai 0503303939

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- **Pach Taas**
 - W-E MARSes
 - Ilya: 0505771907
- **Afcon E**
 - All over SF
 - RAZ: 0526008487
- **Combe**
 - TTNE
 - Ali: 0526767936
- **MEGASON**
 - MOD 2
 - Israel: 0526869393
- **SELA**
 - 9E
 - Yoav: 0548076339

Clean Room

- **Talad** – 20 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 14 GUYS Mod1 – MOD2- 17 line, 7E above coils (EHS Beni 0506232032, Super Shmulik 0549205966)
- **Afcon** – 20 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- **Chemo** –26 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- **Sela** – 10 1E, 2W CRC (Supervisor Yoav 0548076339, EHS Sergey 0526650046)
- **Pach Taas** 3 guys, BF-CA 17 Line (EHS Avigdor 0542010393, Super Netanel 0543301880)
- Protocol 2 guys (Roni 0542496363, Lidia 05072148)
- Talent solution 11 guys CR 2E 1E/W maintenance cleaning (EHS 0508777611, Super Faraz 0547139706)
- W&W 15 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Subcontractor Weekend Work- 24.01.2025

PSSS

- Pach Taas** – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **SK Engineering** – GL4 UL Piping, 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Carmel Bidud Duct** – Spec Gas, BCD, and 2P Roof
 - Foreman –
 - Safety –
- **Combe Waste** – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe UPW** – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- **Lesico** – UN2/Waste Vent Rack
 - Foreman – Selvin – 052-4787370
 - Safety – Oskar – 052-5221474

WJG

- **Afcon** – Lift 2 and Utility Level Cable Tray
 - Foreman: Montu 055 911 6973
 - Safety: Pradeep 055 274 2935
- **Chemo:** 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)
 - Foreman: Maor 050 988 9071
 - Safety: Erez 054 971 6840
- **Pach Taas:** All over (HRA)
 - Foreman: Ilya 050 577 1907
 - Safety: Eran 054 770 6233
- **Lesico:** Natural Gas Piping Utility Level
 - Foreman: Anoop 058 691 1748
- **SK** – (pressure test G water column 4J MAH)
 - Tufik 54-9433592

Subcontractor Weekend Work- 24.01.2025

CUB

Meptagon: CUB1

Foreman: Serghei – 0548038554

Safety: Haym – 0552728807

D&P: CUB1/2

Foreman: Konstantin - 0545501602

Safety: David – 0548894447

Sela: CUB1/2

Foreman: Yoav Yossi - 0548076339

Safety: Sergey Koharchok - 0526650046

Megason: CUB1

Foreman: Israel – 052686939

Safety: Guy Ishbit – 0544915409

Chemo: CUB1/2

Foreman: Dude Cohen – 0509808846

Safety: Daniel Lackford - 0525217434

Trestle

SNJ:

PIPES –T40 - UB CUB - 15 workers (3 teams)

STEEL –Galvanized paint + T30 A+B - 8 workers (2 teams)

Steel adjustment - 10 workers (3 teams)

FORMAN-

Mucles- 0526017477

SAFETY TRESTLE-

Aviram shrike - 0509059920

Siding

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Olizki – Offload 18 & CUB1 trench drains, Southeast CUB1 grading

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Sut

Sela

EHS 052-6650046

Foreman 054-8076339

Daily Coordination Meeting



14:00 Sign In
