

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Tools/equipment inspections

NWTT Roof @ 11:00 pm

Mod1 roof pourbacks to follow


NWTT roof
@ 11:00 pm

אינטל קרית גת

FAB-28




UTILITY LEVEL TRUSS

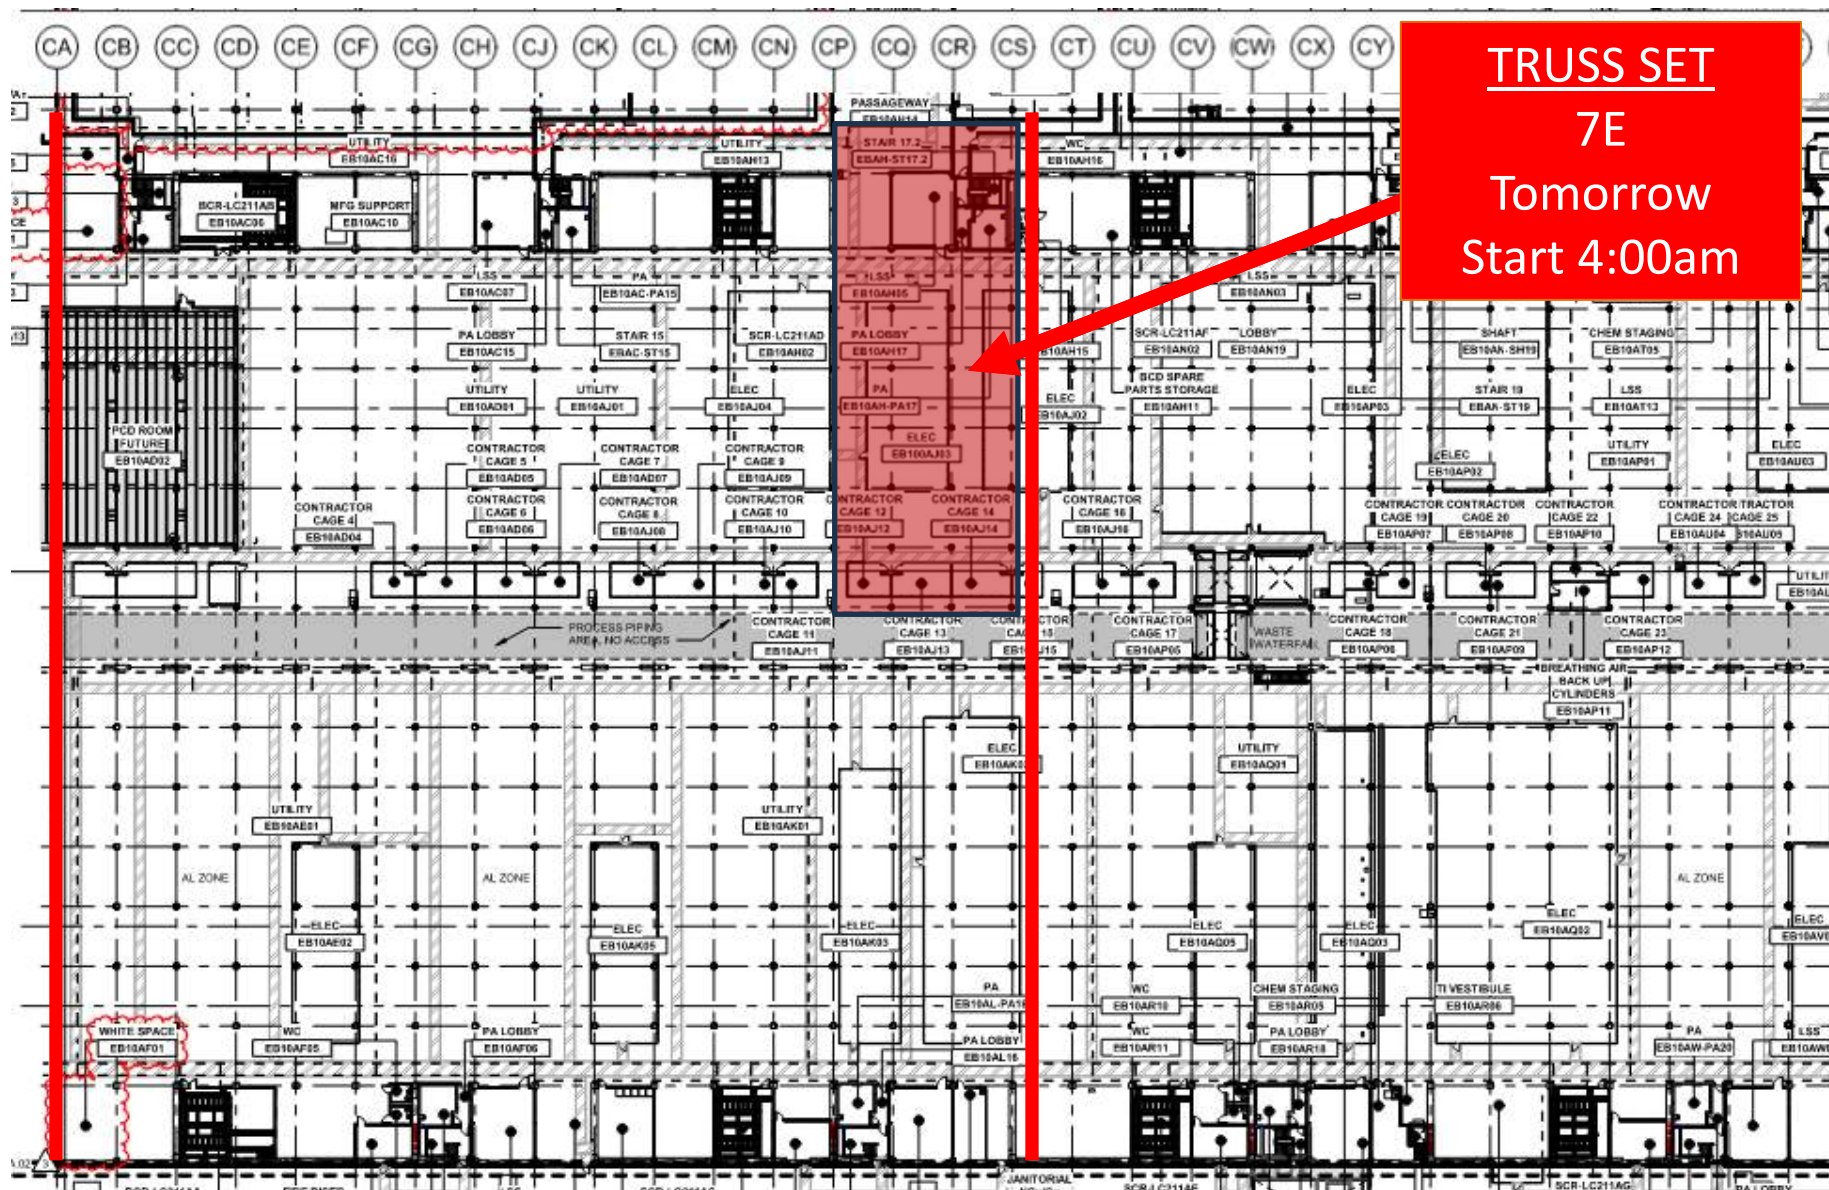



UTILITY LEVEL MOD1

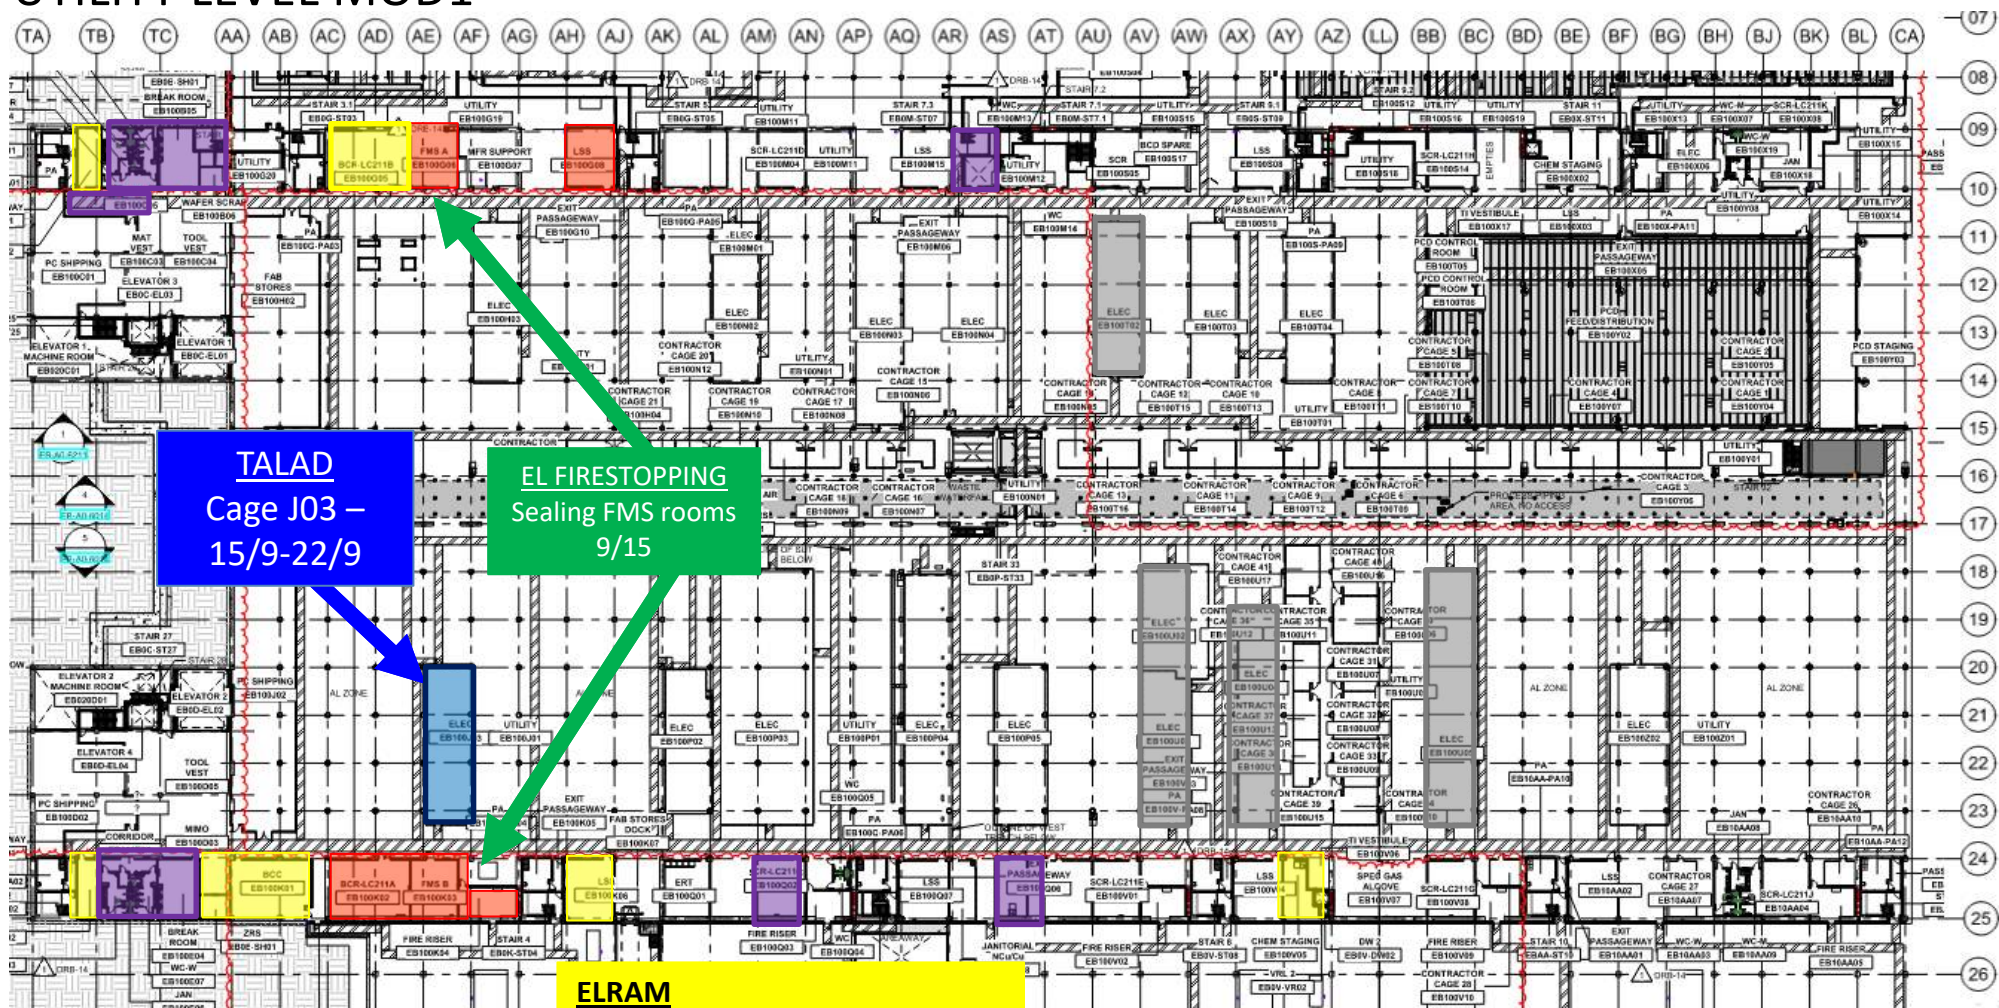

TALAD
Cage J03 –
15/9-22/9

EL FIRESTOPPING
Sealing FMS rooms
9/15


BELFOR
TTNE - Corridor + Toilets + Break R
Stairs 7.3
Wafer scrap
TTNW - Toilets + Break R
SCR 2W
Exit pass 3W

ELRAM
Ongoing
LSS TTNW + TTNE
BCR 1E
CHEN STAGING
LSS 2W
Chem staging
BACKING
BCR 1E+1W – Pending funding
LSS's

MEP+Elctrical
Ready for re-install
FMS A 1E
FMS B 1W
Fire Risers 1W
BCC




UTILITY LEVEL MOD2

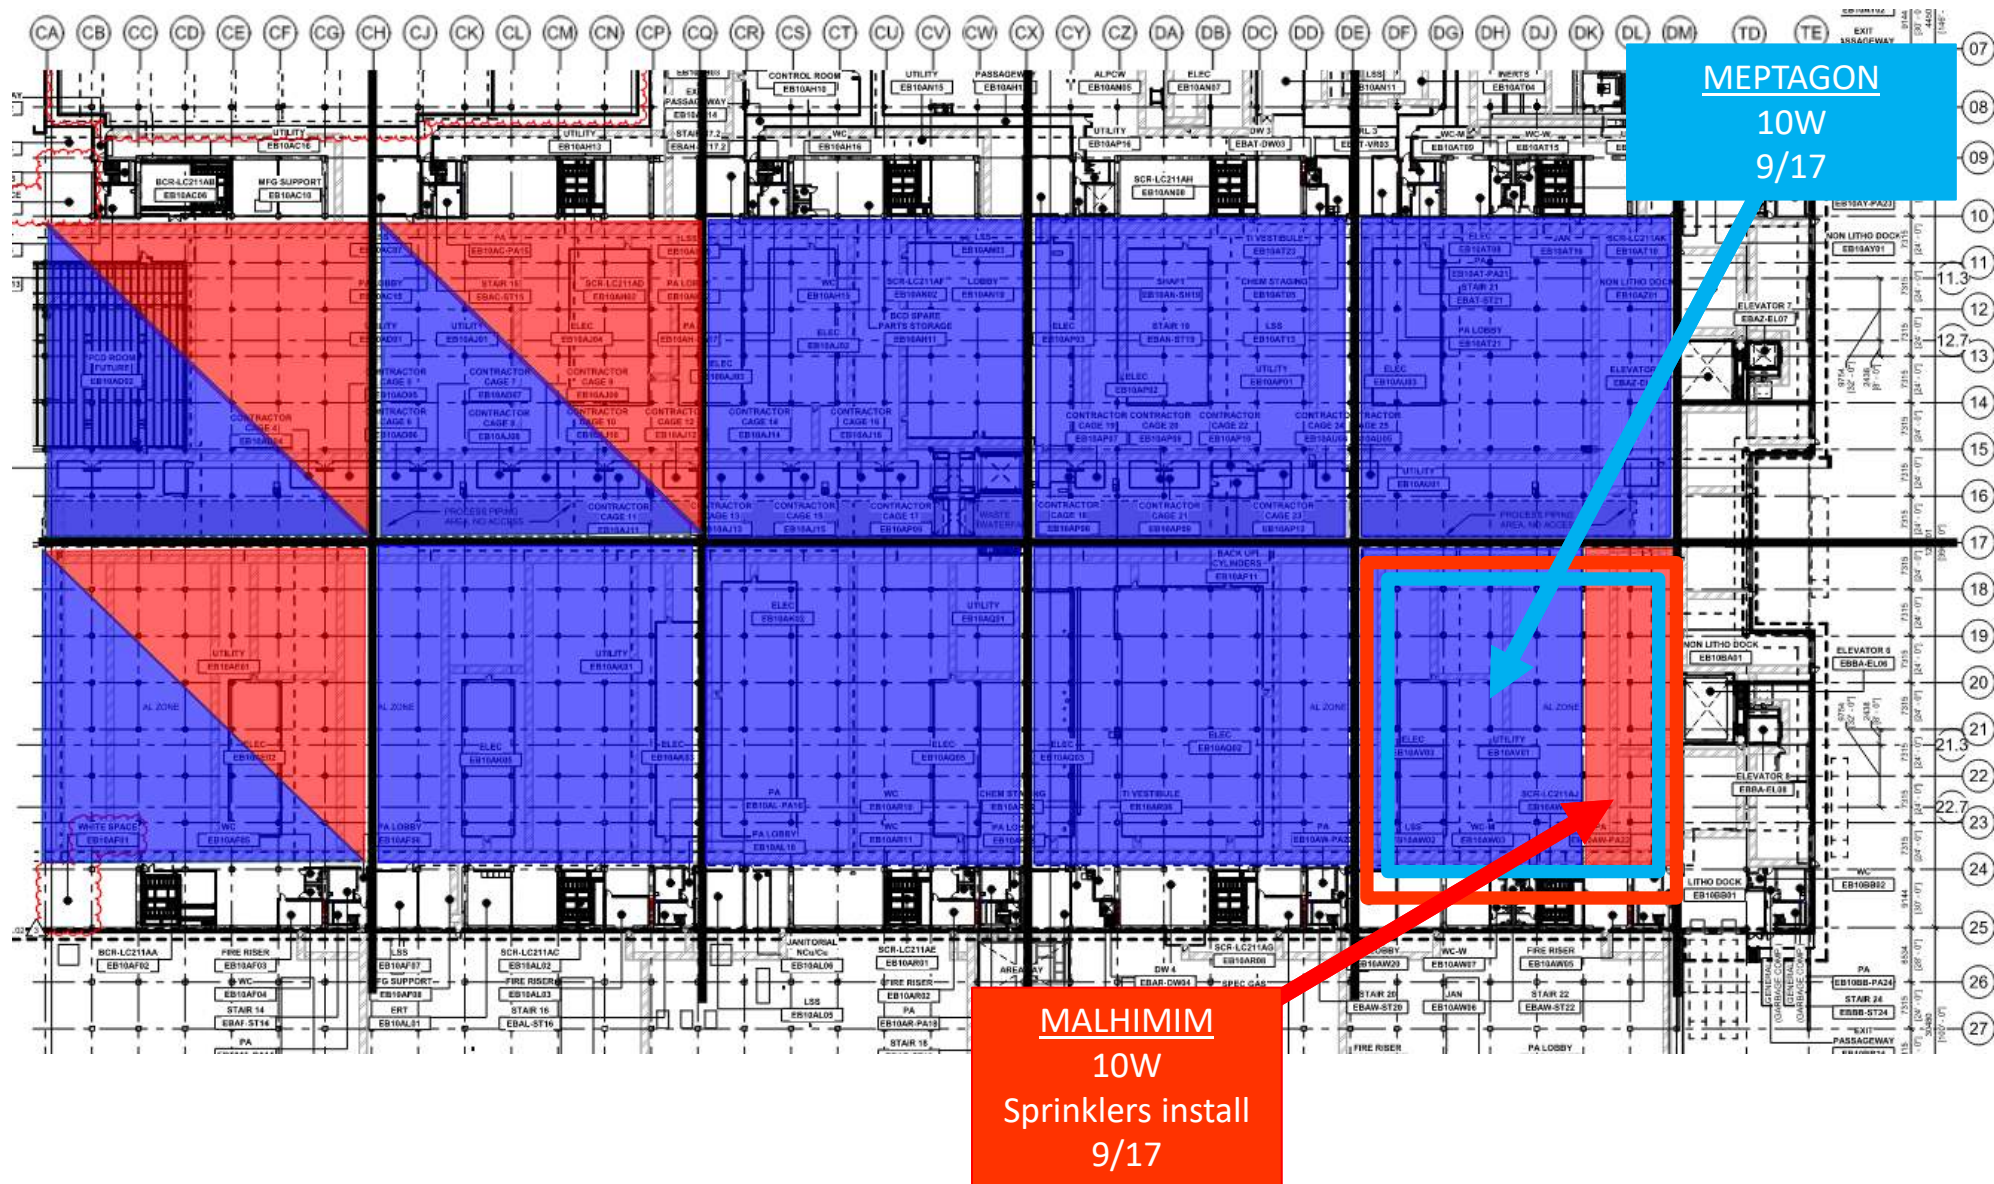




SUT 38.1 LEVEL

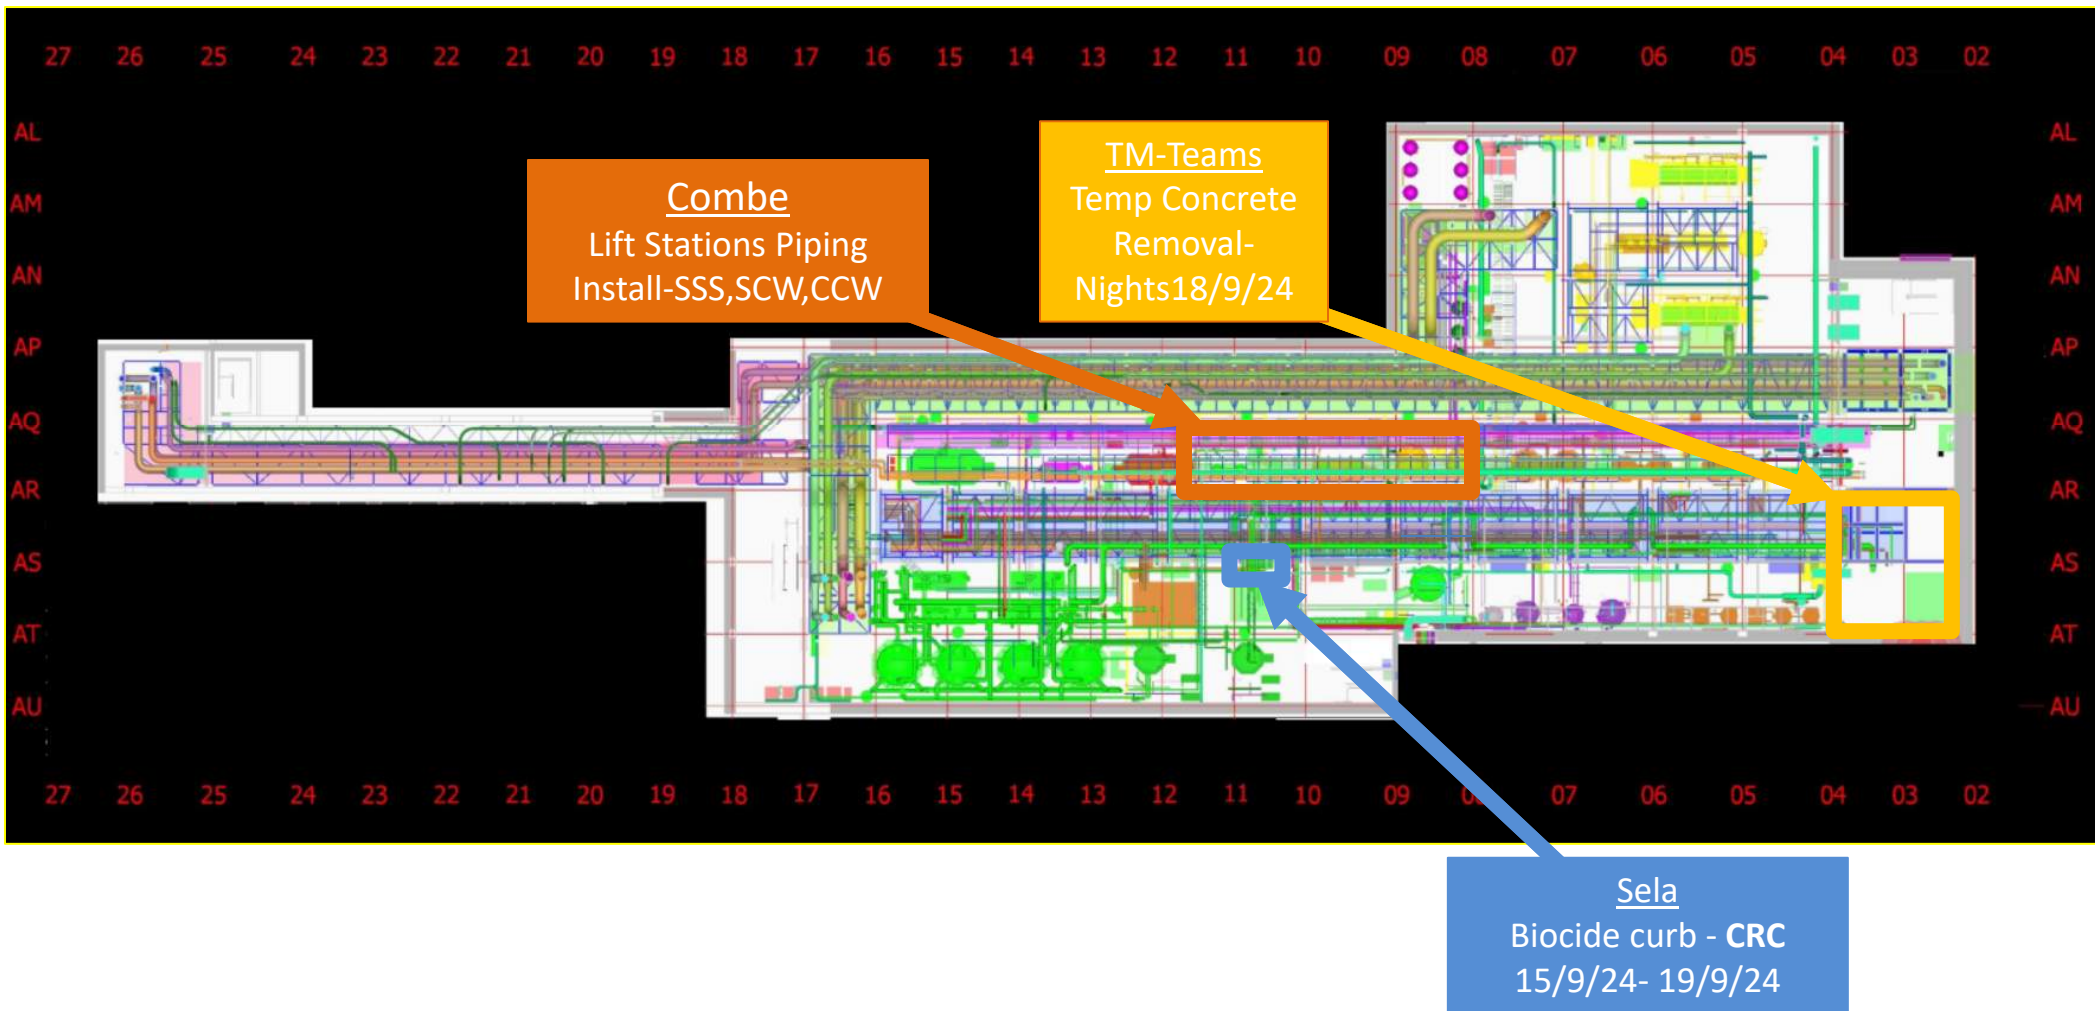

SUT 38.2 LEVEL

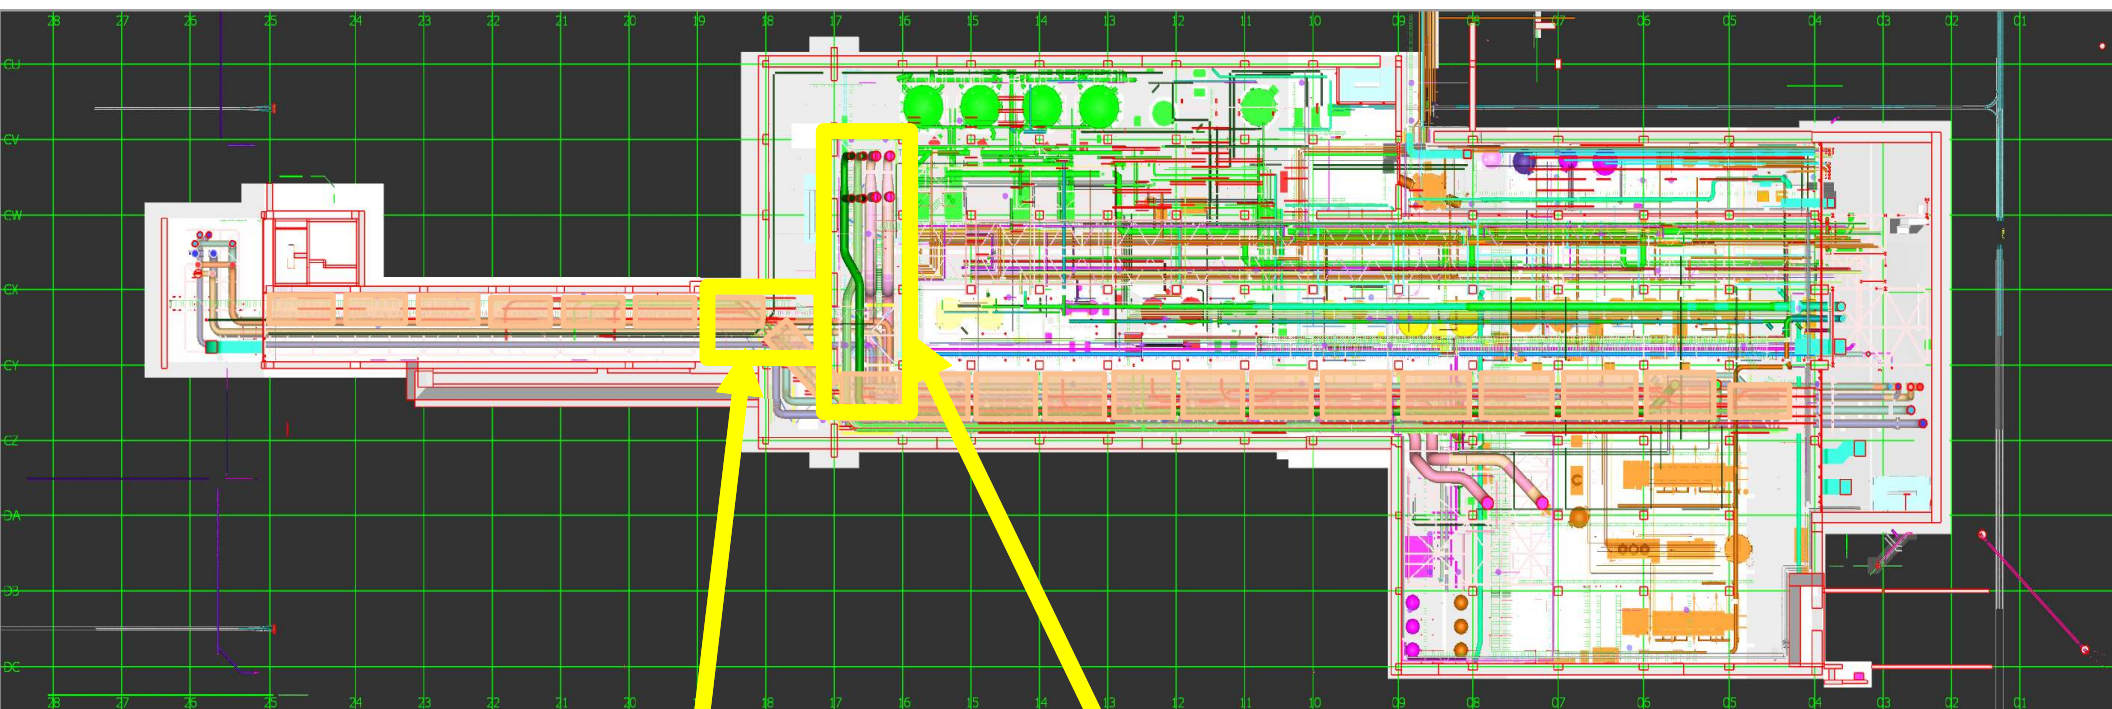


CRW
H&T
NEED PIPING


17-18 line
Bore Loading

16-17 line
lvl2+3
bed lift: Need a
Date


Vesda
H&T
Not actively installing

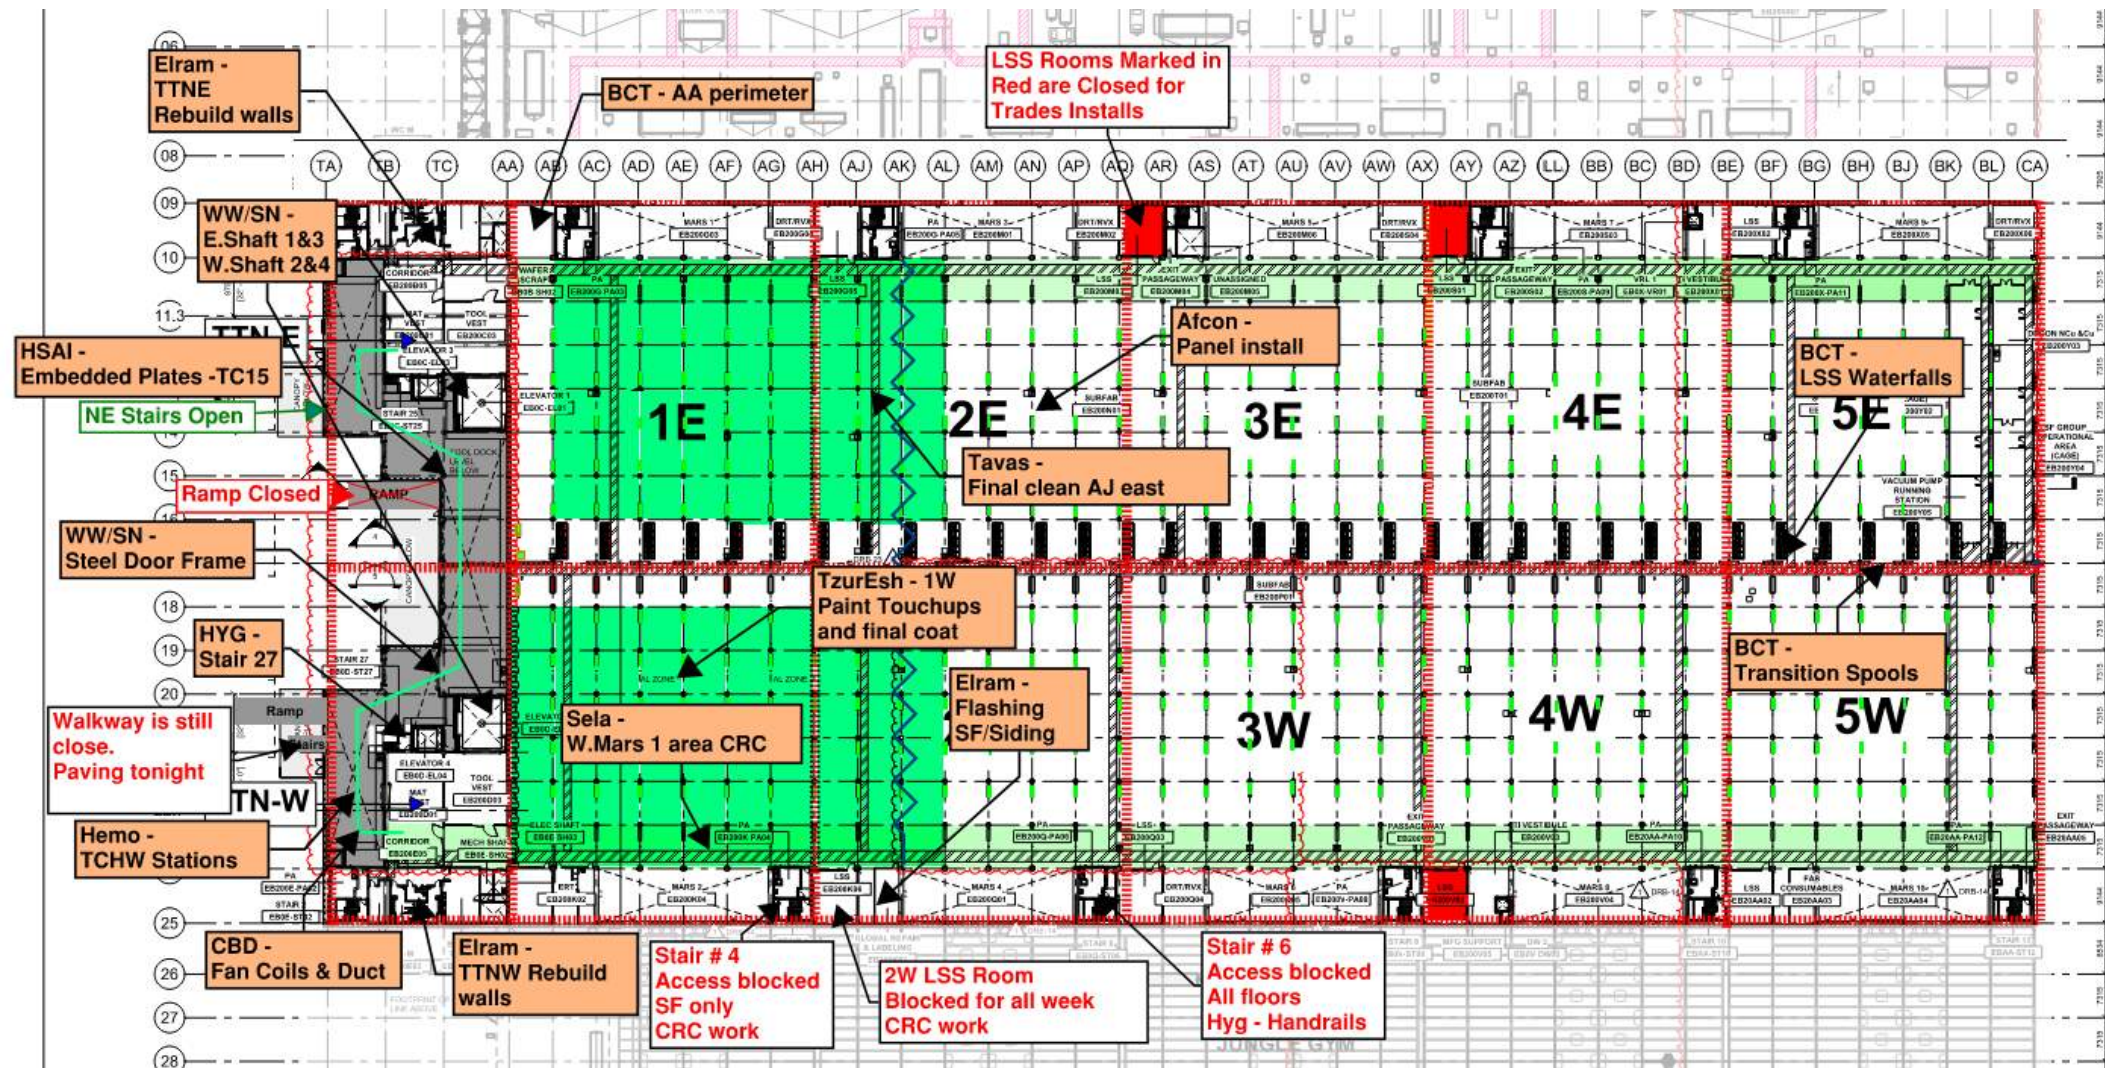


SUBFAB CRC TOPCOAT

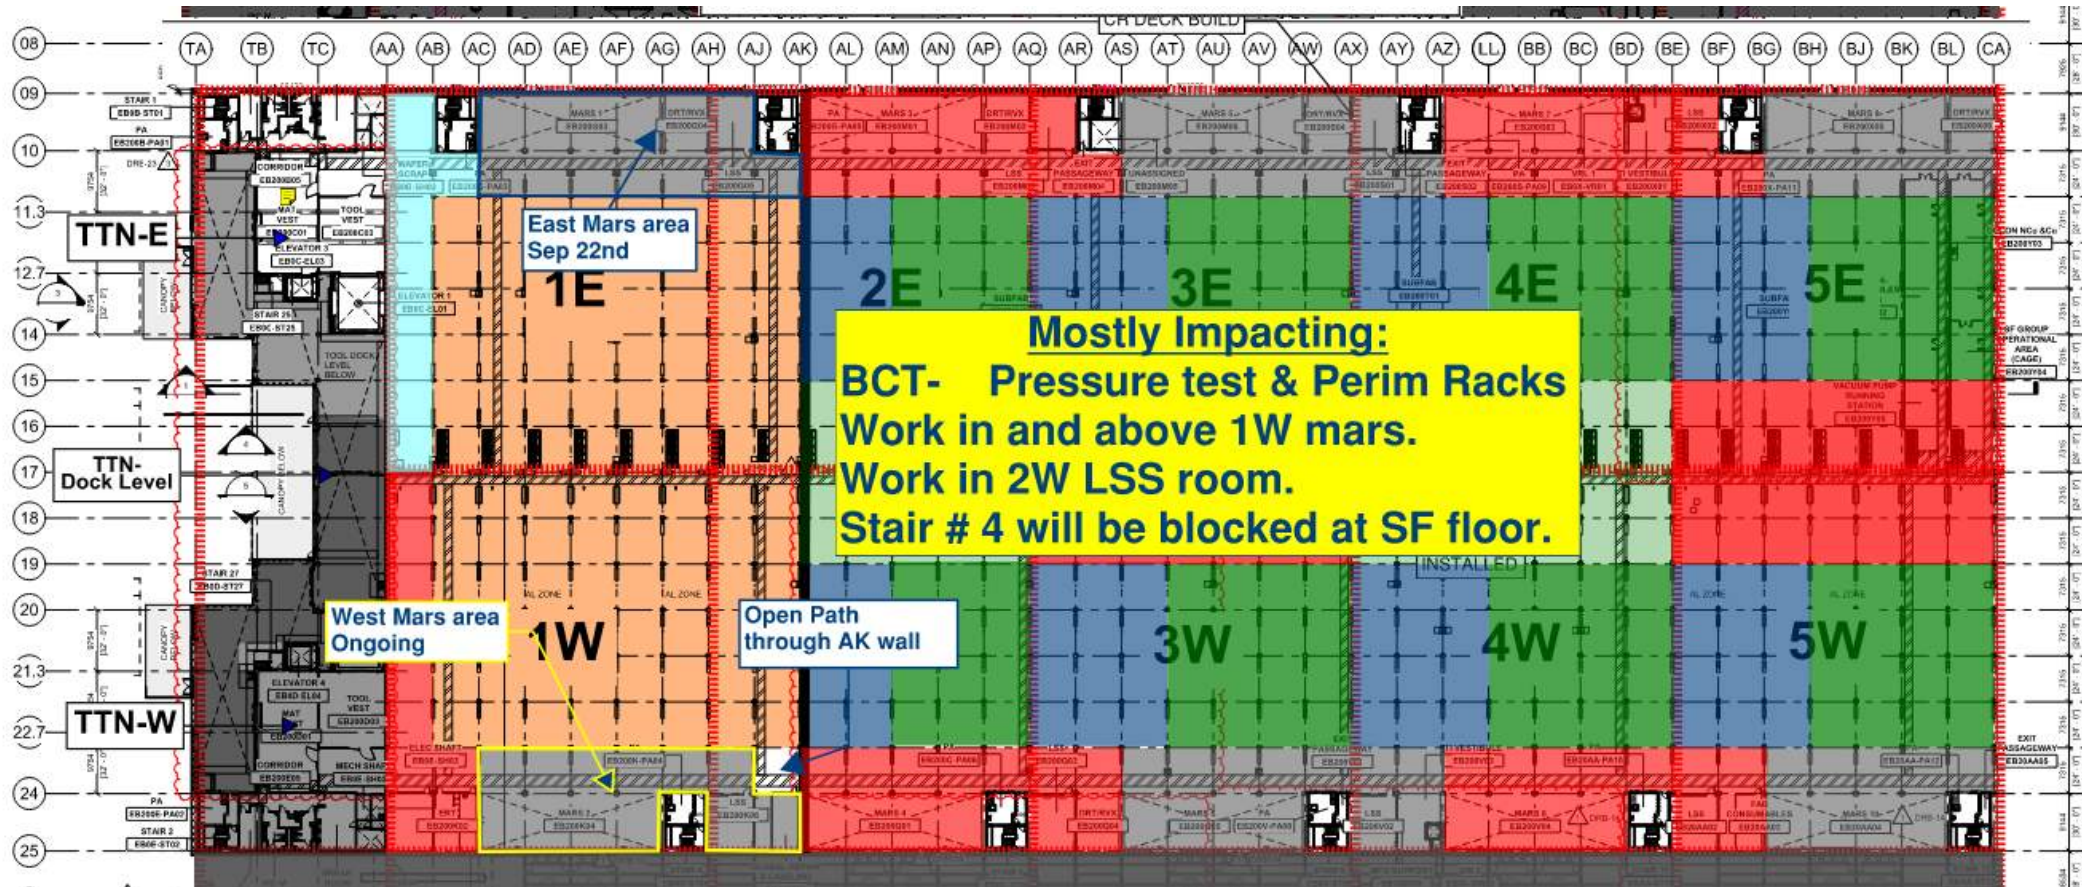


SUBFUB PRESSURE TEST EXCLUSION ZONES

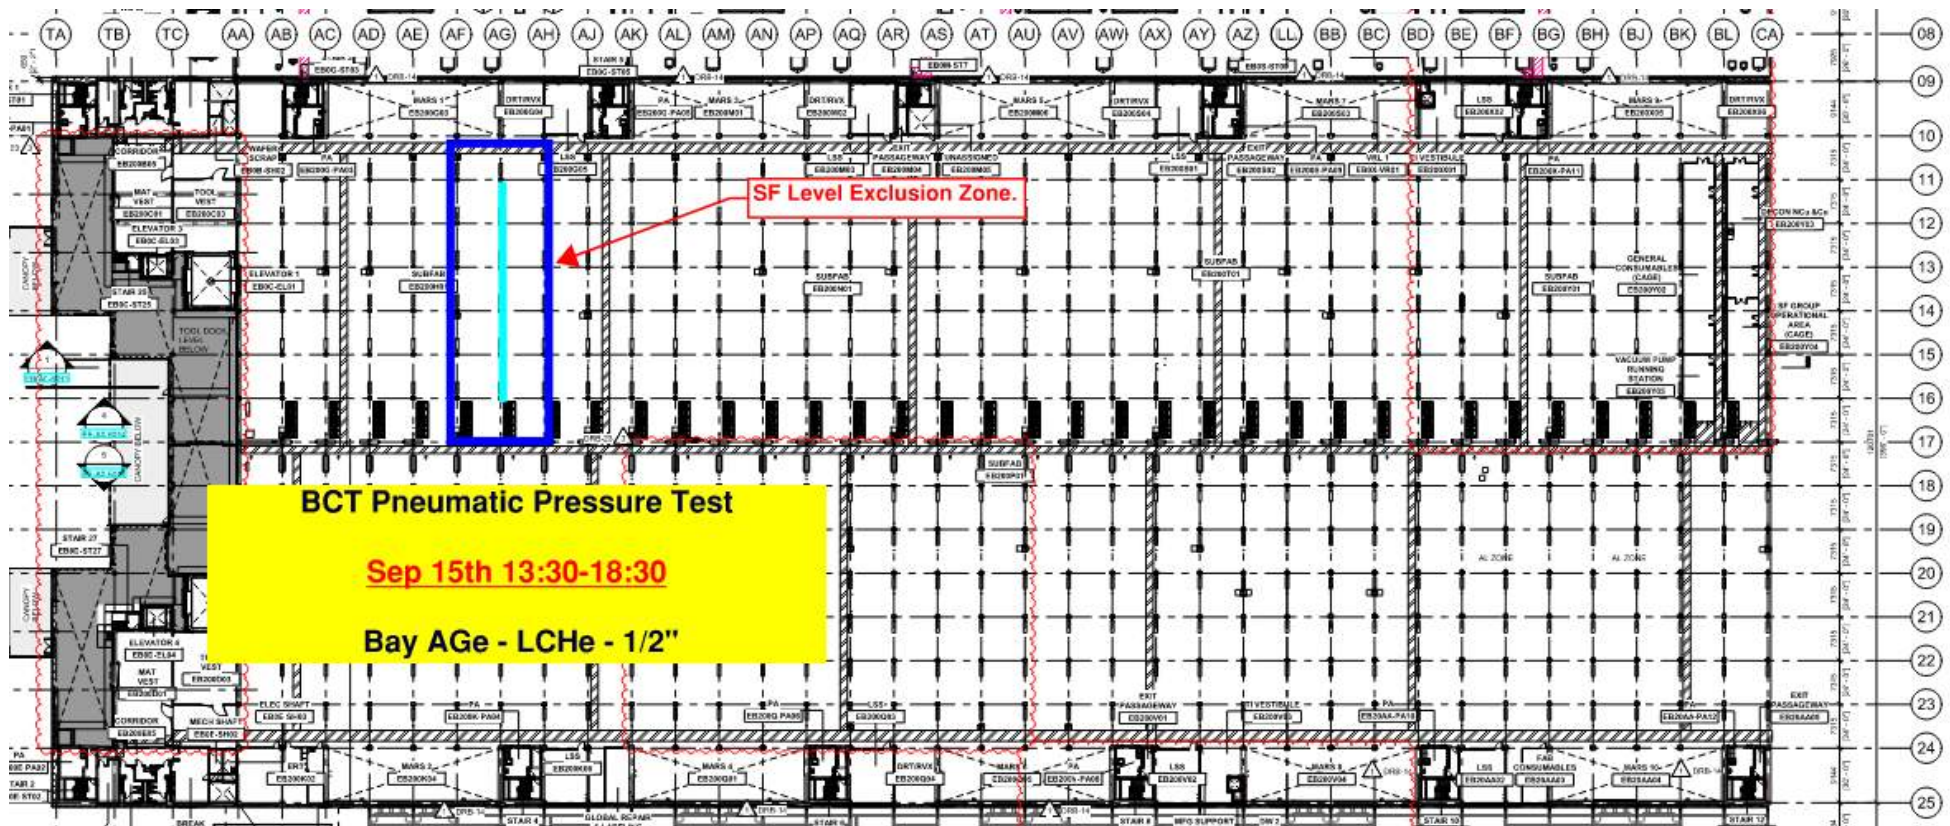



SUBFUB PRESSURE TEST EXCLUSION ZONES

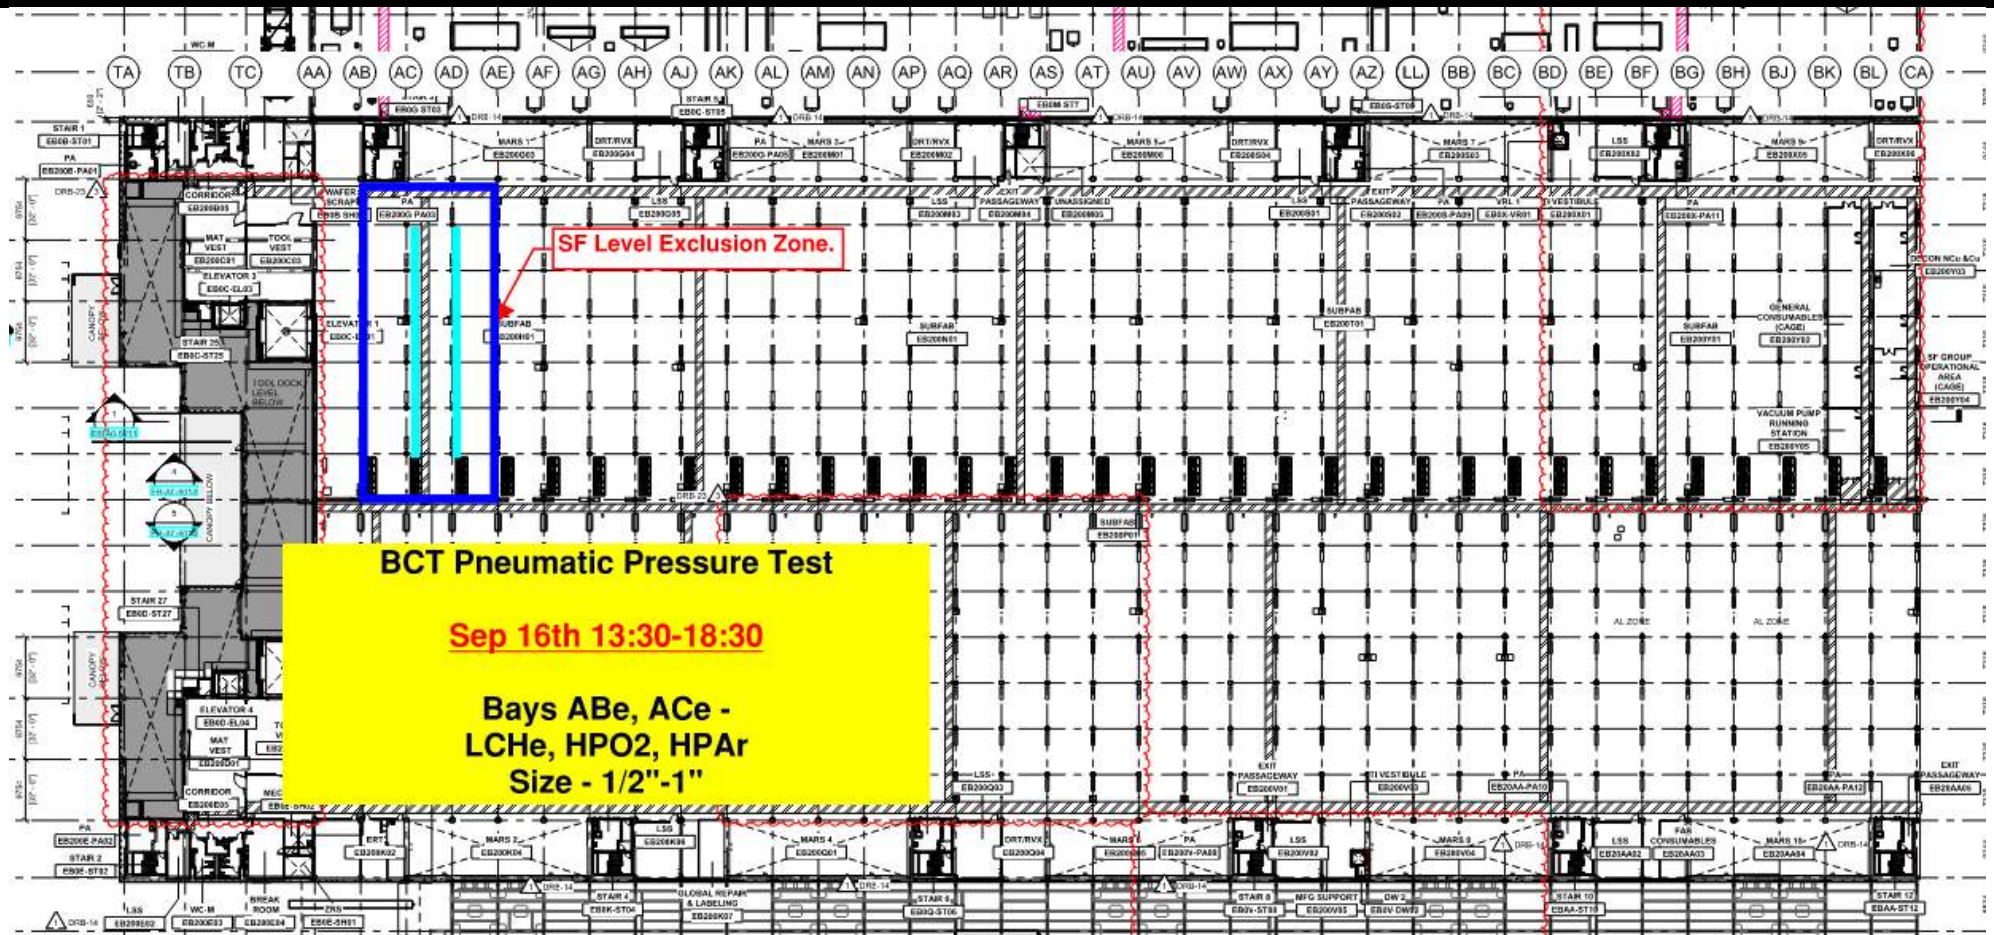


SUBFAB BUILDOUT MOD 2

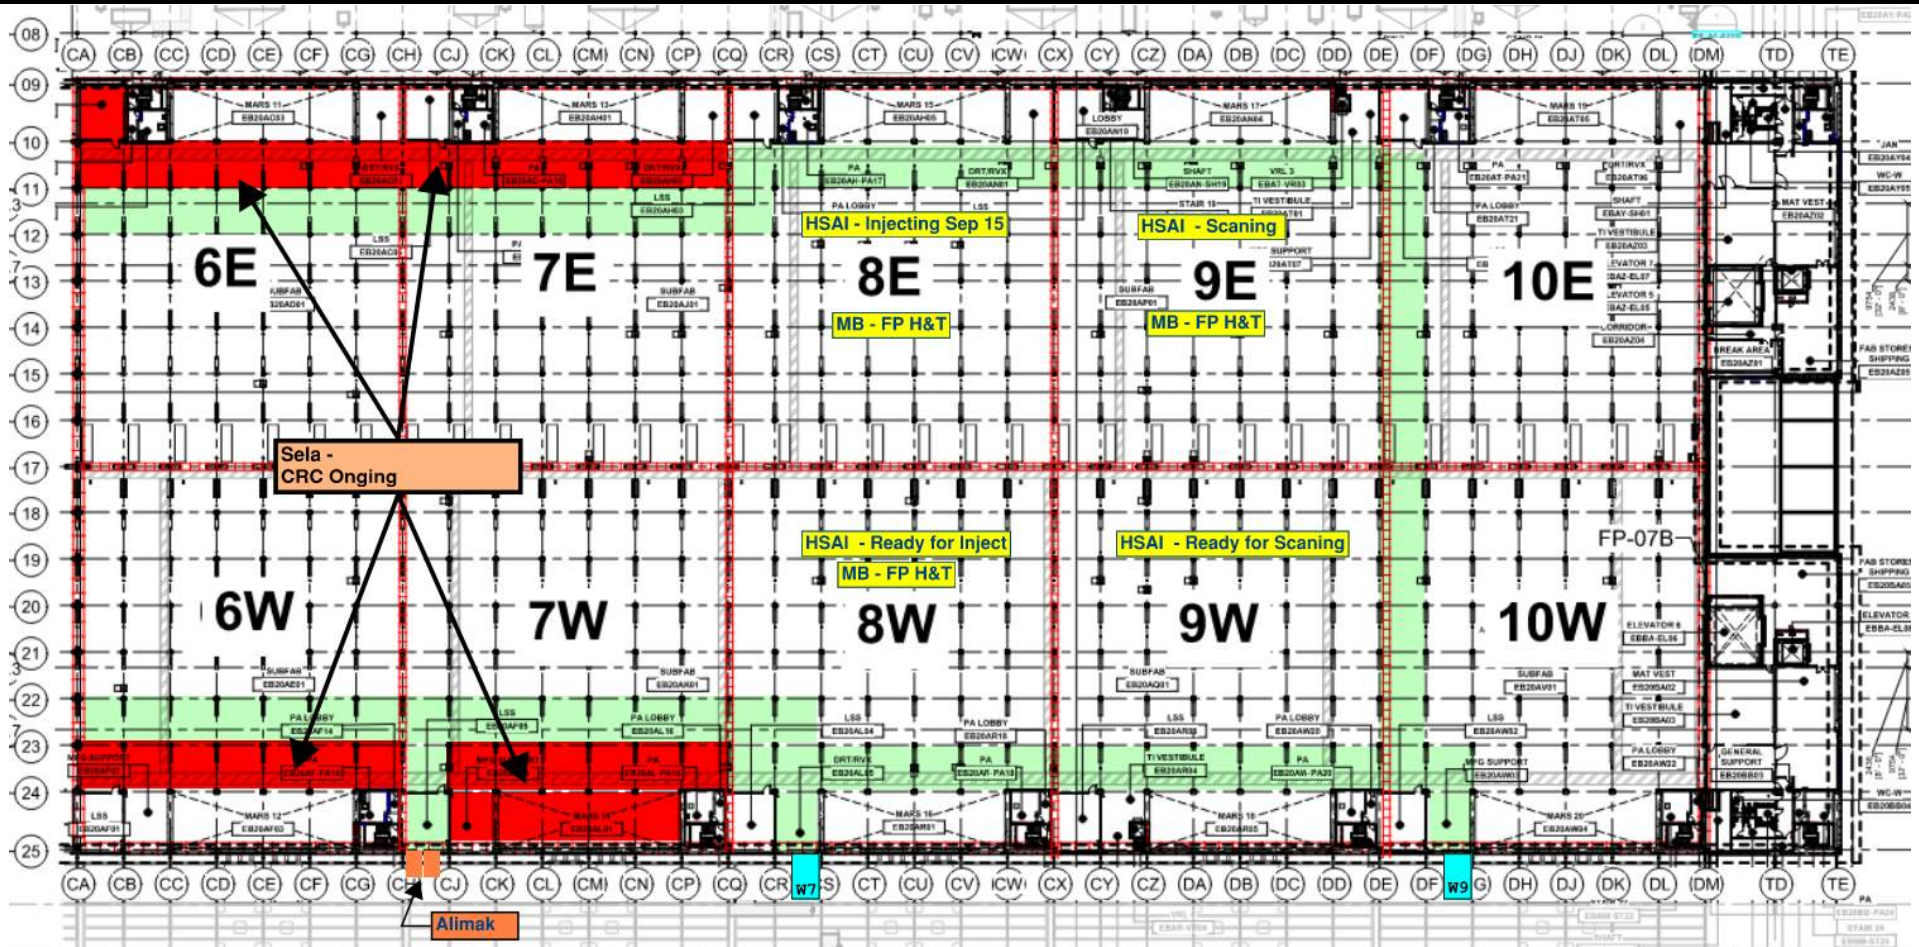

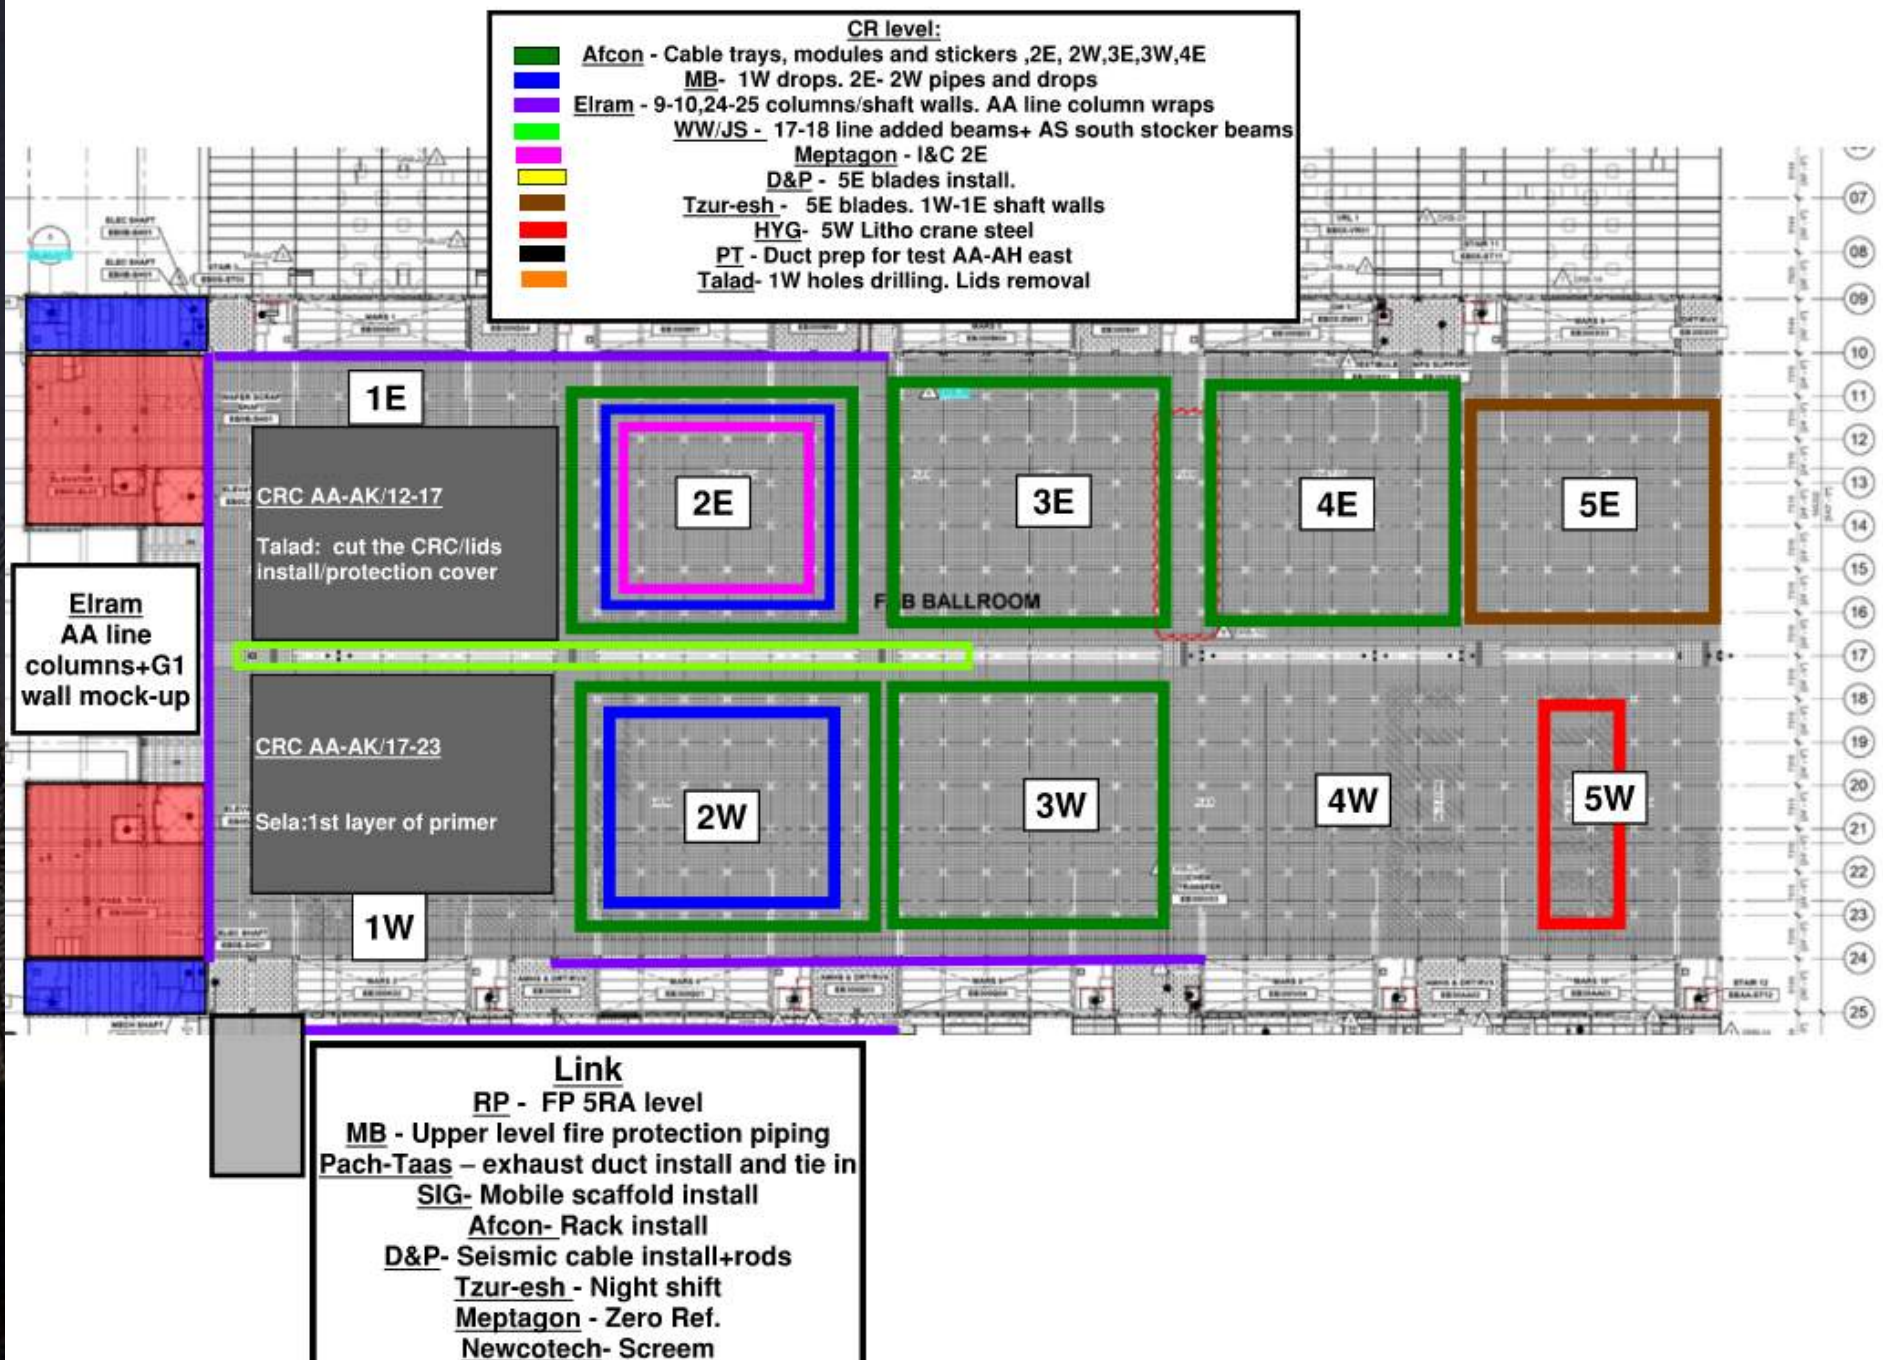

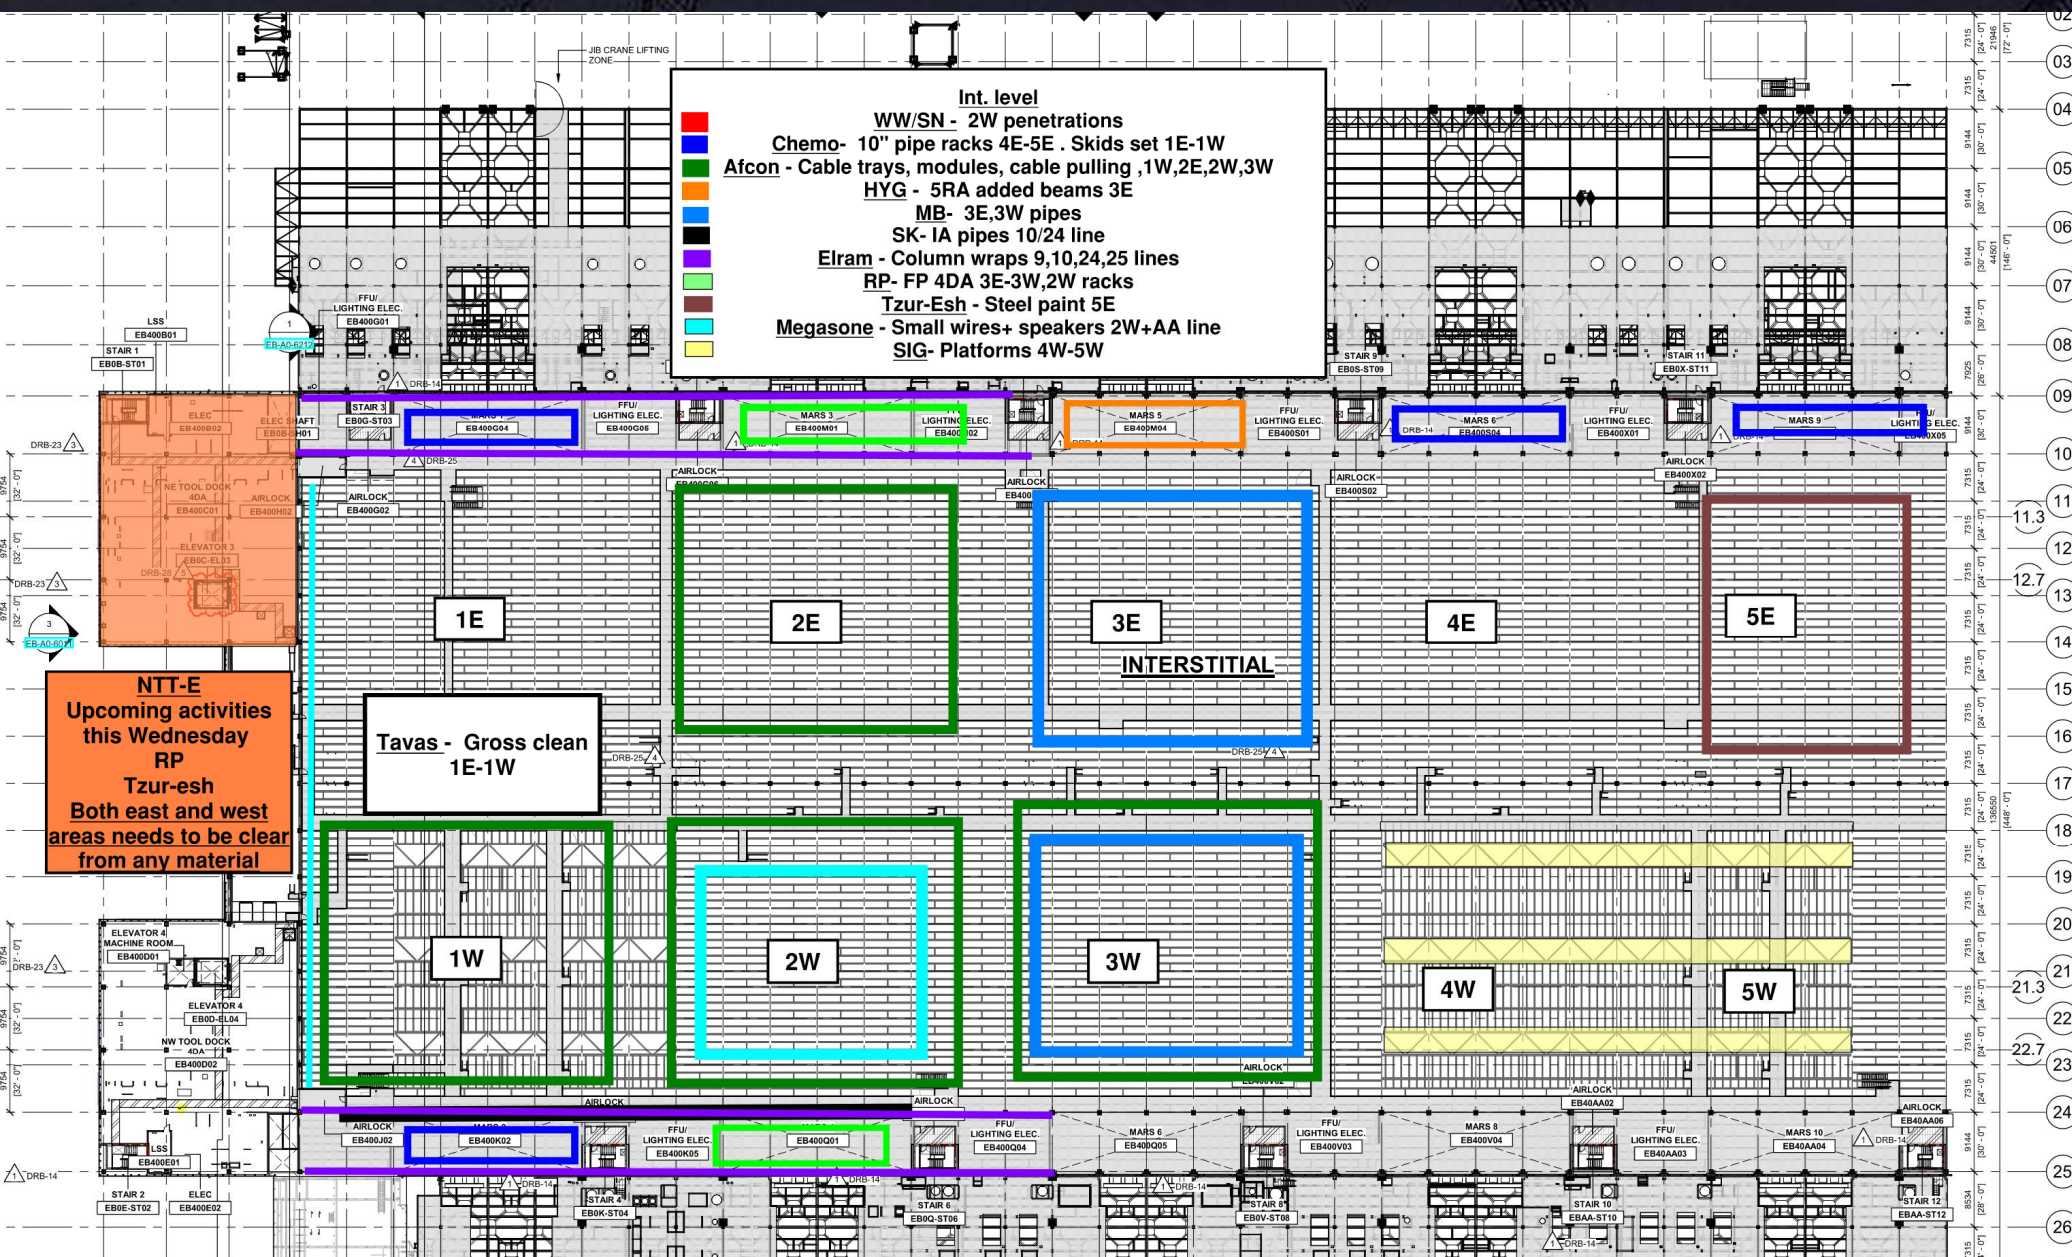



Truss Yard:
RP and Tzur-Esh to start FP and paint trusses on night shift

Infill ongoing


Tzur-esh
MOD2 paint


MIMO 4DA level CB-CC
SIG ongoing


Truss
Wednesday/Thursday


SEQ 270-271 Ongoing

SEQ 281 ongoing

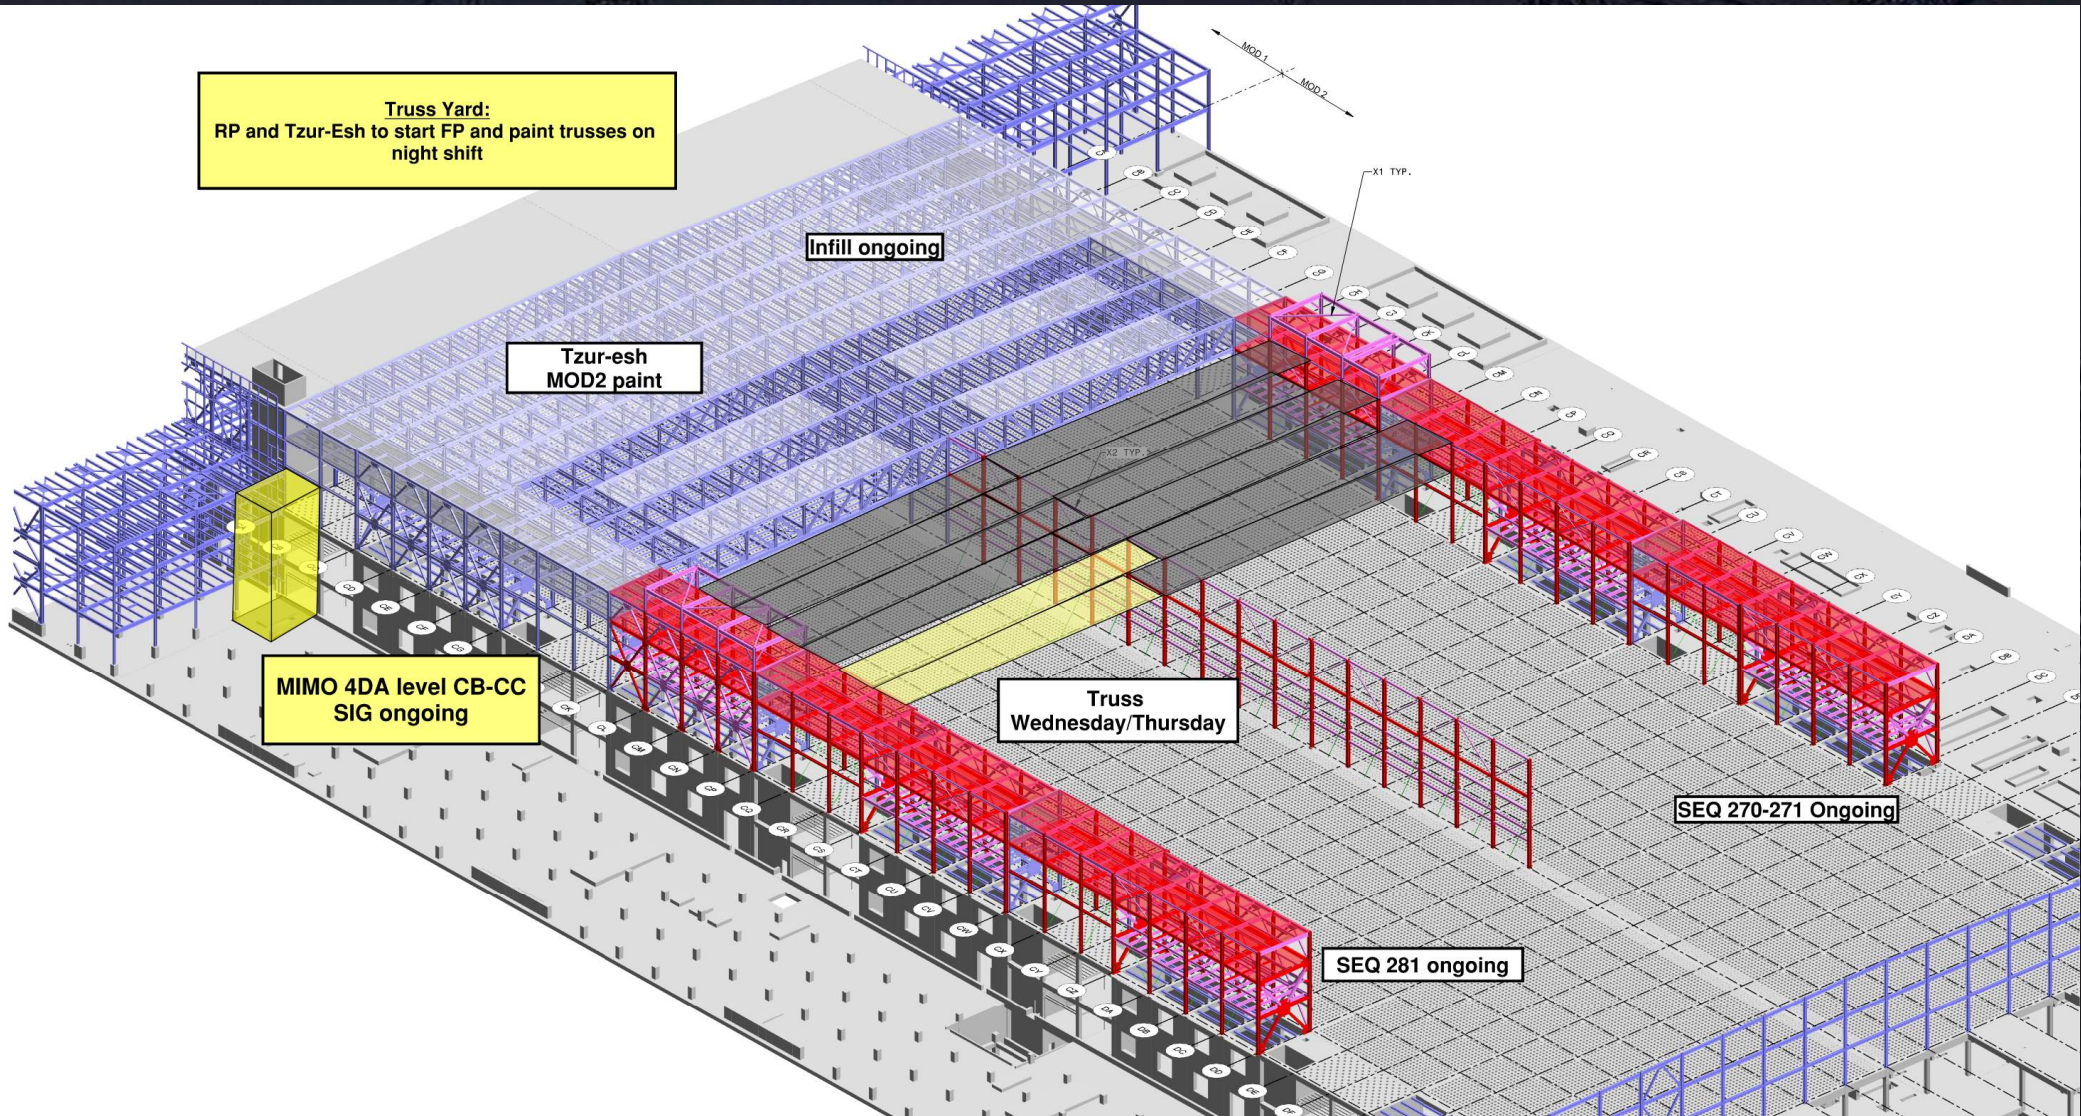

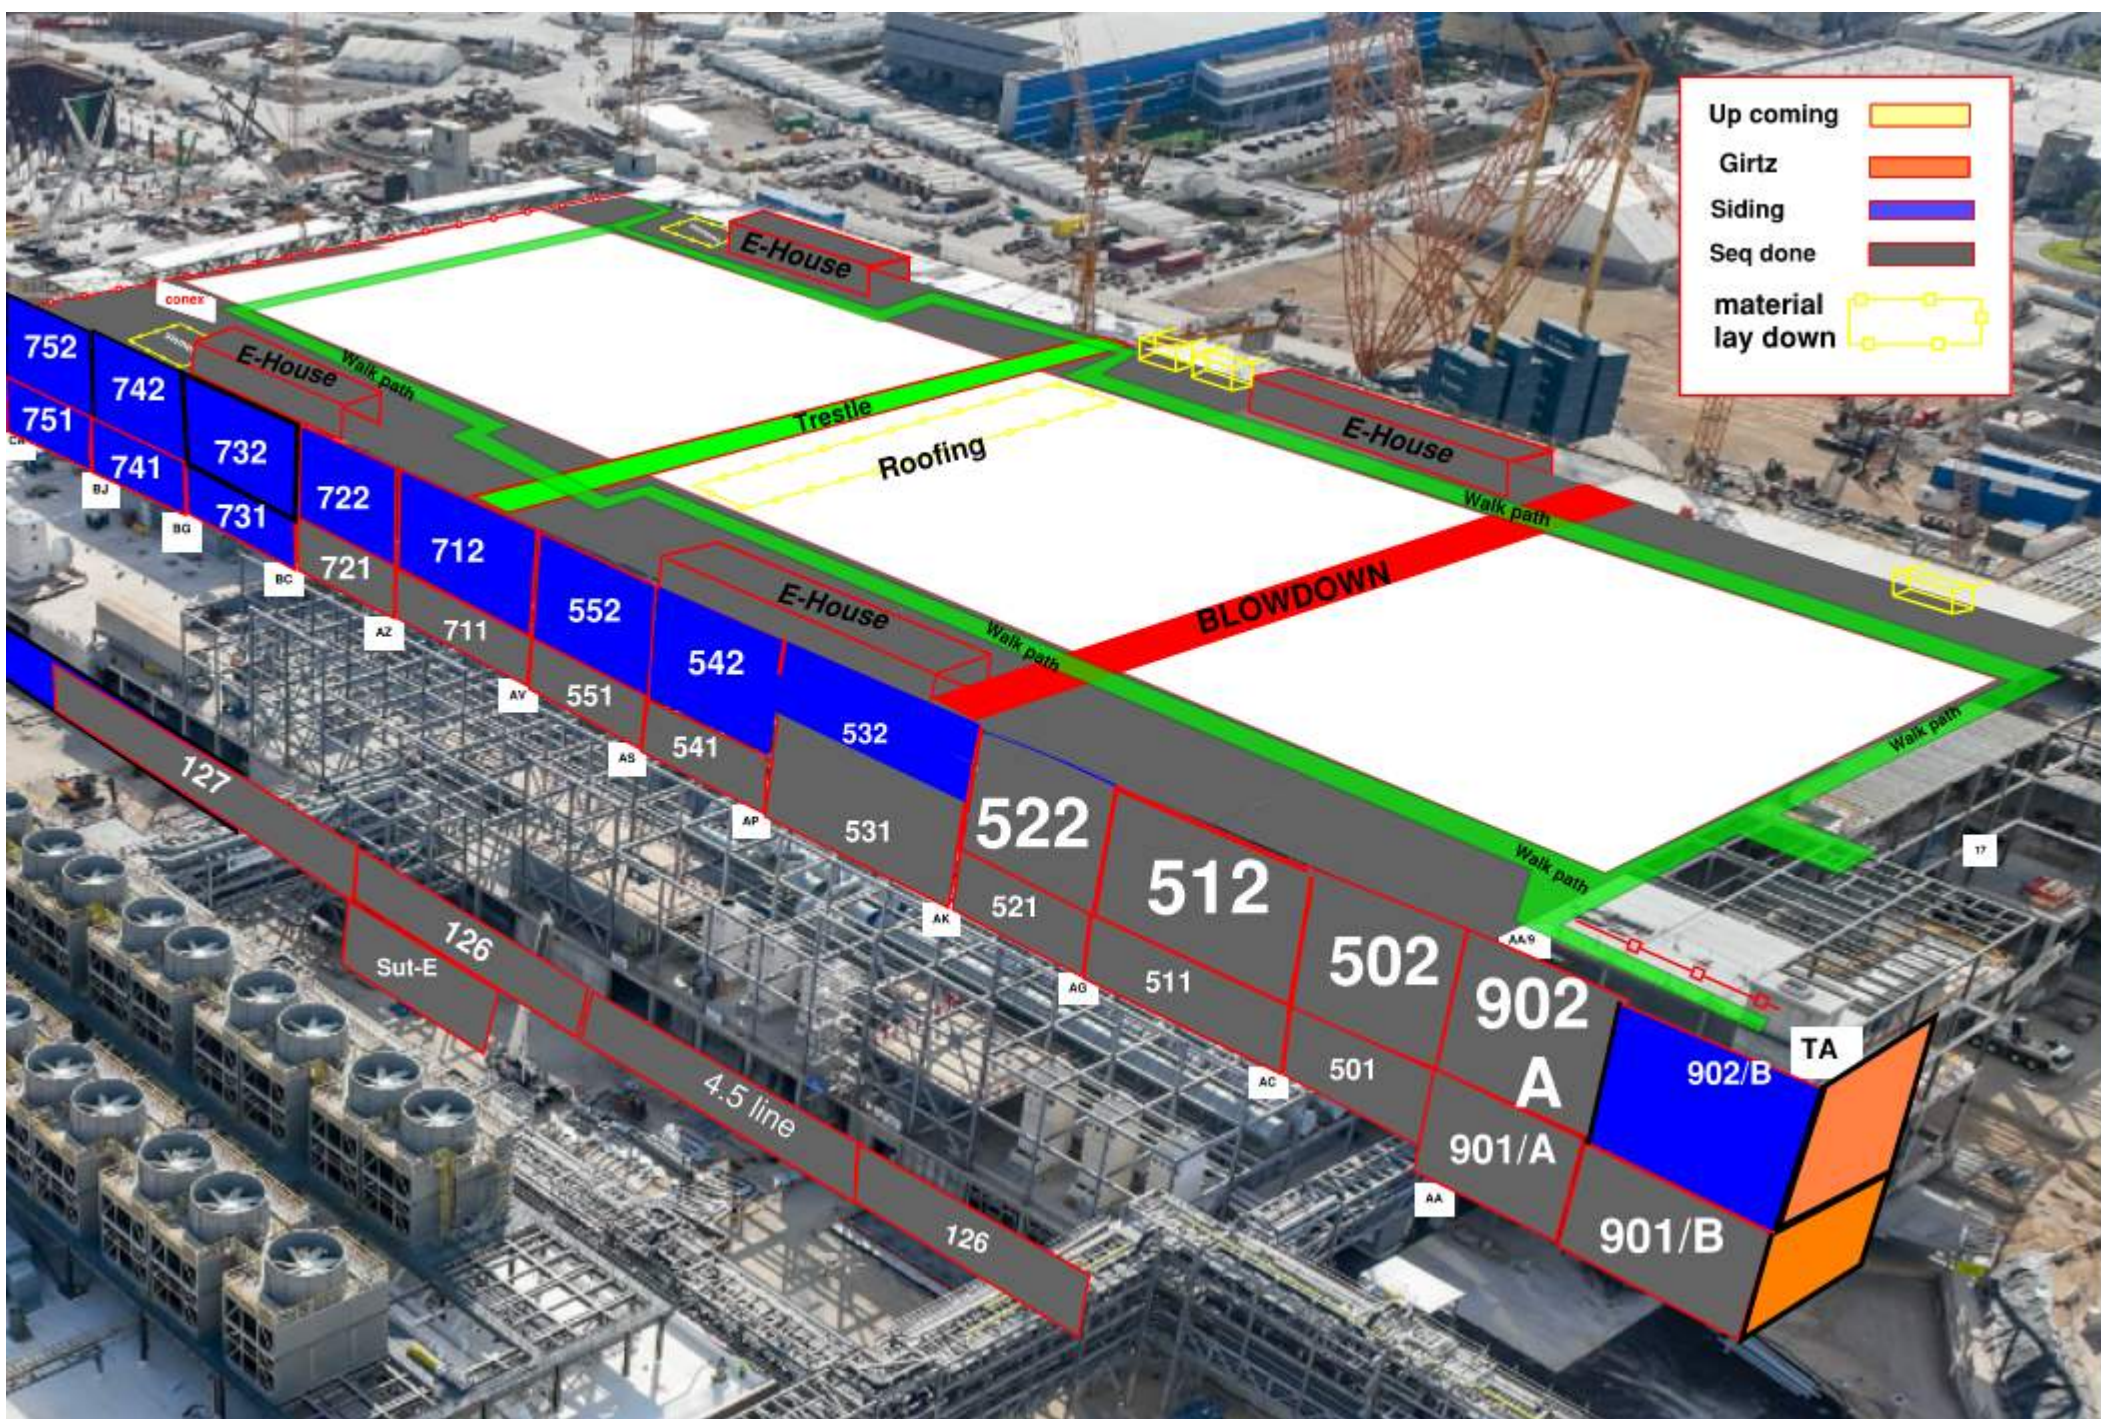

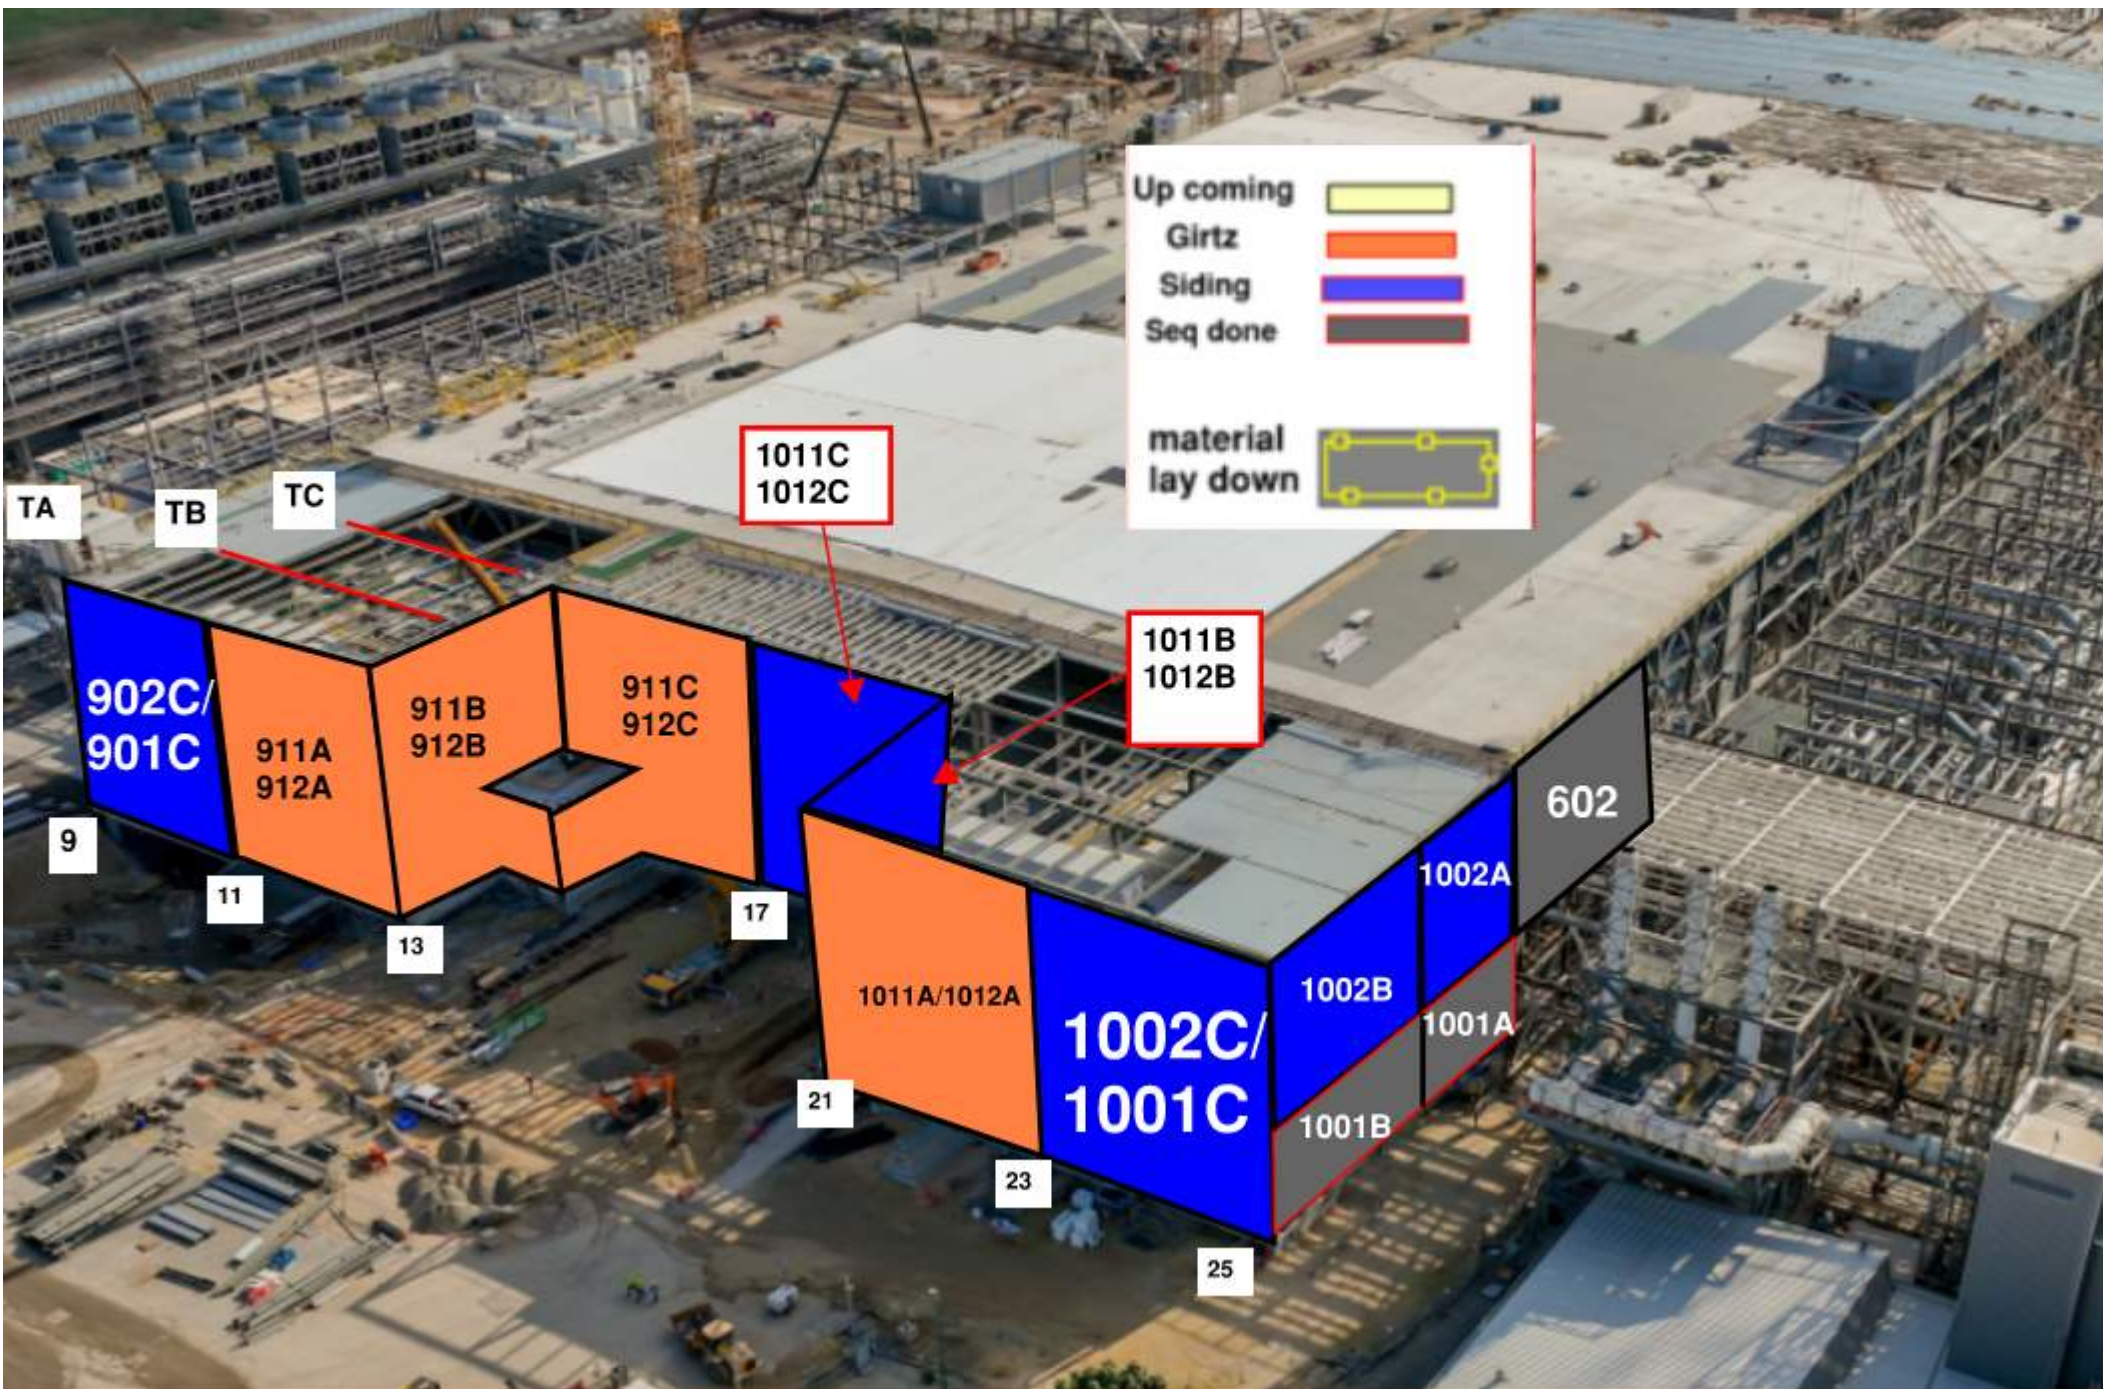

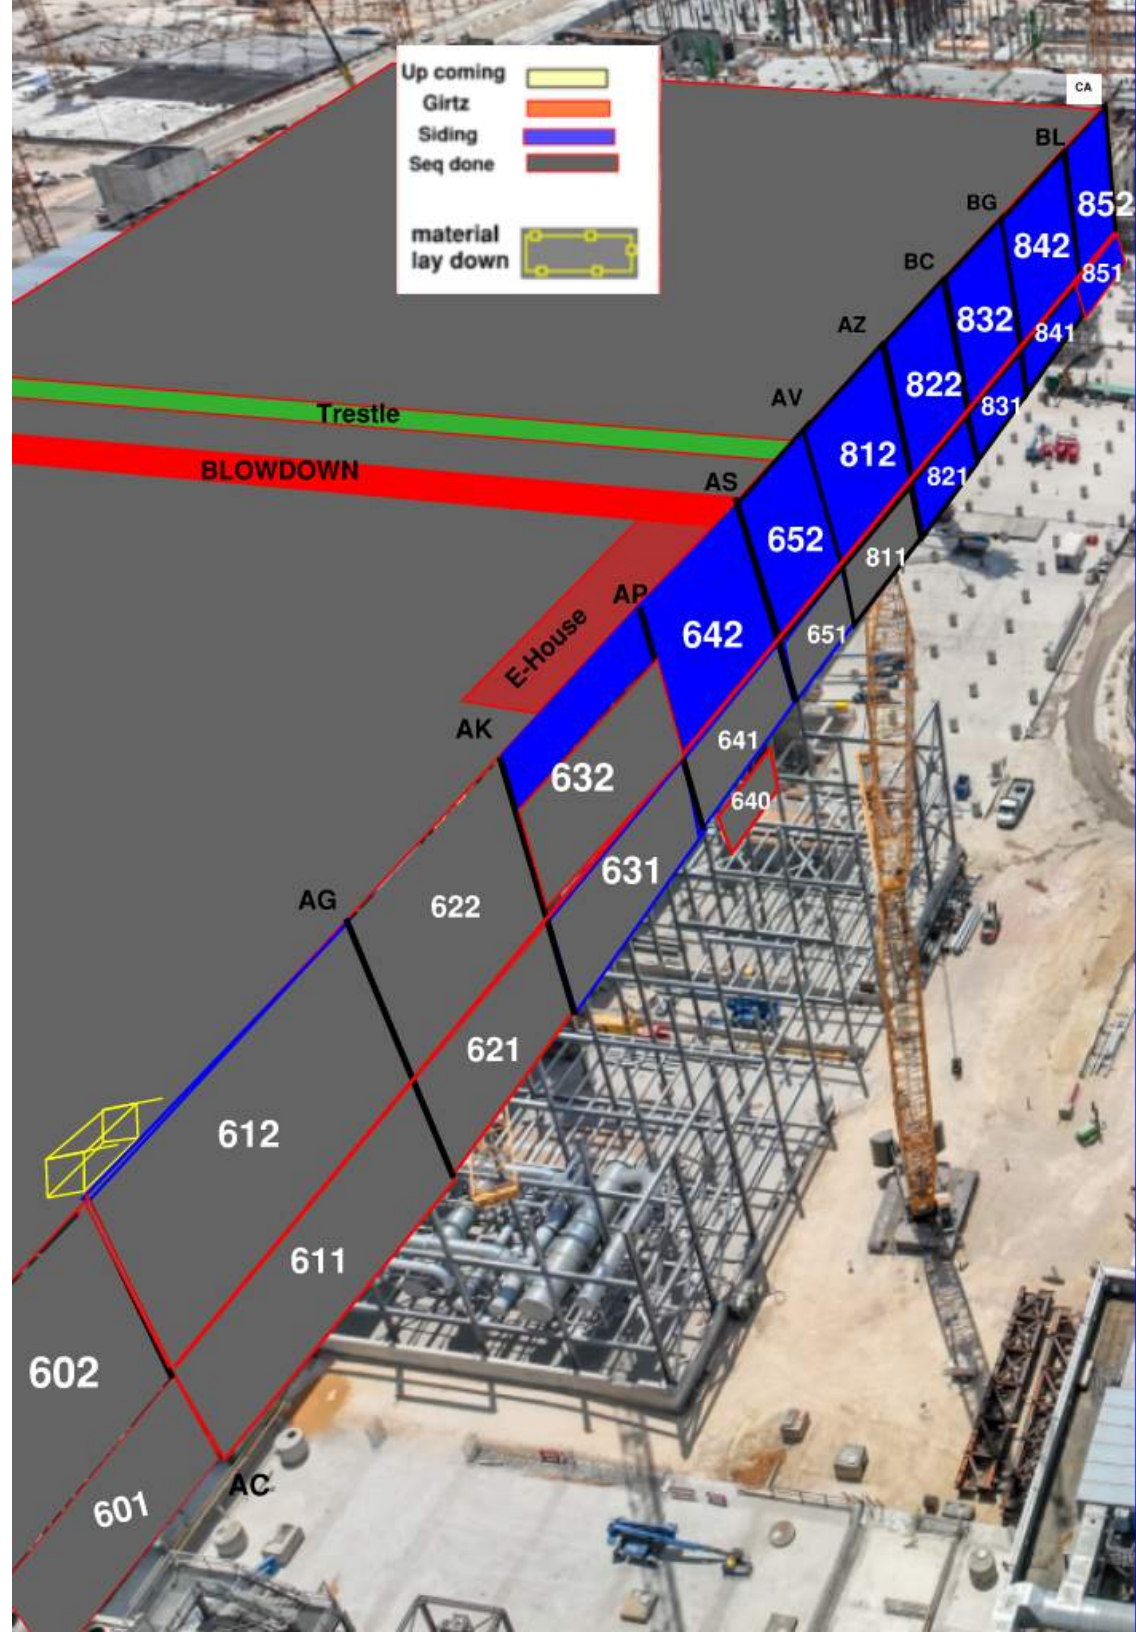

	AD	AE	AF	AG	AH	AI	AJ	AK	AL	AM	AN	AO	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BJ	BK	BL	BM	BN	BO	BP	BQ	BR	BS	BT	BU	BV	BW	BX	BY	BZ
1																																																	
2																																																	
3																																																	
4																																																	
5	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BK	BL	CA																								
6	11 / 632		641 / 642				651 / 652				661 / 662				671 / 672				681 / 682				691 / 692				701 / 702																						
7	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31																										
8	23	13	3	3	14	6	6	6	6	14	14	14	14	6	6	6	6	6	6	6	6	6	6																										
9	74X	42X	29X	29X	45X	19X	19X	19X	19X	45X	45X	45X	45X	19X	19X	19X	6X	6X	6X	6X	6X	6X	6X																										
10																																																	
11																																																	
12																																																	
13																																																	
14																																																	
15																																																	
16																																																	
17																																																	
18																																																	
19																																																	
20																																																	
21																																																	
22																																																	
23																																																	
24																																																	
25																																																	
26																																																	
27																																																	
28																																																	
29																																																	
30																																																	
31																																																	
32																																																	
33																																																	
34																																																	
35																																																	
36																																																	
37																																																	
38																																																	
39																																																	
40																																																	
41																																																	
42																																																	


Siding - East FAB - PSSS

BLOWDOWN 30%

PSSS.1


Utility Level 1YA

PSSS Roof 2SA

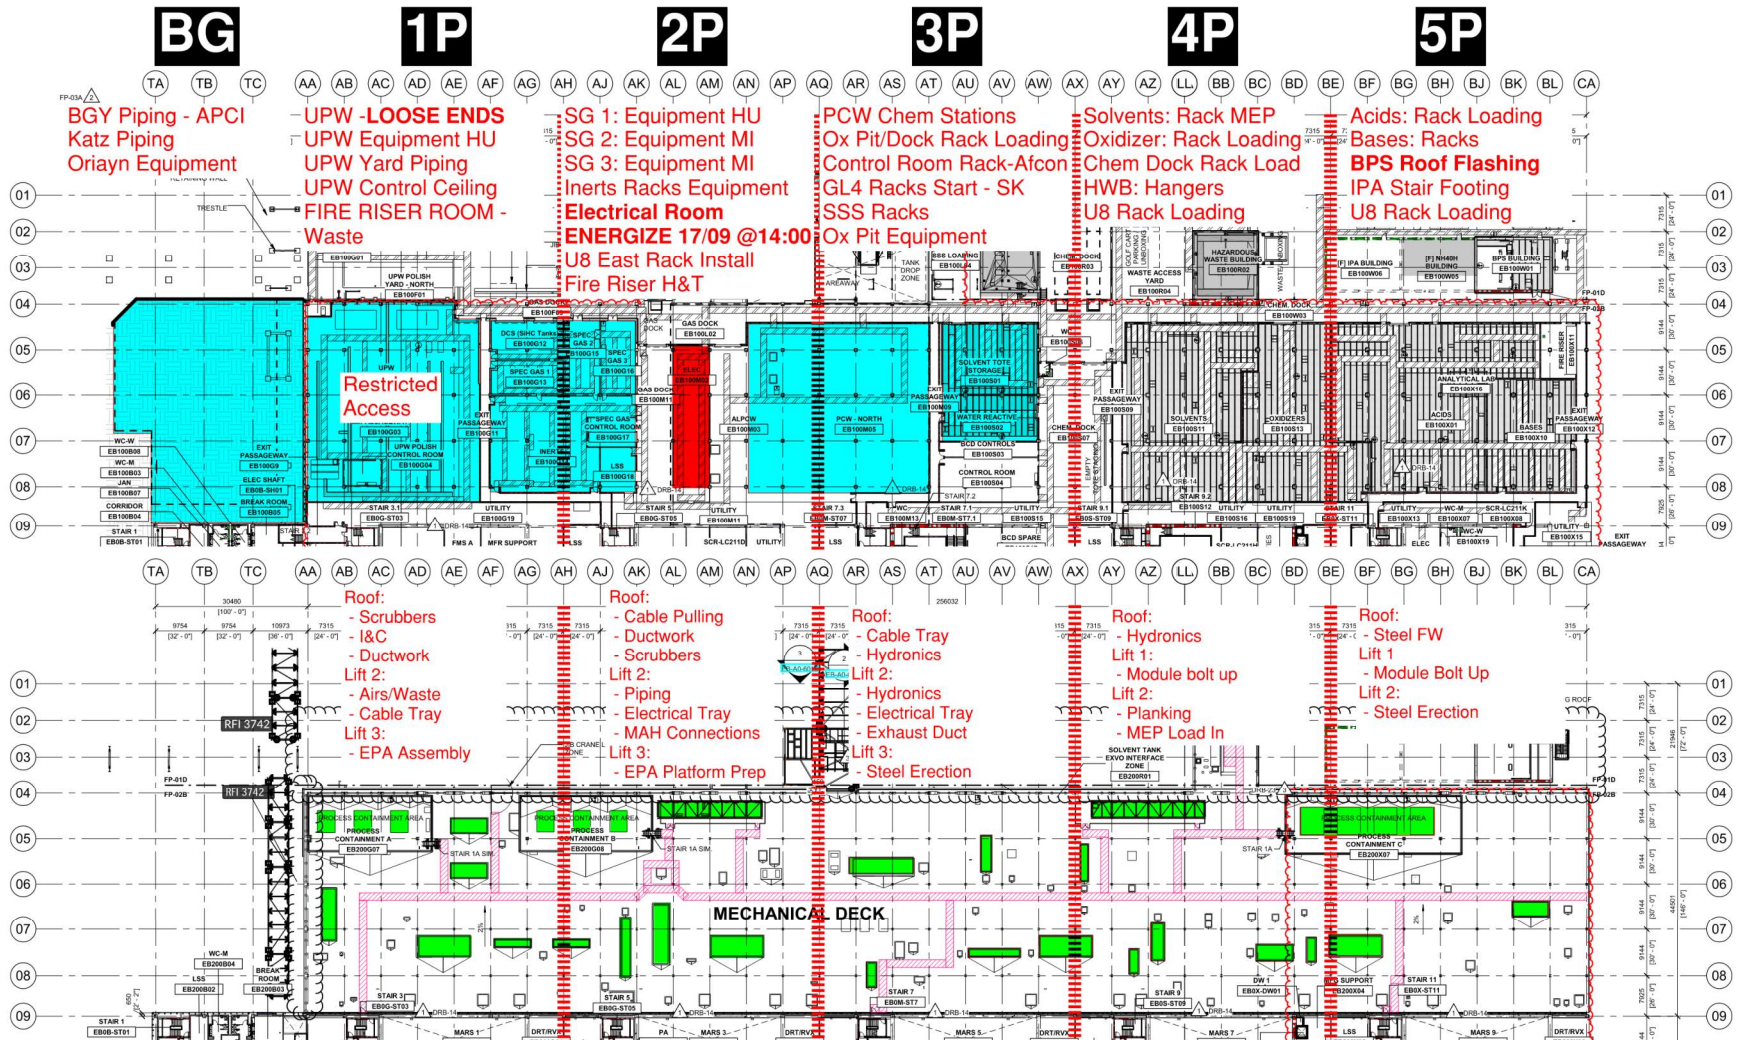


PSSS.2

Utility Level
1YA

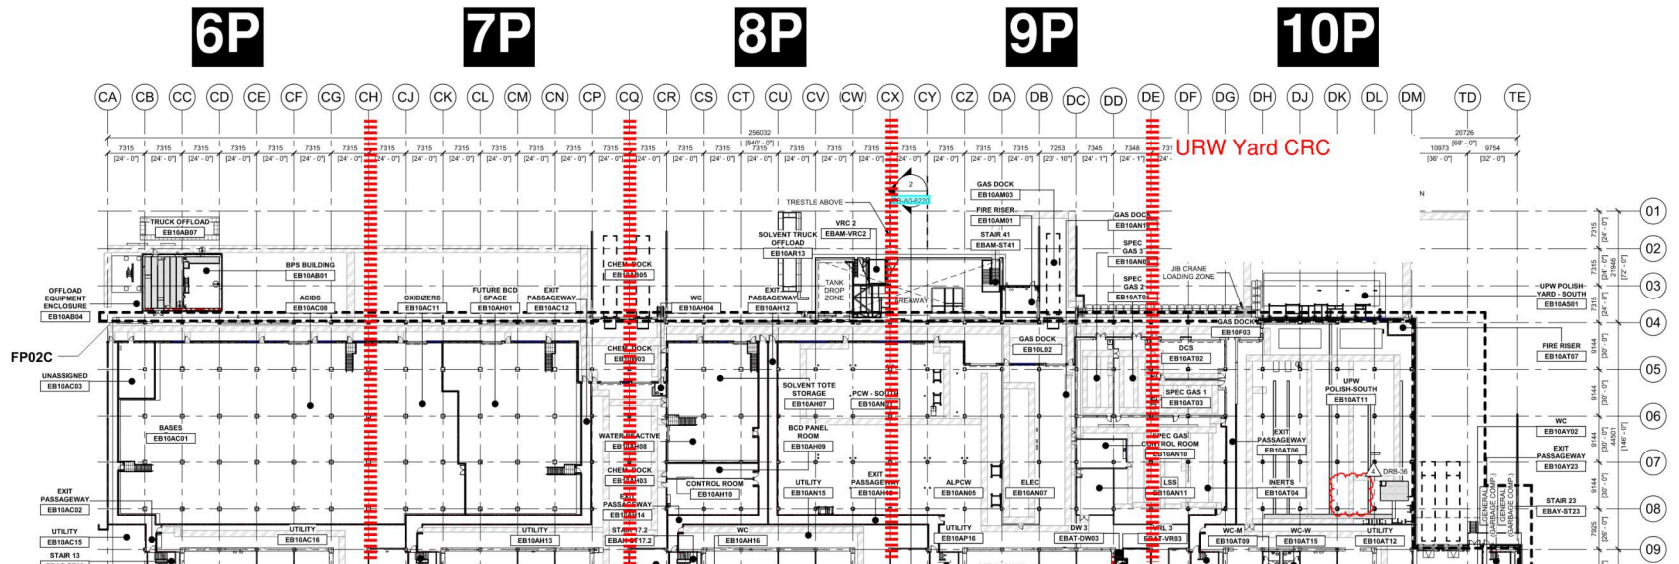

PSSS Roof
2SA

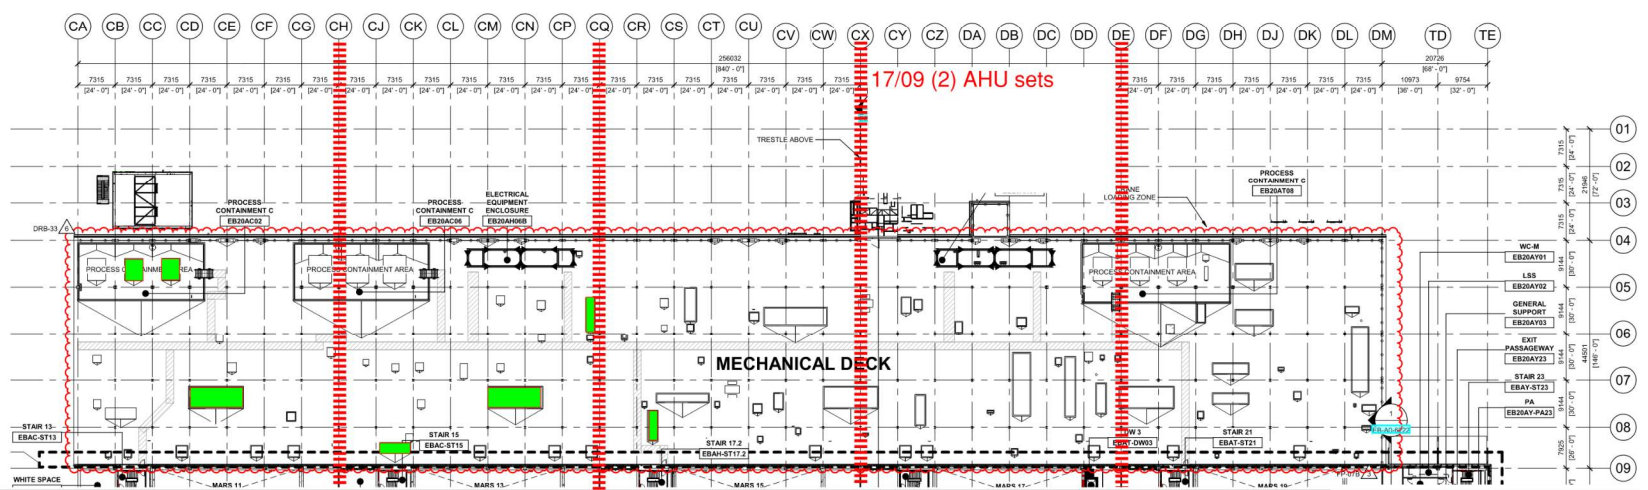


PSSS

4P VFD Set


Crane Mats – 19/09

DMAG Move – 22/09


Hoist VFD – 24/09

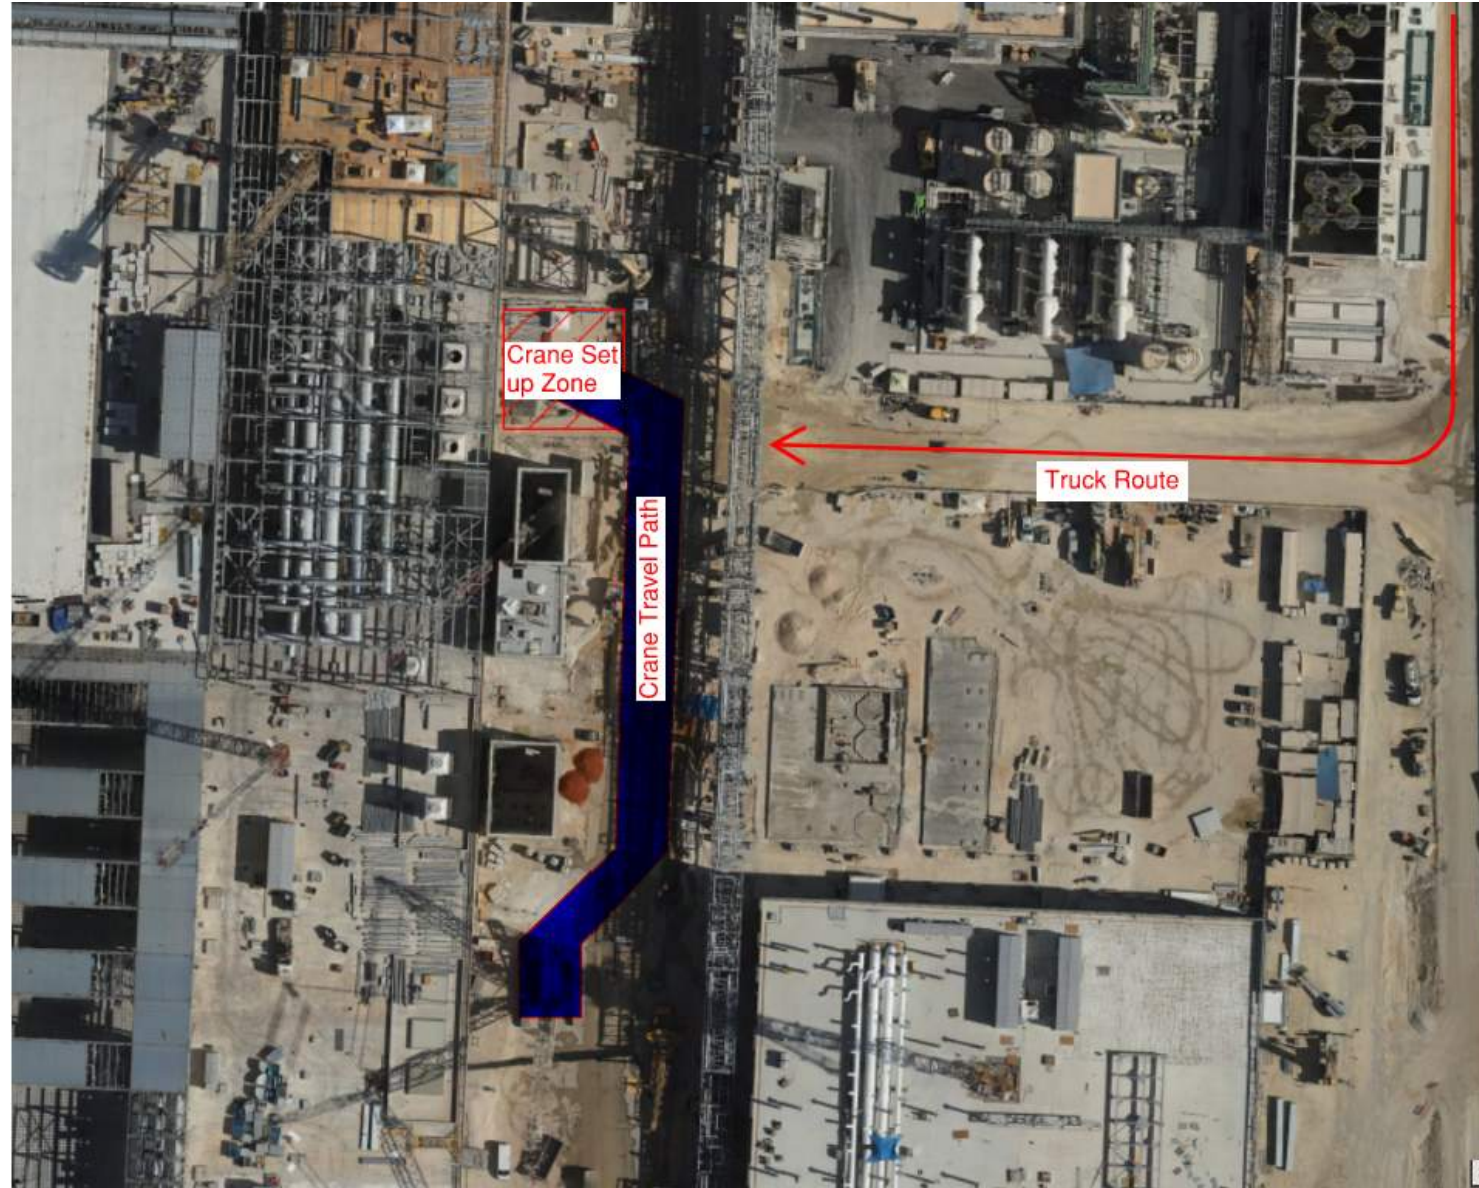


PSSS DMAG ROAD CLOSURES

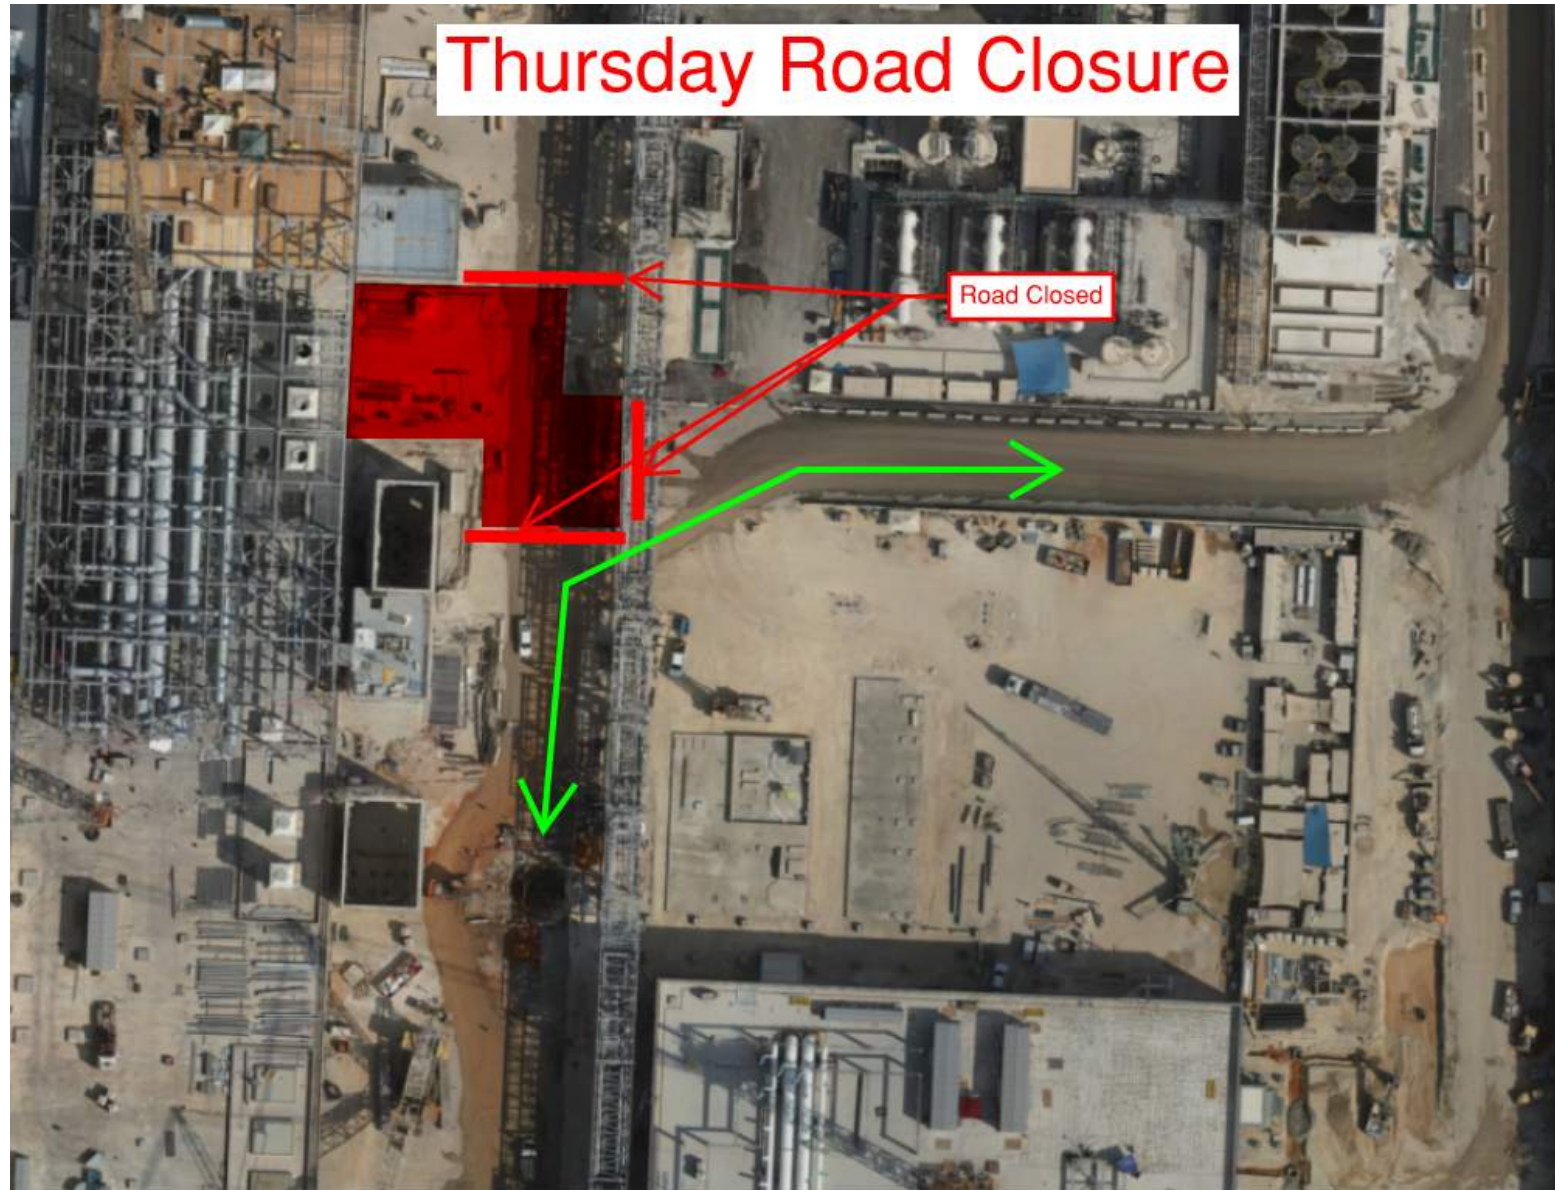


PSSS DMAG ROAD CLOSURES

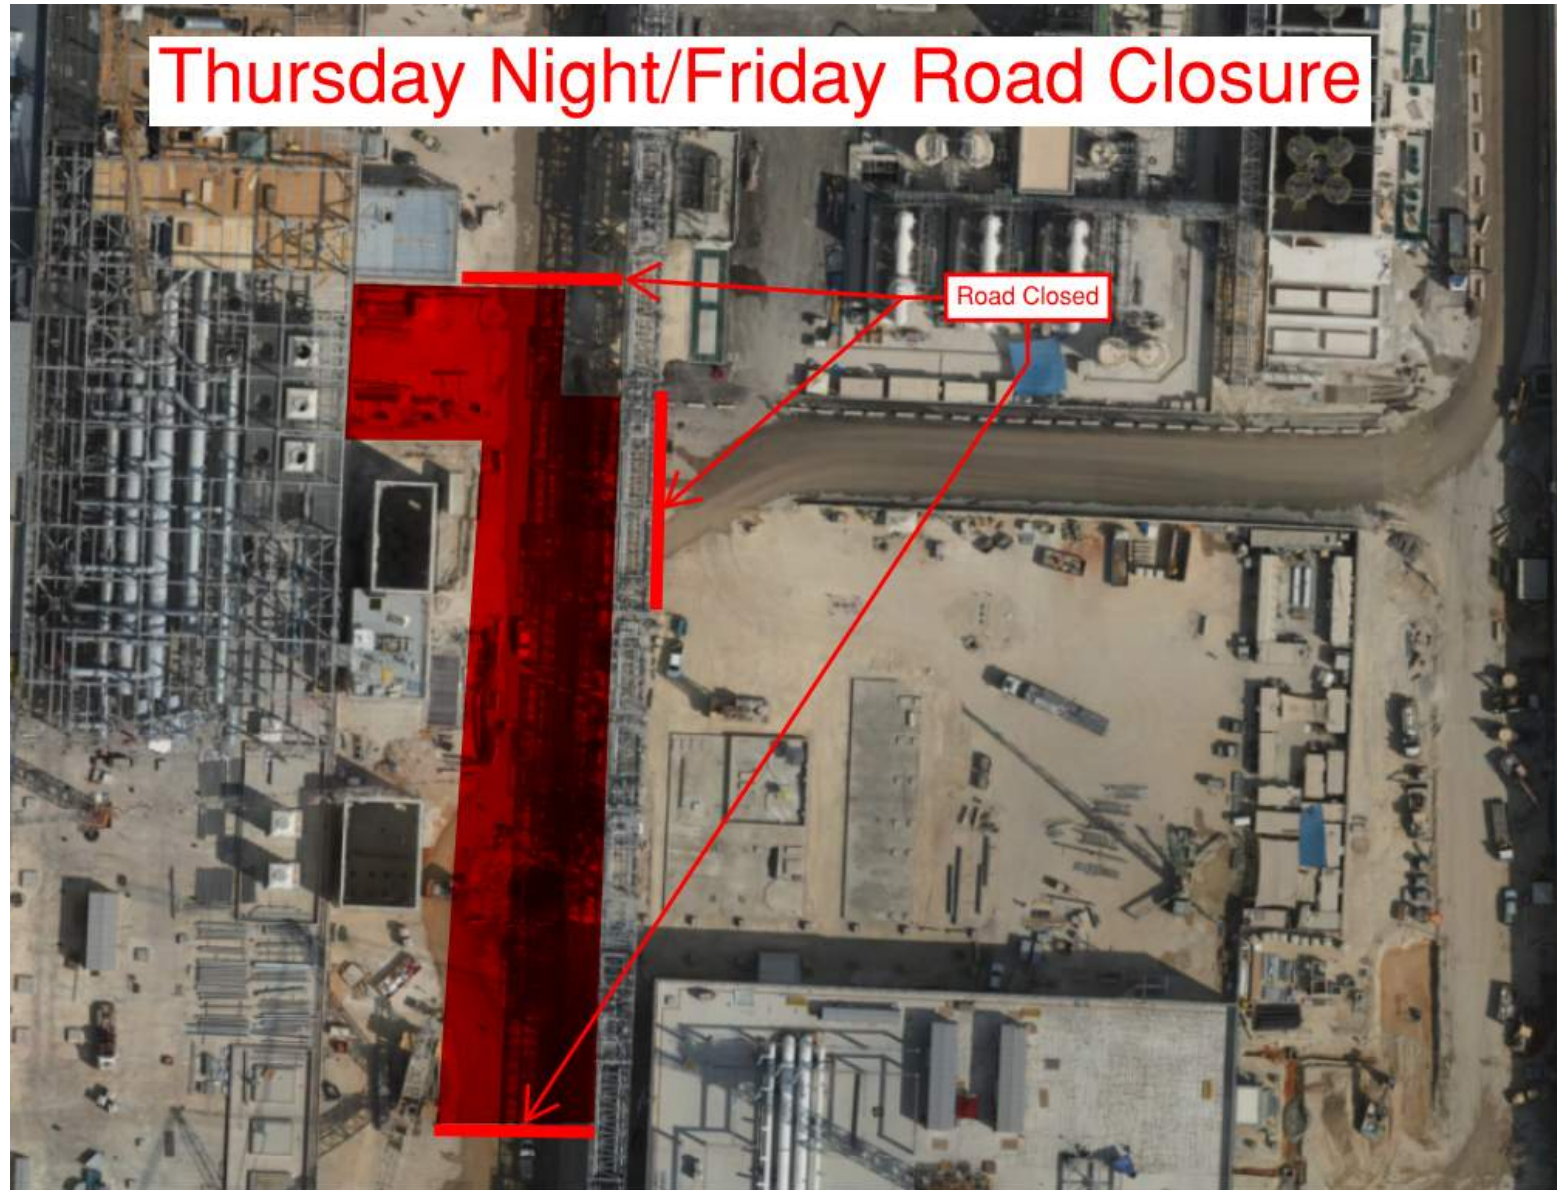


PSSS DMAG ROAD CLOSURES

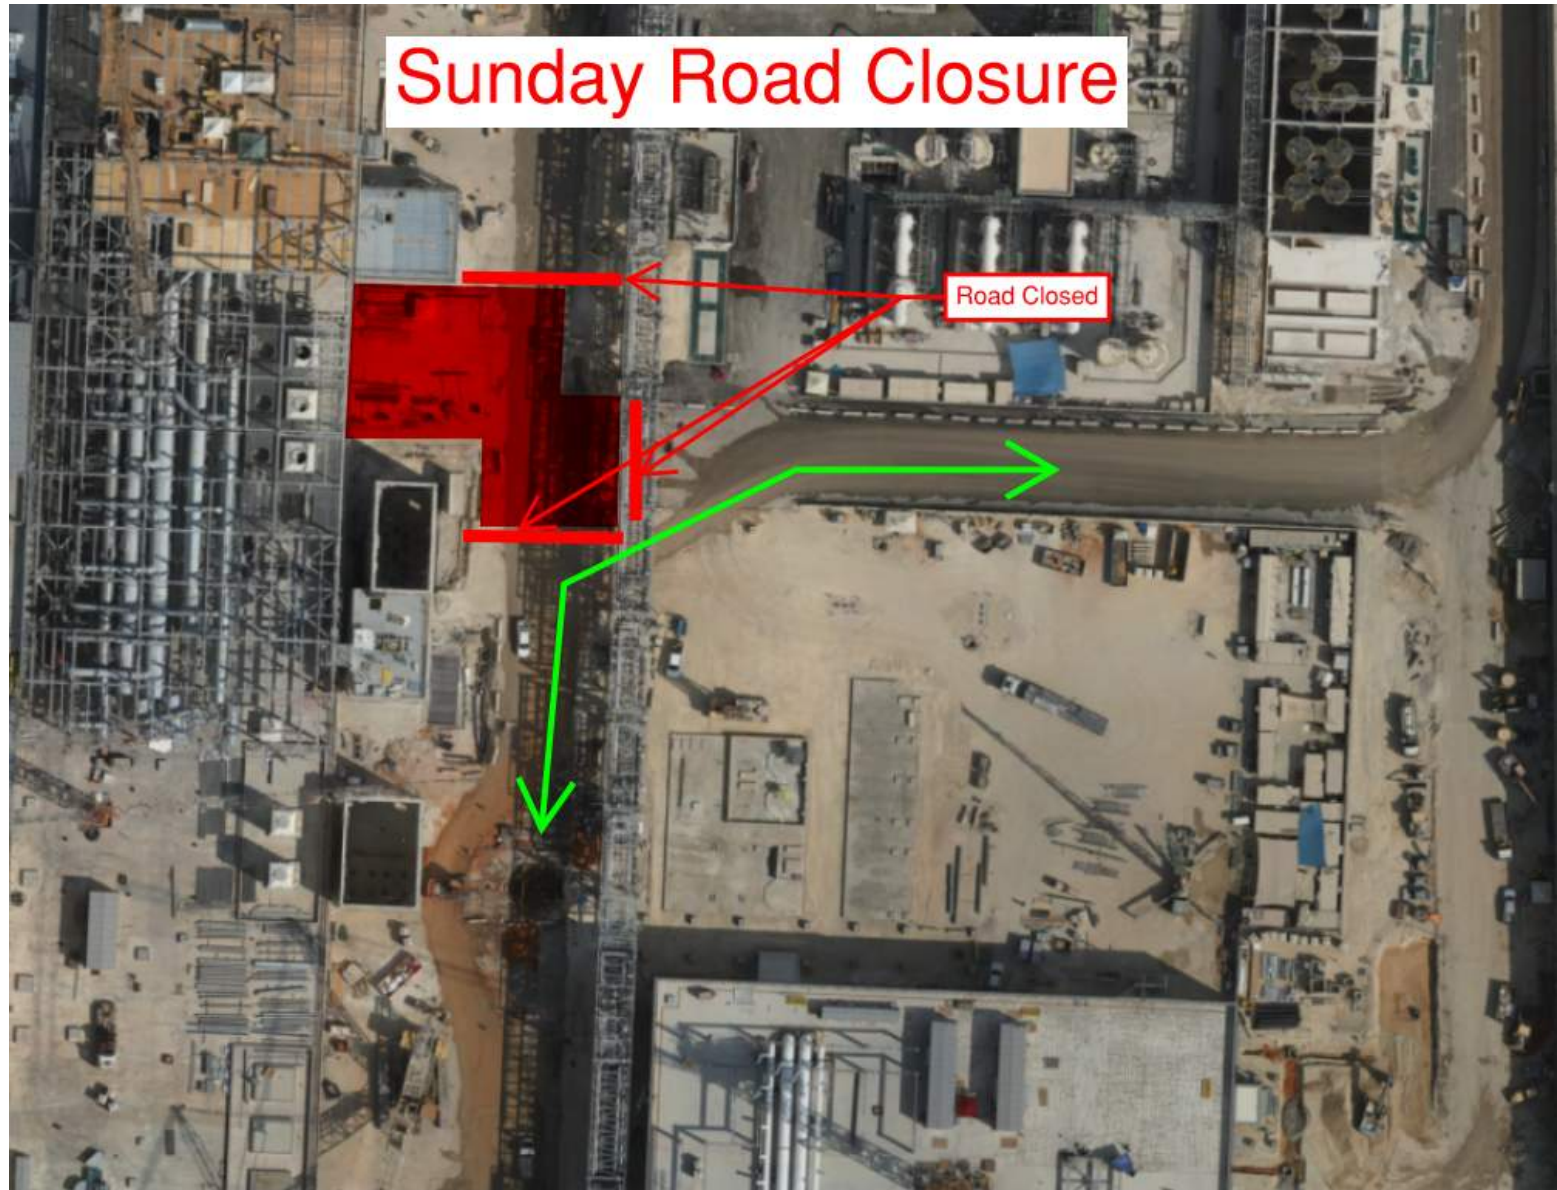





WJG 01J, 02J LIFT 2 & 3

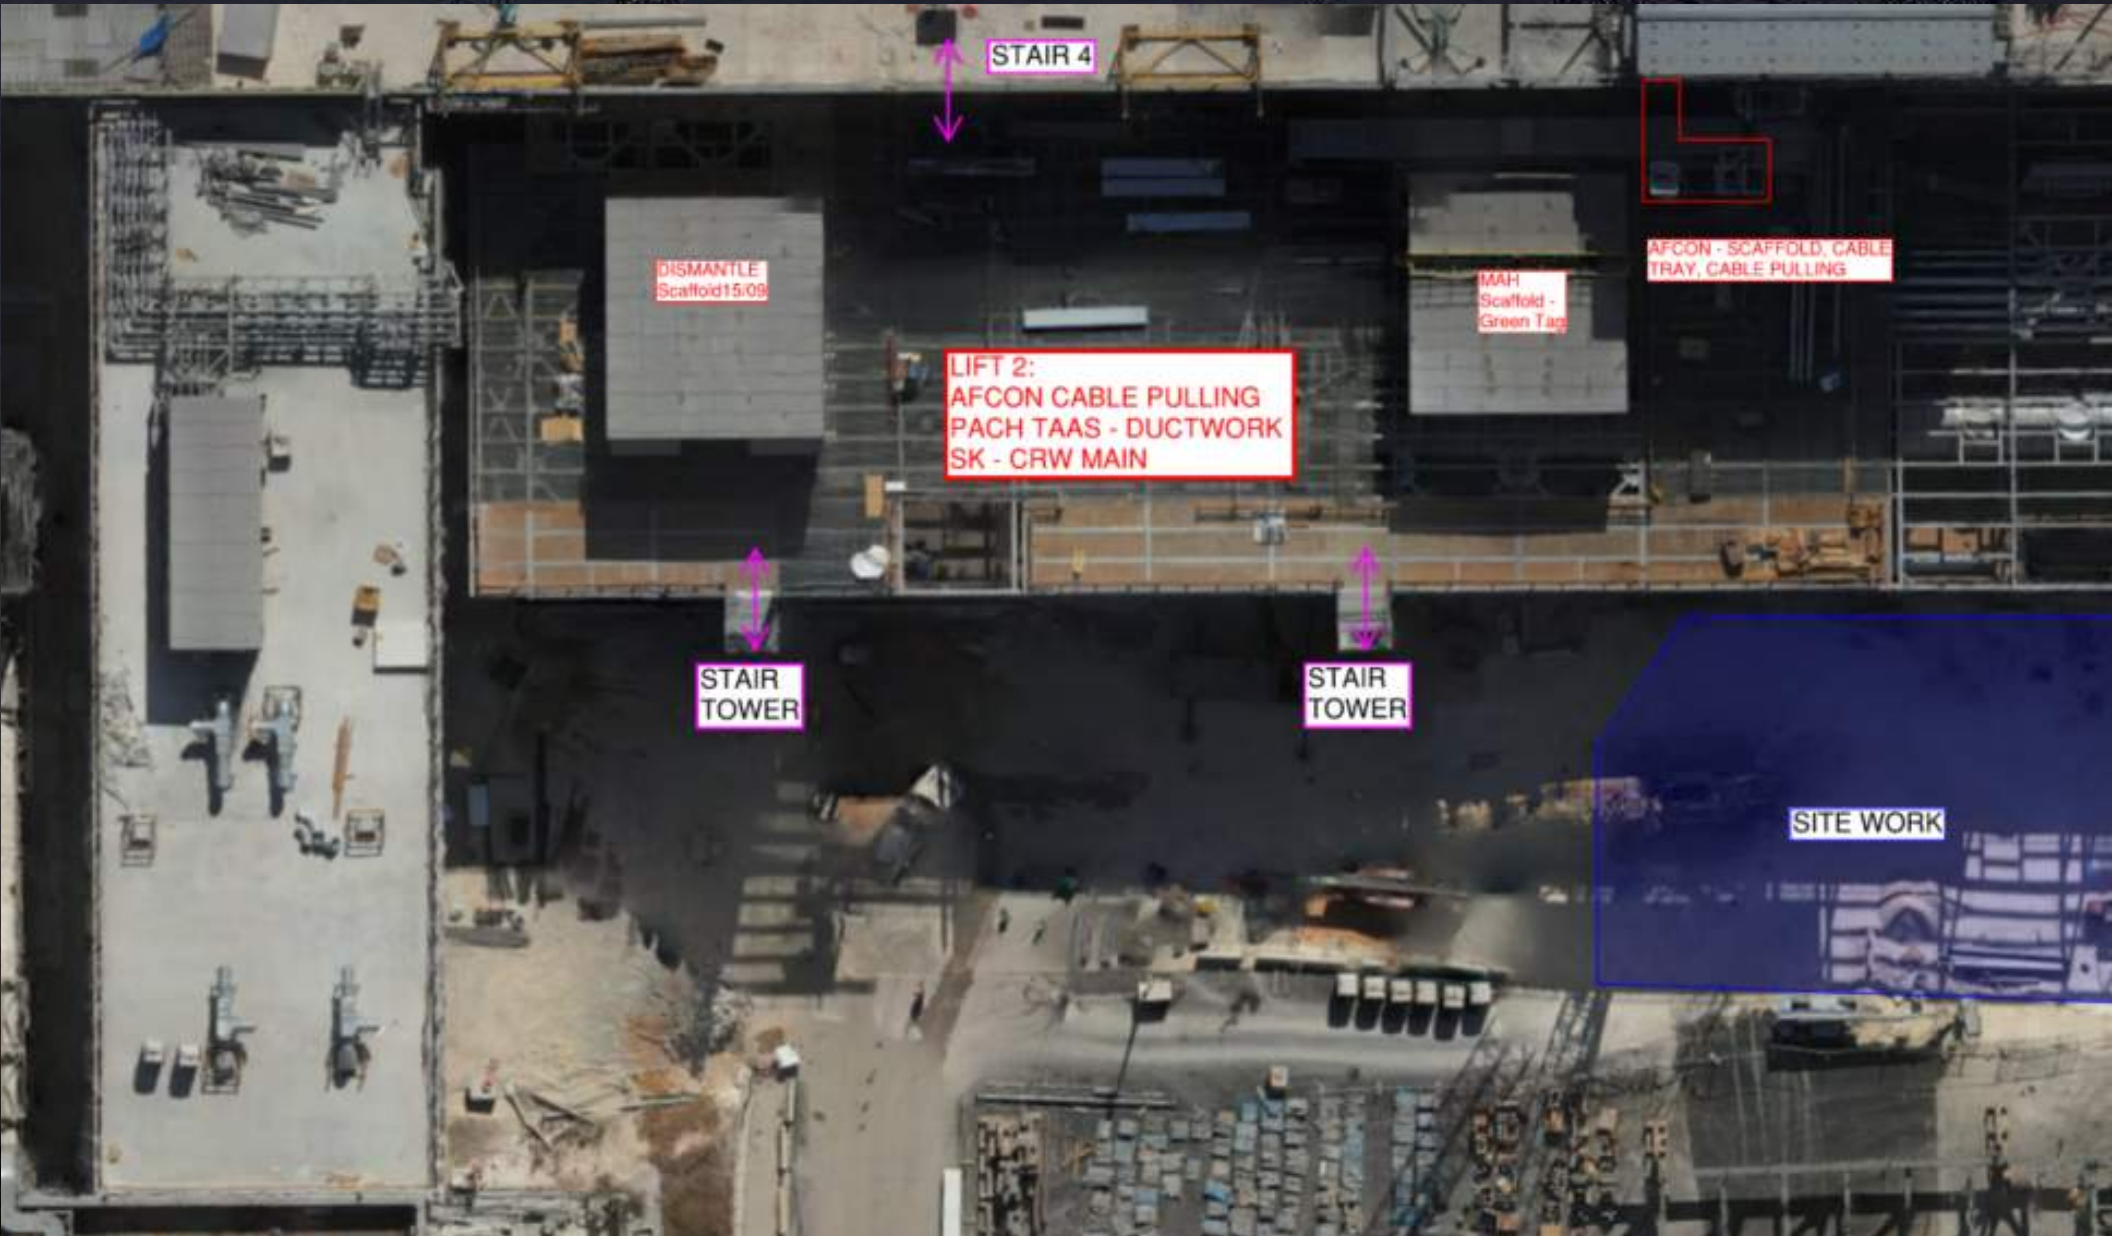

WJG 03J, 04J, 05J LIFT 2 & 3




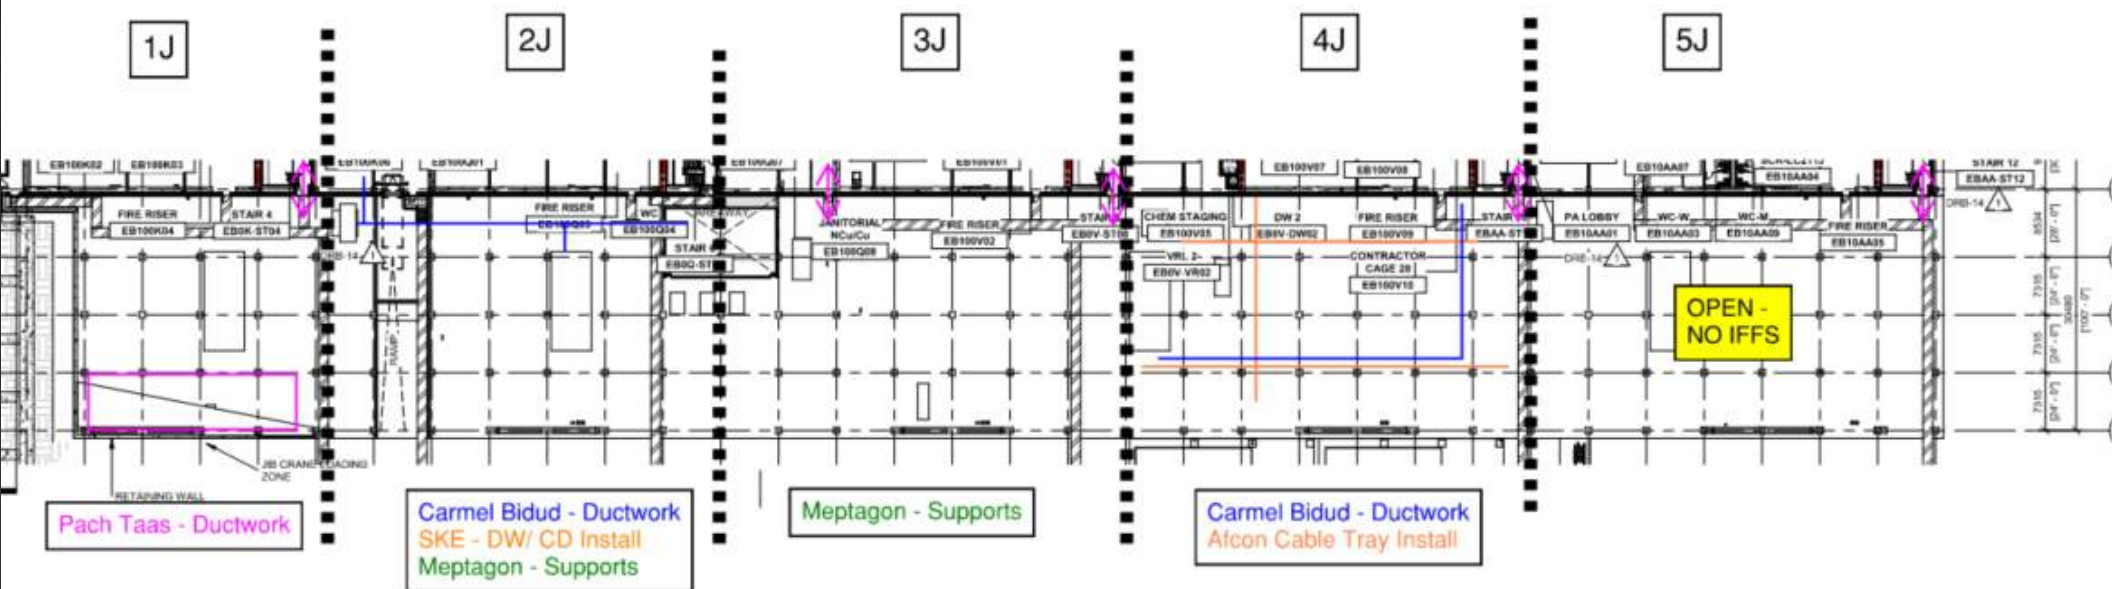





WJG Closed Night Shift 17/09/2024

SKE IA/PA PNEUMATIC TEST
138 PSI - 8 Hour
30m EXCLUSION ZONE
MAIN GL 28 @ UTILITY LEVEL
Date: 17/09/2024
2100 - 0600

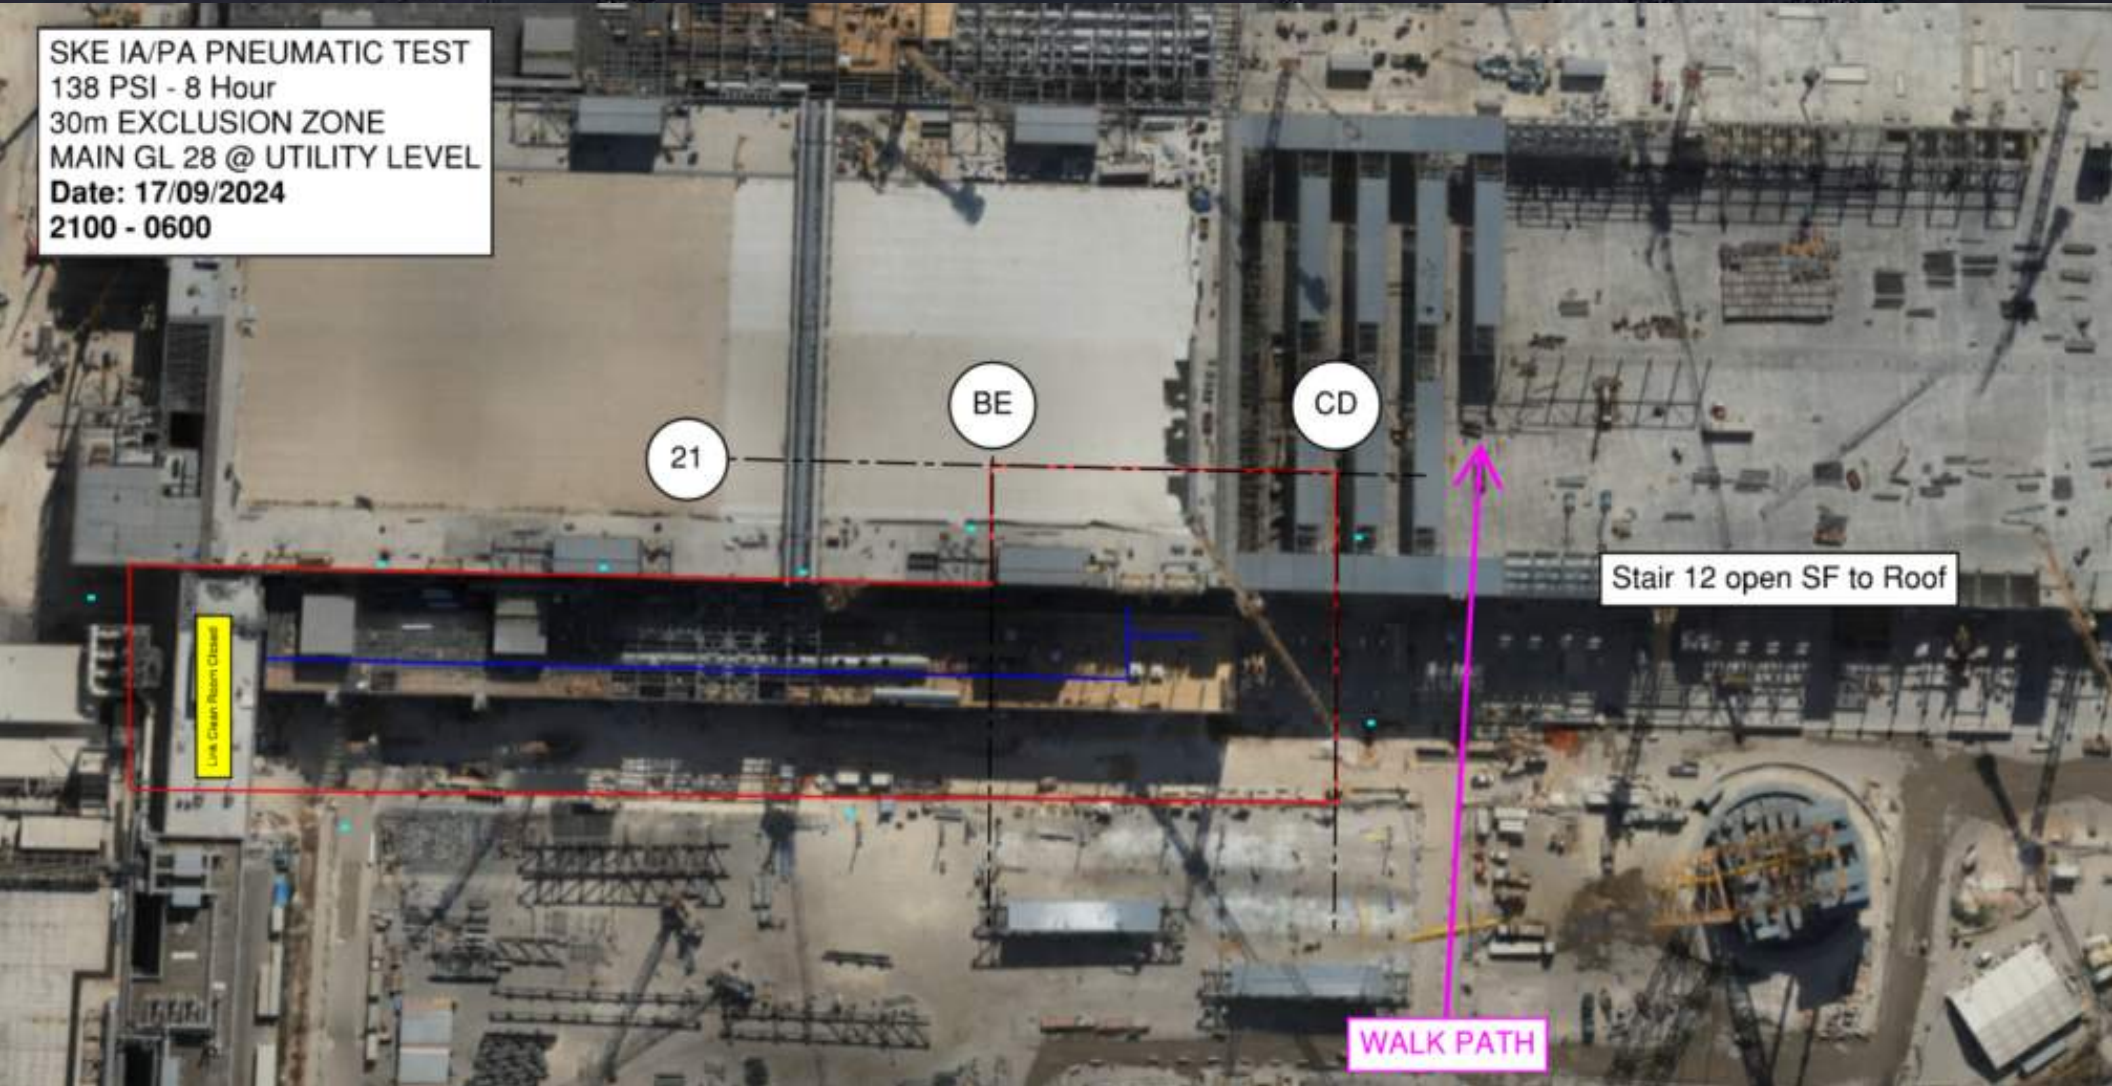



VFD SET 16/09/2024 & 18/09/2024

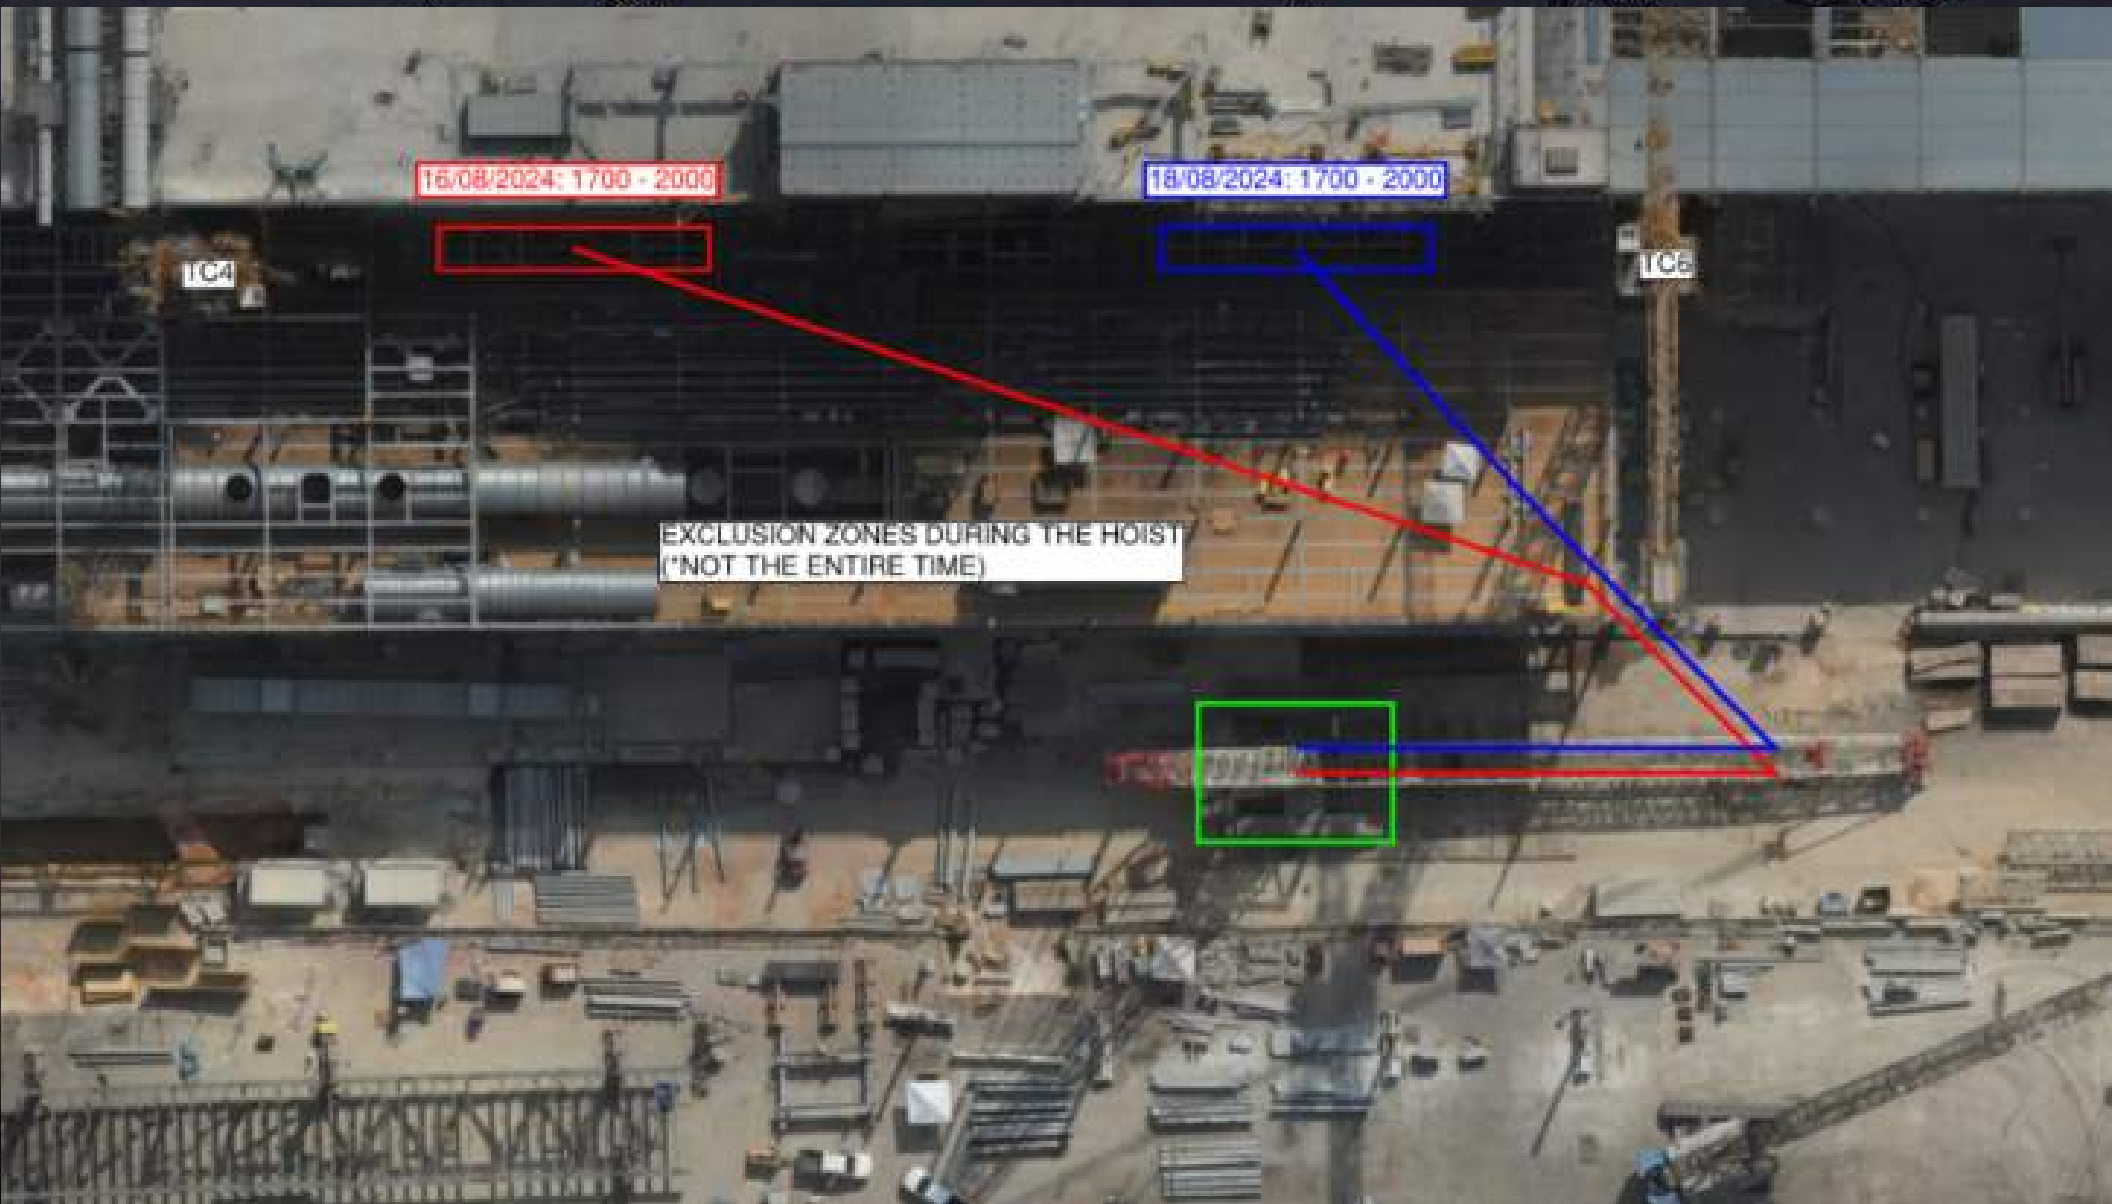


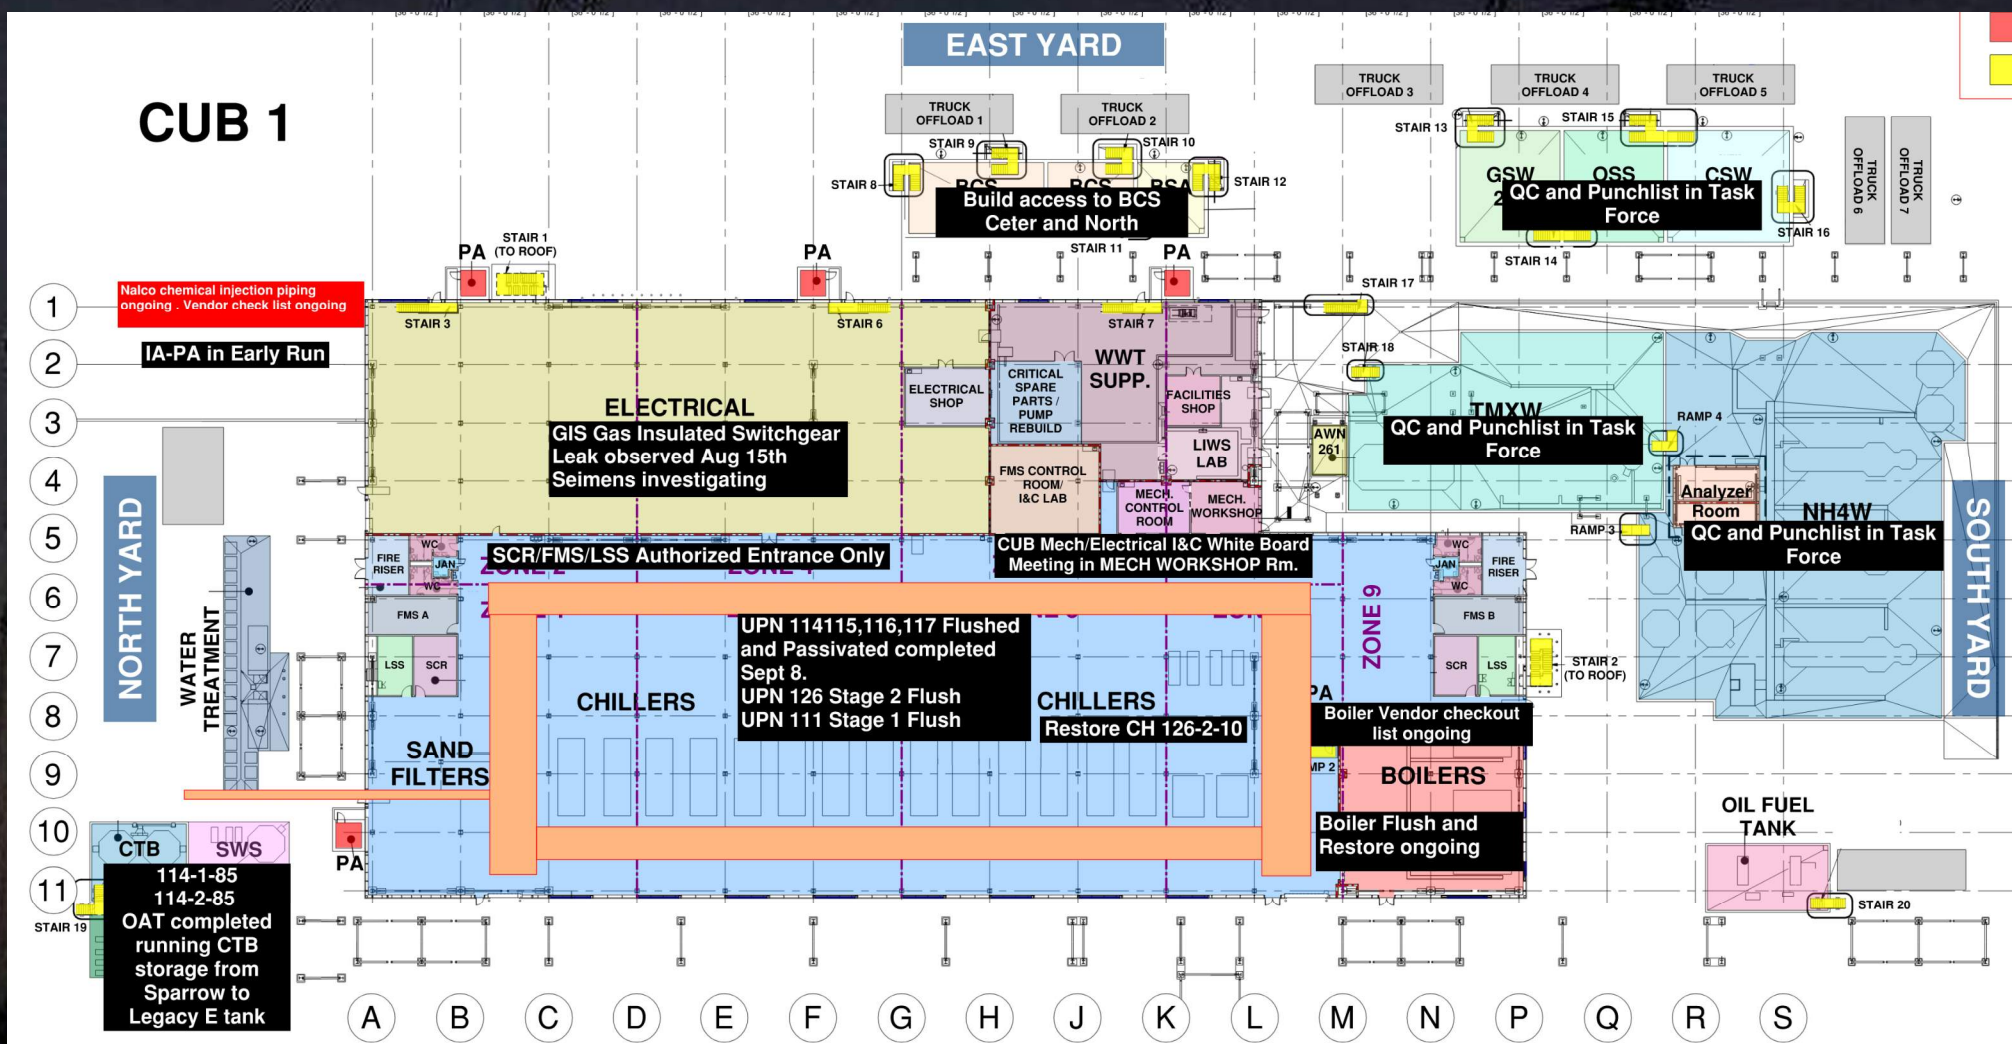



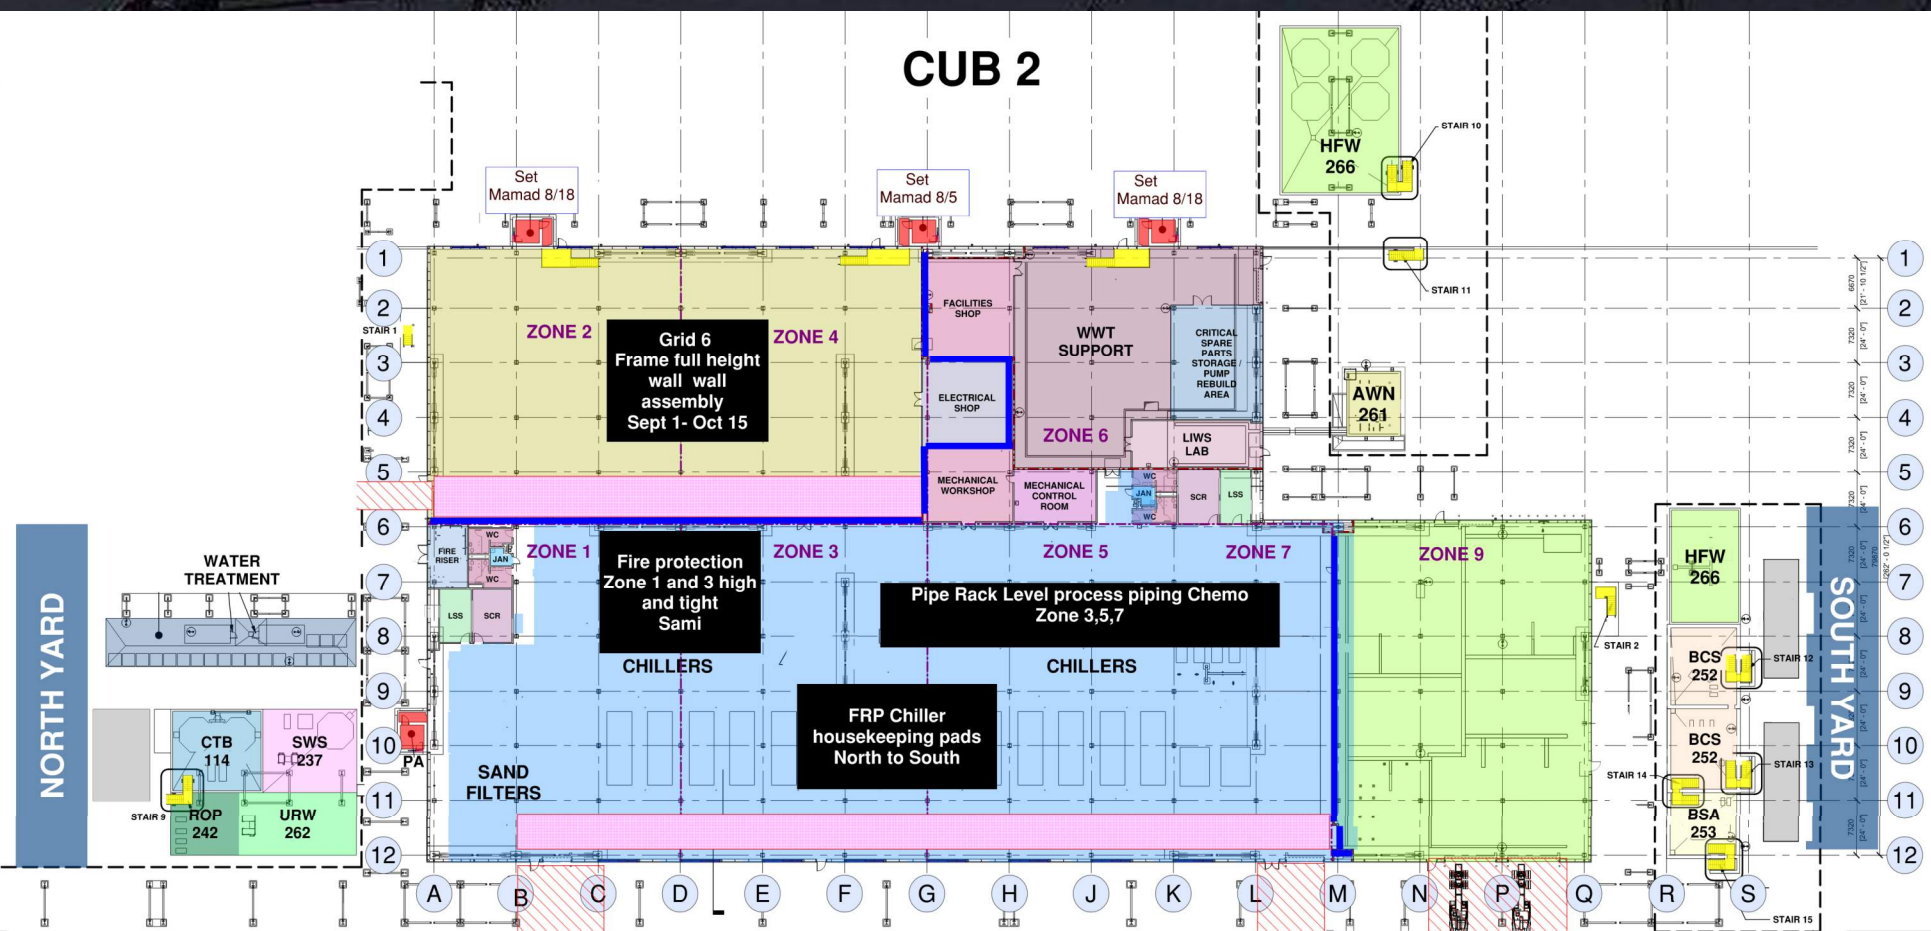

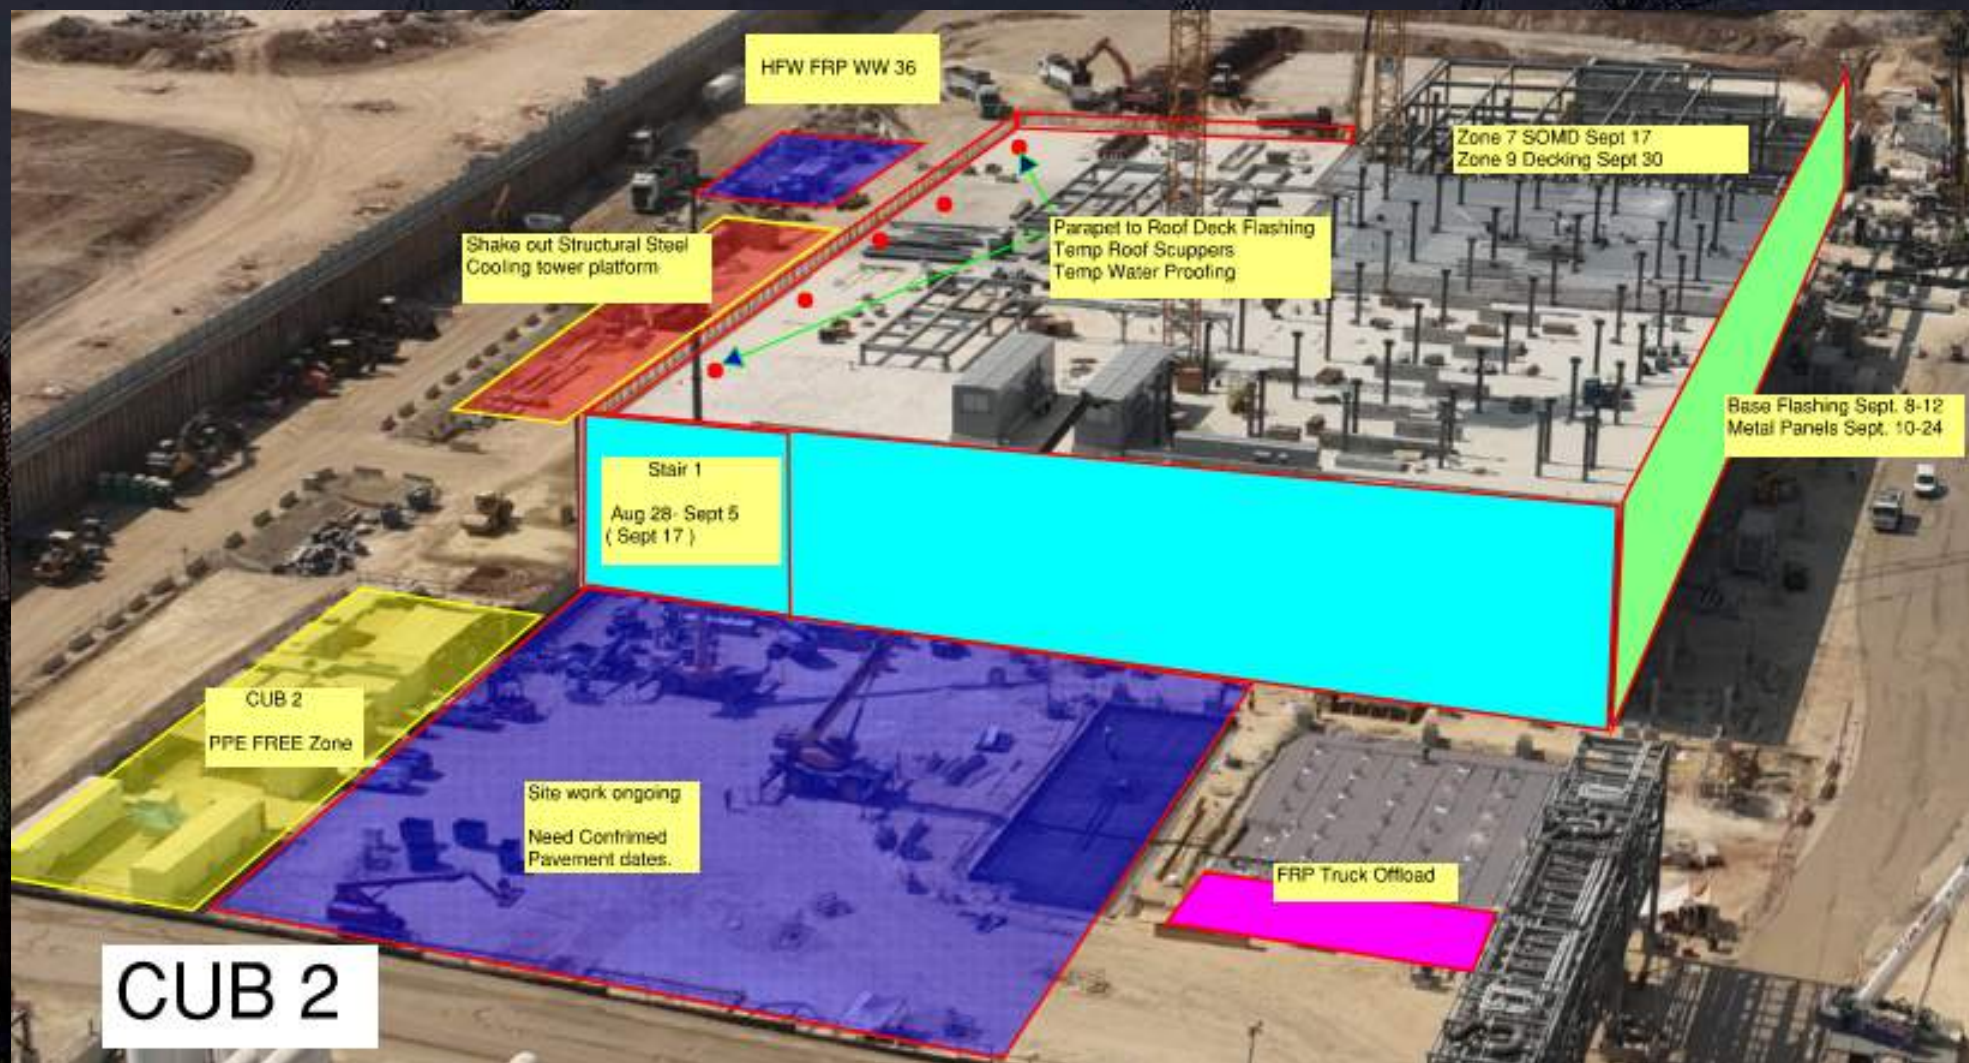

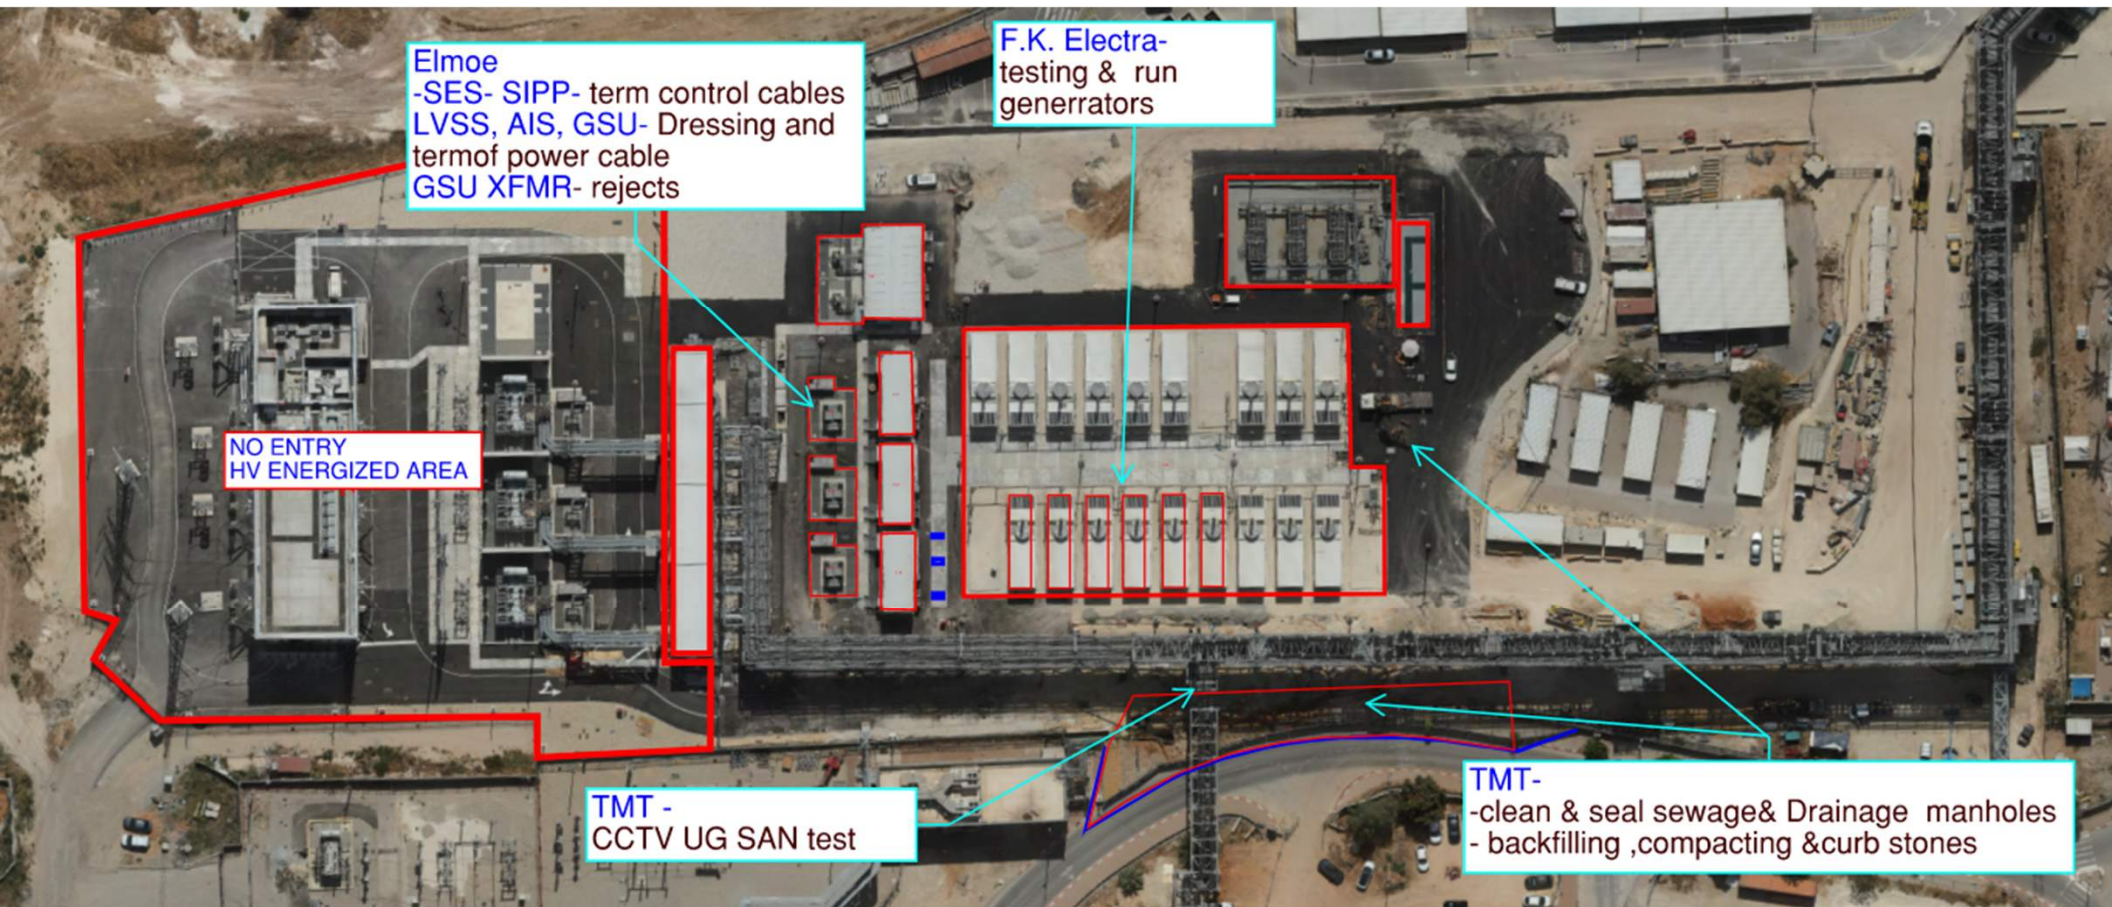


Elmoe
-SES- SIPP- term control cables
LVSS, AIS, GSU- Dressing and
termof power cable
GSU XFMR- rejects

NO ENTRY
HV ENERGIZED AREA


F.K. Electra-
testing & run
generators

TMT -
CCTV UG SAN test

TMT-
-clean & seal sewage& Drainage manholes
- backfilling ,compacting &curb stones



HOFFMAN CONSTRUCTION COMPANY

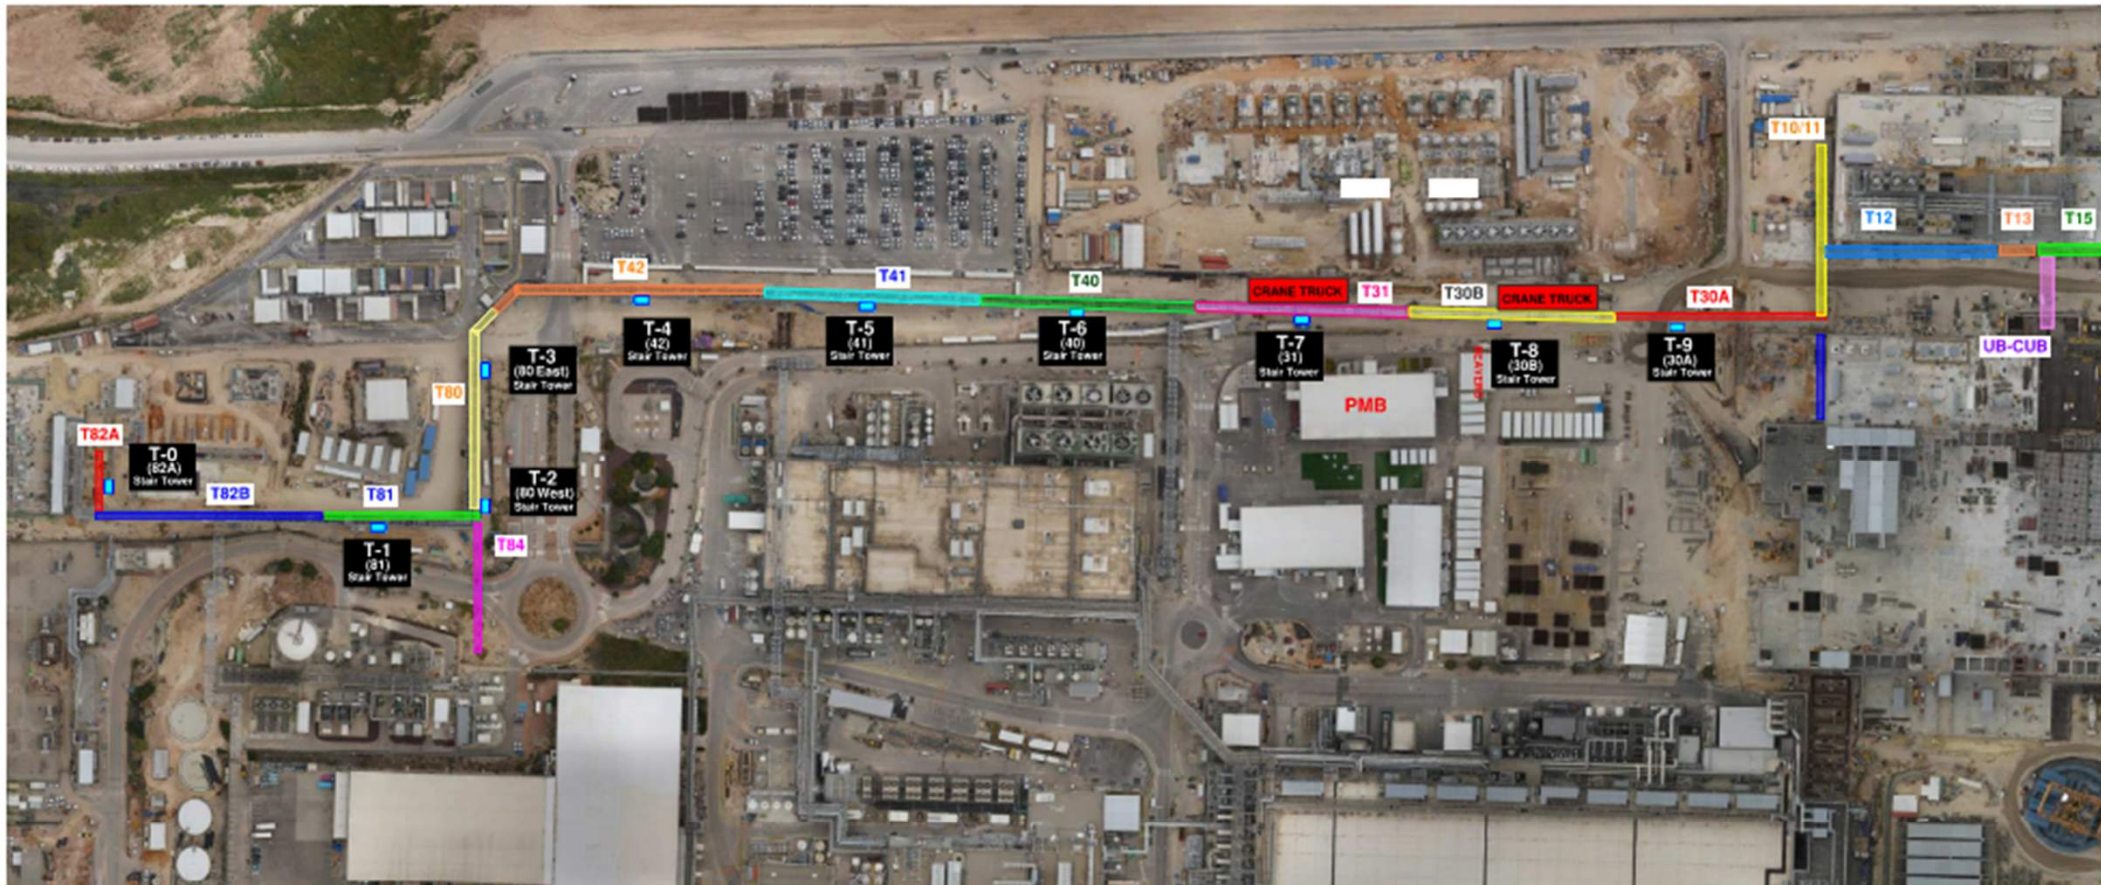



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Gate B






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

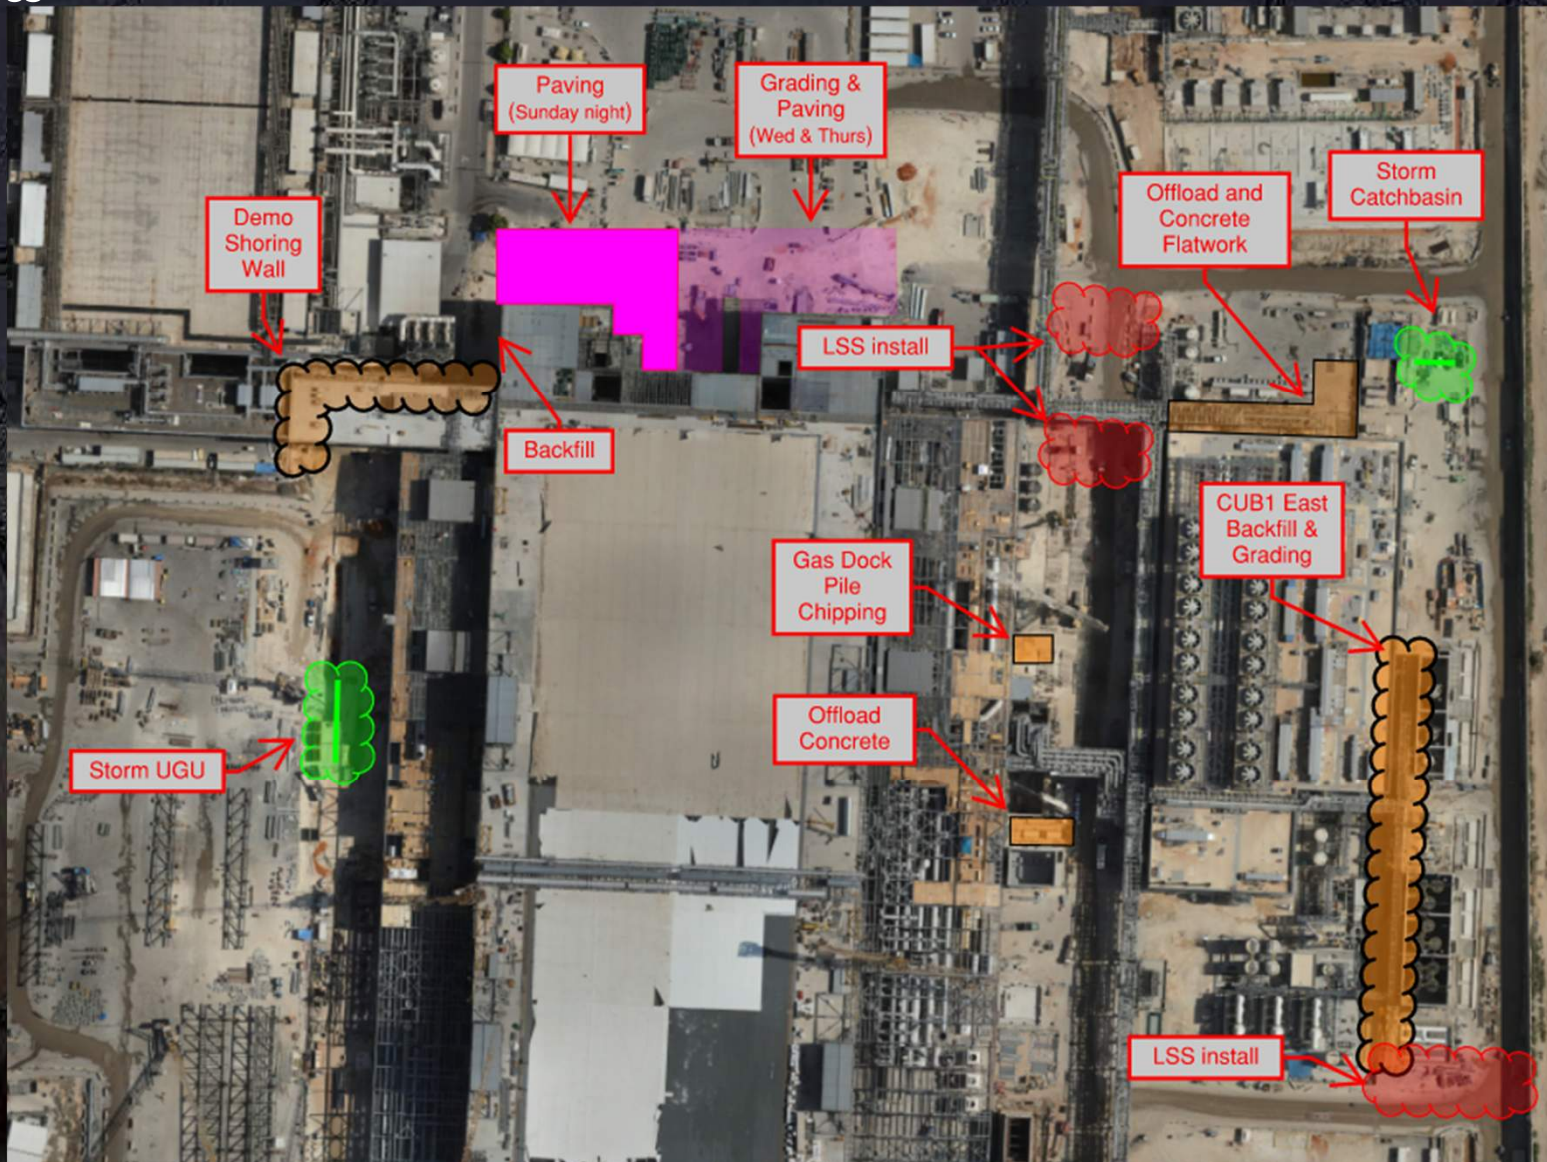



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

Cleanup: Subcontractor shall always keep the project free from the accumulation of waste materials caused by its employees, Subcontractor's employees, or Work on the project. Subcontractor shall continually and thoroughly cleanup and remove from jobsite, at its sole expense, all waste, debris, surplus equipment and surplus materials resulting from Subcontractor's operations. If Subcontractor fails to clean up such waste, debris, surplus materials and surplus equipment, such clean up and removal will be done by others and costs for this work will be deducted from the Subcontract by Contractor.

AREA IN ORANGE = NEY CLEANUP WHICH ALSO INCLUDES THE TRESTLE FRIDAY, 13-September-2024

***BACKCHARGES WILL BE SENT TO AFFECTED SUBCONTRACTORS, COST FOR EMPTY PALLETS AND WOOD WILL BE DIVIDED AMONG ALL SUBCONTRACTORS IN THE AREA.**

***ROPE AROUND MATERIAL DOES NOT MAKE IT ACCEPTABLE TO STORE ITEMS FOR MORE THAN 3 DAYS**

TRESTLE

NEY

Job Services

Work Week 38

- ▶ Deep cleaning tent C2
- ▶ Flyable bathrooms


Deep cleaning on Friday 20th September – tent C2

C1


C2



Deep cleaning on Friday 20th September – tent C2

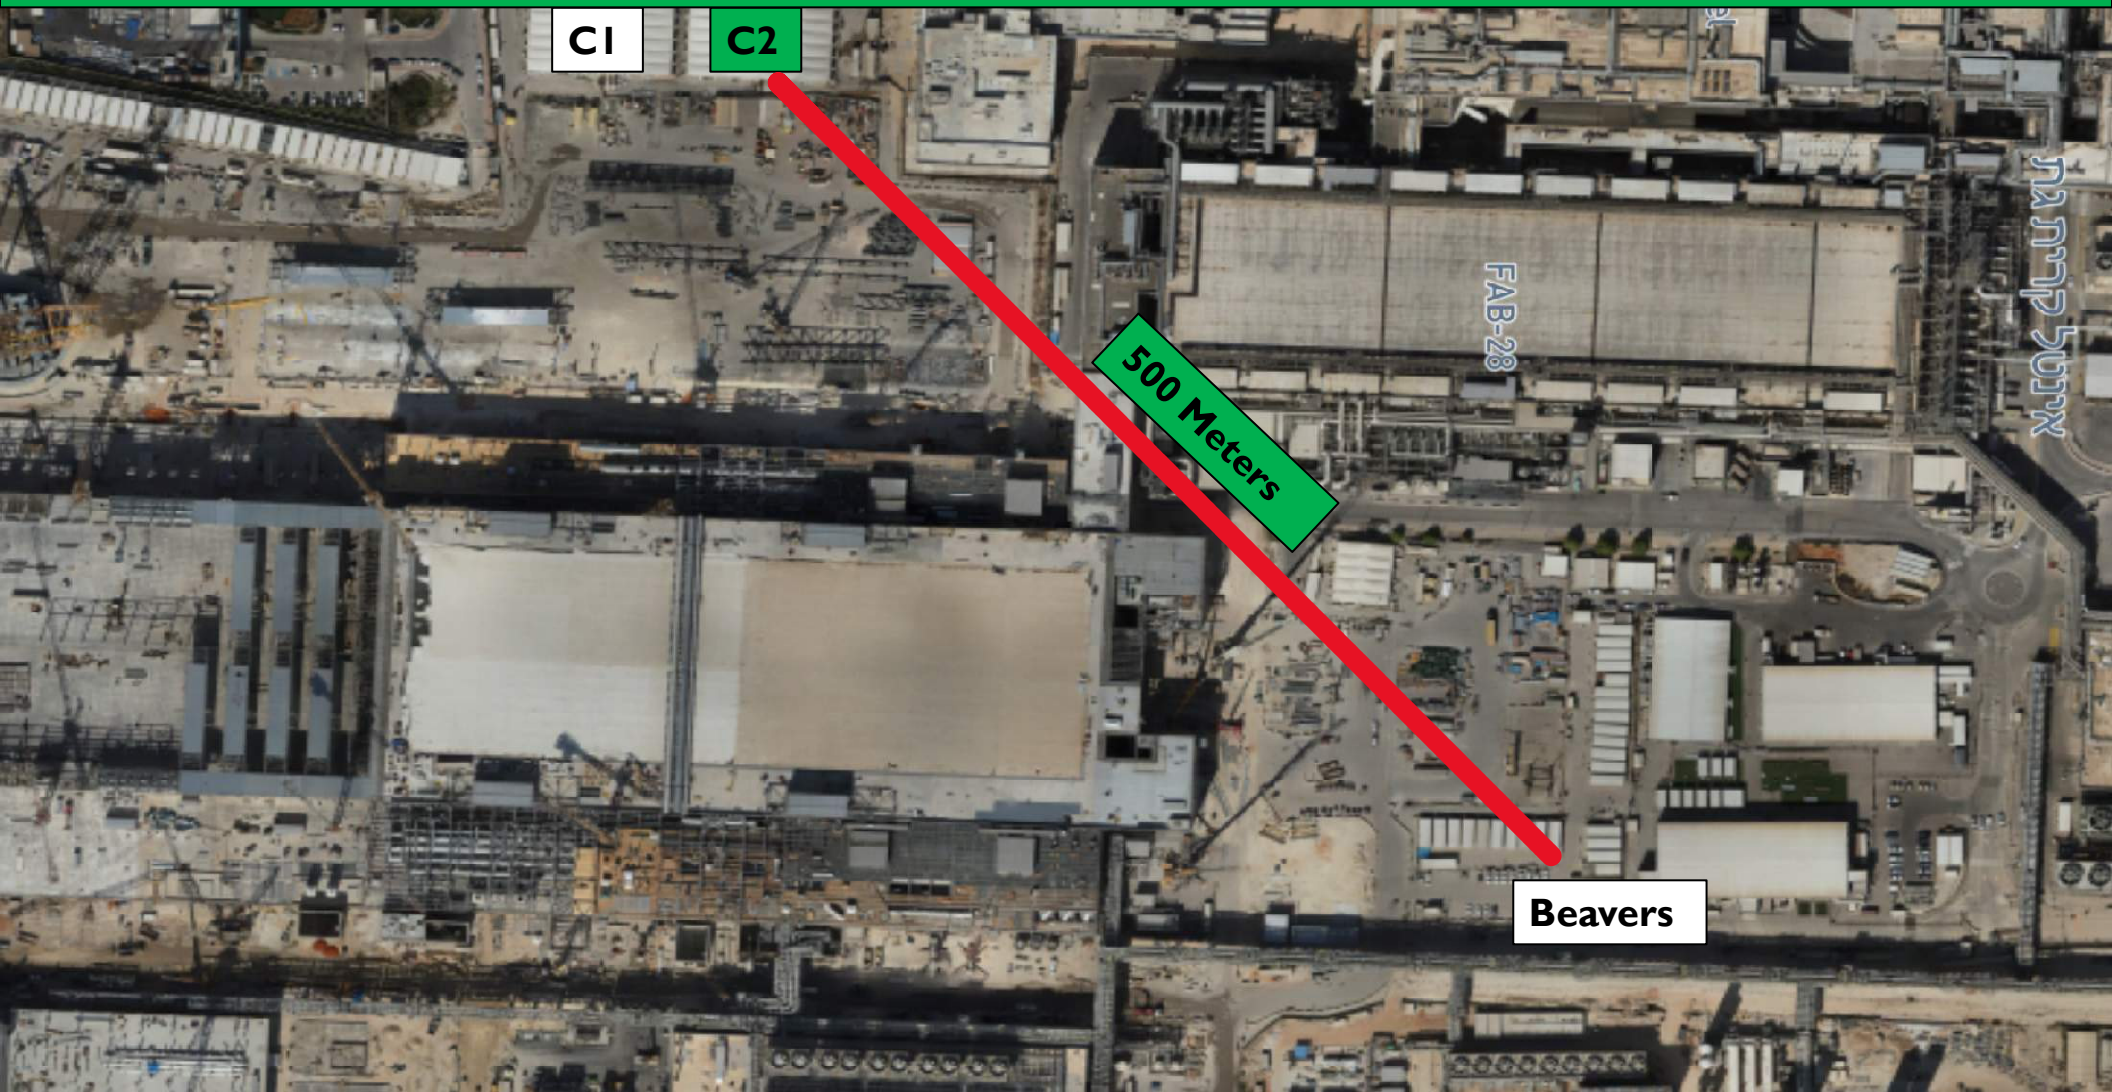

Flyable bathrooms

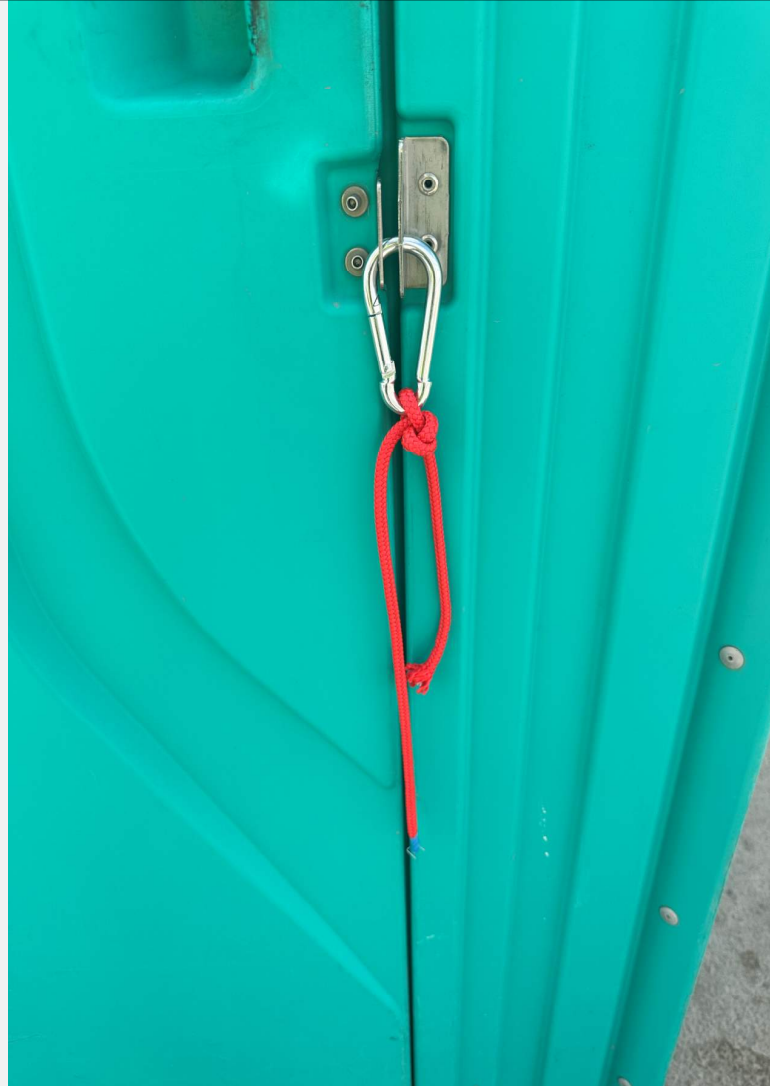





Open CORs by Subcontractor

WW 37 – 504 CORs

WW 38 – 553 CORs

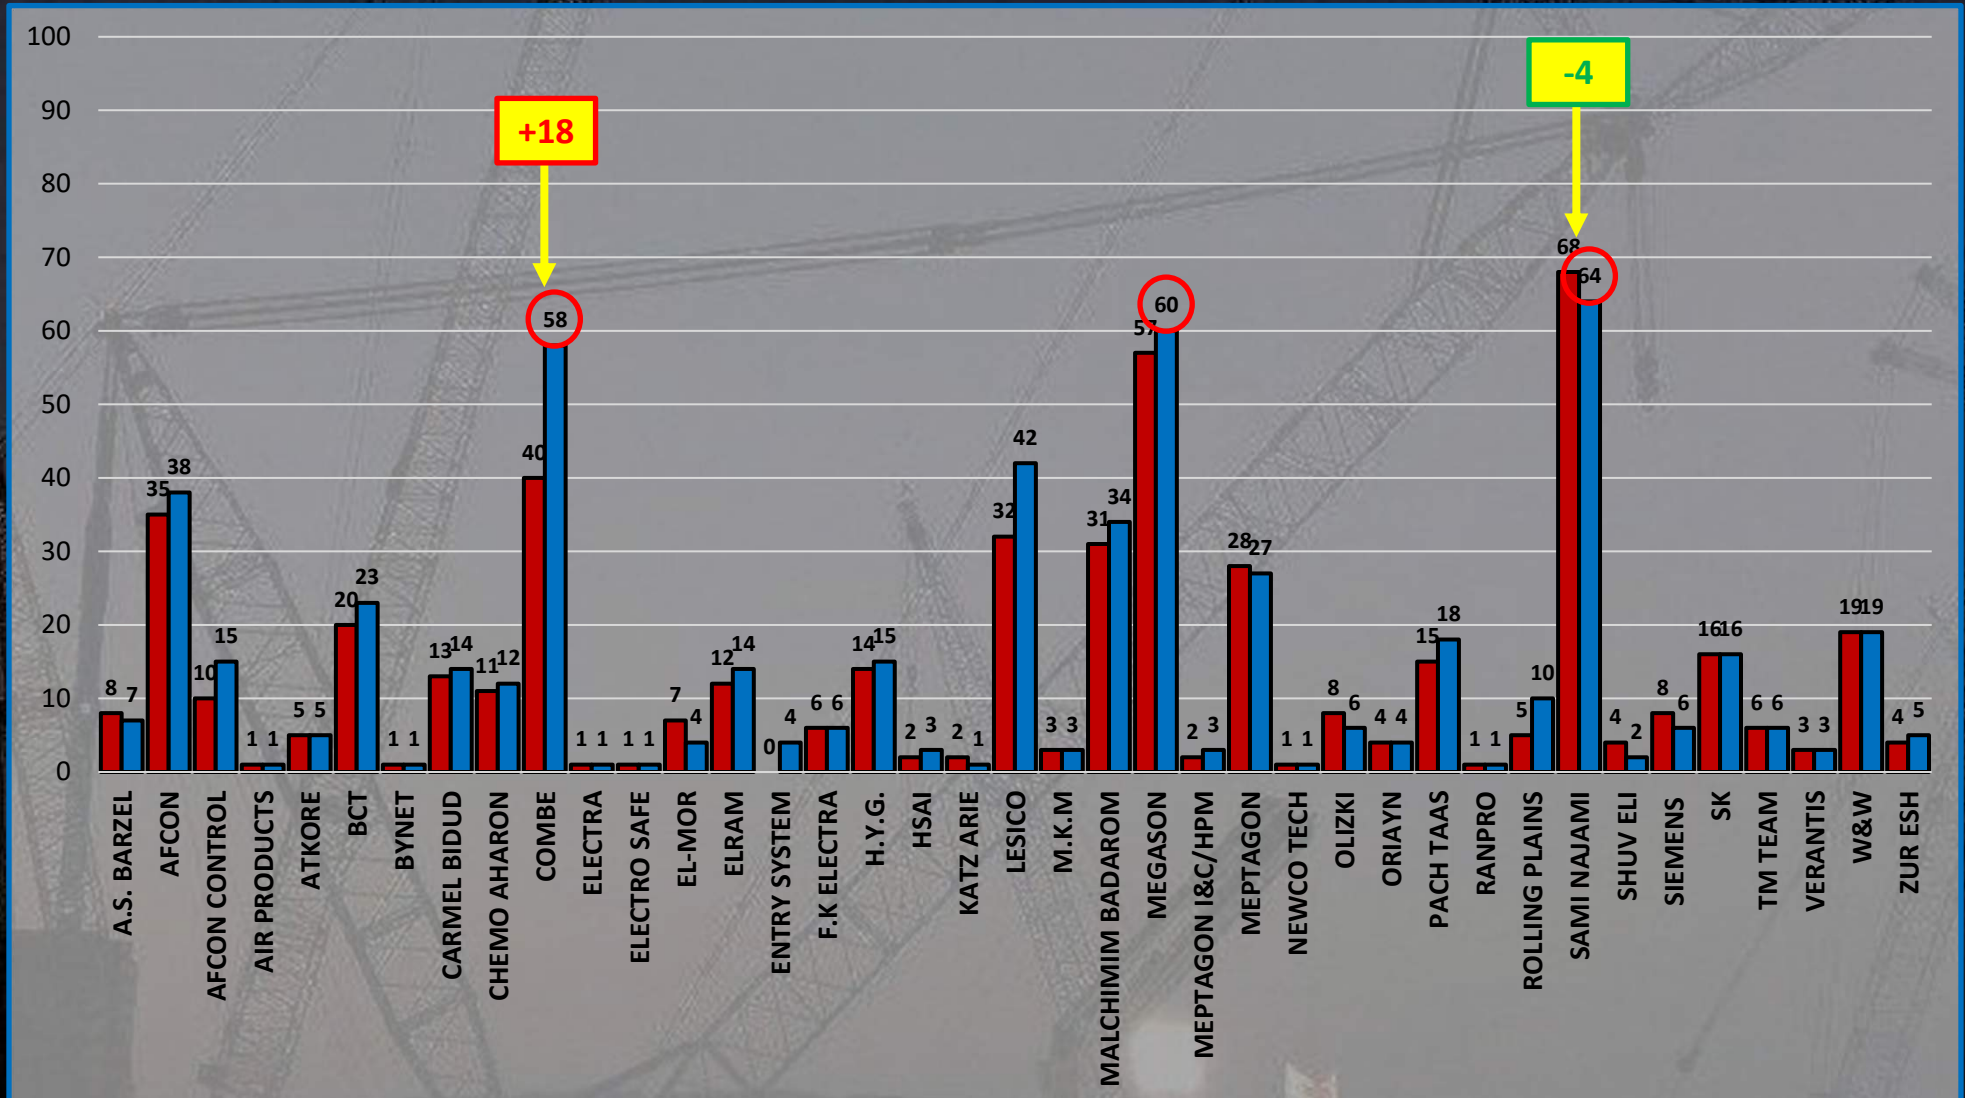



Overdue CORs by Subcontractor

WW 37 – 168 Overdue CORs

WW 38 – 148 Overdue CORs



Electrical Inspections- Get Ready

- New quarter is about to begin.
- Make sure that your company is ready to get all electrical inspections done.
- These are required and the equipment must be marked that it has been inspected.
- This includes power tools and extension cords, welding leads, etc.
- Recommend that you start doing cord roll ups so that the cords can be properly inspected (this is supposed to be done each Thursday).

Heat Index- September 17th

	temperature (°F)															
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
45	80	82	84	86	89	93	96	100	104	109	114	119	124	130	137	
50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
55	81	84	86	89	93	97	101	106	112	117	124	130	137			
60	82	84	88	91	95	100	105	110	116	123	129	137				
65	82	85	89	93	98	103	108	114	121	128	136					
70	83	86	90	95	100	105	112	119	126	134						
75	84	88	92	97	103	109	116	124	132							
80	84	89	94	100	106	113	121	129								
85	85	90	96	102	110	117	126	135								
90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127										
100	87	95	103	112	121	132										

 Caution
 Extreme Caution
 Danger
 Extreme Danger

Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures

Daily Coordination Meeting



14:00 Sign In
