

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:


- Trestle Testing – Be out of PMB parking lot by 19:00 today.
- Safety Award – Water Bottles – Get your dailies updated, will be distributed next week.



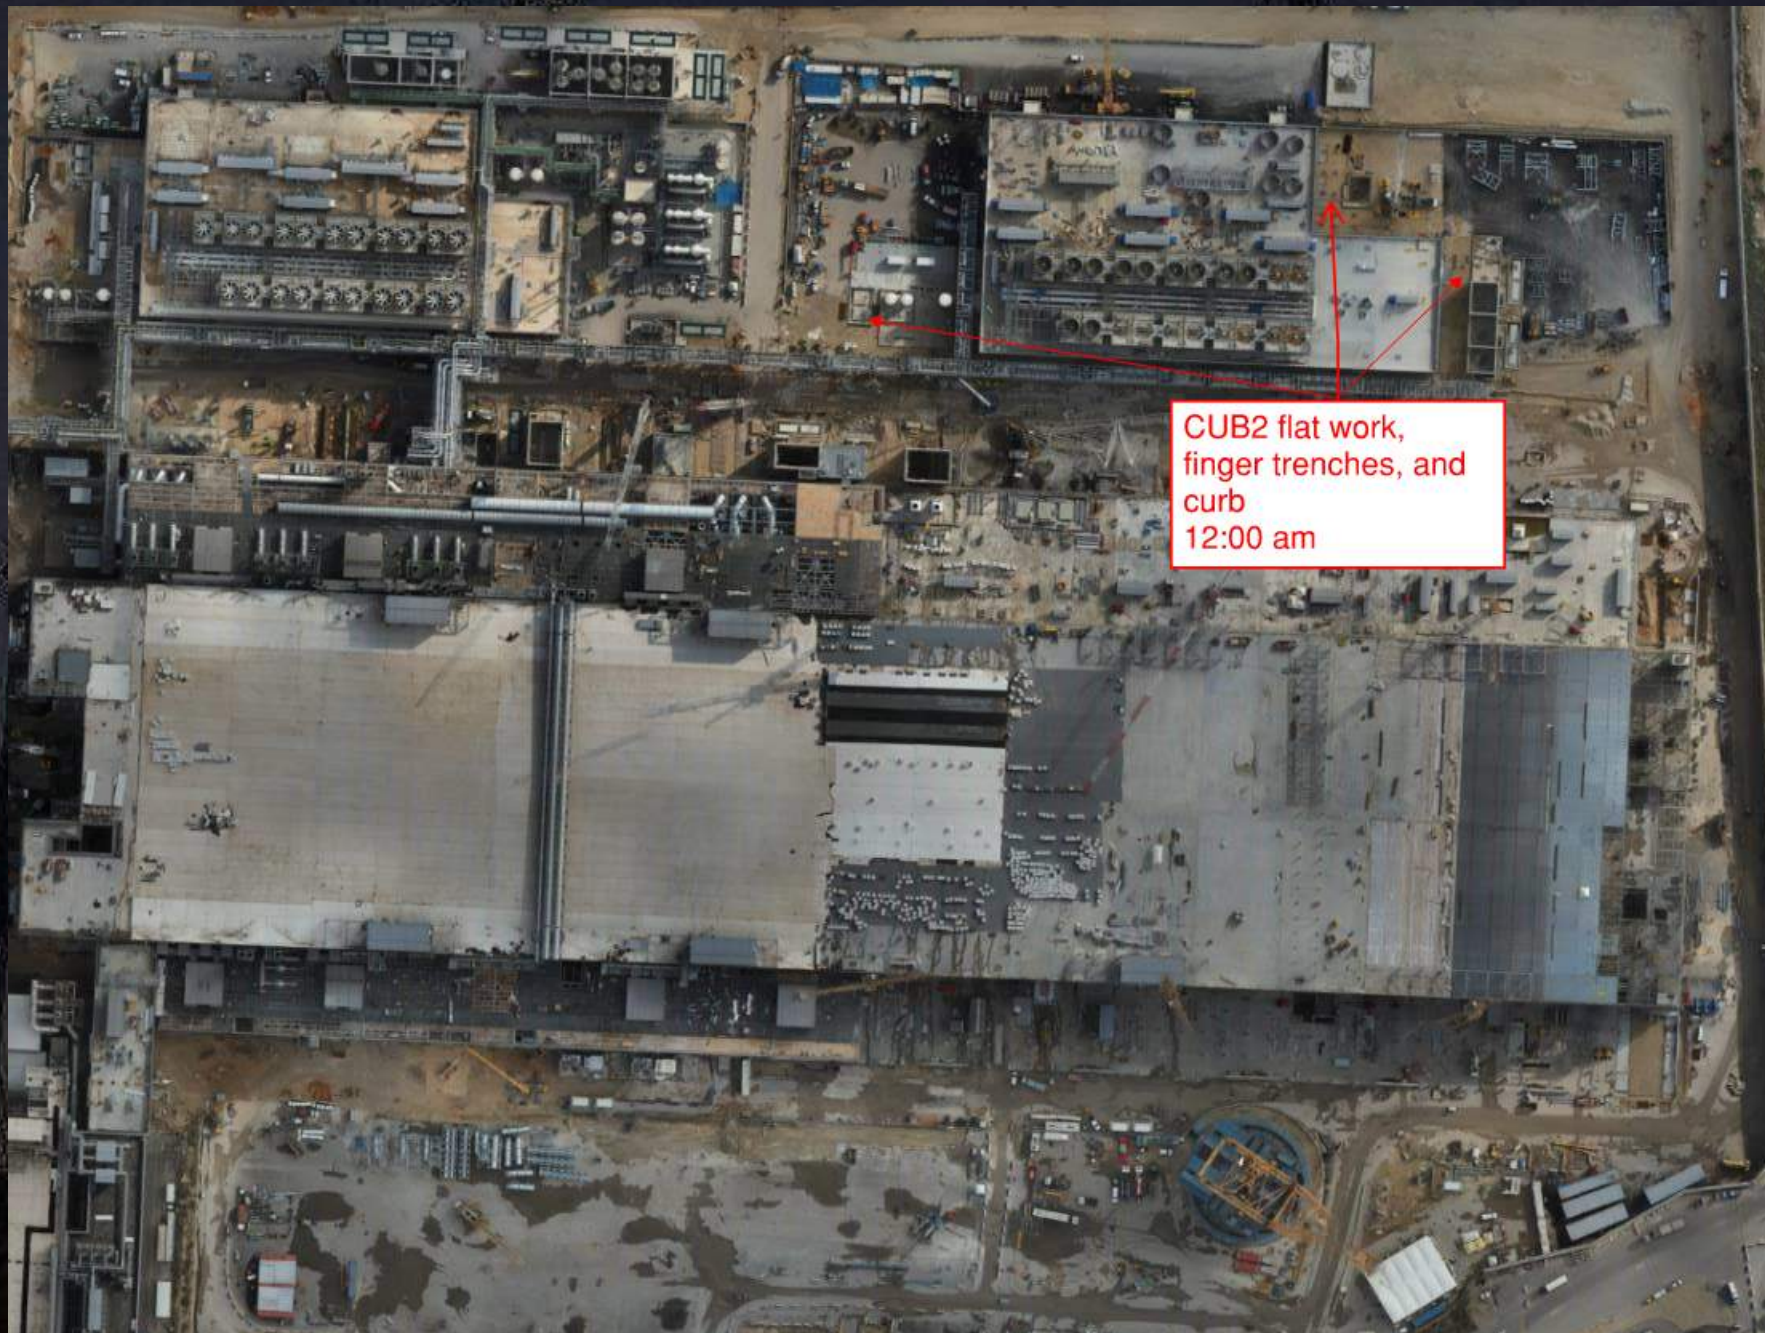

CUB2 flat work,
finger trenches, and
curb
12:00 am


UTILITY LEVEL MOD1

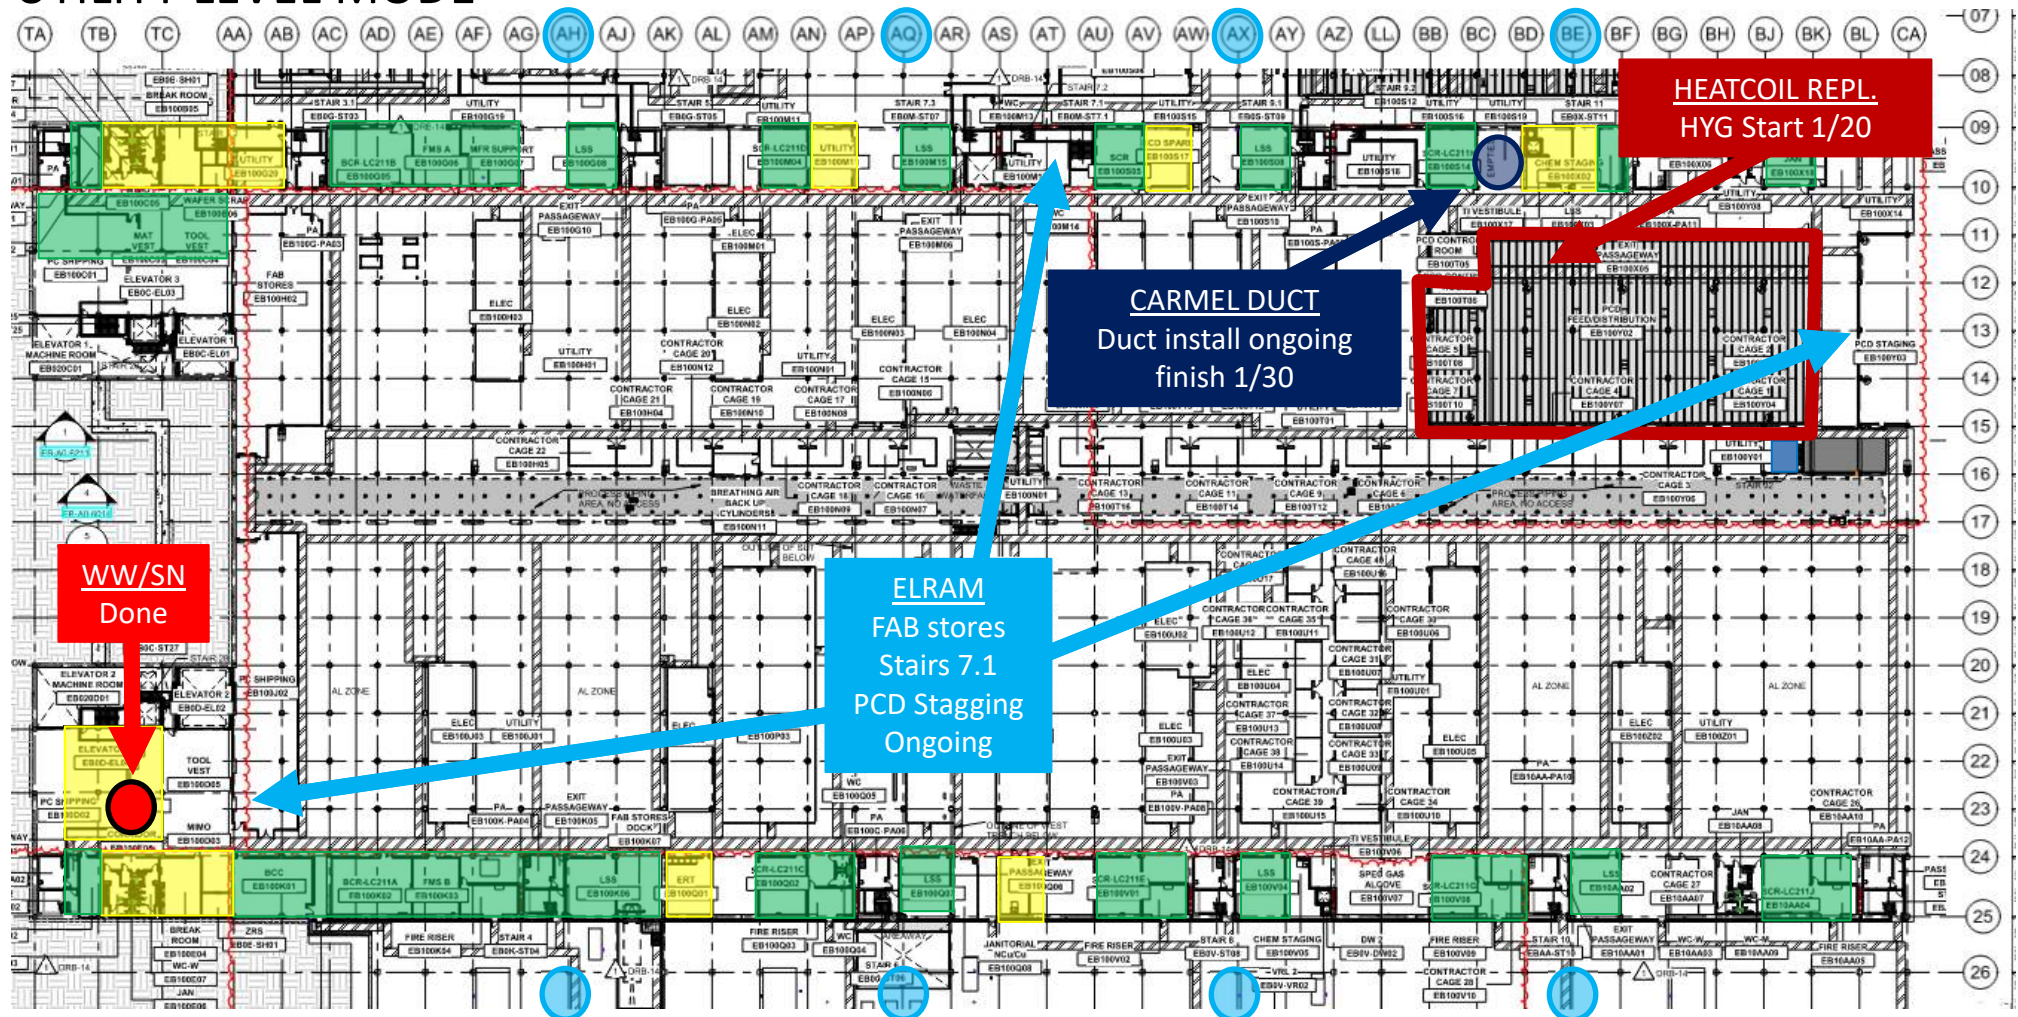


ELRAM
Drywall install

MEP+Elctrical
Ready for re-install

UTILITY LEVEL MOD2

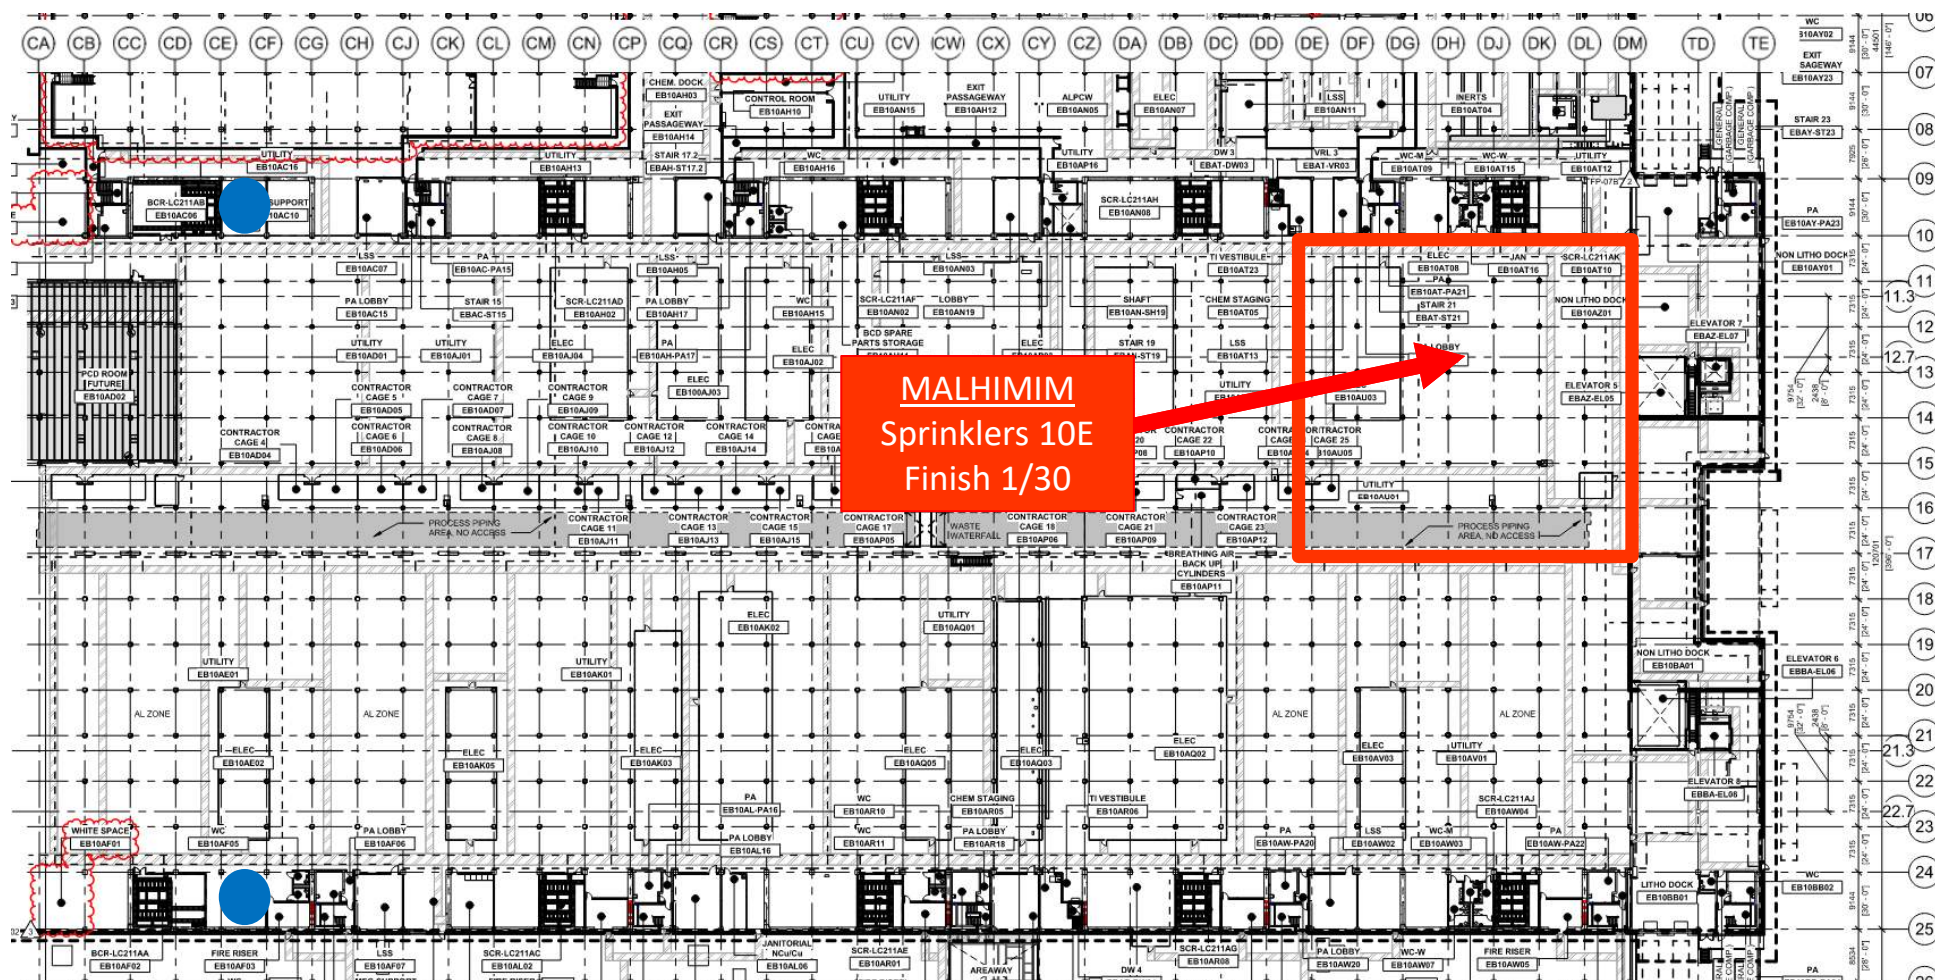


SUT 38.1 Accesses& Egress

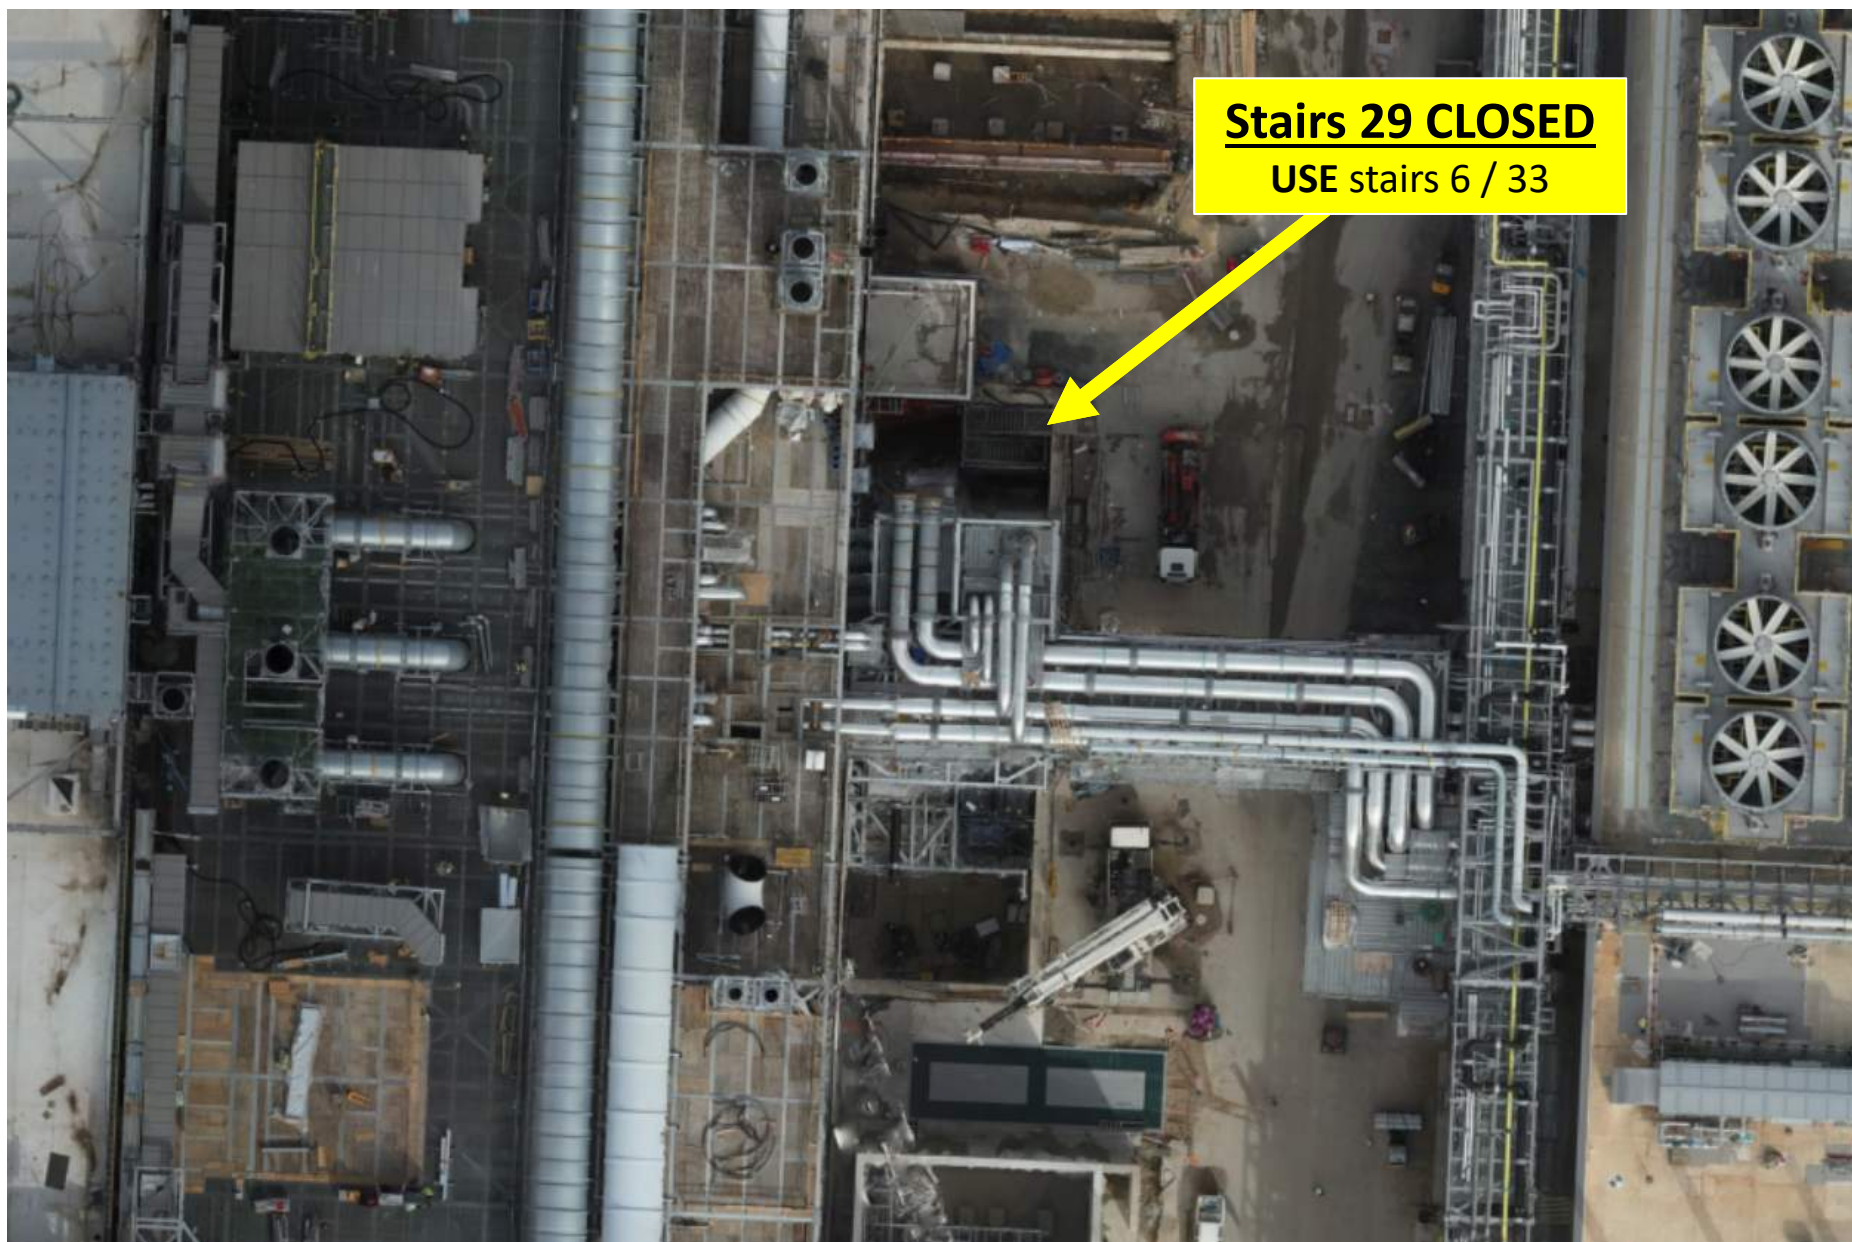

SUT 38.1 LEVEL

Stairs 29 CLOSED

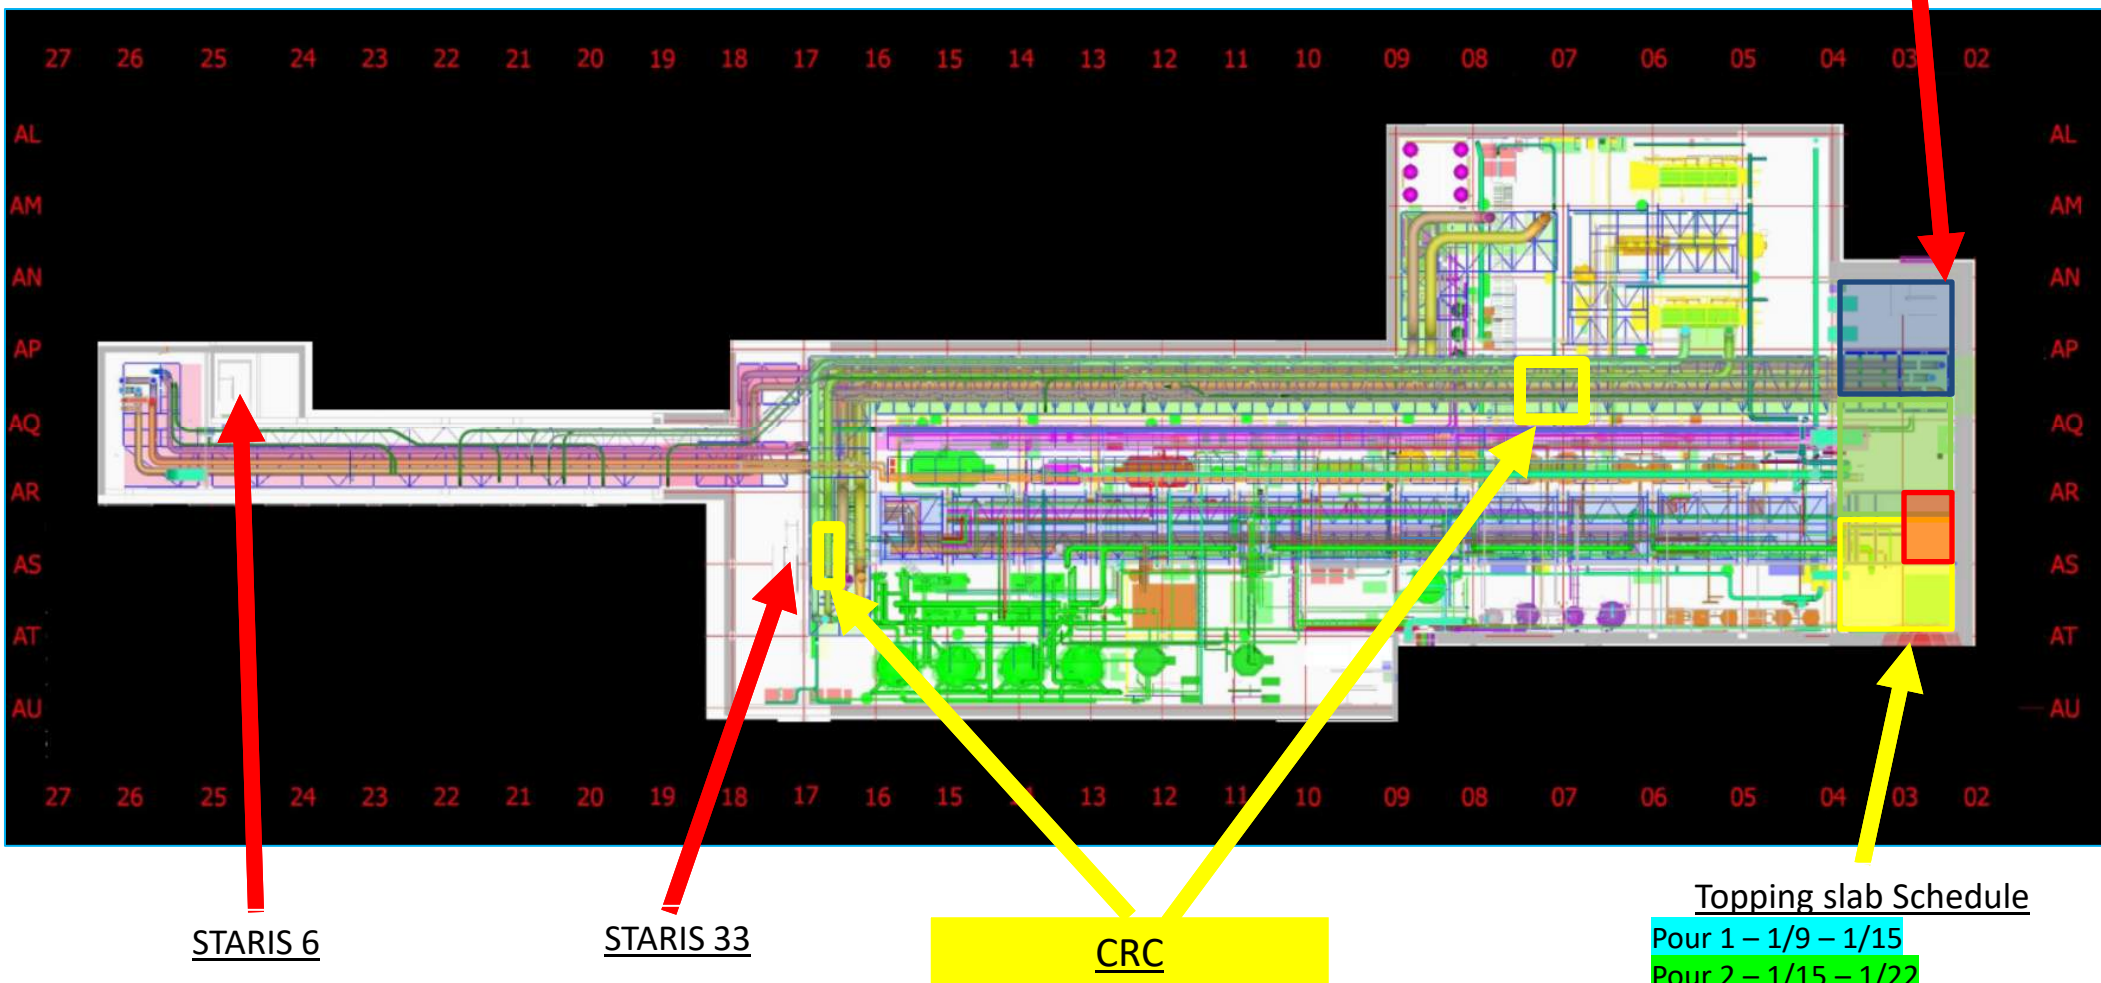


Topping slab Schedule

- Pour 1 – 1/9 – 1/15
- Pour 2 – 1/15 – 1/22
- Pour 3 – 1/22-1/27
- Pour 4 – 1/28-2/4




SUT 38.2 LEVEL

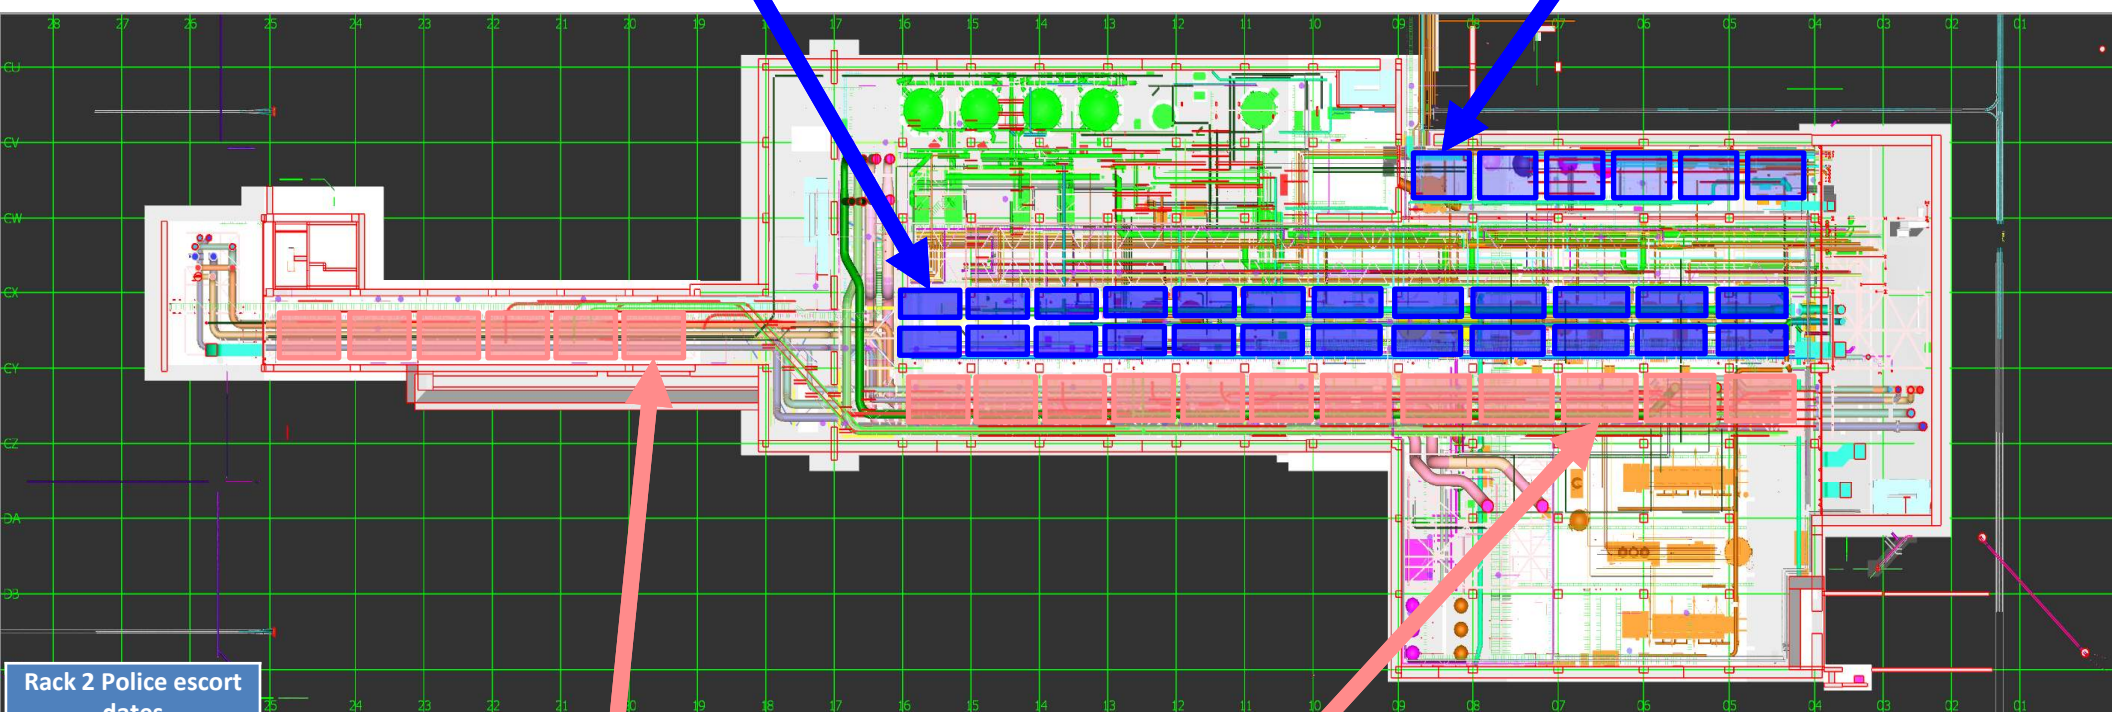


Rack6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25


SUBFAB BUILDOUT MOD 1

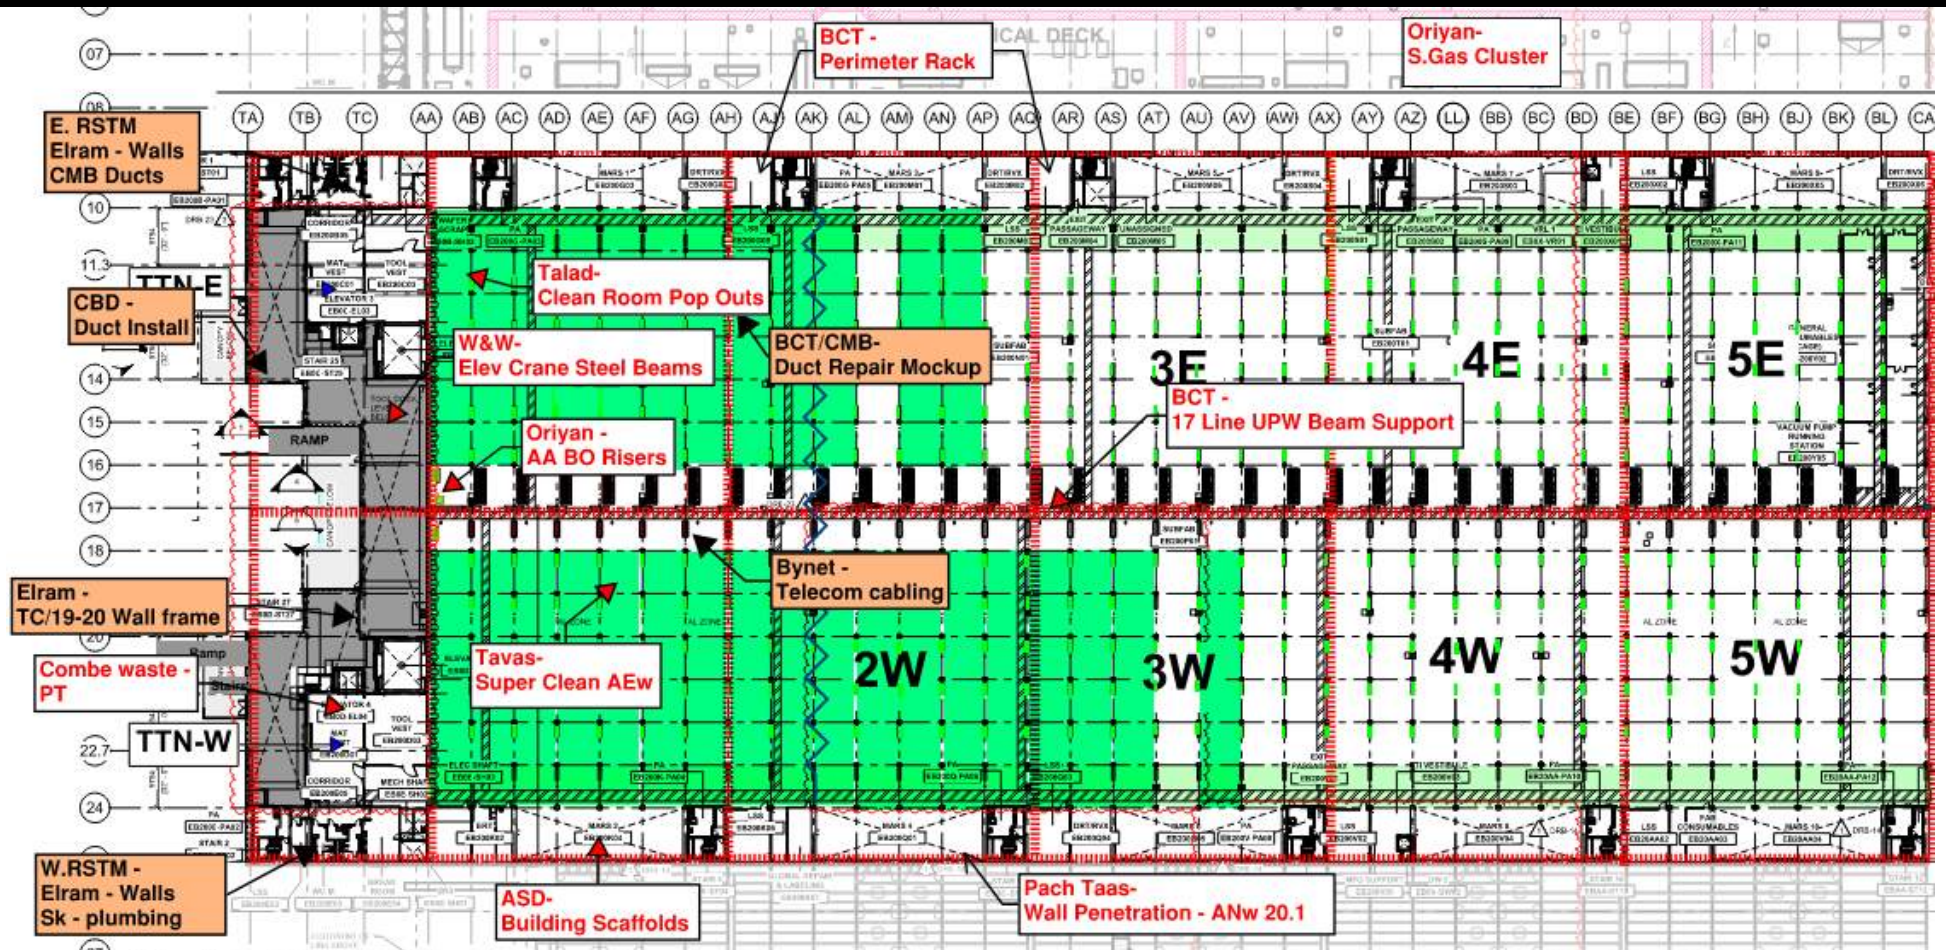


SUBFAB CRC TOPCOAT

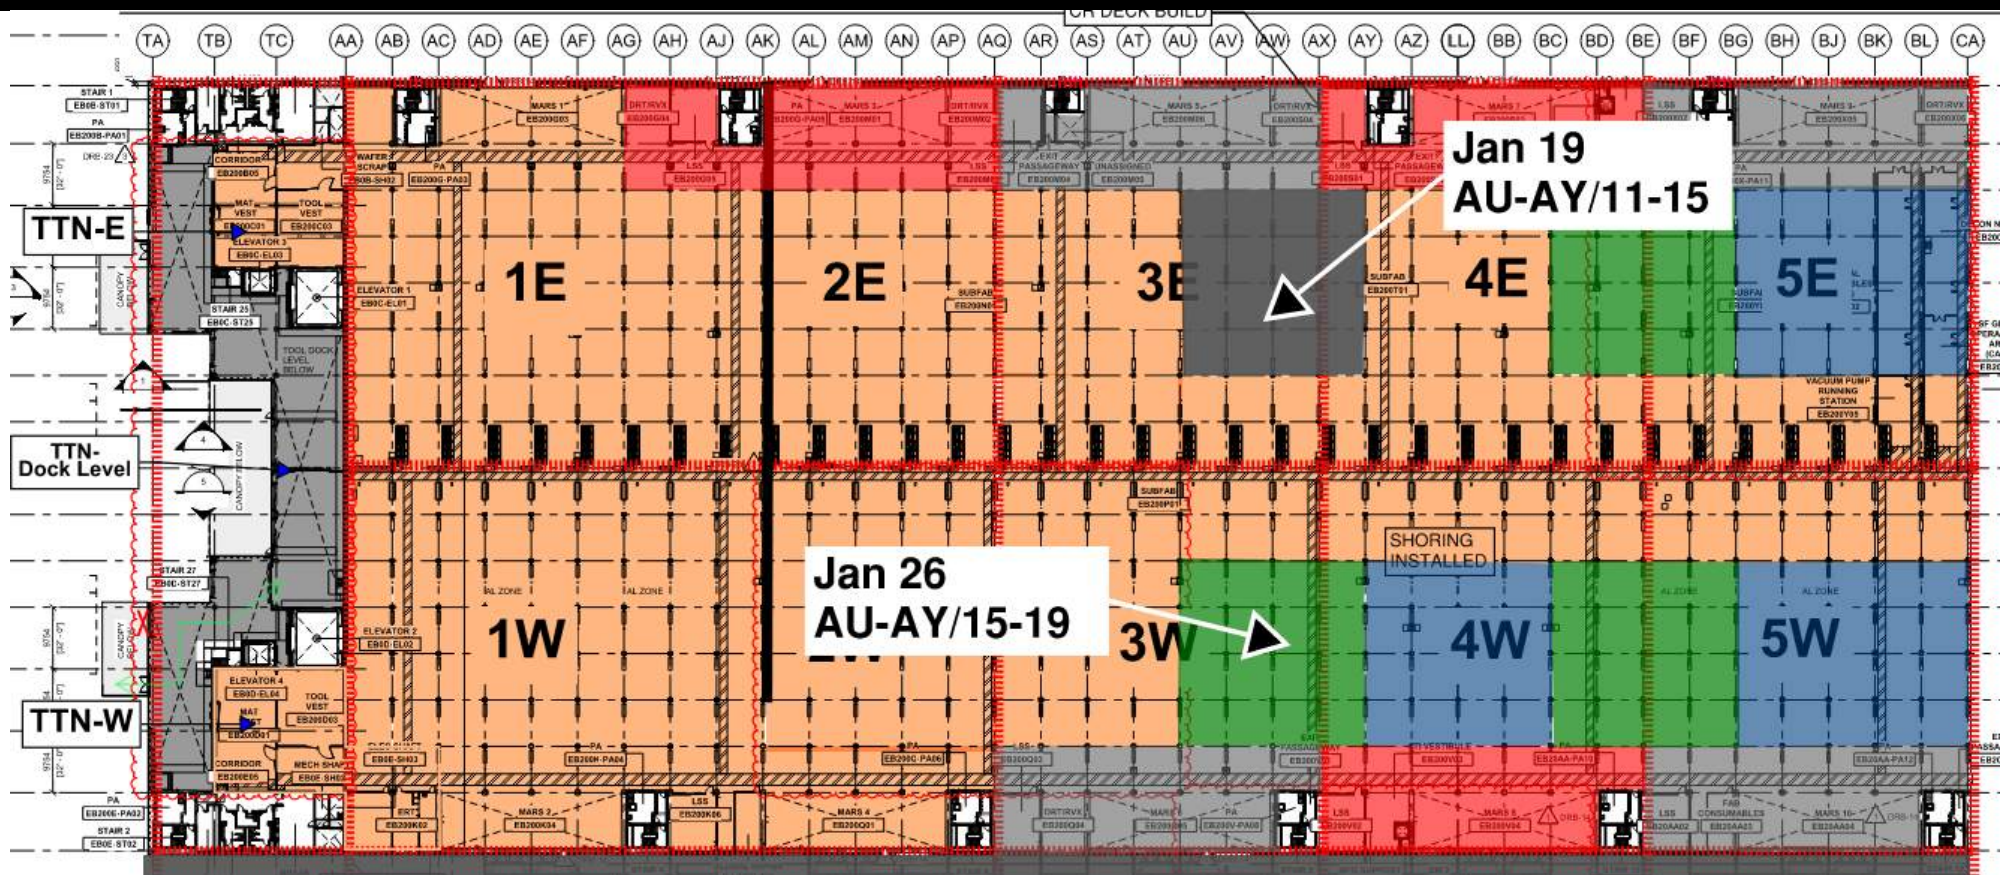


BCT Pressure Test Today

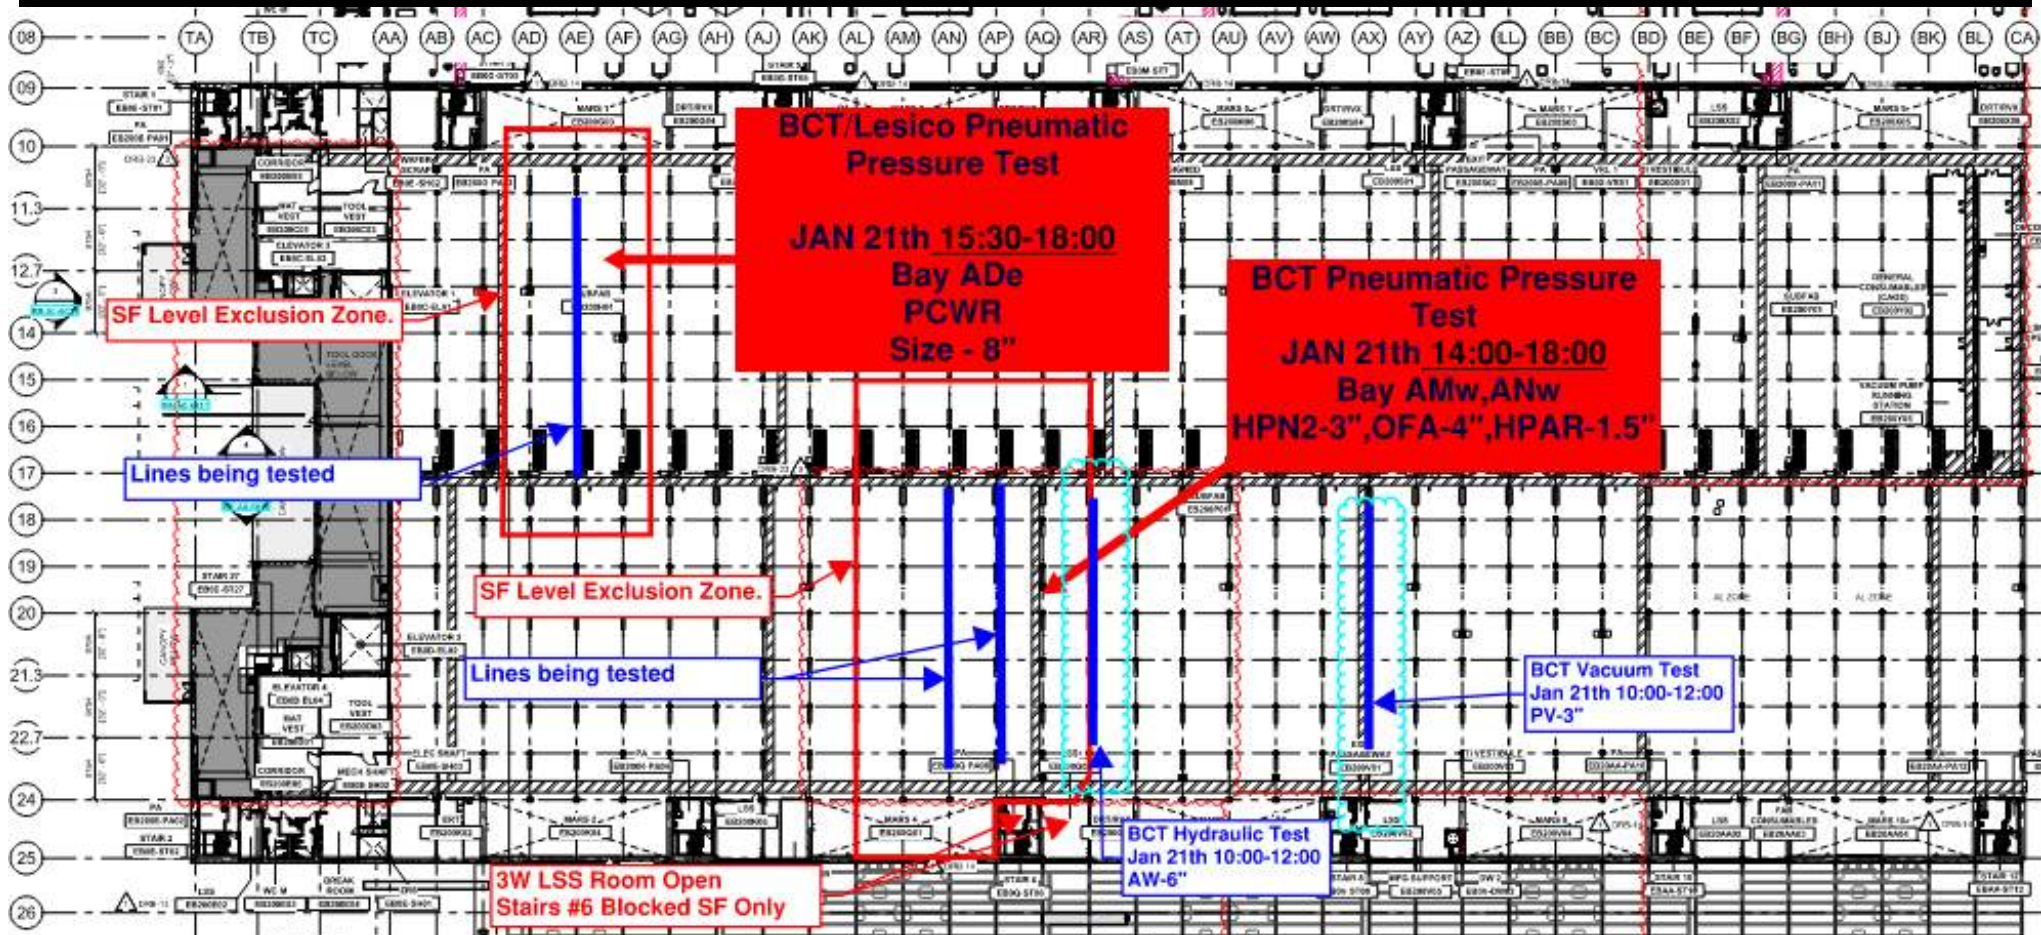



BCT Pressure Test Tomorrow

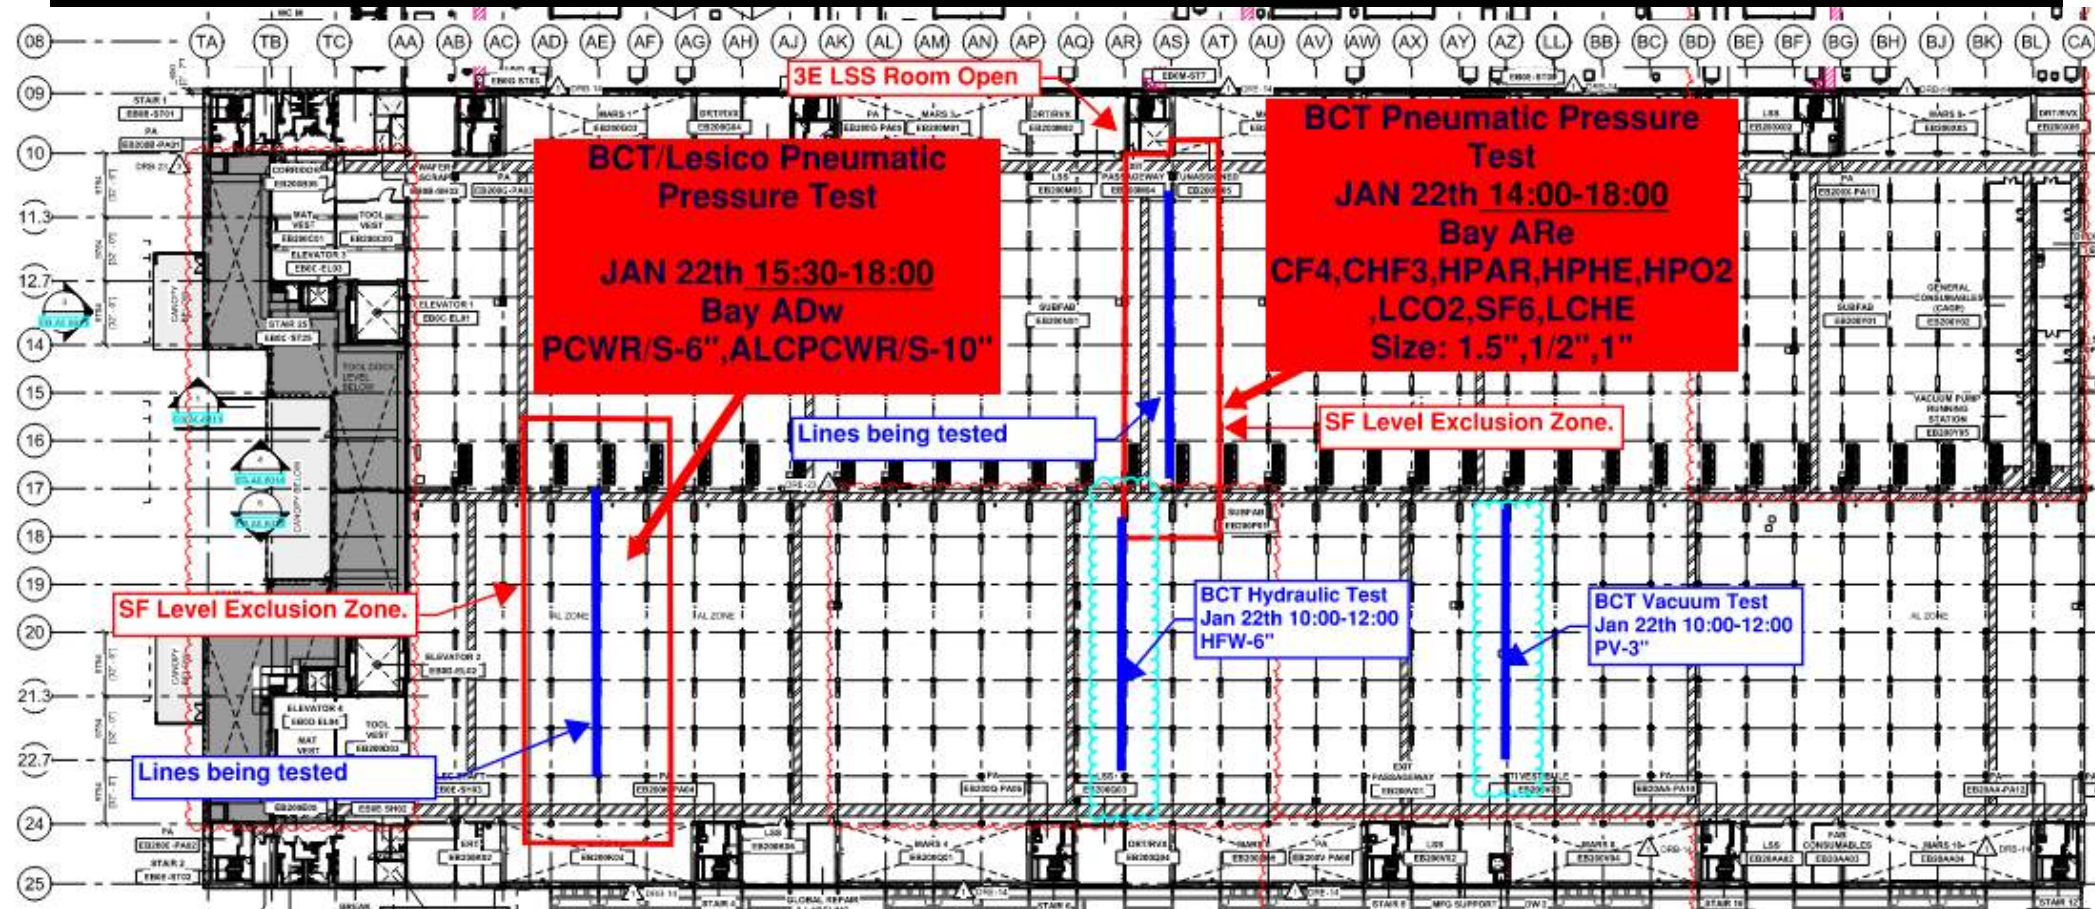


SUBFAB BUILDOUT MOD 2

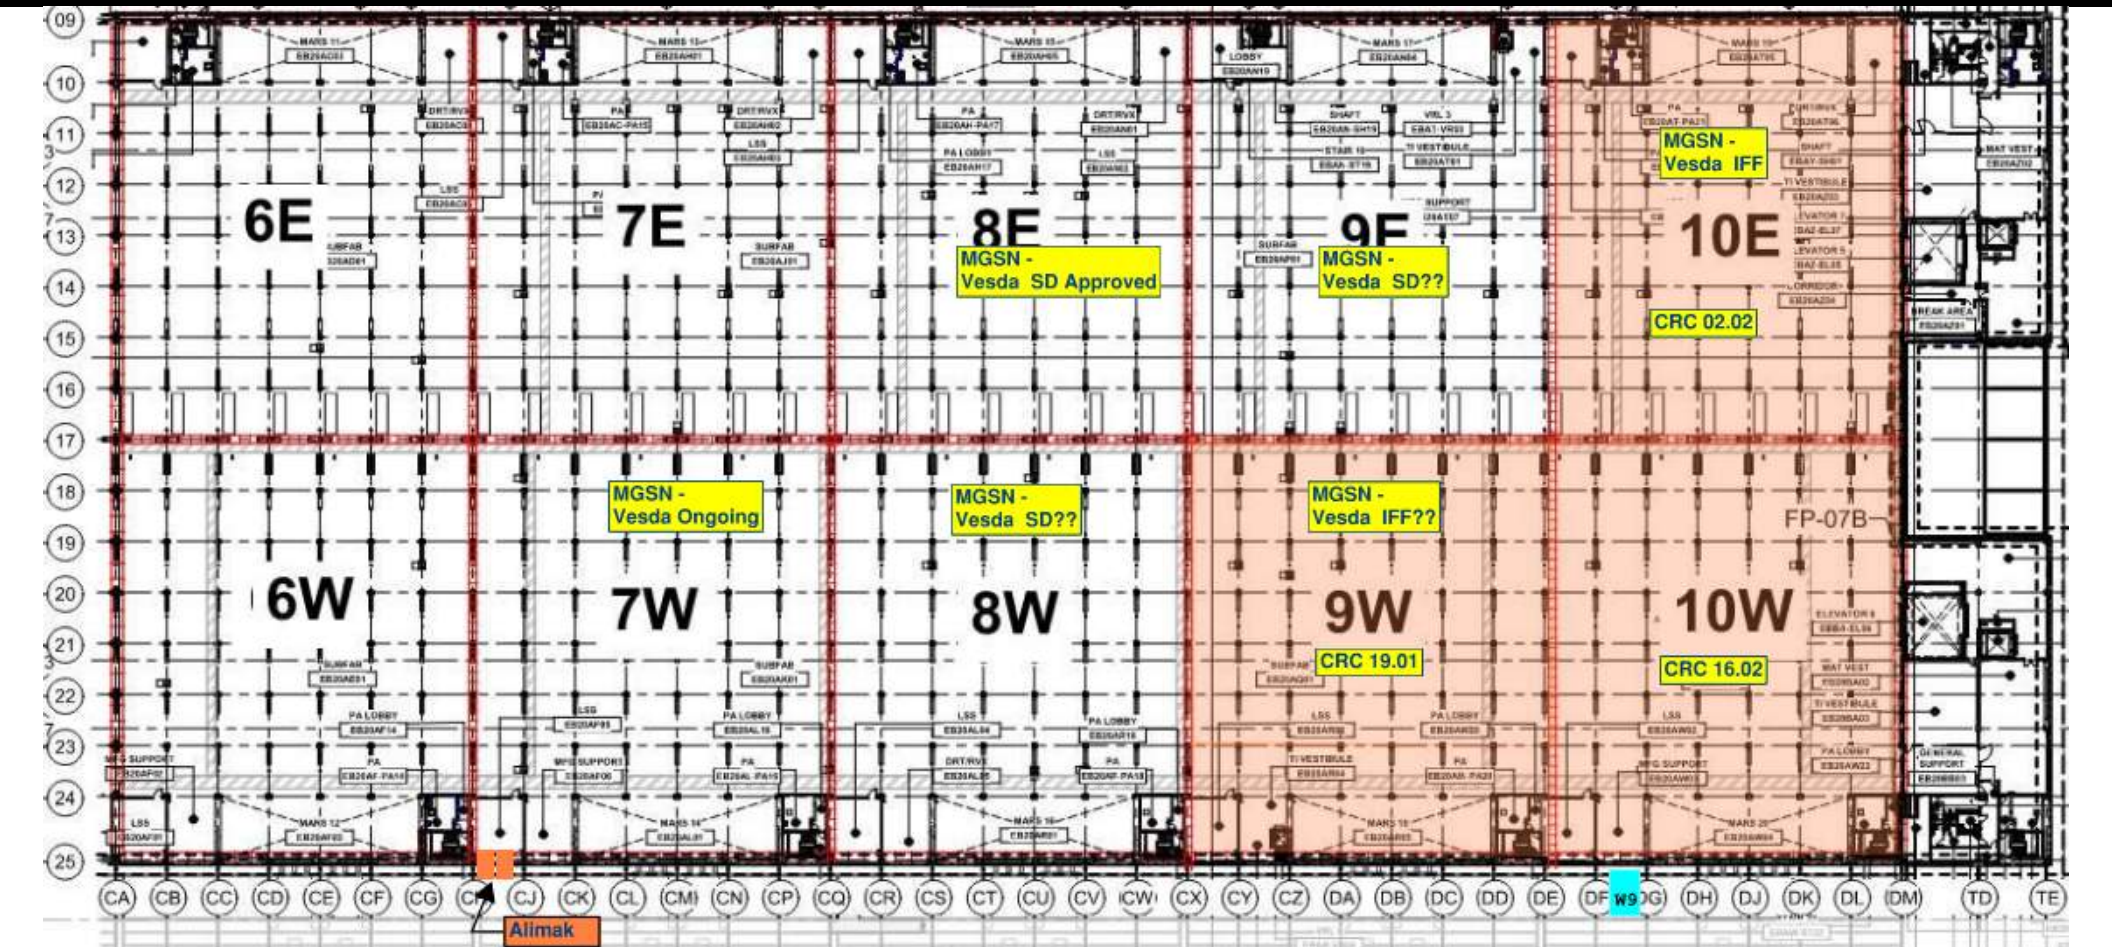

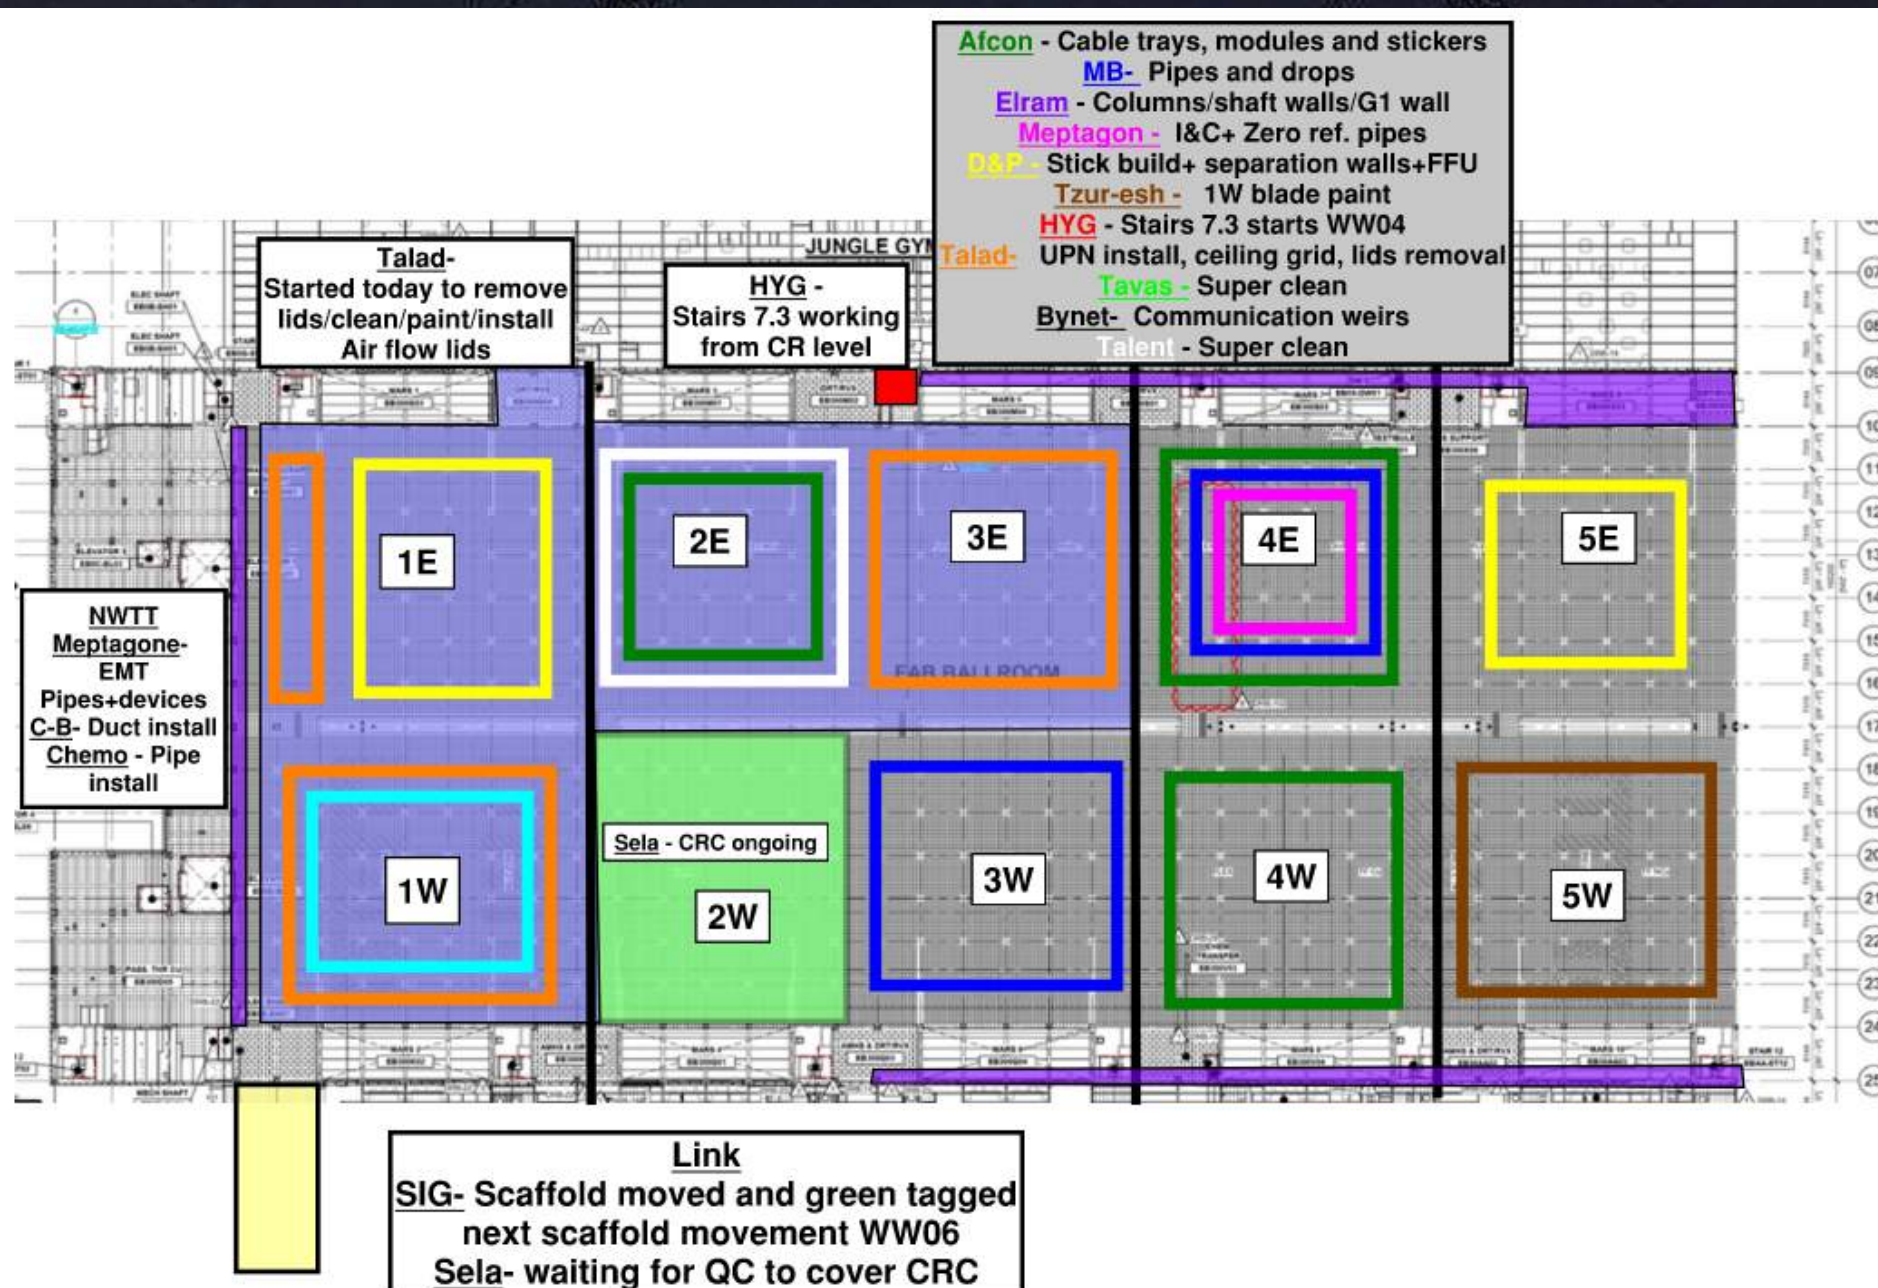

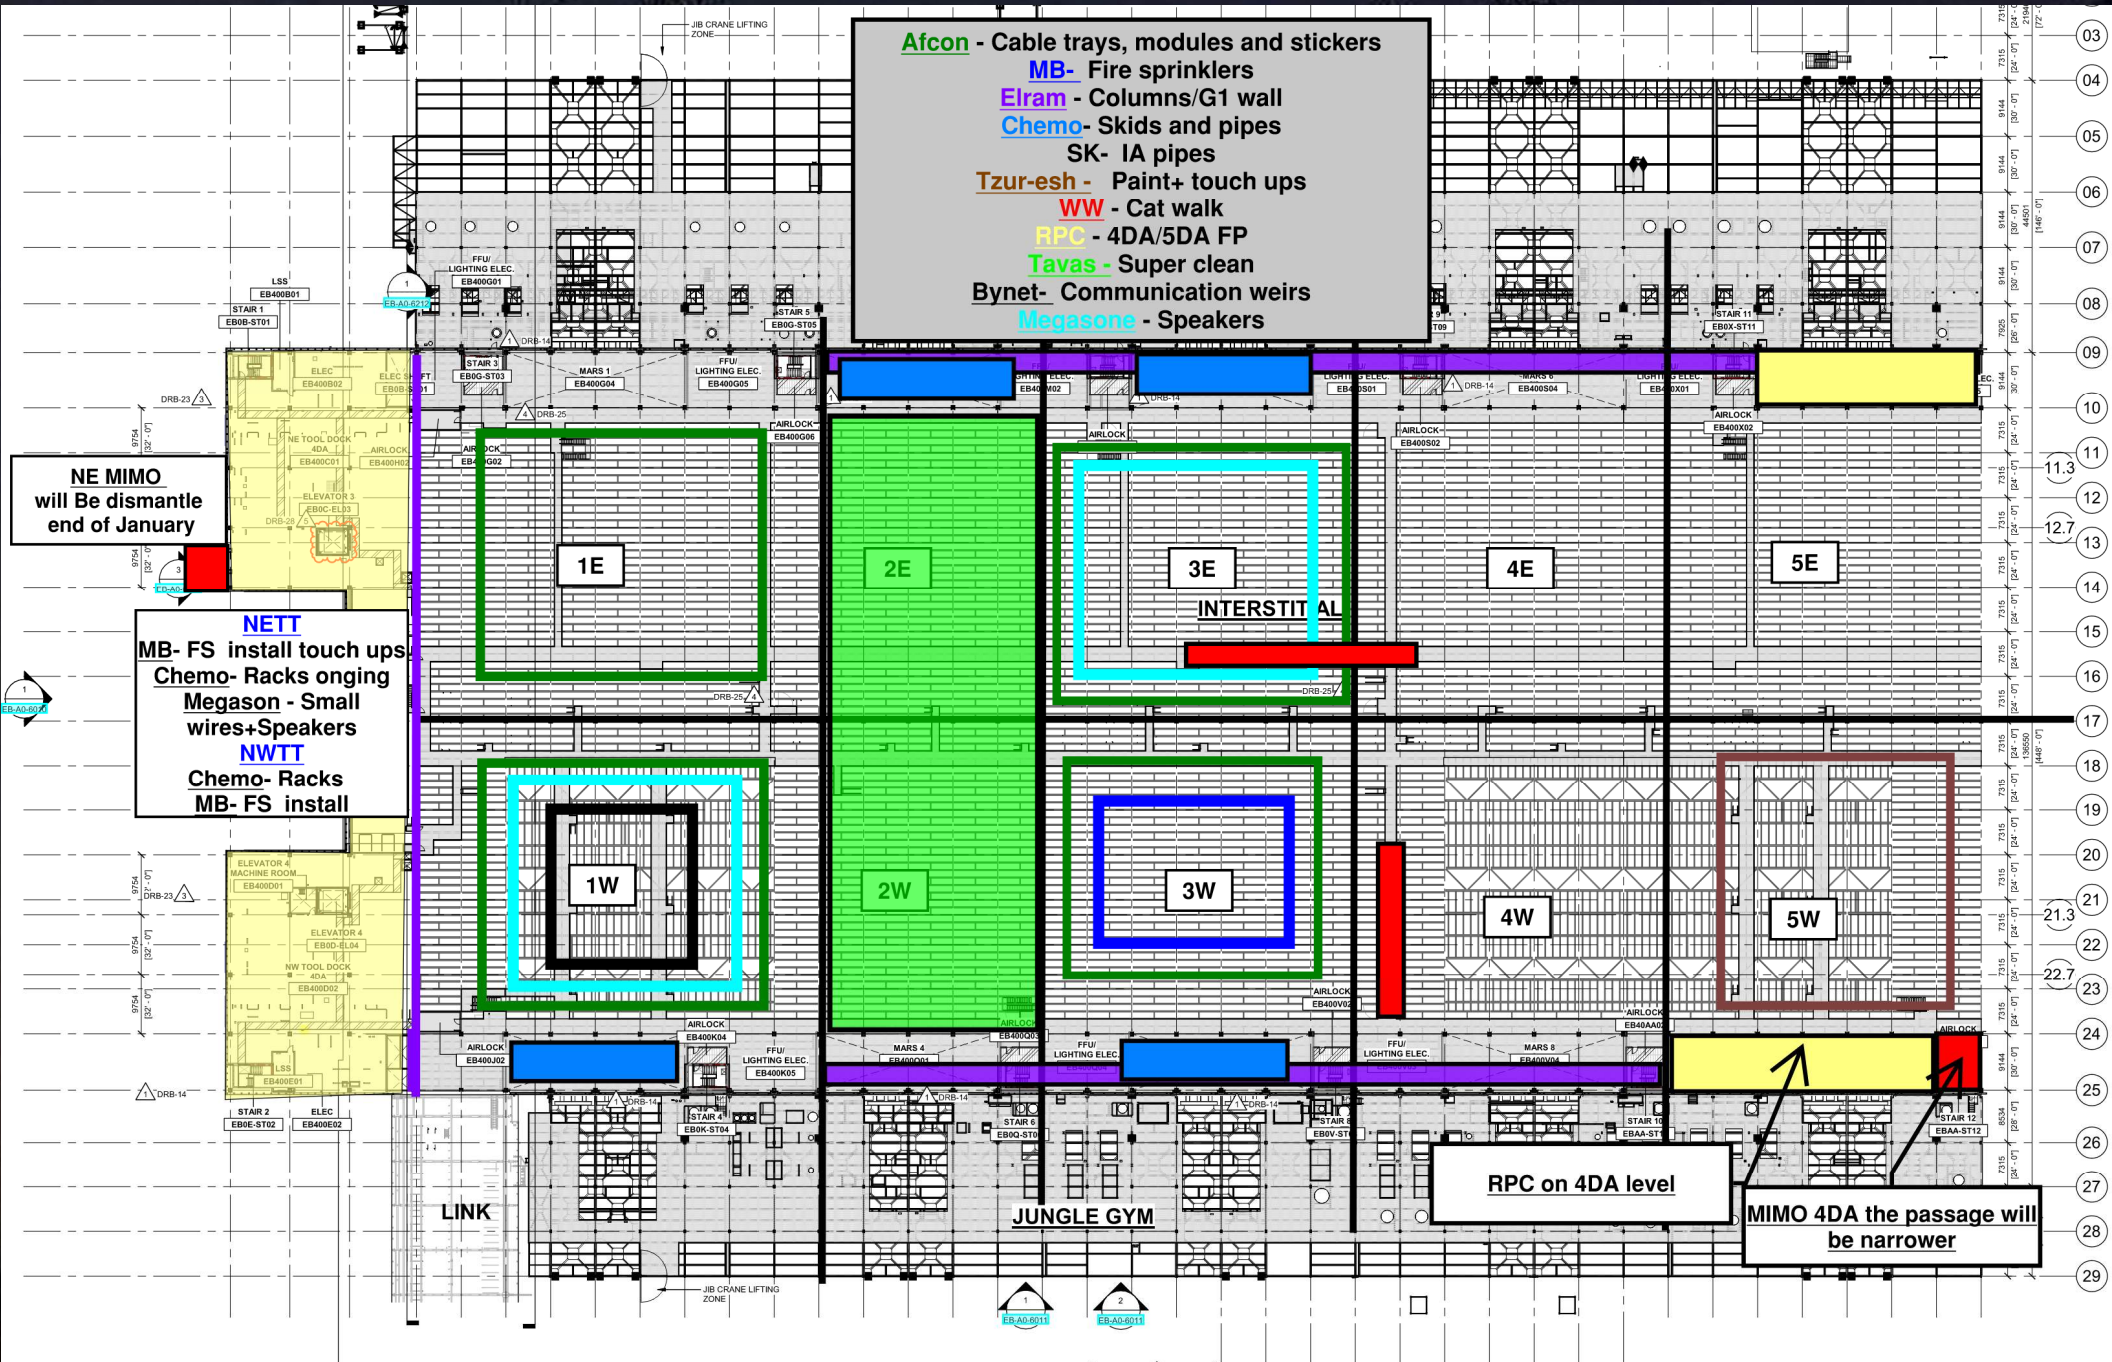

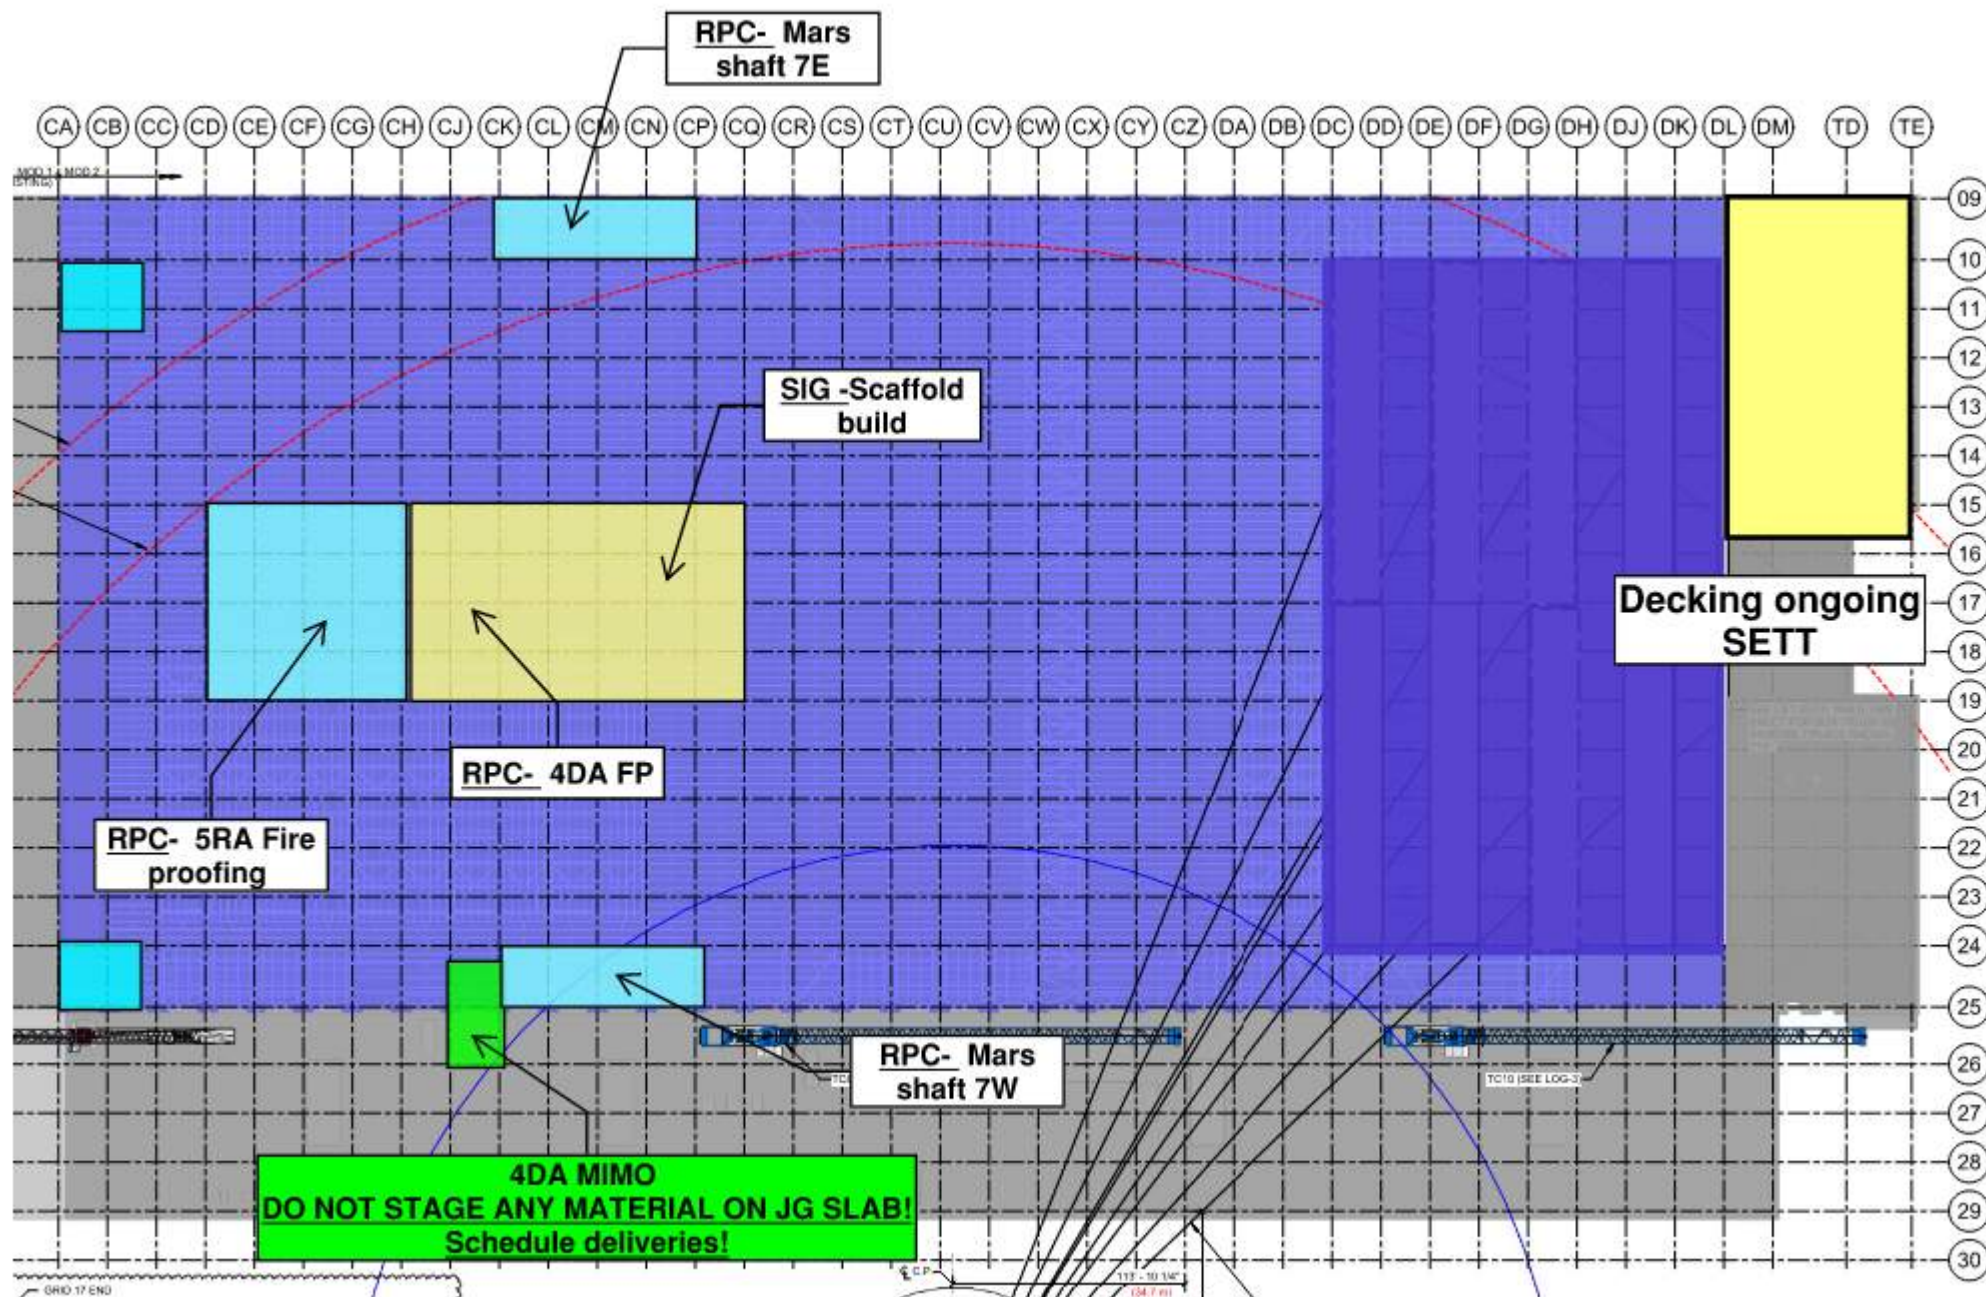

Siding - East FAB - PSSS

BLOWDOWN 30

[illegible]


[illegible]

Siding - North FAB

100% - BLOWDOWN

	9	10	11	12	13	14	TA	TB	TC	14	14.5	15	15.5	16.5	17.5	18.5	19	19.5	20	TC	TB	TA	20	21	22	23	24	25												
Total Installed %	901C / 901C						911A / 912A						911B / 912B						911C / 912C						1011C / 1012C						1011B / 1012B		1011A / 1012A						1001C / 1002C	
	29	29	29	29	29	29	29	29	29	27	18	9	27	27	27	27	27	9	18	29	29	29	29	29	29	29	29	29	29											
	100%	100%	45%	0%	0%	0%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	30%	100%	0%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%											
29	1	1	0				1	1												1	1		1	1	1	1	1	1												
28	1	1	0				1	1												1	1		1	1	1	1	1	1												
27	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
26	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
25	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
24	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
23	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
22	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
21	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
20	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
19	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
18	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
17	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
16	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
15	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
14	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
13	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
12	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
11	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
10	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
9	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
8	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
7	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
6	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
5	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
4	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
3	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
2	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												
1	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1												



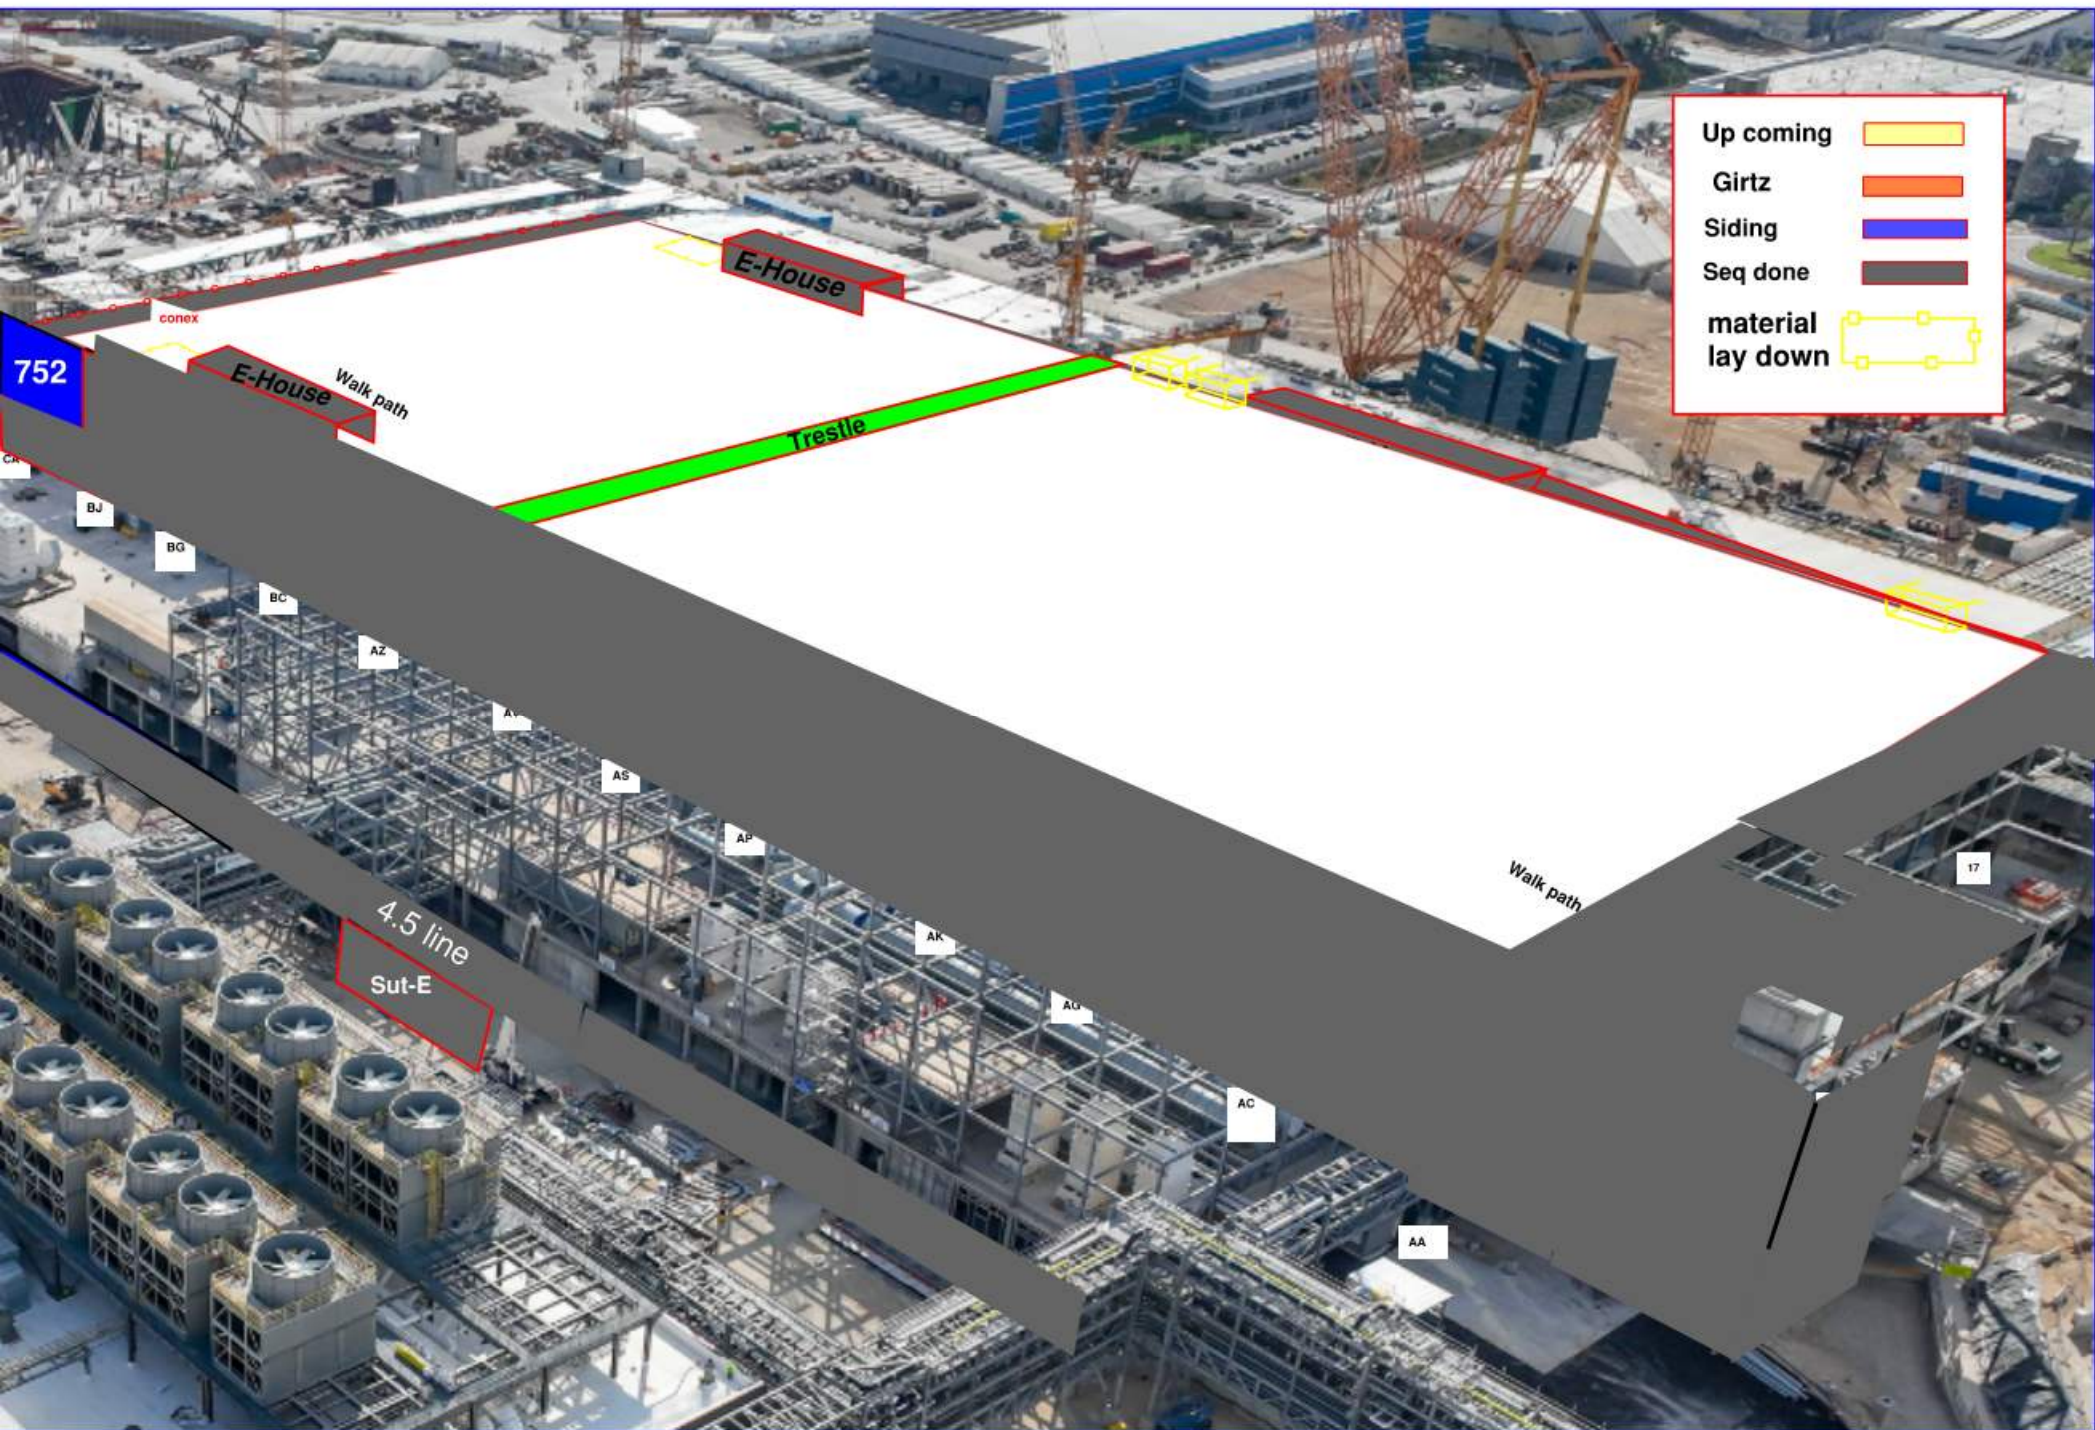


Up coming	
Girtz	
Siding	
Seq done	
material lay down	

PSSS.1

Utility Level 1YA

PSSS Roof 2SA

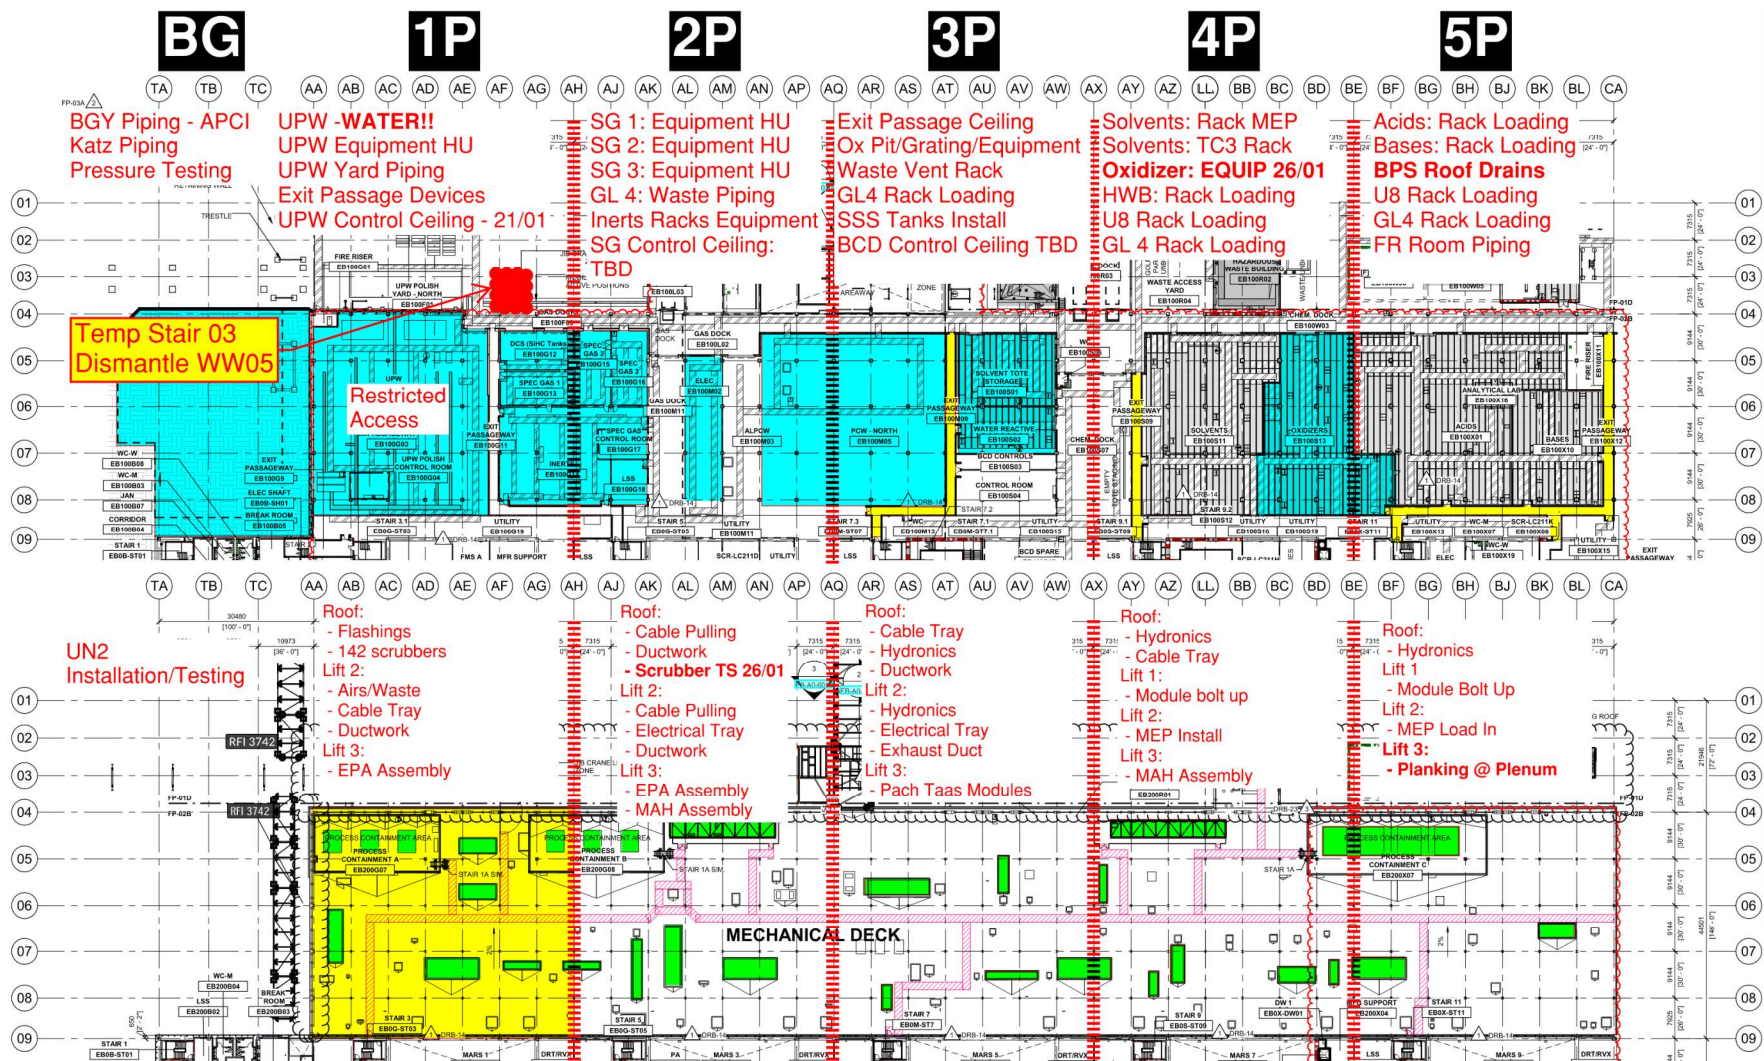

PSSS.2

6P


7P

8P


9P

10P


Utility Level
1YA

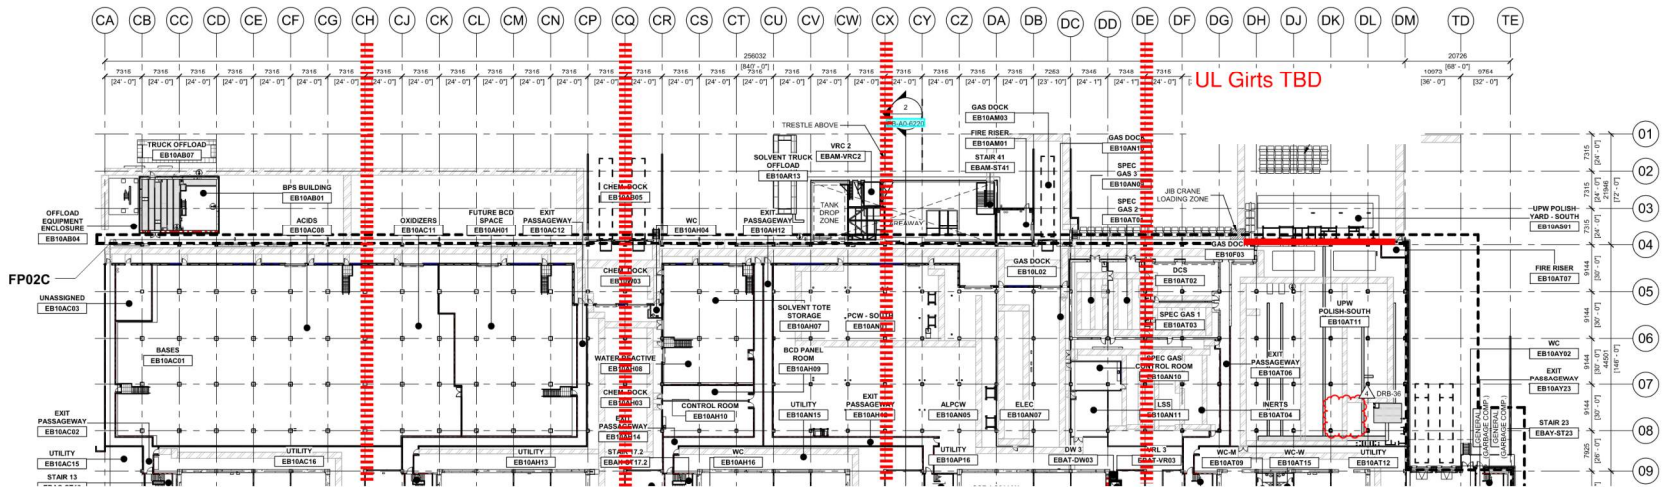

PSSS Roof
2SA

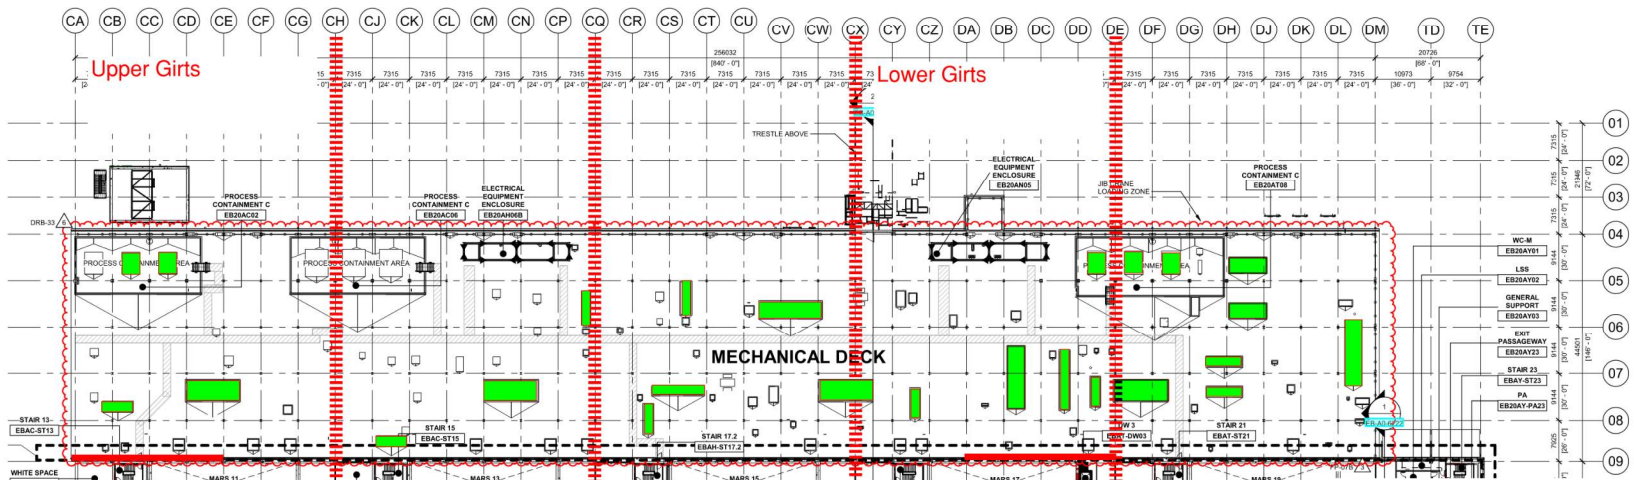


PSSS.1 Pressure Testing

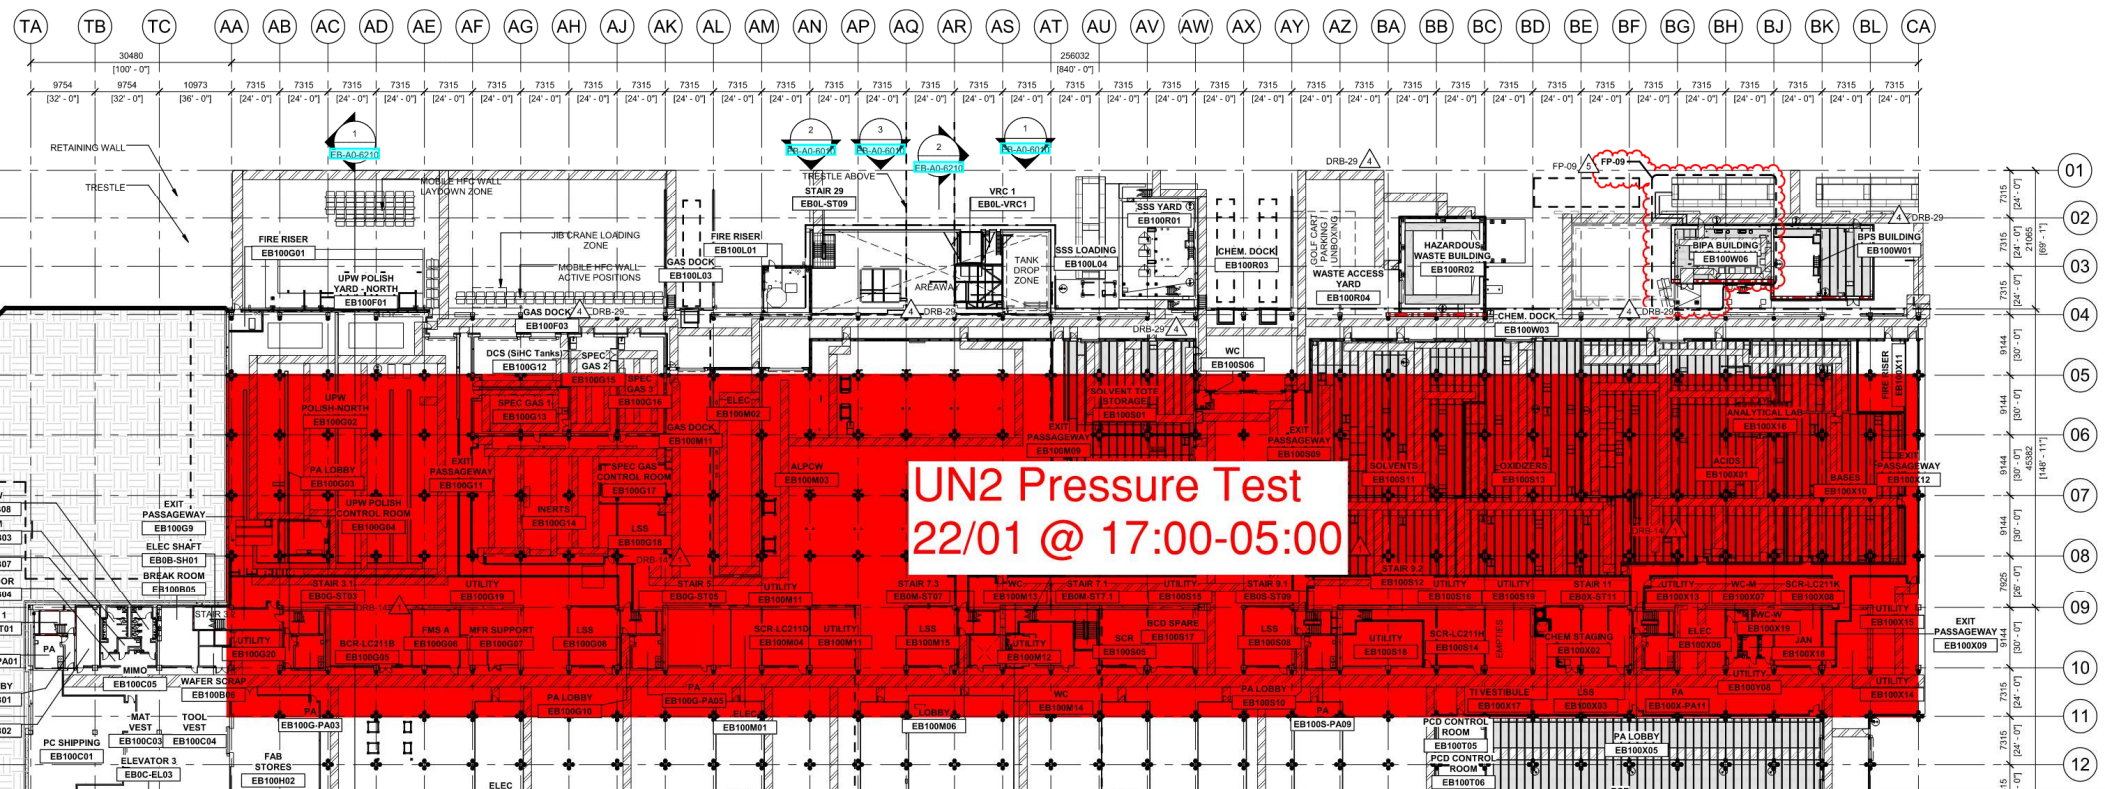



WJG 01J, 02J LIFT 2 & 3

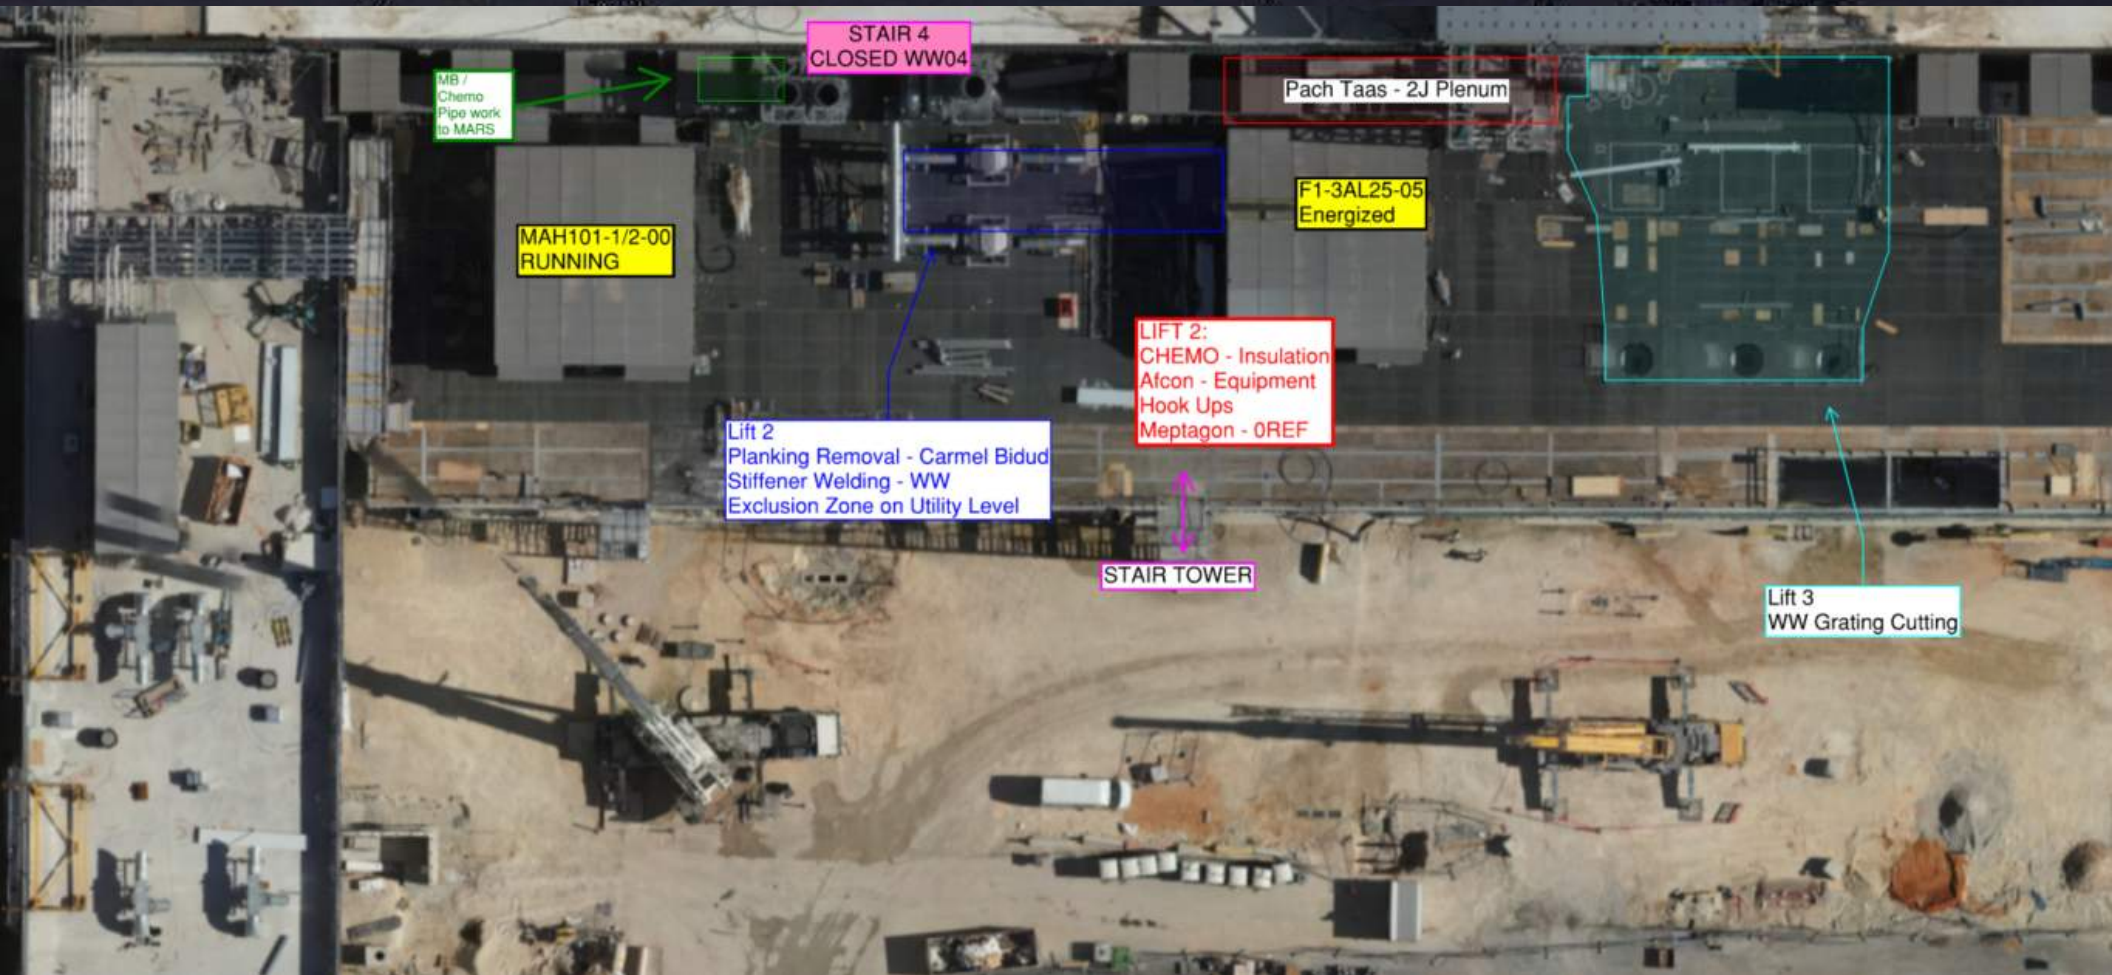




WJG 03J, 04J, 05J LIFT 2 & 3







WJG UTILITY LEVEL BUILD OUT

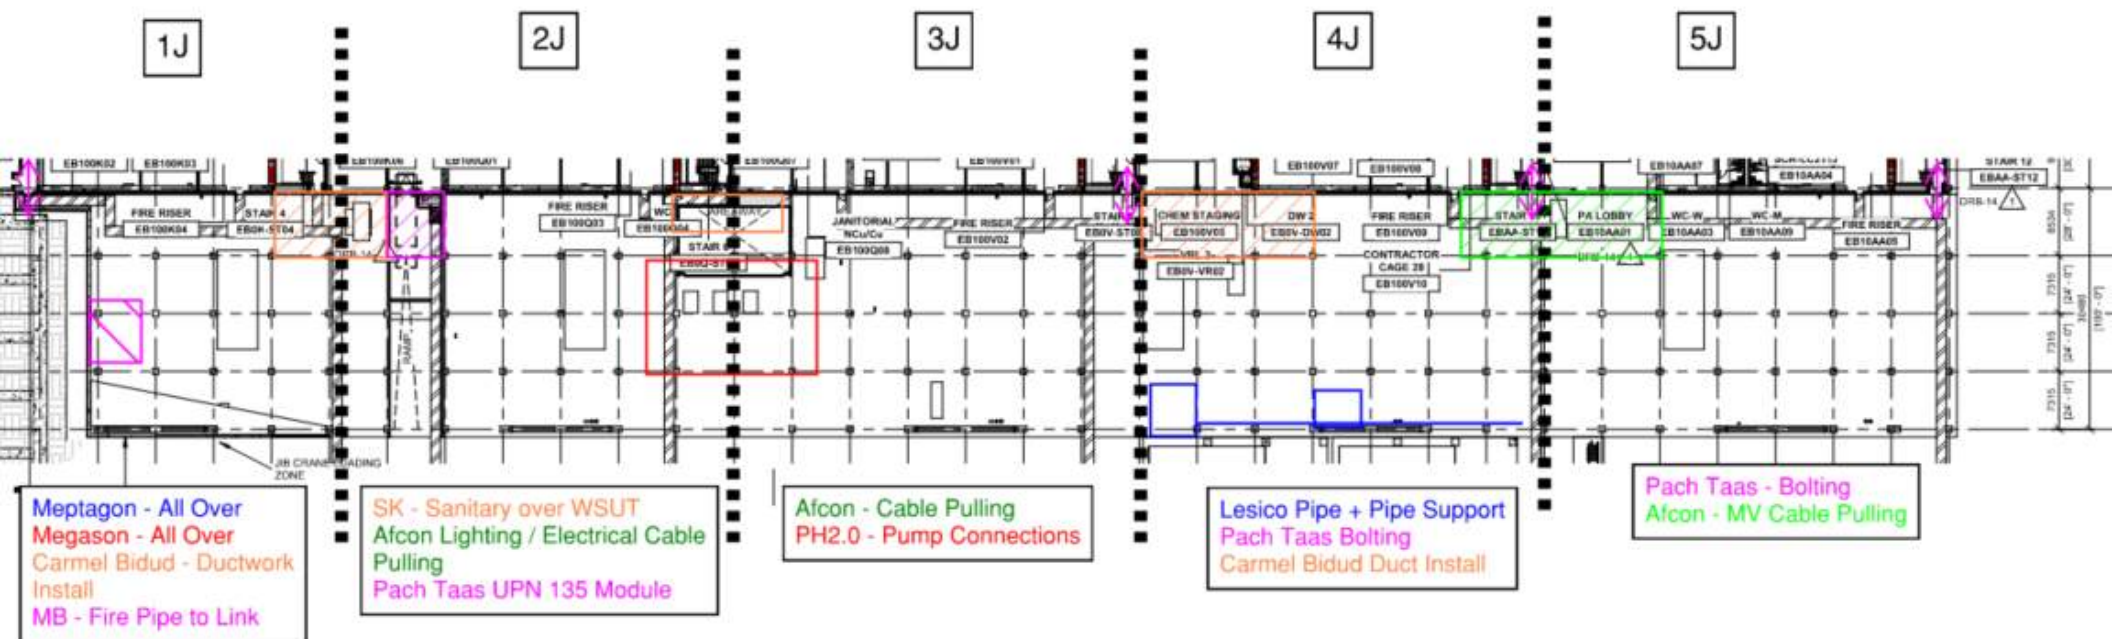

CUB COORDINATION MAP

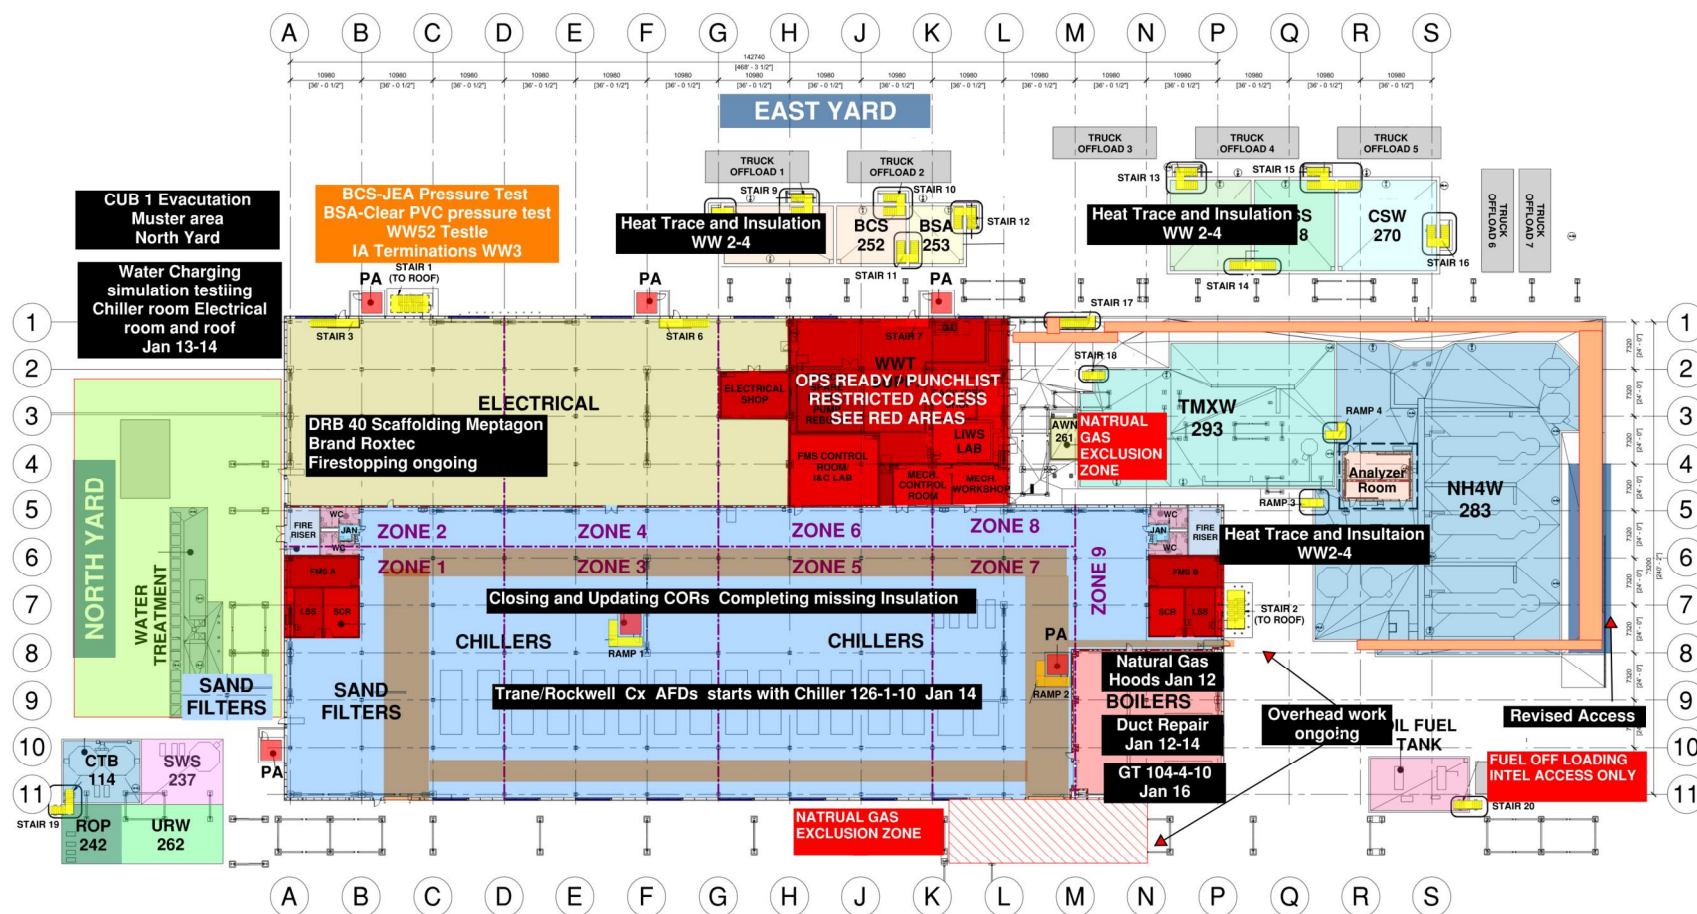


CUB 1 – EXTERIOR/ROOF

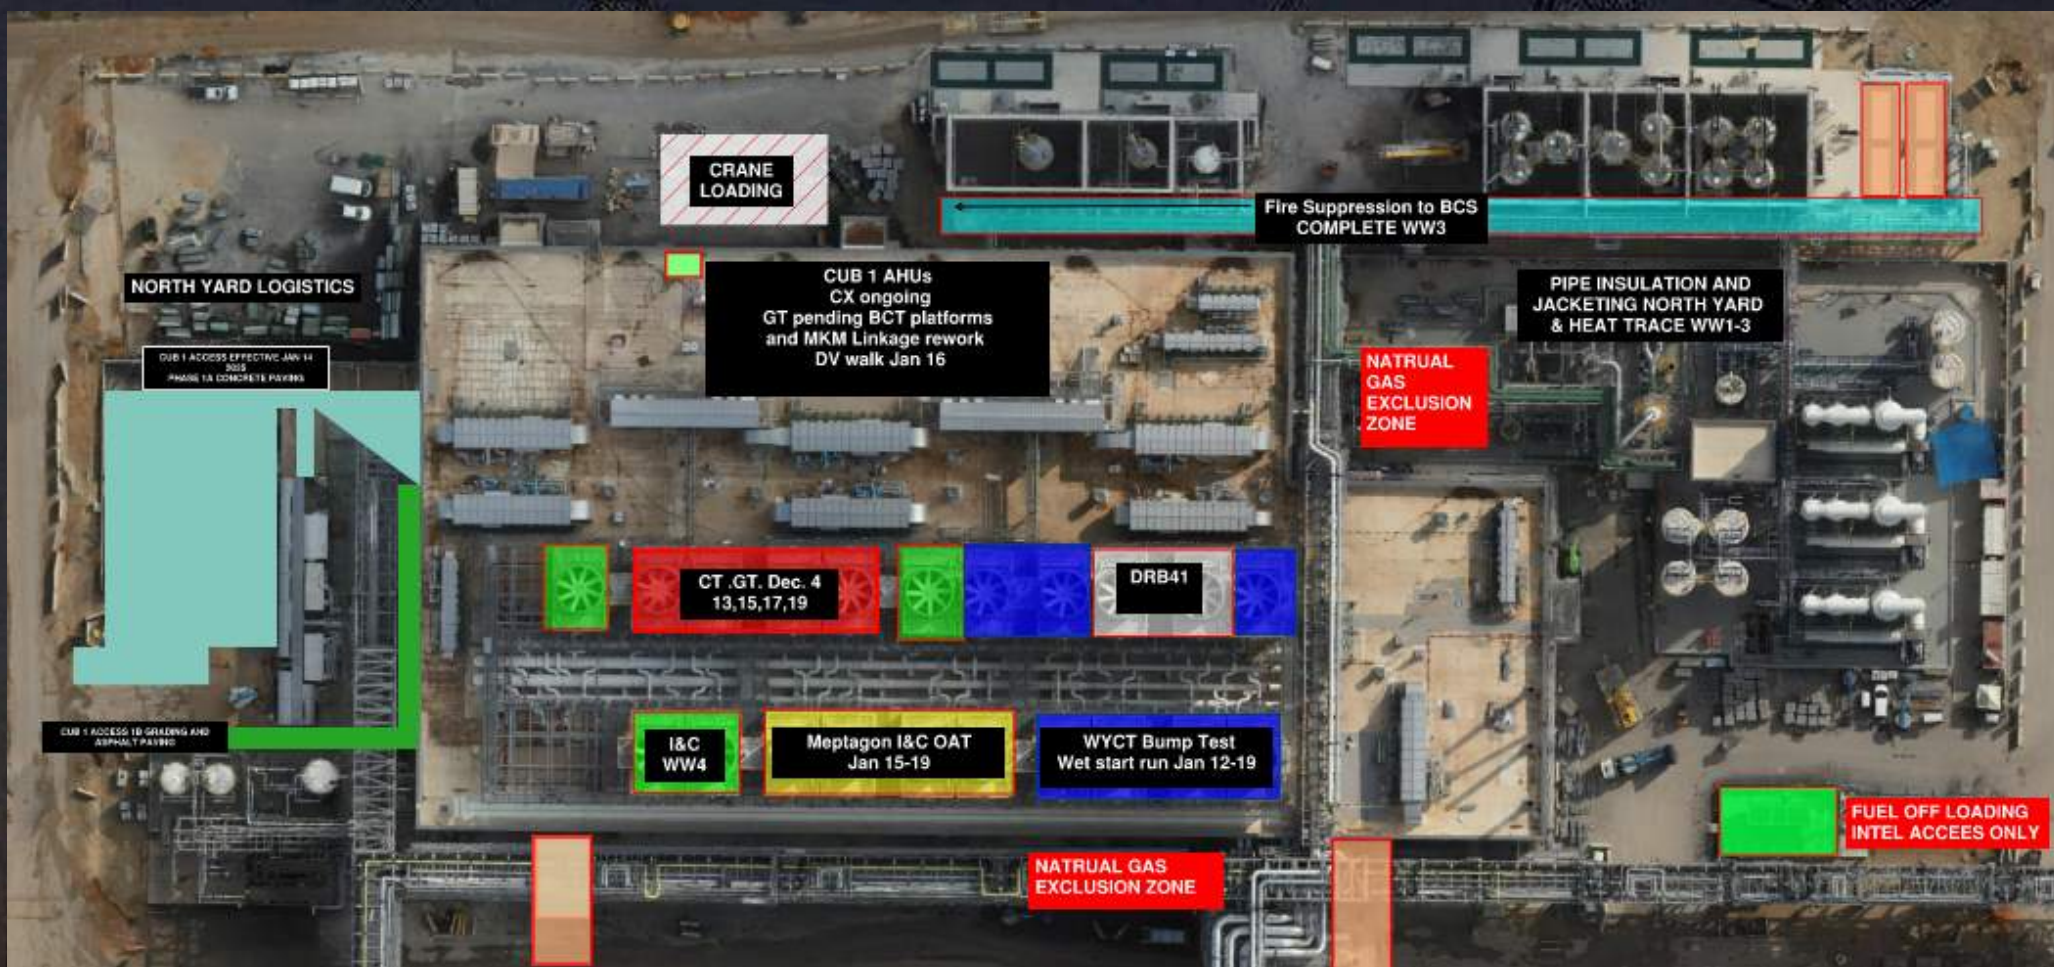


CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

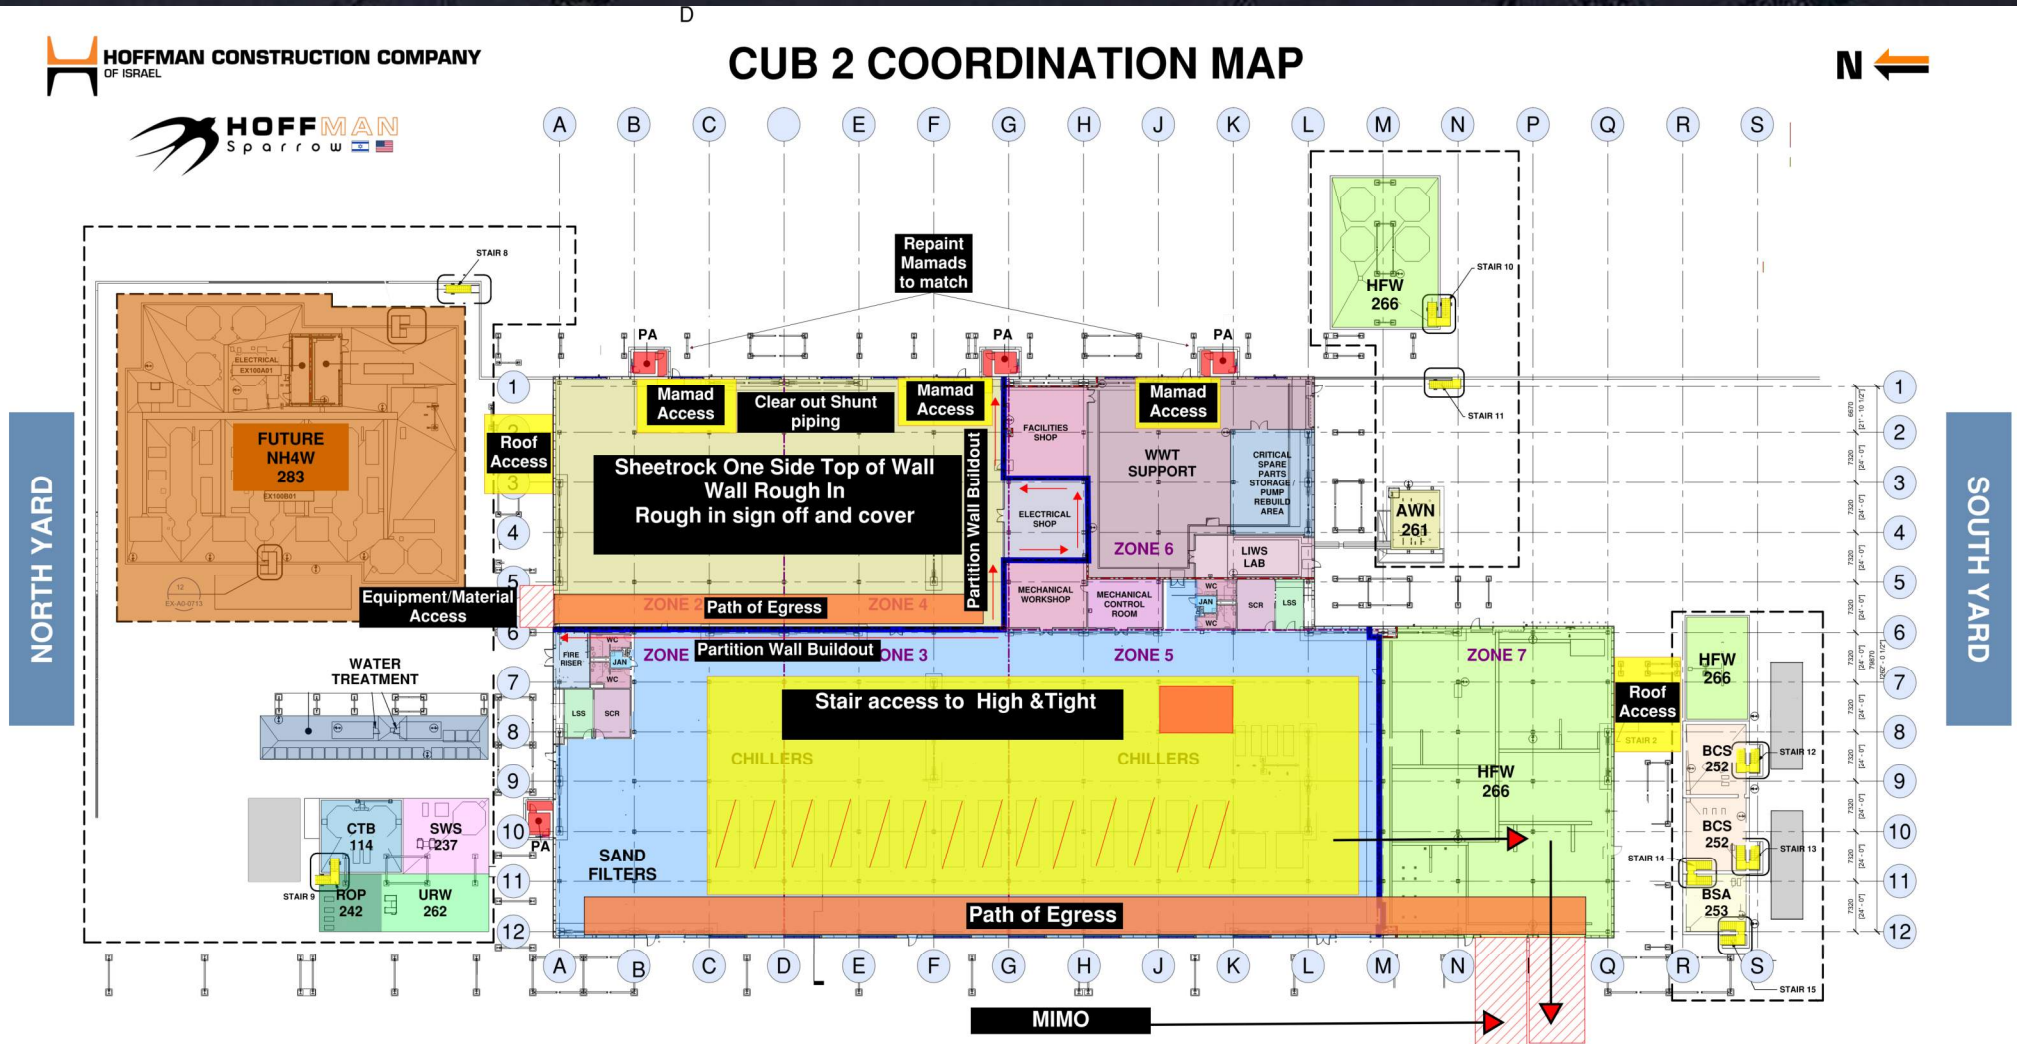


CUB 2 – EXTERIOR/ROOF

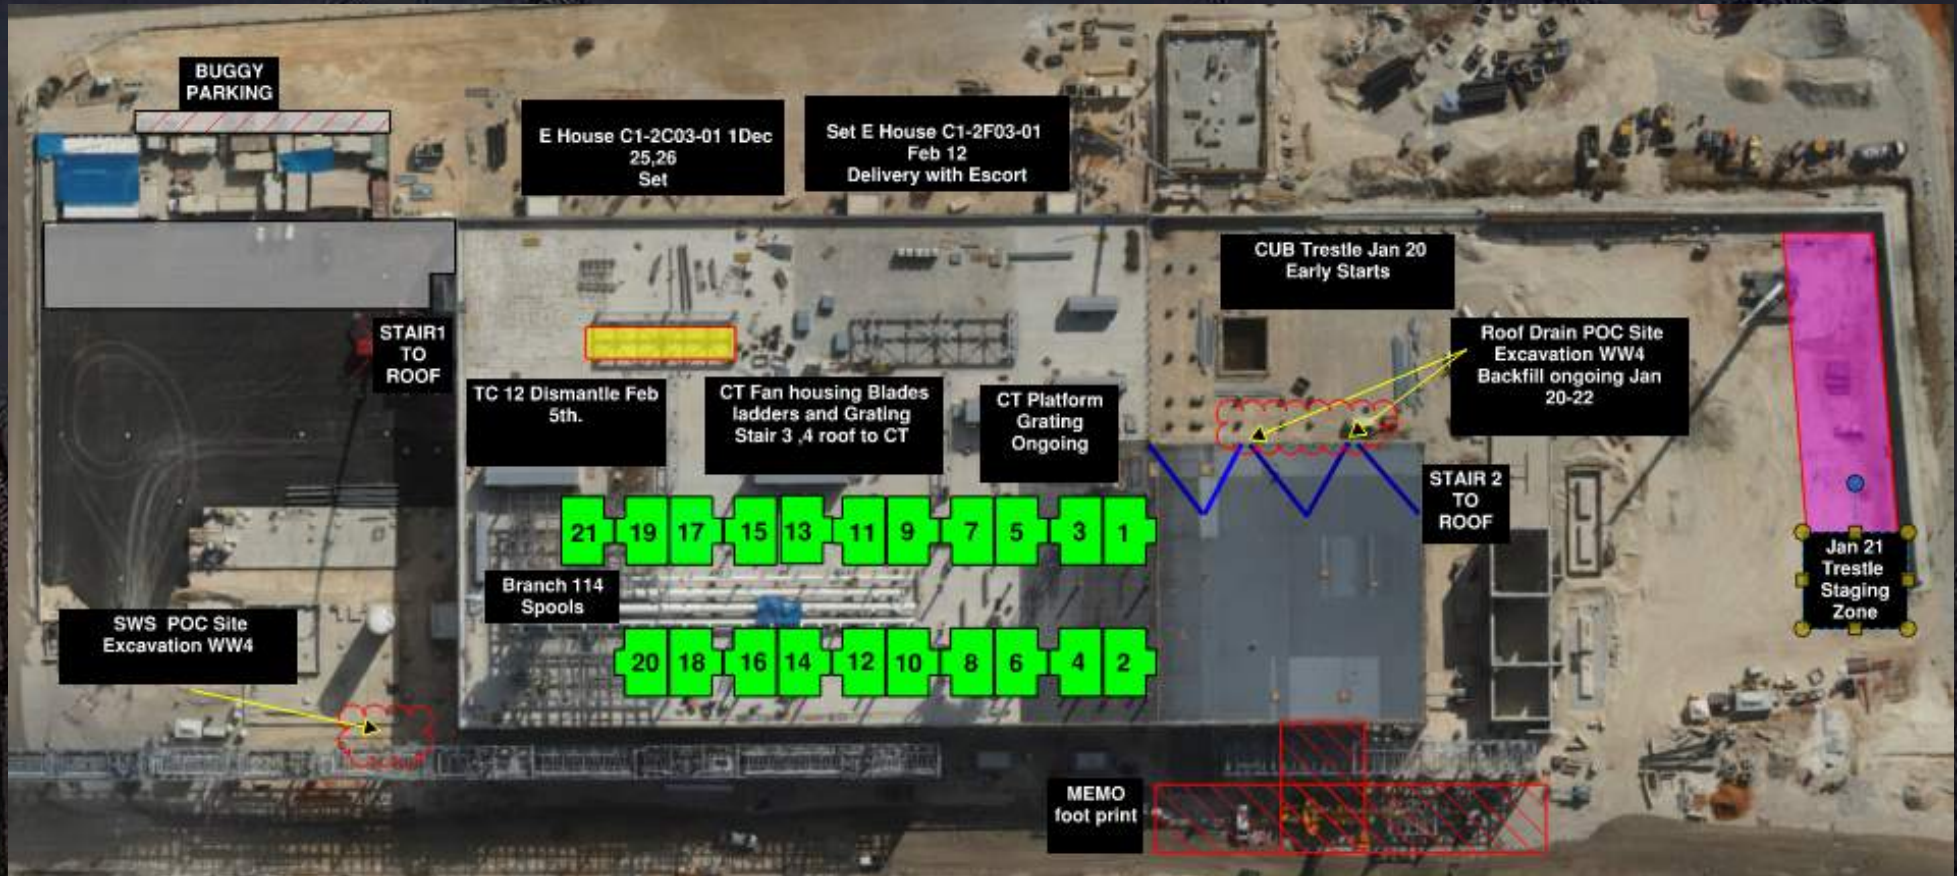



HOFFMAN CONSTRUCTION COMPANY

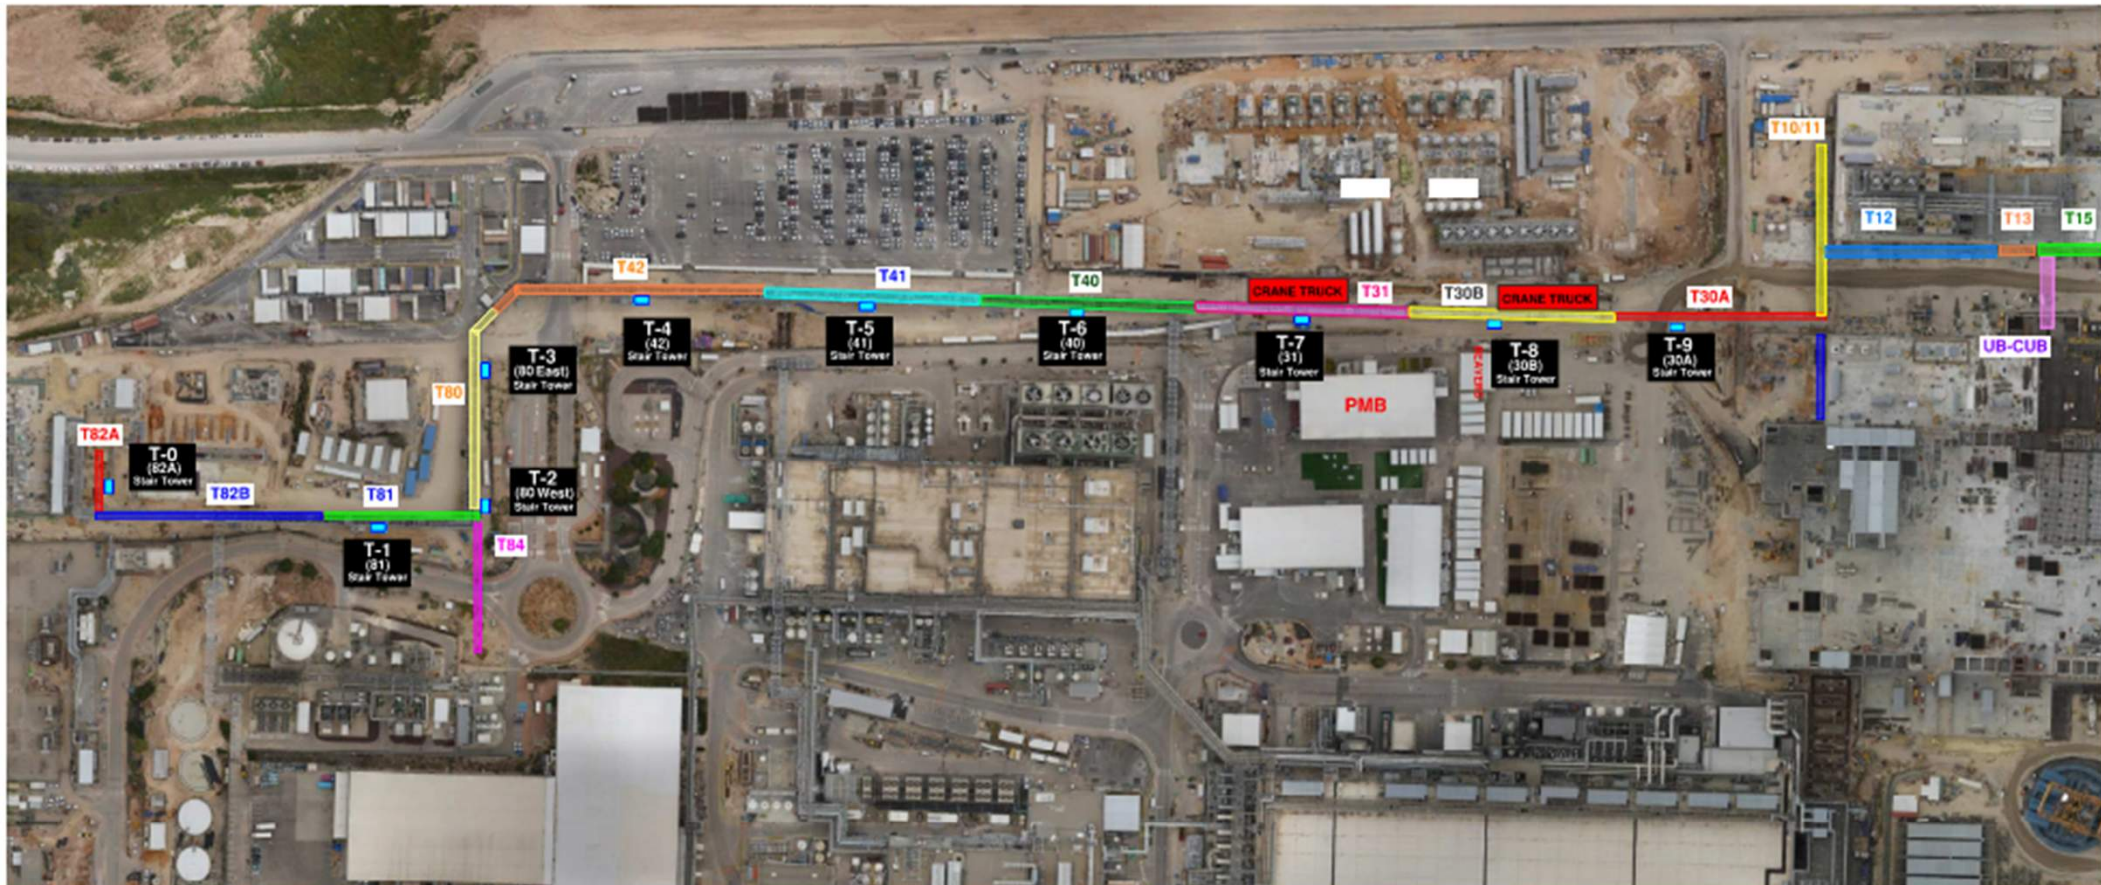





HOFFMAN CONSTRUCTION COMPANY



HOFFMAN

Sparrow

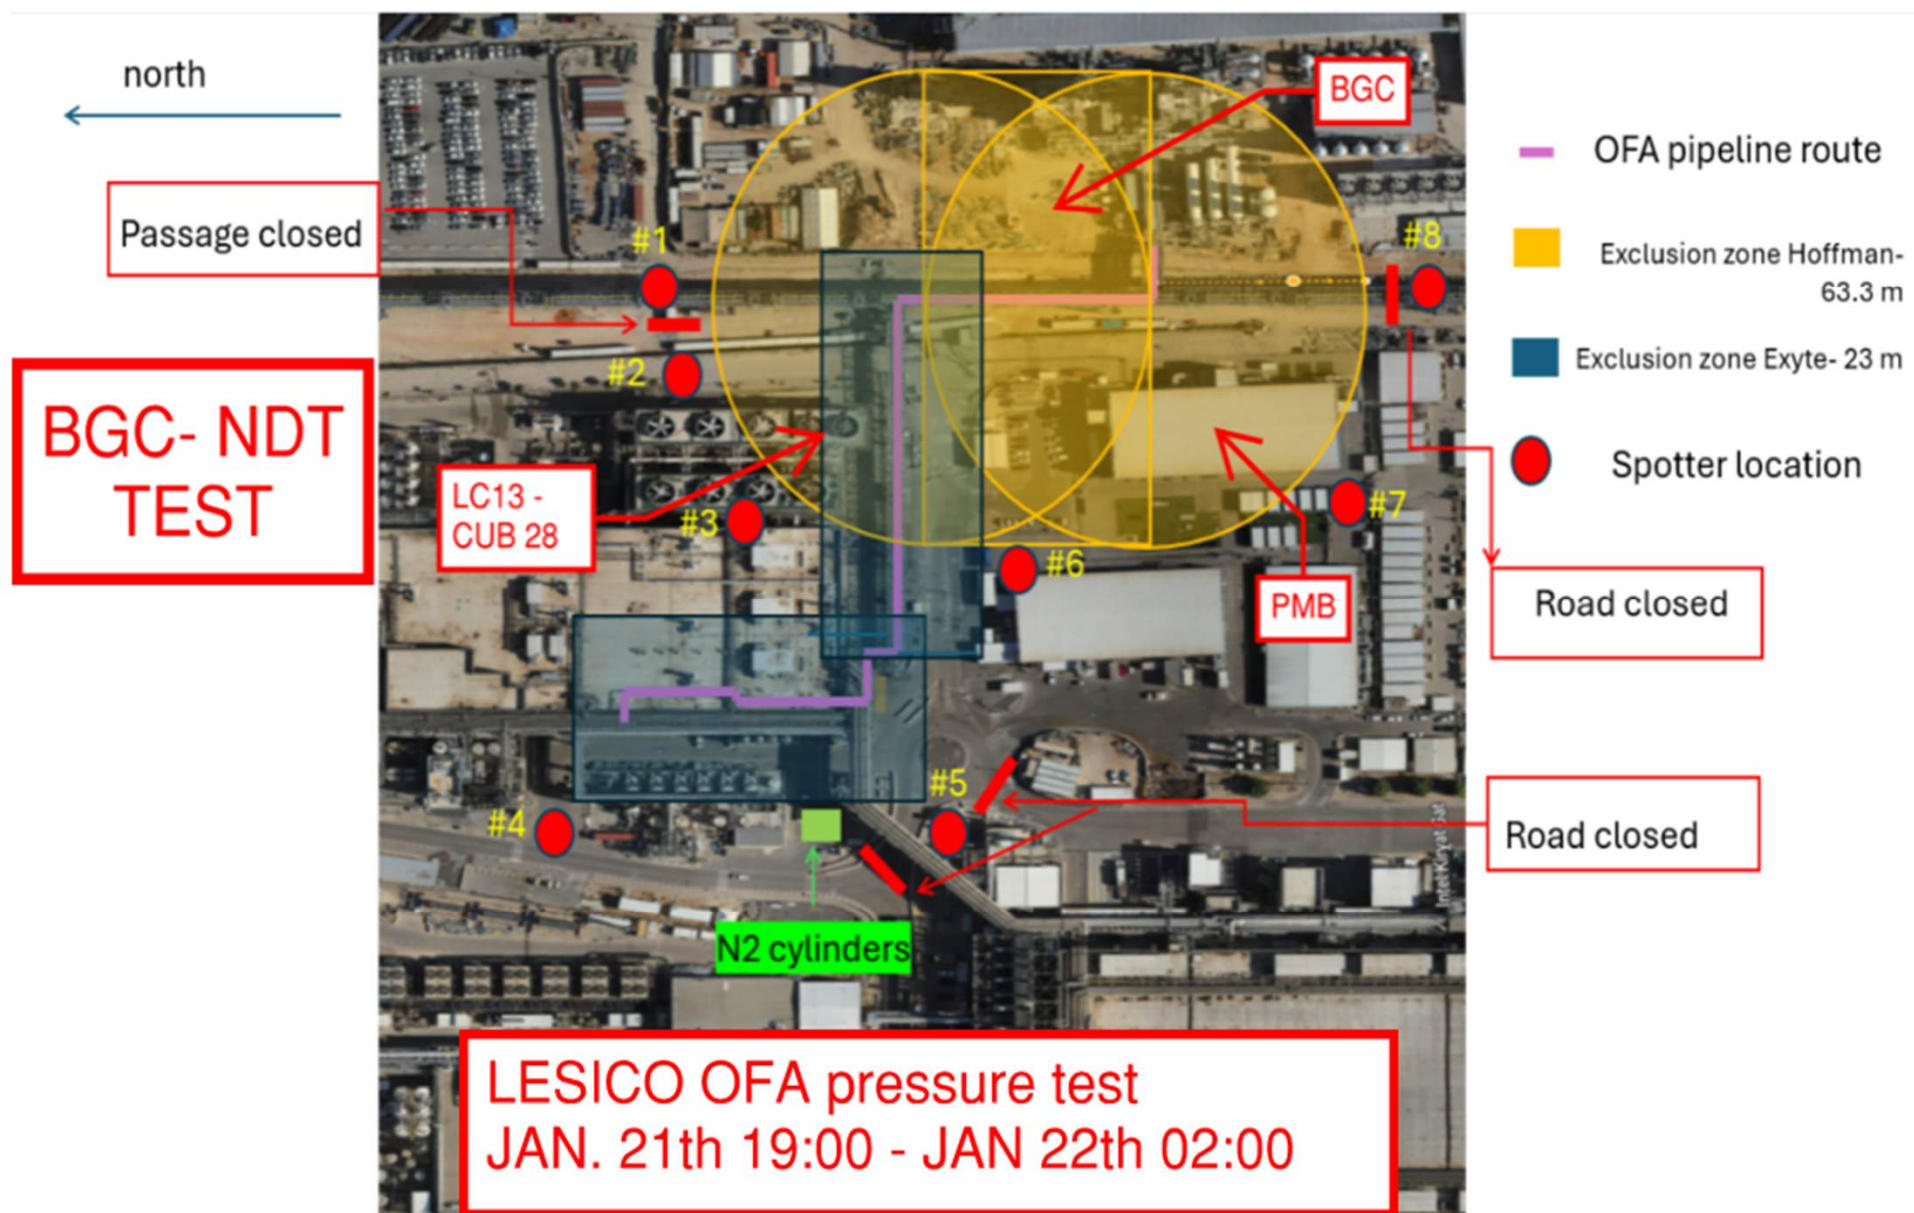




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow

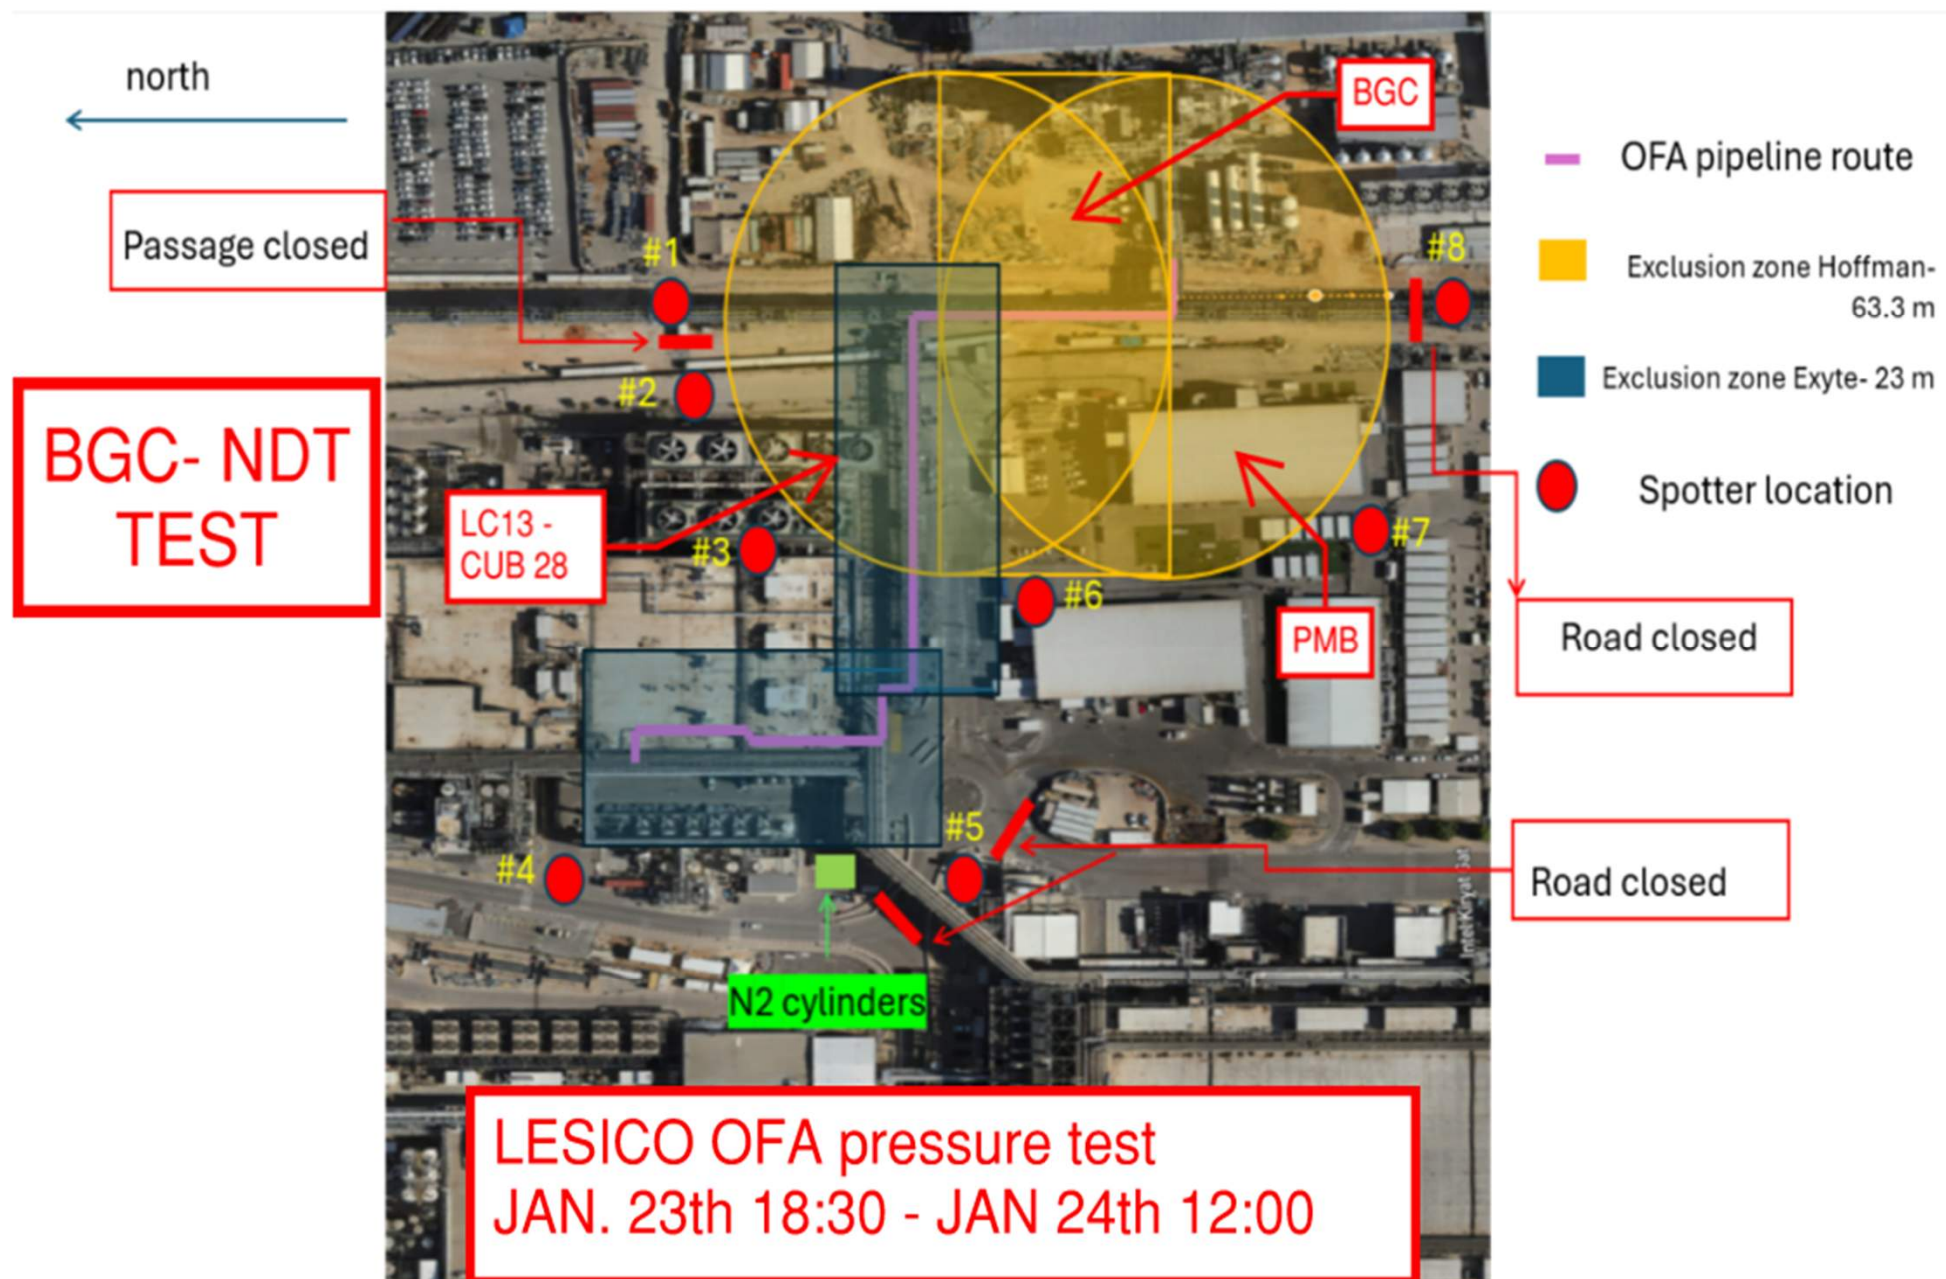



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

MODULES IN FOR STORAGE

1 unit-Tue 21/1+1 unit-Wed 22/1
1 unit-sun 26/1+1 unit-Mon 27/1

GATE A


CUB 2

MODULES STORAGE AREA

Trucks maneuver area


Module access route


Keep a 10-meter-wide passage open



Daily Coordination Meeting

Site Logistics North

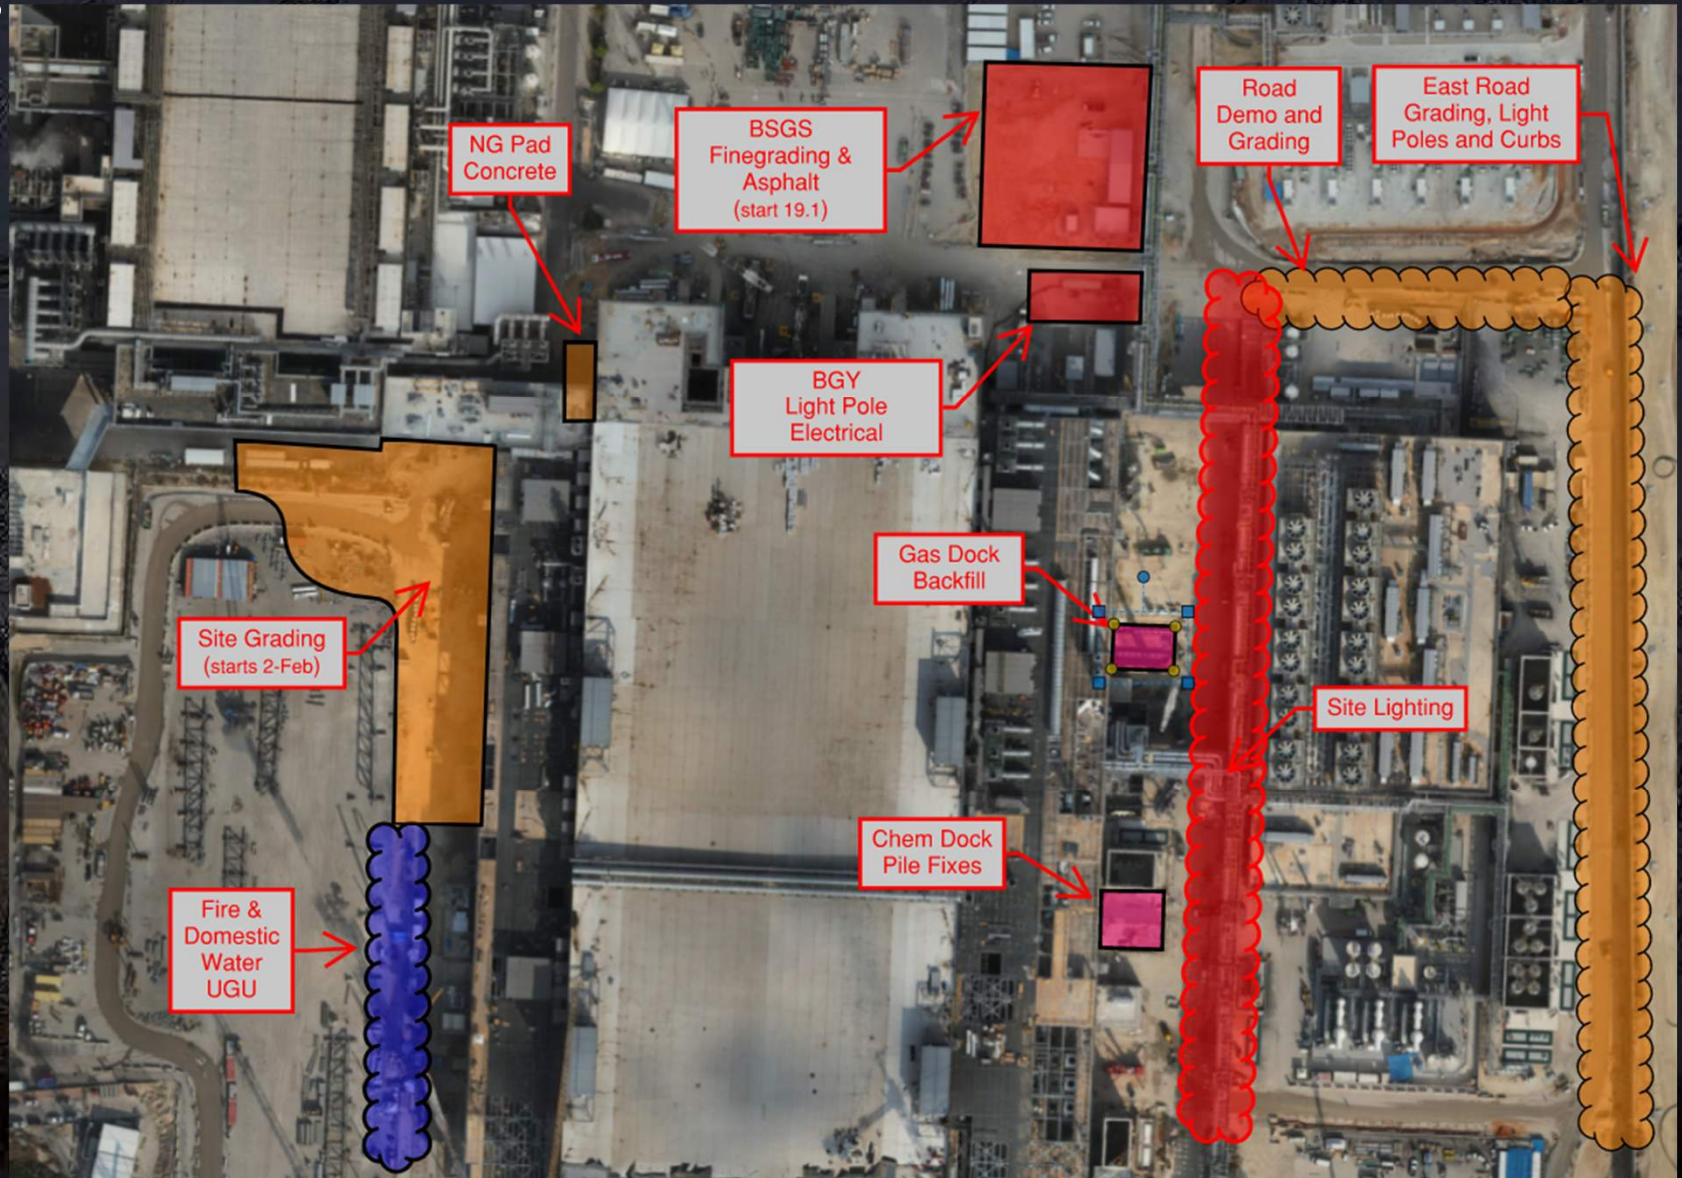




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South

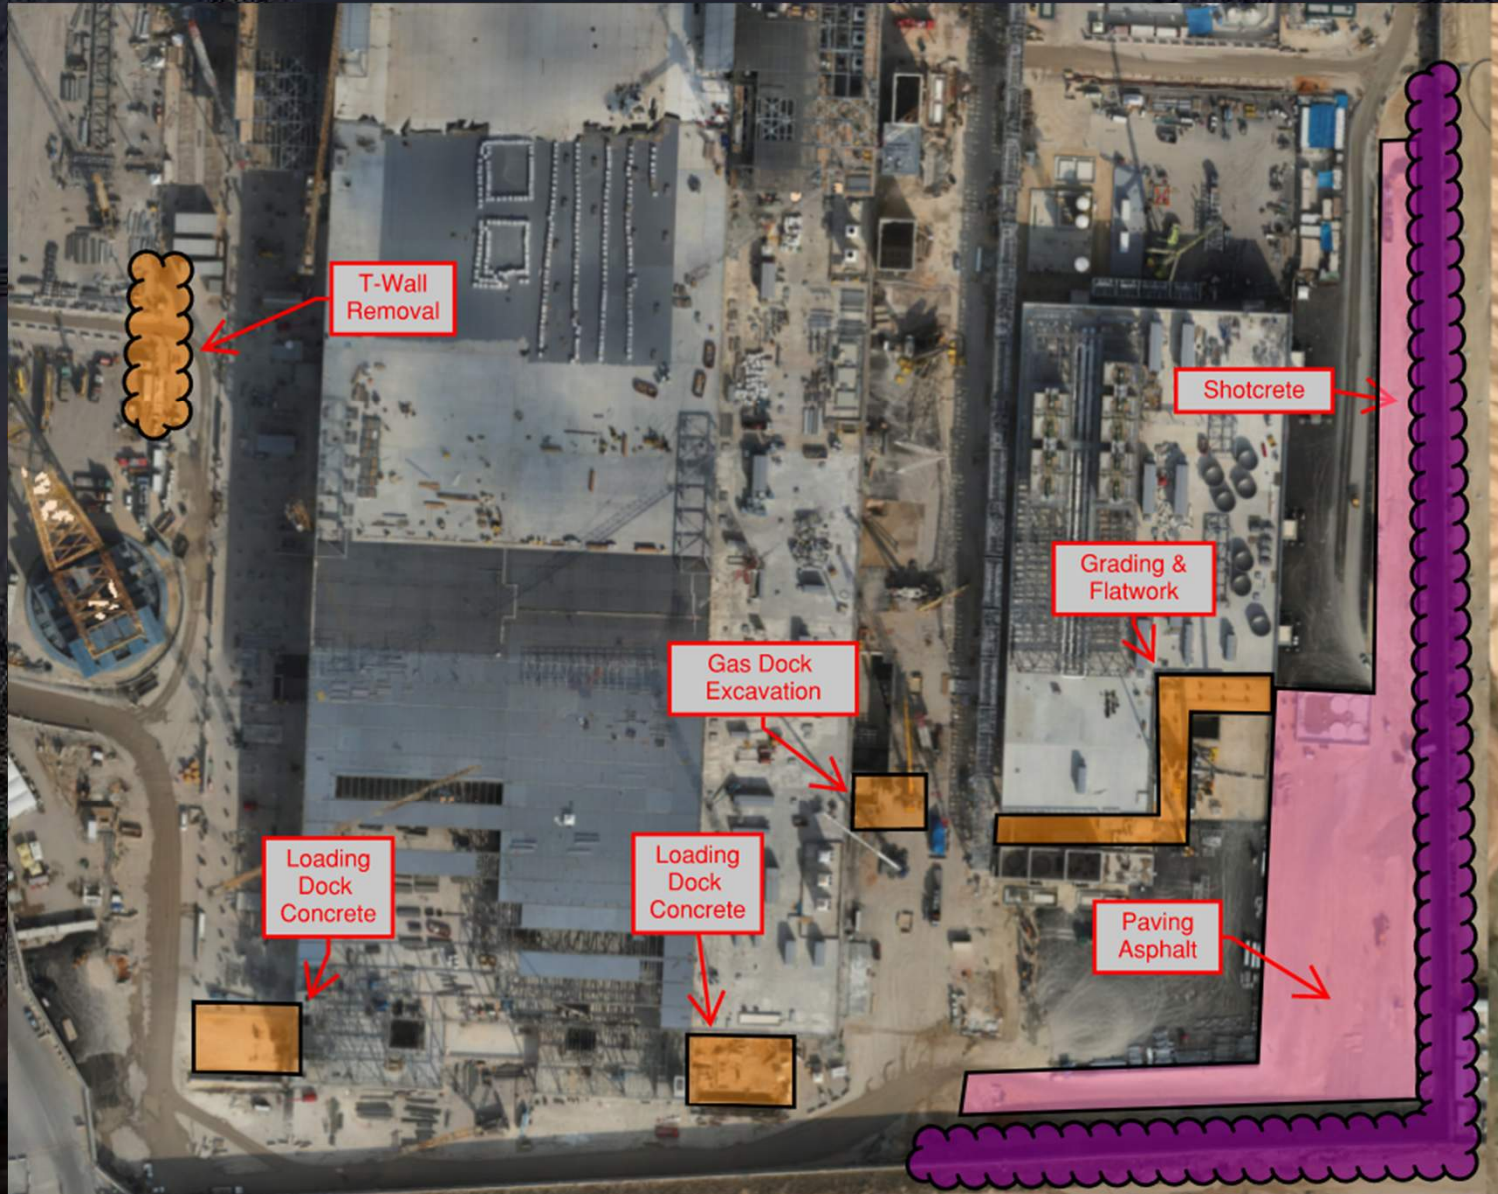

Barricades

- We're seeing an increase in unsafe observations regarding barricades.
- Please make sure that your crews are using this important communication tool effectively.
- Barricades must be fully enclosed. This means that there are no open sides that someone can enter through.
- All barricades must have signs with the hazards and the contact information for the person in charge in the area.
- Red barricades are for immediately dangerous to life and health hazards.
- Yellow barricades are to caution people and bring awareness for a specific hazard.
- Hard barricades are for long term or more control needed for an area and should be treated like red barricades. Hard barricades cannot be used for fall hazards unless they are more than 2 meters from the fall hazard.
- Guardrails are designed for fall protection and should be treated like red barricades.

HCC/EHS Weekend Work- 17.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Zac Ross - 052-7582746

Tamir Hamo - 052-6230917

Yehuda Cohen - 052-3614292

Jimmy S

CSA CM

Girum Abay - 052-2237784

Nick Gividen - 052-3434754

Pauric O'Reilly - 052-3571665

Andrew Thomas - 052-3453815

Patrick Blunt - 052-3155787

Dave B

MEP

David sooter - 052-4121028

Cx

Cranes

Safety

- Safety Foreman - Rami Al Jaar 052-6169466 Rami-AlJaar@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 10.01.2025

FAB

Utility Level / Roof / Stair Shaft

Subfab

- Pach Taas
 - W-E Perimeter
 - Andrey 0502998167
- Afcon E
 - All over SF
 - Avi Eli: 0526008487
- Chemo
 - TTNE/TTNW
 - Tomi: 0523759408
- MEGASON
 - 7E
 - Israel 0526869393
- SELA
 - 5E,5W
 - David 0524382997

Clean Room

- Talad – 10 guys CR 2 W-Lids removal, 1W- Ceiling install, 3E-PVC cover (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 14 GUYS Mod1 – Scaffold removal, MOD2- 17 line (EHS Beni 0506232032, Super Shmulik 0549205966)
- Afcon – 20 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)
- Chemo –16 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Sela – 8 2E CRC (Supervisor David 0524382997, EHS Samuel 0506306031)
- D&p - 40 guys Freddie Hazan 0503827885
- Pach Taas 3 guys, BF-CA 17 Line
- Talent 1E-1W – Maintenance , 2E- Superclean (Super Yosi 0526557130, EHS Evgeniy 0543053595)

Subcontractor Weekend Work- 10.01.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- SK Engineering – GL4 UL Piping, 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112

WJG

- Afcon – Lift 2 and Utility Level Cable Tray
Foreman: Montu 055 911 6973
Safety: Pradeep 055 274 2935
- Chemo: 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)
Foreman: Maor 050 988 9071
Safety: Erez 054 971 6840
- Pach Taas: All over (HRA)
Foreman: Tomer 050 767 0585
Safety: Jad 050 5405016

Subcontractor Weekend Work- 10.01.2025

CUB

D&P:

Constantin - 0545501602
David - 0548894447

Sami Najami:

Husein - 0526917461
Barak - 0542262530

Chemo:

Dudu - 0509808846
Leonid - 0548883878

HSAI:

Sergey - 0552728807

Trestle

SNJ:

PIPES –T40 - UB CUB - 13 workers (3 teams)
STEEL –Galvanized paint + T30 A+B - 8 workers (2 teams)
Steel adjustment - 15 workers (3 teams)
FORMAN
Adiv asaly- 0526017477
SAFETY TRESTLE
Barak mesica tel. 0542262530

Stage Design

Scaffolding – T40-T30 UB CUB – 8 WORKERS
FORMAN
Doron kadan – 0502682680
SAFETY TRESTLE
Osama - 0522851458

Siding

Site

Derech Afar – Shotcrete wall
Supervision = Raed: 054-244203
EHS = Alex: 054-5403849

Olizki – Offload 18 & CUB1 trench drains, Southeast CUB1 grading
Supervision = Or: 052-4917313
EHS = Ben: 052-4033565

Afcon – BGY Electrical
Supervision = Tomer:
EHS =

Daily Coordination Meeting



14:00 Sign In
