

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Development of Access Plans




SETT 4DA SOMD
12:00 am


Pump will block south
road from 11:00 pm
till 3:00 pm no traffic
will be able to get
around




UTILITY LEVEL MOD1

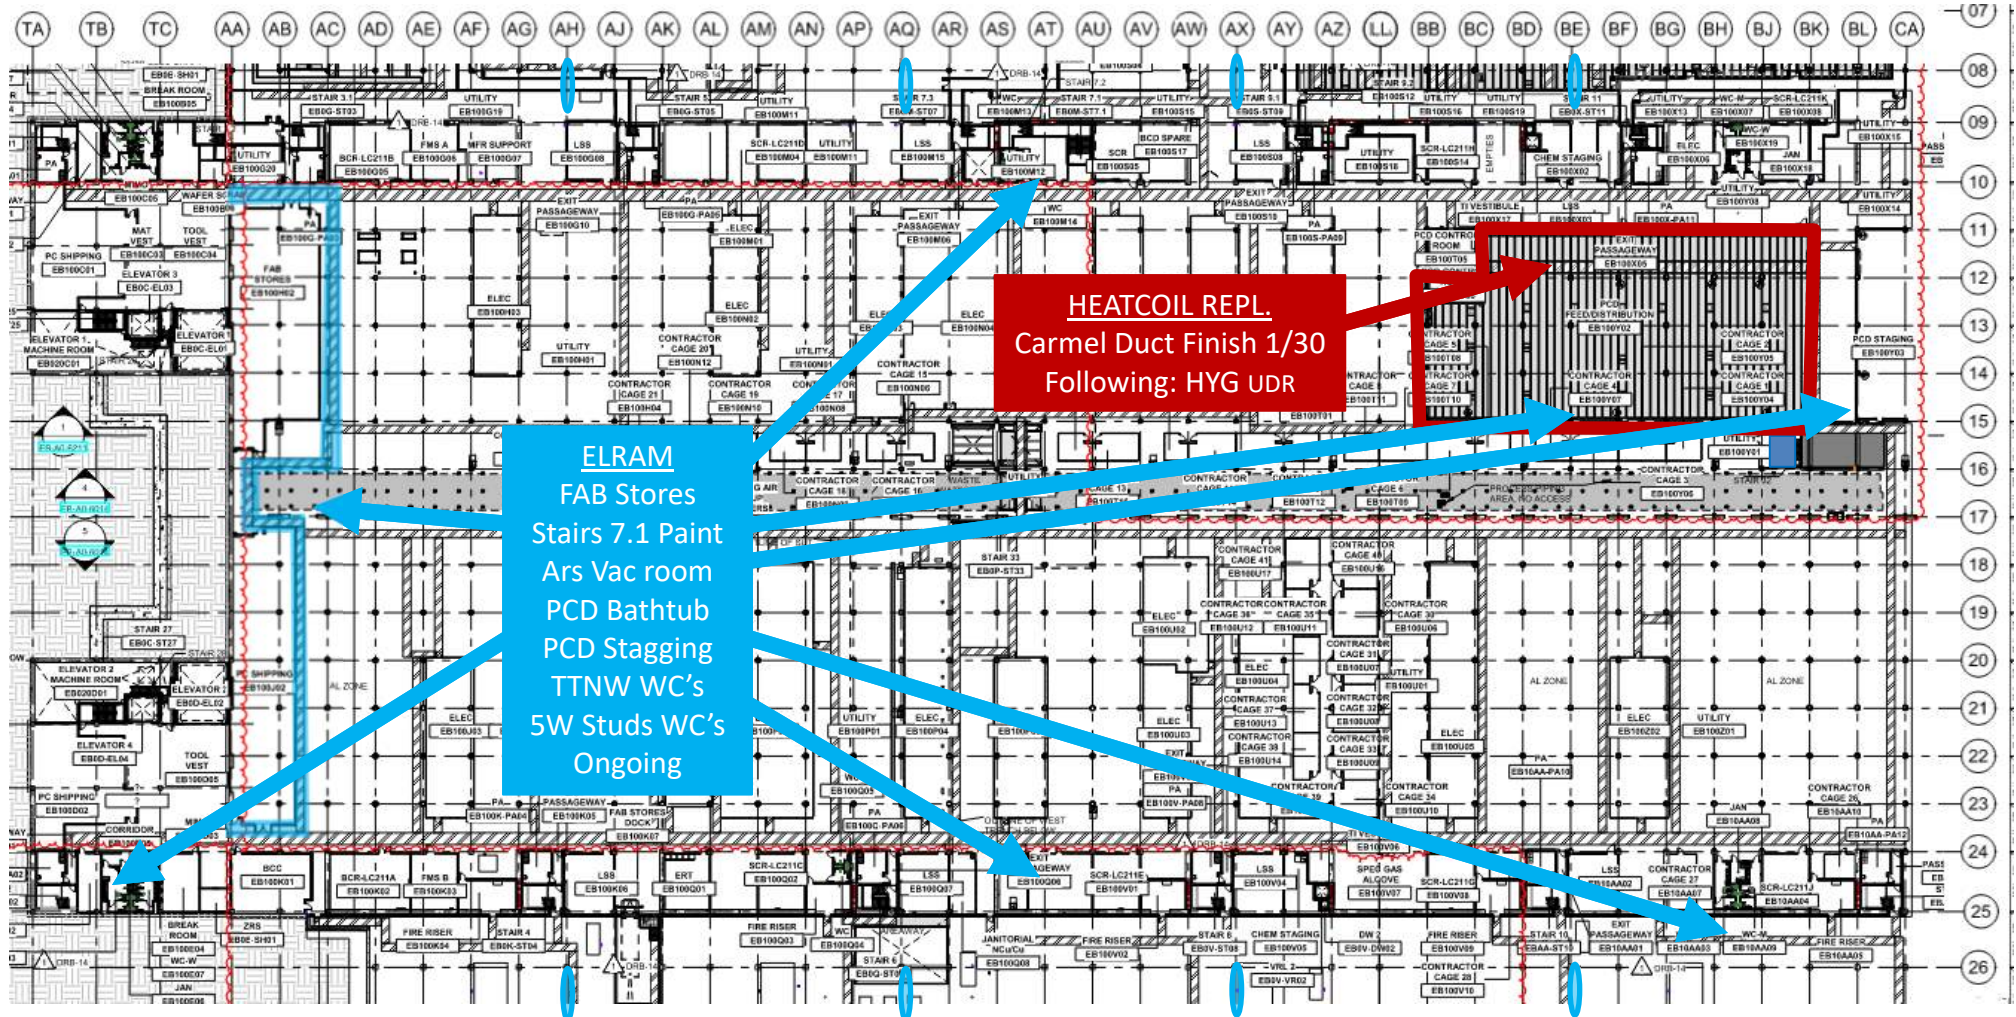


UTILITY LEVEL MOD2

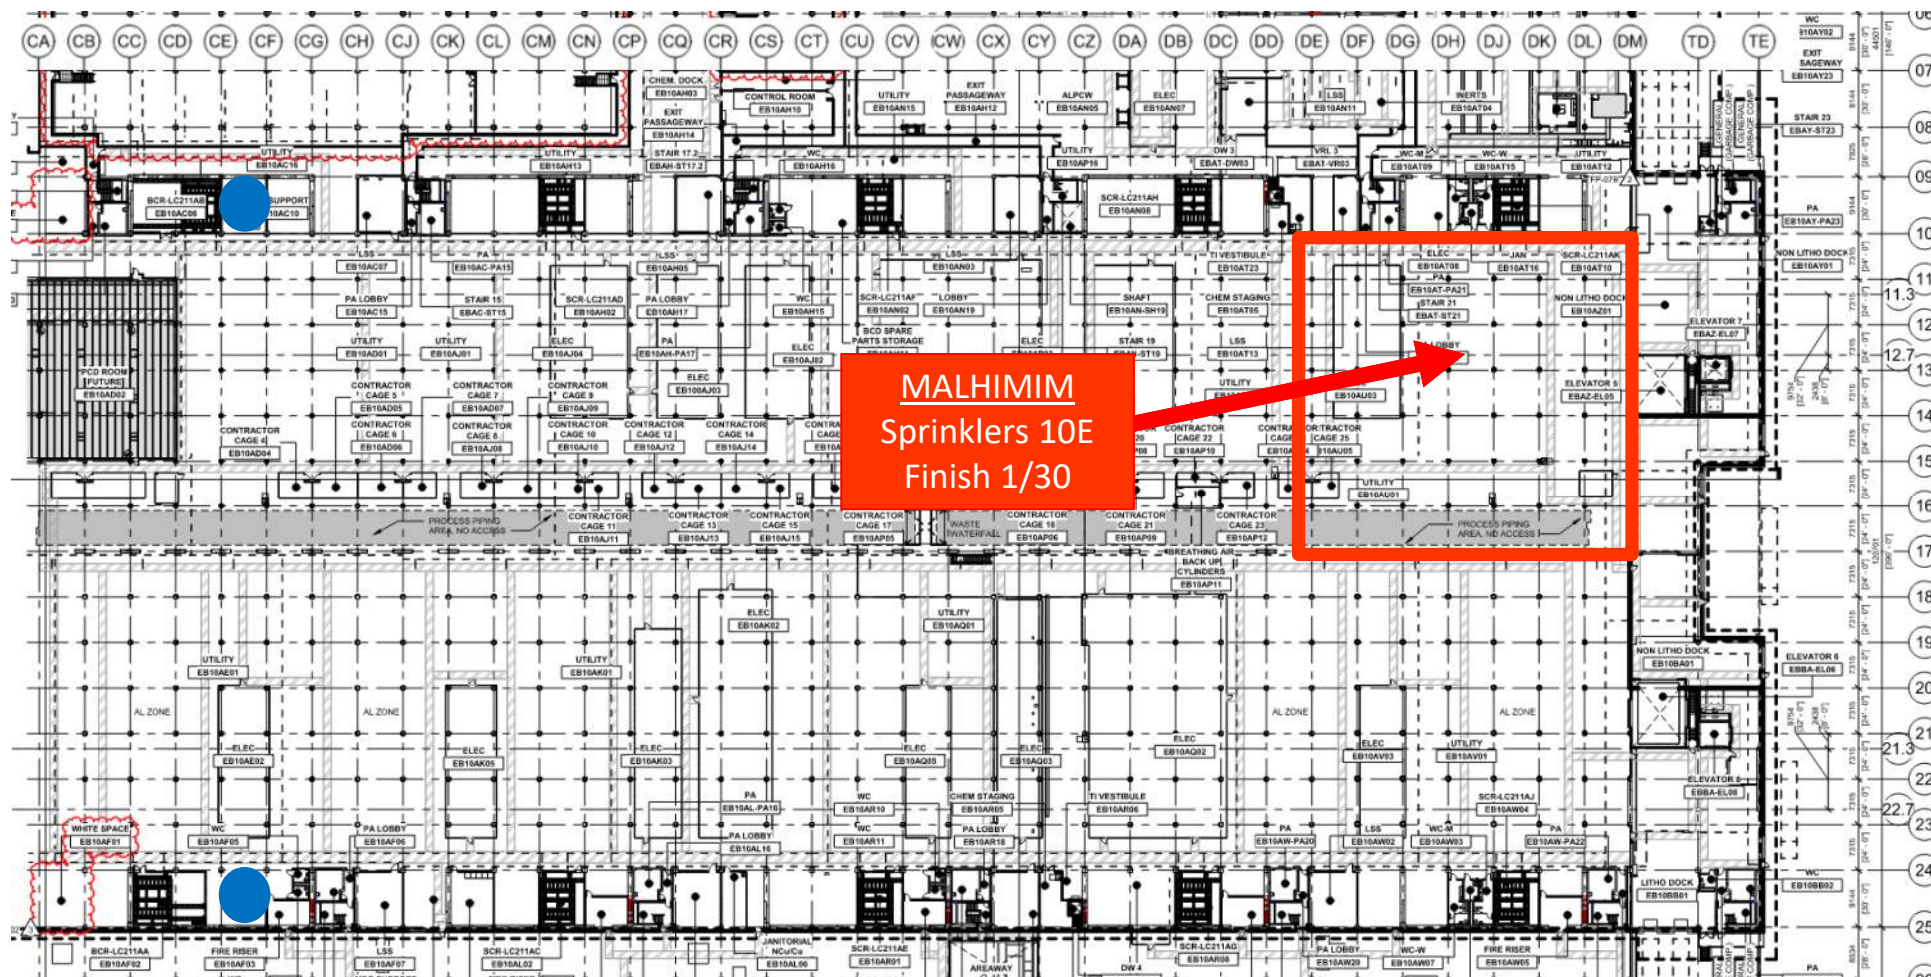

SUT Center+West
M.B pressure test
17:00- 2:00

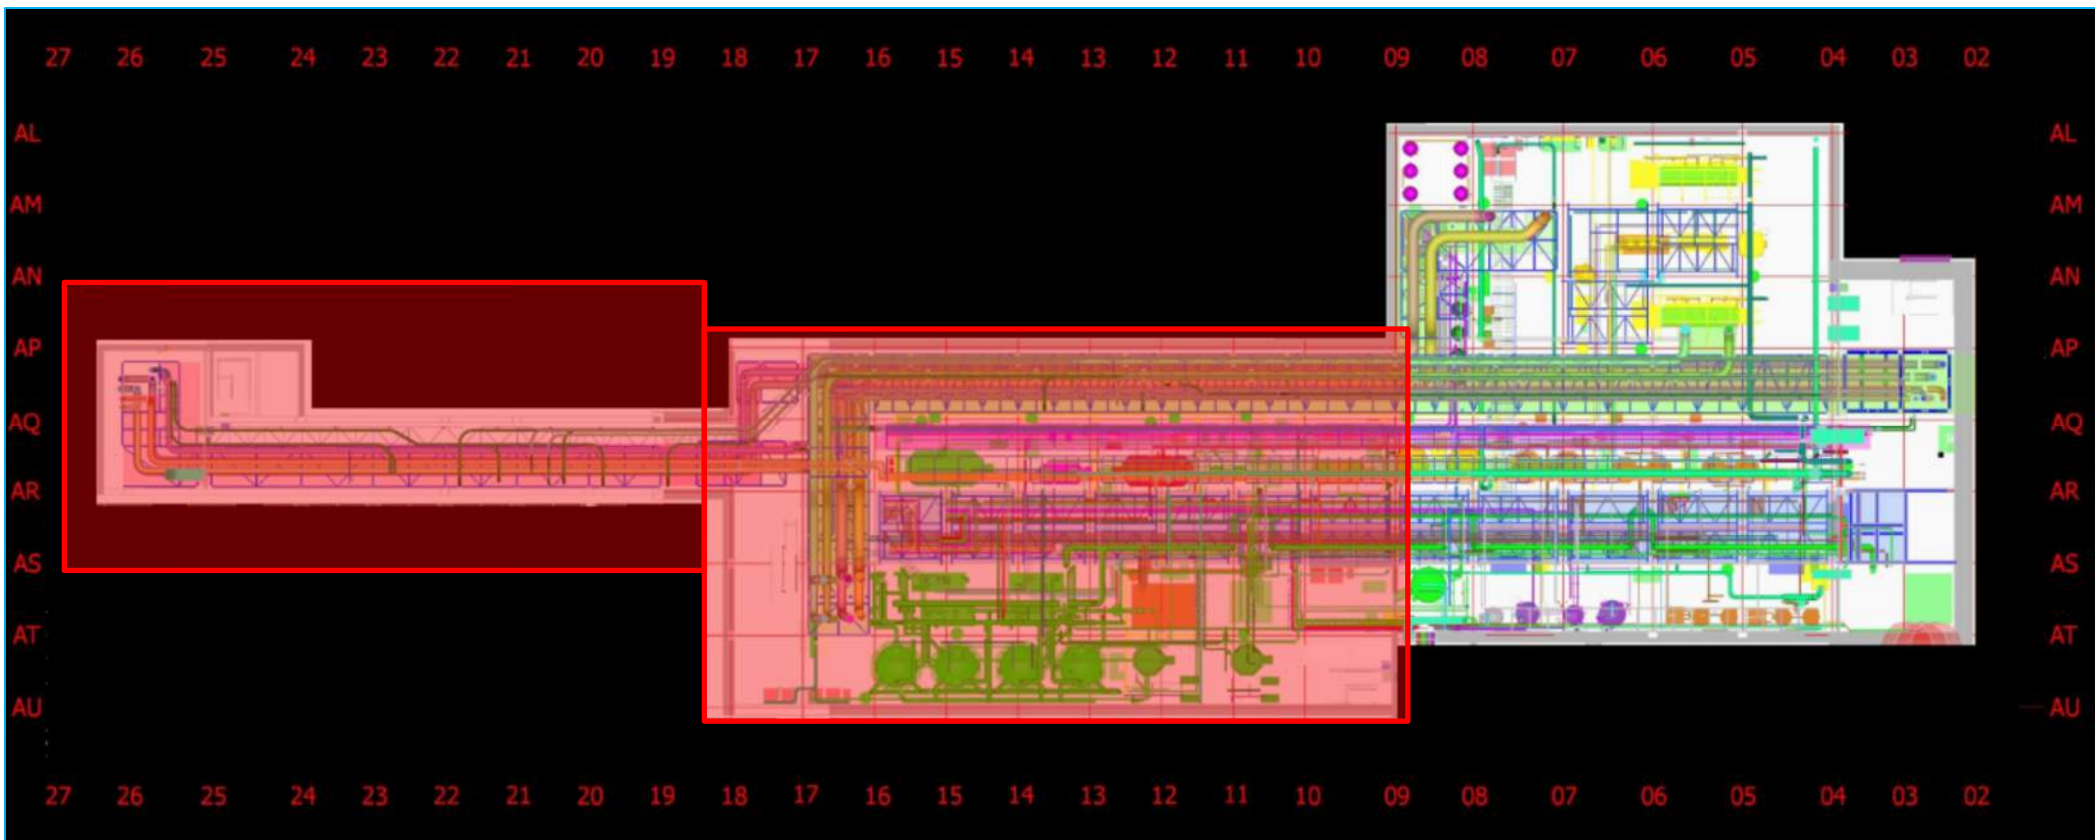

SUT 38.1 LEVEL

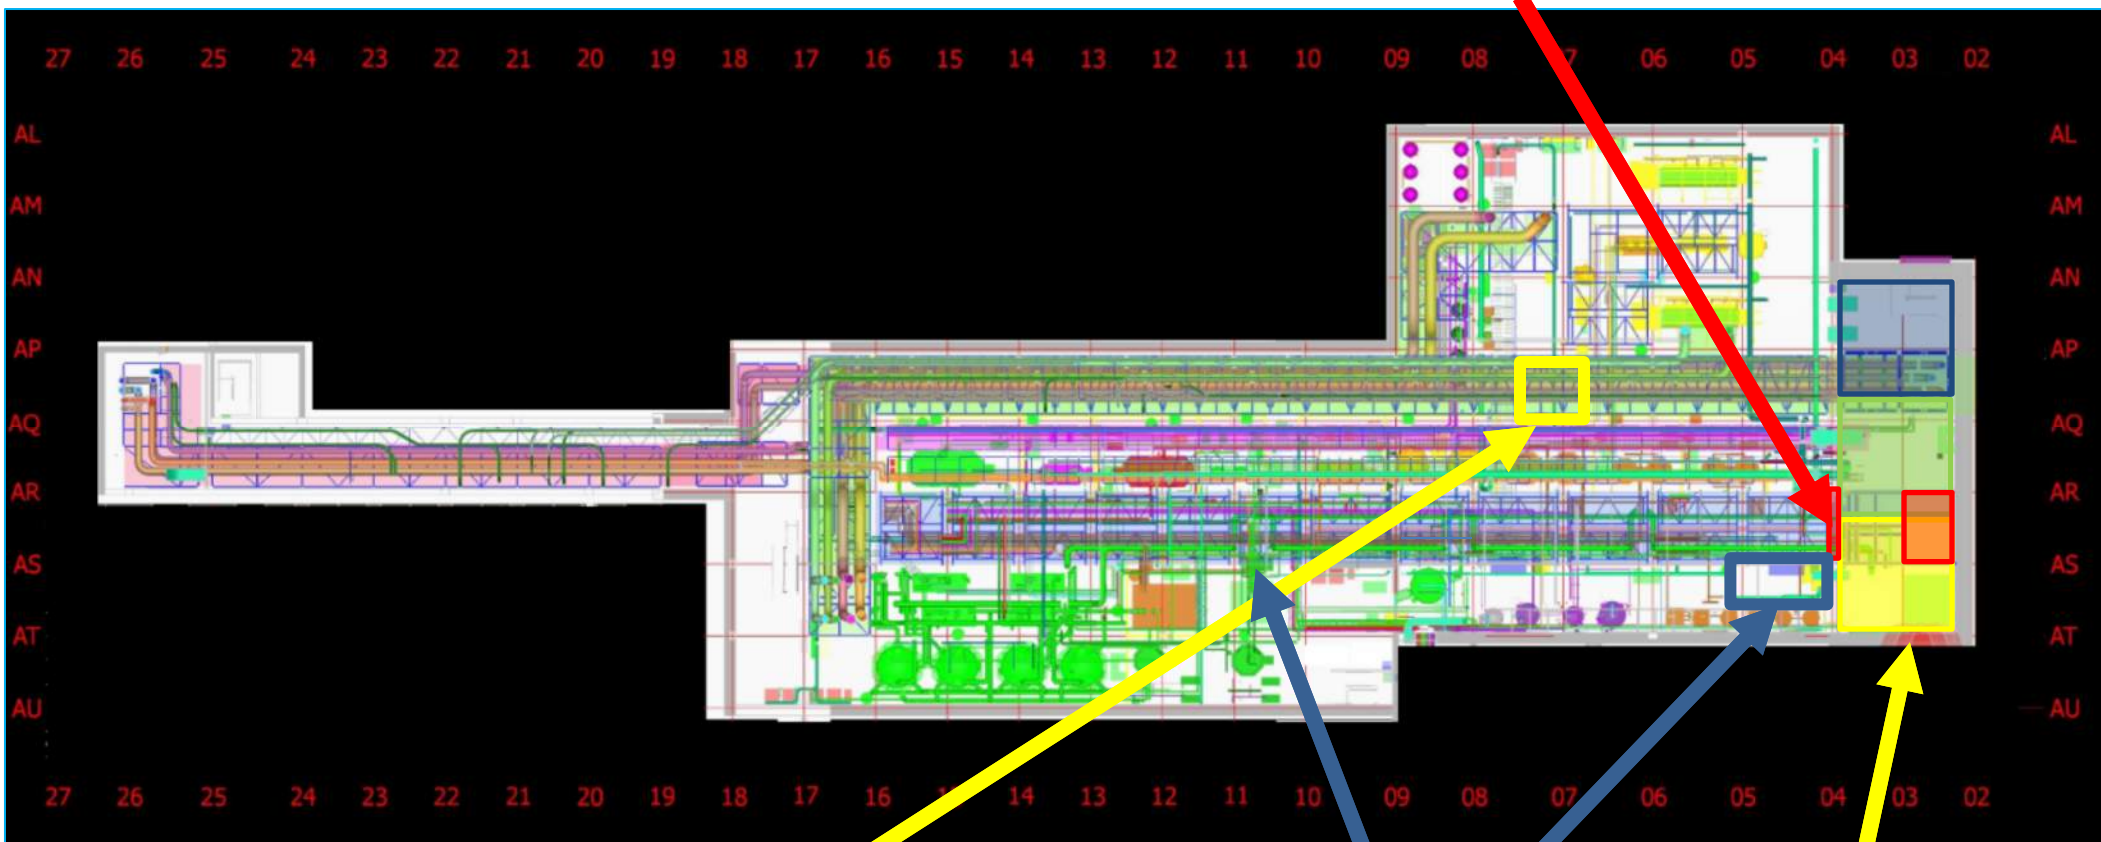

OH roll-up door
Install 30/1

CRC

HYG
Need to install SOG platform +
Bodice Grating ASAP

Topping slab Schedule


Pour 1 – 1/9 – 1/15 V
Pour 2 – 1/15 – 1/22 V
Pour 3 -1/22-1/27 V
Pour 4 – 1/28-2/4



HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

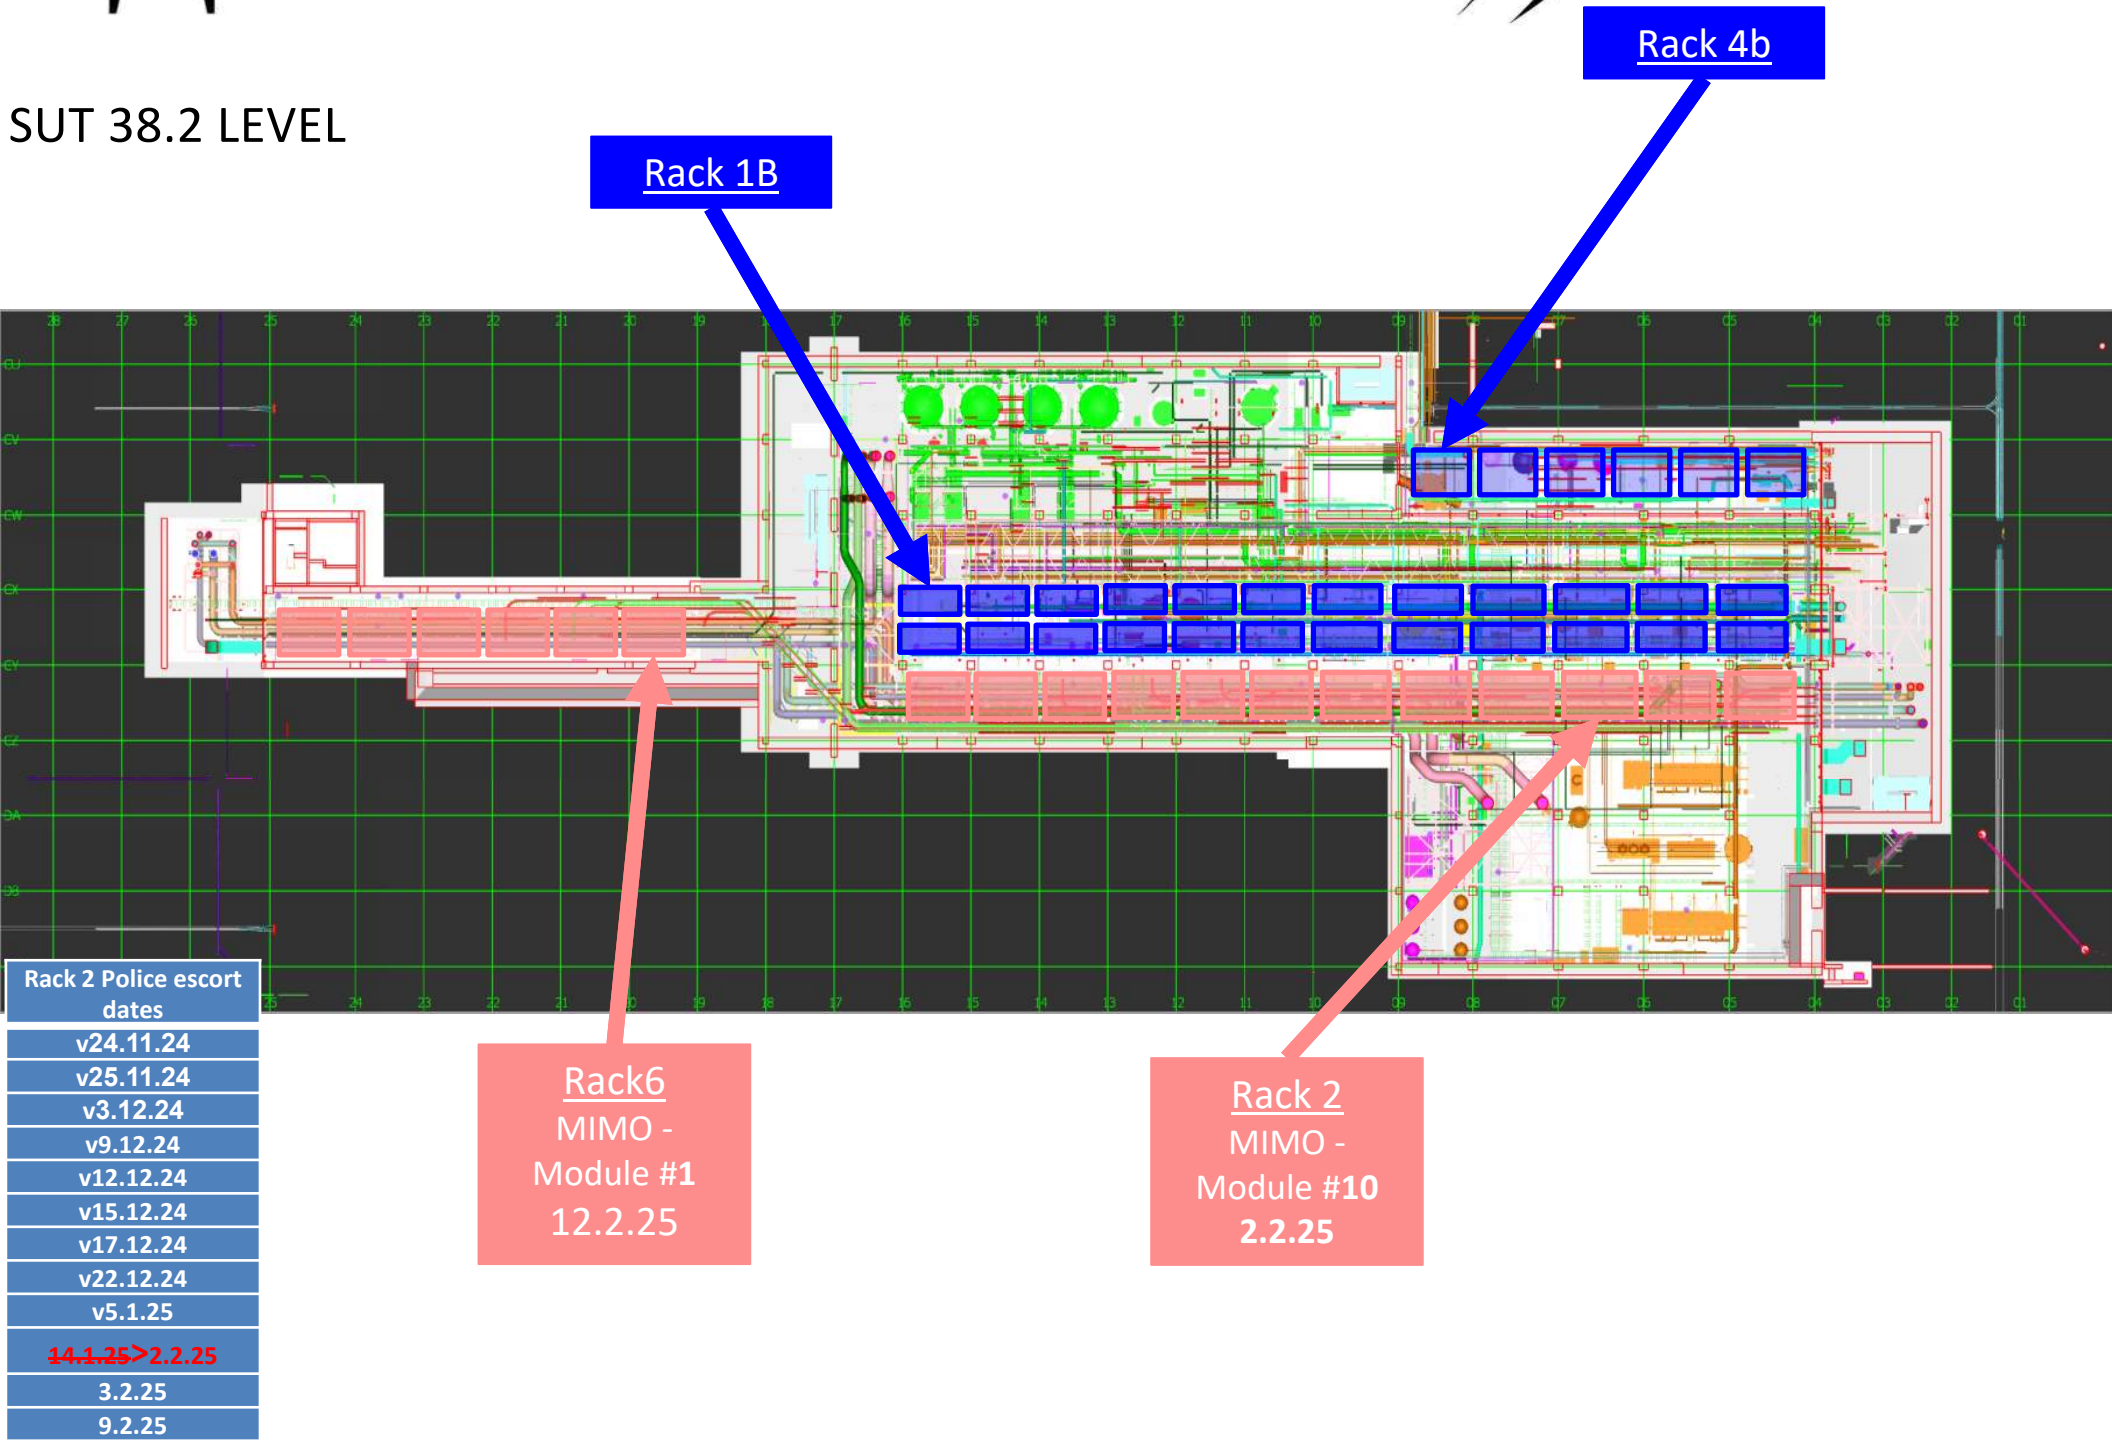

Rack 1B

Rack 4b

Rack 6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25

Rack 2 Police escort
dates

v24.11.24

v25.11.24

v3.12.24

v9.12.24

v12.12.24

v15.12.24

v17.12.24

v22.12.24


v5.1.25

~~14.1.25~~ > 2.2.25


3.2.25

9.2.25


SUBFAB BUILDOUT MOD 1

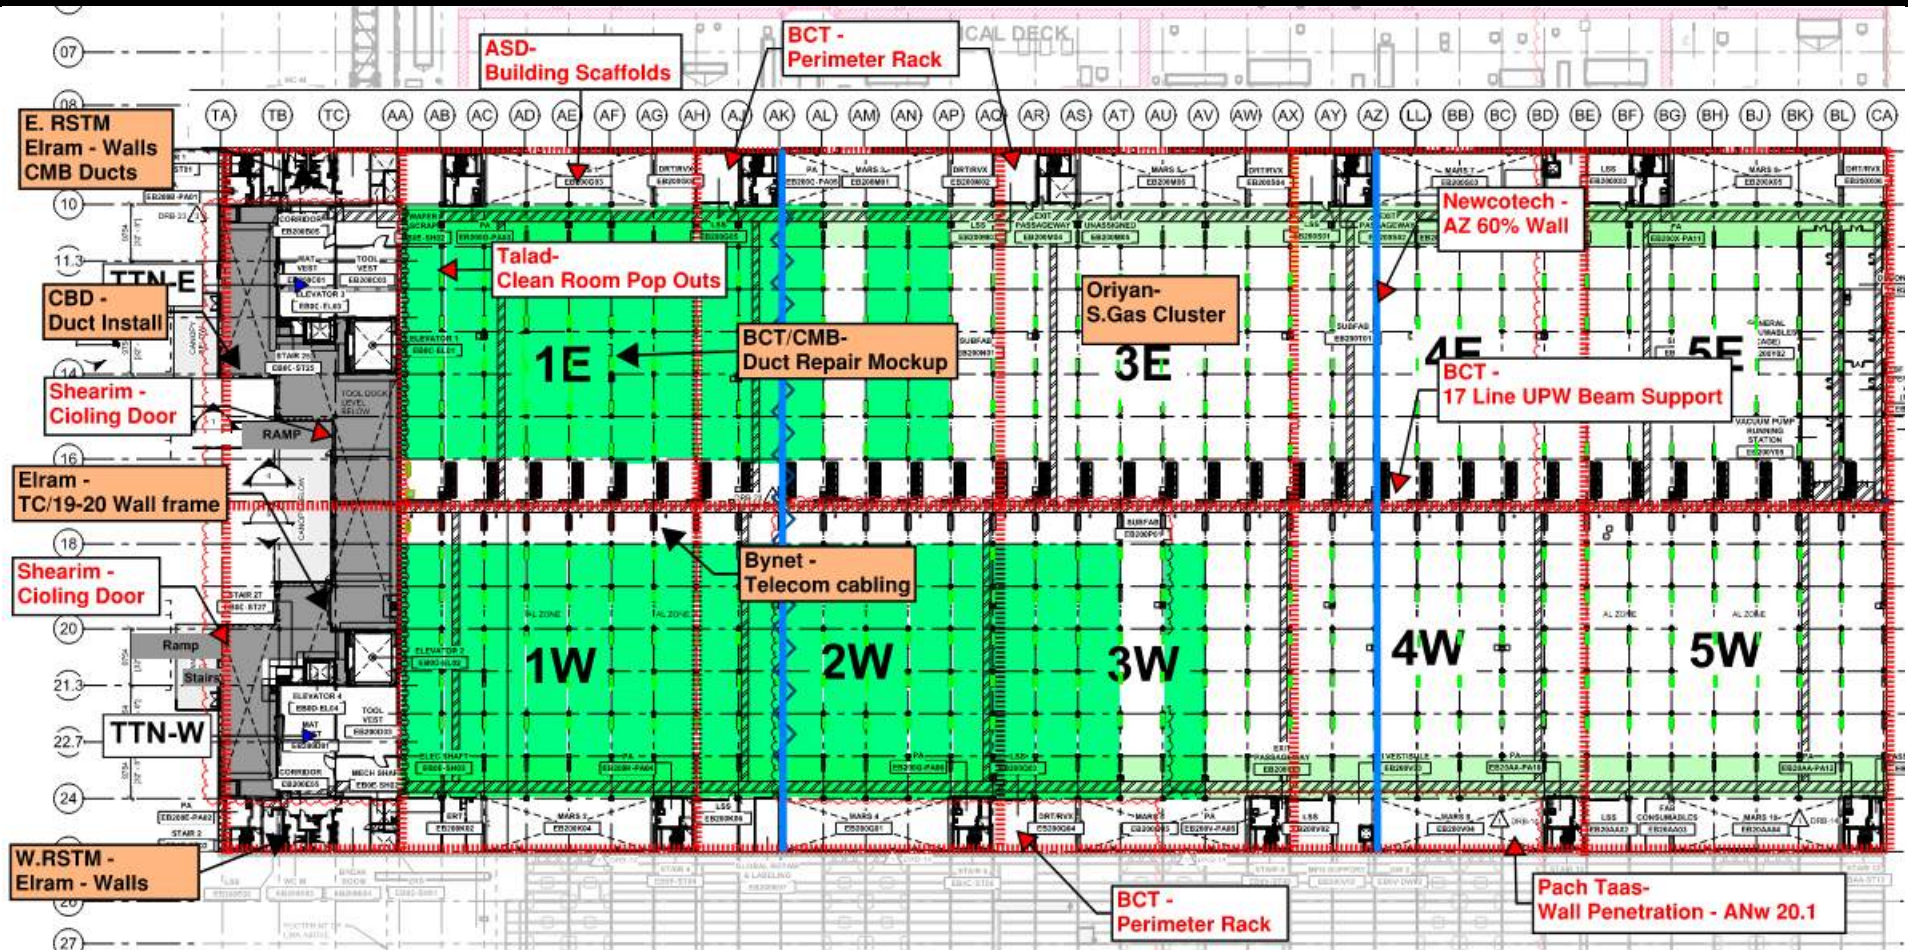


SUBFAB CRC TOPCOAT

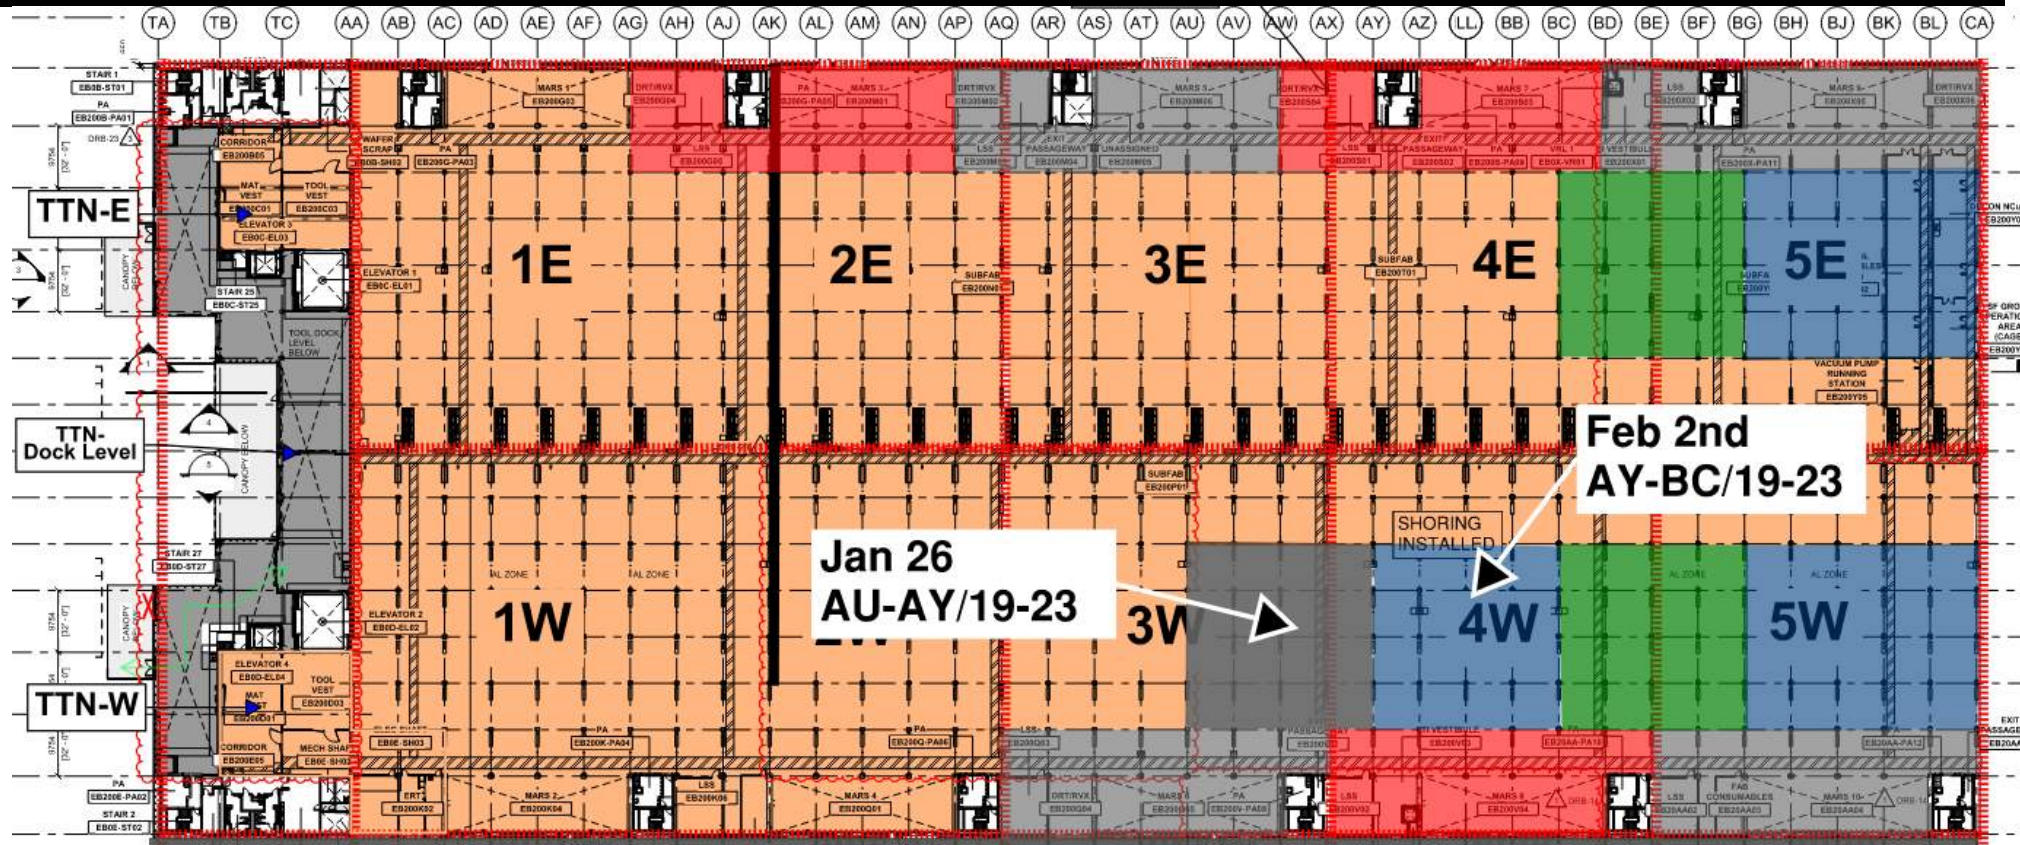


BCT Pressure Test Today

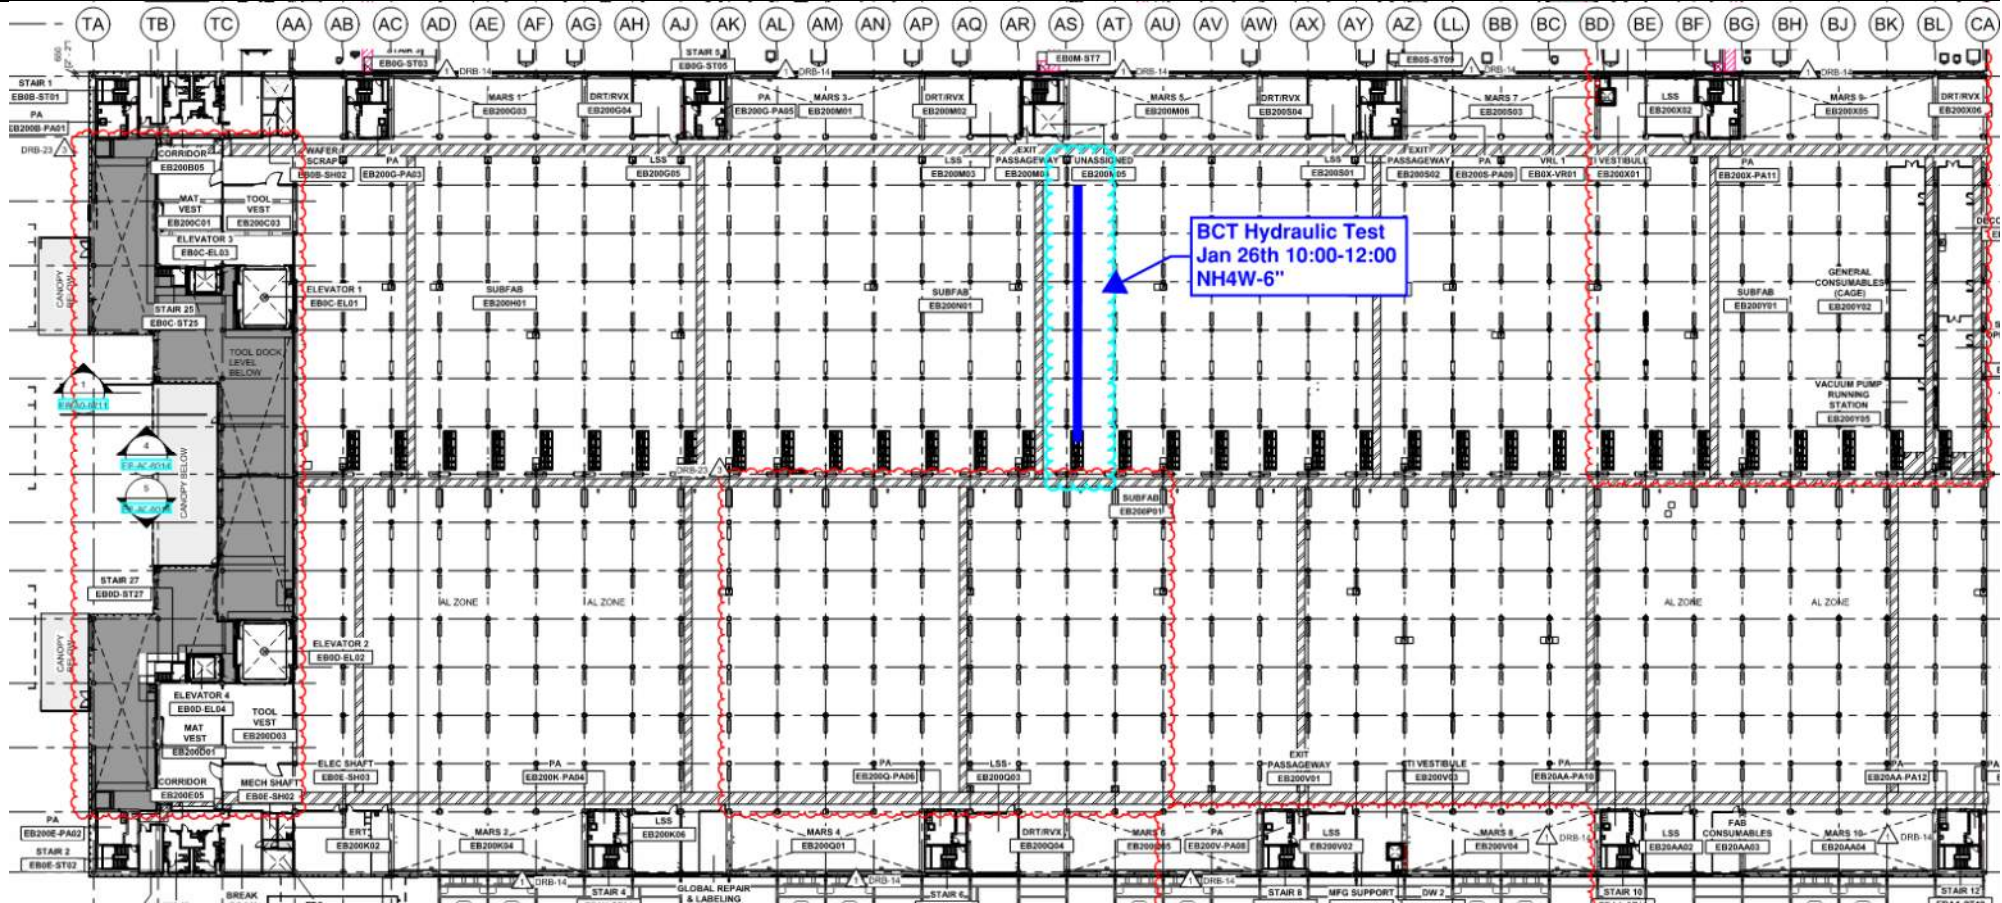



BCT Pressure Test Tomorrow

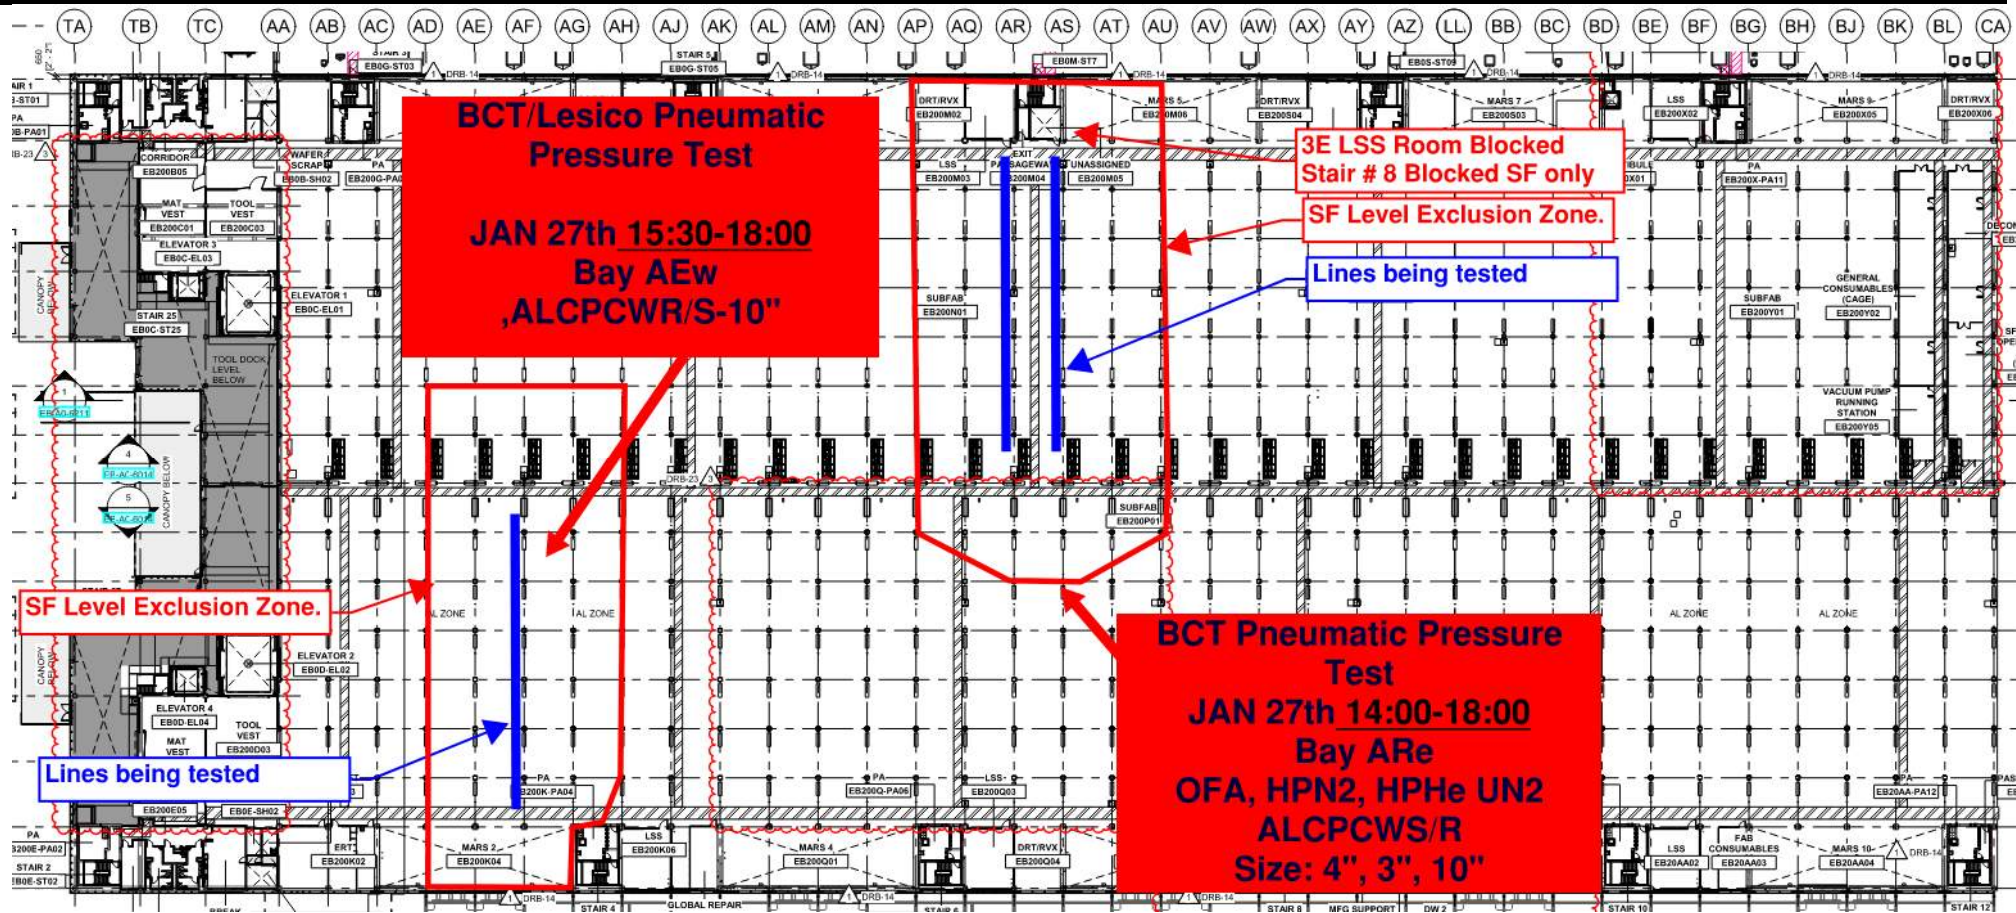



SUBFAB BUILDOUT MOD 2

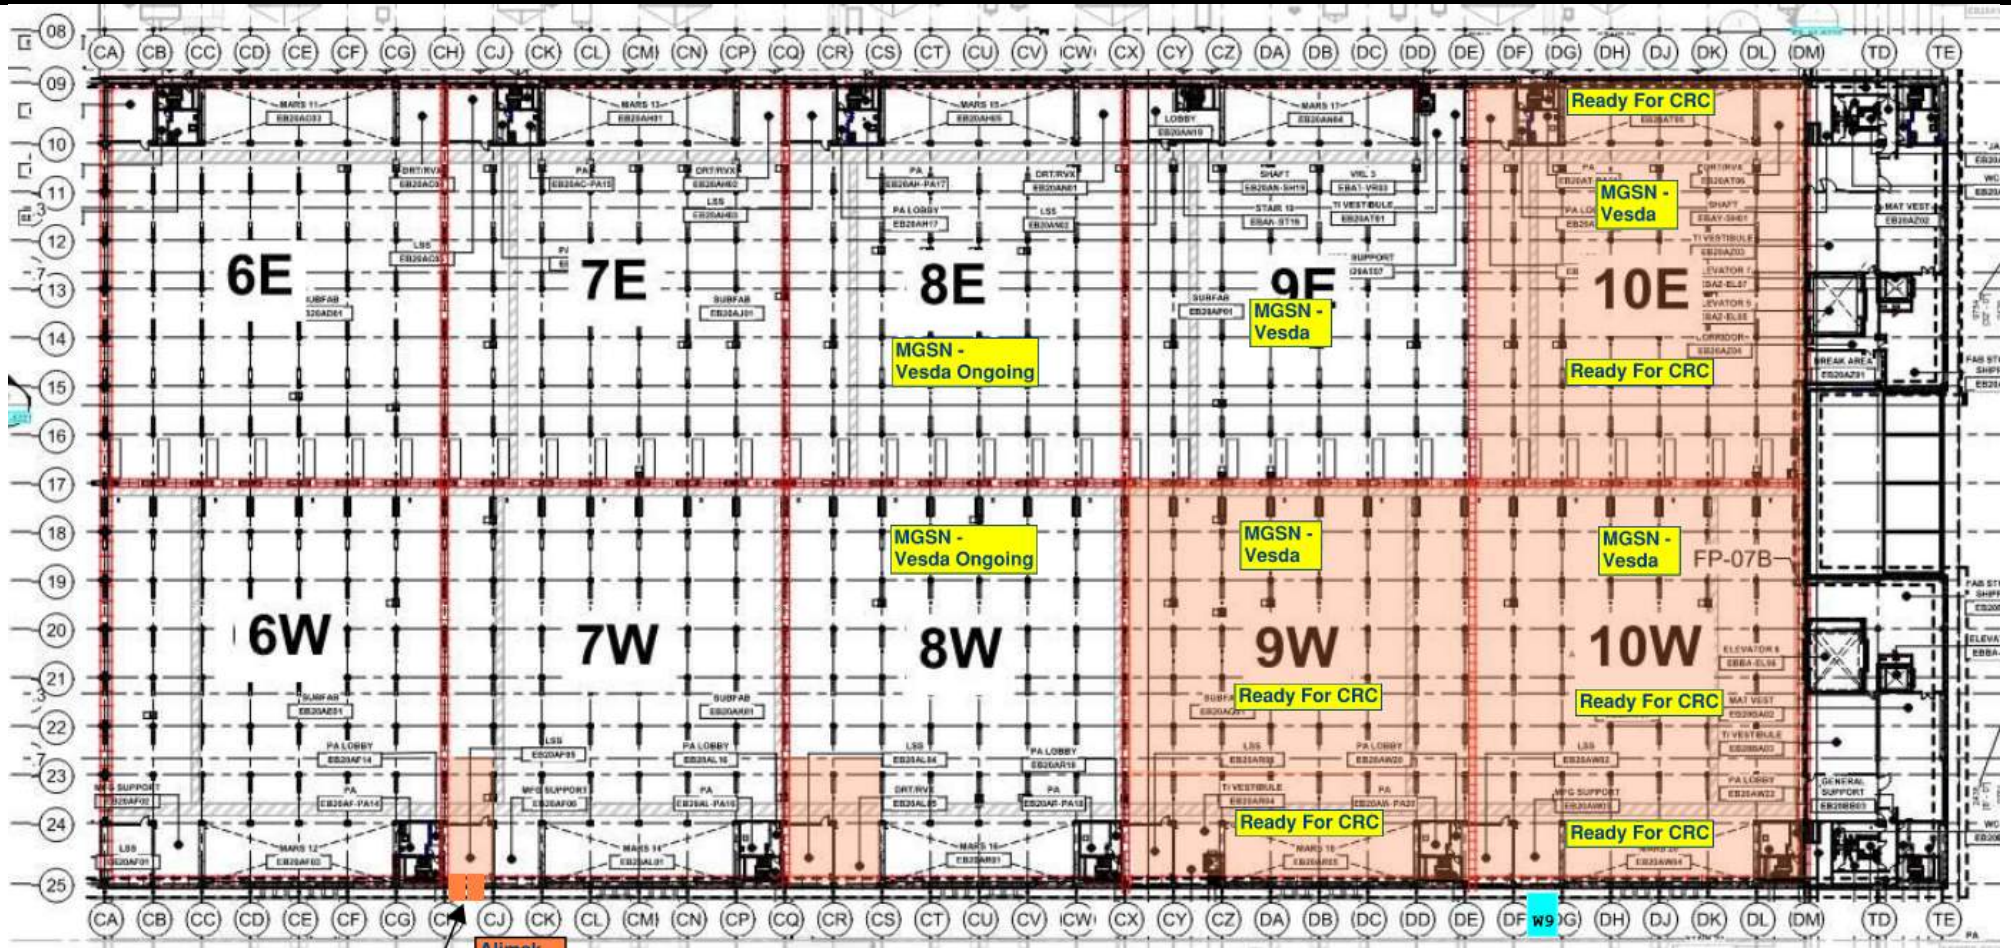

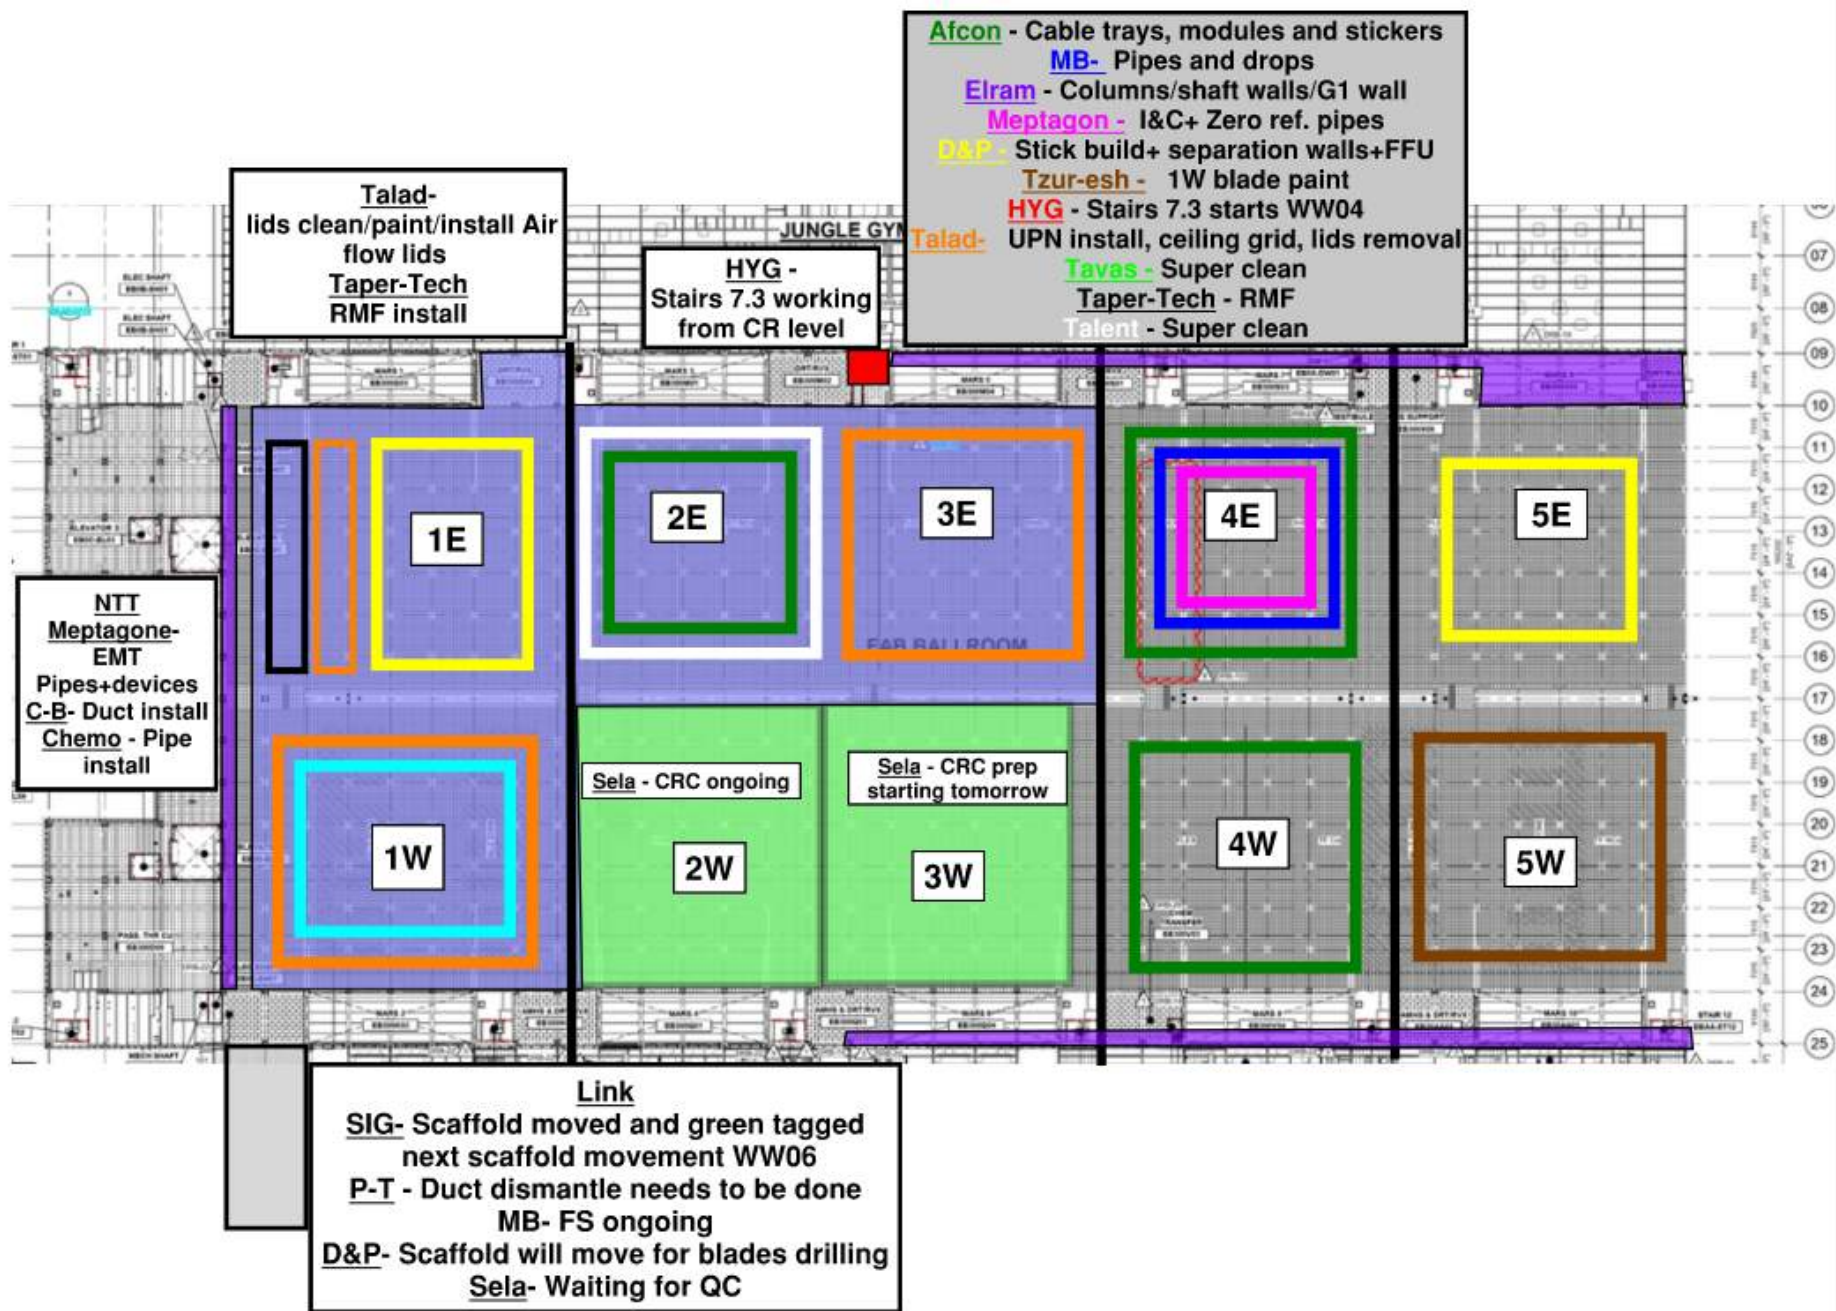

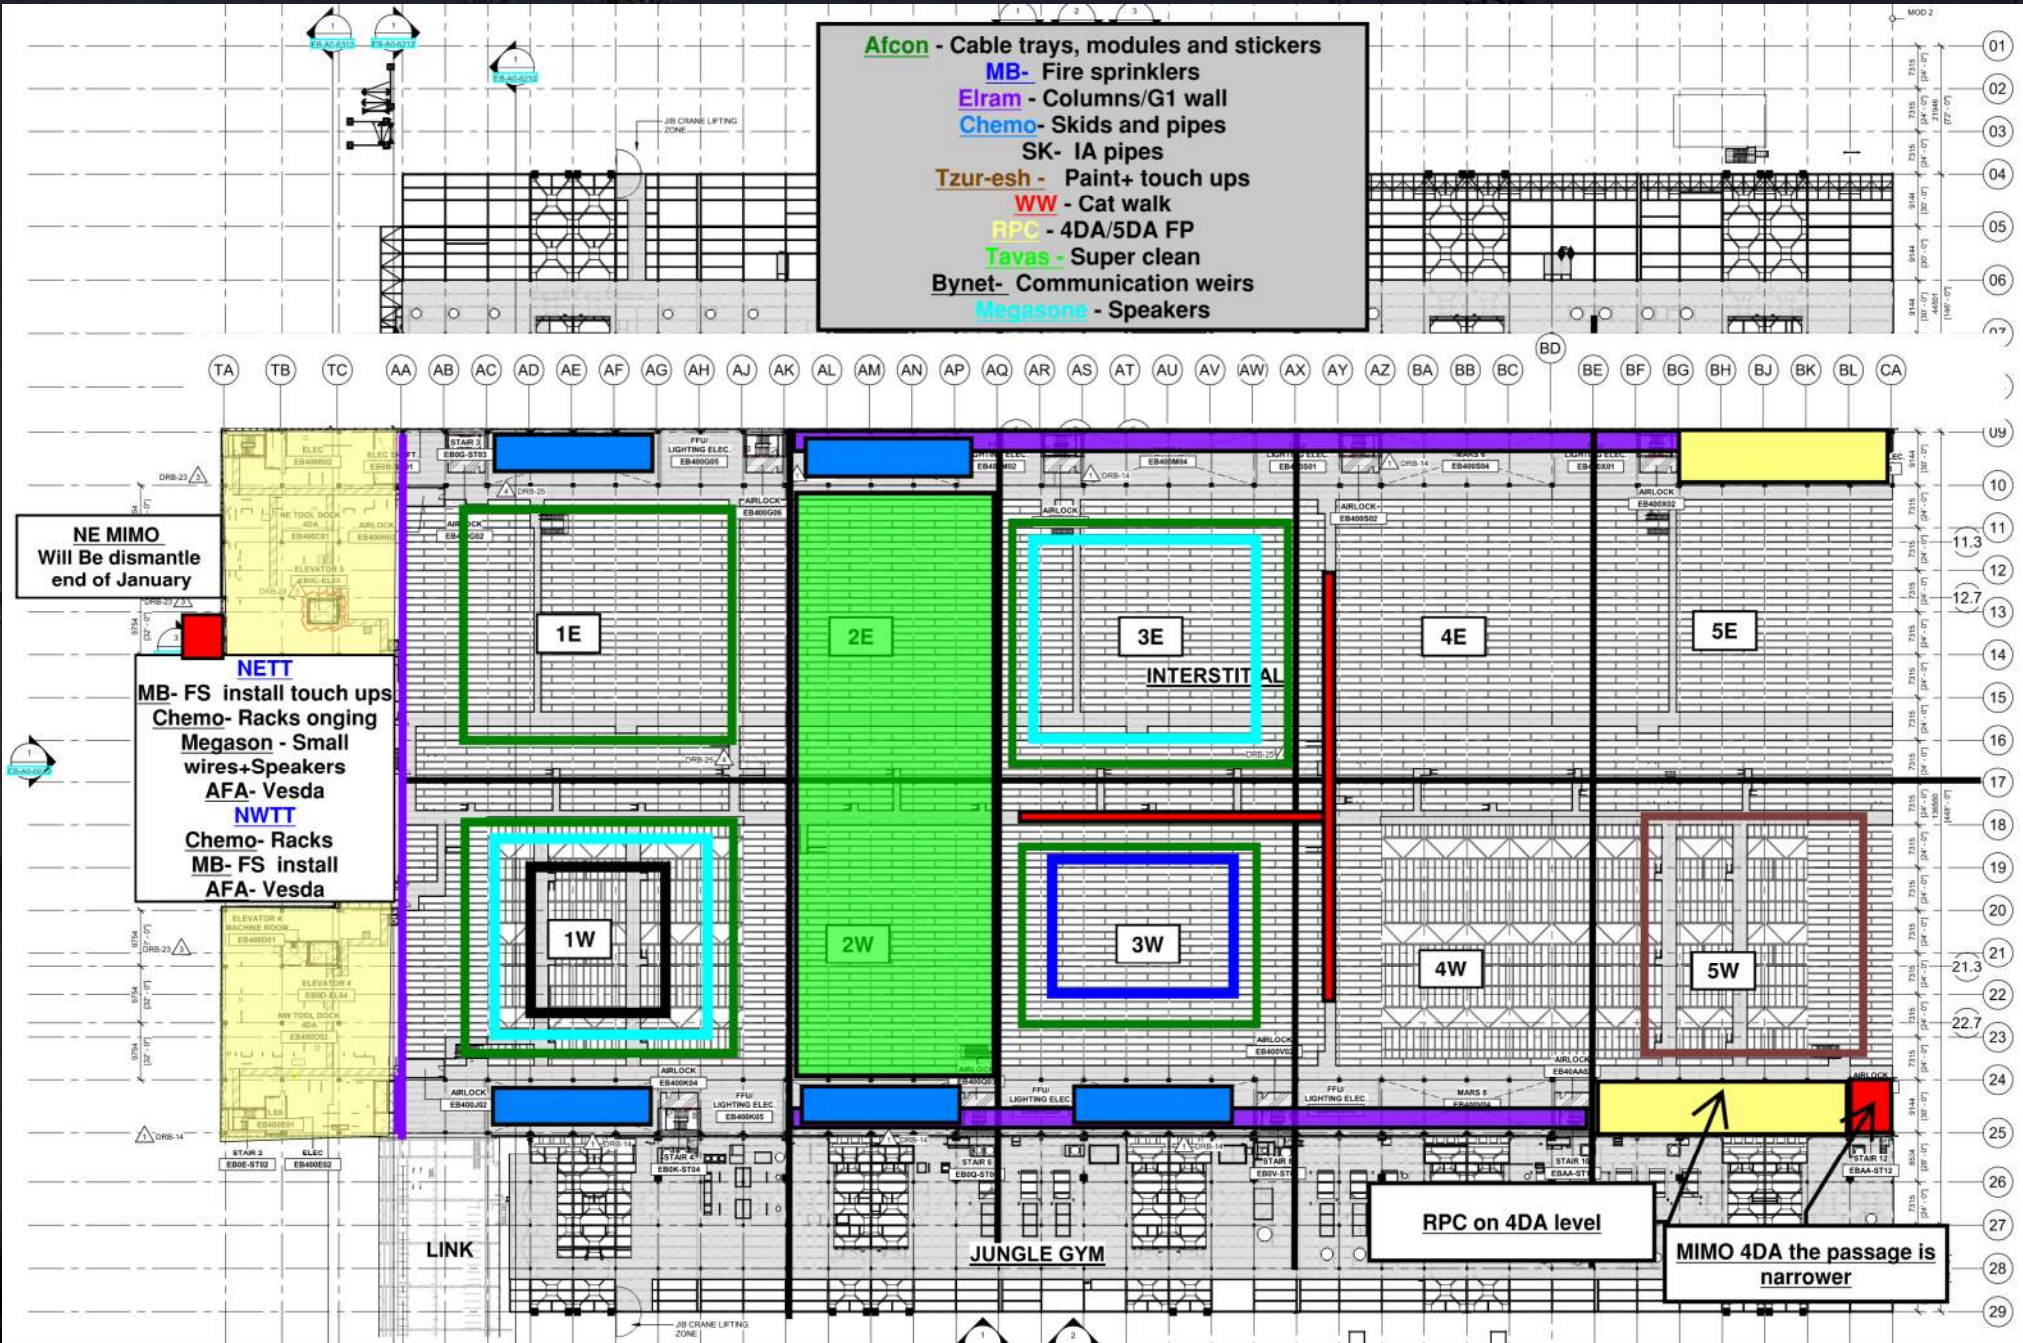

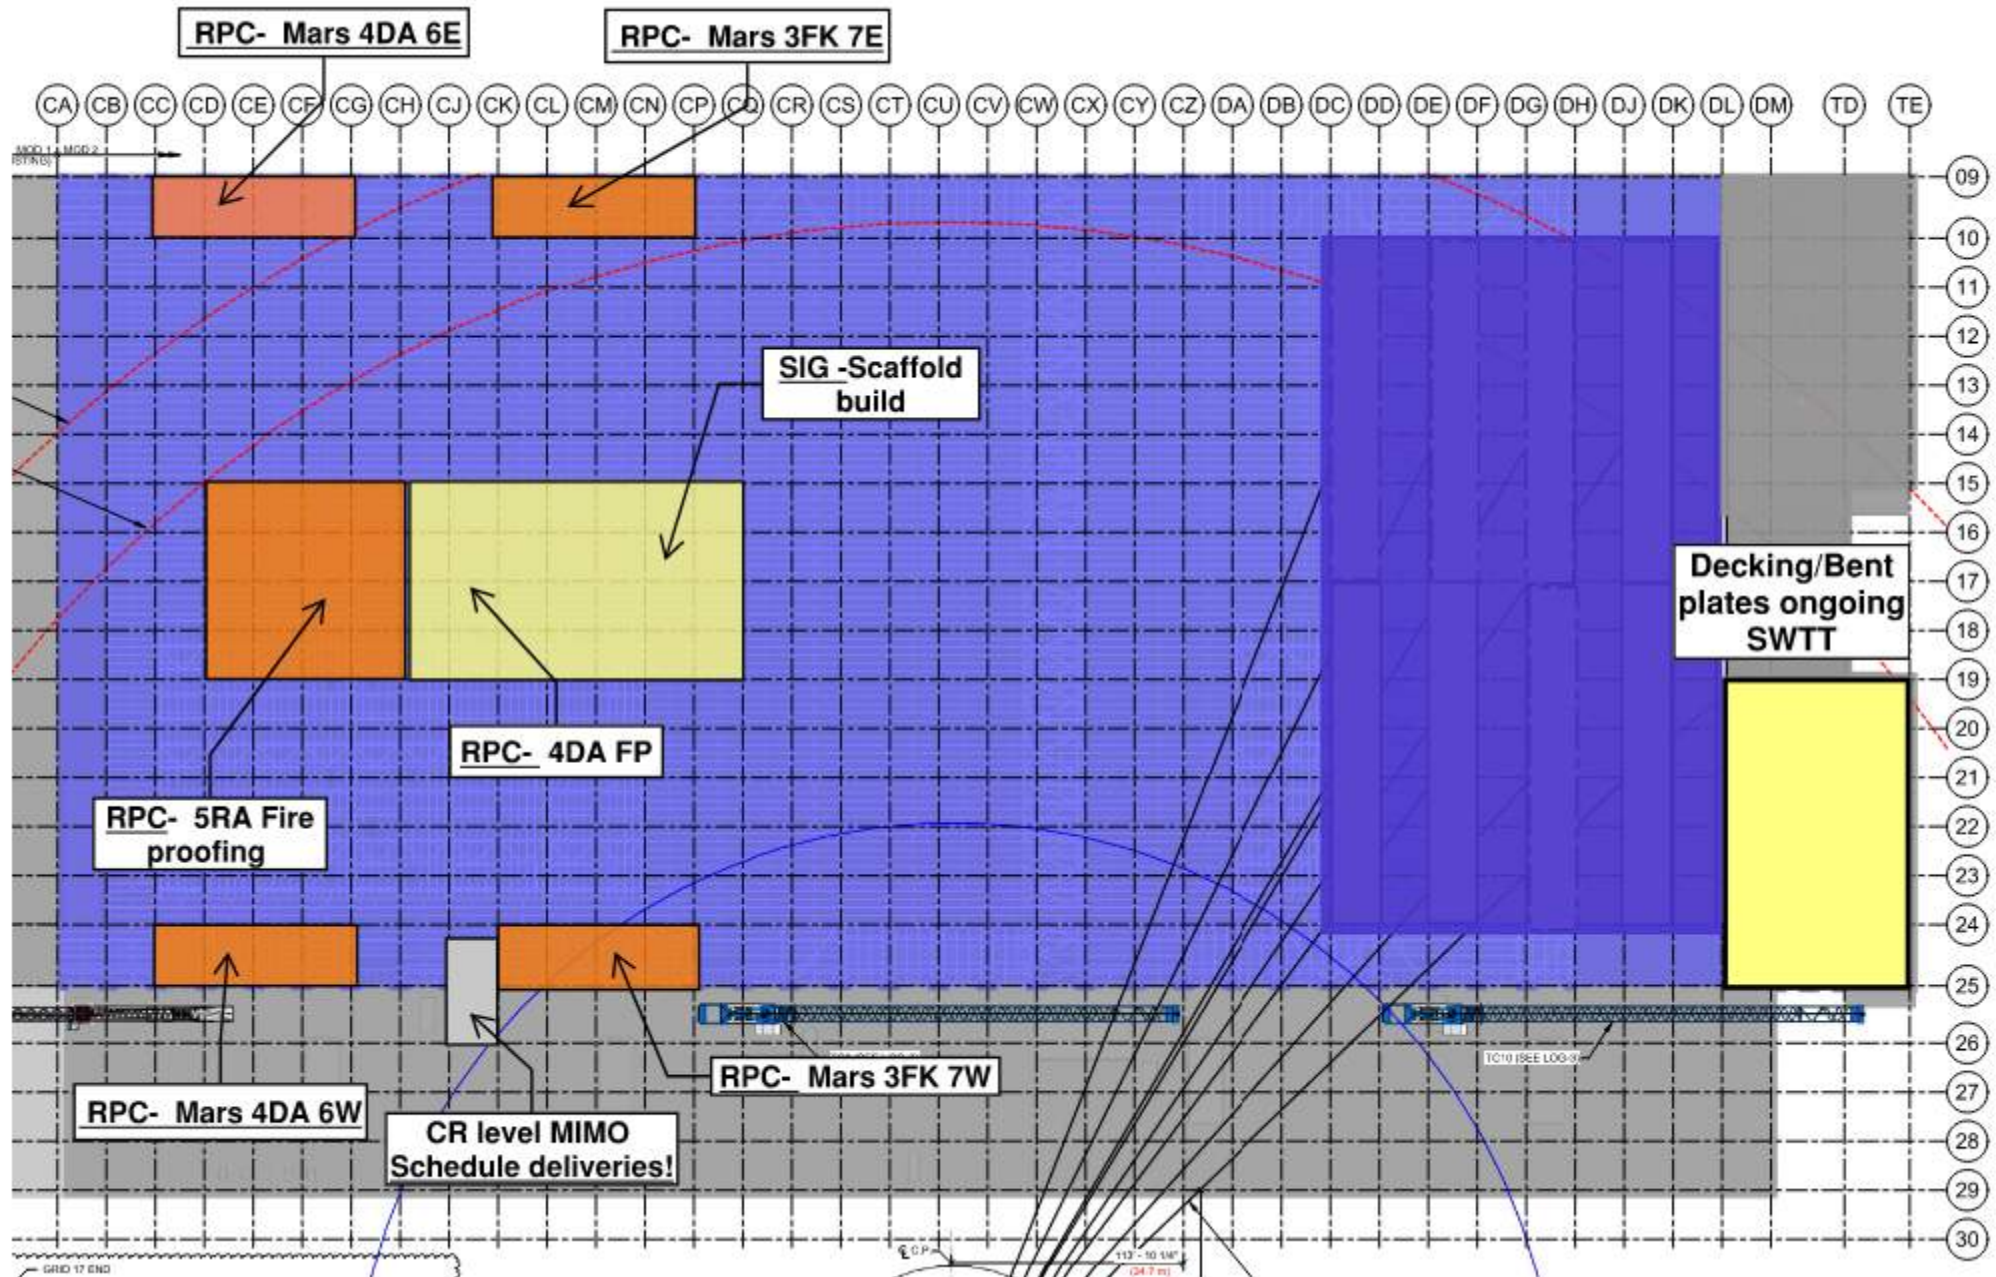



Wall Of Shame

Afcon



M-B



Elram



BLOWDOWN 30%


[illegible]

[illegible]

Siding - North FAB

100% - BLOWDOWN

	9	10	11	12	13	14	TA	TB	TC	14	14.5	15	15.5	16.5	17.5	18.5	19	19.5	20	TC	TB	TA	20	21	22	23	24	25											
Total Installed %	901C / 901C						911A / 912A						911B / 912B						911C / 912C						1011C / 1012C						1011B / 1012B			1011A / 1012A			1001C / 1002C		
	29	29	29	29	29	29	29	29		27	18	9	27	27	27	27	27	9	18	29	29	29	29	29	29	29	29	29											
	100%	100%	45%	0%	0%		100%	100%		100%	100%	100%	100%	100%	100%	100%	30%	100%	0%	100%	100%		100%	100%	100%	100%	100%	100%											
29	1	1	0				1	1												1	1		1	1	1	1	1	1											
28	1	1	0				1	1												1	1		1	1	1	1	1	1											
27	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
26	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
25	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
24	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
23	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
22	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
21	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
20	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
19	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
18	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
17	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
16	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
15	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
14	1	1	0				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
13	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
12	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
11	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
10	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
9	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
8	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
7	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
6	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
5	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
4	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
3	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
2	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											
1	1	1	1				1	1		1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1											

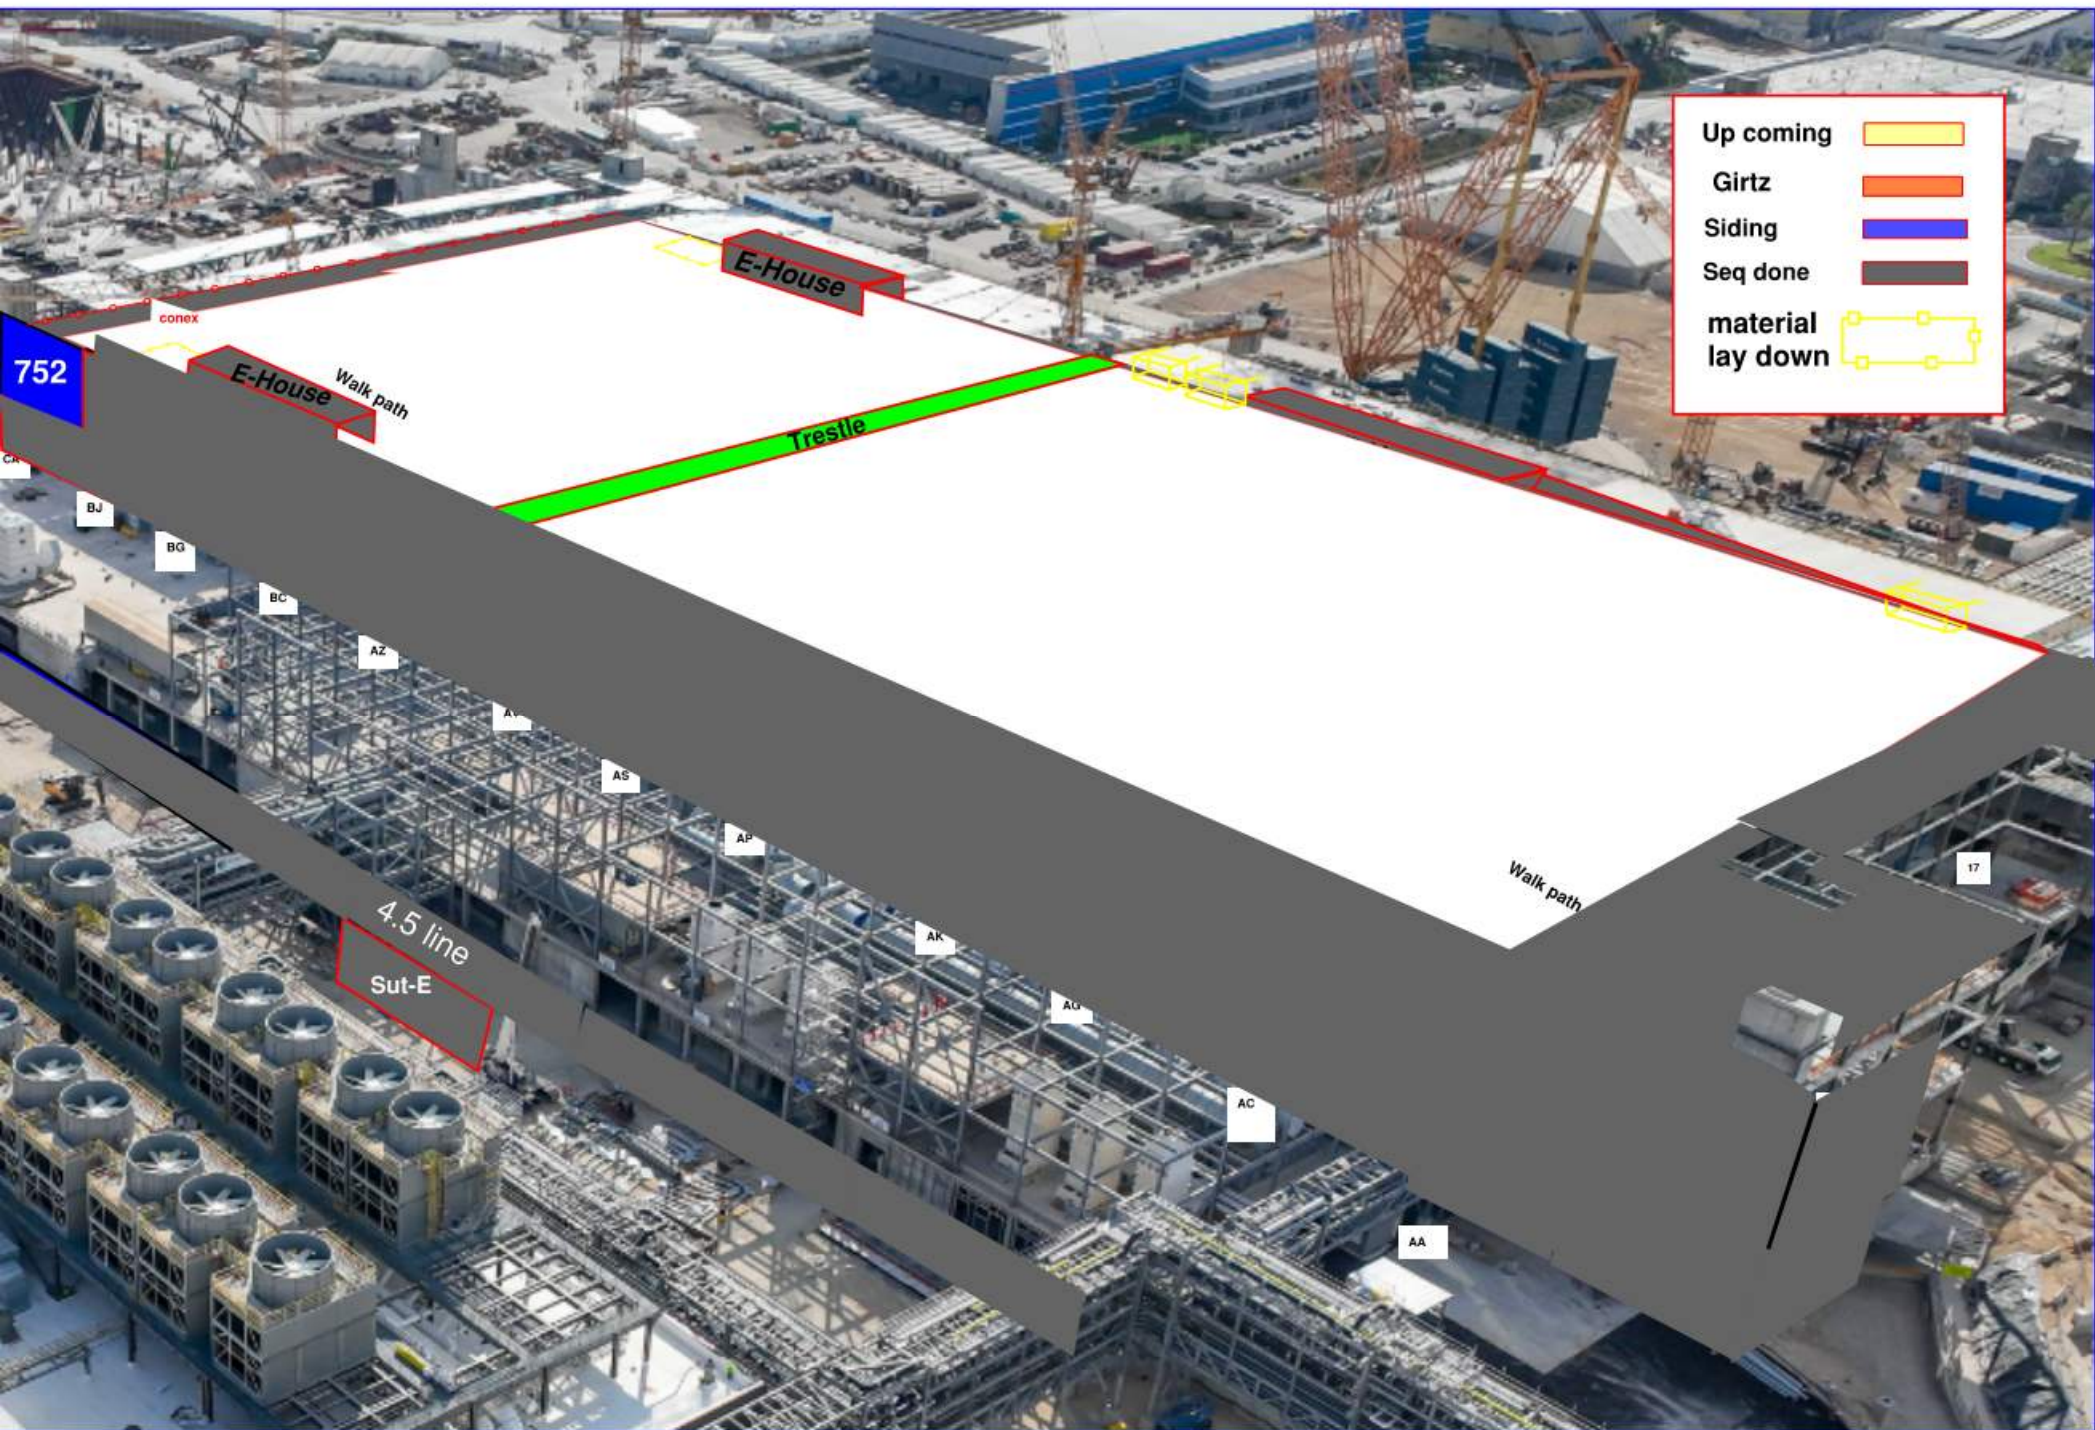

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

752

E-House

E-House

Walk path

Trestle

4.5 line
Sut-E

Walk path

17

BJ

BG

BC

AZ

AV

AS

AP

AK

AU


AC

AA

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

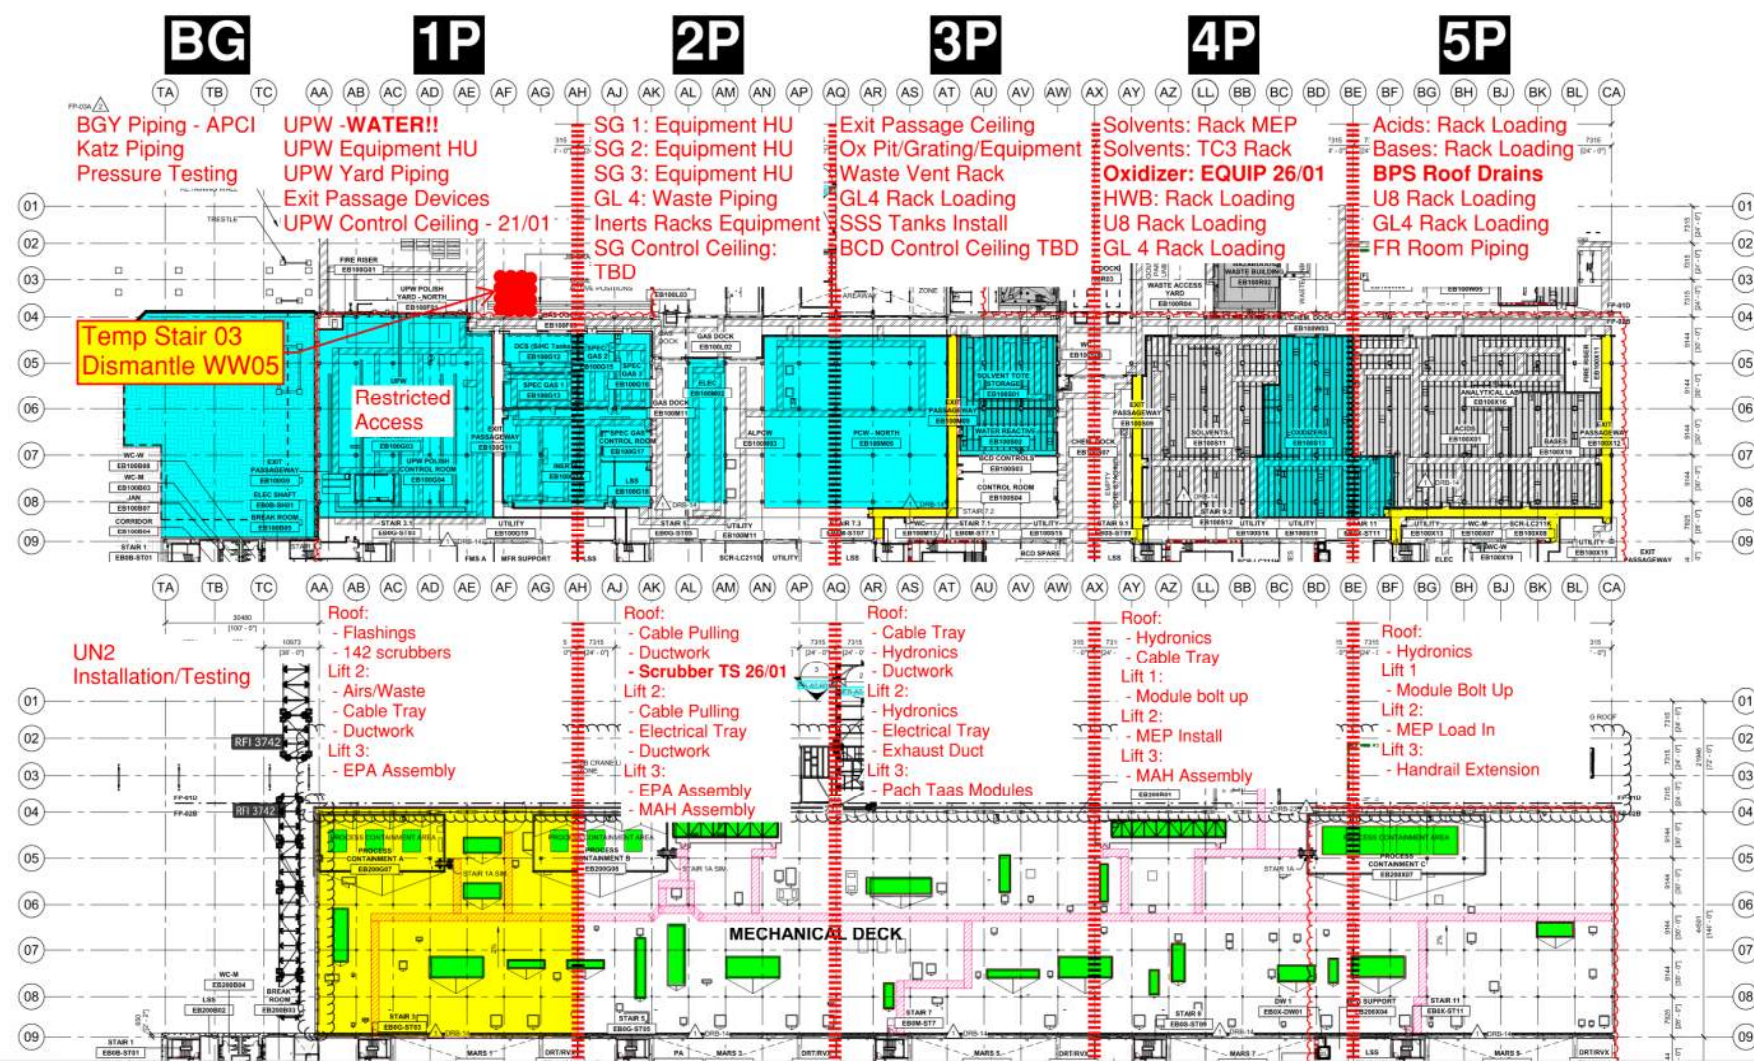


PSSS.2


Utility Level
1YA

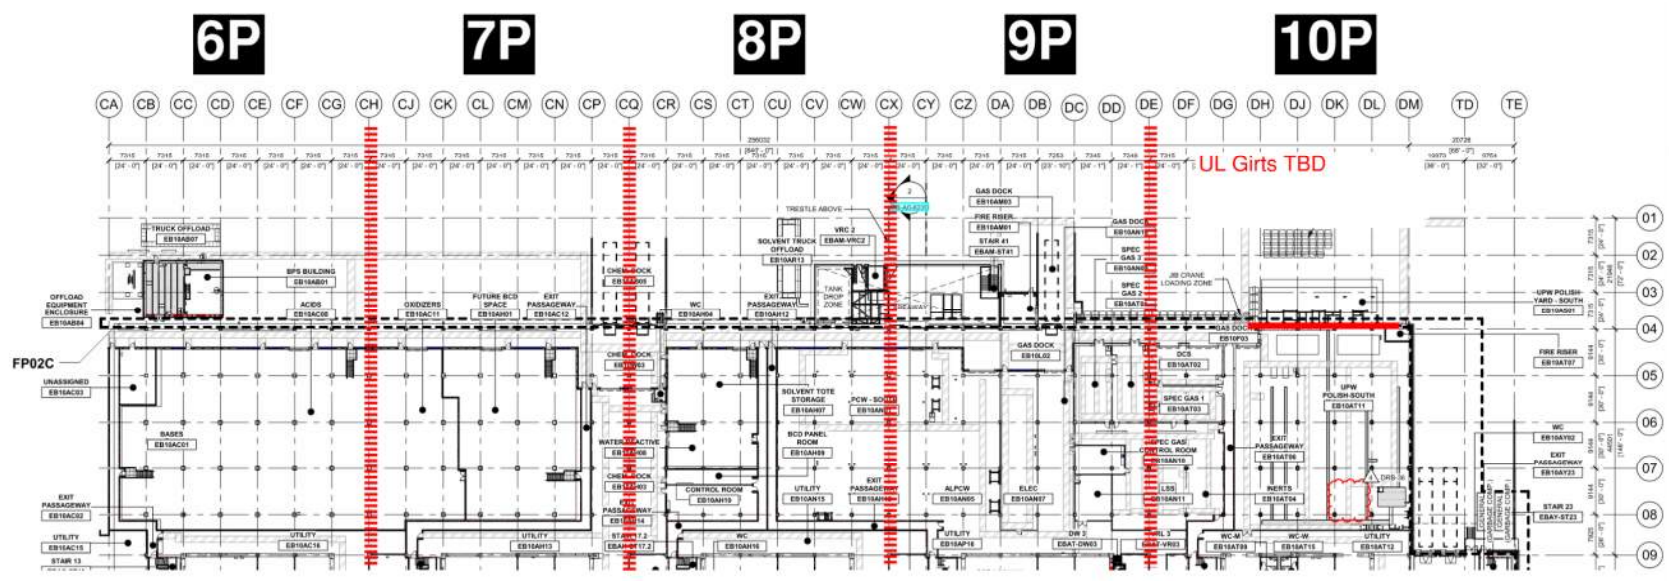


PSSS Roof
2SA

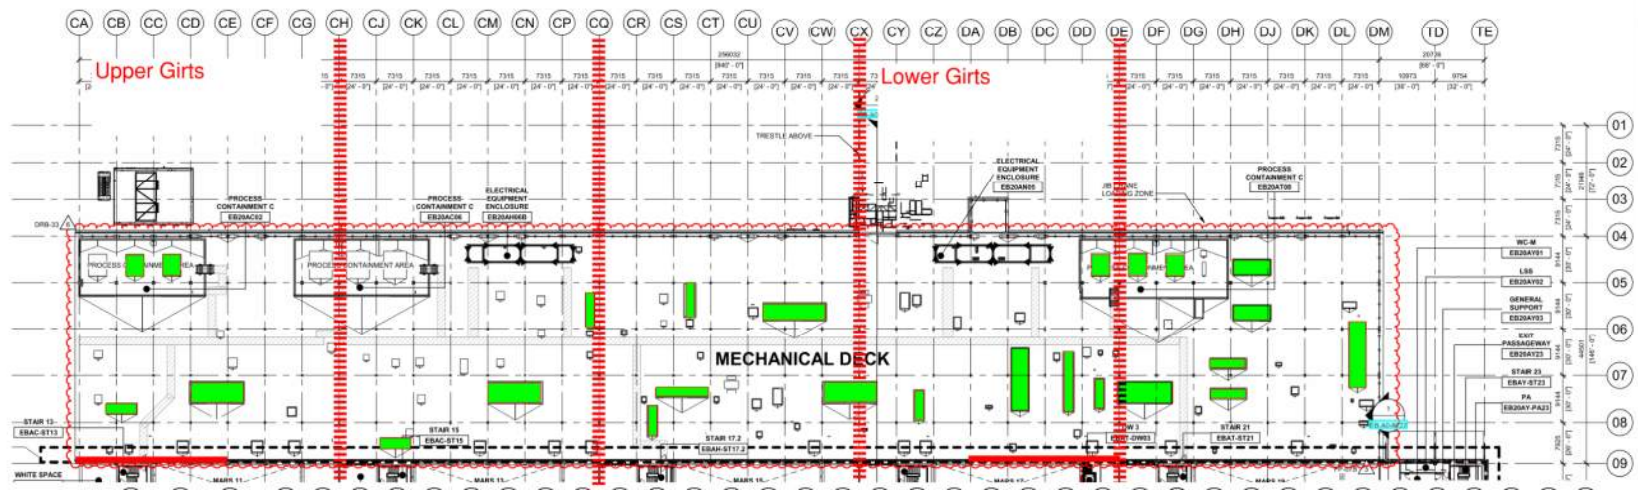



WJG 01J, 02J LIFT 2 & 3

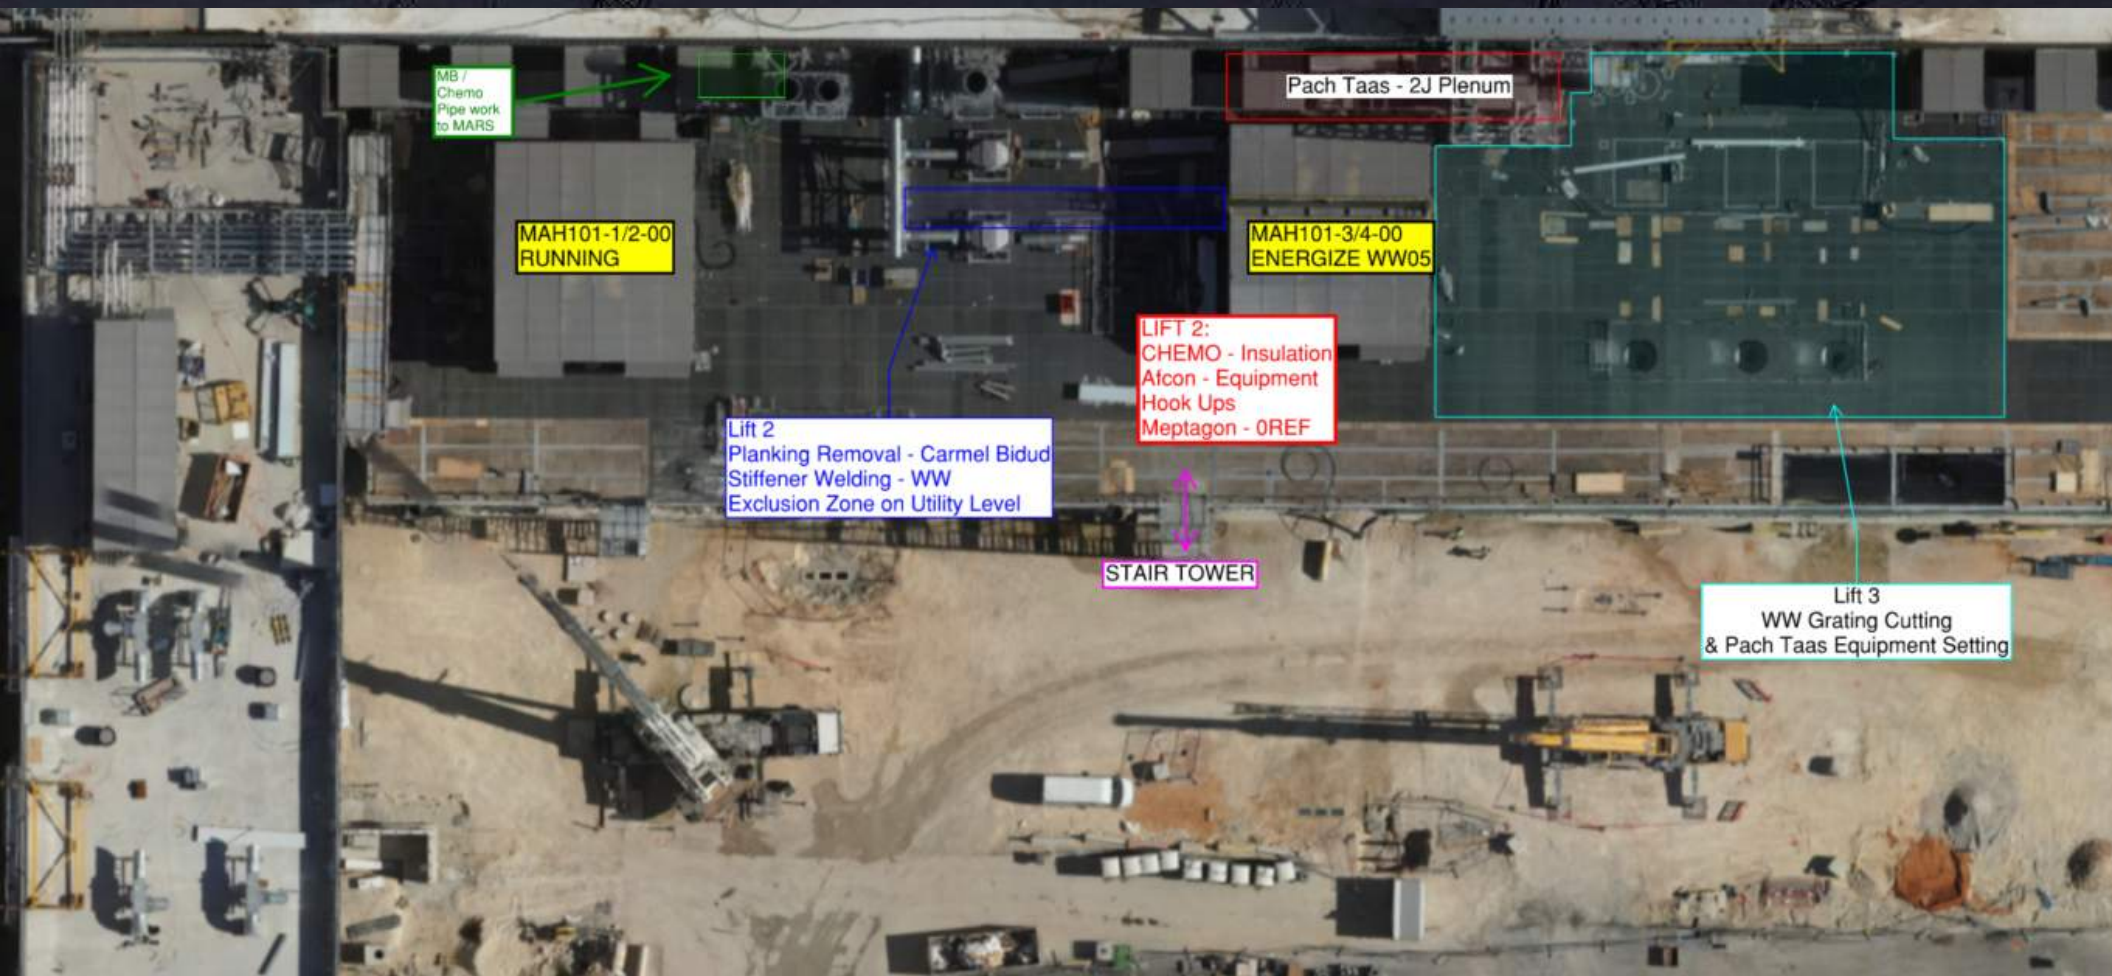





WJG 03J, 04J, 05J LIFT 2 & 3

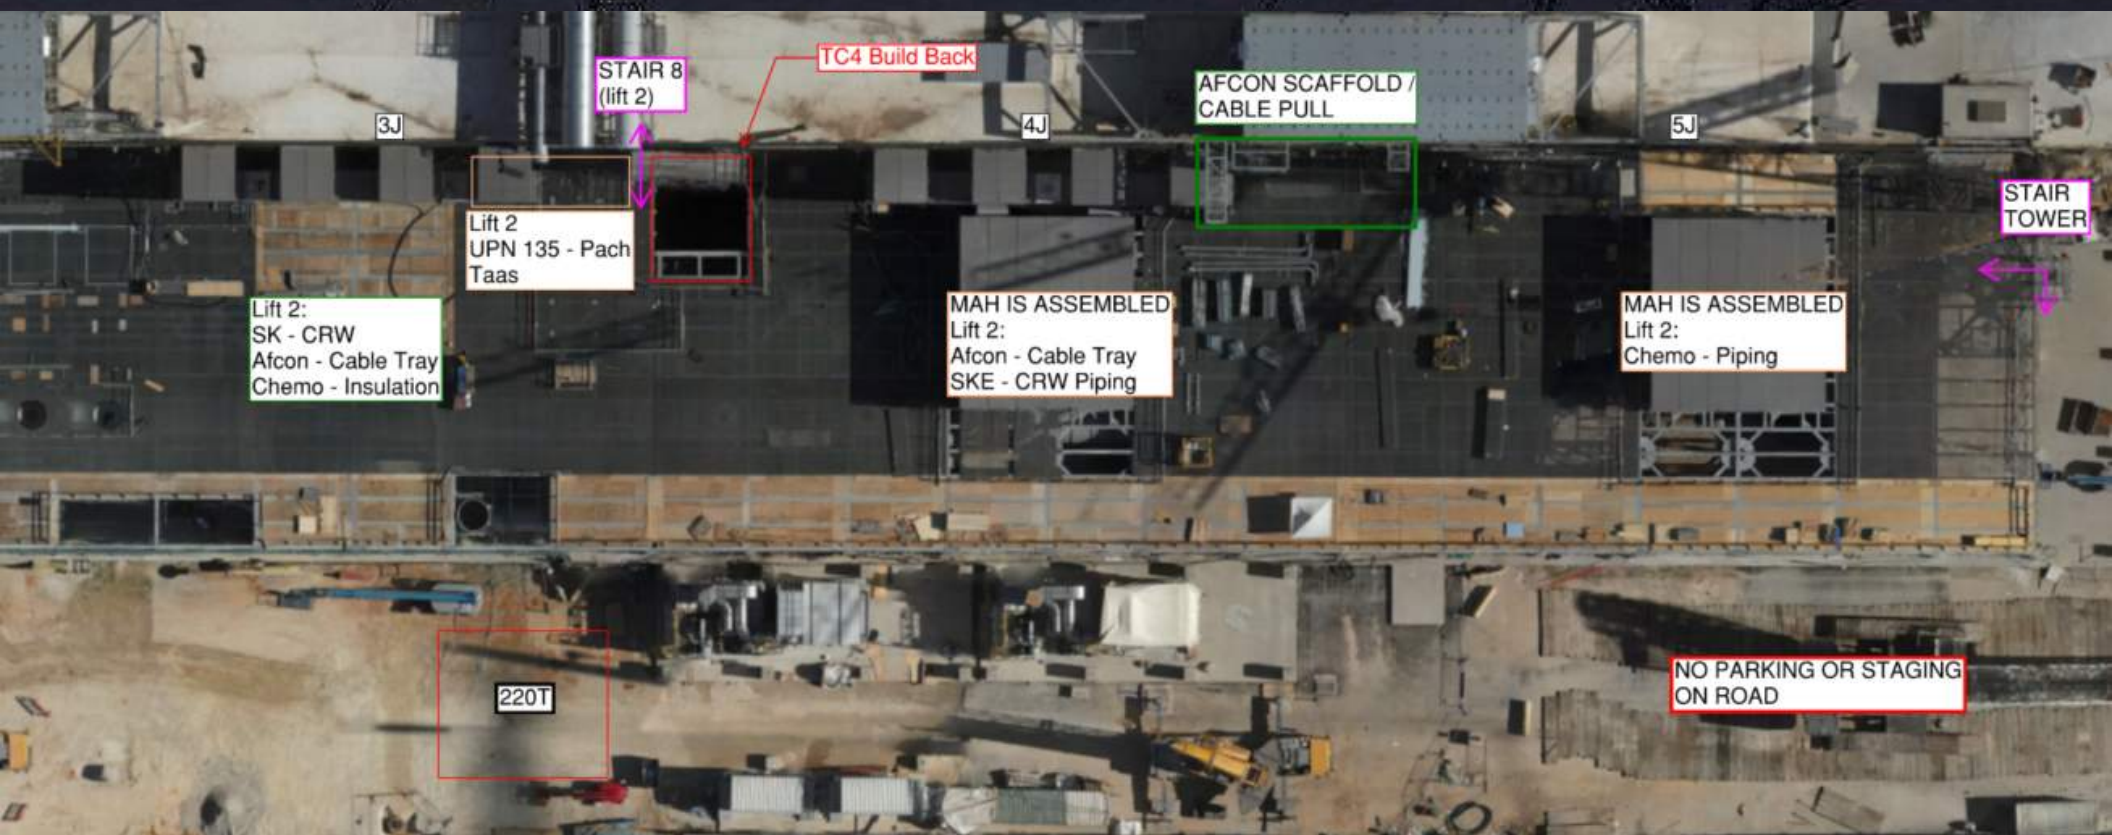

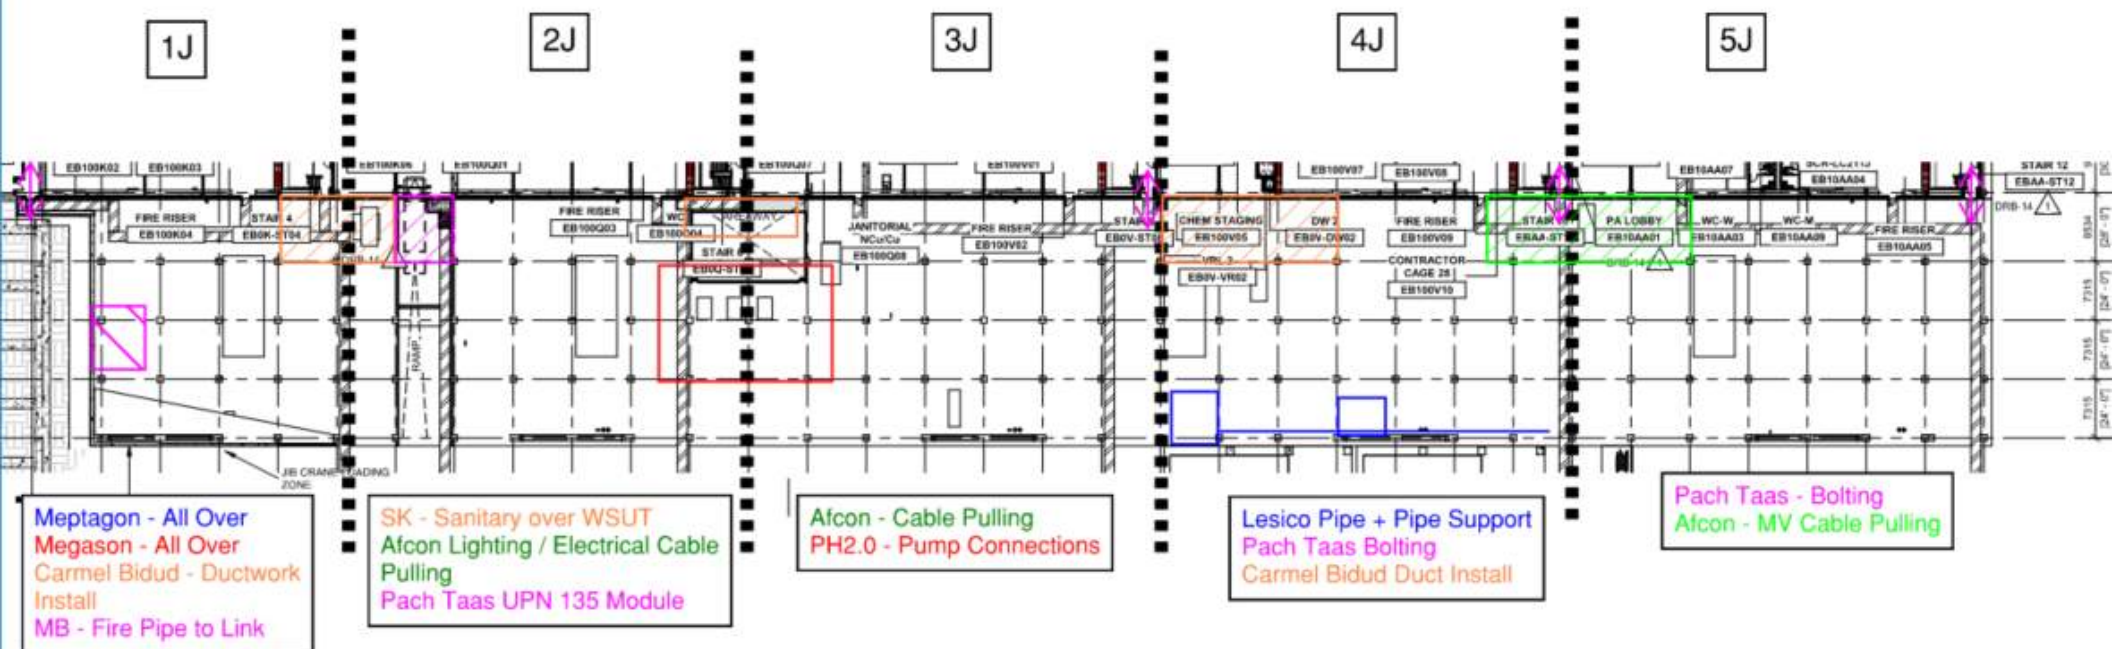

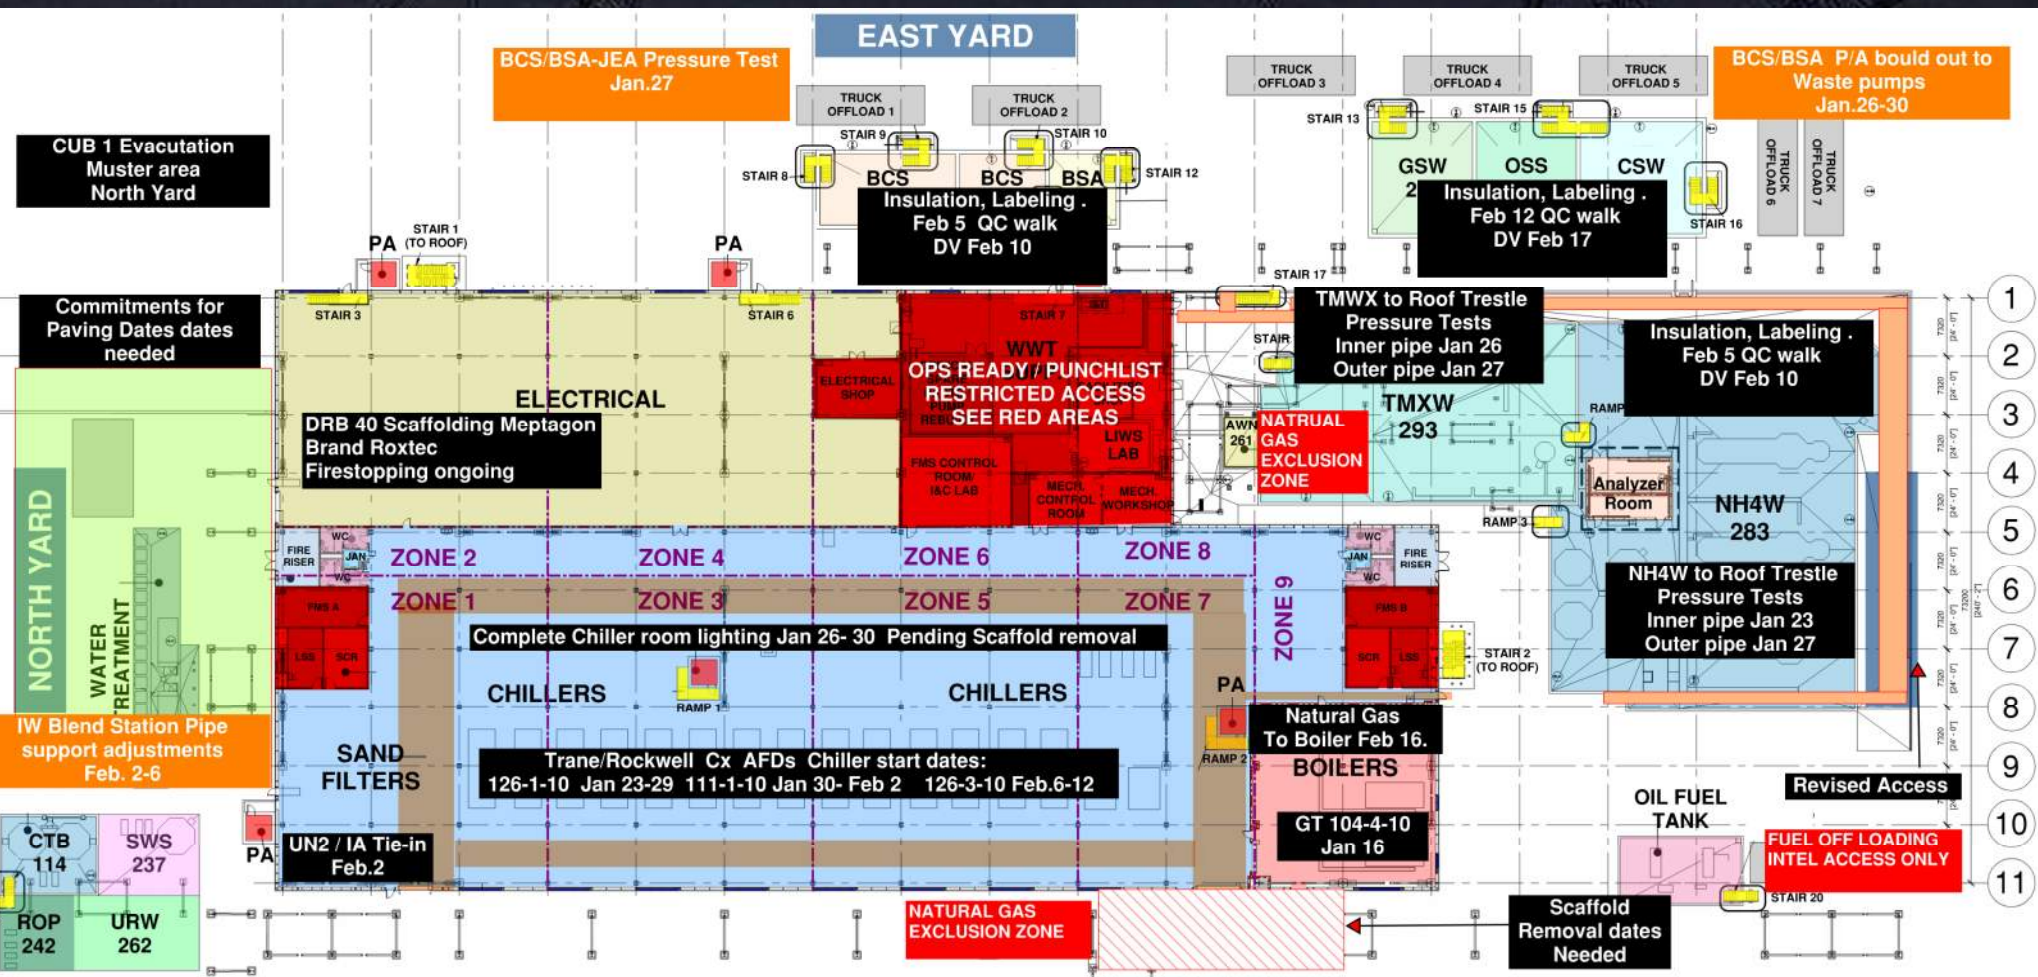


CUB 1 – EXTERIOR/ROOF

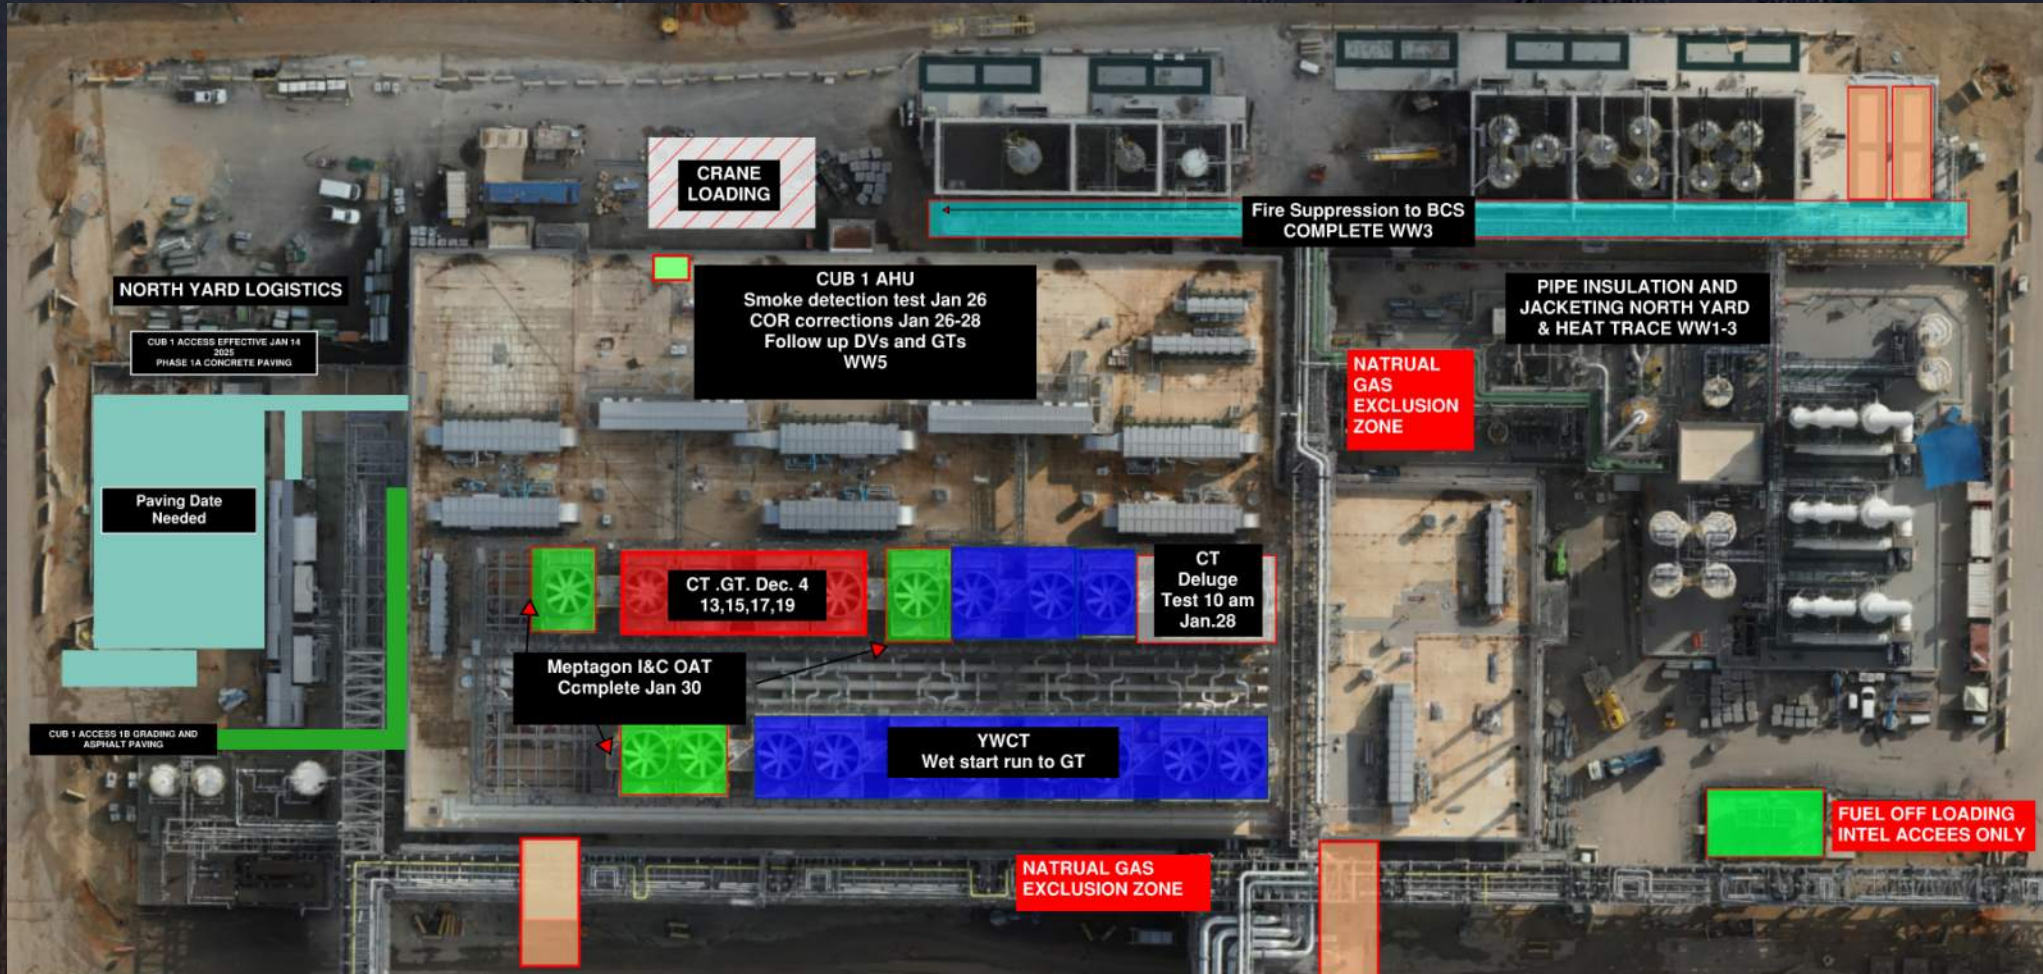


CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

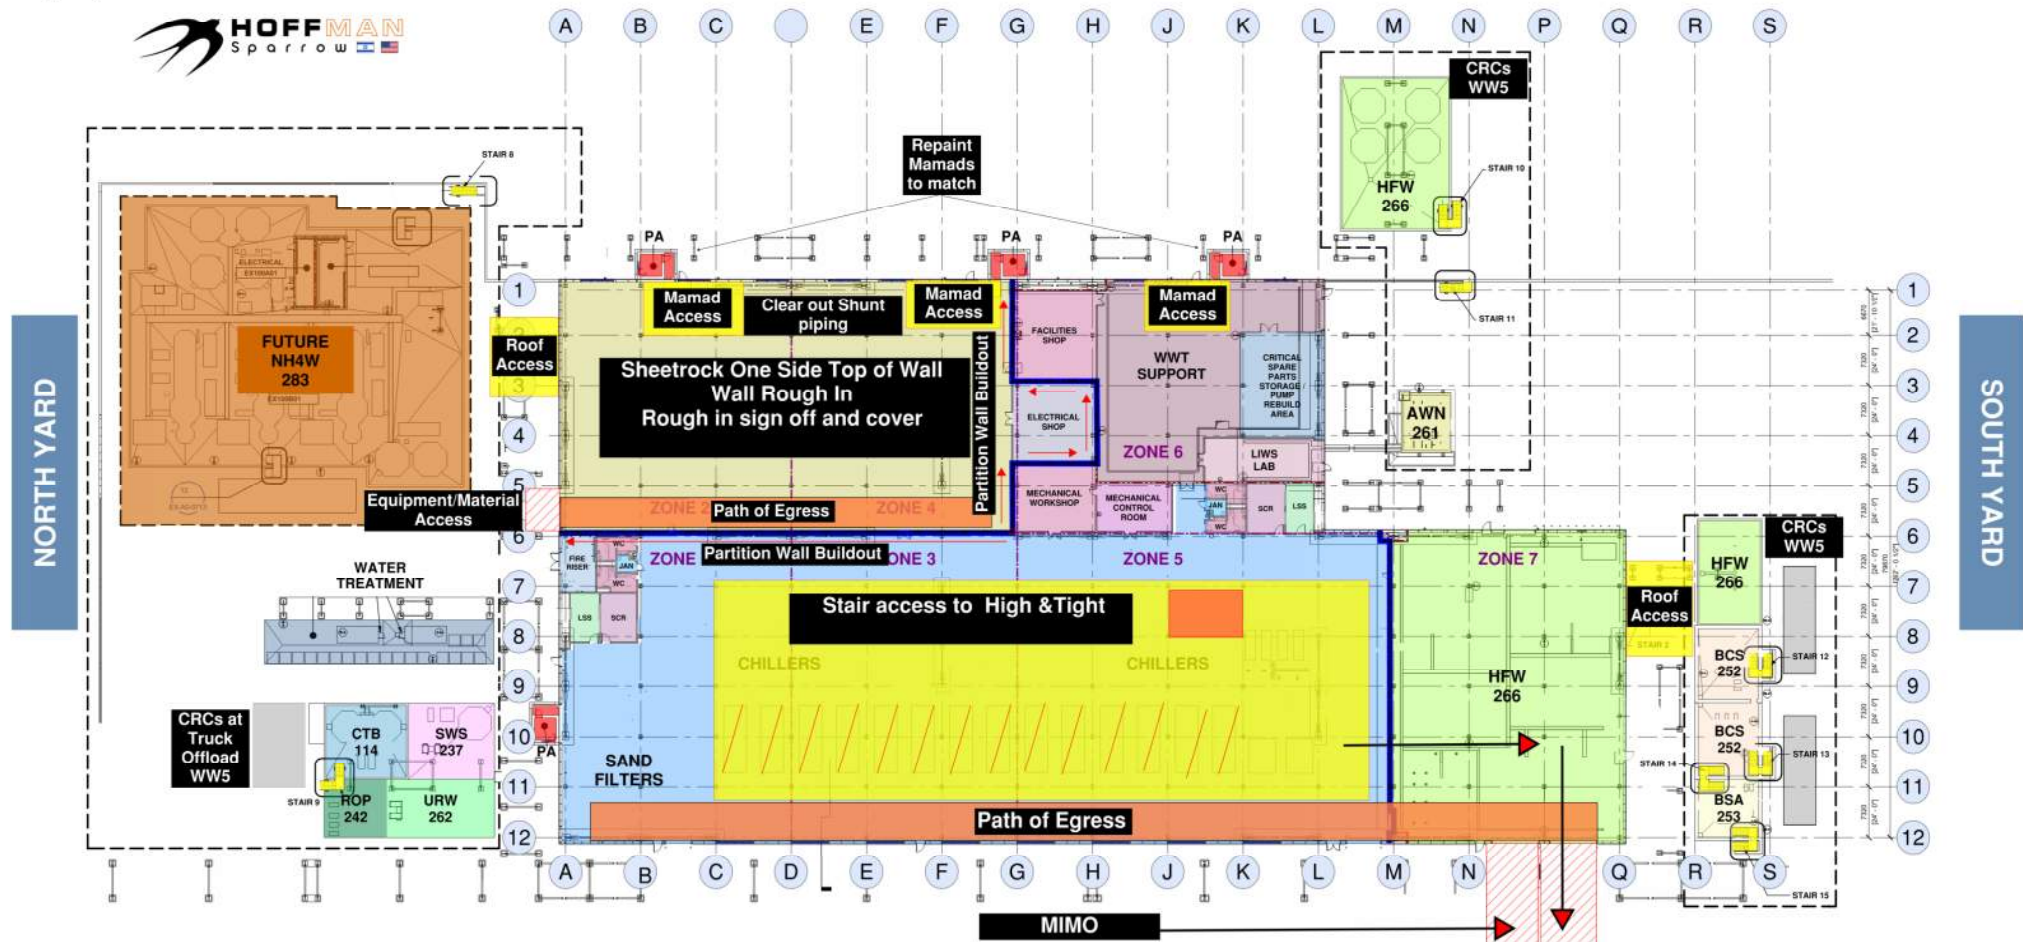

CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY





HOFFMAN
Sparrow  

MODULES IN FOR STORAGE

1 unit-Tue 21/1+1 unit-Wed 22/1
1 unit-sun 26/1+1 unit-Mon 27/1

GATE A

CUB 2

MODULES STORAGE AREA

Trucks maneuver area

Module access route

Keep a 10-meter-wide passage open




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Entry

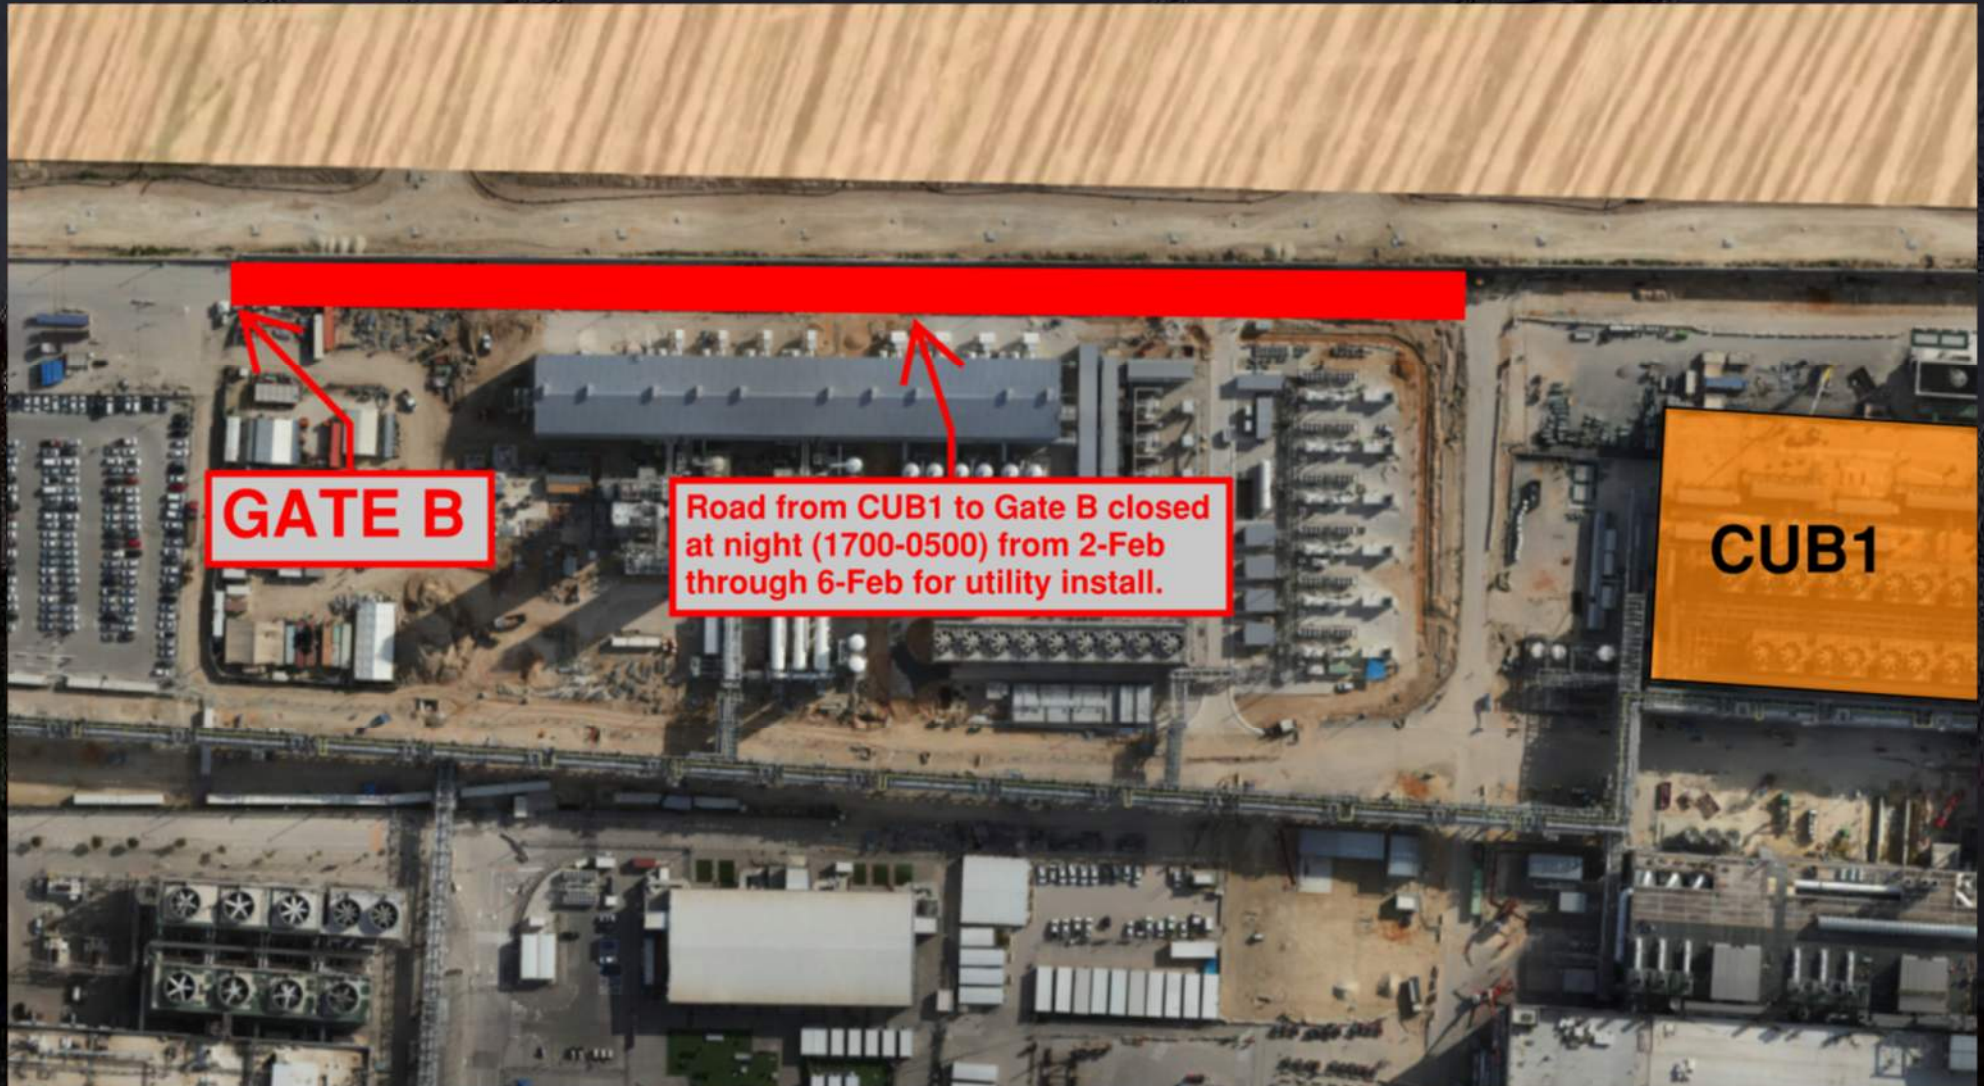



Daily Coordination Meeting

Site Logistics North







HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South

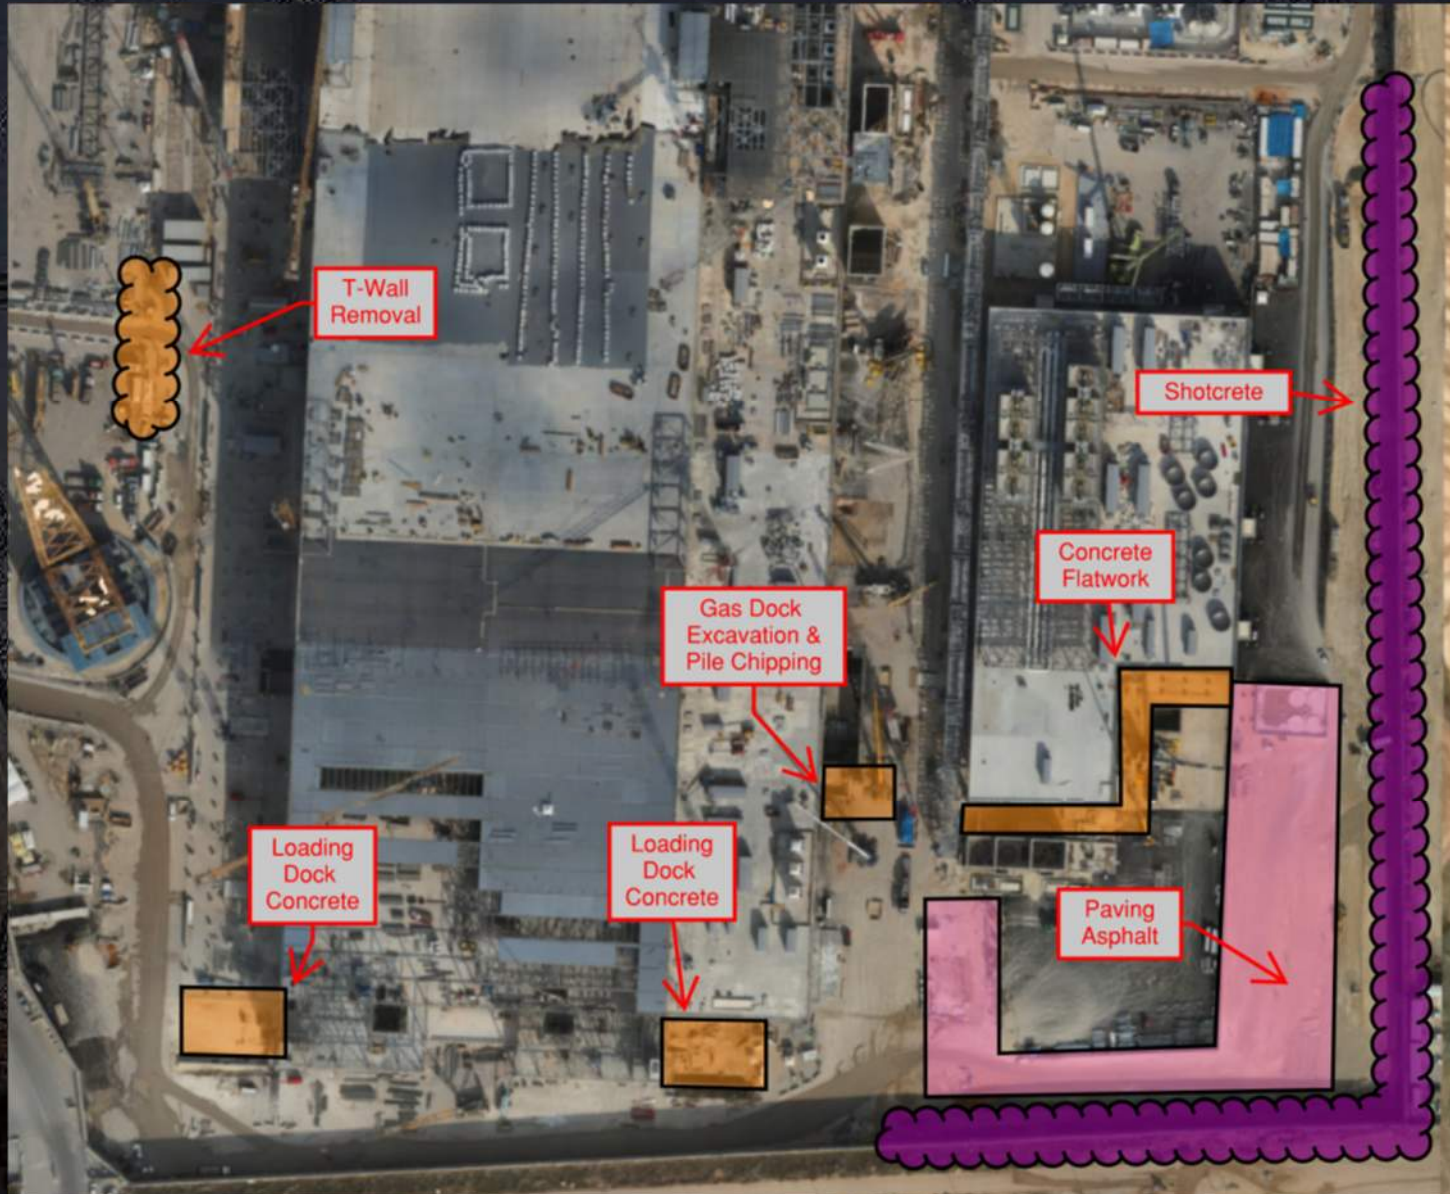





Overdue/Open CORs By Subcontractor WW5 (5% Target)

Open – 631 CORs

Overdue – 136 CORs

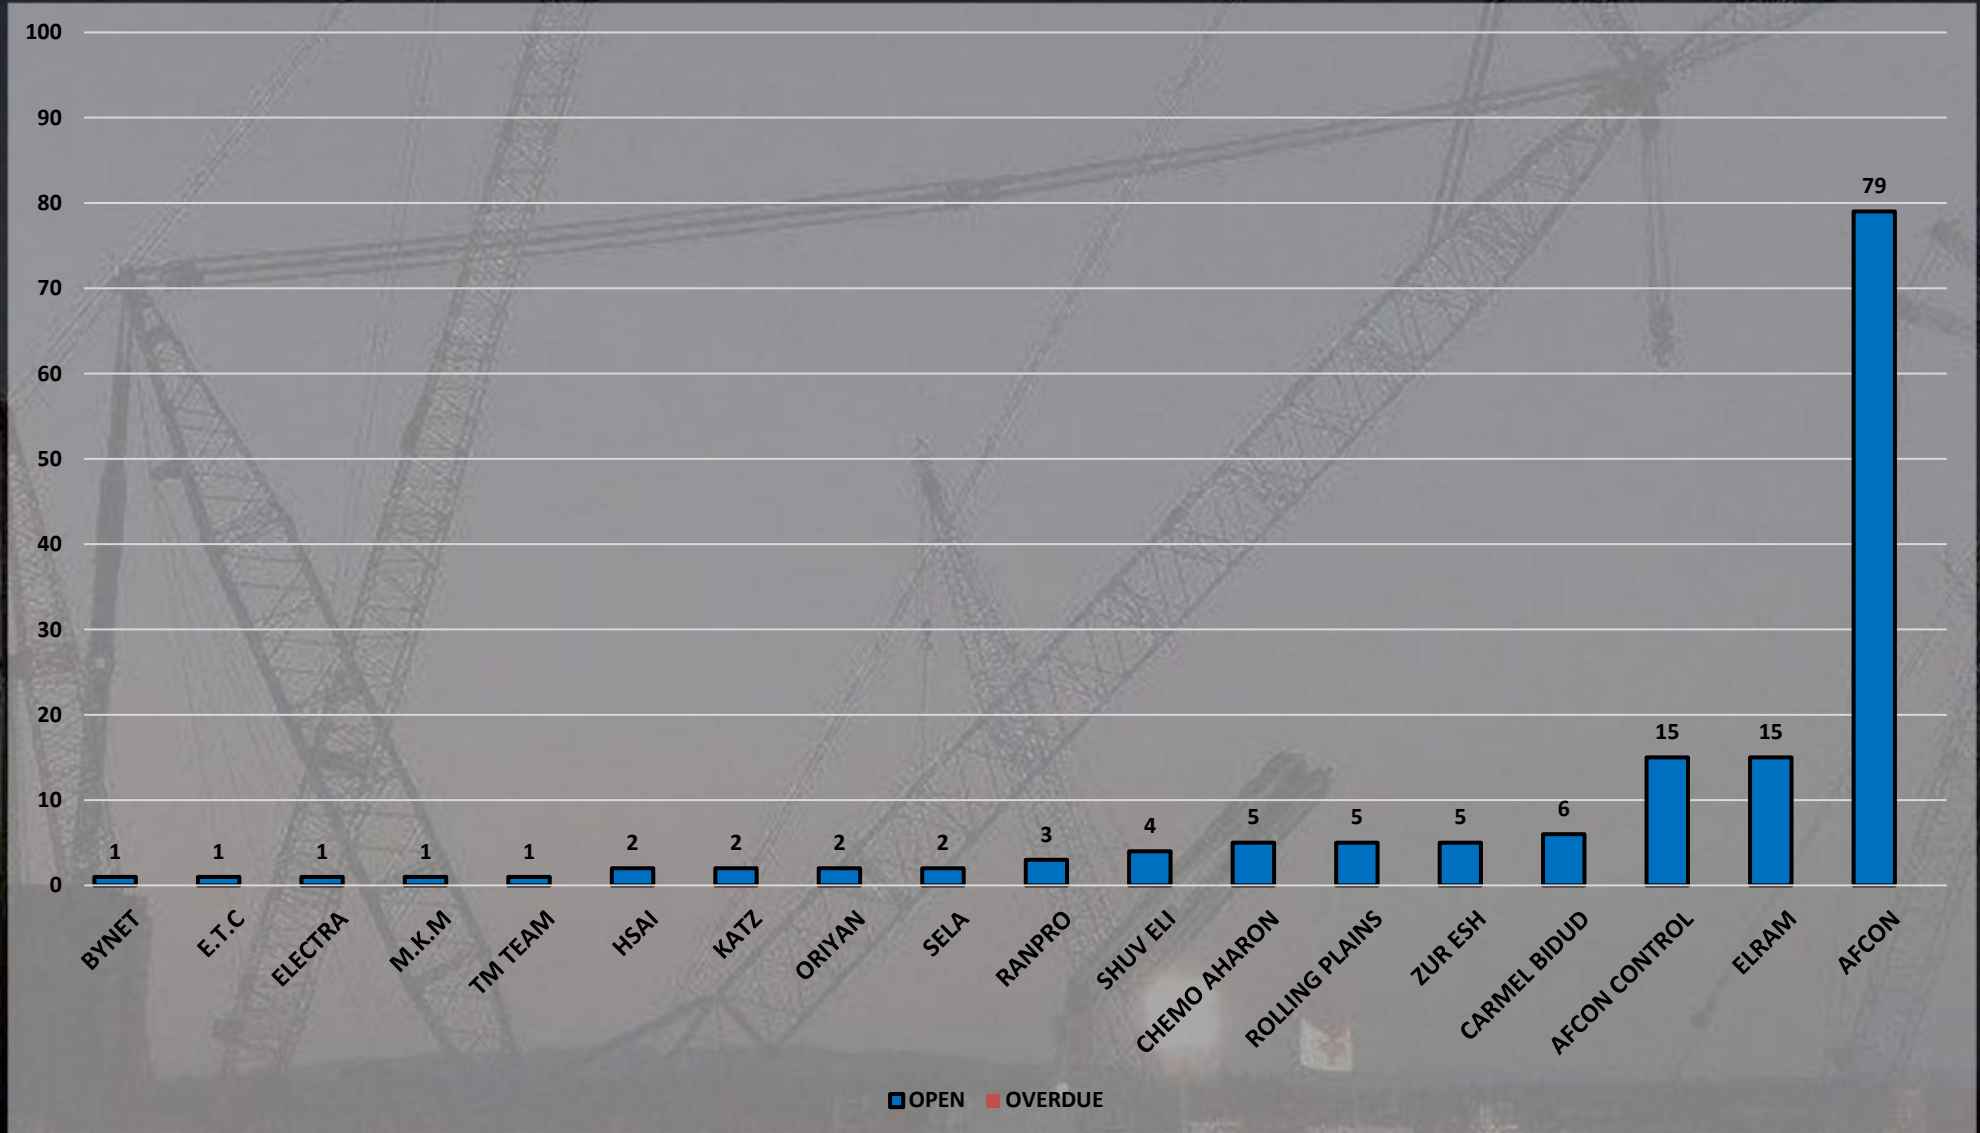




Overdue/Open CORs By Subcontractor WW5 (5% Target)

Open – 631 CORs

Overdue – 136 CORs

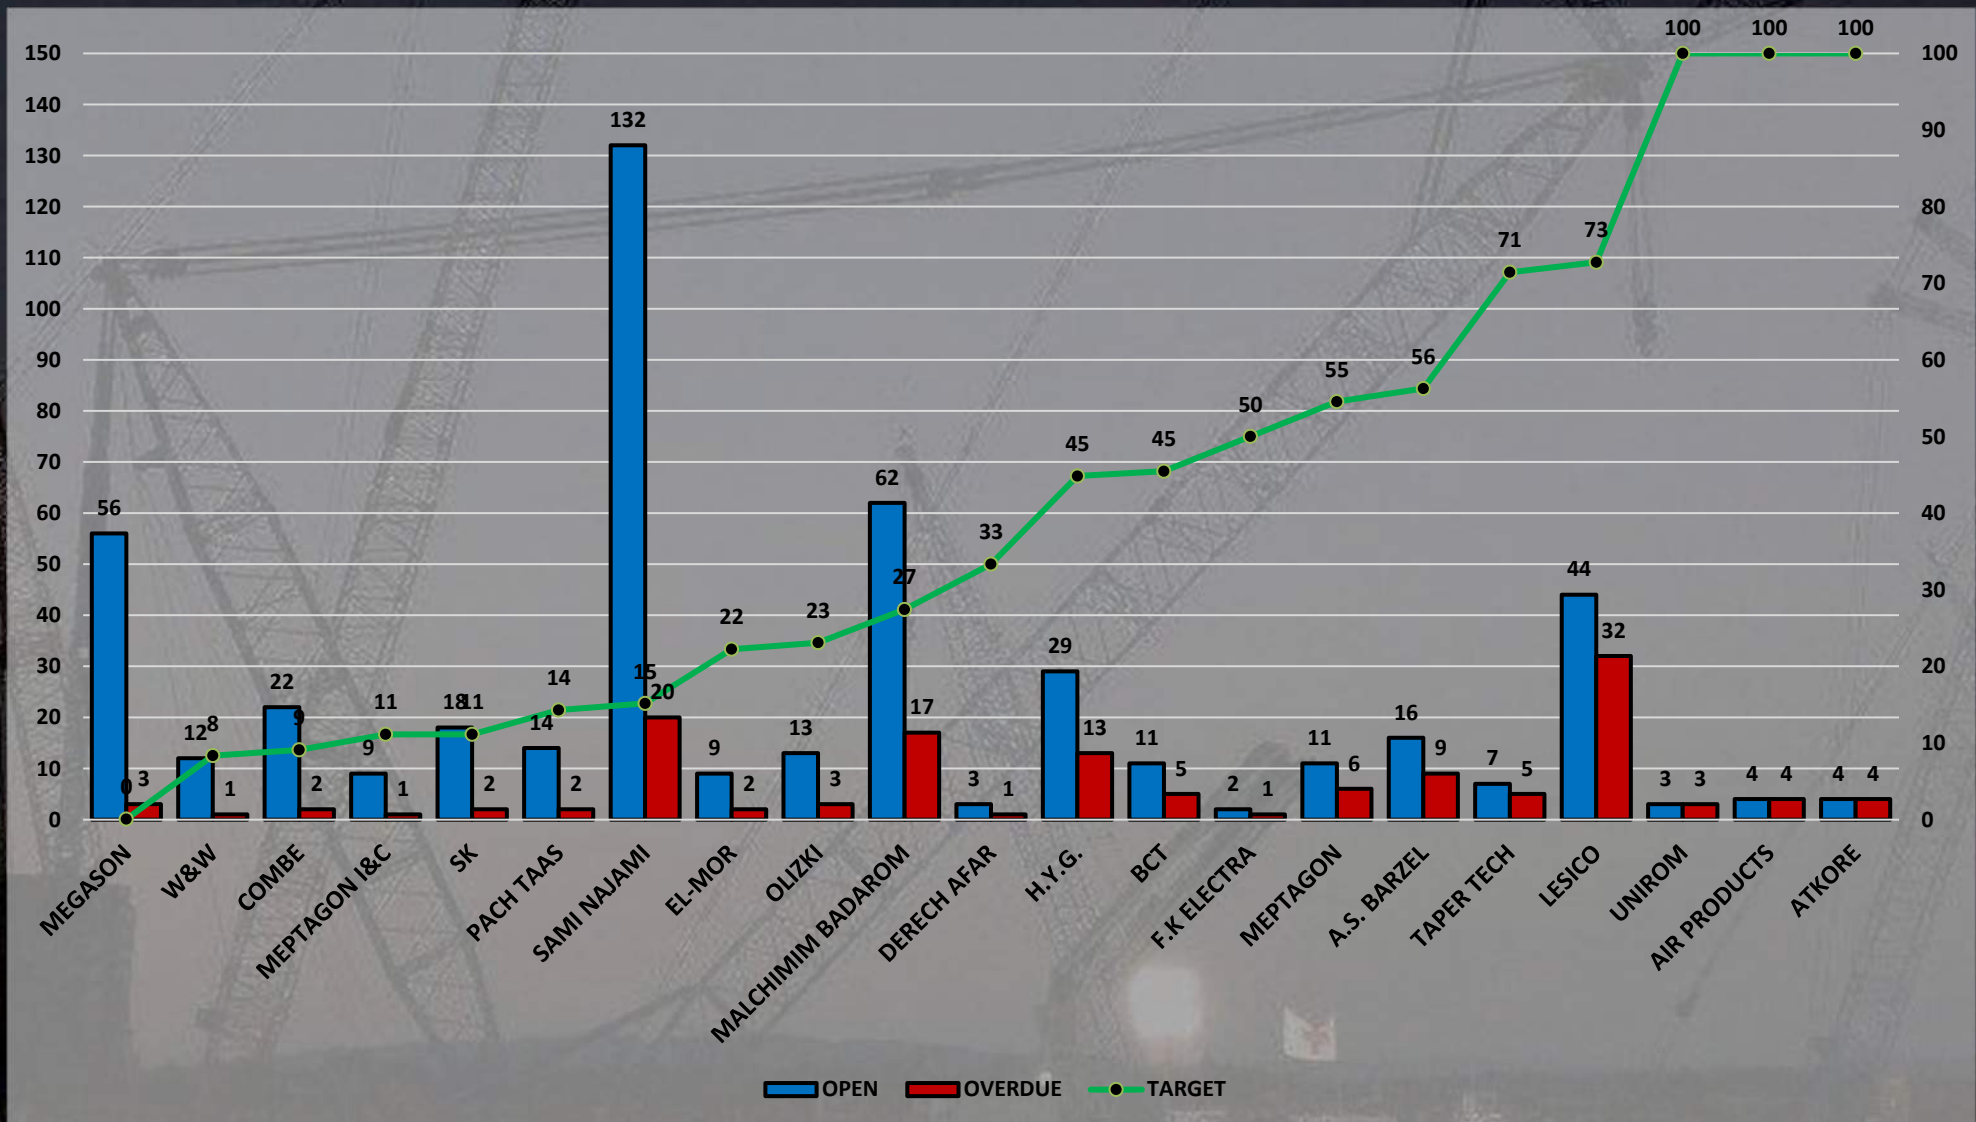

Unloading Trucks

- Loads need to be inspected prior to attempting to unstrap or unload them to ensure that they are stable.
- If the load appears unsafe to unload, it should be turned away.
- All personnel need to be out of the line of fire at all times.
- The area behind the truck (on the opposite side that you are unloading from) must be clear of all personnel and be red barricaded.
- You must have a plan for unloading the truck. All lifting tools need to be assessed, and capacities/weights must be verified.

HCC/EHS Weekend Work- 24.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Jesse Fritch - 052-3697329

Ibrahim A

Or Yaakov - 052-4268250

CSA CM

Cody Baumann - 052-7582613

Eyal Ben Shabat - 052-2239767

Brandon Feerer - 052-878-4285

Mark Santiano - 052-6937203

Shmuel Rosenberg - 052-3878052

Abhilash Parameswaran - 052-6938827

Eden I

Max P

MEP

Cx

Cranes

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional - Or Pitusi- 054-812-4788 Or-Pitusi@Hoffmancorp.com

Subcontractor Weekend Work- 24.01.2025

FAB

Utility Level / Roof / Stair Shaft

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

HYG

Ehs Salah 0507773119

Foreman Avishai 0503303939

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- **Pach Taas**
 - W-E MARSes
 - Ilya: 0505771907
- **Afcon E**
 - All over SF
 - RAZ: 0526008487
- **Combe**
 - TTNE
 - Ali: 0526767936
- **MEGASON**
 - MOD 2
 - Israel: 0526869393
- **SELA**
 - 9E
 - Yoav: 0548076339

Clean Room

- **Talad** – 20 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 14 GUYS Mod1 – MOD2- 17 line, 7E above coils (EHS Beni 0506232032, Super Shmulik 0549205966)
- **Afcon** – 20 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- **Chemo** –26 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- **Sela** – 10 1E, 2W CRC (Supervisor Yoav 0548076339, EHS Sergey 0526650046)
- **Pach Taas** 3 guys, BF-CA 17 Line (EHS Avigdor 0542010393, Super Netanel 0543301880)
- Protocol 2 guys (Roni 0542496363, Lidia 05072148)
- Talent solution 11 guys CR 2E 1E/W maintenance cleaning (EHS 0508777611, Super Faraz 0547139706)
- W&W 15 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Subcontractor Weekend Work- 24.01.2025

PSSS

- Pach Taas** – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **SK Engineering** – GL4 UL Piping, 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Carmel Bidud Duct** – Spec Gas, BCD, and 2P Roof
 - Foreman –
 - Safety –
- **Combe Waste** – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe UPW** – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- **Lesico** – UN2/Waste Vent Rack
 - Foreman – Selvin – 052-4787370
 - Safety – Oskar – 052-5221474

WJG

- **Afcon** – Lift 2 and Utility Level Cable Tray
 - Foreman: Montu 055 911 6973
 - Safety: Pradeep 055 274 2935
- **Chemo:** 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)
 - Foreman: Maor 050 988 9071
 - Safety: Erez 054 971 6840
- **Pach Taas:** All over (HRA)
 - Foreman: Ilya 050 577 1907
 - Safety: Eran 054 770 6233
- **Lesico:** Natural Gas Piping Utility Level
 - Foreman: Anoop 058 691 1748
- **SK** – (pressure test G water column 4J MAH)
 - Tufik 54-9433592

Subcontractor Weekend Work- 24.01.2025

CUB

Meptagon: CUB1

Foreman: Serghei – 0548038554

Safety: Haym – 0552728807

D&P: CUB1/2

Foreman: Konstantin - 0545501602

Safety: David – 0548894447

Sela: CUB1/2

Foreman: Yoav Yossi - 0548076339

Safety: Sergey Koharchok - 0526650046

Megason: CUB1

Foreman: Israel – 052686939

Safety: Guy Ishbit – 0544915409

Chemo: CUB1/2

Foreman: Dude Cohen – 0509808846

Safety: Daniel Lackford - 0525217434

Trestle

SNJ:

PIPES –T40 - UB CUB - 15 workers (3 teams)

STEEL –Galvanized paint + T30 A+B - 8 workers (2 teams)

Steel adjustment - 10 workers (3 teams)

FORMAN-

Mucles- 0526017477

SAFETY TRESTLE-

Aviram shrike - 0509059920

Siding

Site

Derech Afar – Shotcrete wall

Supervision = Raed: 054-244203

EHS = Alex: 054-5403849

Olizki – Offload 18 & CUB1 trench drains, Southeast CUB1 grading

Supervision = Or: 052-4917313

EHS = Ben: 052-4033565

Sut

Sela

EHS 052-6650046

Foreman 054-8076339

Daily Coordination Meeting



14:00 Sign In
