


Daily Coordination Meeting

General Topics:


- Assume all systems are live
- 17M Safety lunch on Tuesday - Volunteers needed!!
- Weekend work




SUBFAB LEVEL

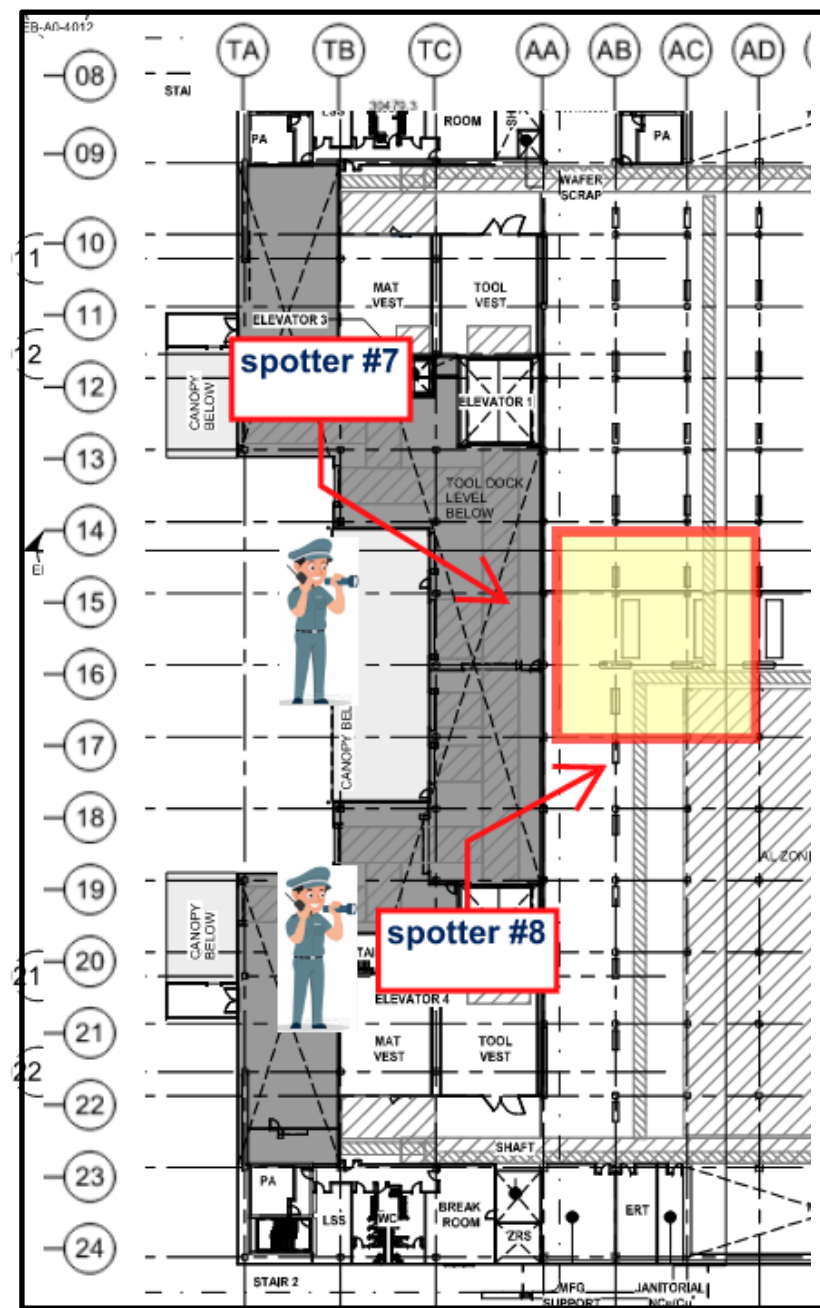

UTILITY LEVEL MOD1

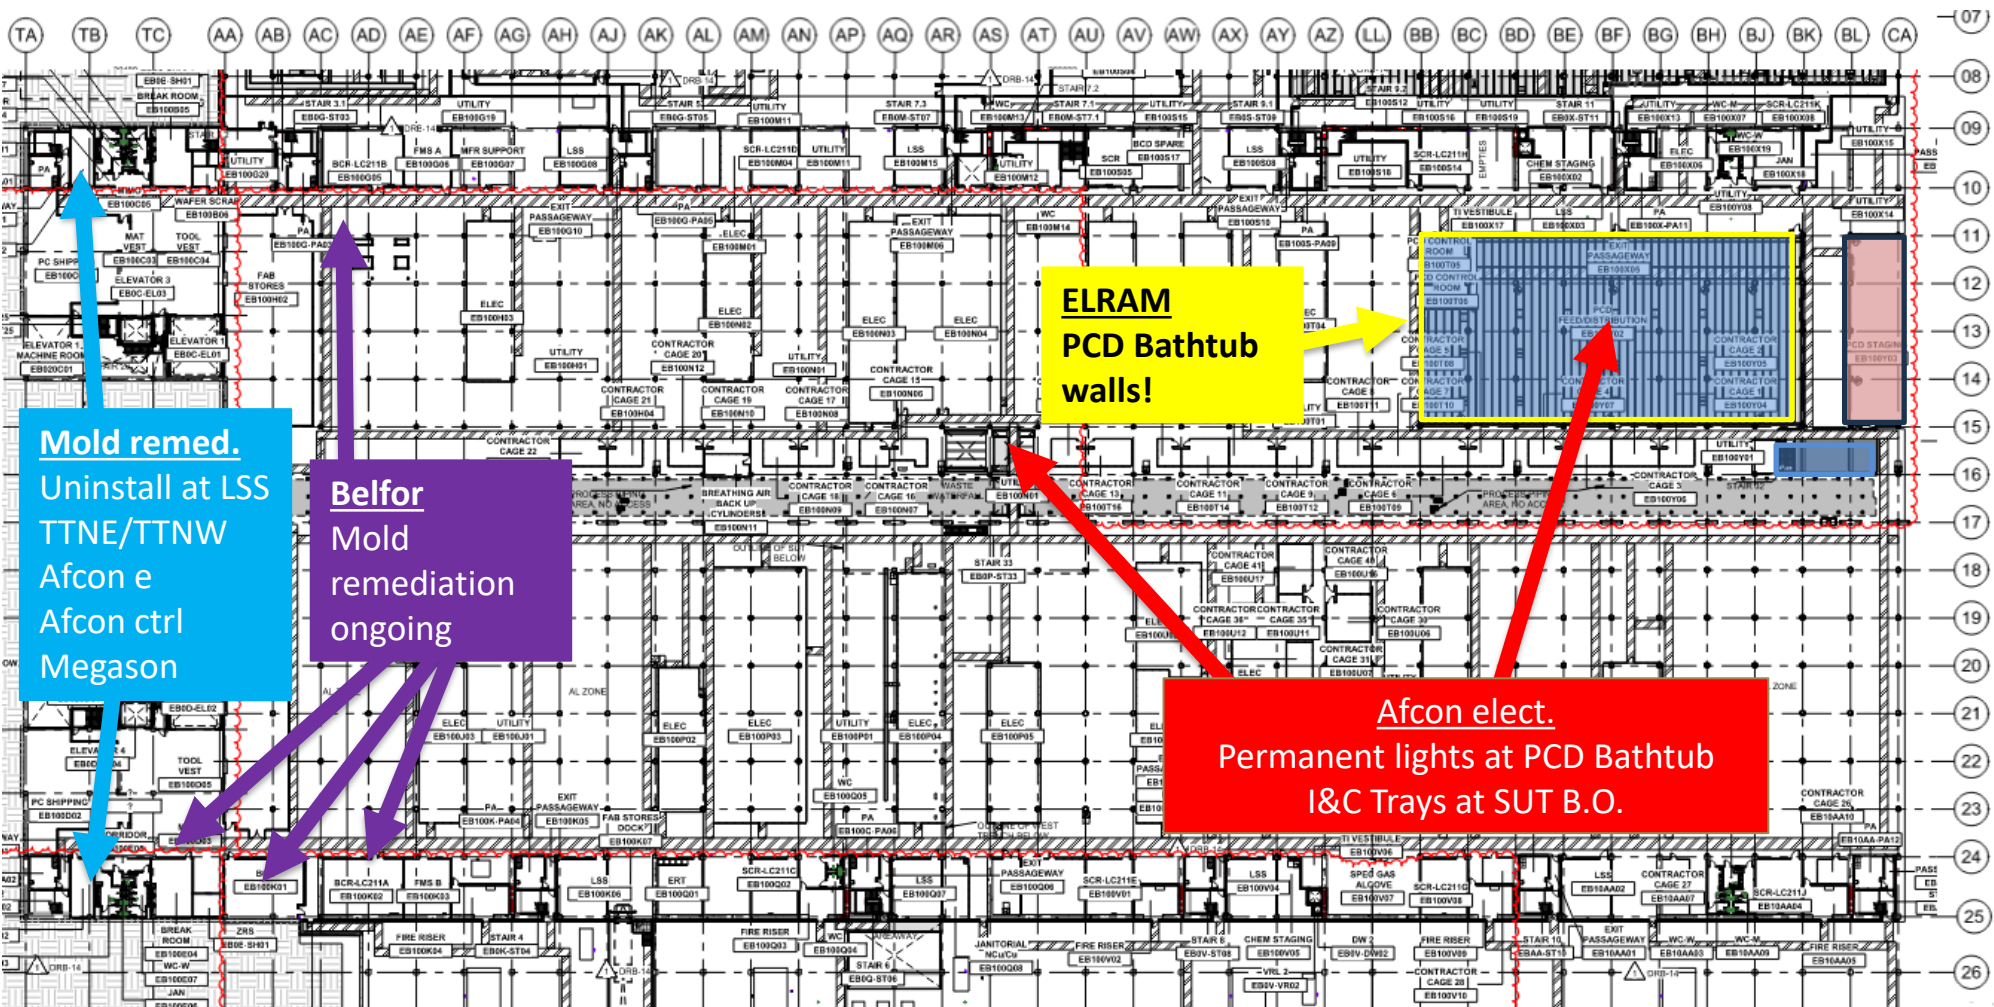

UTILITY LEVEL MOD2

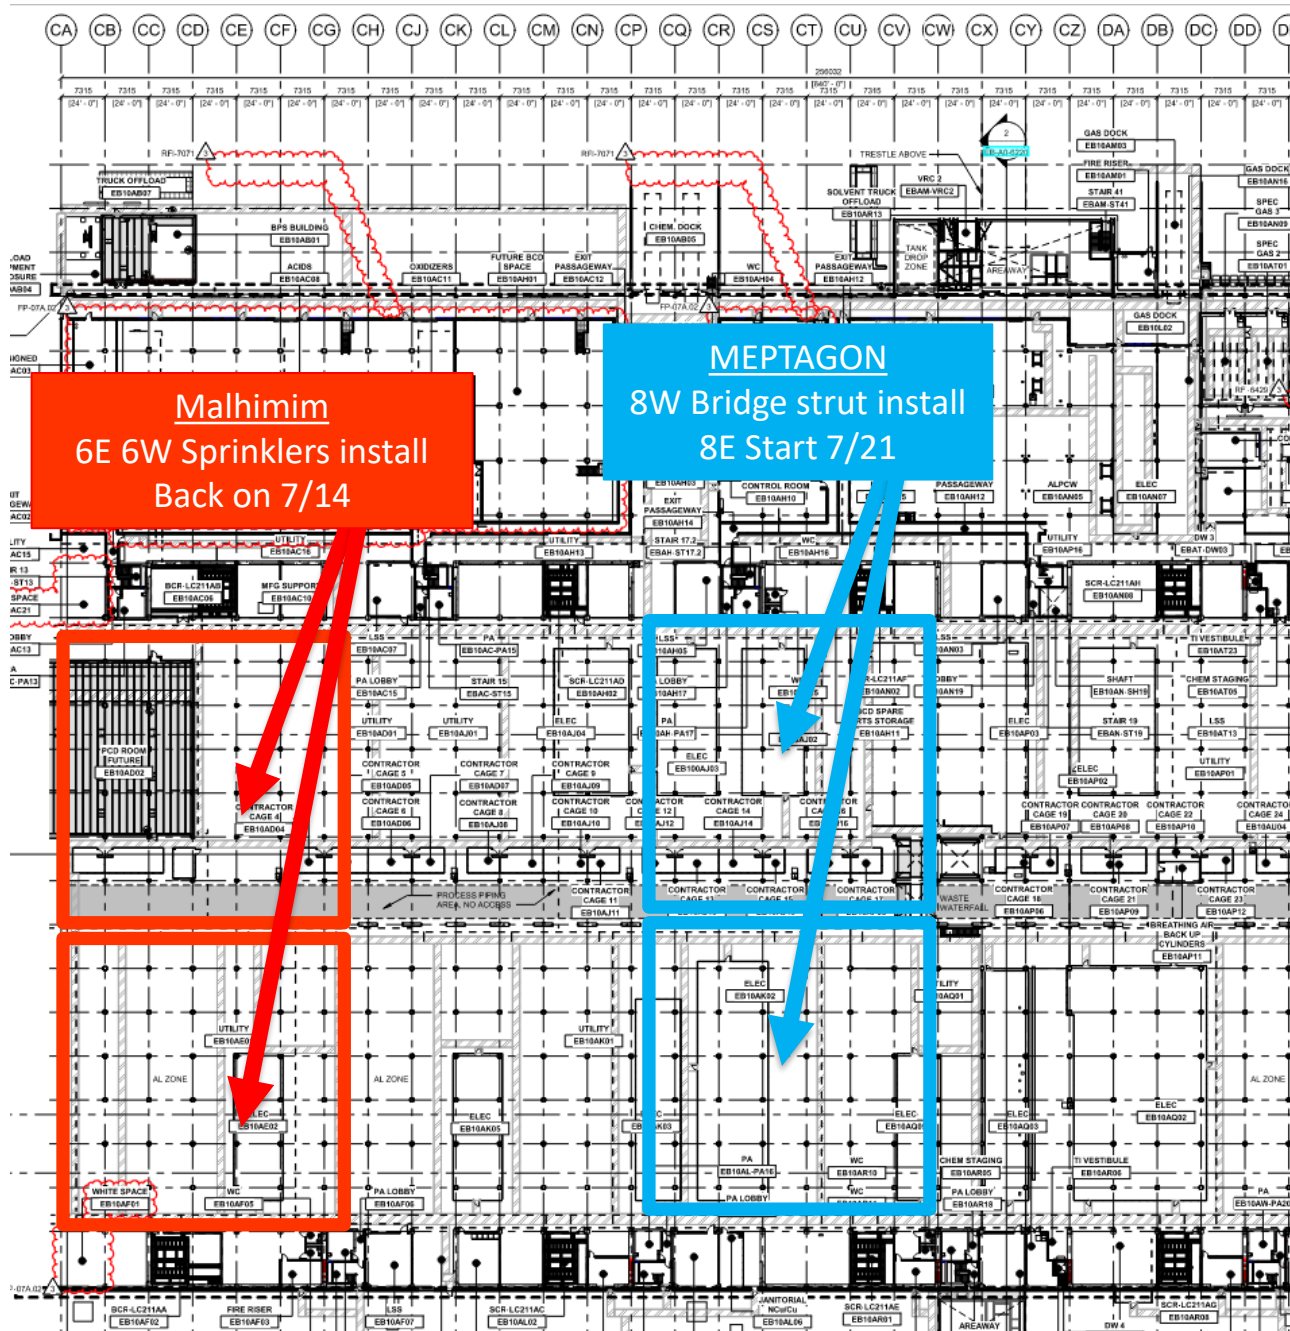




SUT 38.1 LEVEL

SKE
Safety shower's
Need Bulletproofing

Lift station
CRC Sela – NH4W, CCW
C&R ,TriMix

AWN-
Piping Connections.

SWS
Hx hock up

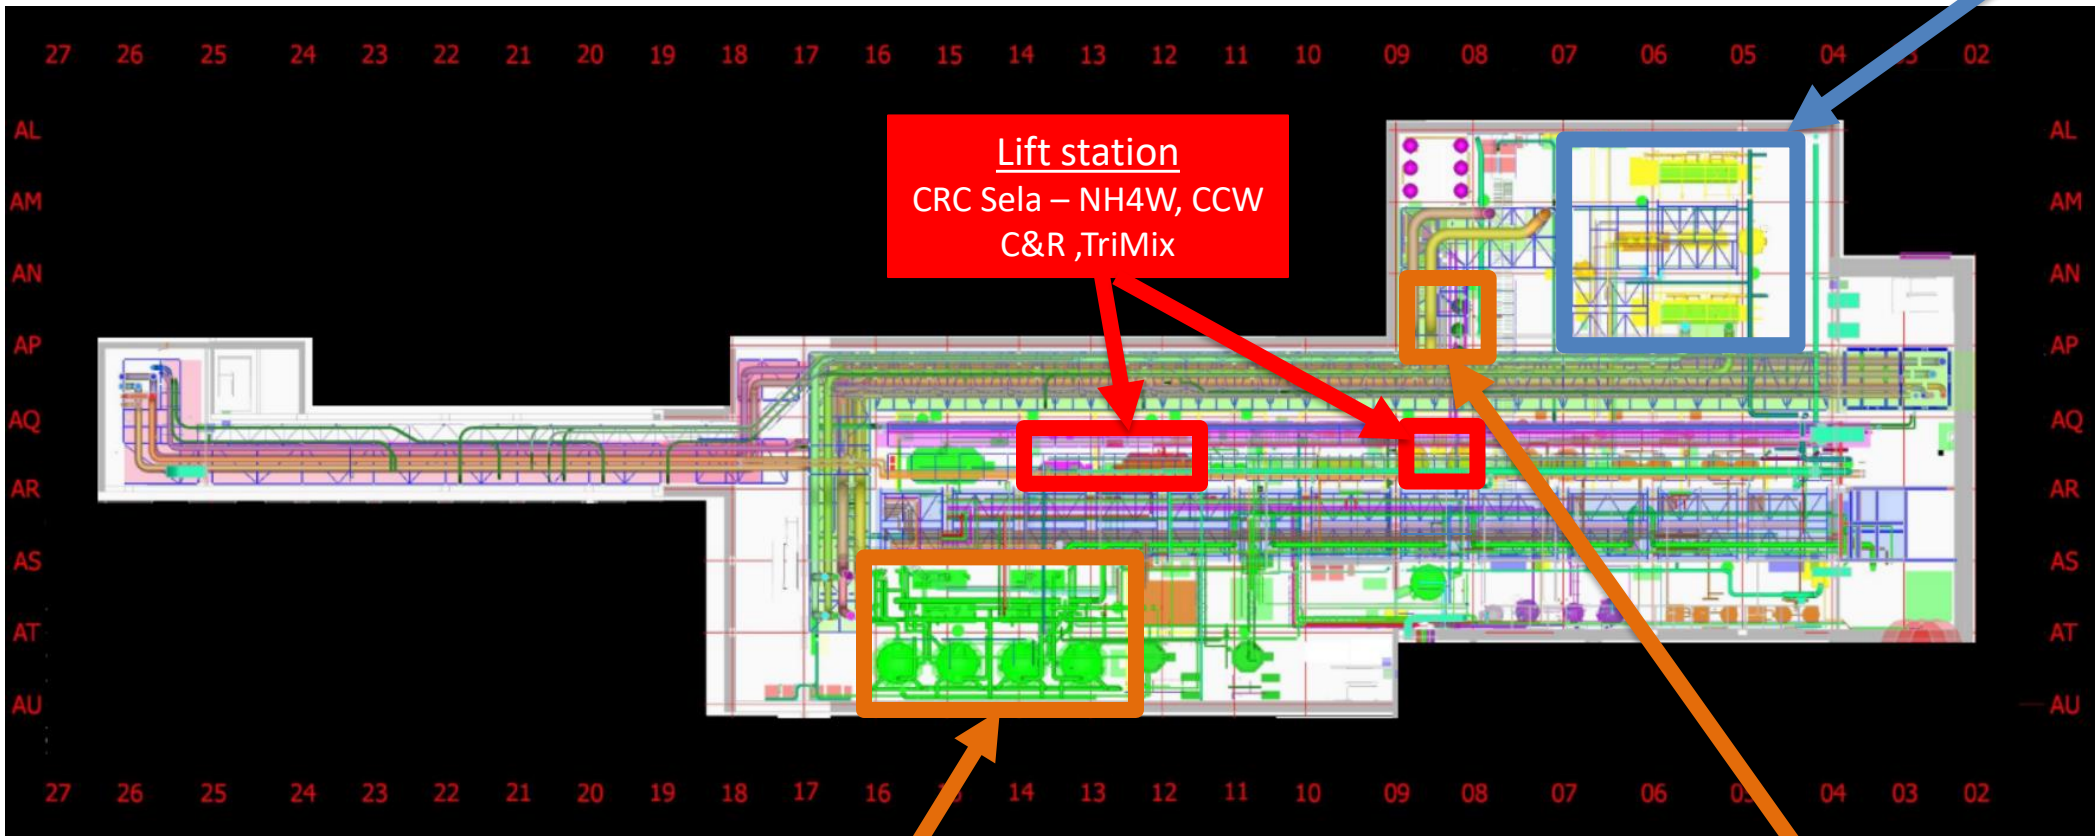




HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

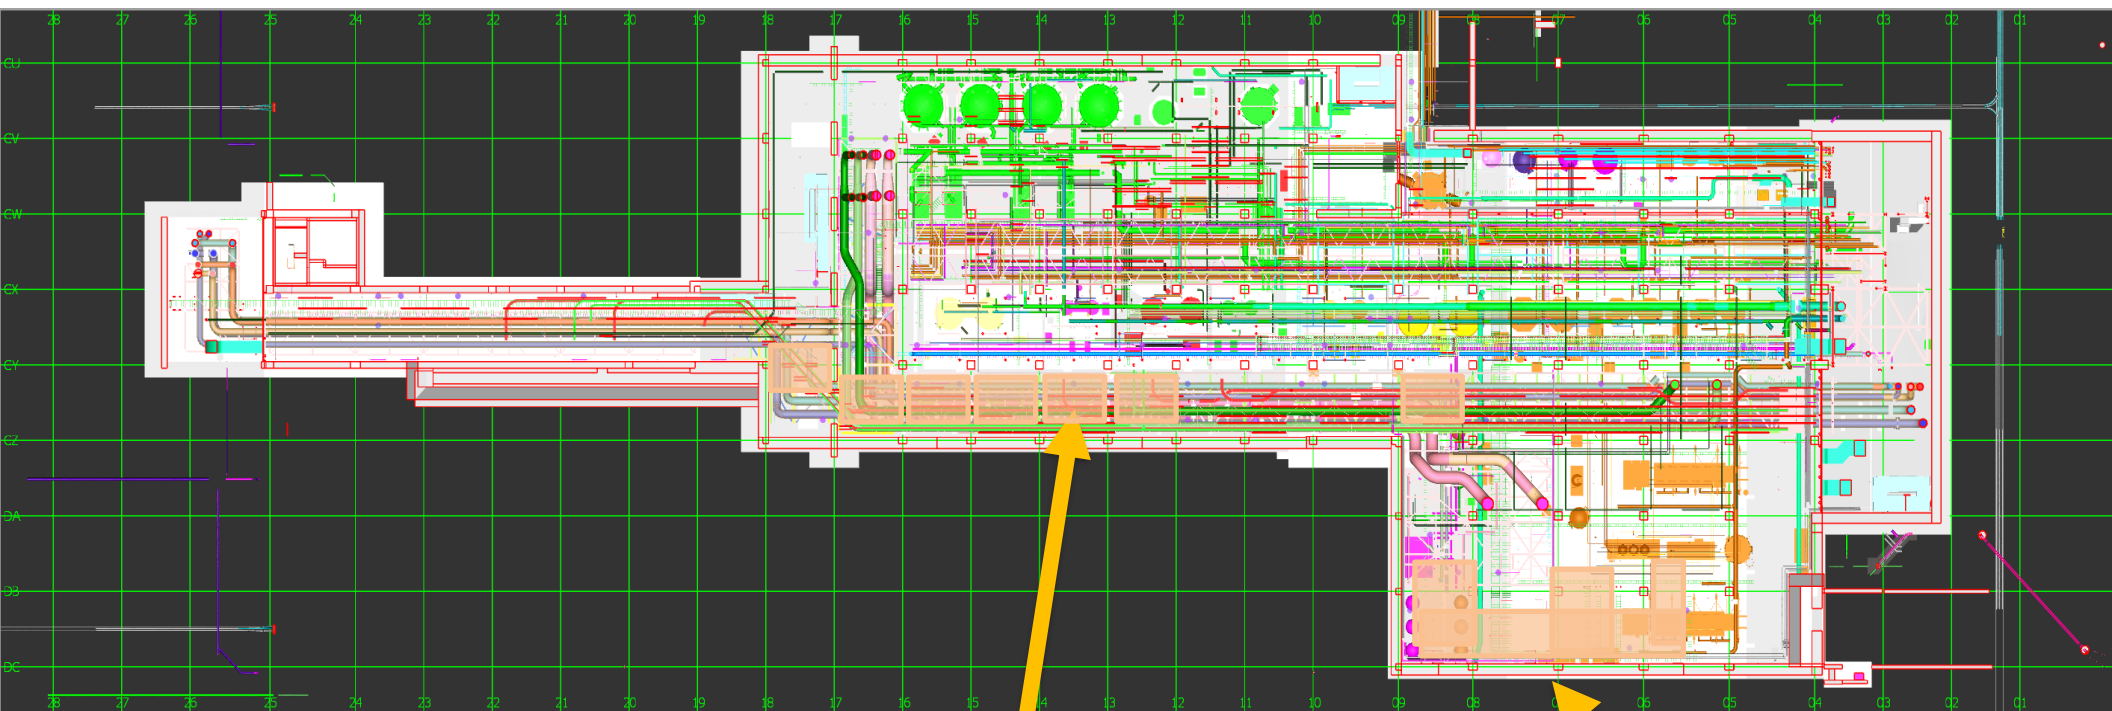

SKE
H&T
CRW
Move-In date ?


Vesda
H&T
Move-In ??

1A Rack
Lifting


8 Rack
Pending
Martials

SUT 38.2 LEVEL


CRC Plan

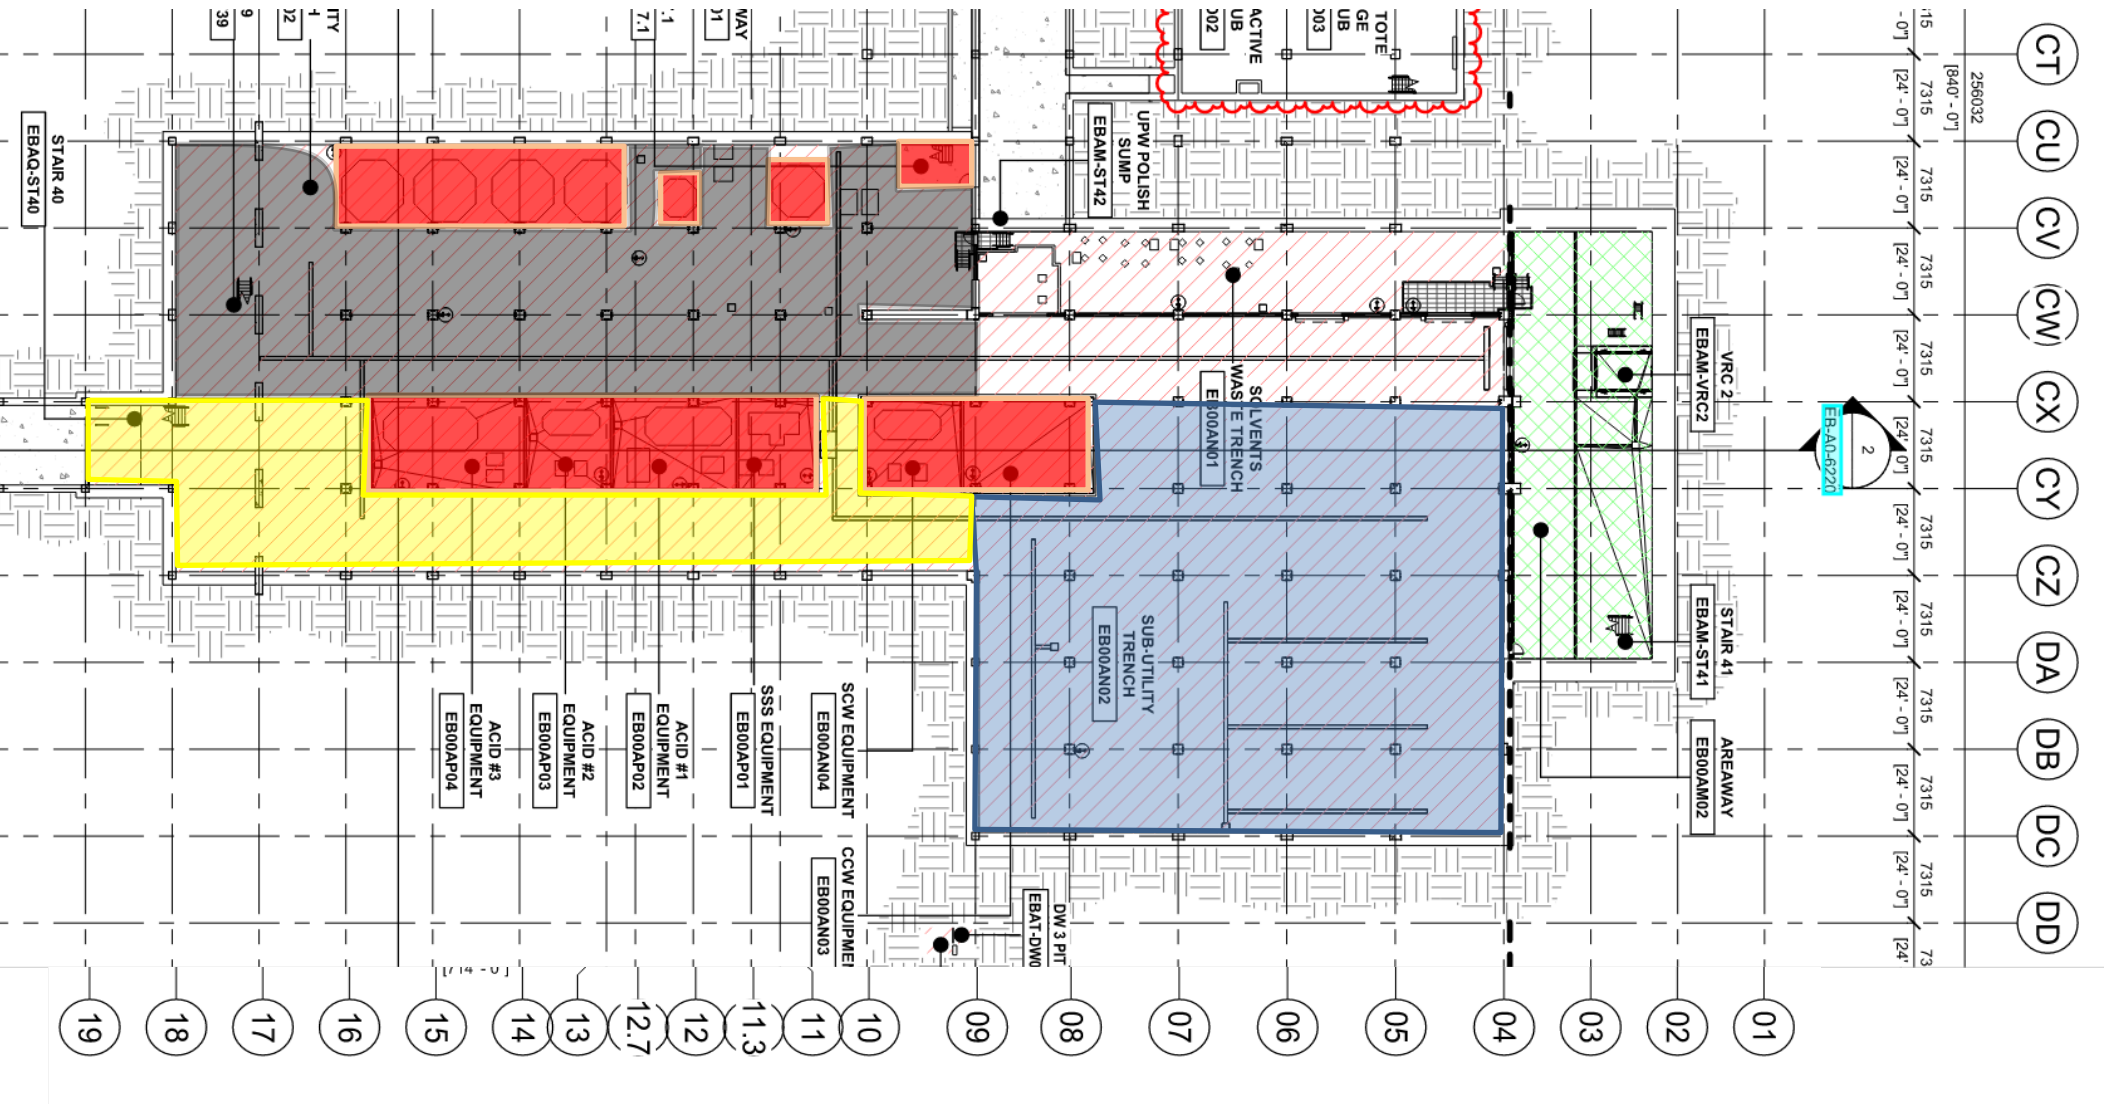


SUBFAB BUILDOUT MOD 1

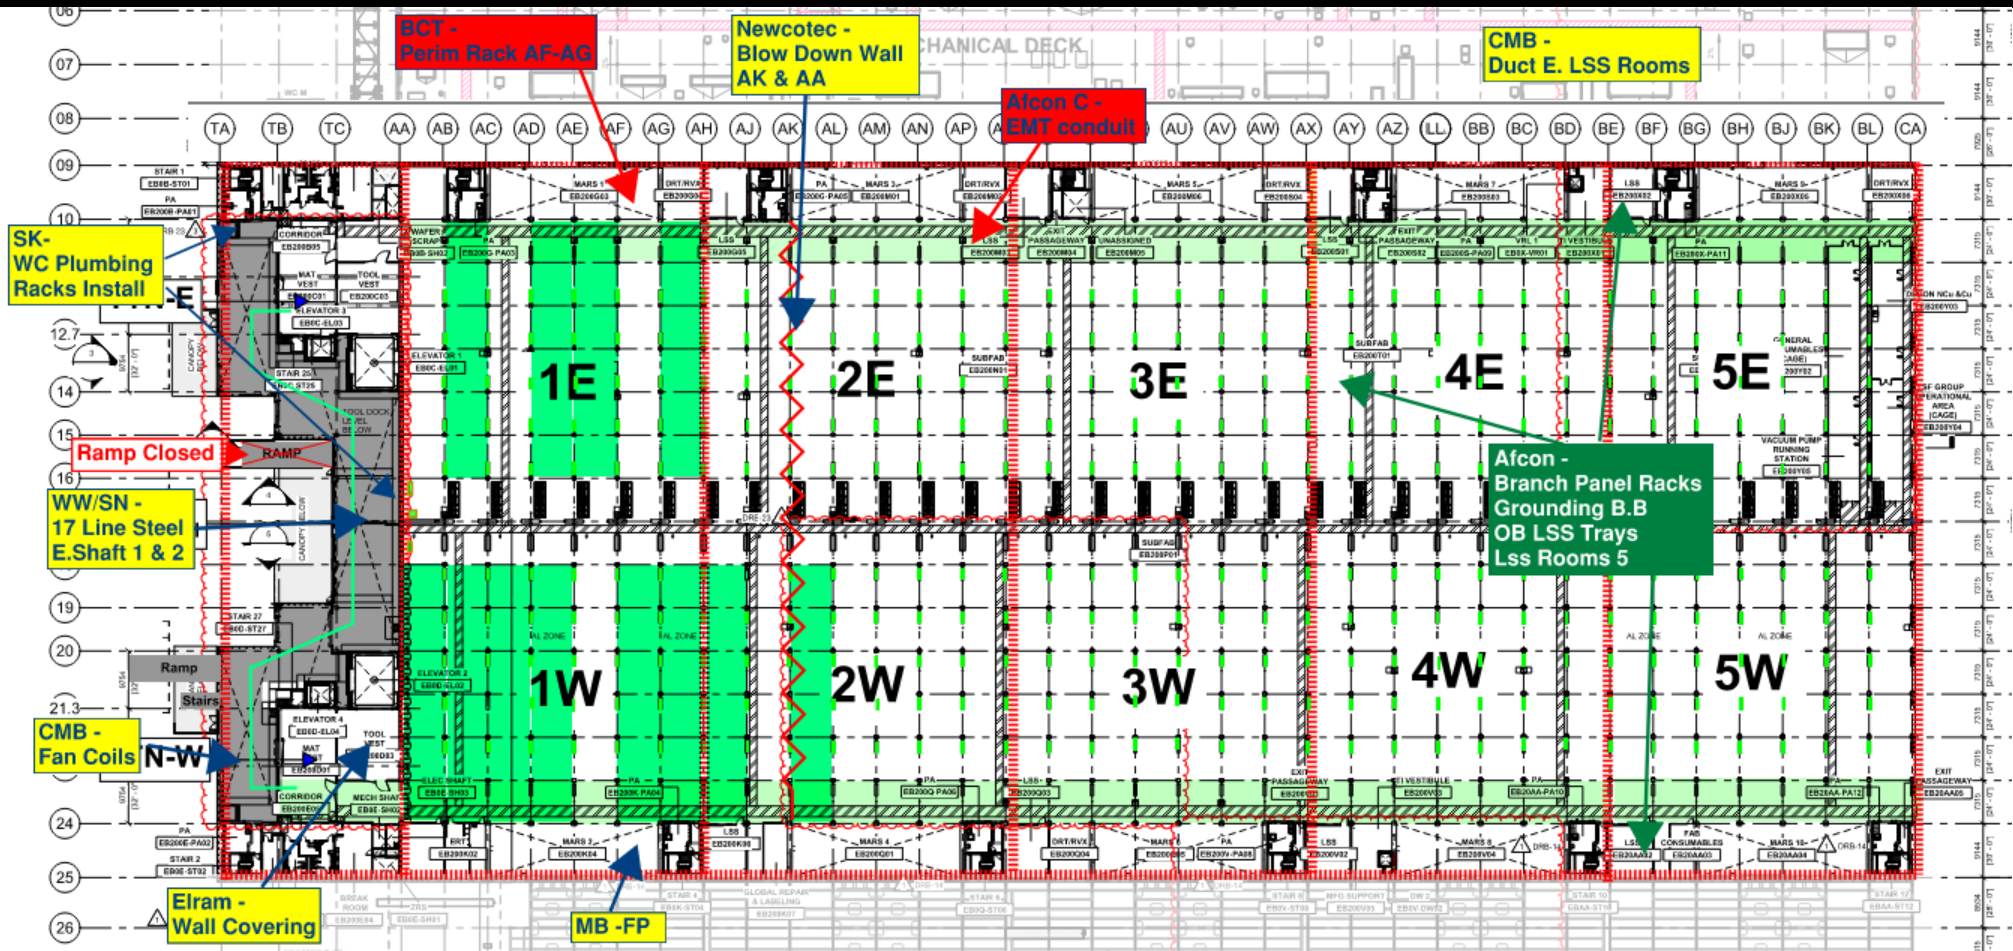


SUBFAB BUILDOUT MOD 2

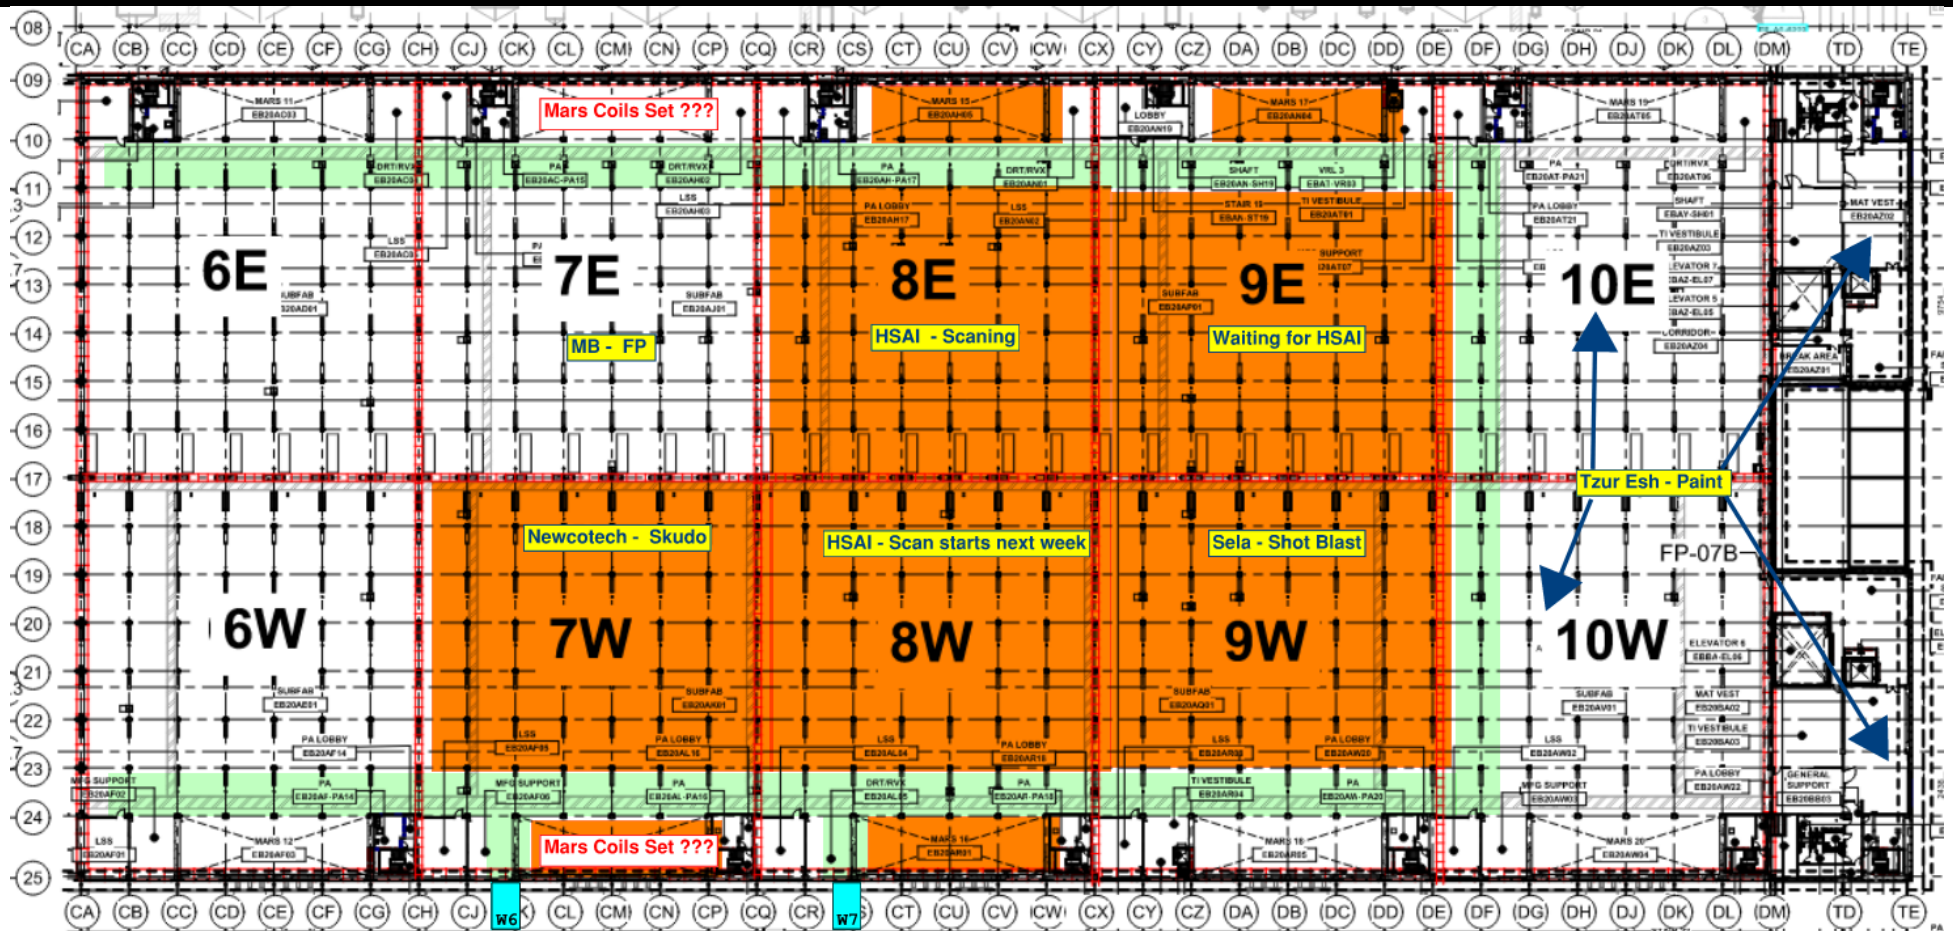



HOFFMAN CONSTRUCTION COMPANY





CR level:
Afcon - Cable trays, modules and stickers 1W, 2E, 2W
MB- 1E drops, 1W pipes. 2E-2W needs to start
Eiram - 10, 24 columns fix. 9,25 columns on going
9,25 line columns wrapping
Meptagon - Zero tolerance pipes 1E, 1W, 3E
D&P - Ceiling rods 1E
Tzur-esh - 24-25 lines. 4W. To start 17 line AB-AK paint
HYG - 1W Litho crane touch ups, 5W Litho crane steel
PT - Duct 3W
Talad- Selsmic cables

NTTEW
WW- 4DA steel TTW
Tzur-esh- to complete paint 4DA
Eiram - QA/QC raise floors?
SK - Pipes, testing and QA
HYG - To start decking and bent plates
HSI - To pour slabs

CB- To build scaffolds to support FP, Eiram and Tzu-esh
SIG - Scaffold support FP, Eiram and Tzu-esh

1E

2E

3E

4E

5E

FAB BALLROOM


1W



2W


3W


4W


5W


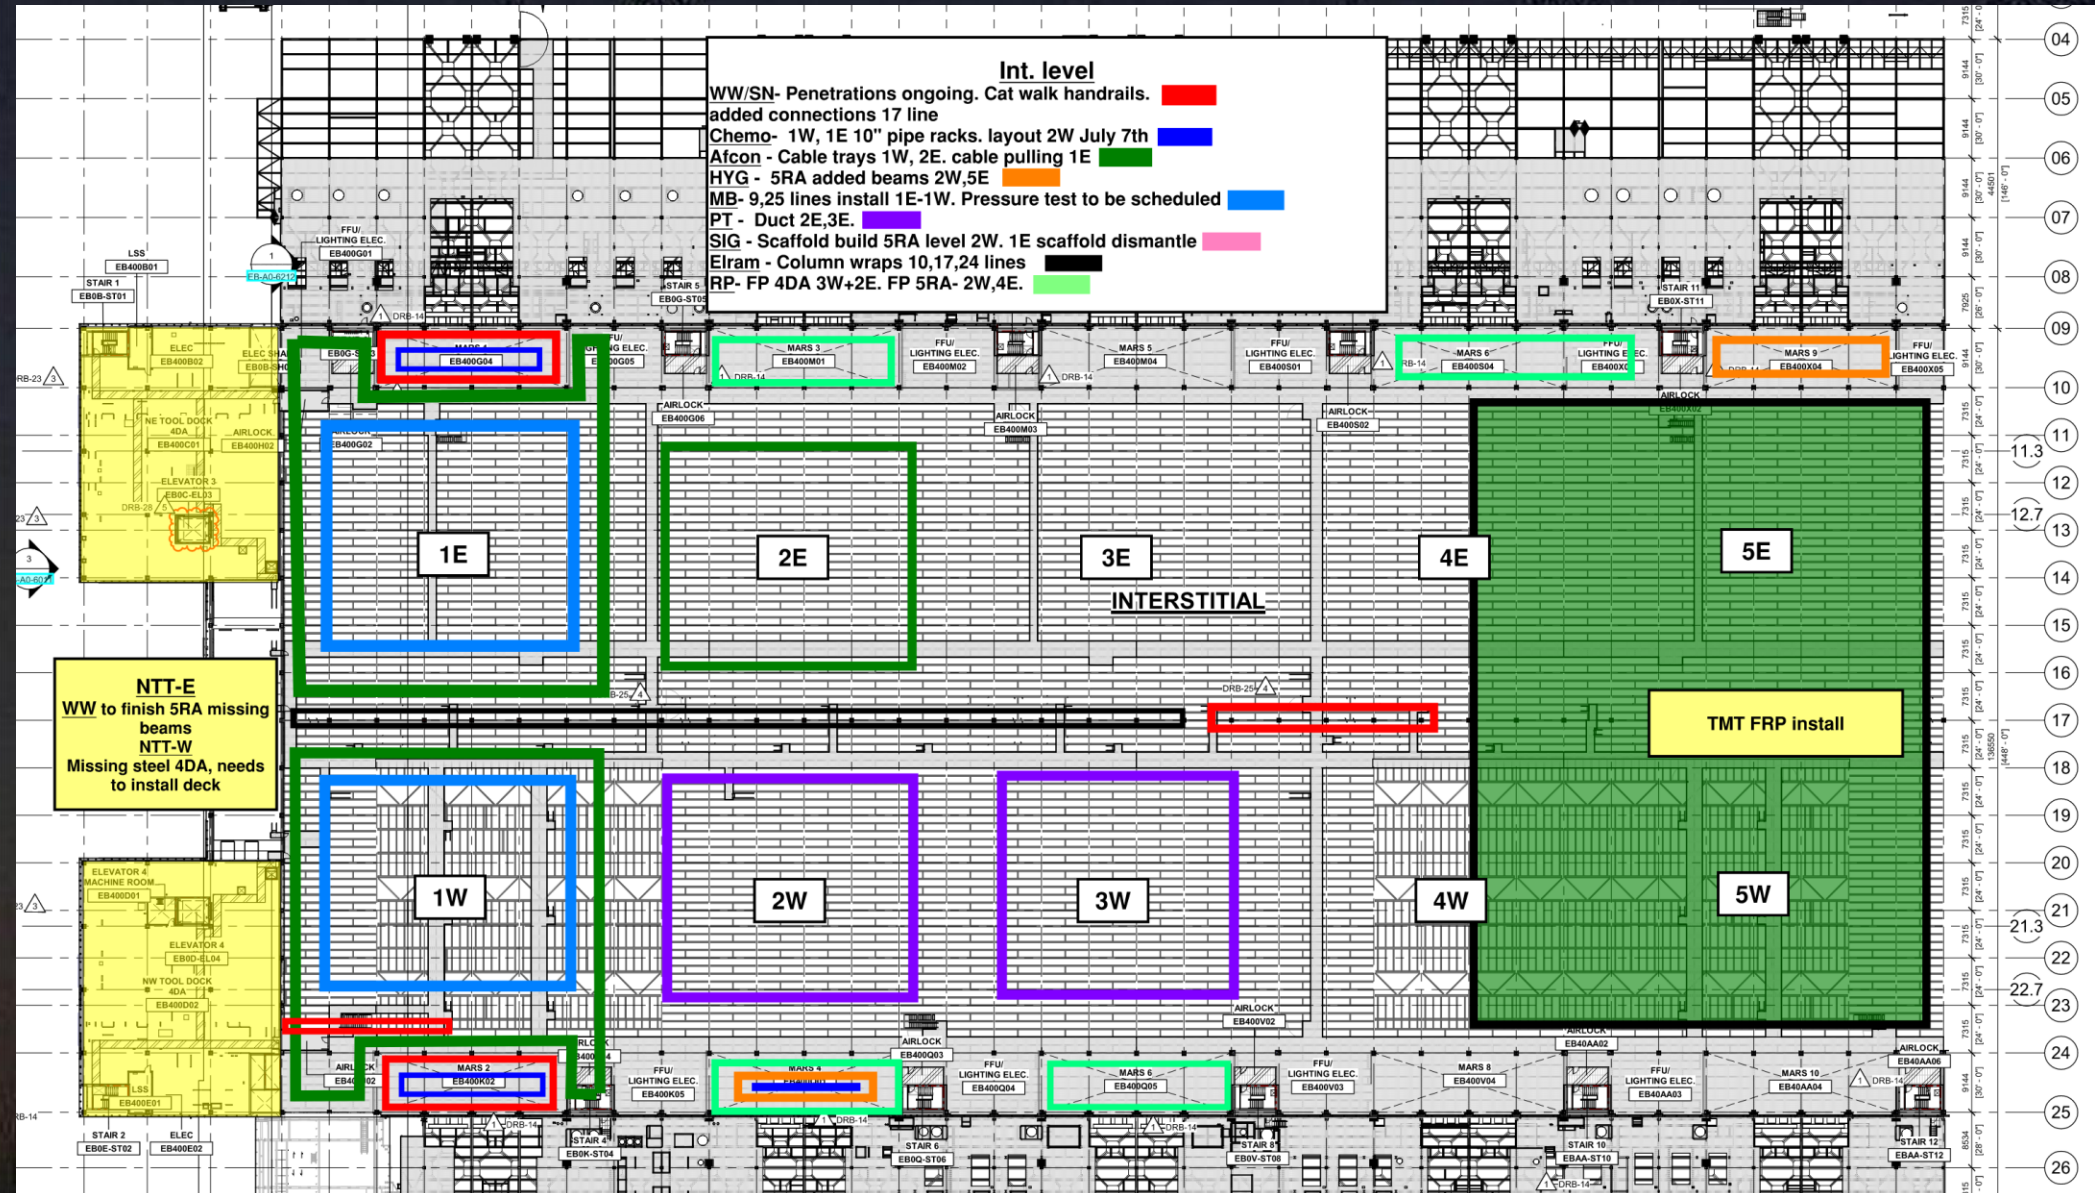


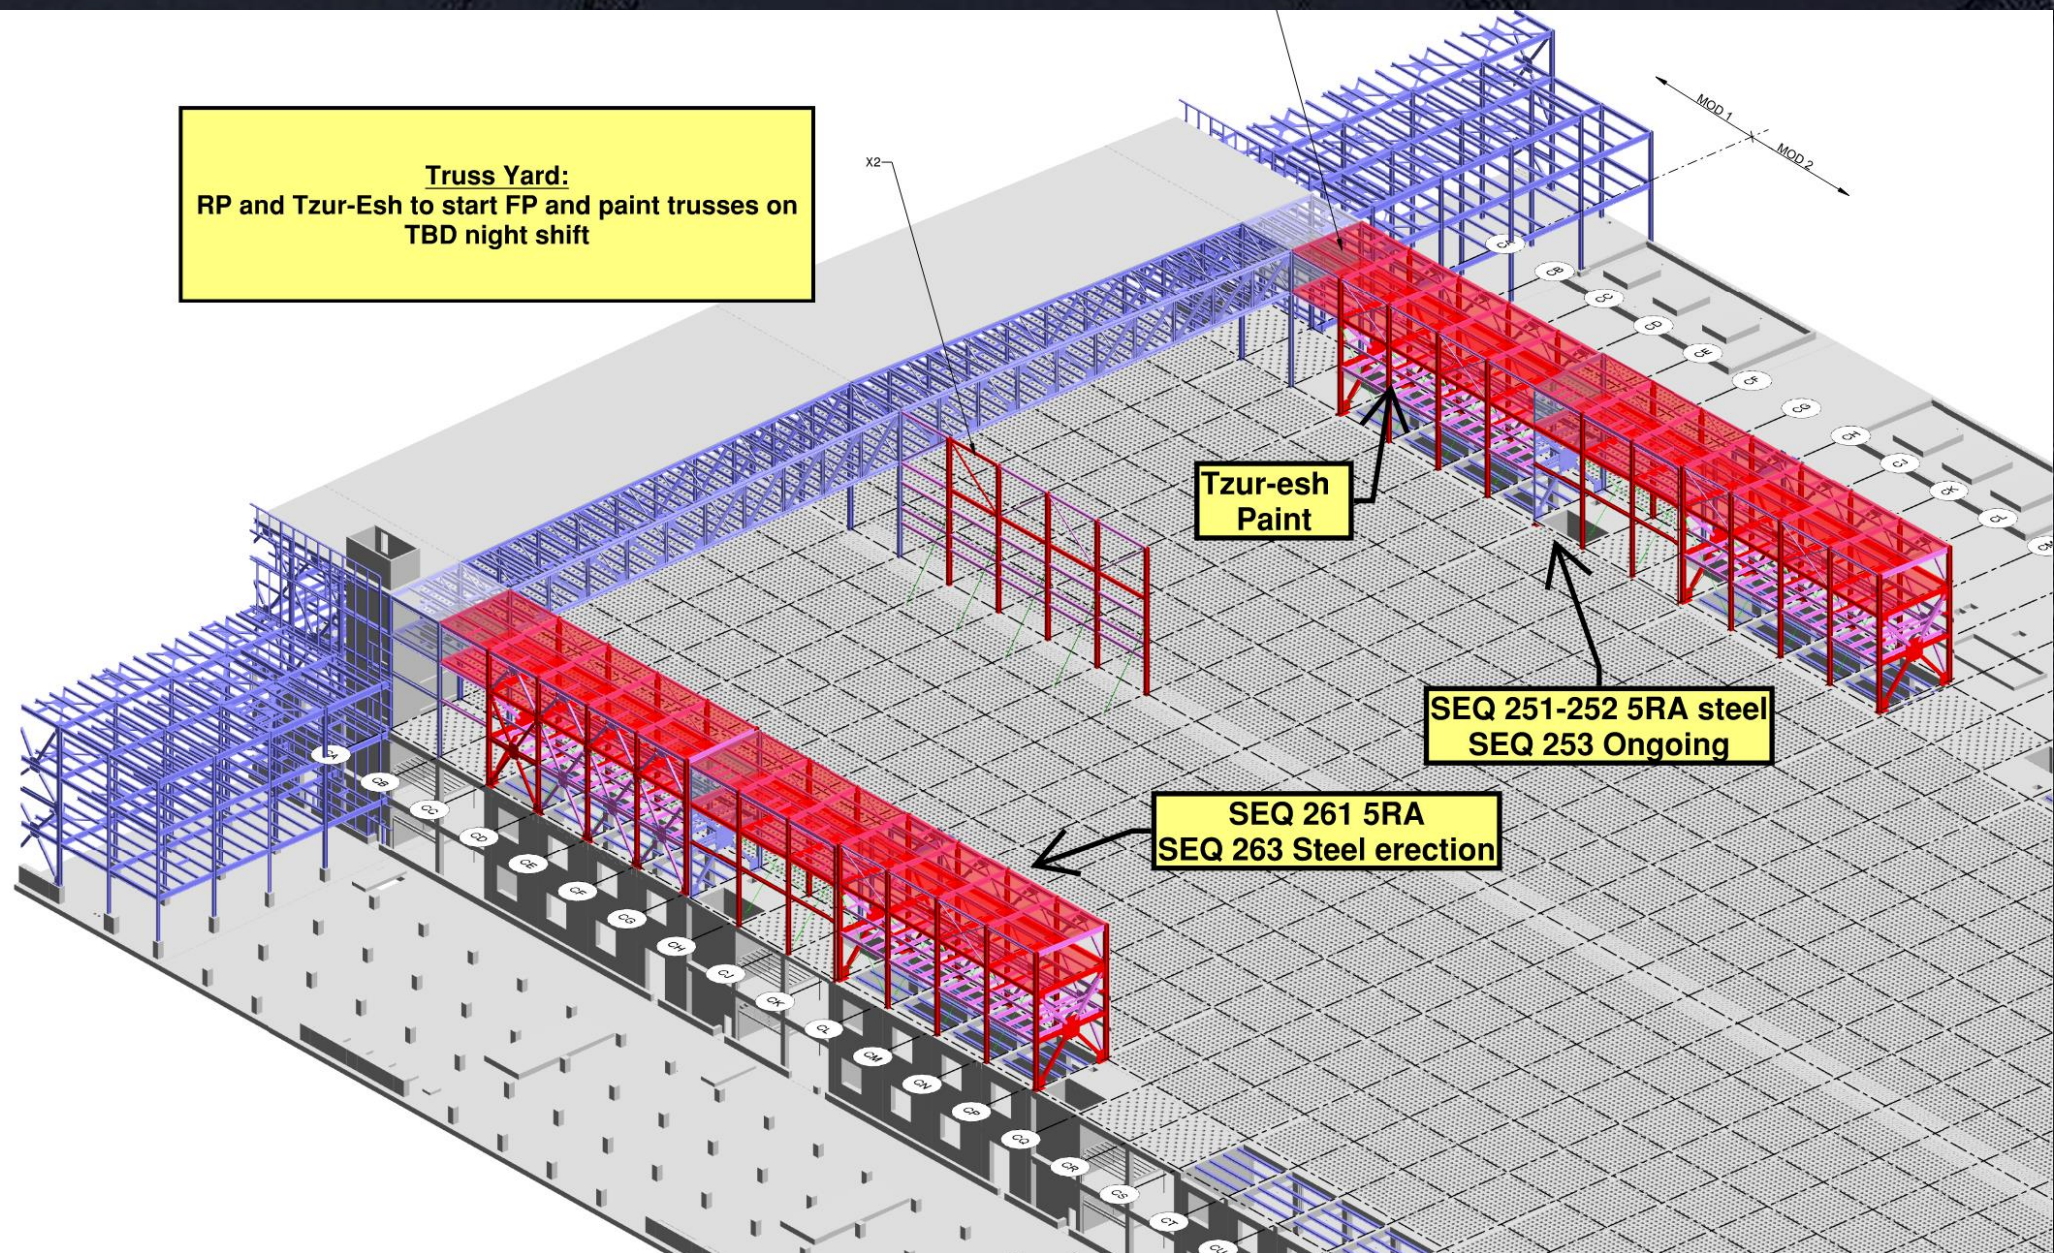

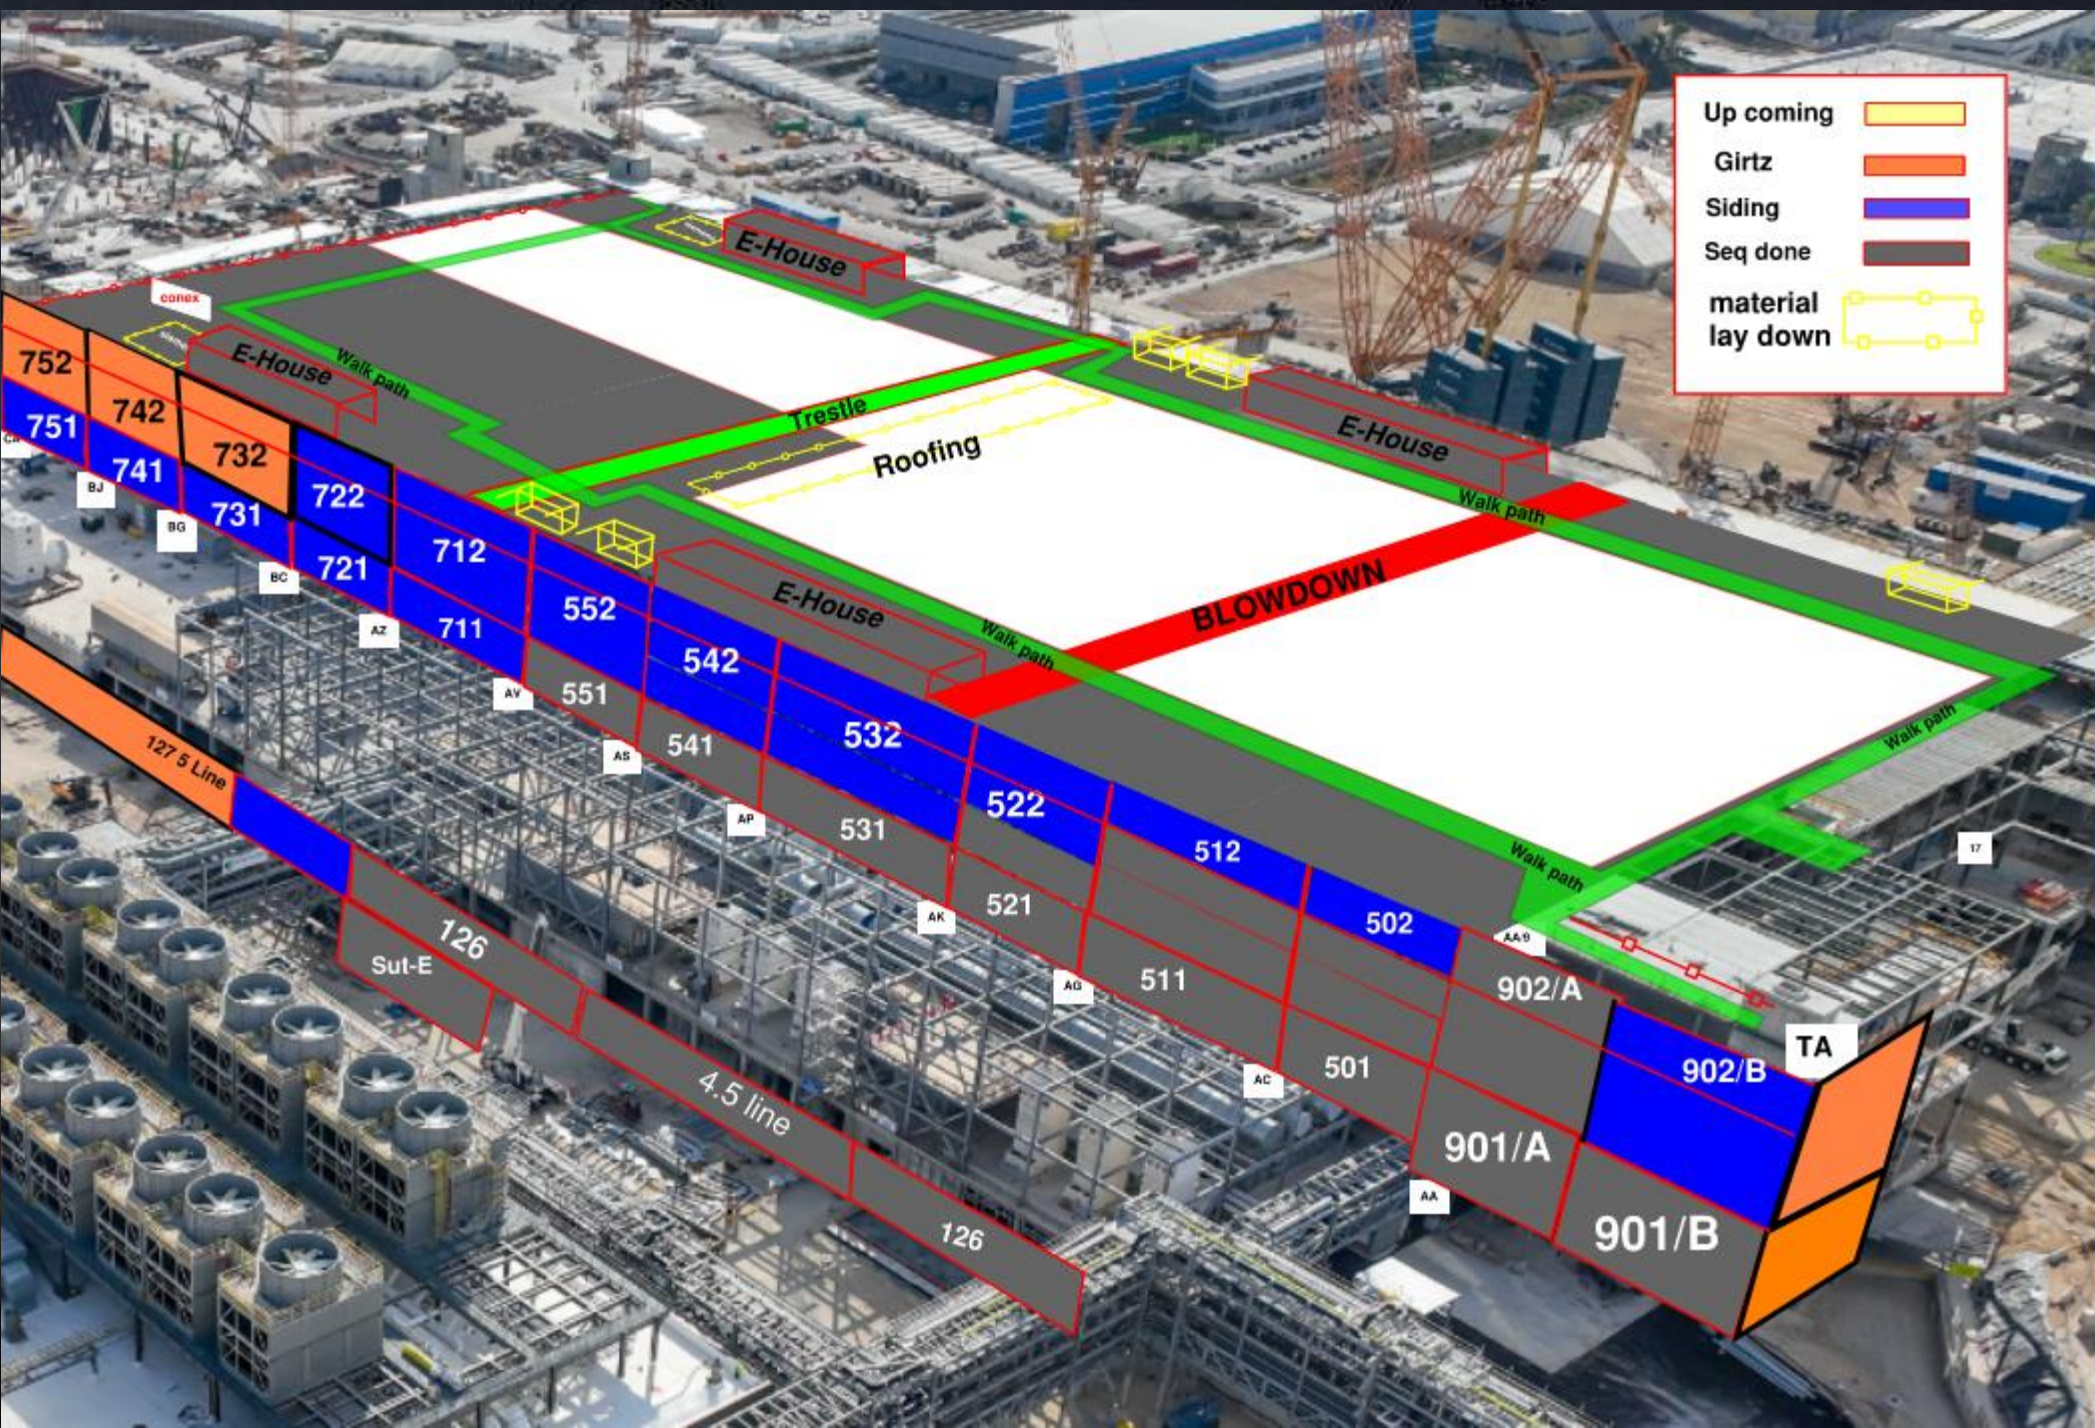


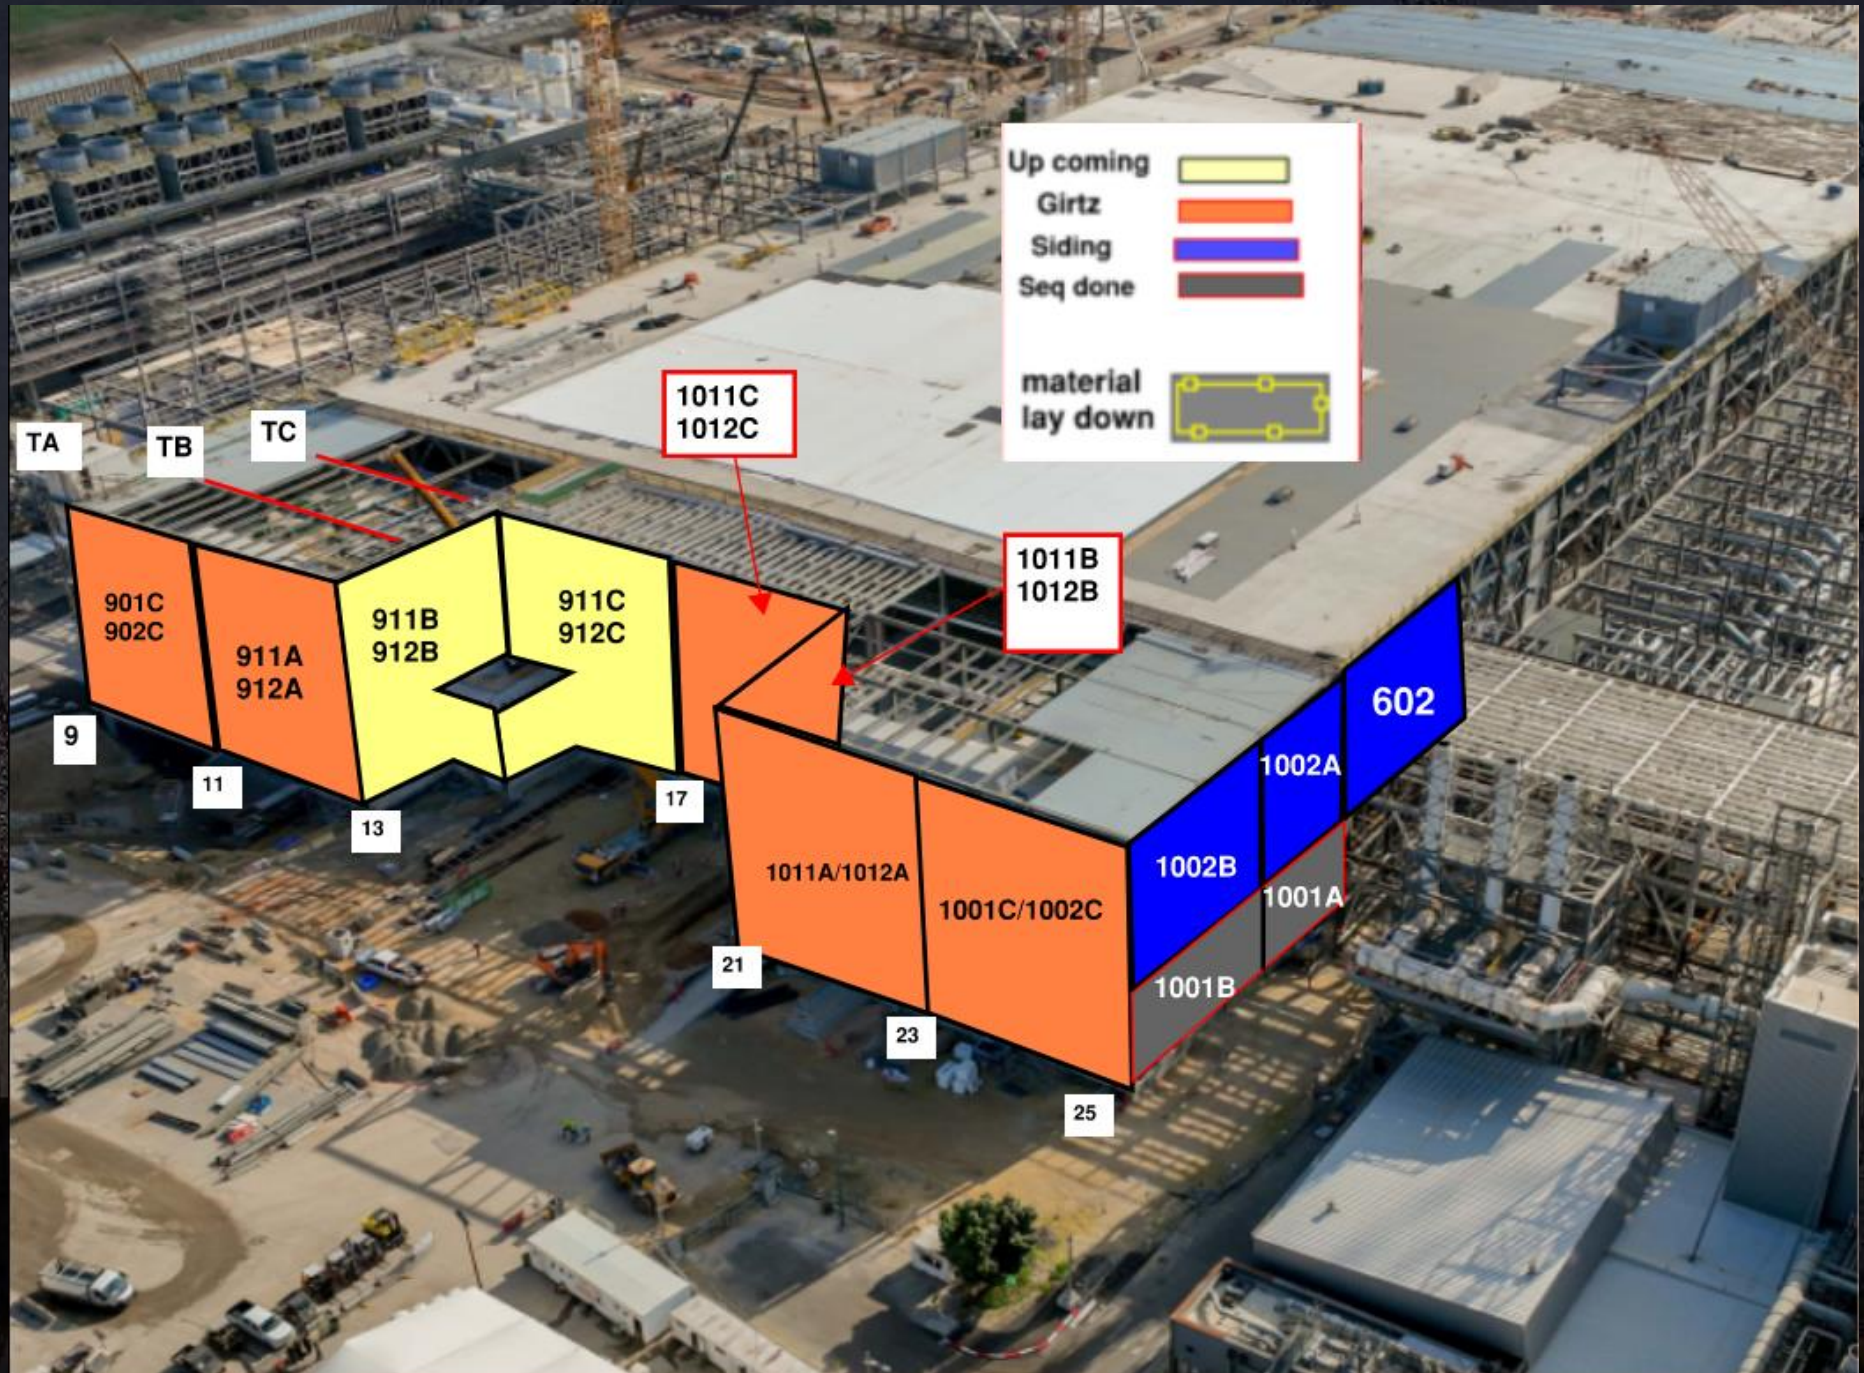

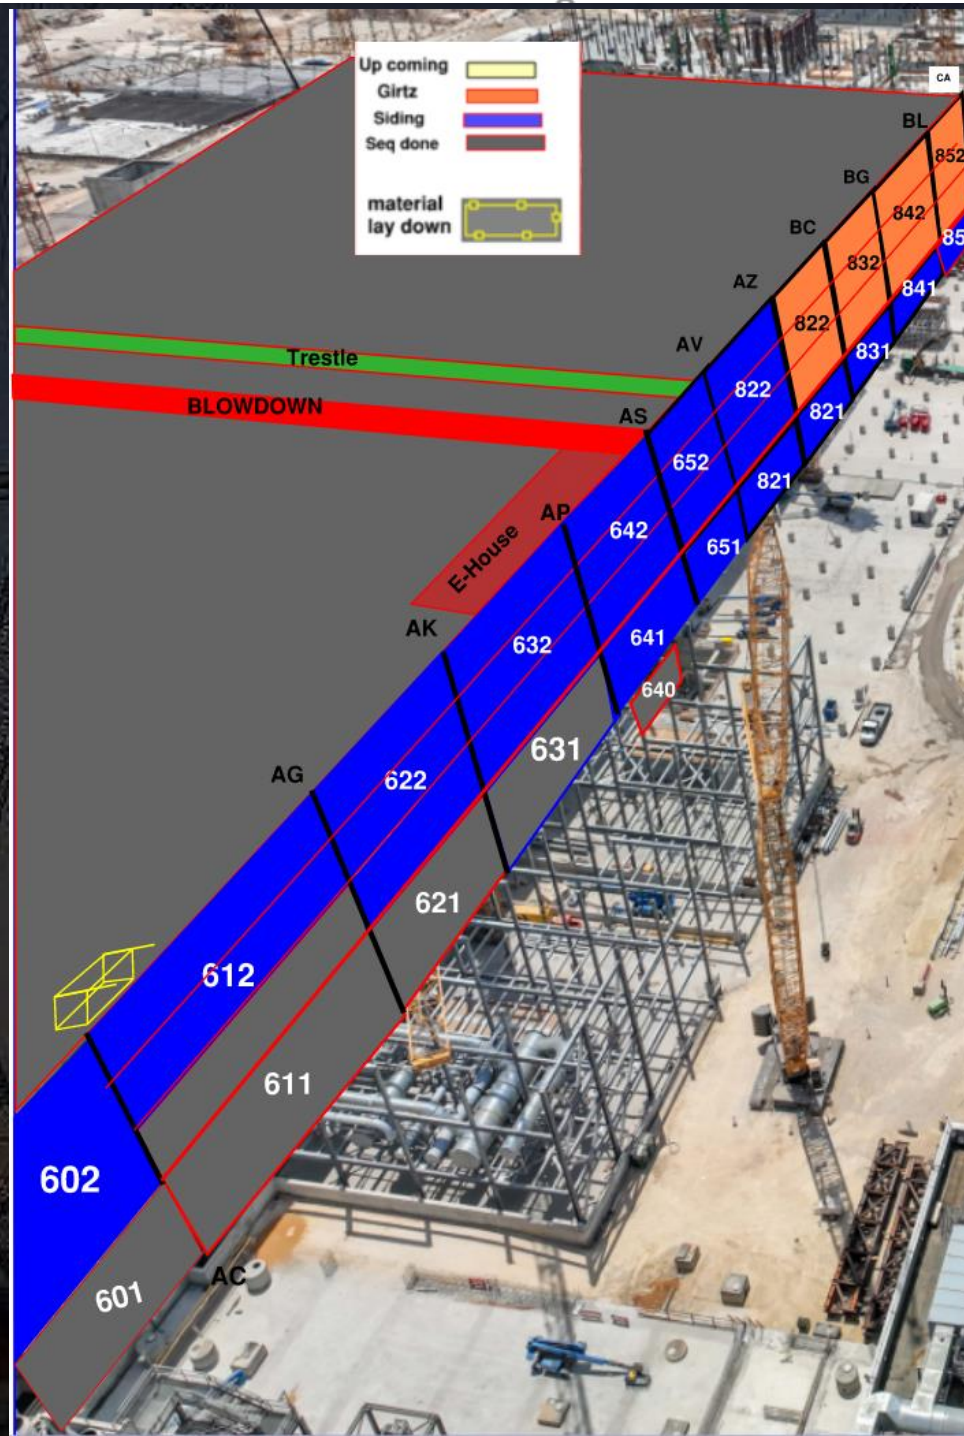

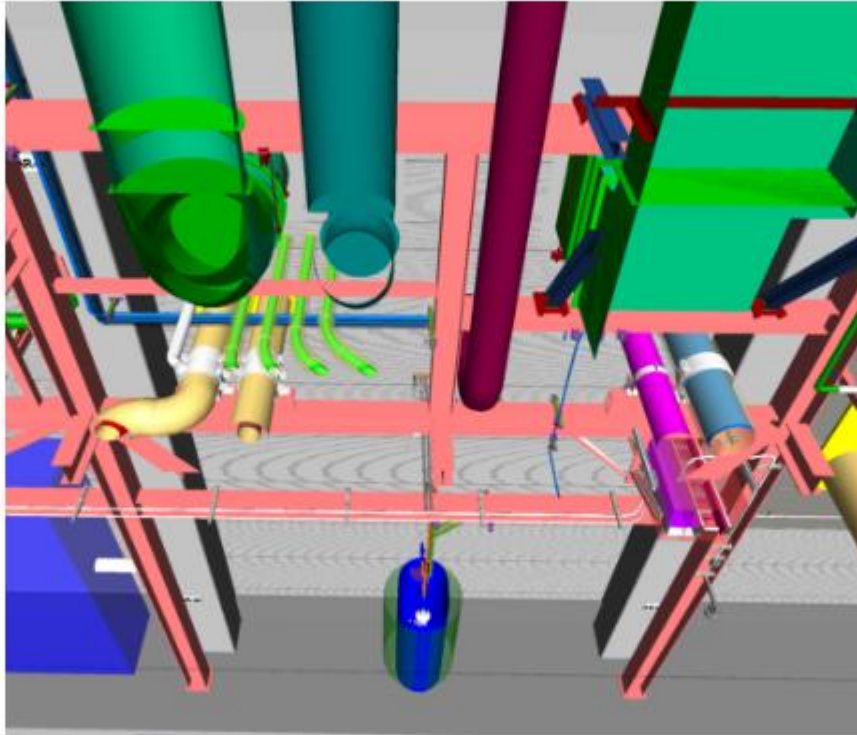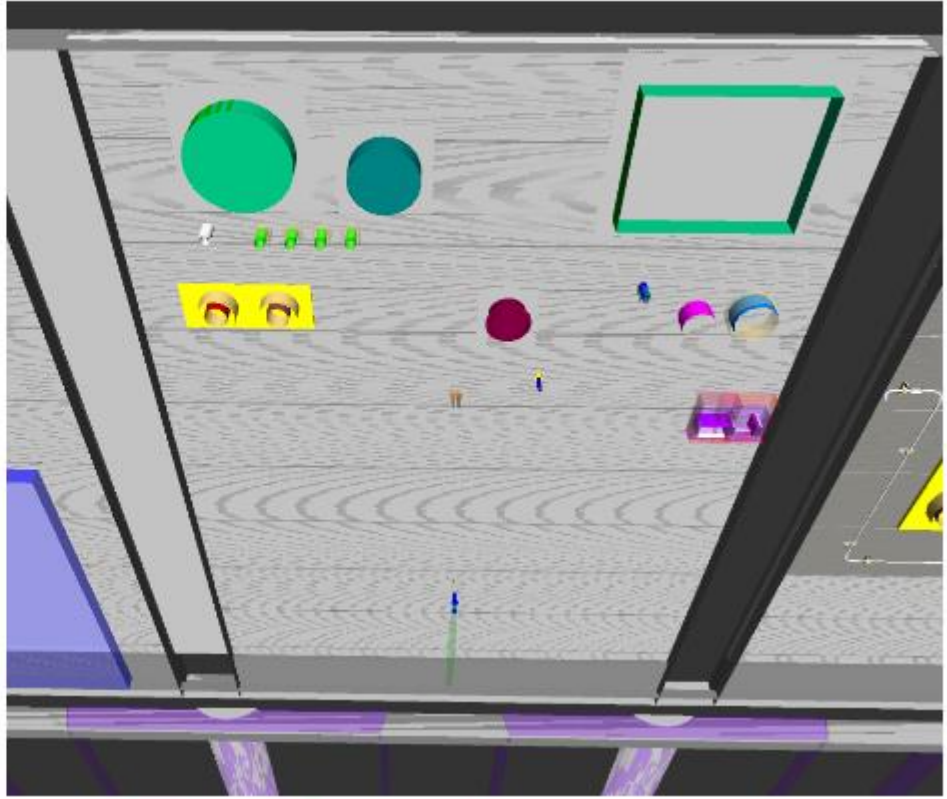

E-SUT1

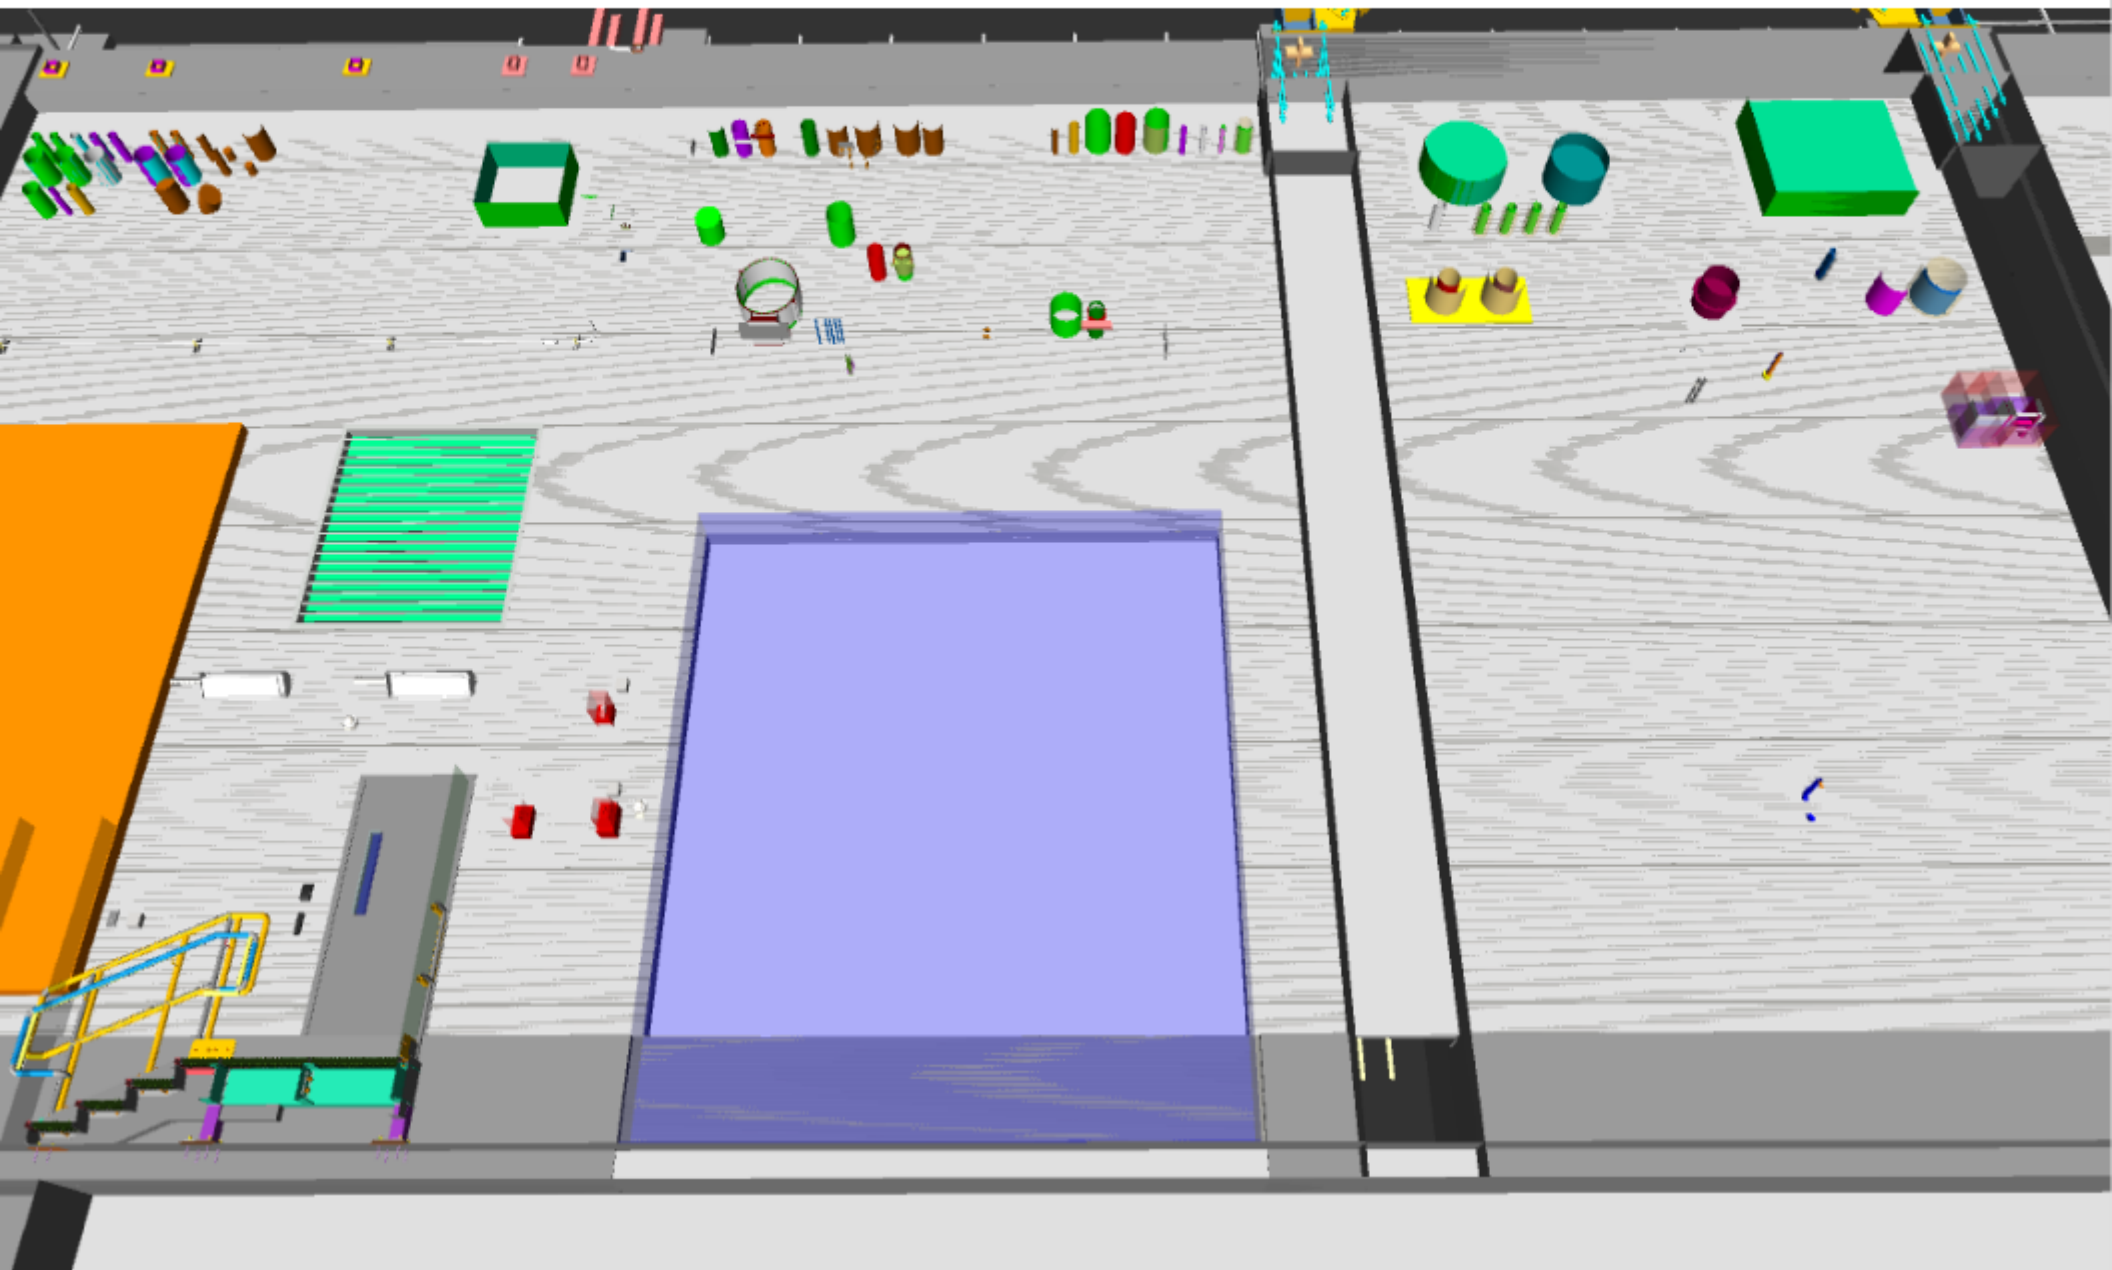


W-SUT1



AC/9

502

AA/9

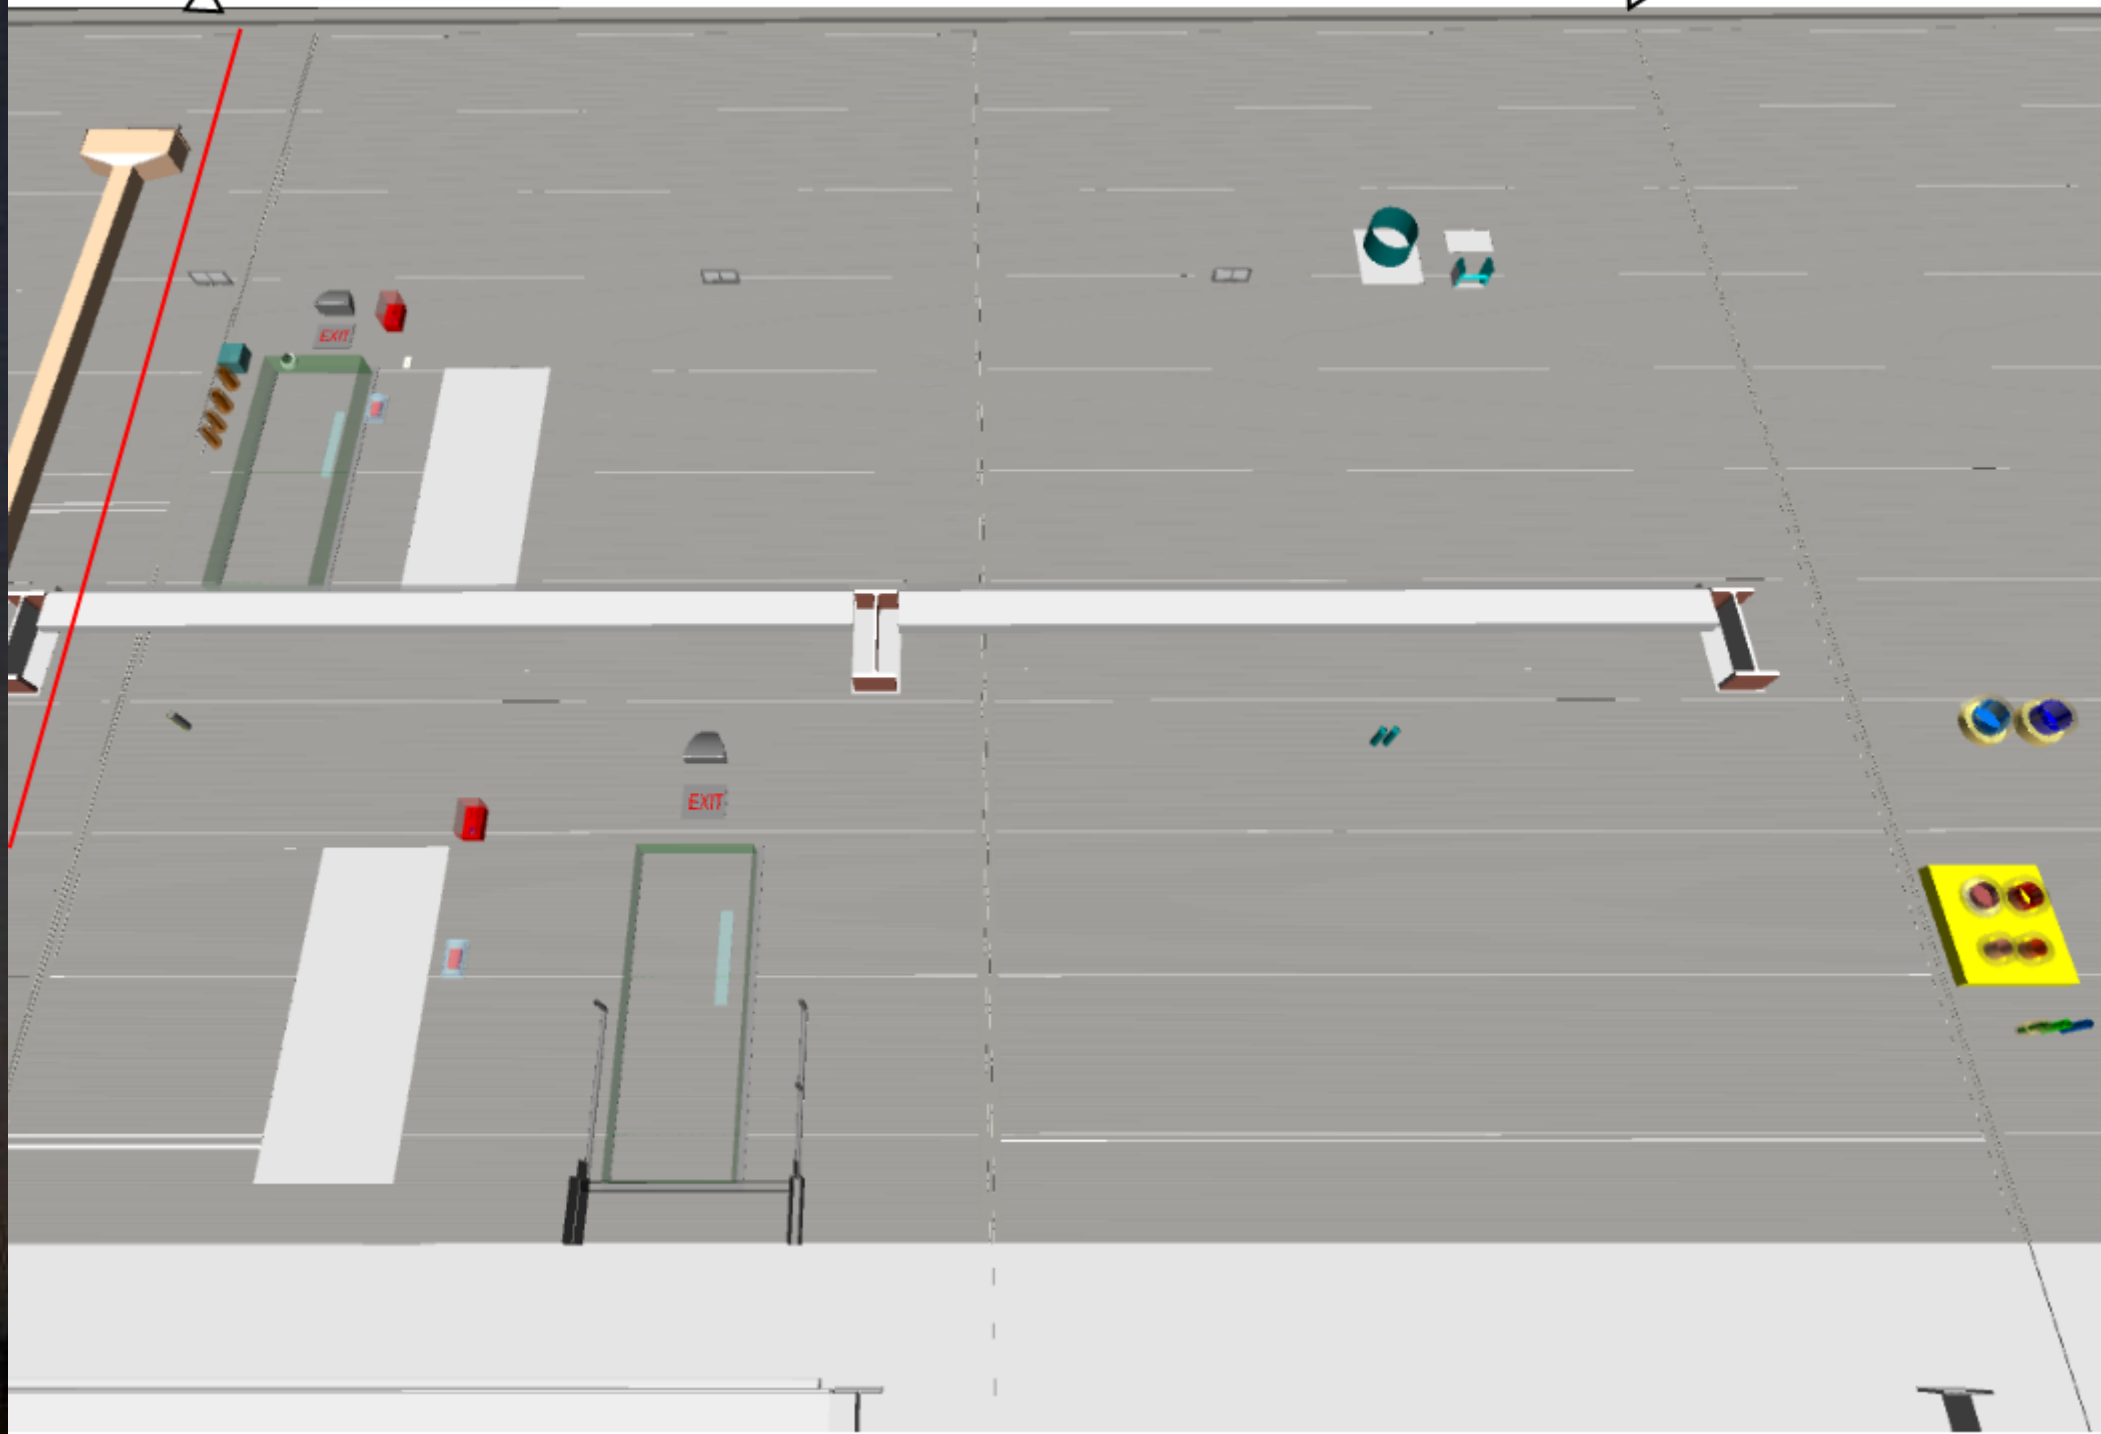


AF-09 and AN/9

SKE

Lift 1

AF-09

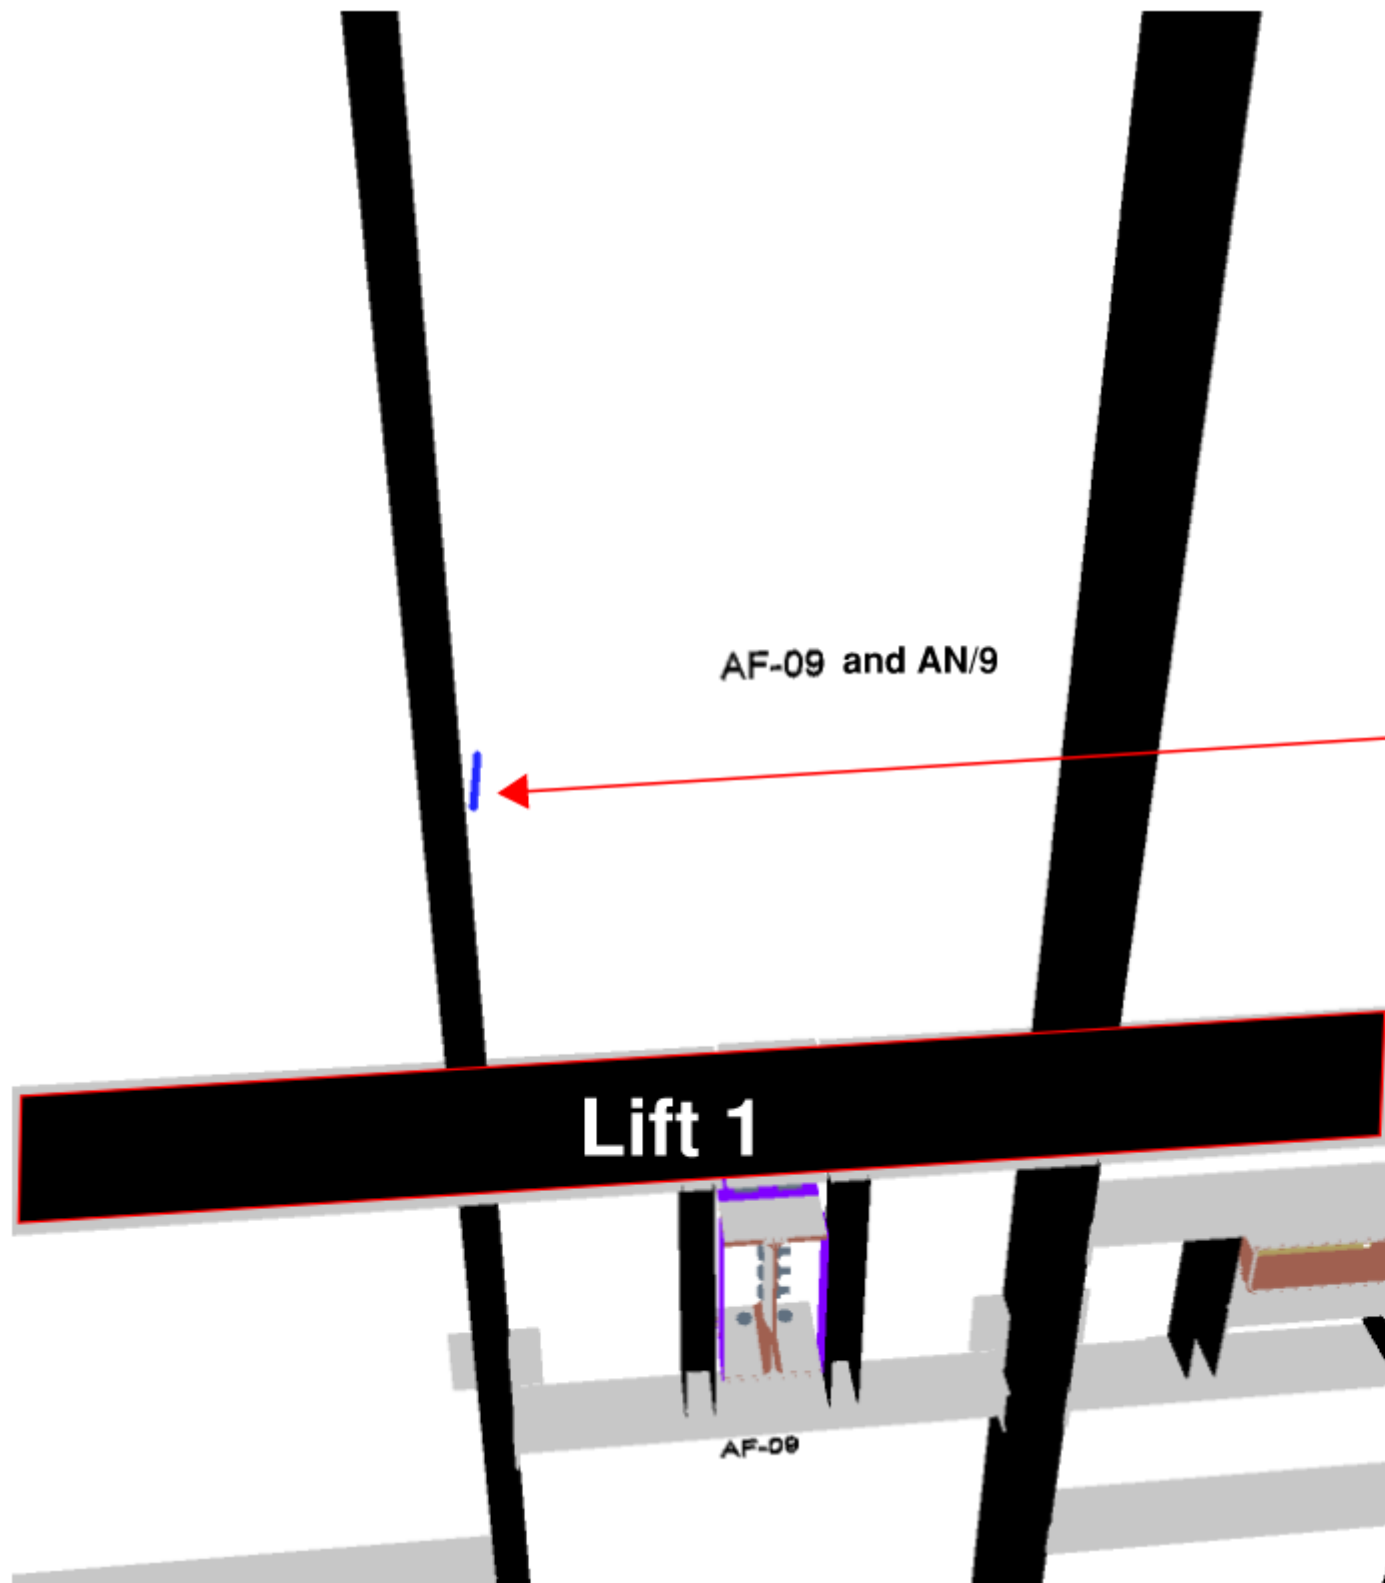

AD/25


612 lift 2

AG/25



Siding Penetration Request Form

Siding Penetration Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

smartsheet

Siding Penetration Requests

Location of Penetration * ← What Gridline and Elevation is the penetration?
Gridline and Elevation of where the penetration is being requested.

Layout Used * ← How was the penetration laid out
What was used to layout the penetration

Size of Penetration * ← What is the required penetration size?
Input the size of the requested penetration in mm.

Company * ← Company Requesting Penetration
Company that is requesting the penetration

Contact Person * ← Who to call in event of questions
Who is the contact for this request

Contact Phone Number * ← Phone Number of said person

Contact Email * ← Email of said person

Layout has been Confirmed * ← Confirmation of layout
Confirmation that the layout has been double checked. If the layout is incorrect, the requesting contractor will be responsible for all required repairs or panel replacements.
☐

Date of Request * ← Date of Request


Photo of Layout * ← Photo of completed layout in the field
Upload a photo of the layout that has been completed

☐ Send me a copy of my responses

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

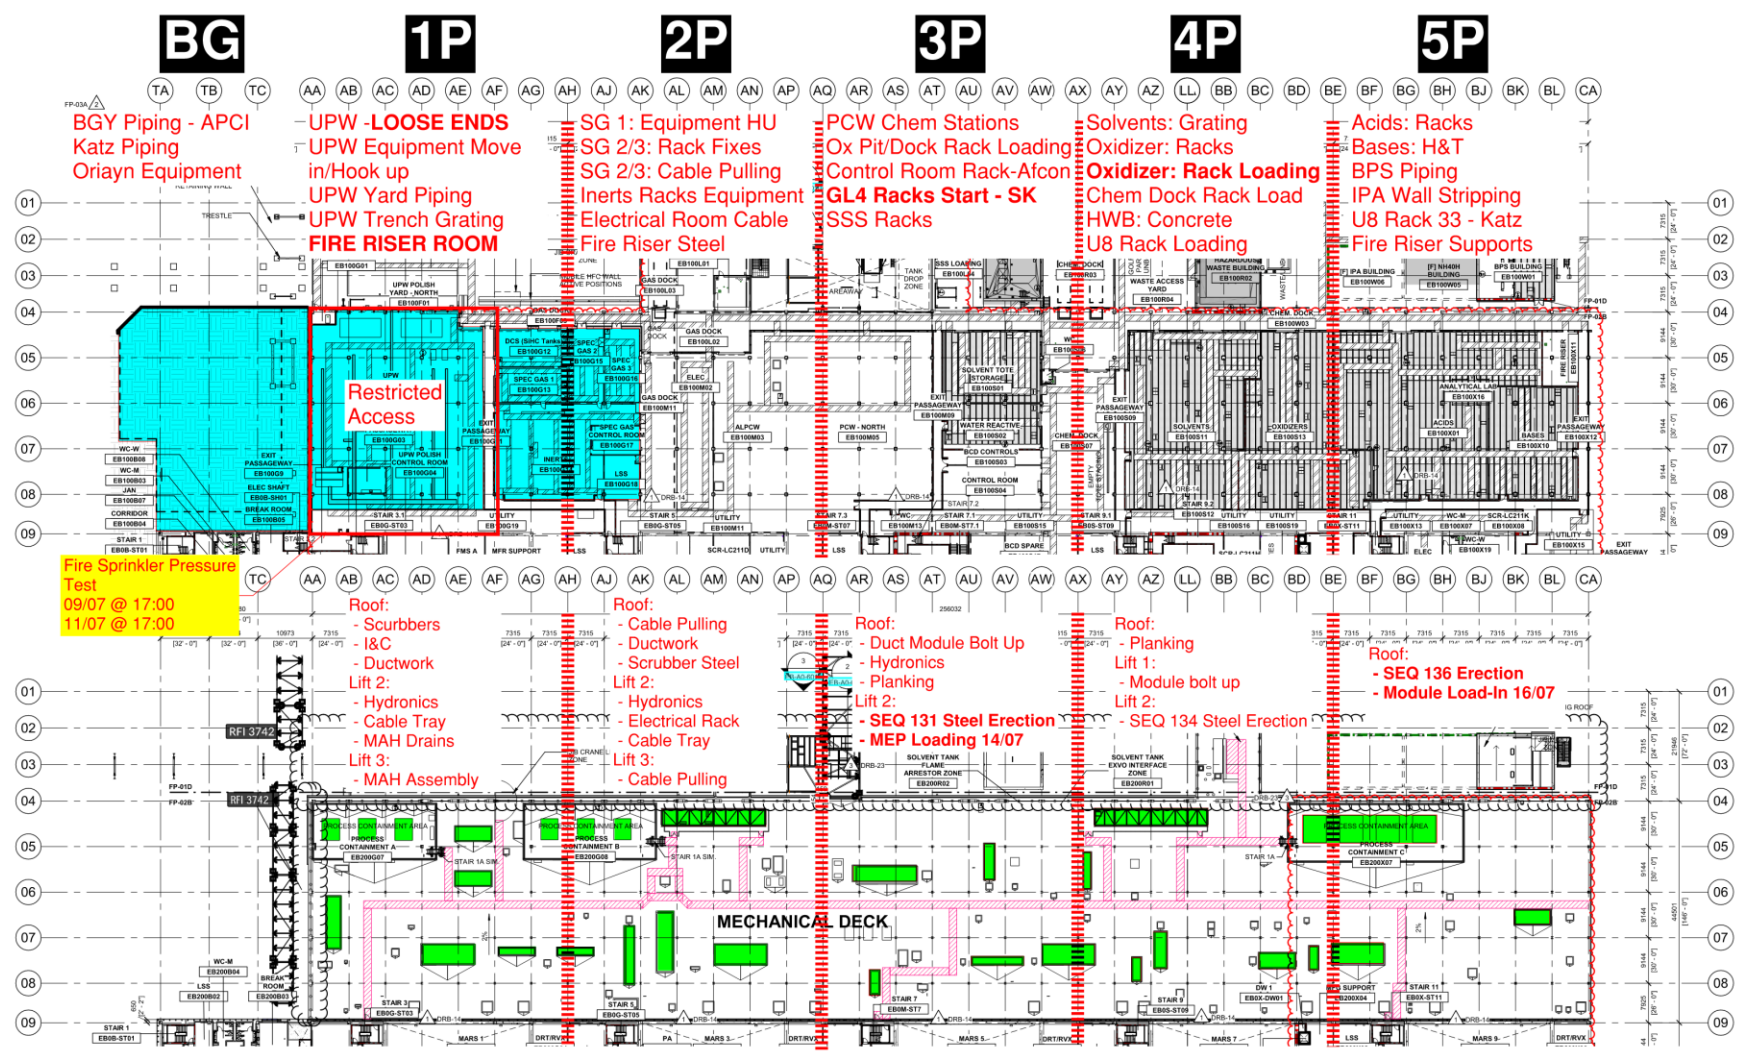


PSSS DMAG DISMANTLE

- July 21st-25th
 - UPW MIMO CLOSED
 - GAS MIMO CLOSED
 - GUT ROAD BLOCKED FROM TRESTLE BRIDGE TO TRESTLE BRIDGE

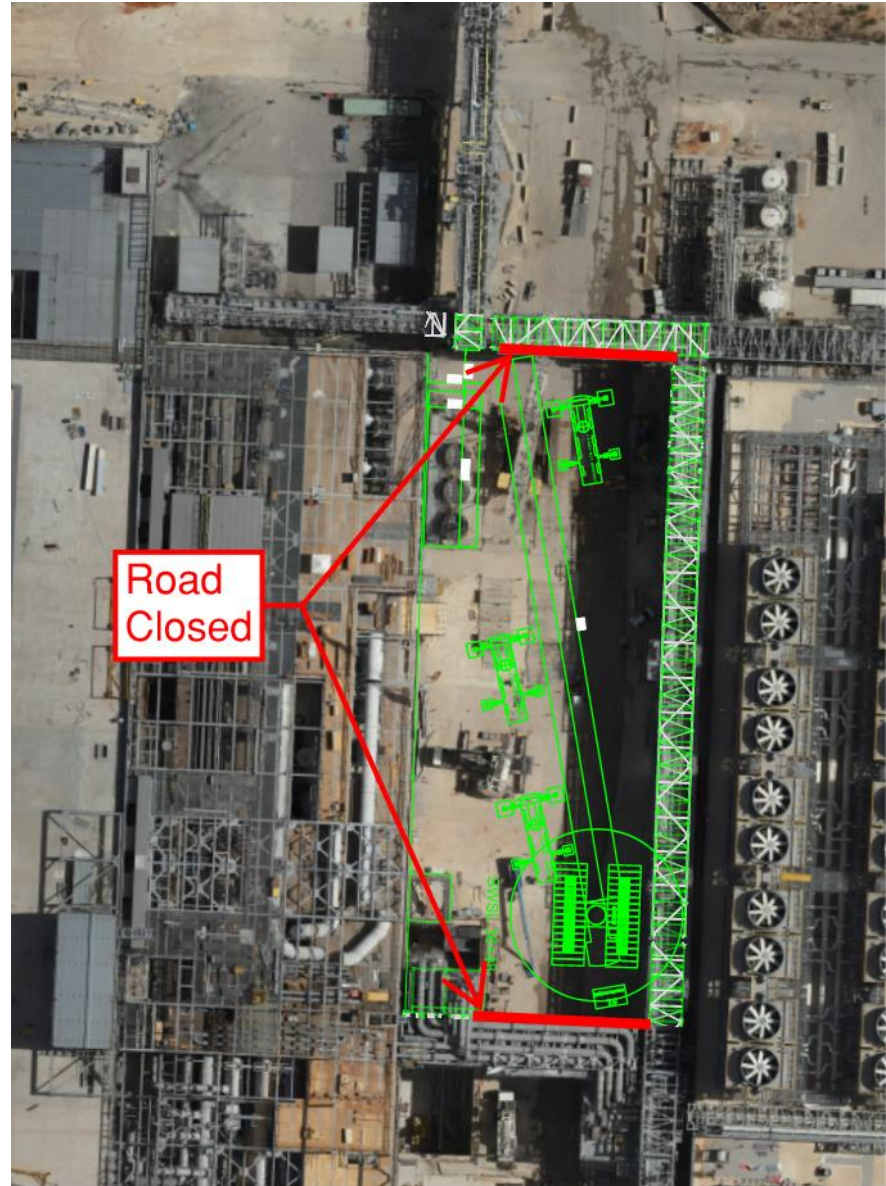

EJG/WJG Grating/Planking Penetrations



JG Grating/Planking Penetrations

Type of Penetration *
What side of the building is the penetration located?

Location of Penetration *
Provide gridlines of where the penetration is needed

Zone of Penetration *
What zone is the penetration

Lift of Penetration *
What lift of Steel is the penetration

Gridlines of Penetration *
Input the gridlines of where the penetration is located

Size of Penetration *
Put size of penetration required in mm

Contact Company *

Contact Number *
Contact number in the case of questions

Contact Email *
Email of person to get notifications on penetration

Layout Confirmation *
Confirmation that layout has been confirmed by requesting contractor. If layout is incorrect, the requesting contractor will be responsible for all fixes, build backs, replacement, etc. cost associated with the incorrect layout.
☐

Photo of Layout in the field *
Upload a photo of the layout once complete

Drag and drop files here or [browse files](#)

☐ Send me a copy of my responses



WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3





WJG UTILITY LEVEL BUILD OUT

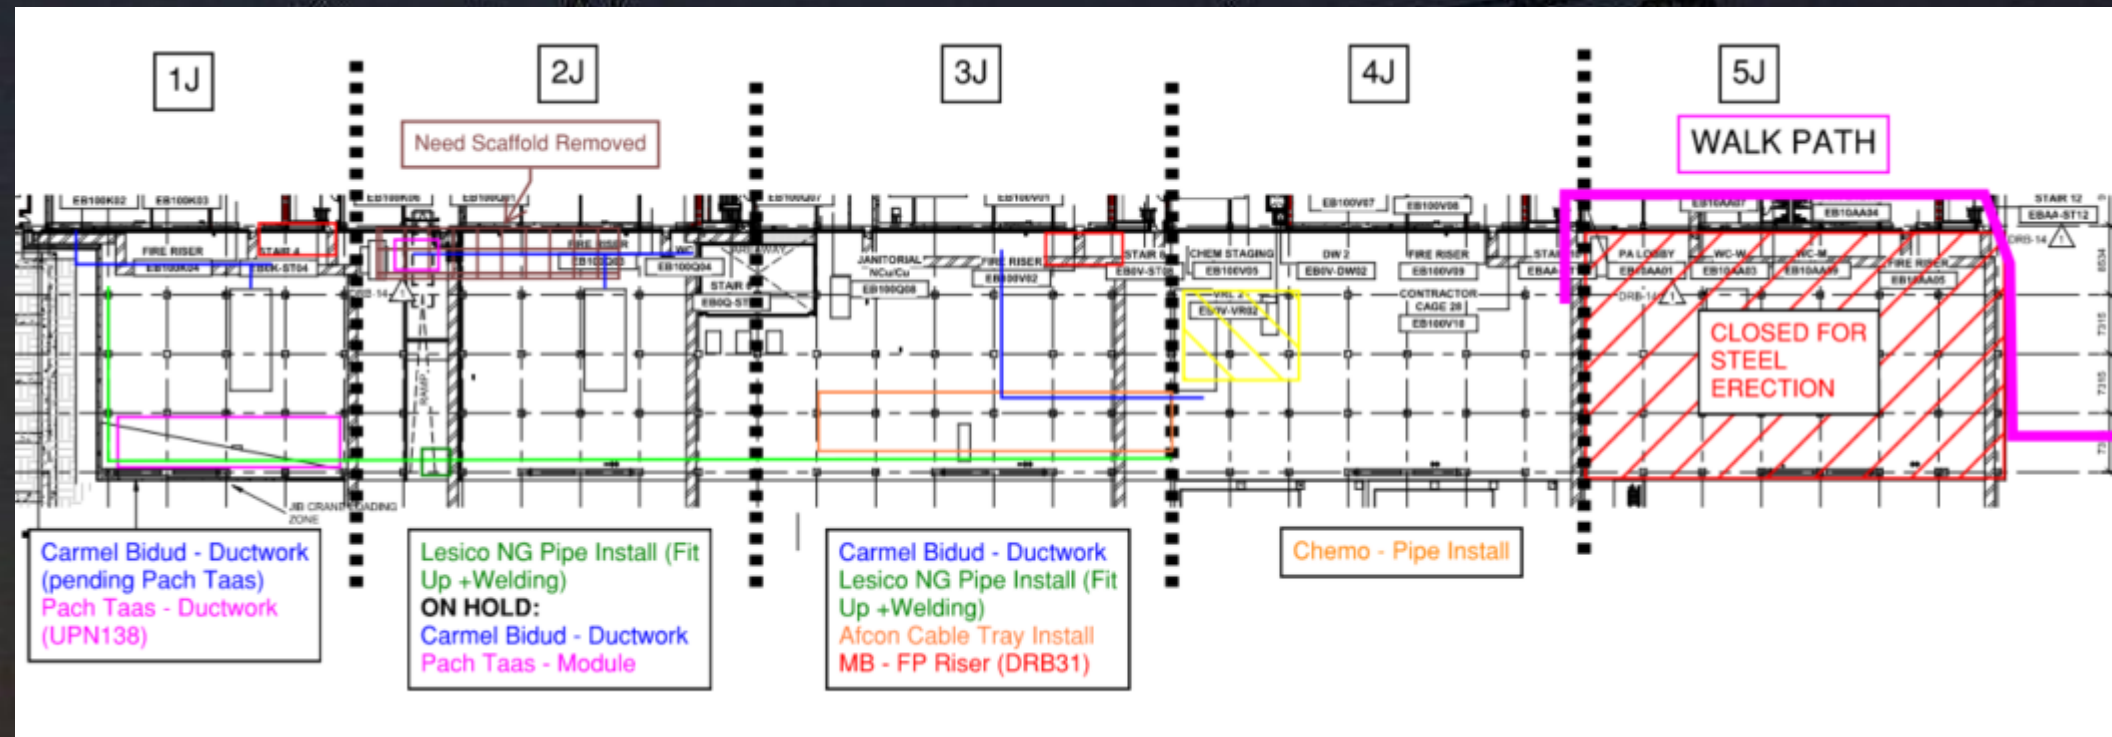


UPN 116





Flushing will enable
HUPW Heat
Exchangers (located on
Utility level sector 2W)


UPN 117

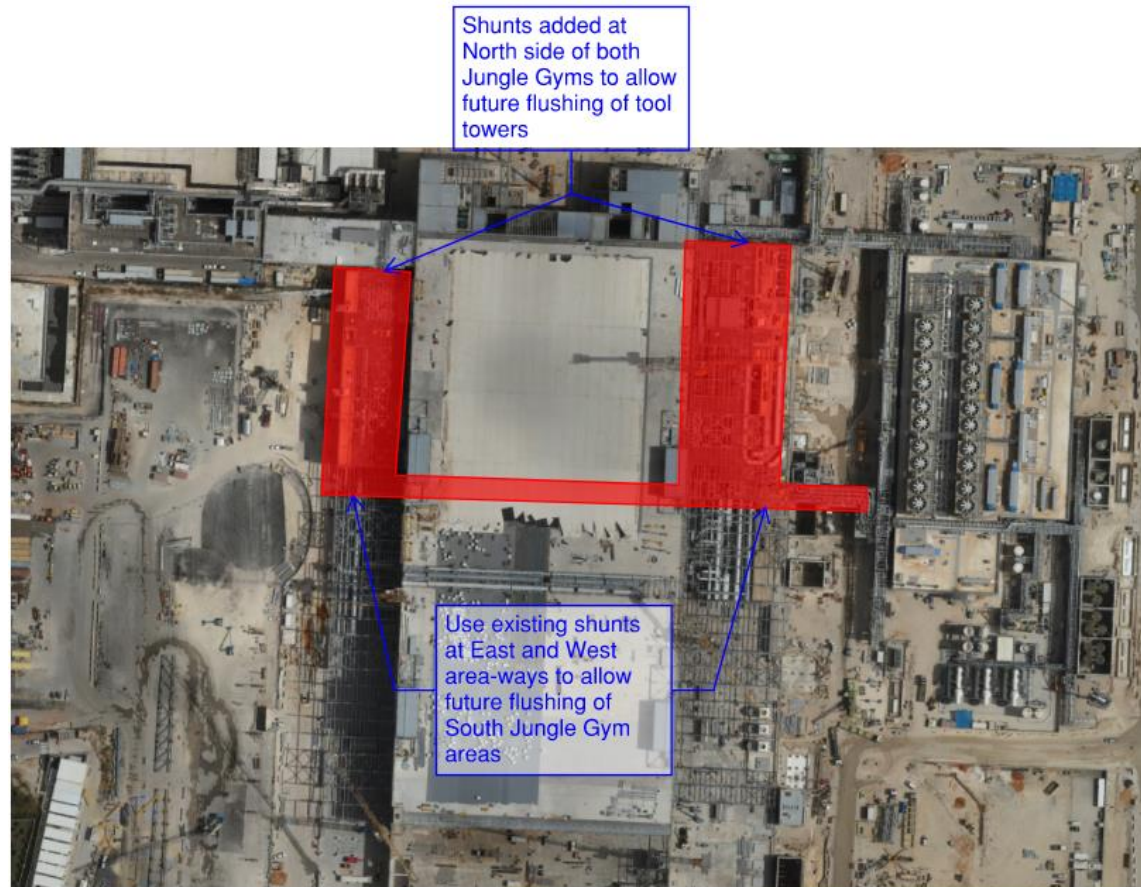


Flushing will enable
30% Blowdown MAH's
and Spec Gas room
Heating coils

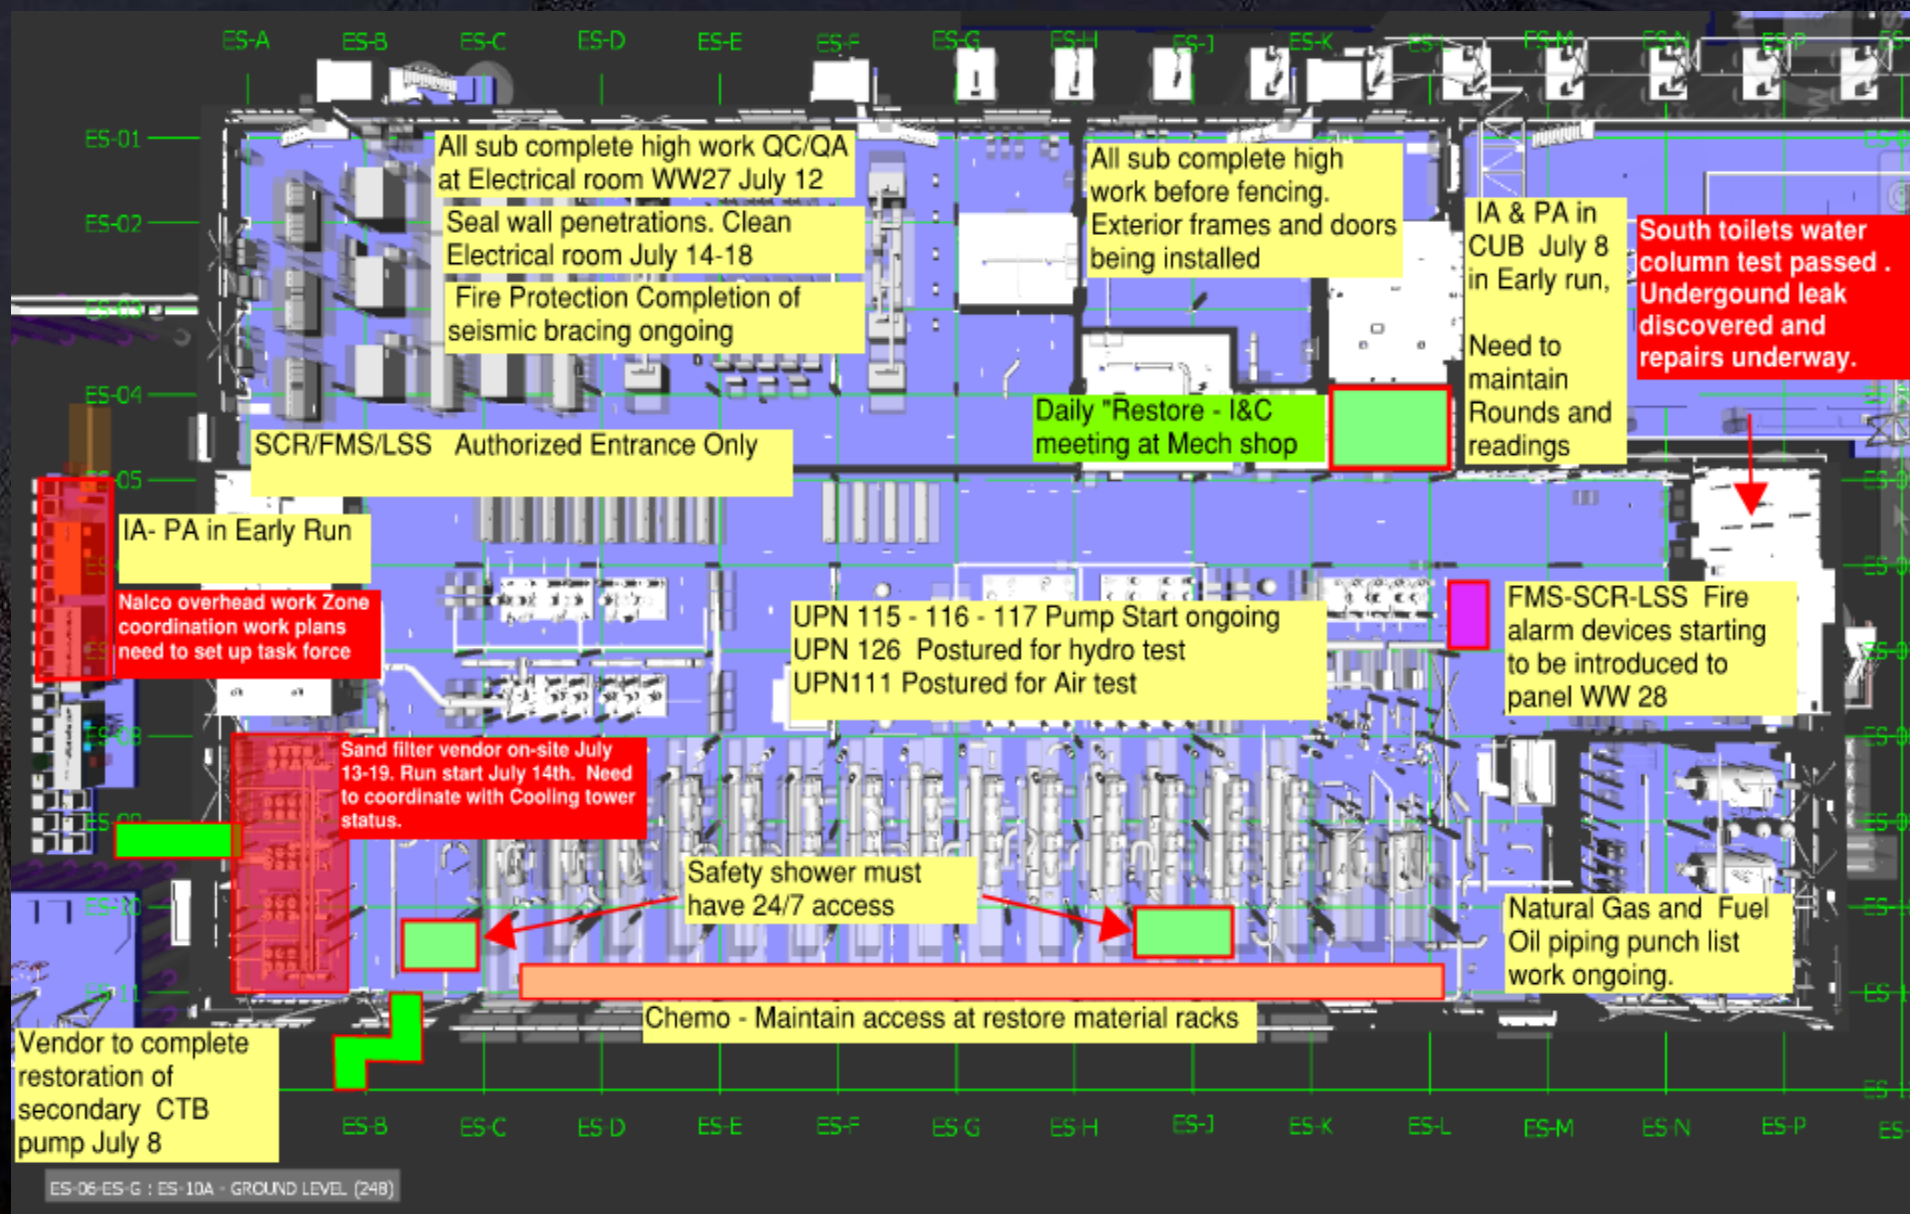

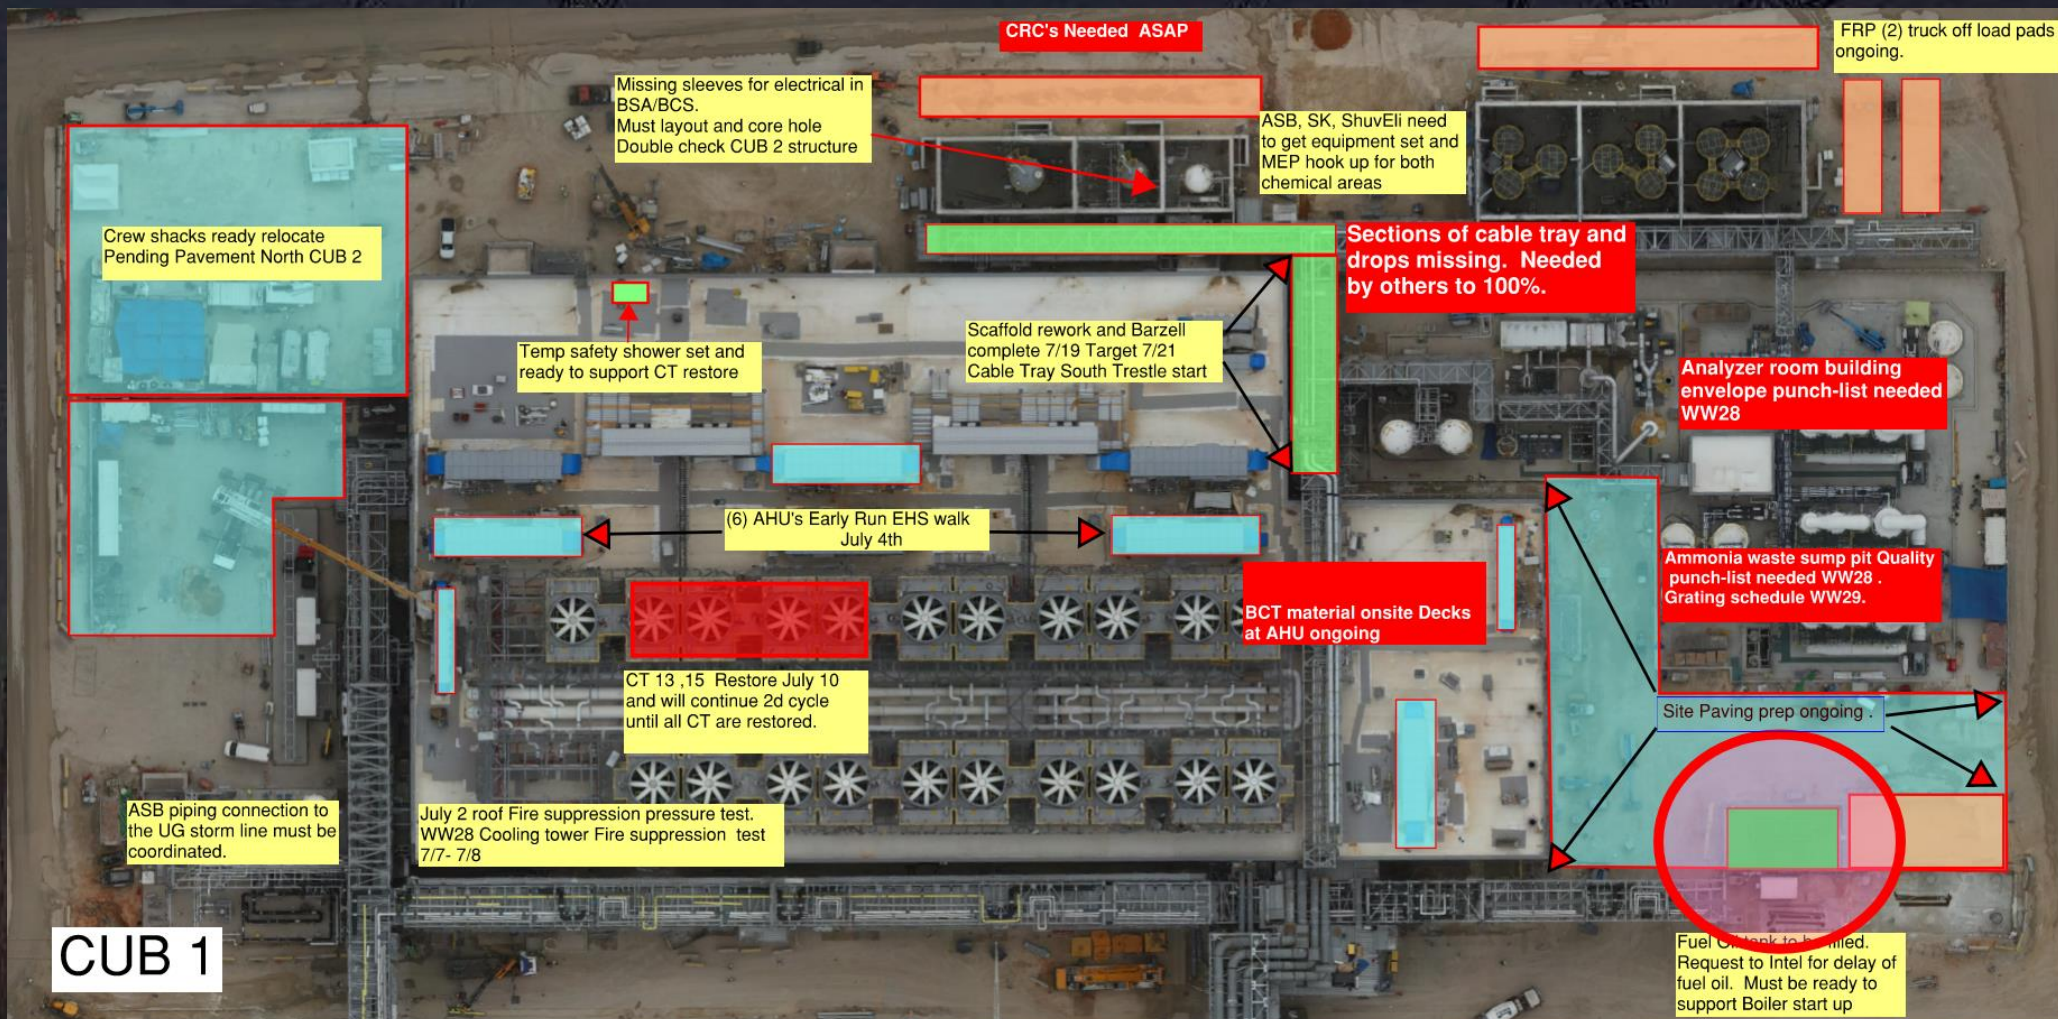

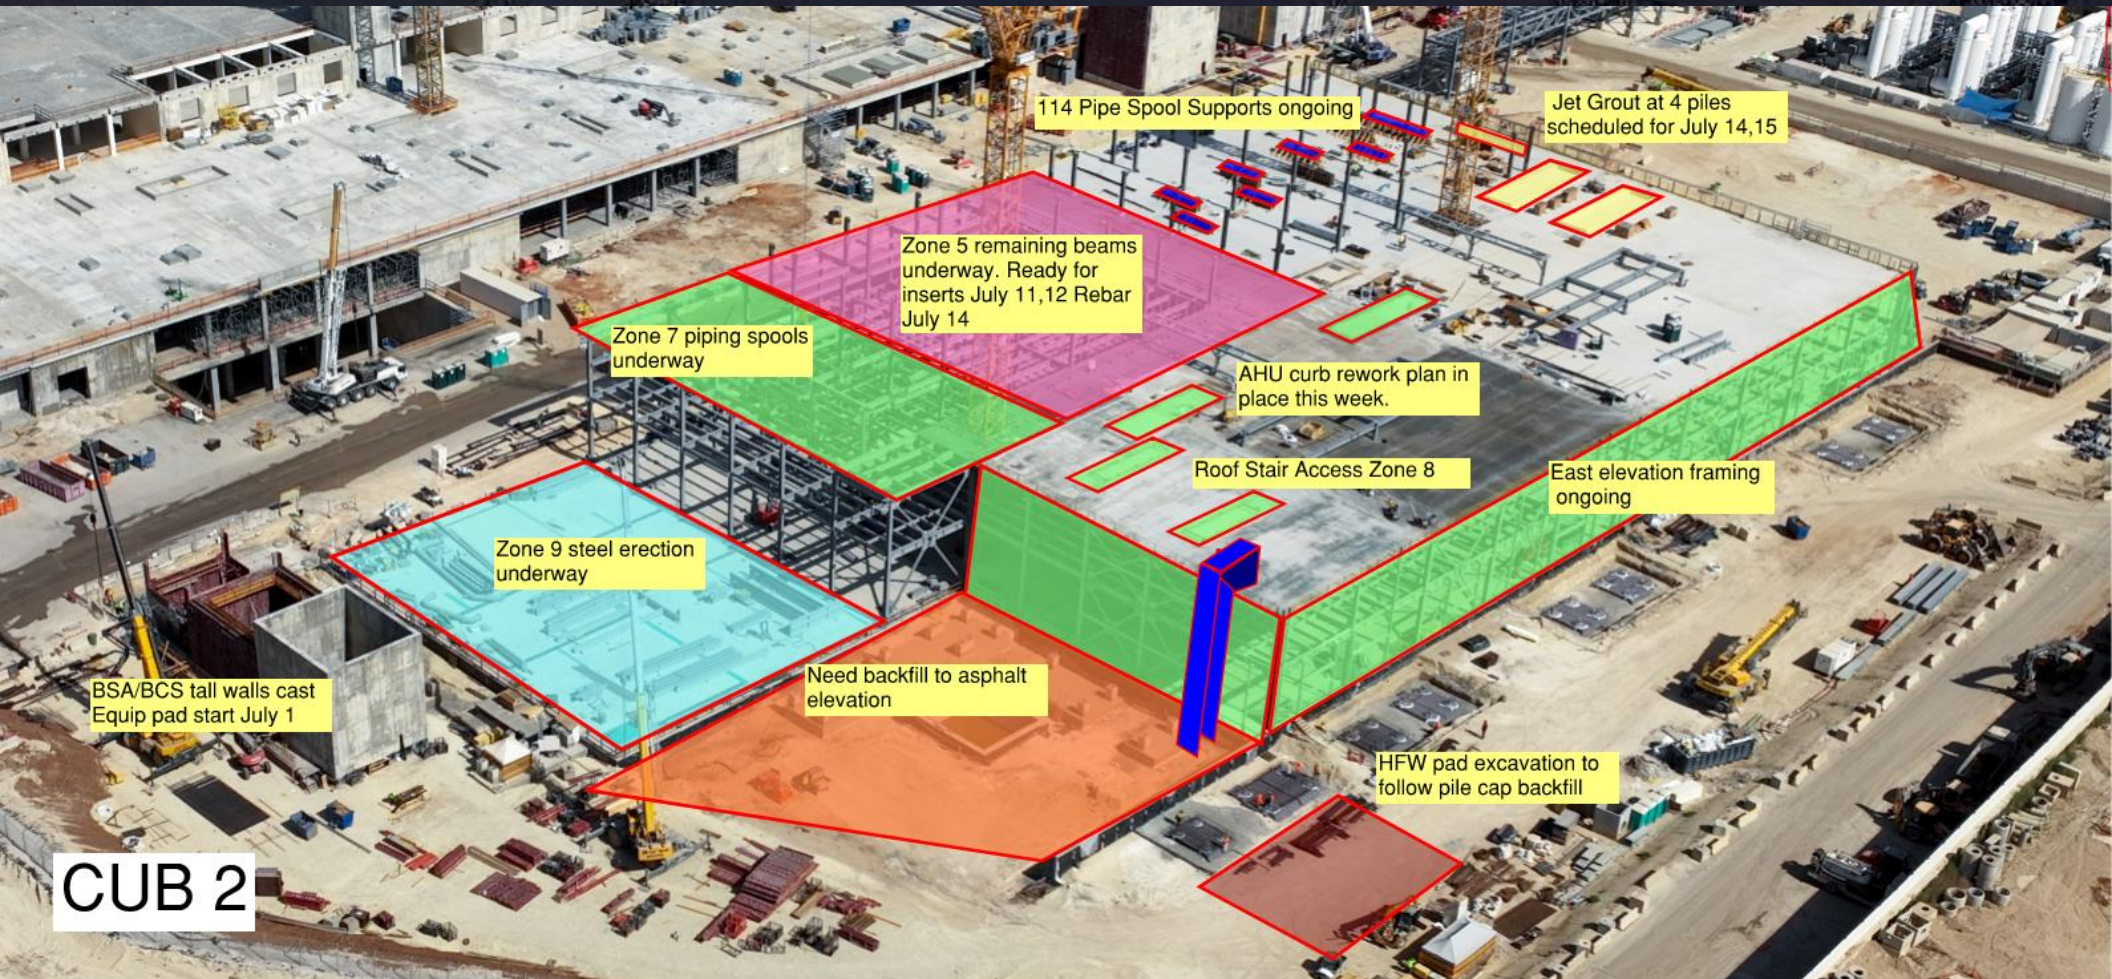

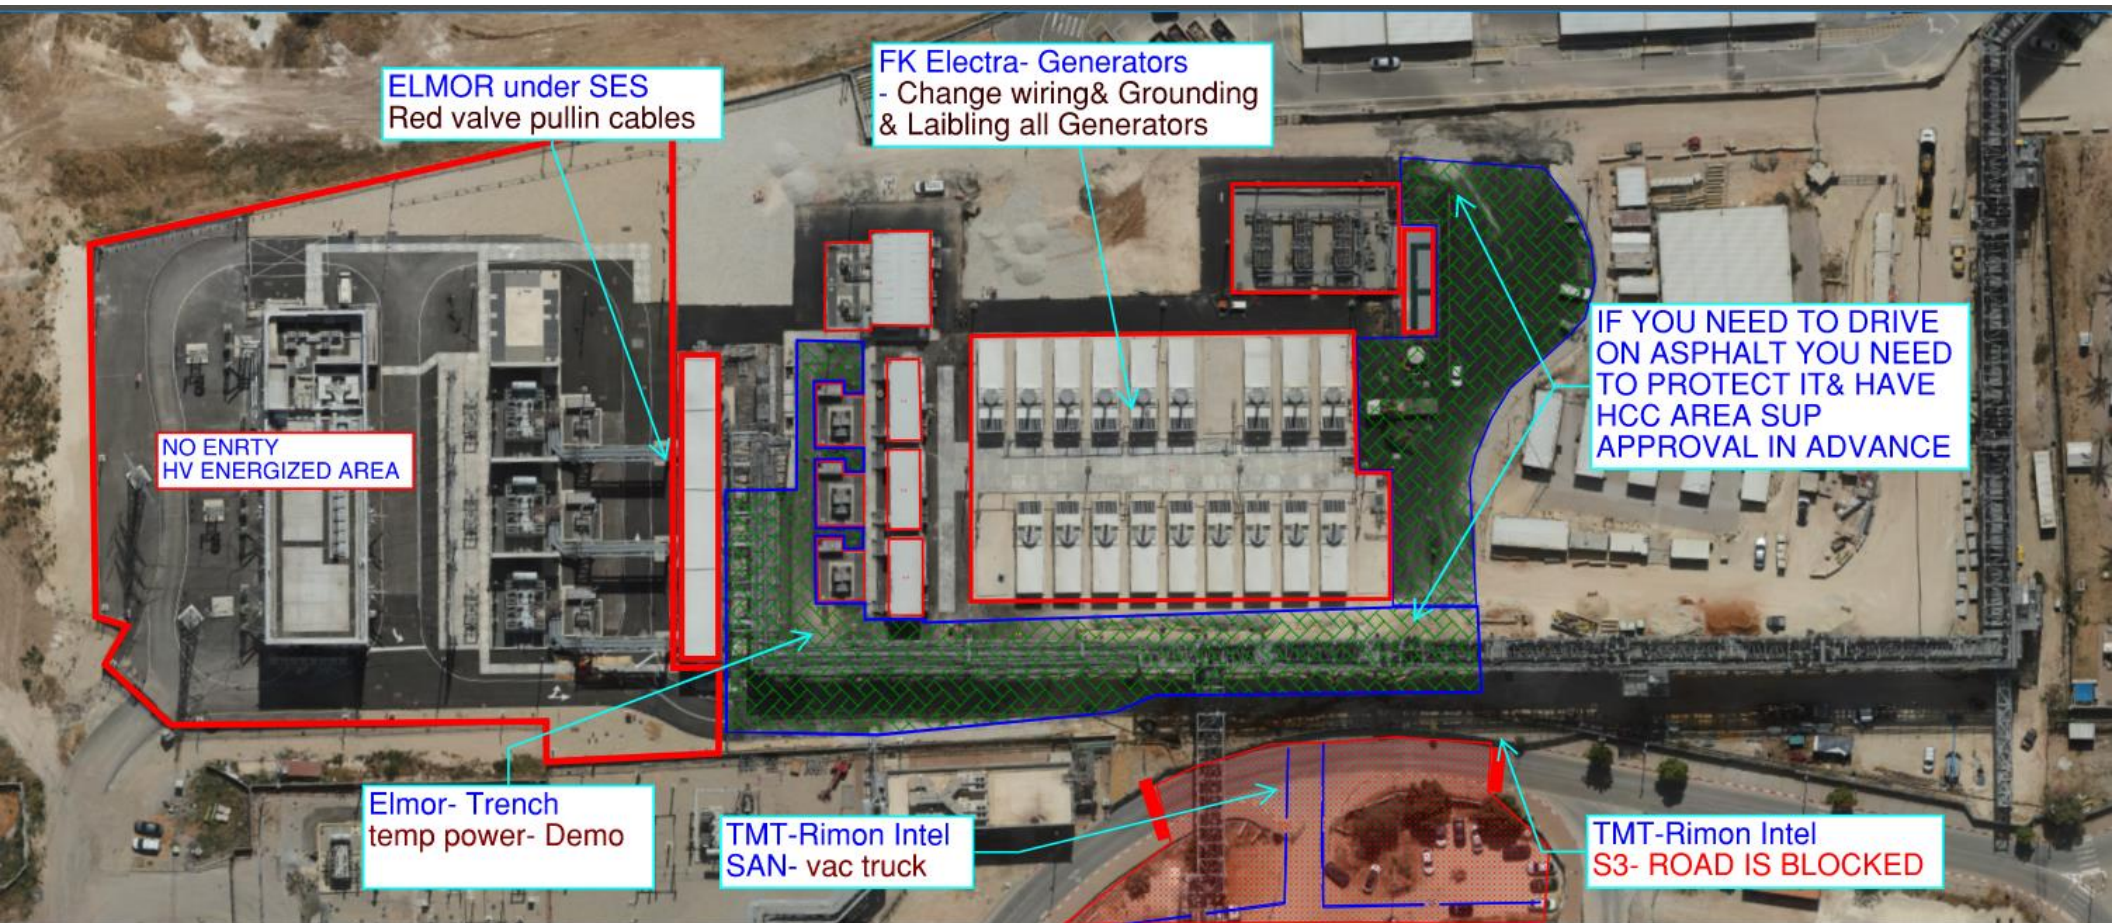

ELMOR under SES
Red valve pullin cables

FK Electra- Generators
- Change wiring & Grounding
& Laibling all Generators

NO ENRTY
HV ENERGIZED AREA

IF YOU NEED TO DRIVE
ON ASPHALT YOU NEED
TO PROTECT IT & HAVE
HCC AREA SUP
APPROVAL IN ADVANCE


Elmor- Trench
temp power- Demo

TMT-Rimon Intel
SAN- vac truck

TMT-Rimon Intel
S3- ROAD IS BLOCKED

HRA AREA


Planning machinery-
truck, boom lift, fork
... etc work- requires
coordination in
advance Hcc Sup &
meet the requirement
before starting work
to insure not damage
facilities

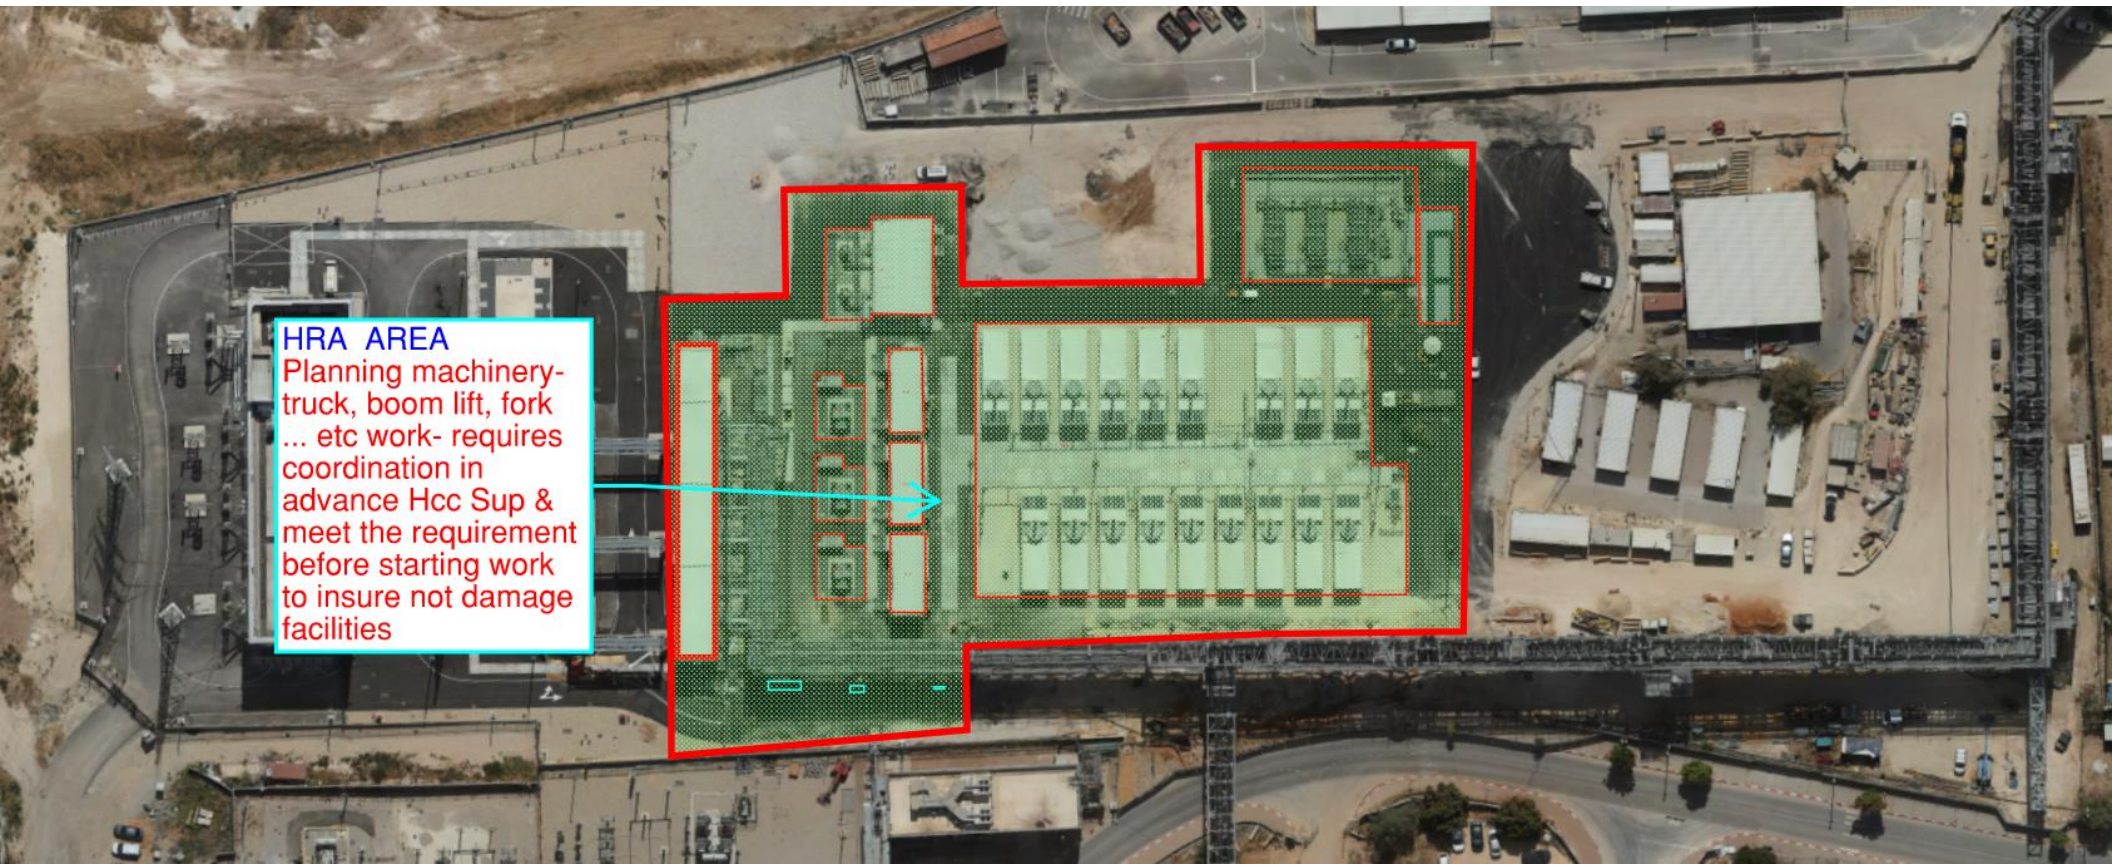




HOFFMAN CONSTRUCTION COMPANY



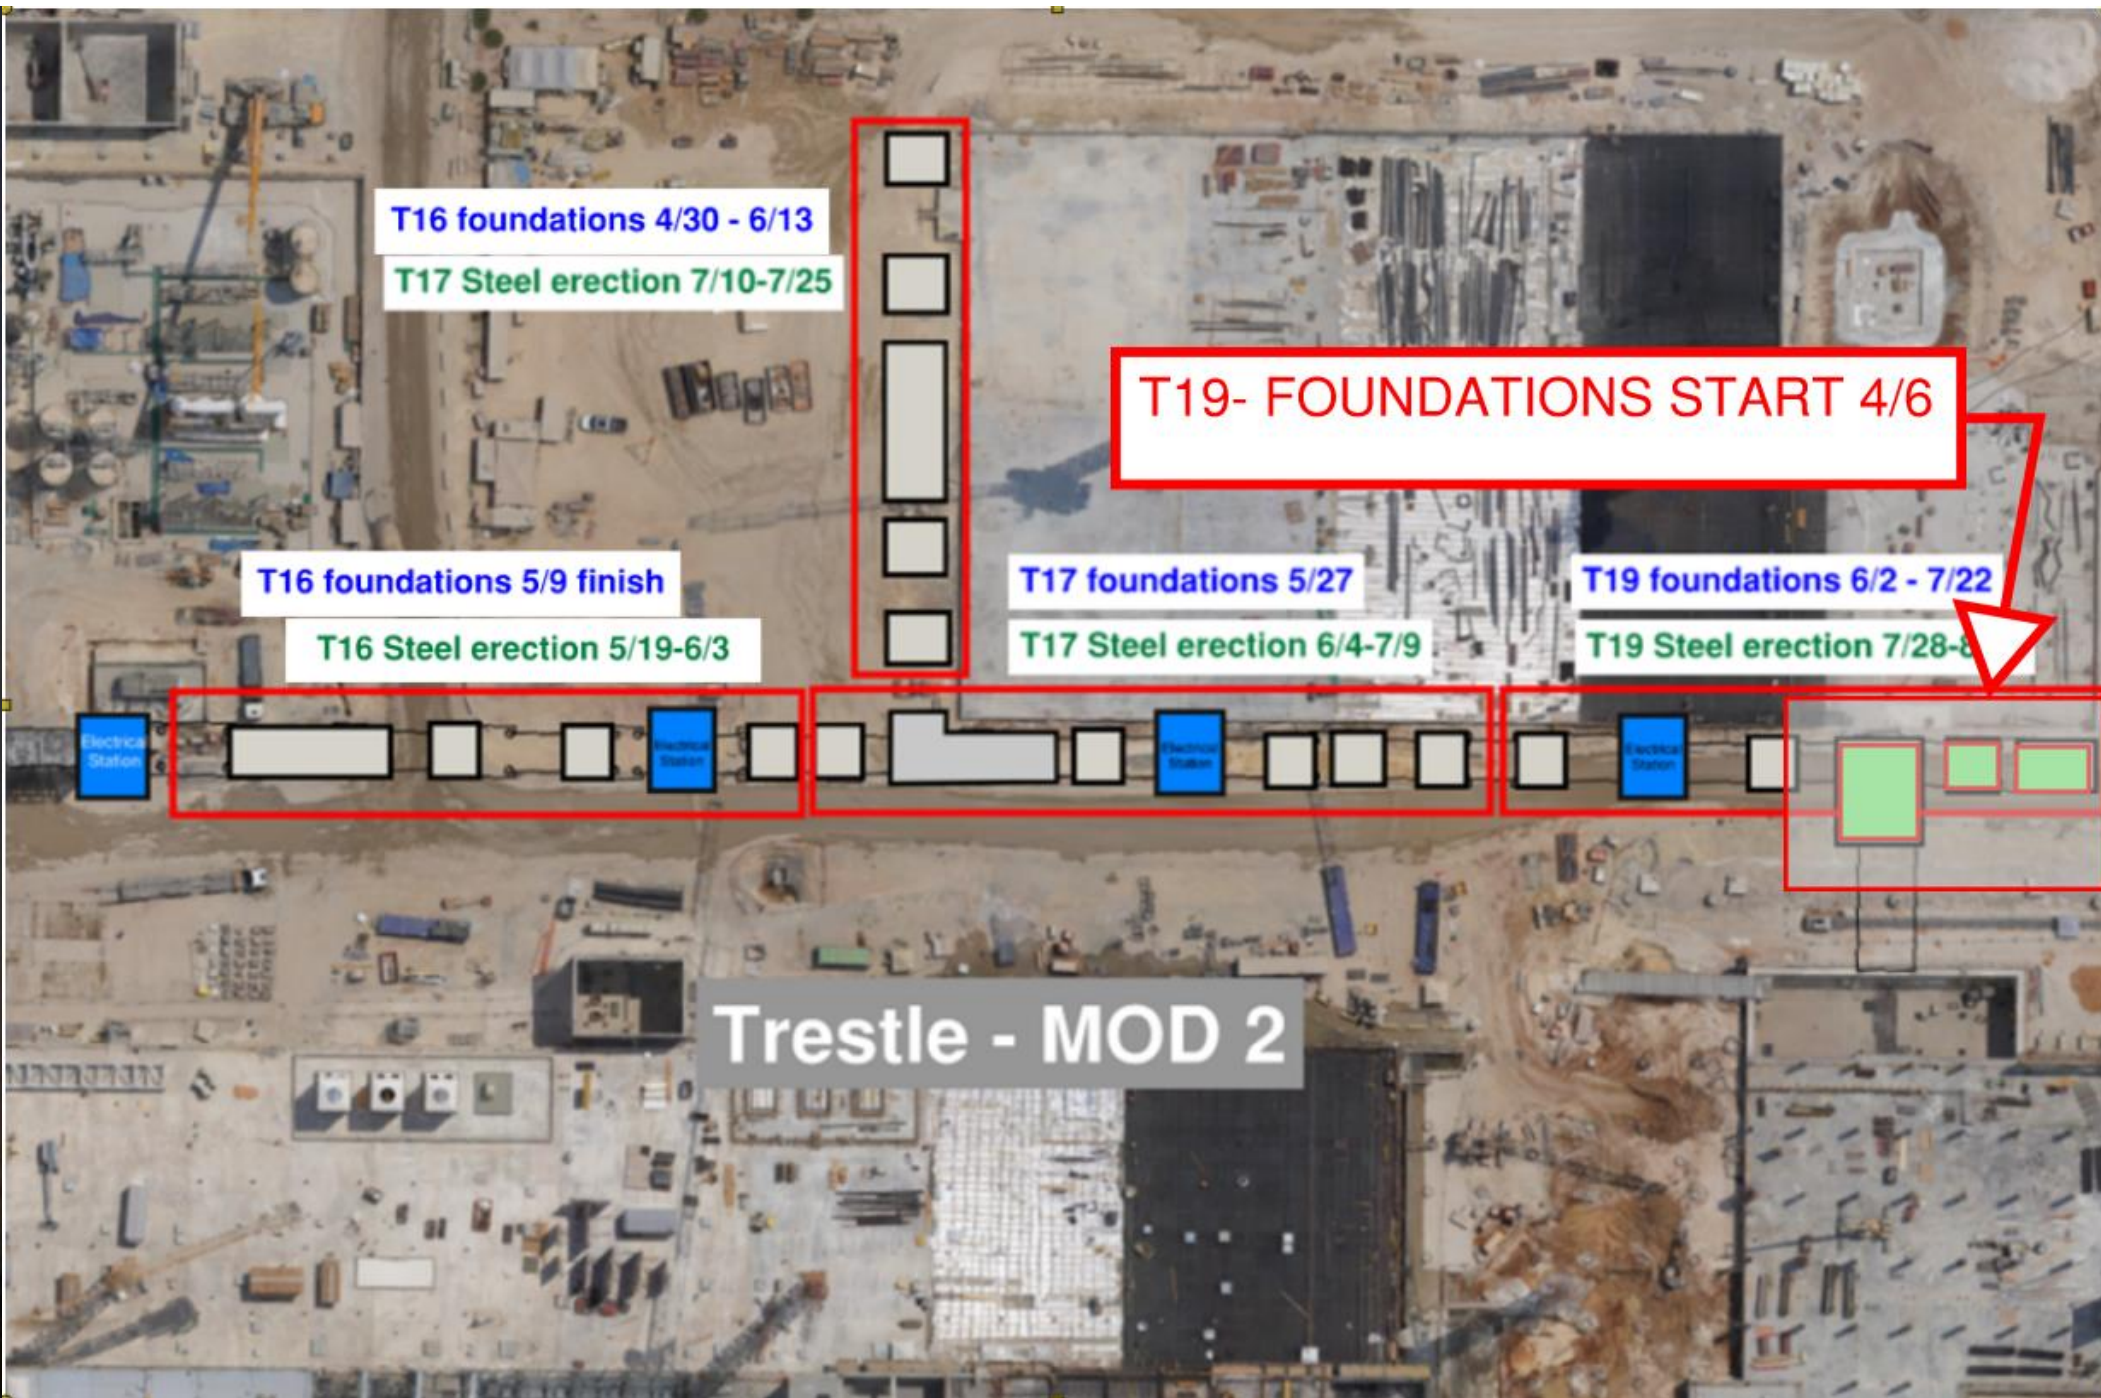

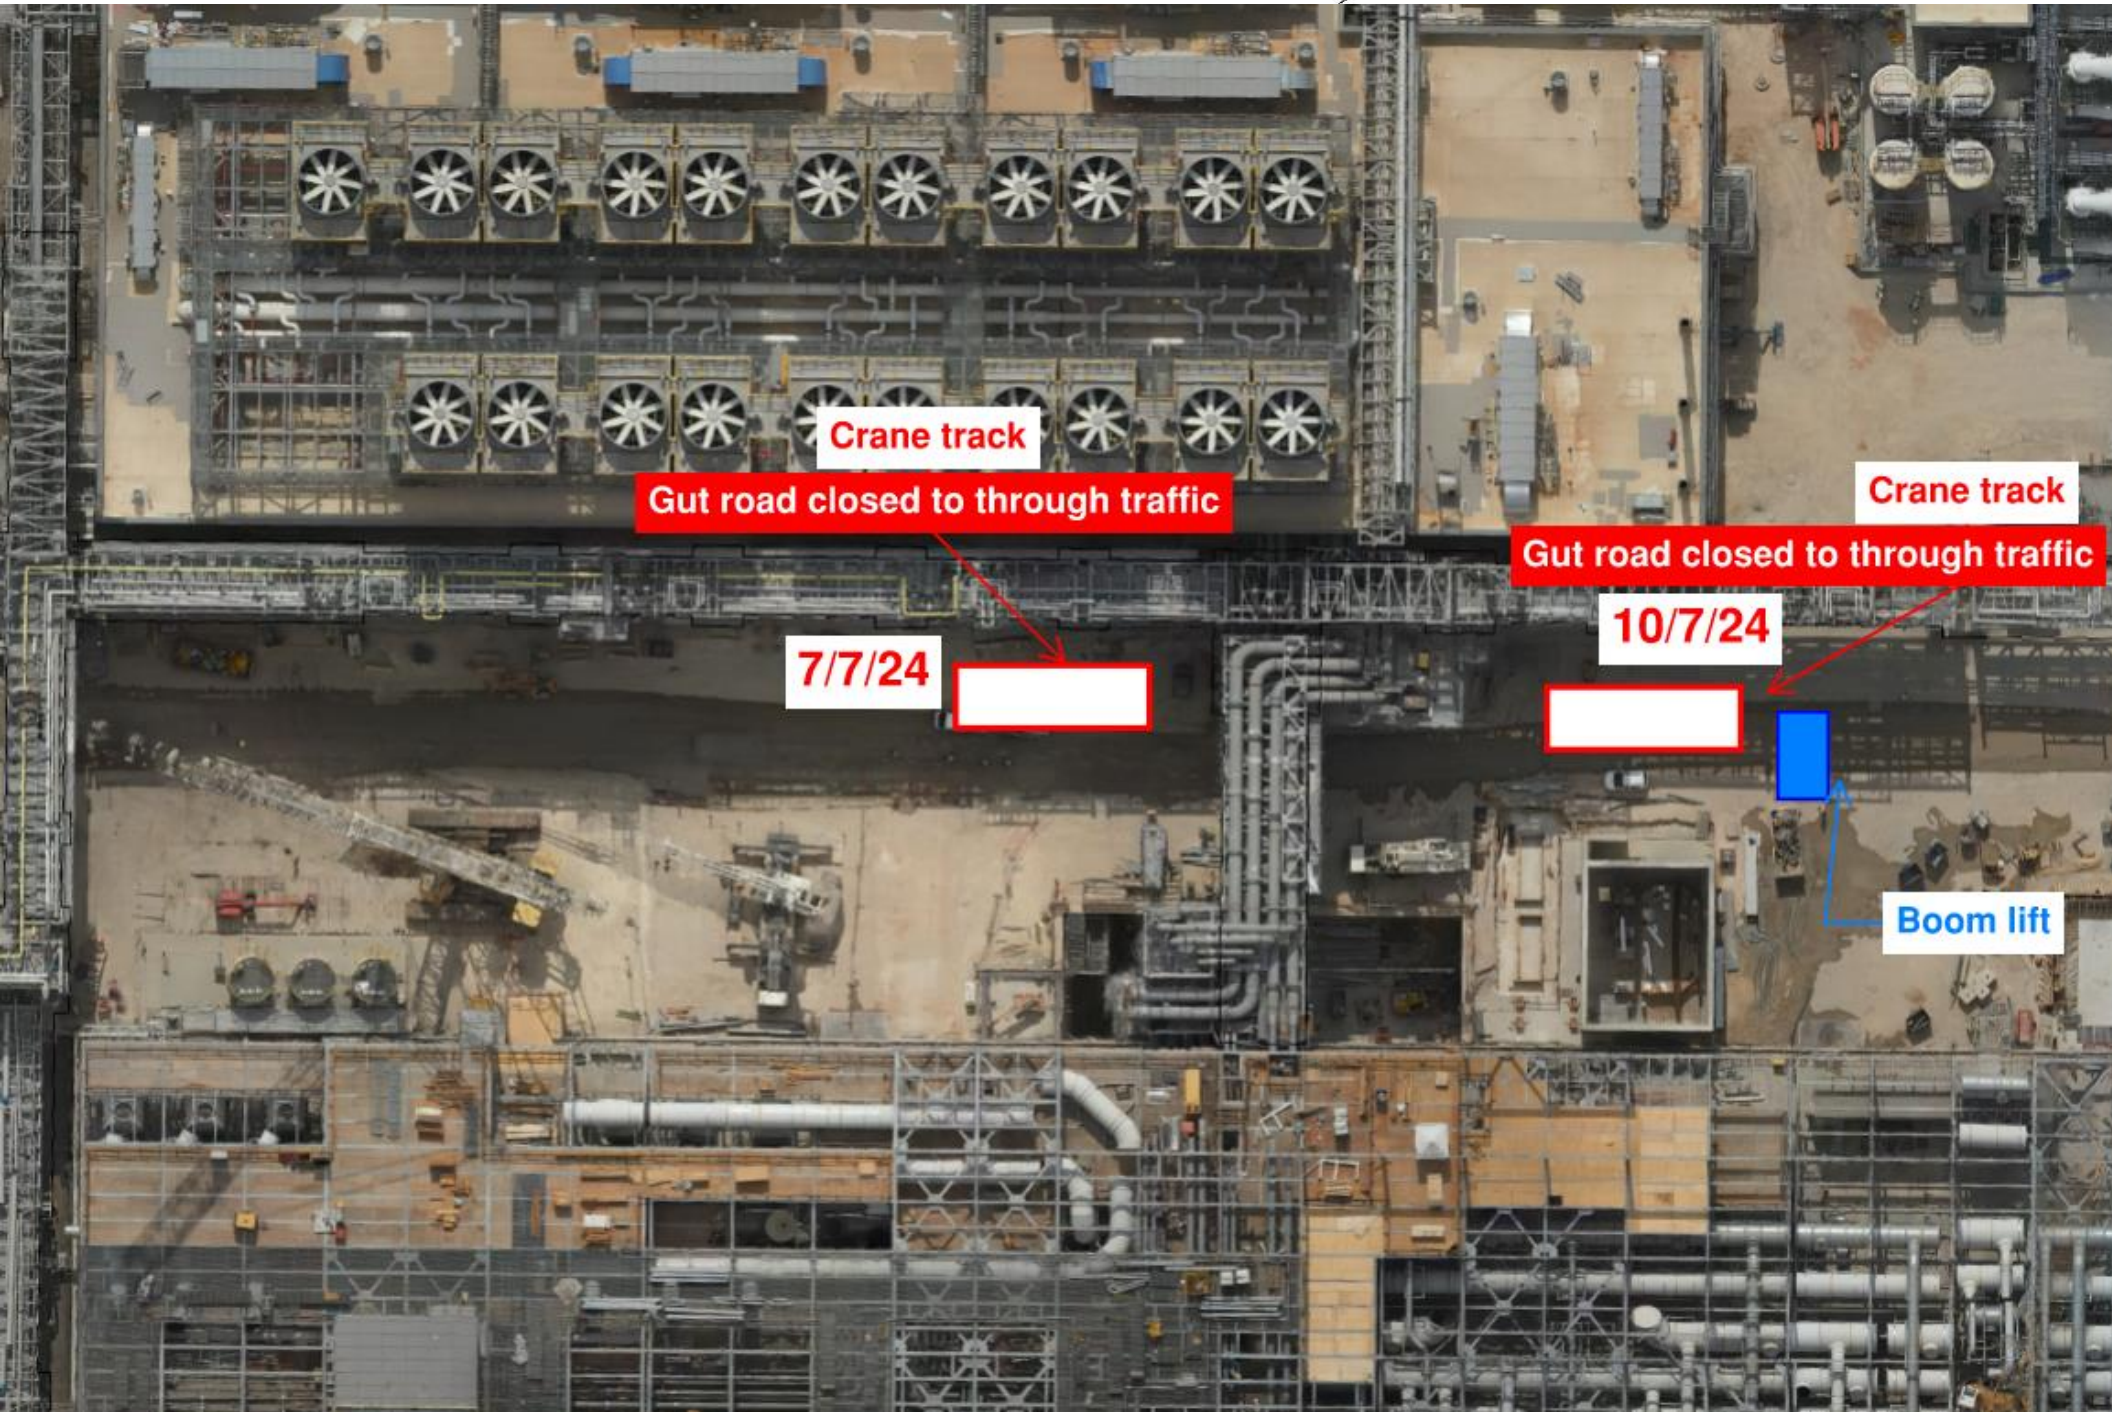

Crane track

Gut road closed to through traffic

7/7/24



Crane track

Gut road closed to through traffic

10/7/24




Boom lift

BSGS



Daily Coordination Meeting

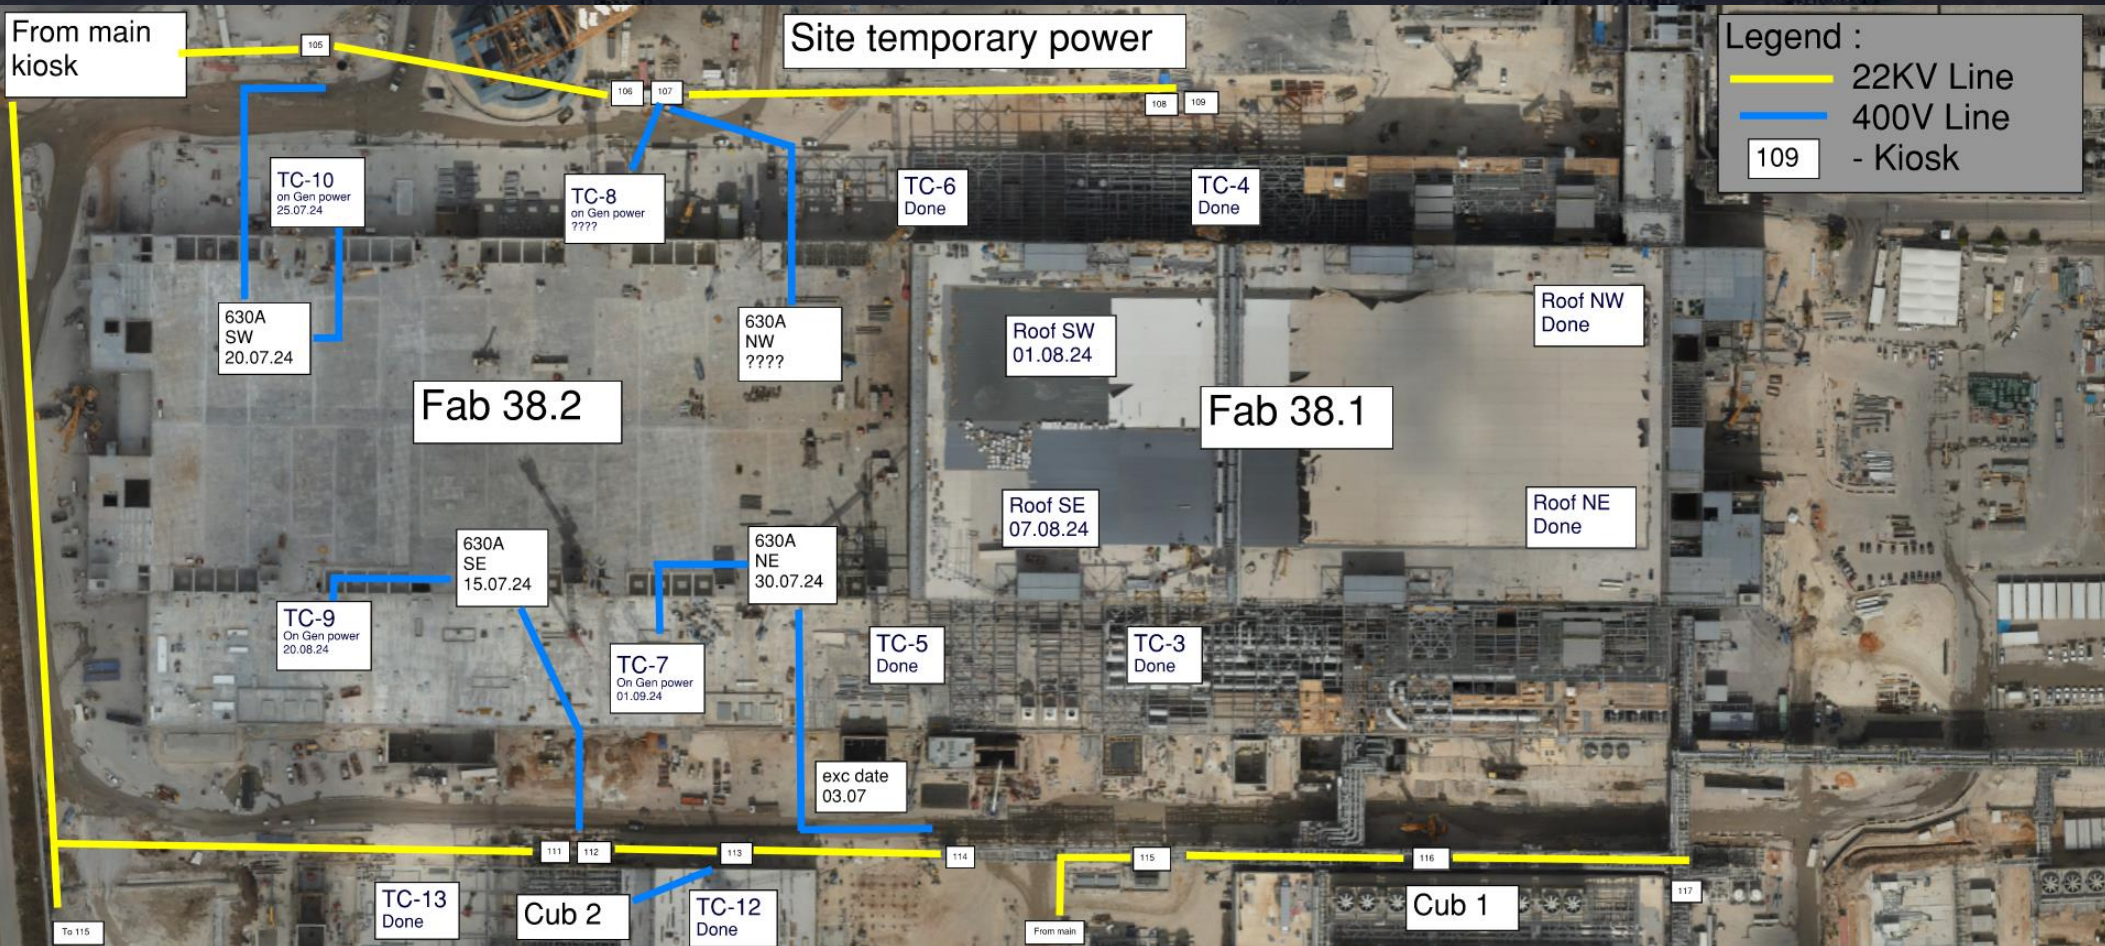

Daily Coordination Meeting


Site Logistics
North Gate B



Daily Coordination Meeting

Site Logistics

North

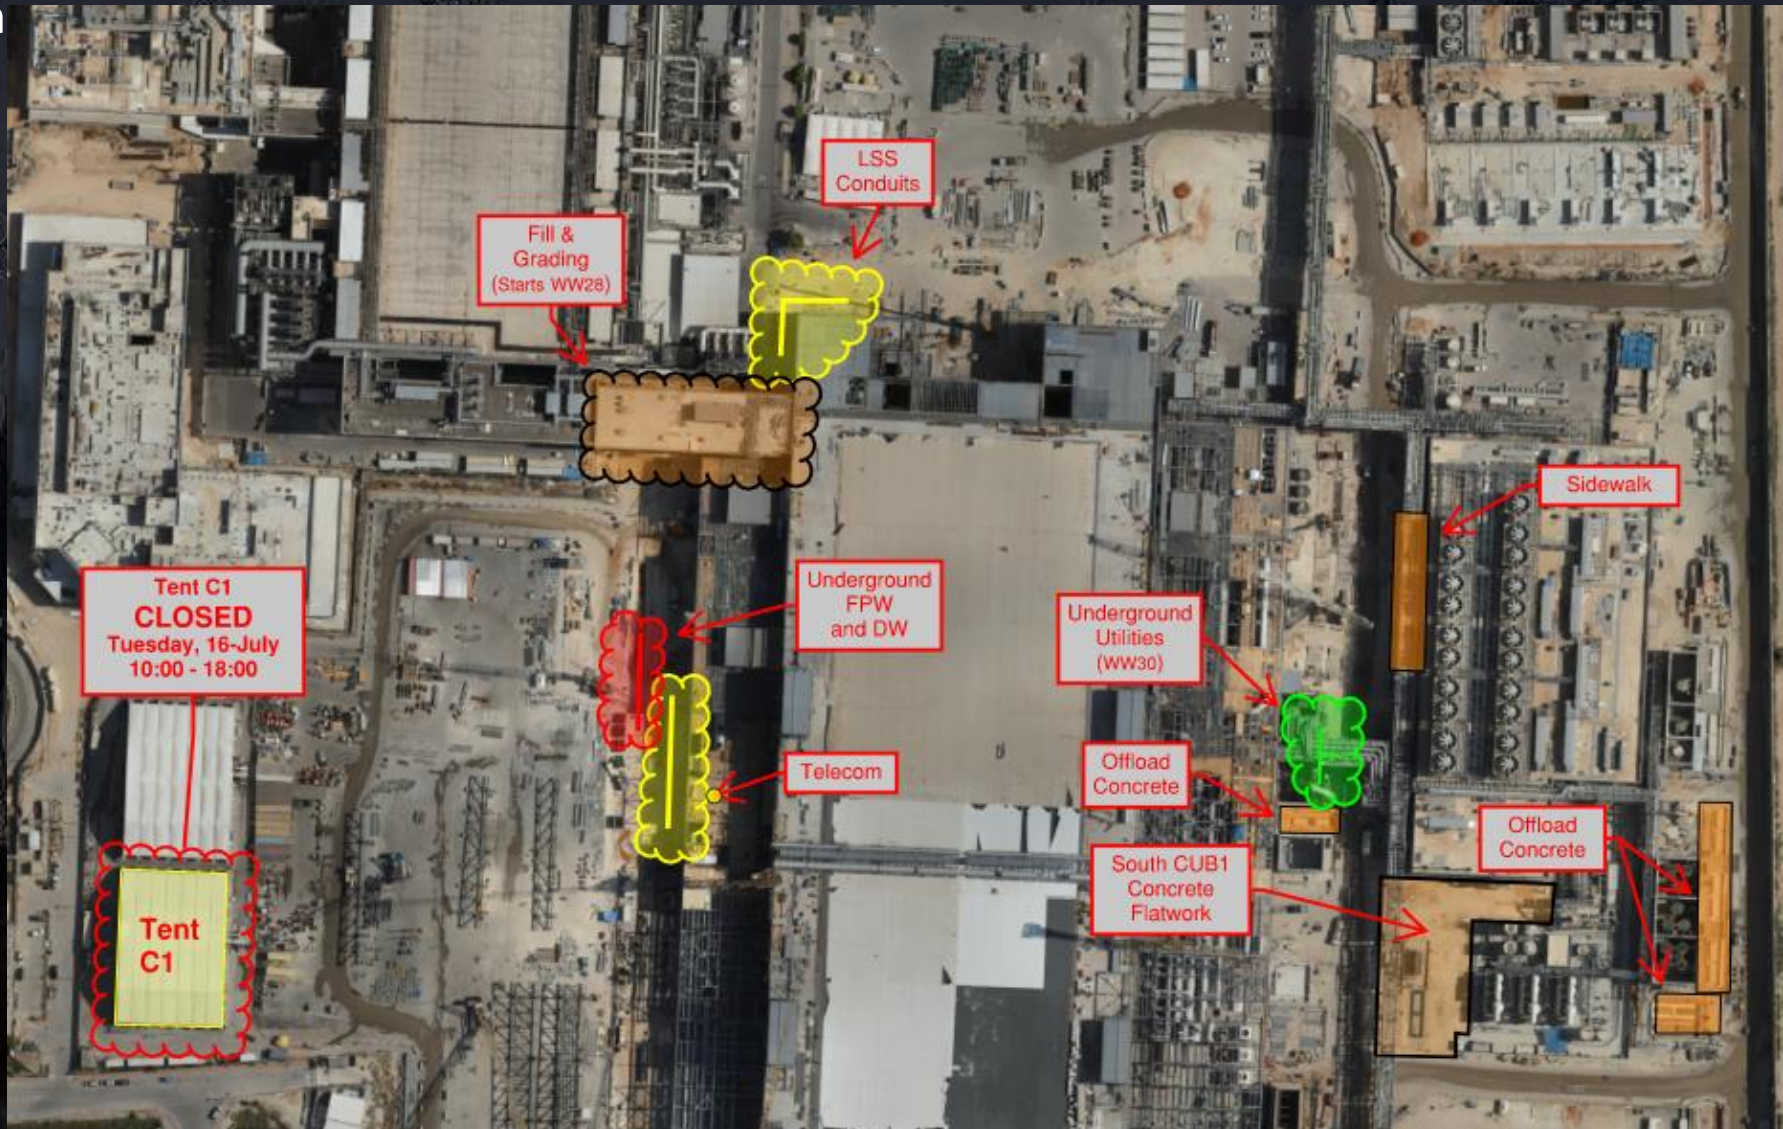



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics


South



Daily Coordination Meeting

Site Logistics


Smoking Areas

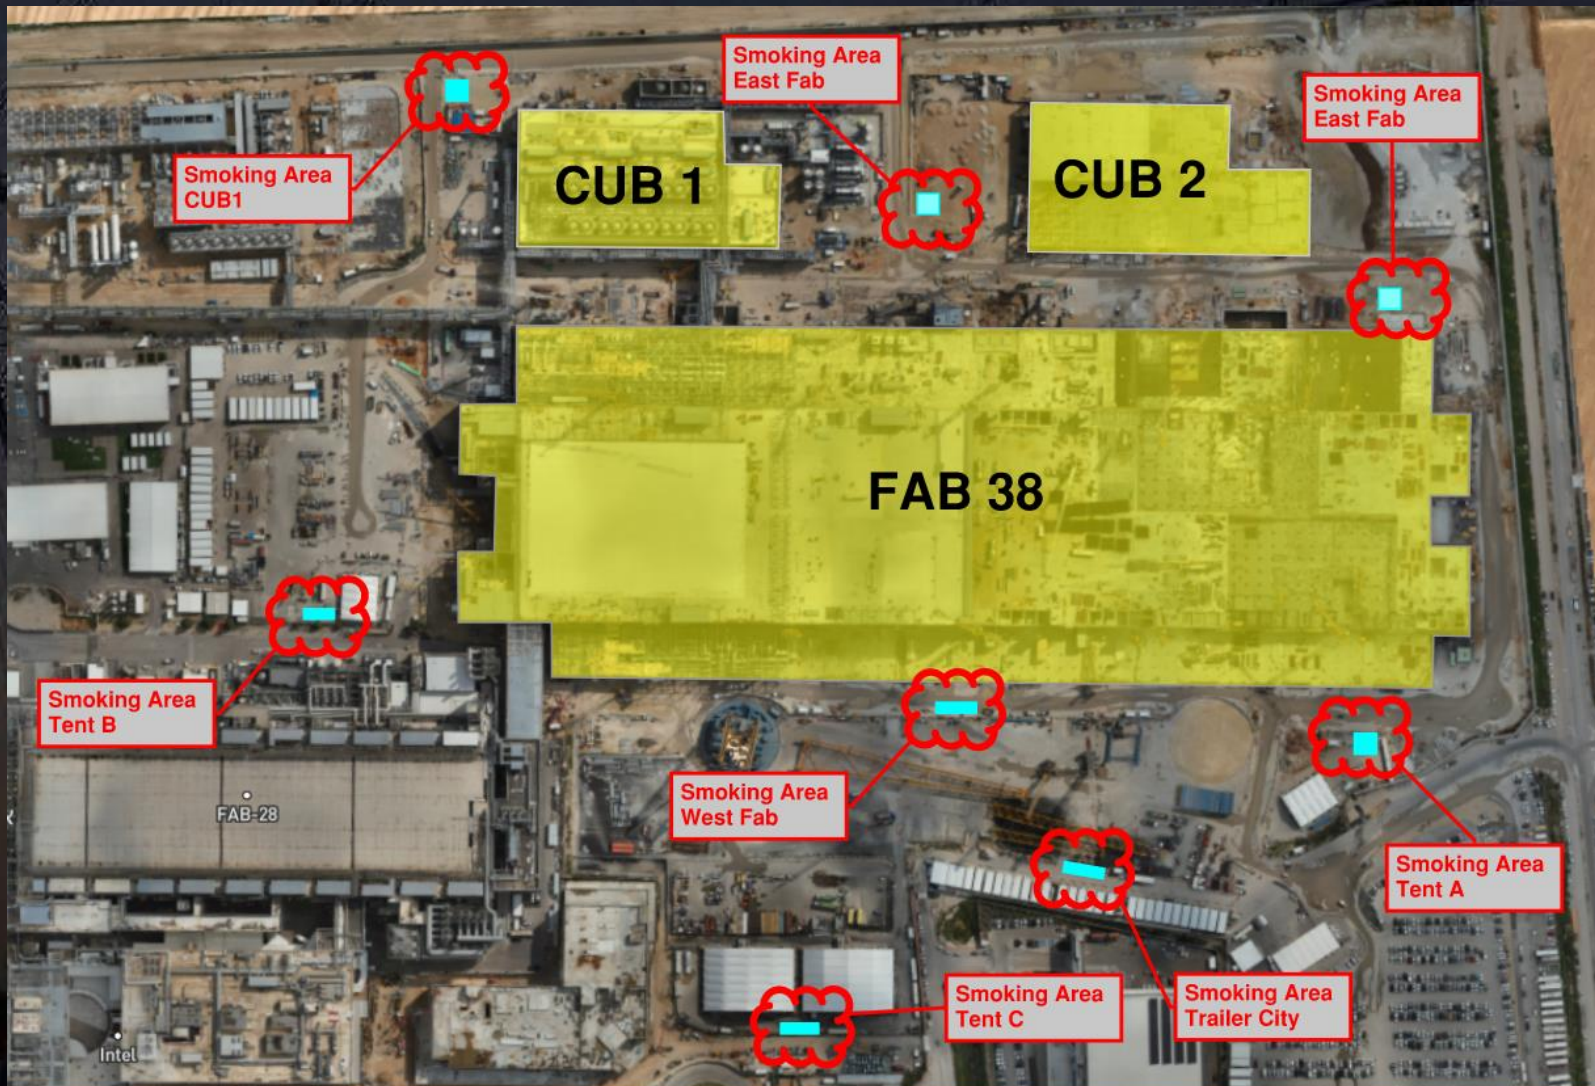

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

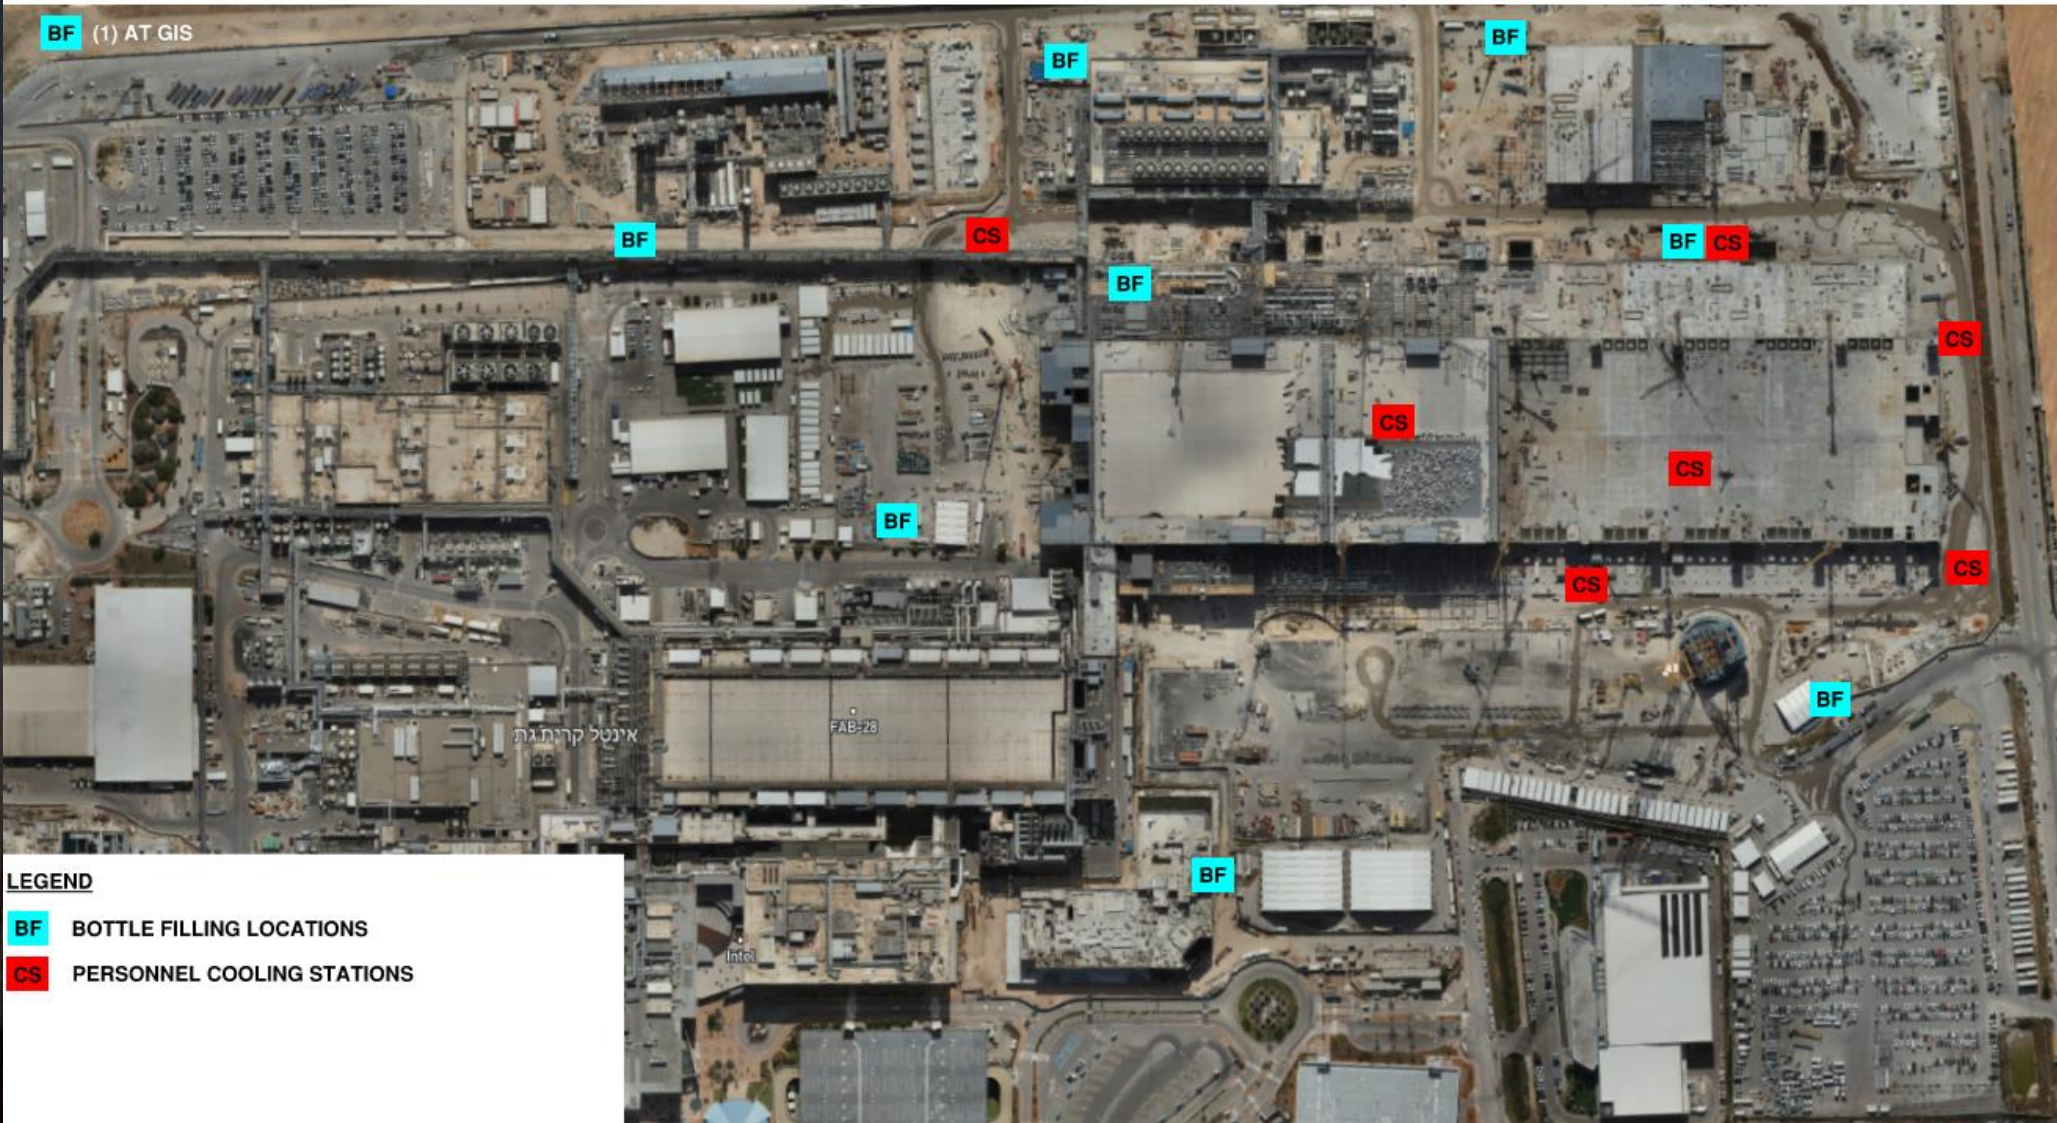

Sub - Fall Protection Equipment Audit

This form must be submitted for all on-site fall protection equipment regardless of whether it is in use or not.

Company *

Select

Equipment *

- ☐ Anchoring Device ☐ Connecting Device ☐ Full Body Harness
☐ Life-Line

Type *

Manufacturer *

Model *

Serial # *

Status *

- ☐ Approved ☐ Not-Approved

Inspected by: *

File Upload *


Drag and drop files here or [browse files](#)

☐ Send me a copy of my responses

Submit

FALL PROTECTION EQUIPMENT SUBMITTED BY CONTRACTORS

1870

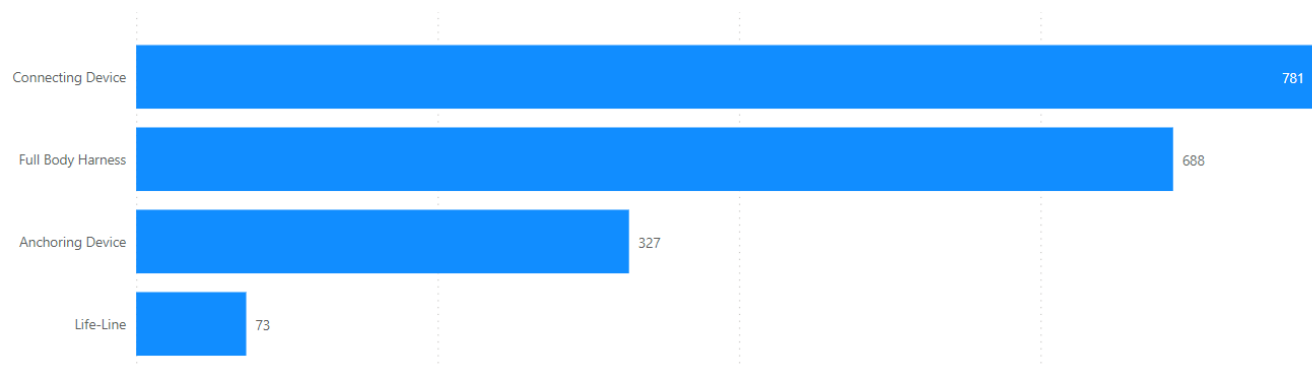



HOFFMAN CONSTRUCTION COMPANY



**17 MILLION SAFETY
WORKING HOURS
BBQ LUNCH!!!**

16.07.2024





LUNCH WILL BE SERVED IN 4 DIFFERENT SHIFTS.
EACH SHIFT WILL HAVE A SPECIFIC WRIST BAND COLOR
(WILL BE PROVIDED BY THE SAFETY TEAM)

11:30 - 12:15 GROUP A (BLUE)
12:15 - 13:00 GROUP B (GREEN)
13:00 - 13:45 GROUP C (YELLOW)
13:45 - 14:30 GROUP D (ORANGE)
21:00 NIGHT SHIFT

See next page
for GROUP shift hour



LOCATION AND ENTRANCES
FULL PPE REQUIRED WHILE
WALKING THROUGH JOB SITE!!!

- *Group shift will be updated



HOFFMAN CONSTRUCTION COMPANY



Please email me to sign up to Volunteer to serve
Rebecca-WeinsteinAttar@Hoffmancorp.com

HCC/EHS Weekend Work- 12.07.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Fred Dumorne 052-2506949
- Mohammad Hassan 052-2342880
- Roi Zaidin 052-2146194

CSA CM

- Ben Holmberg 052-6047723
- Konstantyn (Kosta) Povetkin 052-2124018

MEP

- John Leamy 052-3899876
- Michael (Mikhail) Klyuchik 052-2085629
- Igal Amano 052-6217328
- Gregory Leal 052-5102705

QA/Cx

- Patrick Blunt 052-3155787

Cranes

- Craig Mowry 052-3002769

Safety

- Safety Foreman- Asher Avisdris- 058-6867997
- Safety Assistant- Hudifa Alshieck- 054-9408858
- Safety Professional – Hamad Hammoudi- 051-2405061

Subcontractor Weekend Work- 12.07.2024

FAB

Utility Level

- Carmel rack
- Carmel duct
- Combe upw
- Elram
- Afcon electrical

Carmel duct

Hitam 0527053353 ehs

Aviv 0543471309 forman

Elram

Eliezer 0544236899 forman

Shlomo 0545551702 ehs

Afcon elec

Nisim 0526227627 forman

Stiven 0559129333 ehs

Pradip 0552742935 ehs

Clean Room

- Elram – INT 17,24 lines, CR 10,24 line -shaft removal (EHS Shlomo Amar – 0545551702, Supervisor Ivan - 0545868048)
- Afcon – CR – 2E, 2W, INT-1E, 2E,1W (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Chemo – INT -1E+1W 10” pipe install +racks (EHS Rotem - 0544477112, Supervisor Maor – 0509889071)
- S/N - Fan deck grating penetration , 1W catwalks handrails (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- Rolling Plains – INT 4DA fireproofing Balkony 2E, LINK AW- B6,9,10, 5RA Level, AK-AQ 25 5 RA (EHS Ovidiu 0546993648, Supervisor Oleg - 0542689370)

Subfab

- Afcon E –
 - 5E & 5W Grounding in ballroom.
 - 5E & 5W LSS Rooms.
- WW –
 - TTNE Elevator Shaft 1
- HYG- hand rails

PSSS

- Pach Taas – Module bolting PSSS Roof and Lift 2
 - Foreman – Eduard – 054-7915874
 - Safety – Ofek – 050-7838486
- Carmel Bidud Scaffold – 2P Lift 2 MAH Scaffold
 - Foreman - Farhi – 052-6105266
 - Safety – Micel – 054-2634700
- W&W – SEQ 131,134,136, and 2P Scrubber Grating
 - Foreman – Mike Lagana – 052-4093401
 - Safety – Gary Lambert – 1-405-833-8910
- Katz – U8 Rack 7 Plate Install
 - Foreman - Polishchuk - 054-750-1845.
 - Safety – Solomon Nemirovsky – 054-579-9304
- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- MB – 1P Fire Riser Room
 - Foreman -
 - Safety -
- Combe UPW – UPW Room, UPW Yard, and Water Reactive Piping
 - Foreman – Dani Karsin – 052-6527883
 - Safety – Shimon Ben Amo – 054-5348843
- Chemo A. – PSSS Roof and Lift 2
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112

Girts

SN- 832 line

SN- 635 Sidings

Subcontractor Weekend Work- 12.07.2024

WJG

- W&W – Steel Erection 5J
Foreman: Chris Isaac – 052 588 3215
Safety: Moshe 054 801 2959
- Afcon – 3J UL Cable Tray, 2J Lift 2 Cable Tray
Foreman: Sarat 055 274 0190
Safety: Pradeep 055 274 2935
- Pach Taas: 1J UL, 2J Lift 2 Module Bolting
Foreman: Nuriel 054 901 2343
Pachtas safety : Ofek ben arosh 0507838486
- Chemo: 2J & 3J Lift 2 Piping
Foreman: Maor 050 988 9071
Safety: Rotem 054 447 7112

Site

- Derech Afar – Sanitary lift station & underground fire protection (Raed – 054-2442030)
- Olizki – Sweepers and water trucks, truck offloads, concrete flatwork (PCC) & excavation (Or – 052-4917313)
- TM Team – LSS conduits (Rafi – 050-8723363)

Trestle

- SNJ – FOUATION -15 WORKERS
FORMAN abed 0528168353
- SNJ- PIPING 12 WORKERS
FORMAN HAMADA SALEM tel. 0543516972
2safety trestle Alon Matan tel. +972 50-989-5008
- AA STAGE DESIGN – 12 WORKERS
FORMAN- DORON KADAN
SAFETY – OSAMA ALSAYED 0522851458...
 - Olizki- BSGS slab backfill

CUB

- Chemo ahron at cub1
- T.m team dirt work at the north yard of cub 2
- Thank you,have a good weekend

GIS/NEY

No work
