

Daily Coordination Meeting



Daily Coordination Meeting

General Topics:

- PMB closed at 18:00 tonight and Friday
- Safety showers in CUB – live, don't use
- Weekend work

CSL01.12



HOFFMAN CONSTRUCTION COMPANY



UTILITY LEVEL

TOOL TOWERS / NO STORAGE FROM March 16



CHEMO / AFCON e



HOFFMAN CONSTRUCTION COMPANY



UTILITY LEVEL

TOOL TOWERS / NO STORAGE FROM March 16





HOFFMAN CONSTRUCTION COMPANY



UTILITY LEVEL


TOOL TOWERS / NO STORAGE FROM March 16



MEGASON / AFCON e


UTILITY LEVEL PRESS TEST

Lesico
HPOFA test
3/16
From 17:00
till 5:00

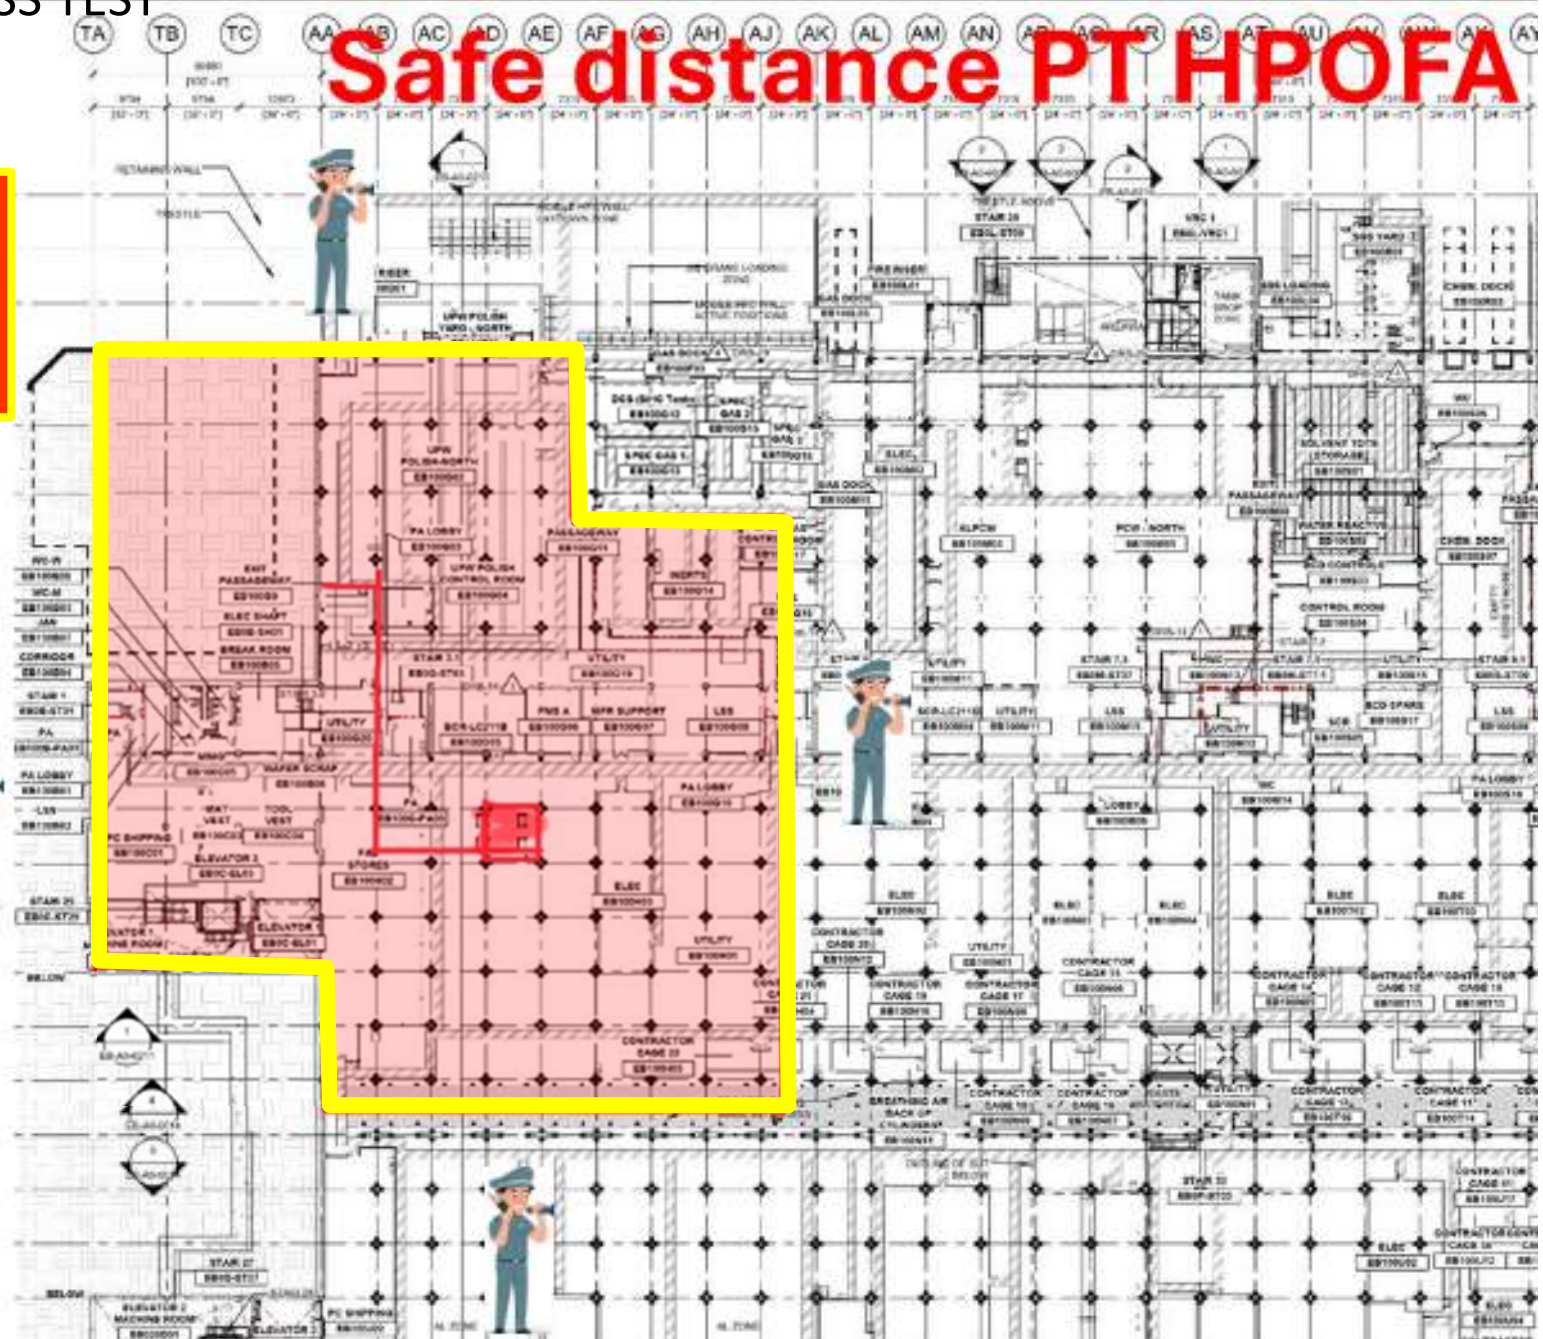



UTILITY LEVEL MOD1

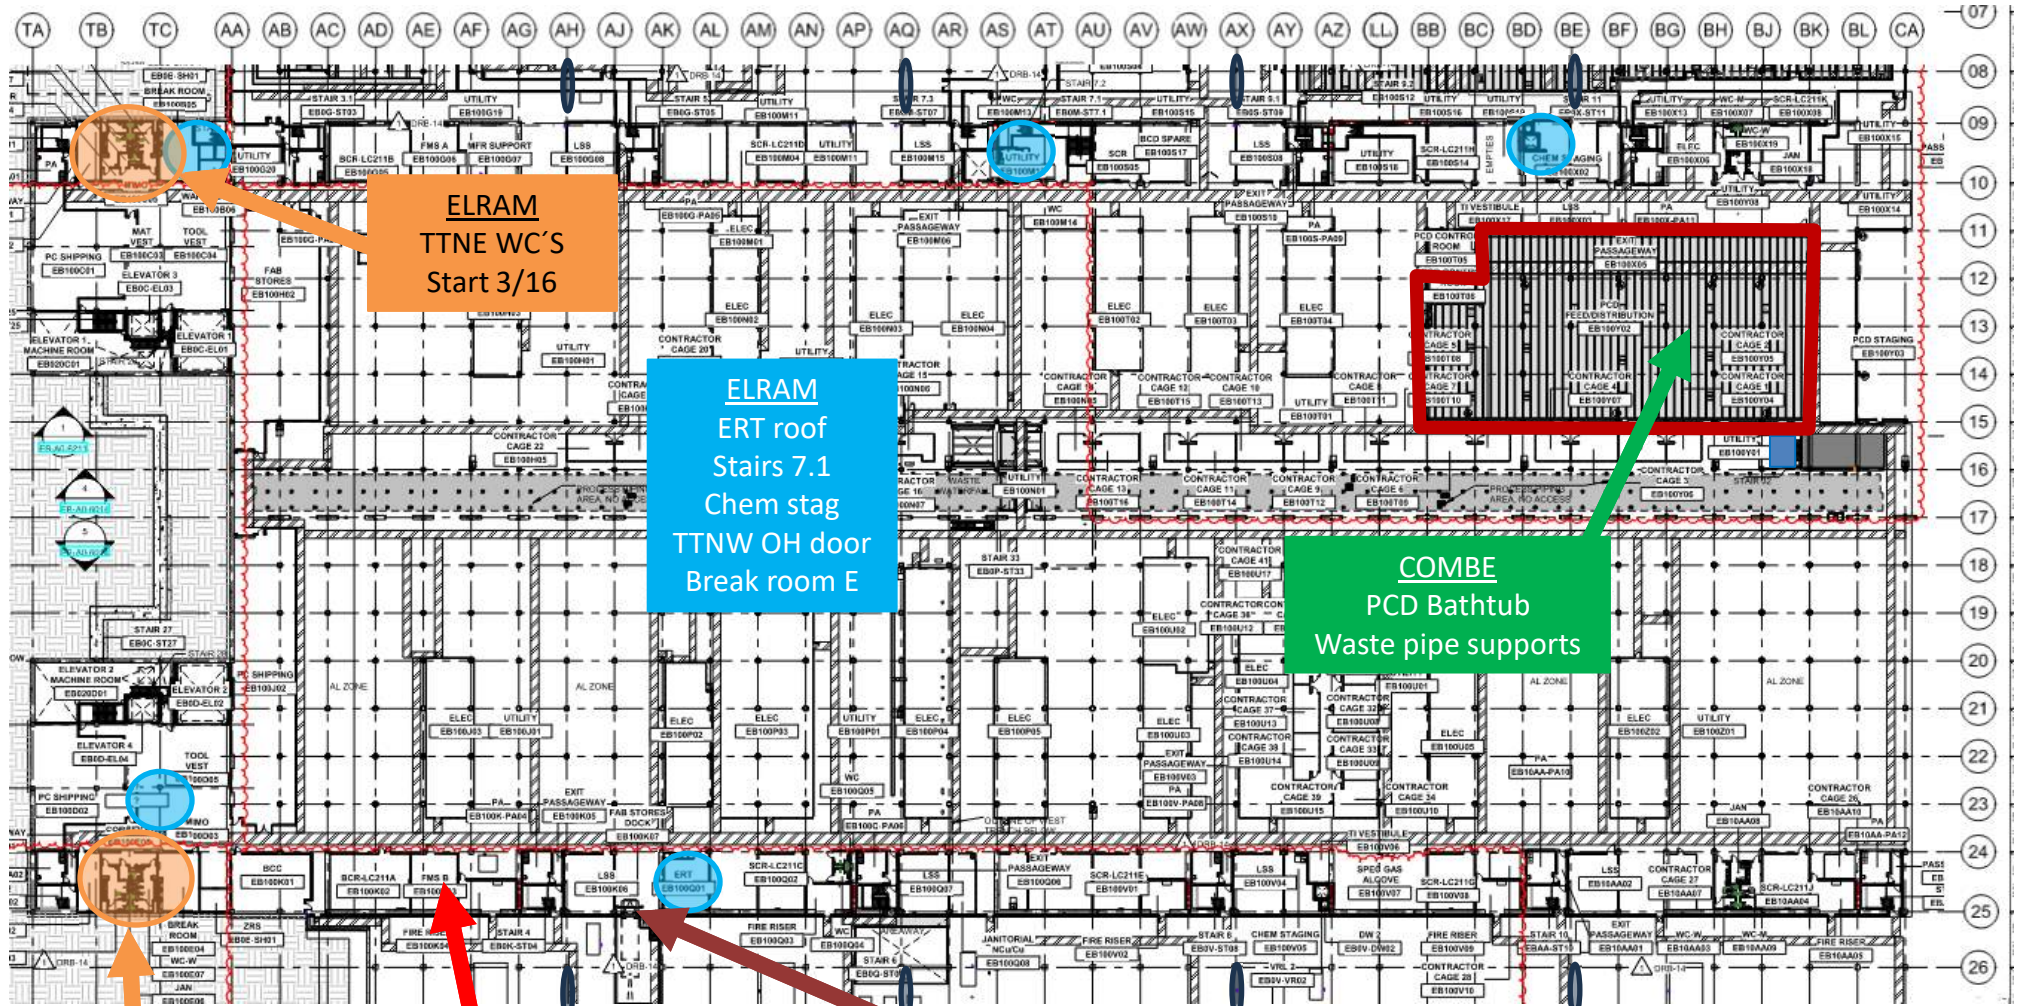

ELRAM
TTNE WC'S
Start 3/16

ELRAM
ERT roof
Stairs 7.1
Chem stag
TTNW OH door
Break room E

COMBE
PCD Bathtub
Waste pipe supports

SamiN
TTNW WC'S
pressure test
ongoing

HYG
FMS B
3/16


SHEARIM
Need start
date !?




SUT 38.1 LEVEL




SUT 38.2 LEVEL

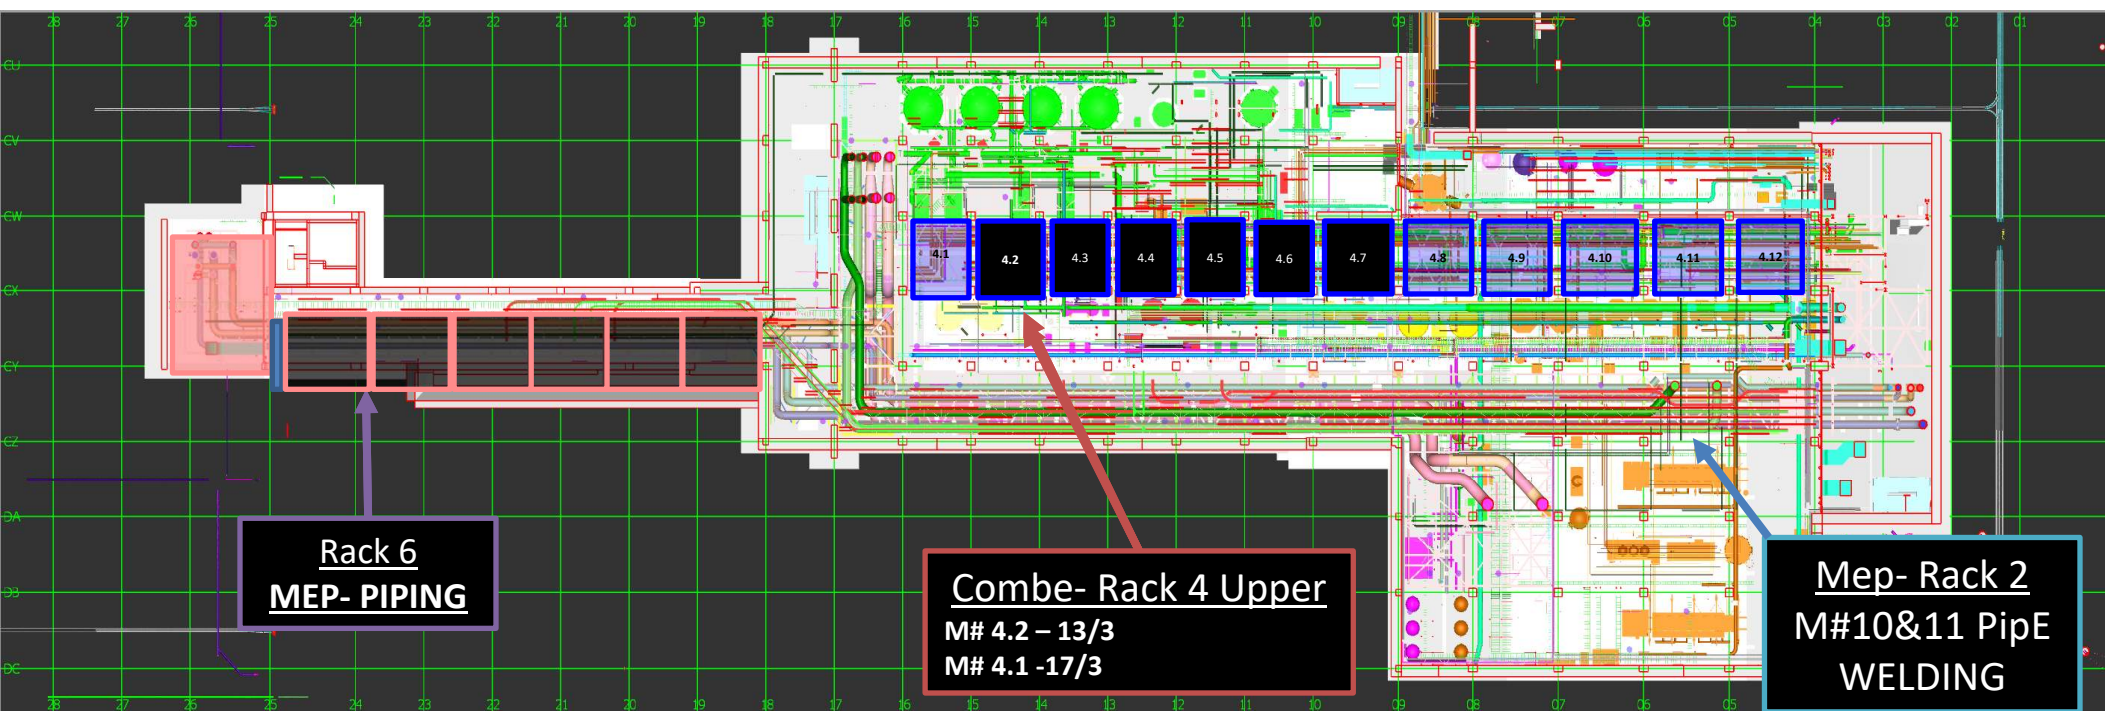


SUBFAB BUILDOUT MOD 1

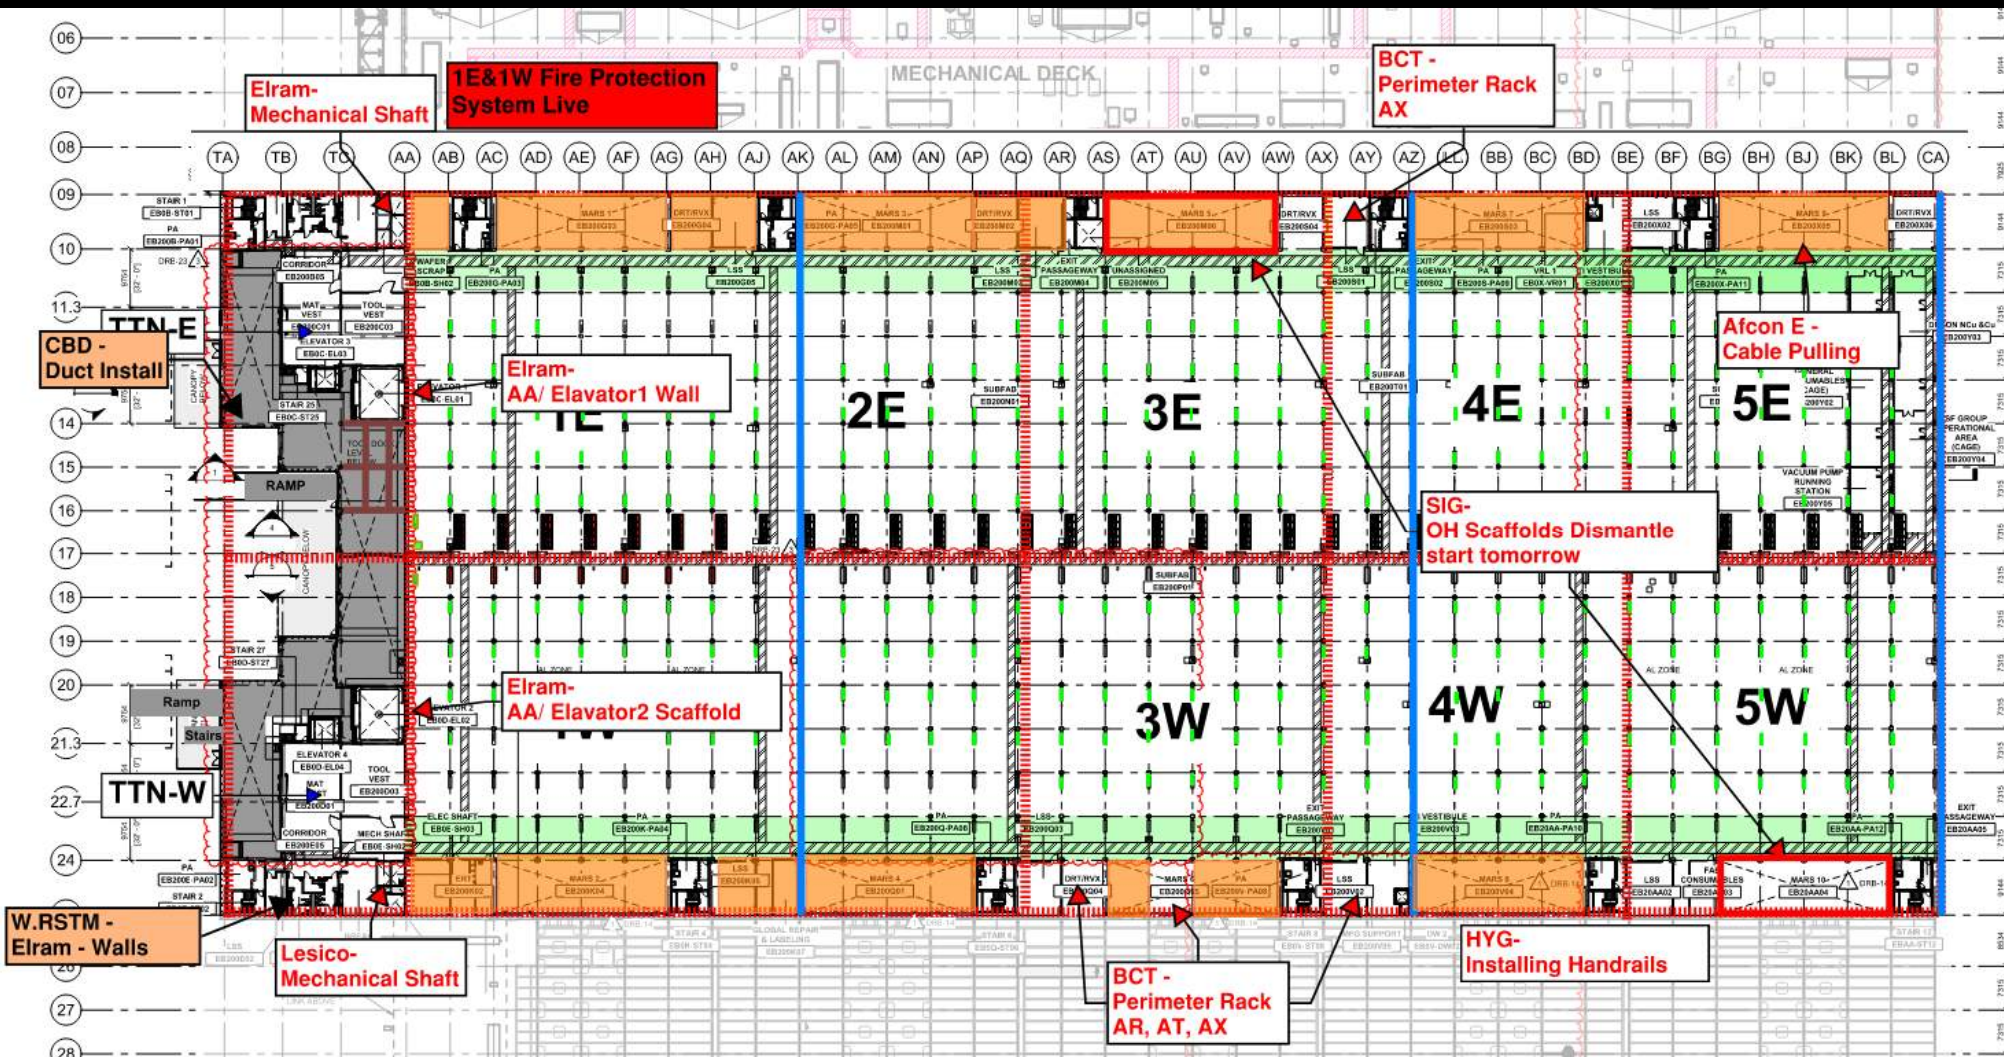



BCT Pressure Test Friday

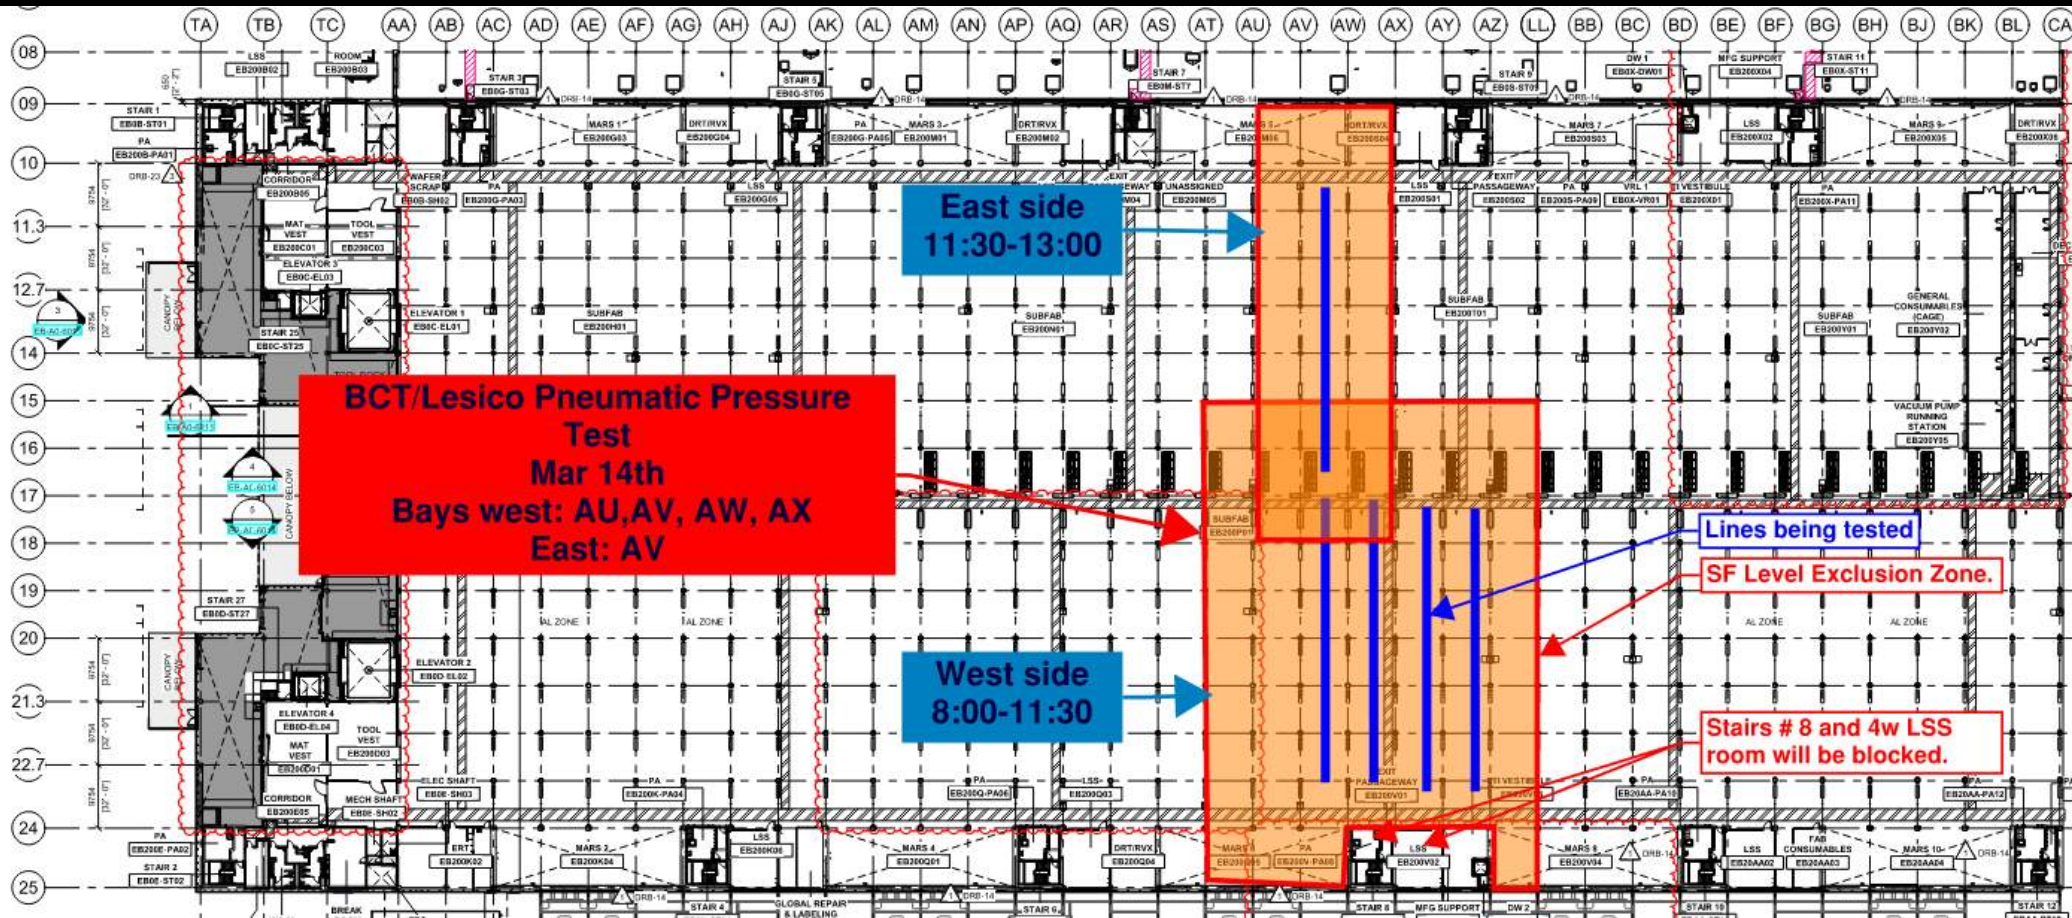

SUBFAB CRC TOPCOAT

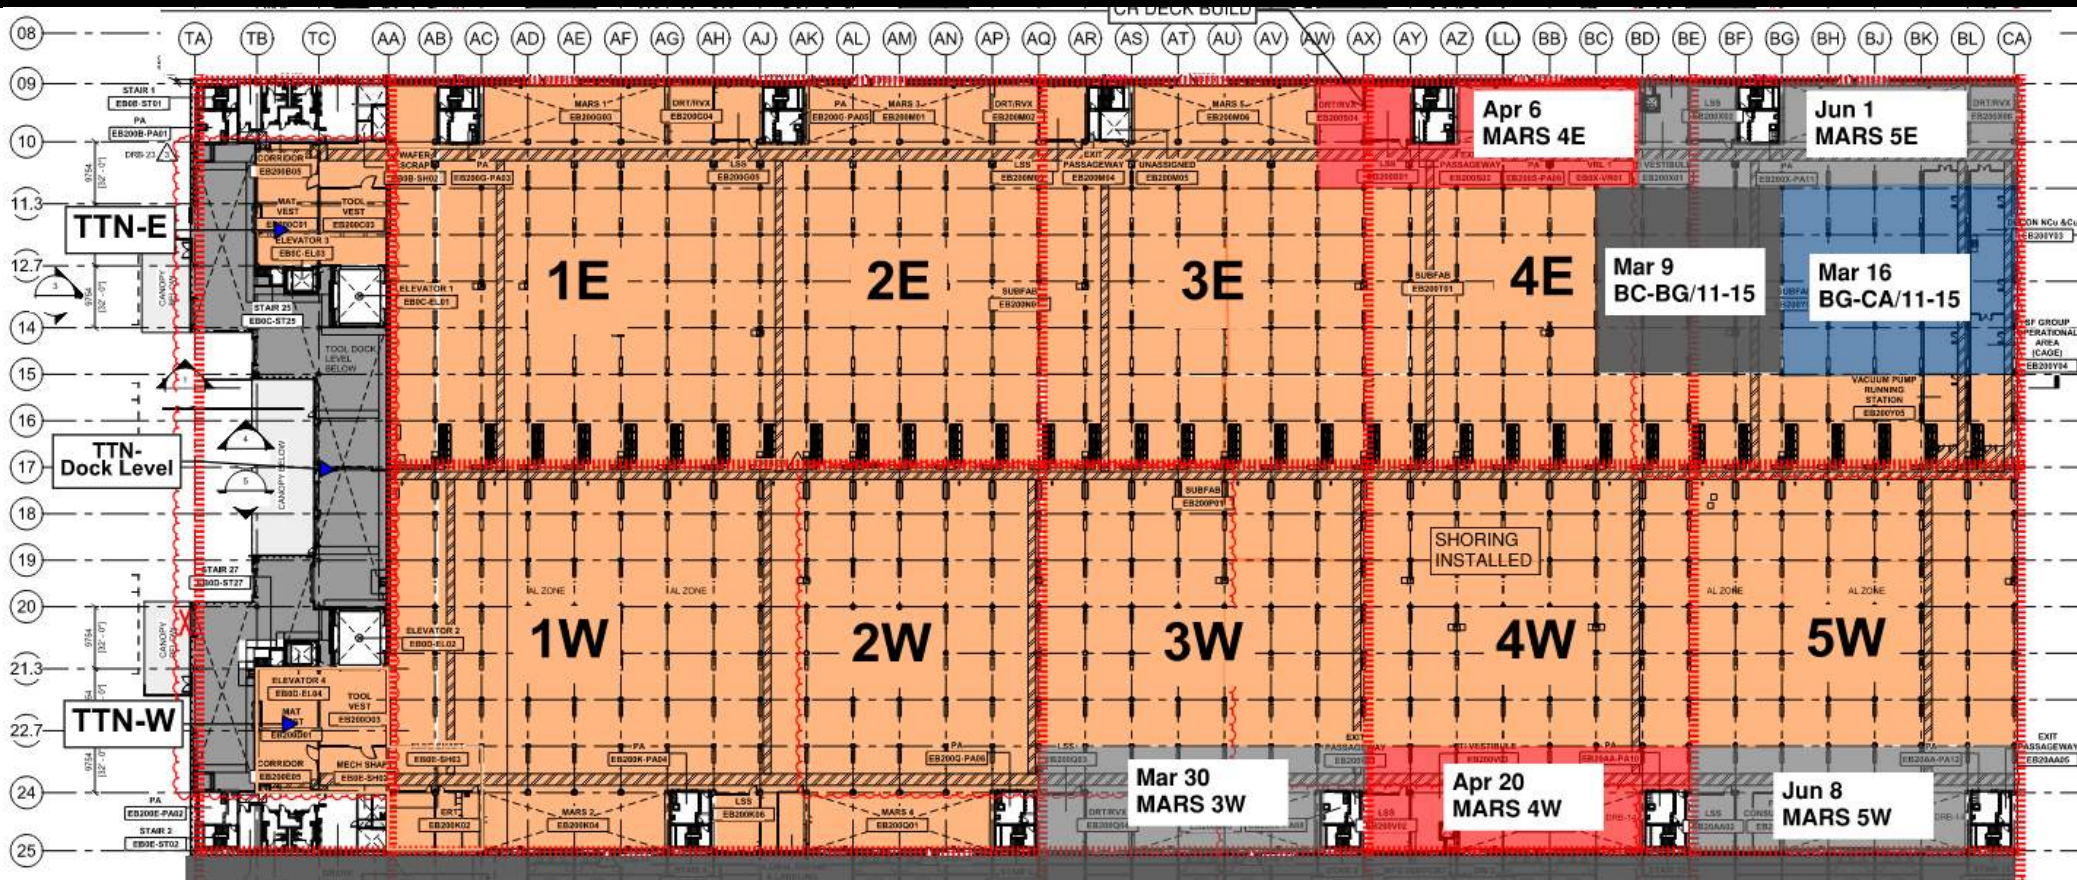

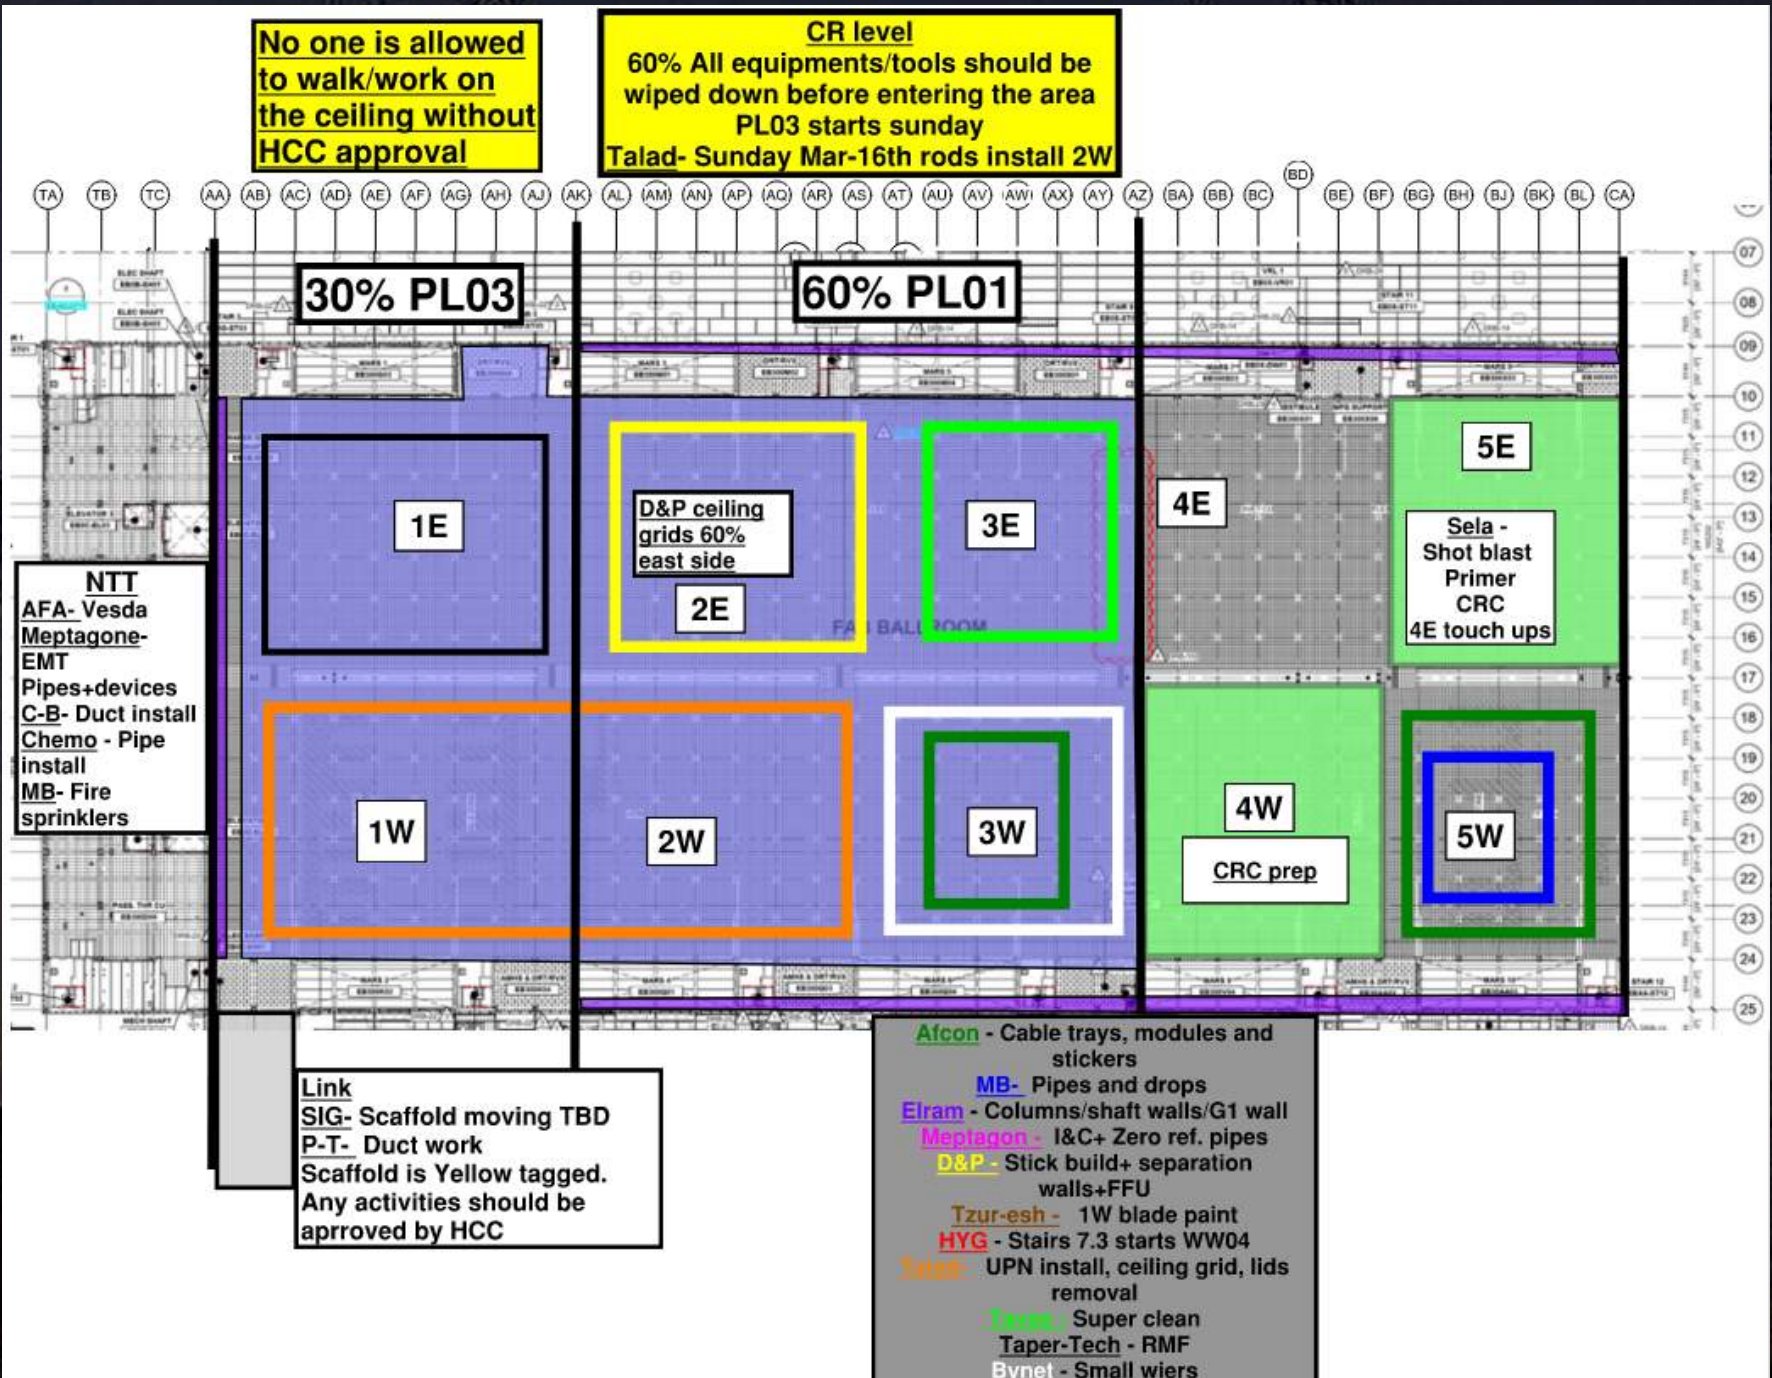

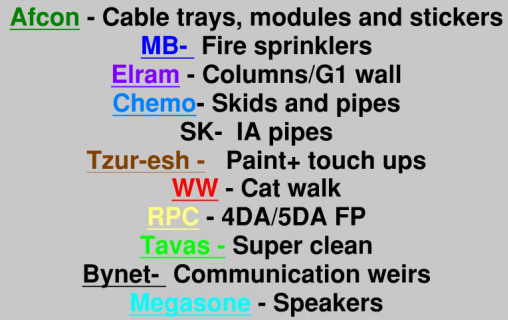

60% All equipments/tools should be wiped down before entering the area
Taper-tech- Sunday MAH will move to correct position

30%

60%

NETT
Chemo- Racks ongoing
Megason - Small
wires+Speakers
RPC- FP rack/girts
NWTT
Chemo- Racks
MB- FS install
AFA- Vesda
RPC- TBD

WW/SN - Handrail install
Elram- G1 metal sheet

TMT- Penetrations for Afcon, D&P, Talad and MB

1E

2

3E


4

51


1V

2V


3W

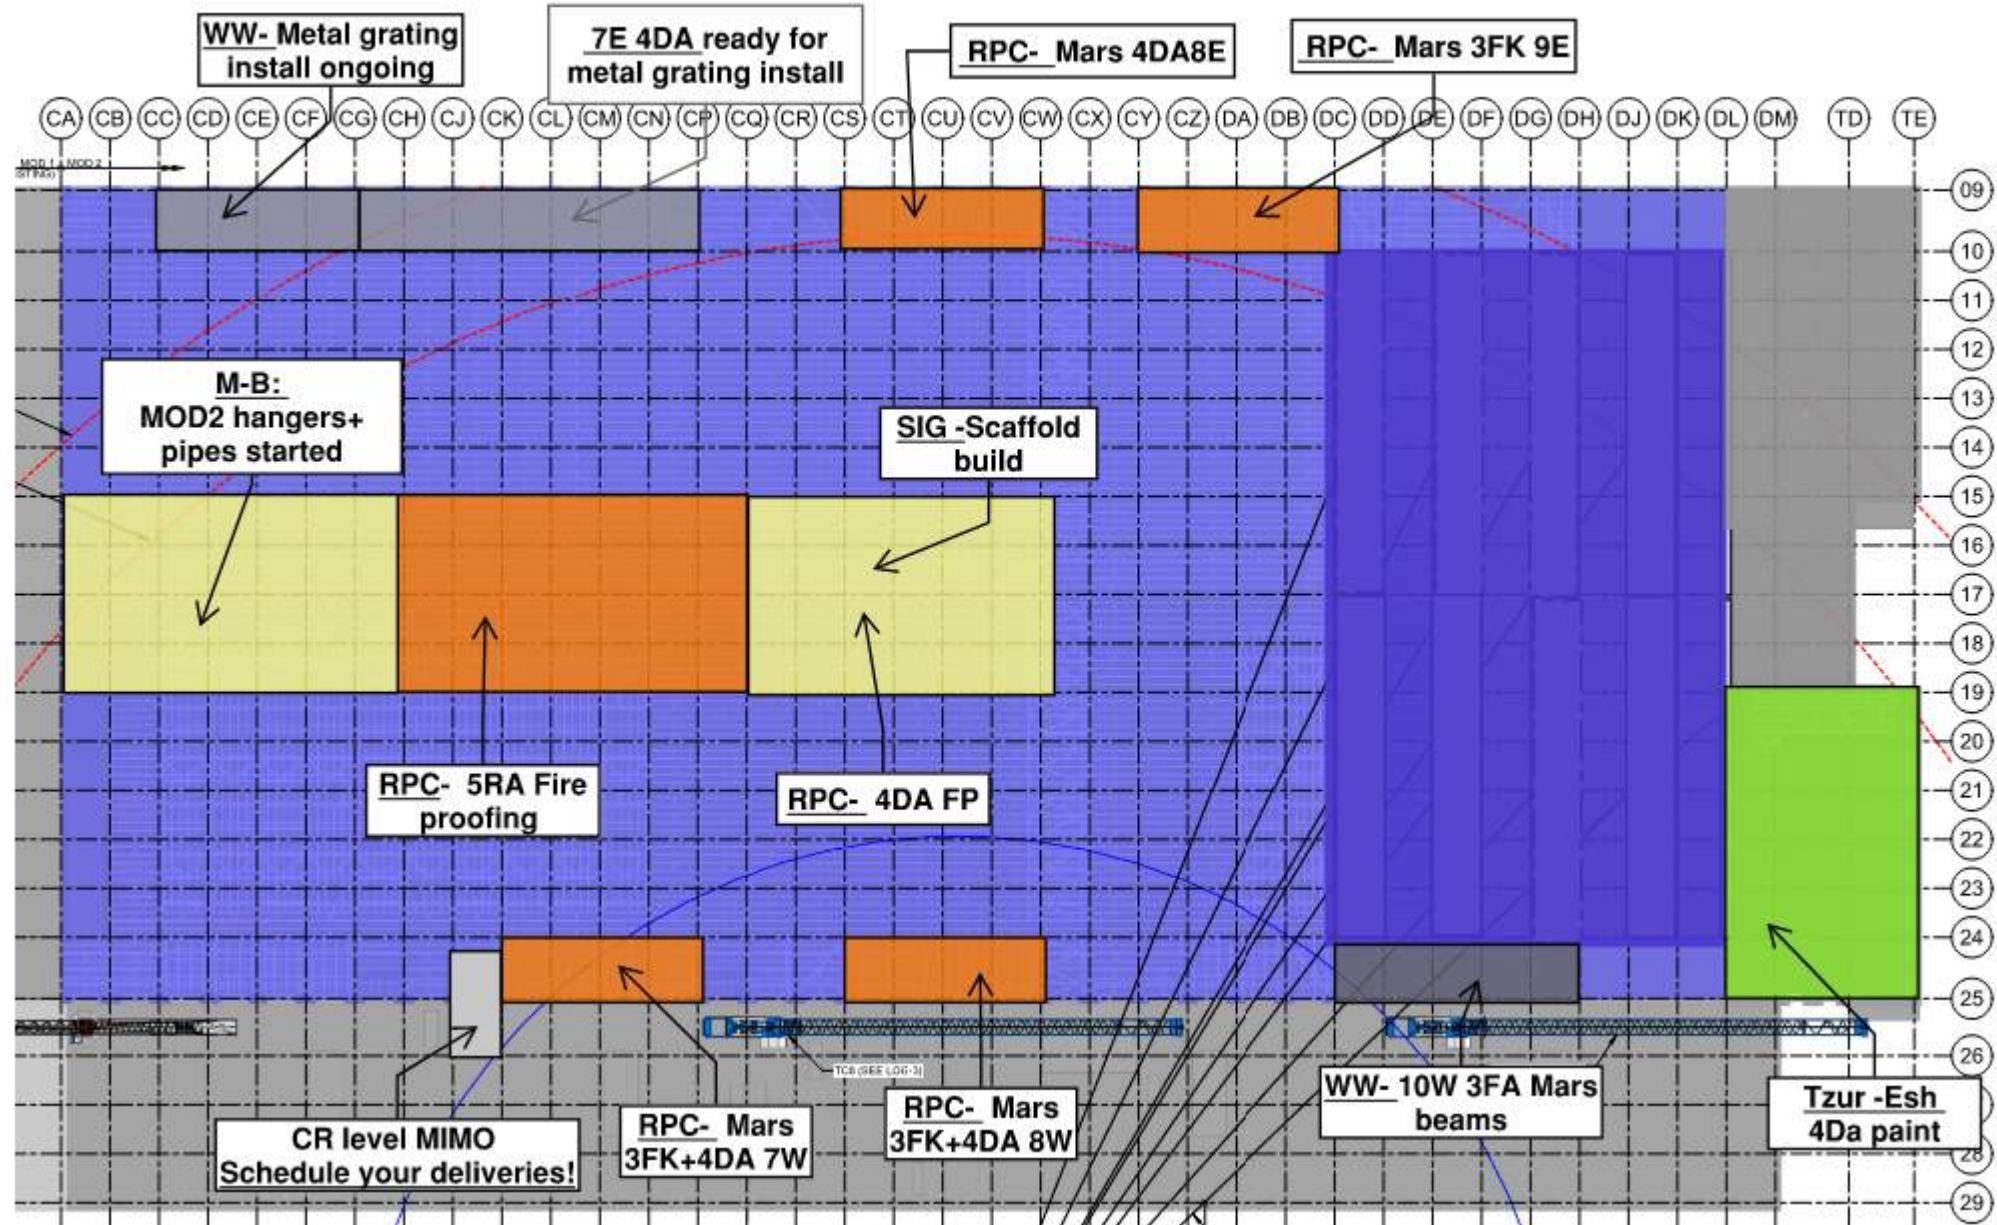

Siding Penetration Request Form

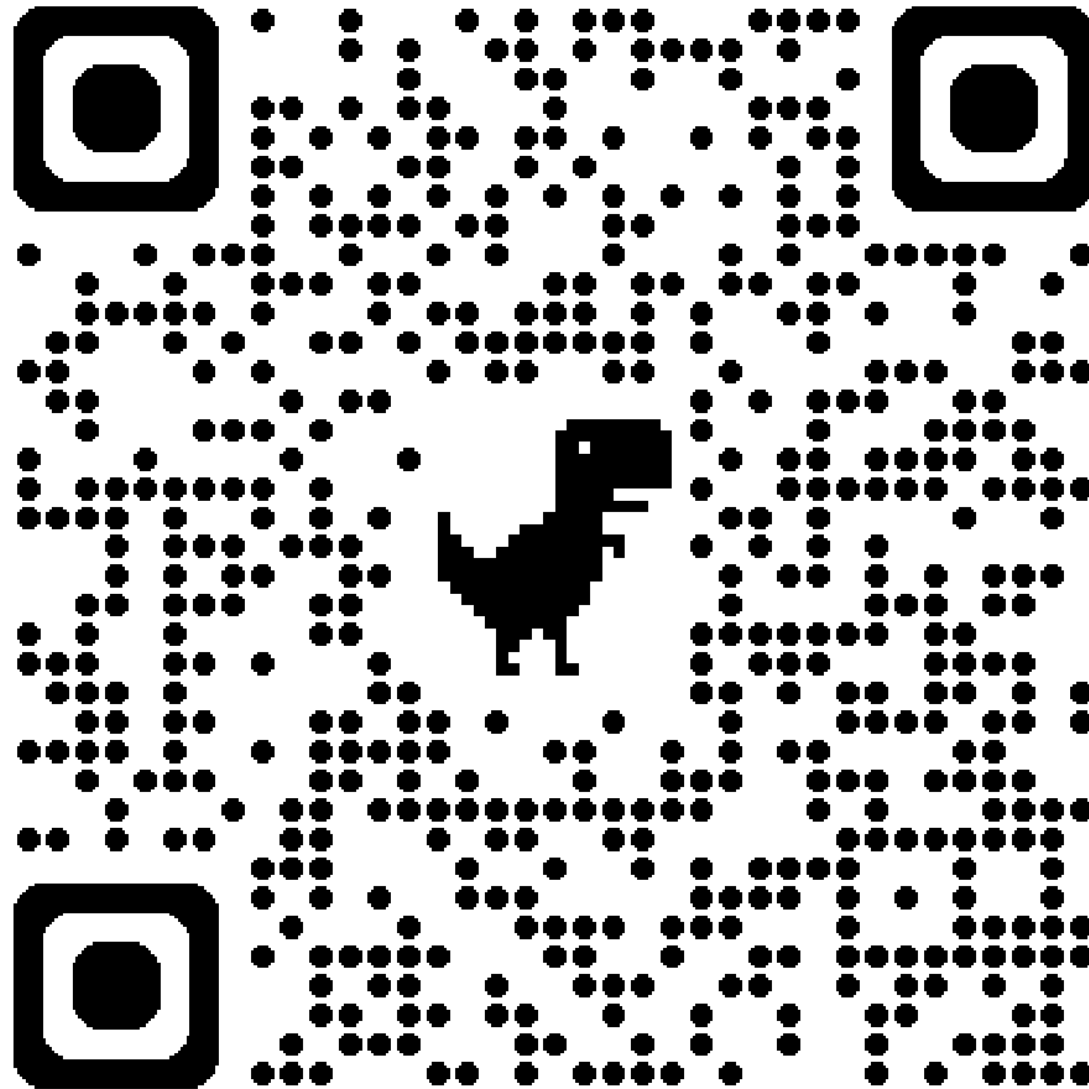

Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

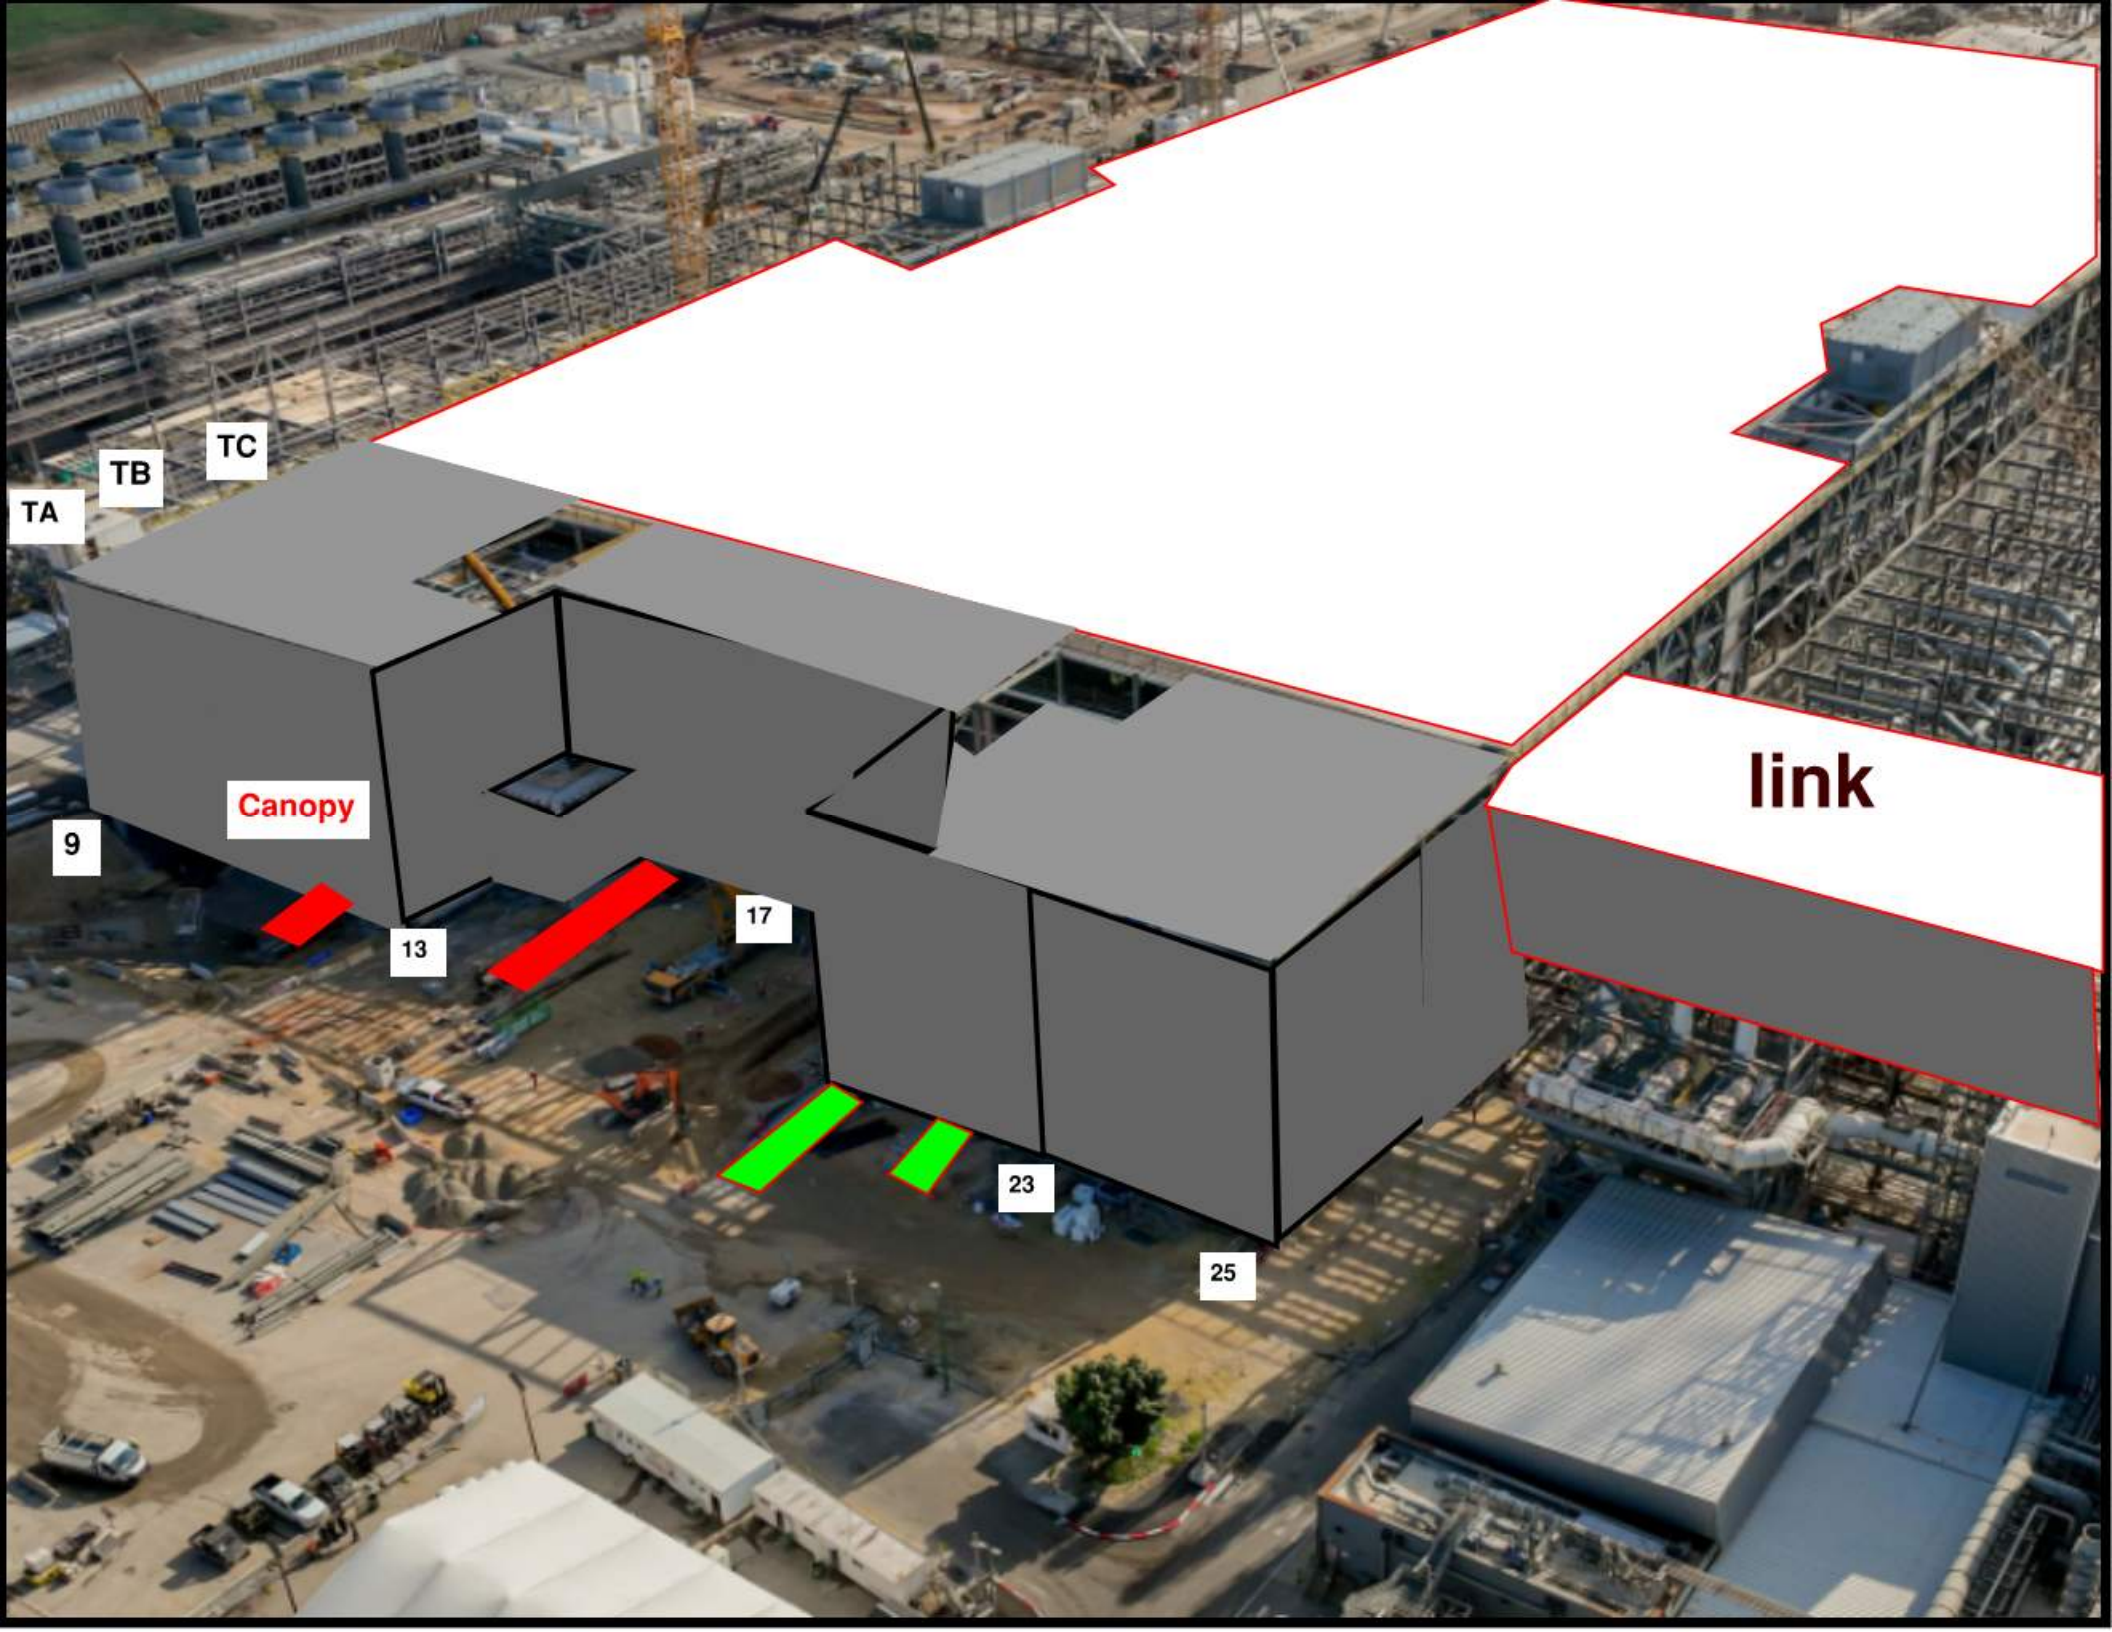

TA

TB

TC

Canopy

link

9

13

17

23

25



MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 

PANELS INSTALLED 

2602/
2601

M
I
M
O

2612/
2611

MIMO
2622/
2621

2632/
2631

2642/
2641

2652/
2651

2812/
2811

2822/
2821


2832/
2831

2842/
2841


2852/
2851

PSSS.1

Utility Level 1YA

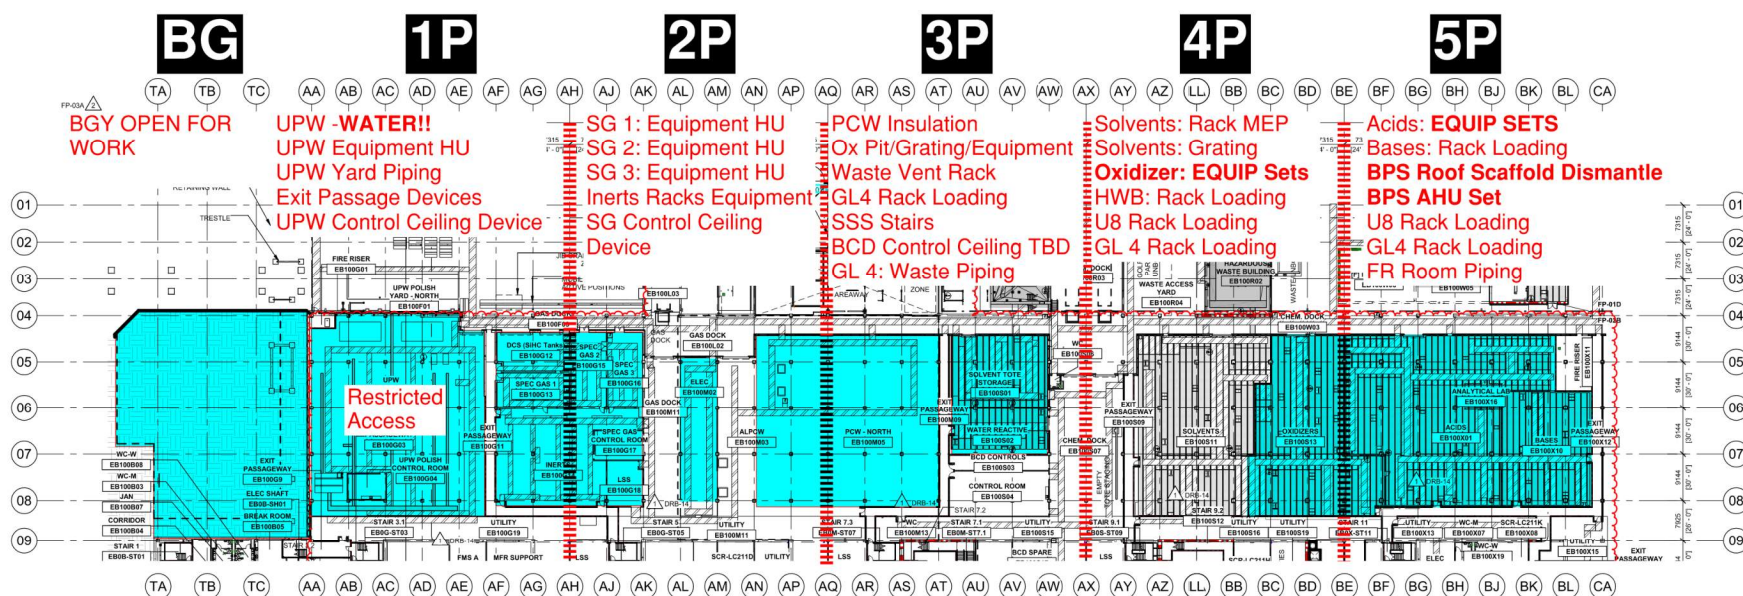


PSSS Roof 2SA

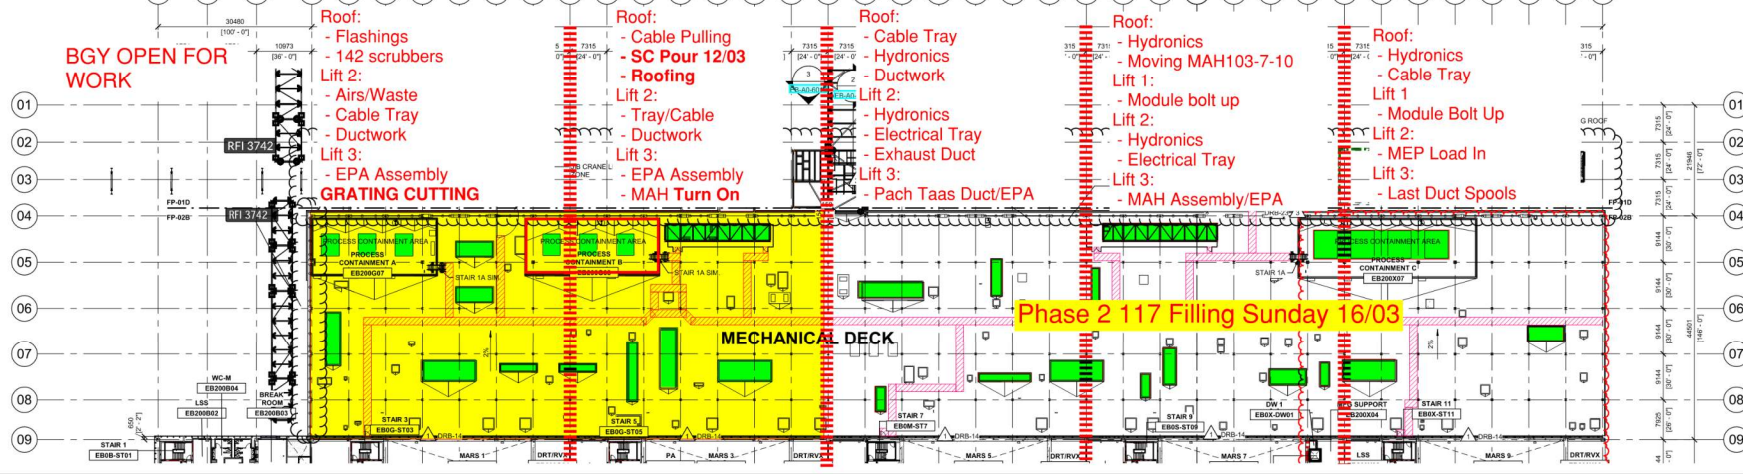

PSSS.2


Utility Level
1YA

PSSS Roof
2SA

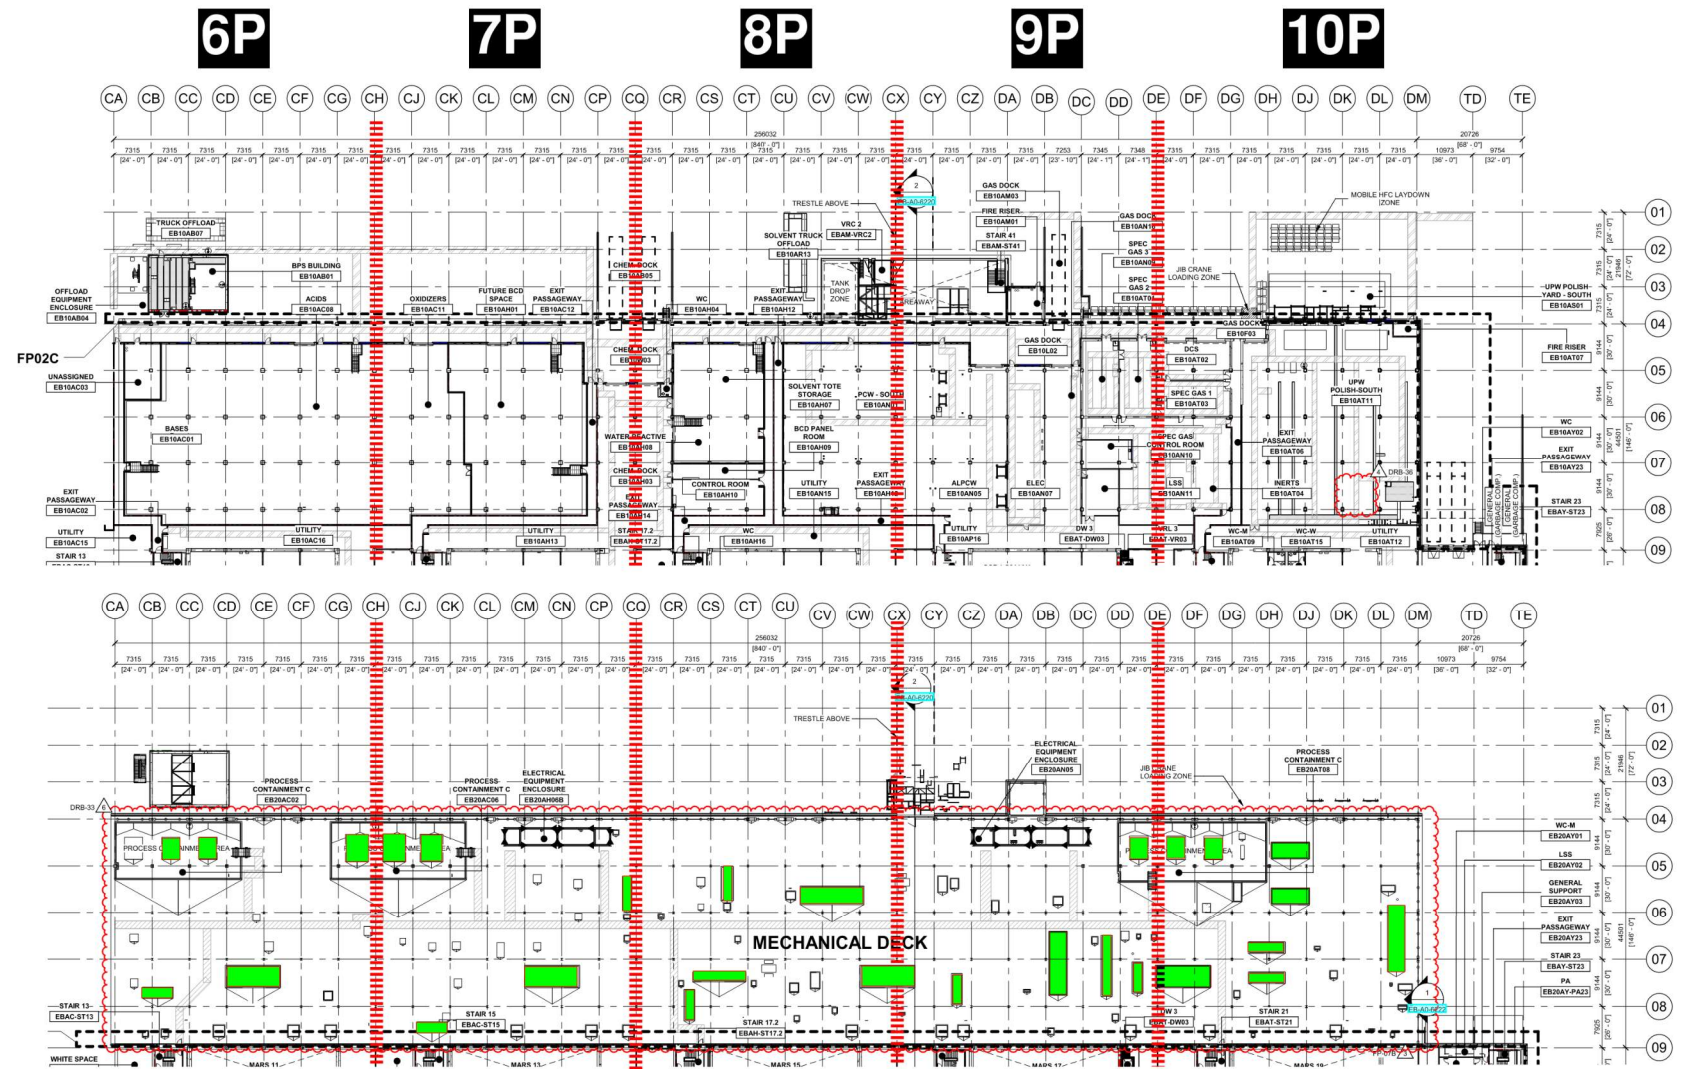

Utility Level

1YA

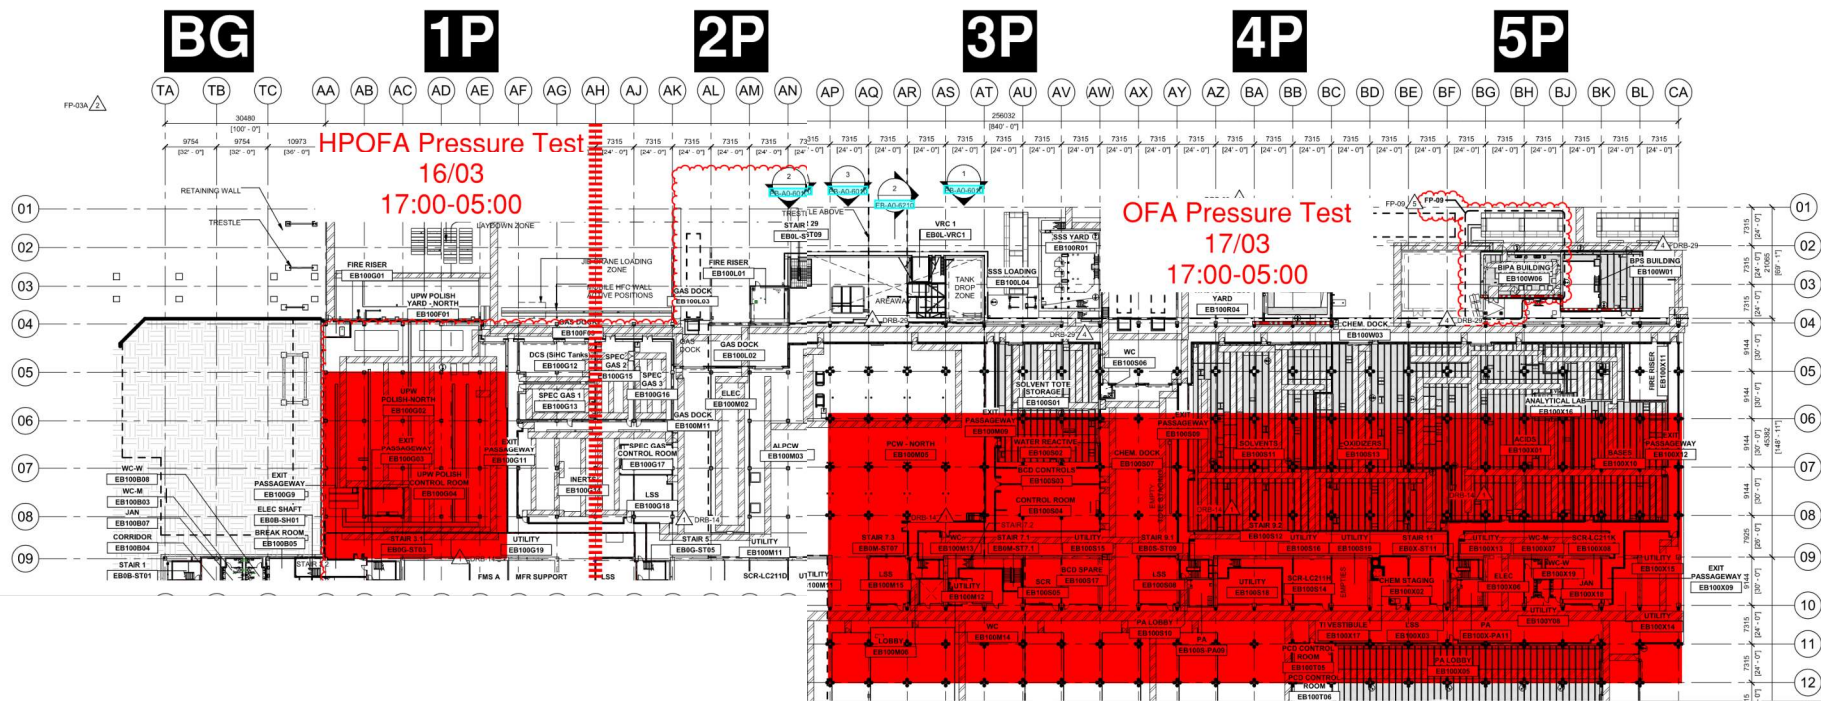


WJG – UL

* BCT - installation of permanent stairs to AHU

* Pach Taas - installation of modules in west SUT.
* BCT - installation of permanent stairs to AHU

* W&W - welding of shims for outriggers
* Carmel Bidud - installation of air ducts from AH

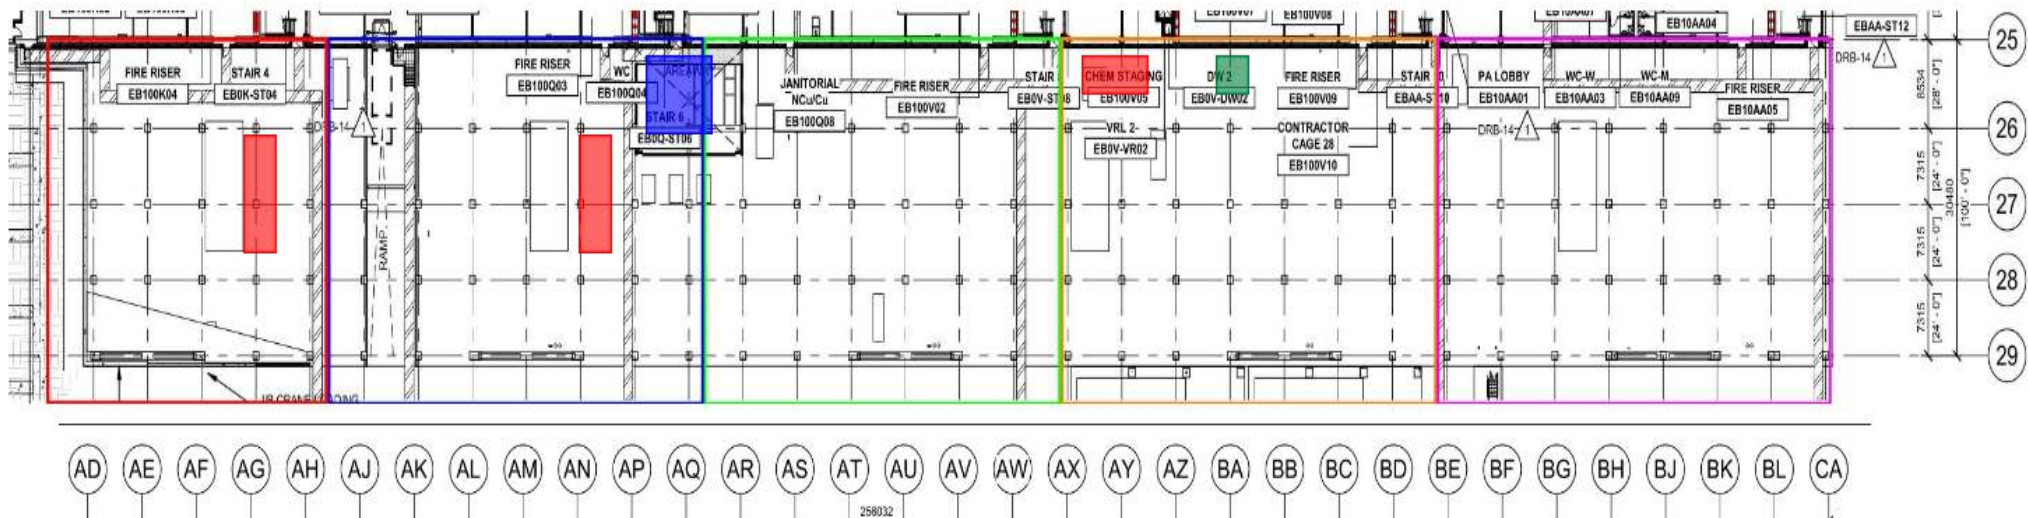




WJG – Lift 2

* Chemo - finishing connection of the Nalco skid for washing and preparing MARS pipes of 2J

* Pach Taas -connection to single stack to exhaust fans

* Carmel Bidud - erection of 5J MAH scaffold

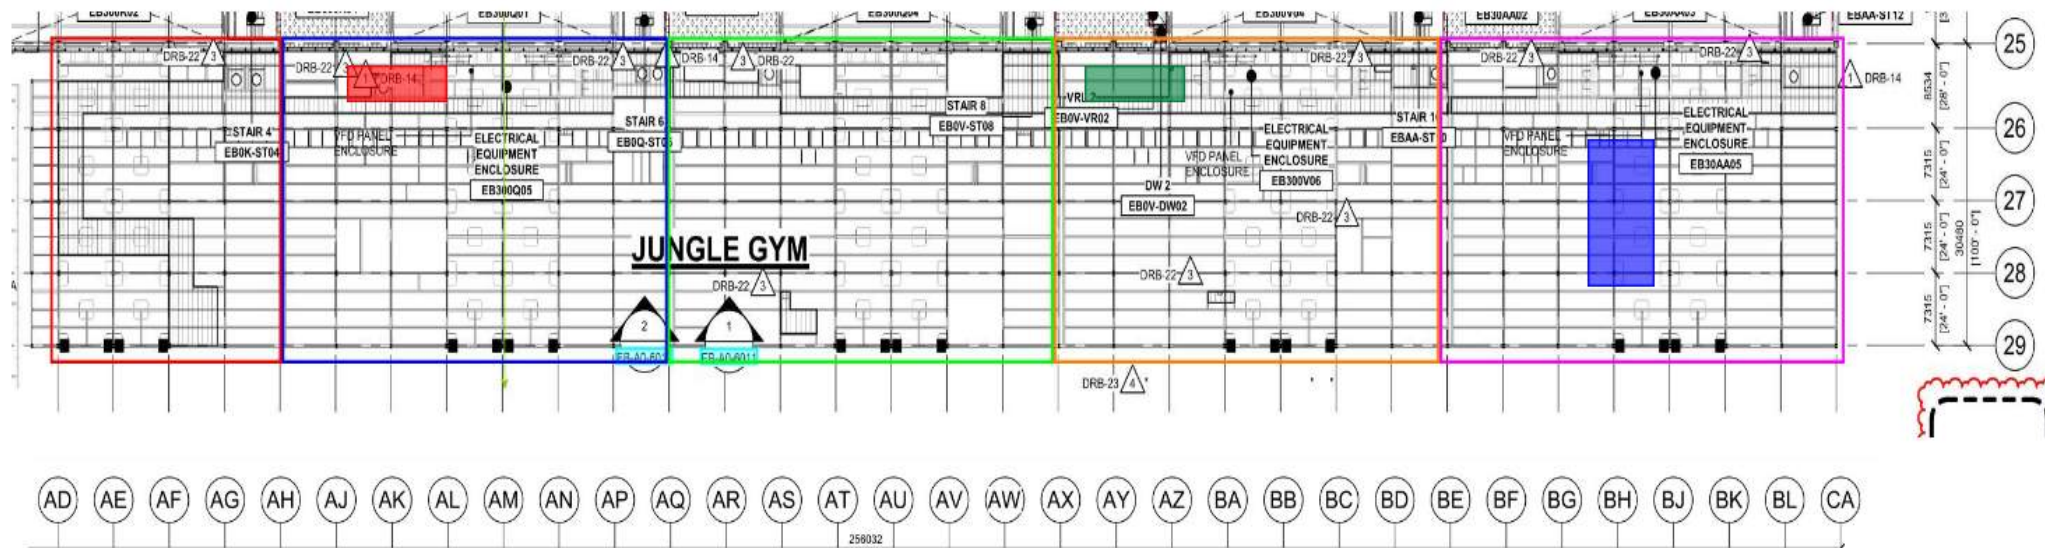

WJG – Lift 3

		* SN removing, cutting gratings and welding supports 	* SN - cutting gratings and welding supports * Pach Taas - hoisting and installing part 1 of the EPA platform 	* SN -cutting grating penetrations * SIG - handrail modifications
--	--	--	--	--







Crane logistics

Crane: 750 ton crane
located at AV-AW.
until 31/03/25



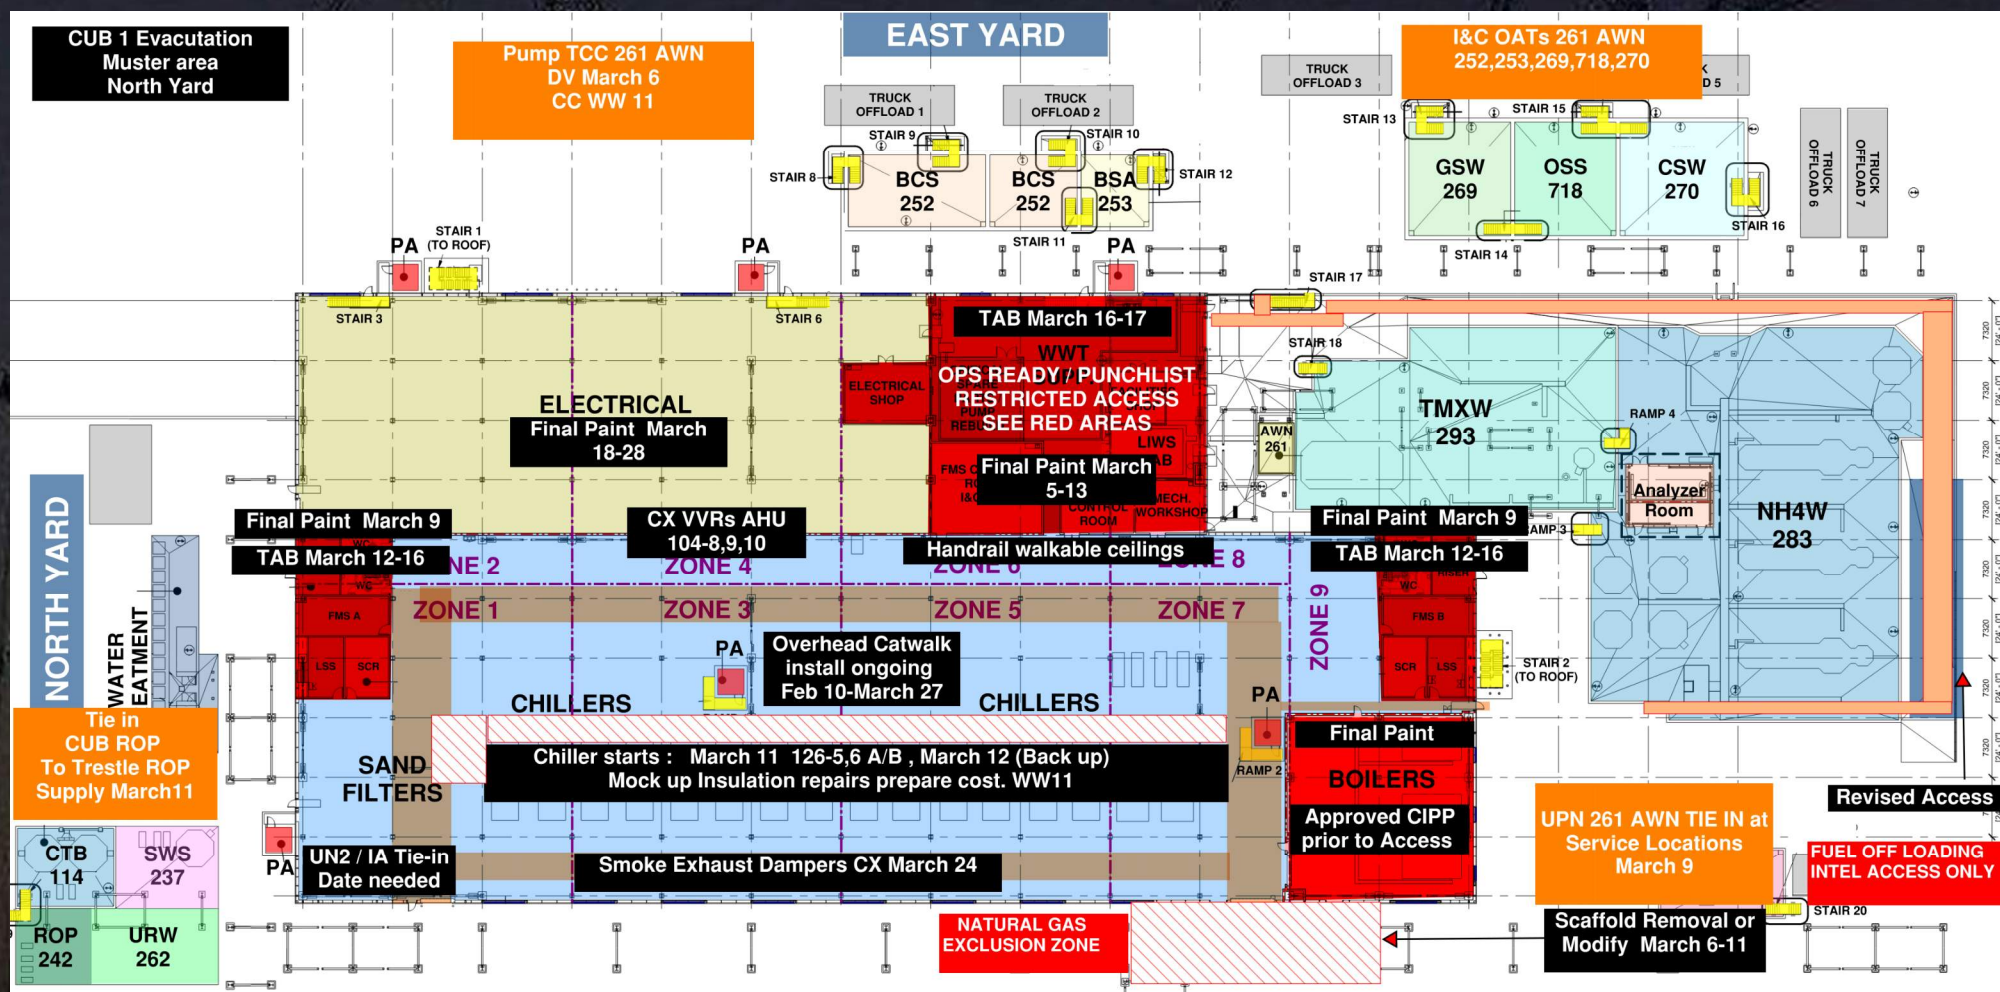

CUB 1 West Wall coordination /Trestle/Site

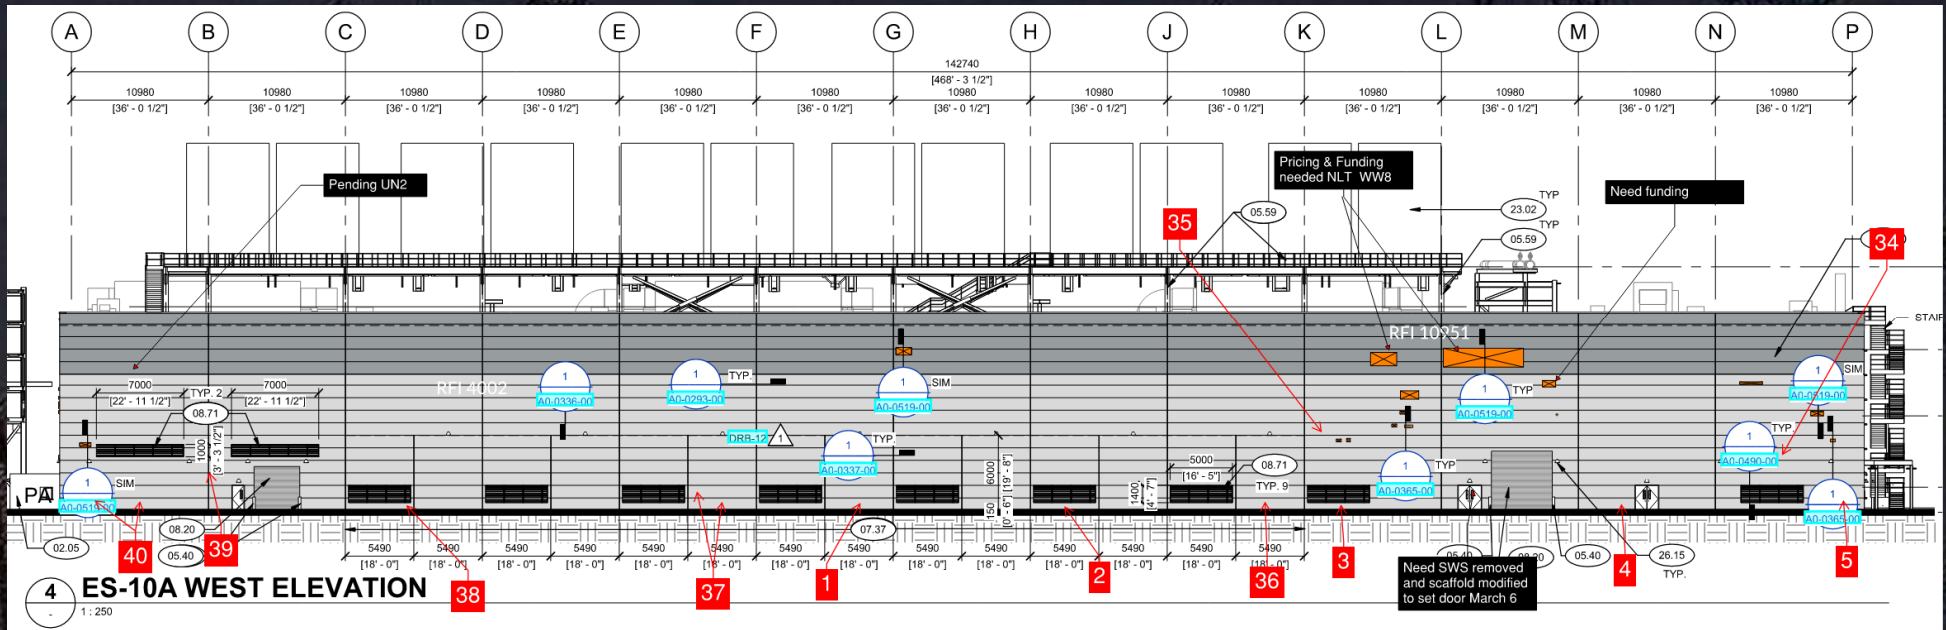


- Waste Systems Pressure Testing Wrap up 3d March 4-5
- Trestle Scaffold removal 5d March 6-11
- Metal flashings and Panel work Man Door 5-7d March 12-20
- Claim Envelope ready for DVs March 20
- DV acceptance list and corrections 7d April 2
- Ops Ready April 3
- Concrete removal Site Grading Form rebar pour concrete 5-7 d Schedule under review
- Bullards 2d April 1-2


CUB 1 – EXTERIOR/ROOF




CUB 2- Load in ,H&T, Framing and Sheetrock

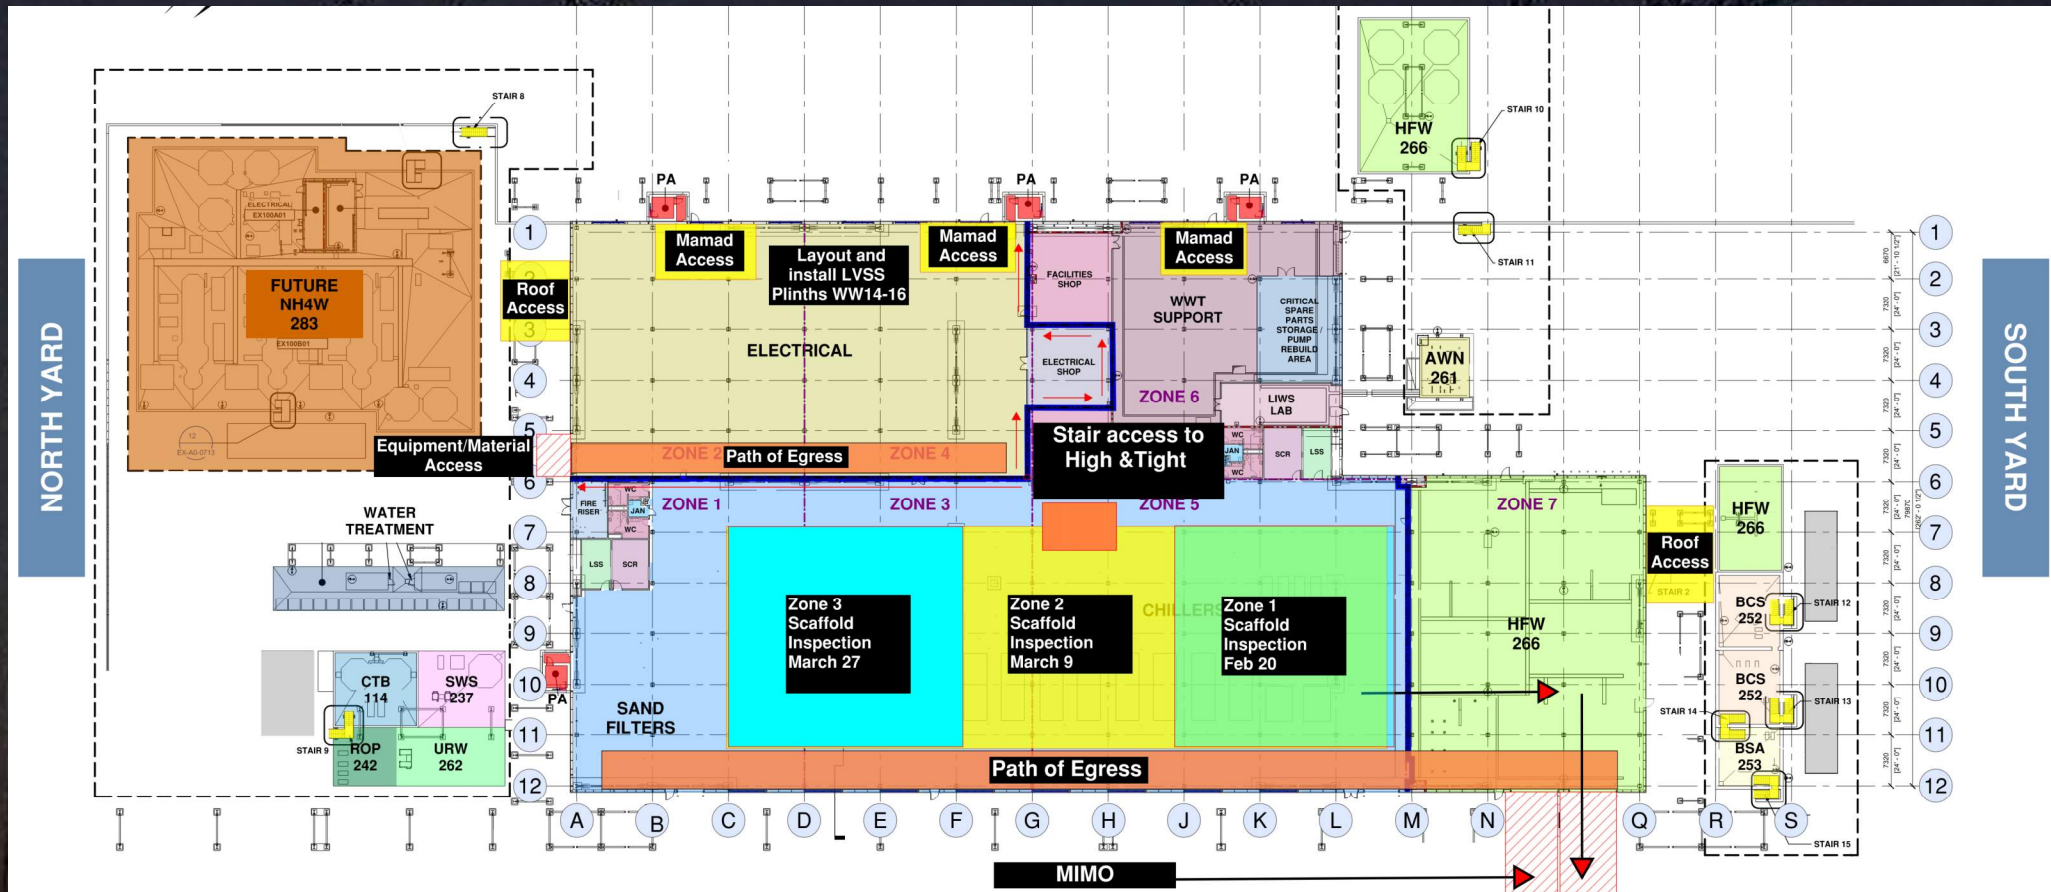



CUB 2 – EXTERIOR/ROOF

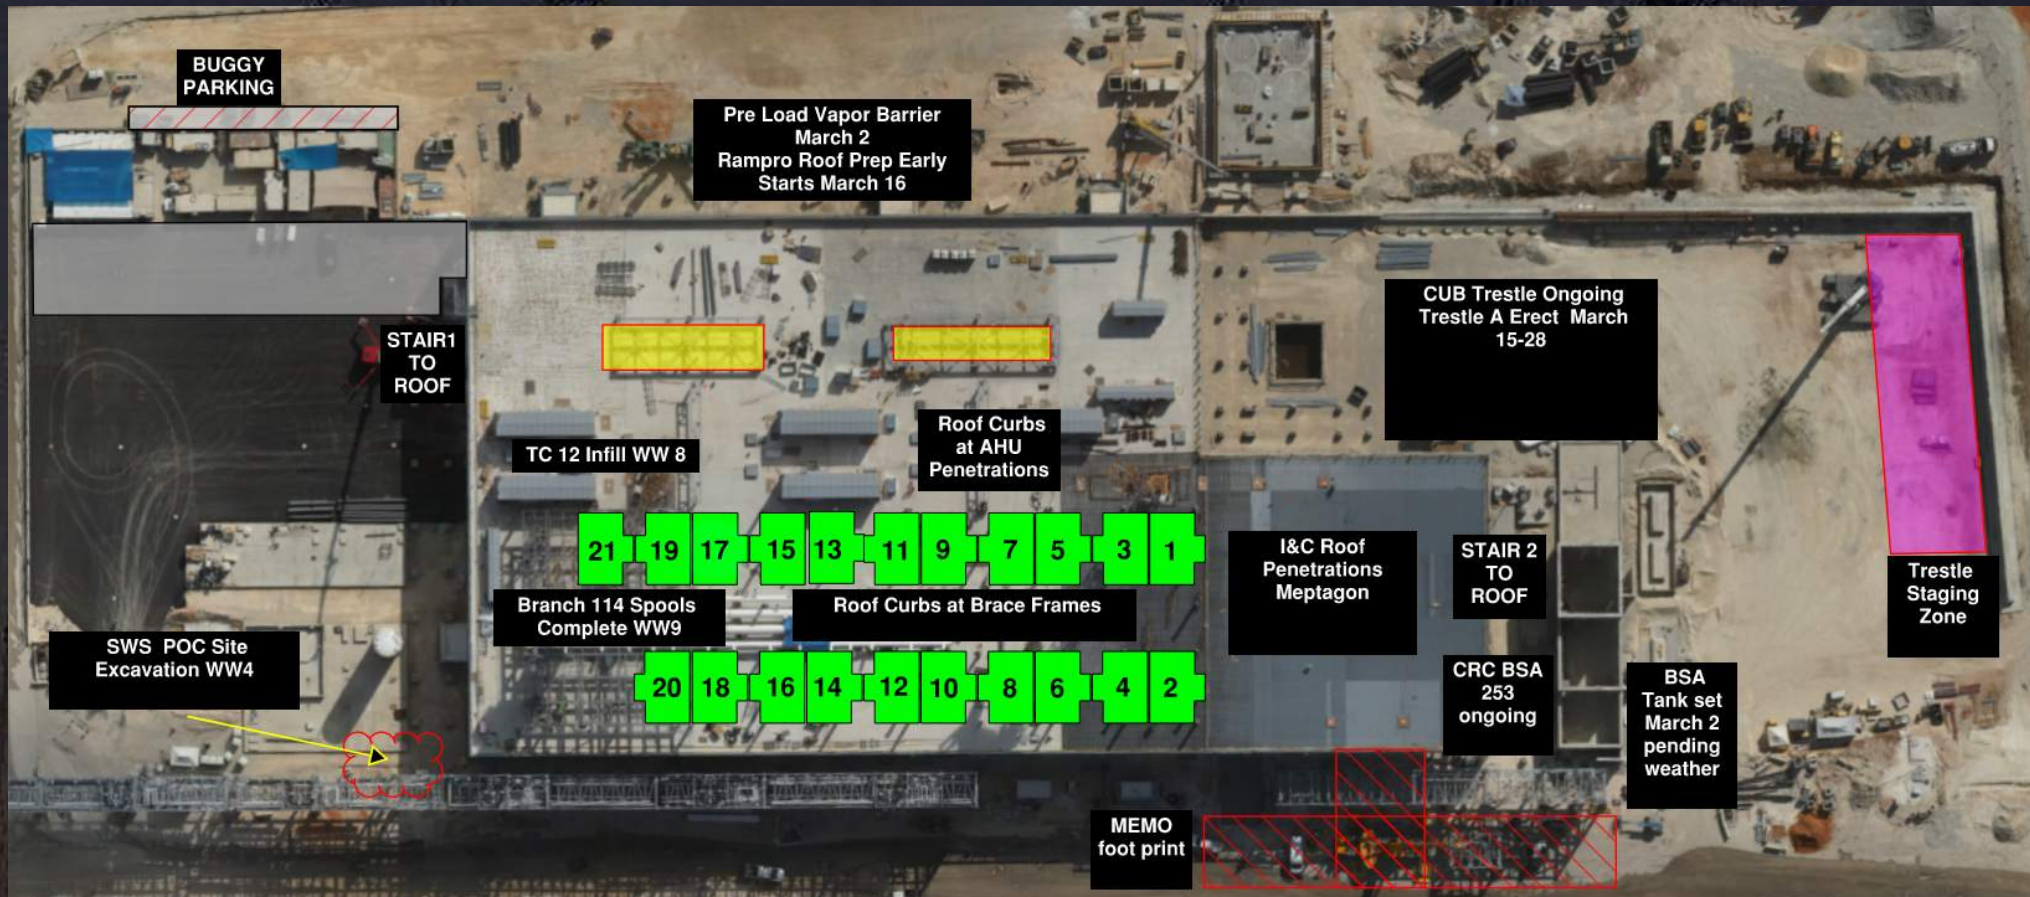



HOFFMAN CONSTRUCTION COMPANY

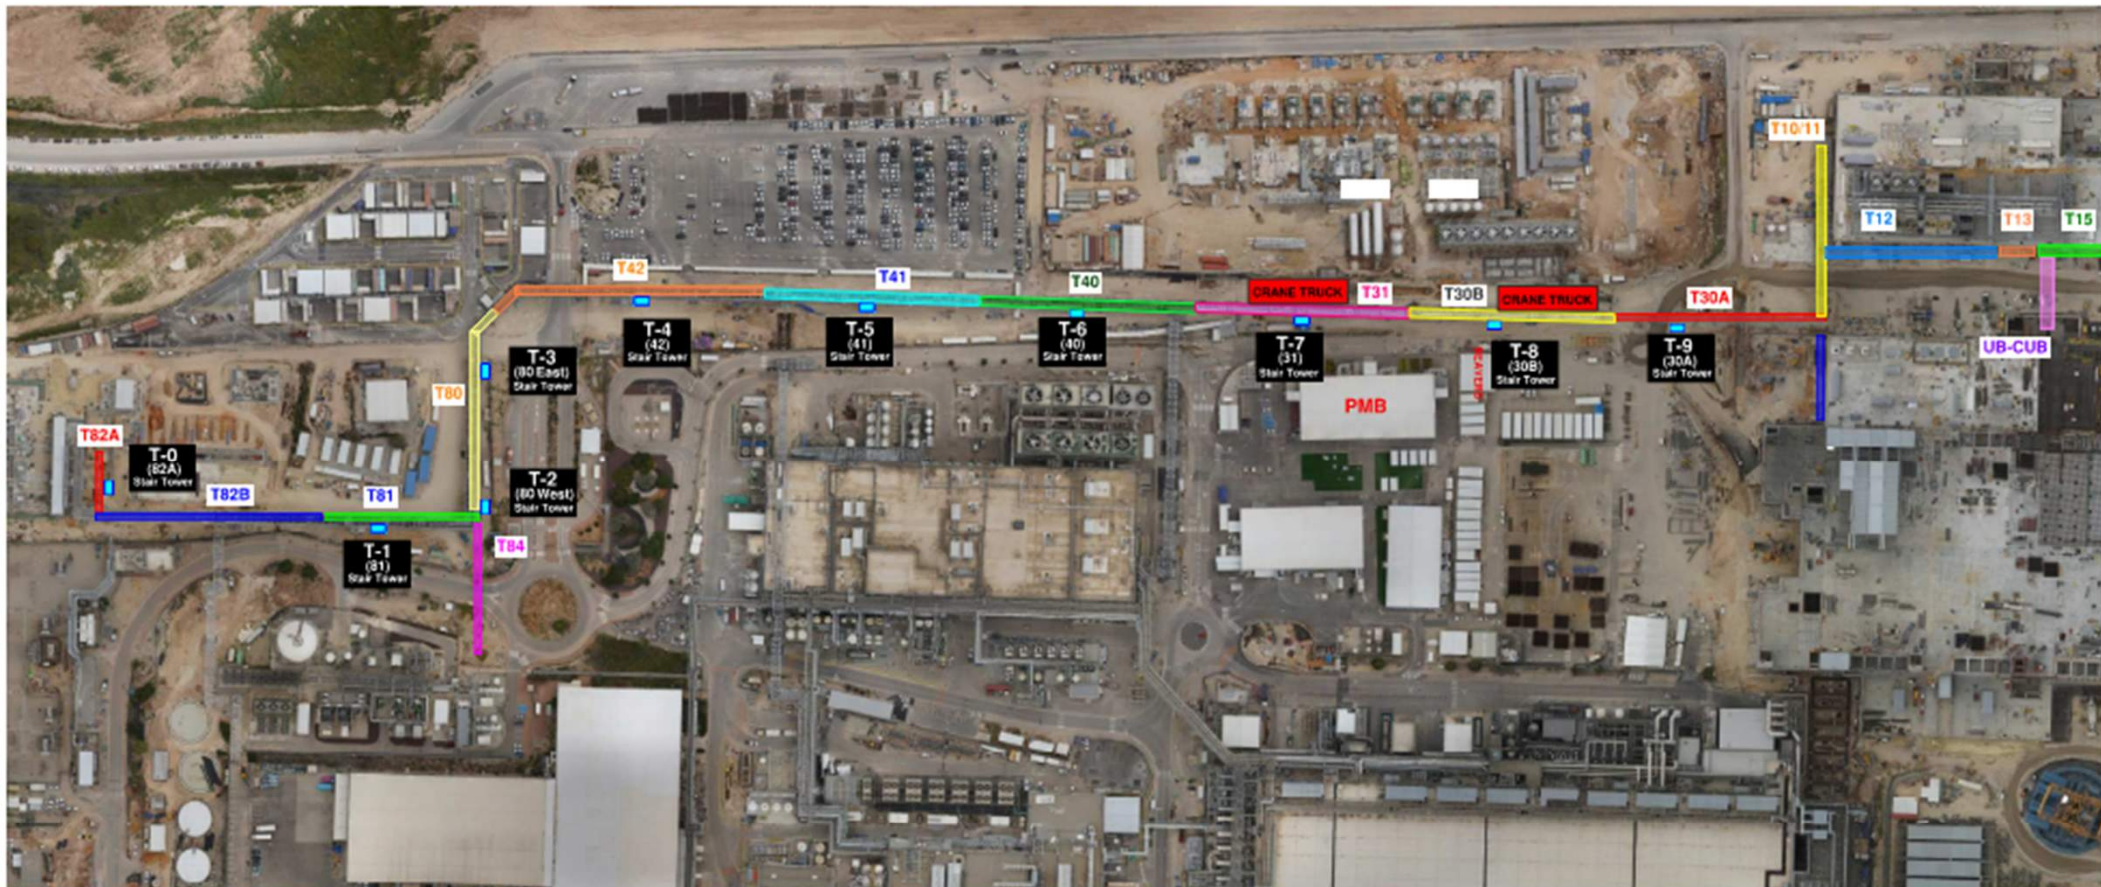



HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

INTEL- blue fence

OFA PRESSURE TEST

THURSEDY

MAR.13 18:00

FRIDAY


MAR.14 -14:00



Daily Coordination Meeting

Site Logistics

North

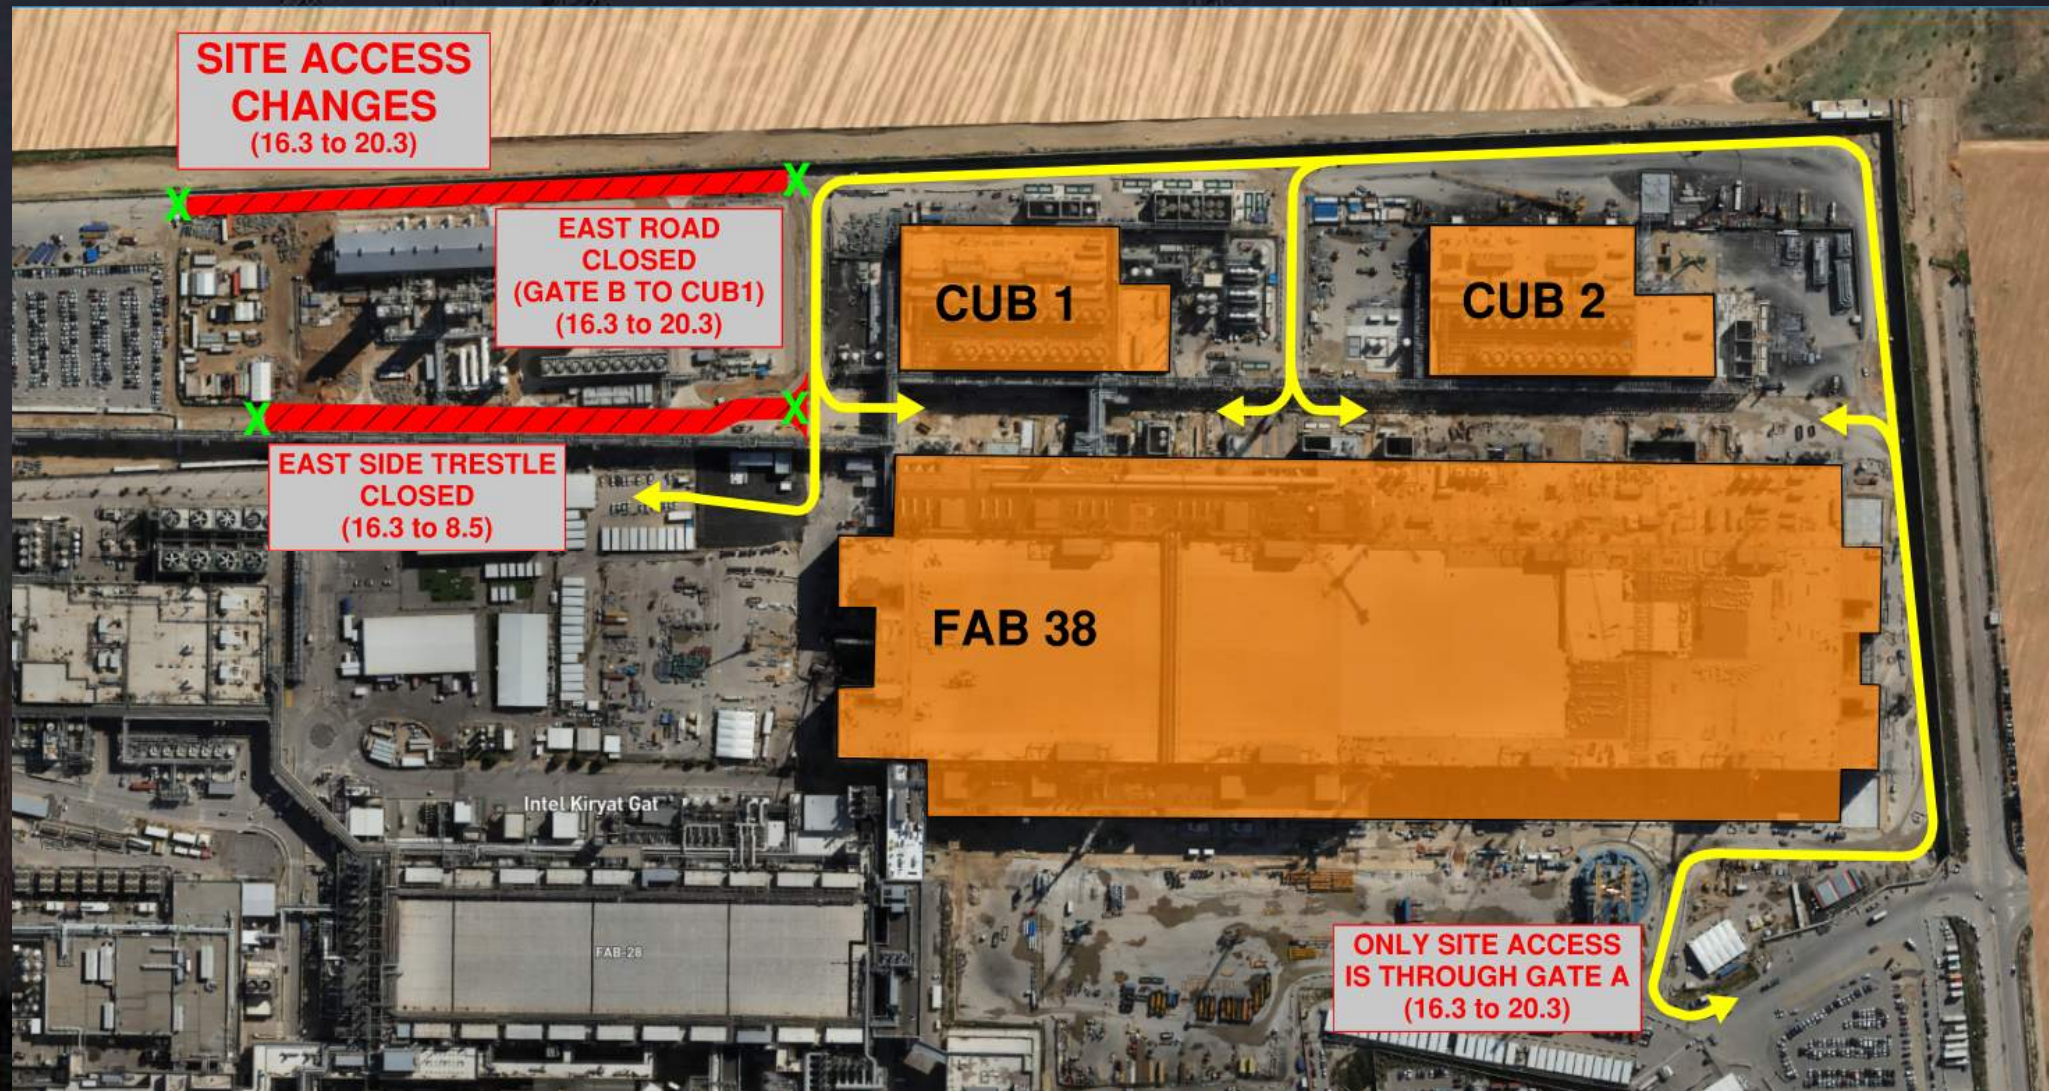



Daily Coordination Meeting

Site Logistics

North






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South

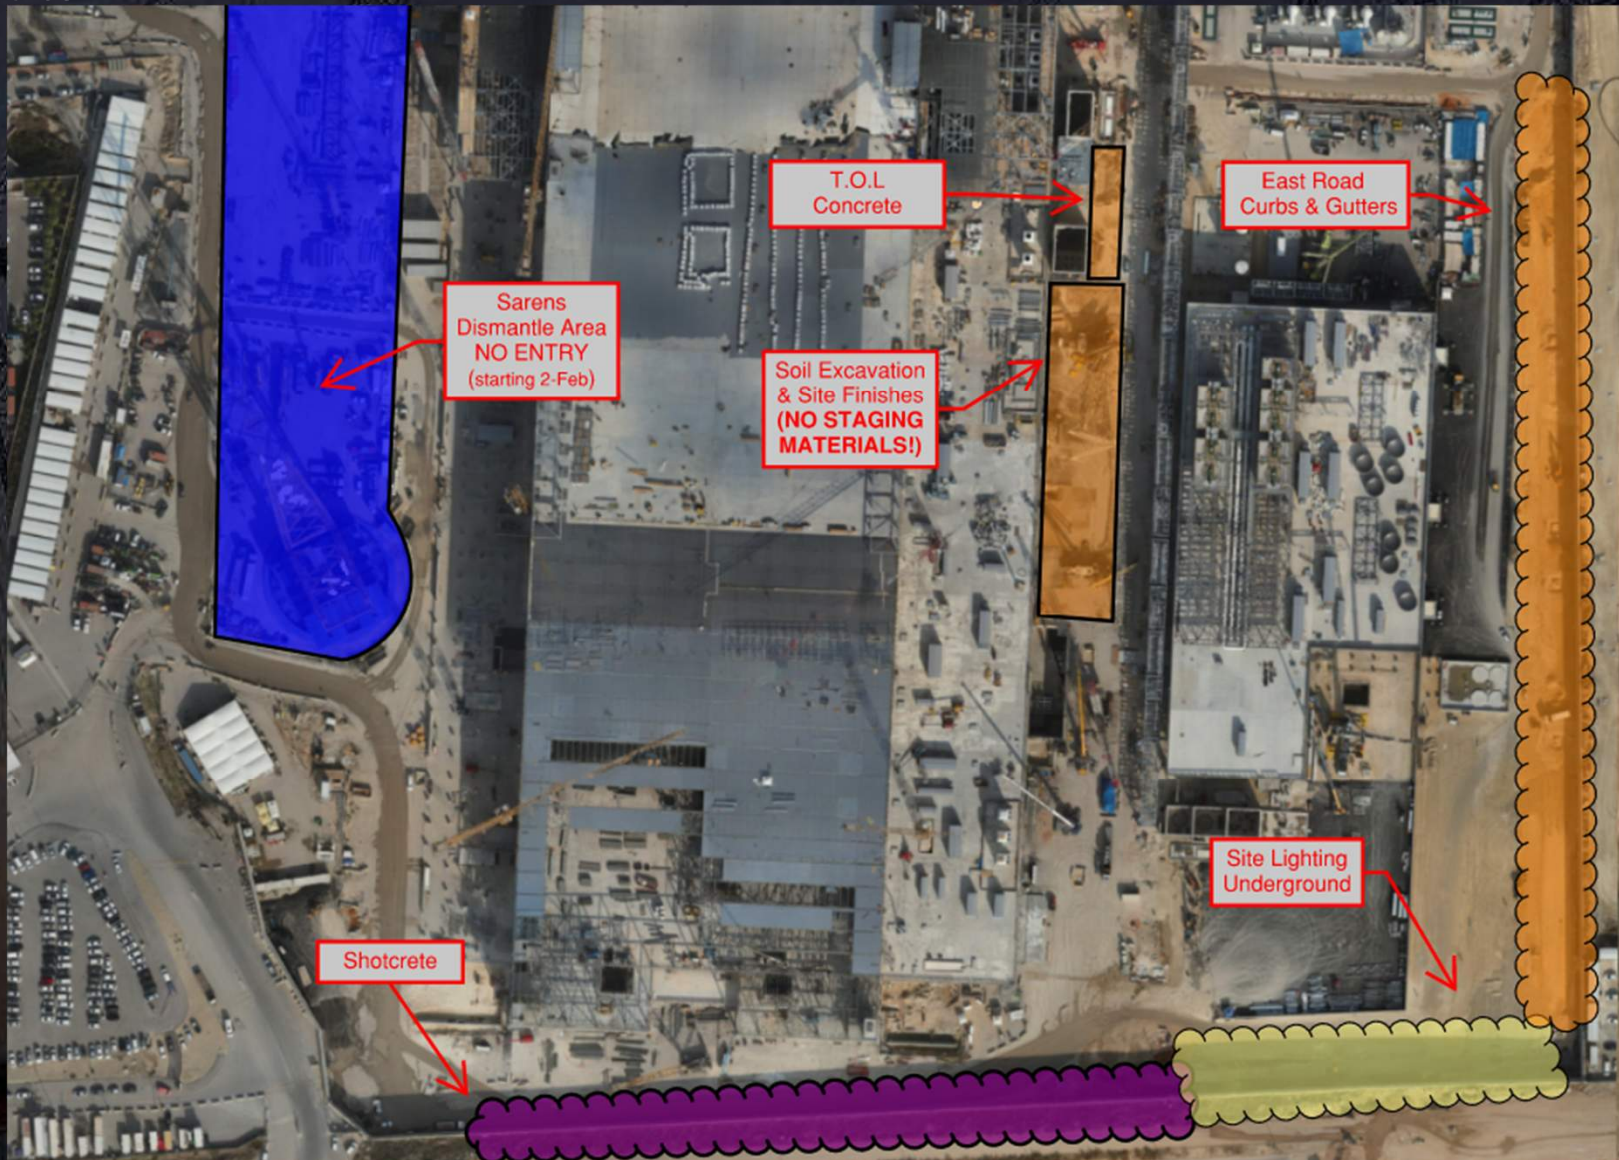



Strong winds

A reminder to ensure the work areas are tidied up before leaving for the weekend. Additionally, please make sure that all equipment on-site is locked and secured. A strong winds is expected today and over the weekend, so ensure that all wheels and equipment are stable, and will not move, damage, or collide with other equipment or objects during the storm.

Also, don't forget to empty any full trash bins in the work area before leaving. Please make sure all bins are cleared. If anyone needs assistance, feel free to reach out to HCC.

HCC/EHS Weekend Work- 14.03.2025

White Board Meeting in Beavers at 06:30

Superintendents

John Scot - 052-3291705
Sahar-Samin - 052-2759653
Roi Zaidin - 052-2146194
Netanel-Grably - 054-4887622
John-McCradden - 052-3756957
David-Jollands - 052-3961675
Tony Dixon - 052-3952068
Sean-Murphy - 052-2563950
Atias Yosi - 052-3060790

CSA CM

Zach-Niebergall - 052-3471103
Yaruslav Zemskich - 052-2438340

Crane

Maksym Panov - 055-9181086

Cx

David-William - 052-3470794

Safety

- Safety Foreman- Mohammad Zakakti- 054-8121212 Mohammad-Zakakti@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Officer - Arkady Gerber-050-6851432 Arkady-Gerber@Hoffmancorp.com

Subcontractor Weekend Work- 14.03.2025

FAB

SNJ – Liran – 052-8939558

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Clean Room

- Talad – 30 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Igor 0544509386)
- Chemo – 25 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Liran 0532323696, Eden 0585335445)
- Sig – 20 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Oleg 0542689370, EHS Ovidiu 0546993648)
- Tavas – 18 guys , 12 cleanroom maintenance, 6 at interstitial (Super Inas 0537148630, EHS Vadia 0528412021)
- W&W 20 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)

Subfab

- Pach Taas
3W 4W MARS
 - Team lead: Nethanel - 0556862261
 - EHS: Yazen – 0528104038
- Afcon E
All Over SF
 - Anklesh - 0526008487
- Lesico
 - 3W,3E PT
 - Gabriel 0549892929
- Sela
 - 10W MOD2
 - Team lead: Dolev - 0548100126
 - EHS: Shmuel – 0506306031
- Sig
 - SF Marsh Shafts
 - Shmulik - 0549205966

Subcontractor Weekend Work- 14.03.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/Lift 2 Waste Piping
- Foreman – Chaim – 054-5210133
- Safety – Marzuke – 054-447-7112
- Lesico – Low Point Drains on PSSS Roof/OFA in Solvents
- Foreman – Suju Pally – 052-7755967
- Safety – Tal Madar – 052-8229109
- SK Engineering – Lift 2 MAH 4P/DW Punchlist
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- W&W – Grating Cutting Lift 3 1P
- Foreman –
- Safety –

WJG

Afcon:

Safety: Steven Shartho – 0559129333

Foreman: Mantu Singh – 0559116973

Pach Taas:

Safety: Yazan – 0528104038

Foreman: Netanel idleberg – 0556862261

SK:

Safety: Majdi – 0546192581

Foreman: Marcelo – 0542072784

SN:

Safety: Wisam -

Foreman: Maxim – 052-2774533

Subcontractor Weekend Work- 07.03.2025

CUB

Chemo CUB 2:

Dudu - 0509808846

Leonid - 0548883878

Sela CUB 2:

Dolev - 0548100126

Shmuel - 0506306031

SKE CUB 2:

Mario - 0548991051

Majdi - 0546192581

Trestle

SNJ:

Piping:

17 People - pipe pressure test

Safety - Yossi Strol 0544965867

Team leader - Muchless attack
0528341298

Site

- Derech Afar – Shotcrete wall

Daily Coordination Meeting



14:00 Sign In
