

Daily Coordination Meeting




Daily Coordination Meeting

General Topics:


- Upcoming work hours= Fri-normal, Sun-closed&no night shift, Mon-open at 6:00 (MSM@07:00)

UTILITY LEVEL MOD1

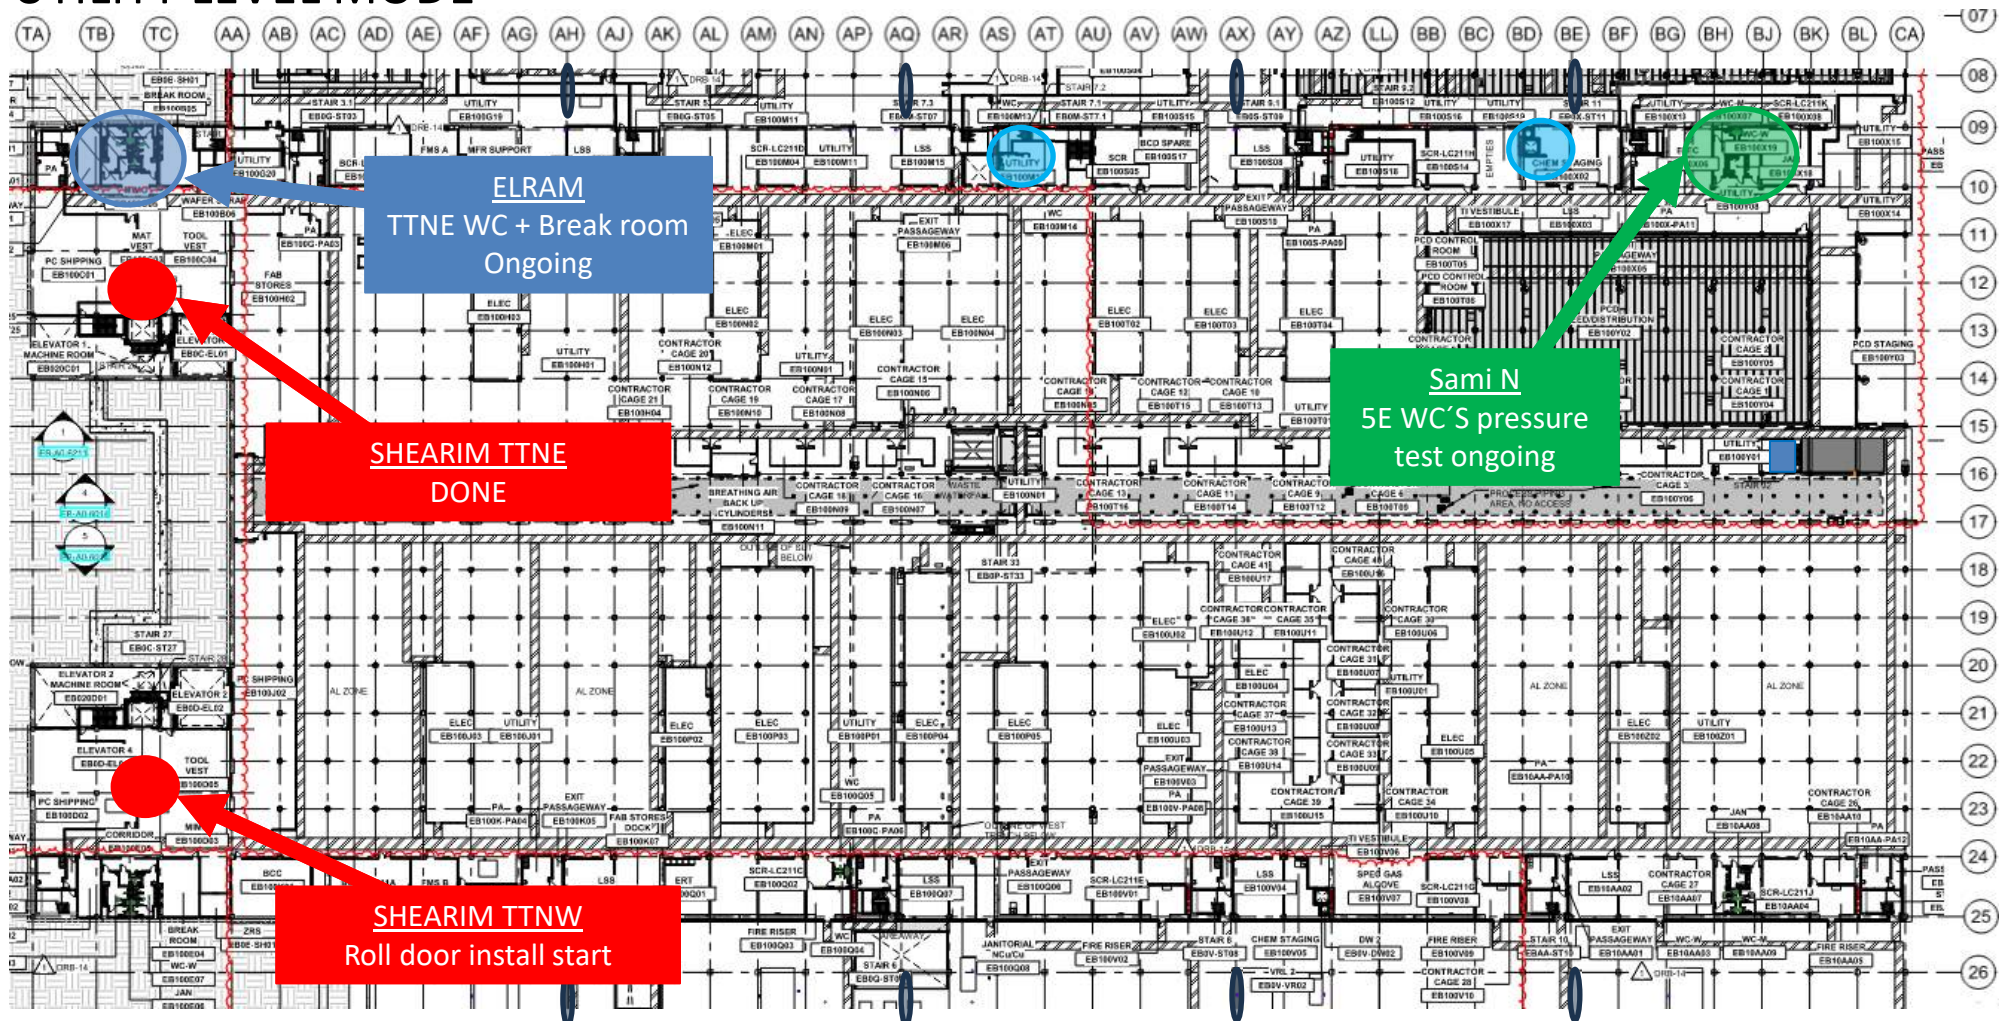




SUT 38.1 LEVEL

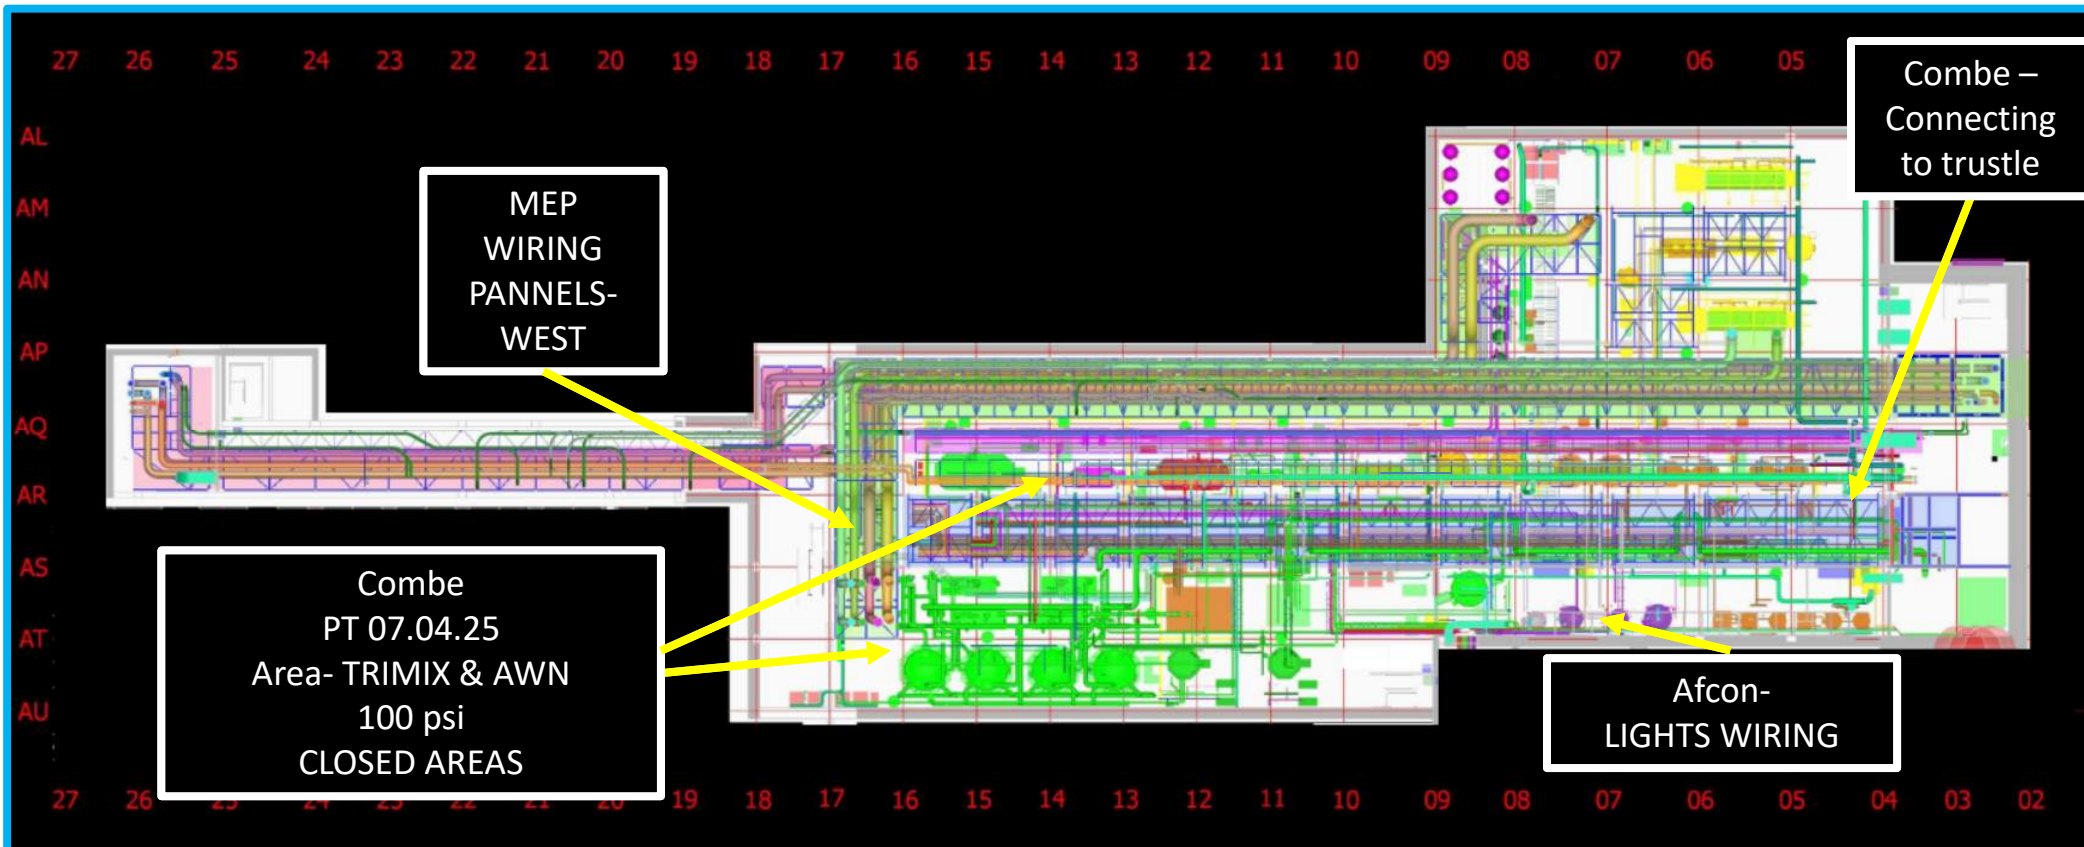

SUT 38.2 LEVEL

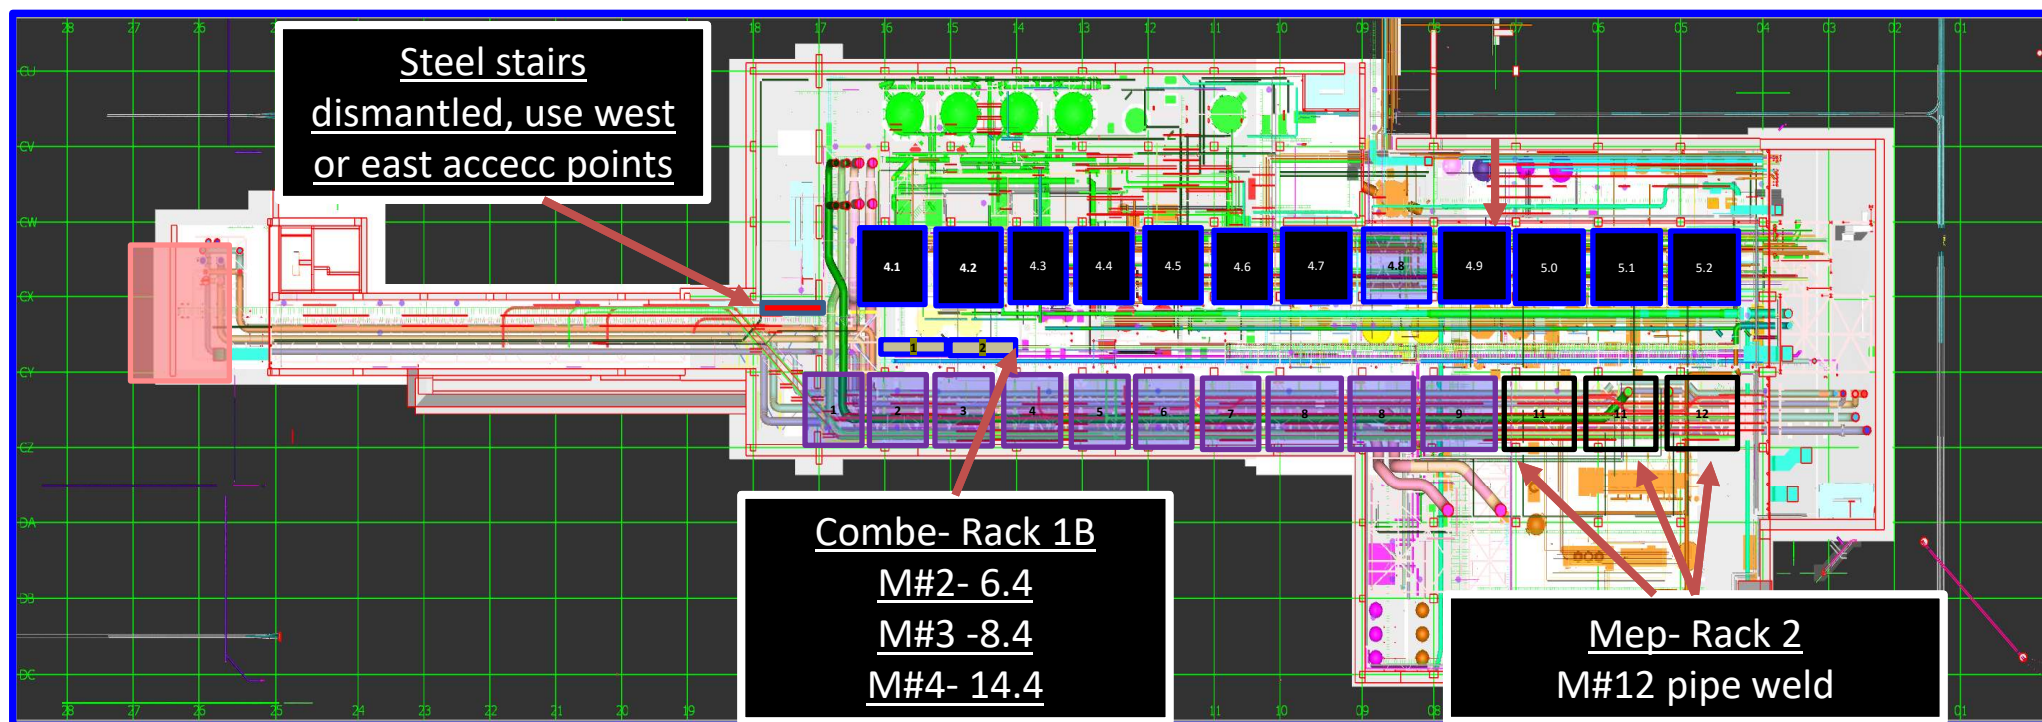


Slide 5

IK1


Ibrahim Krinawi, 3/5/2025


SUT 38.1 LEVEL

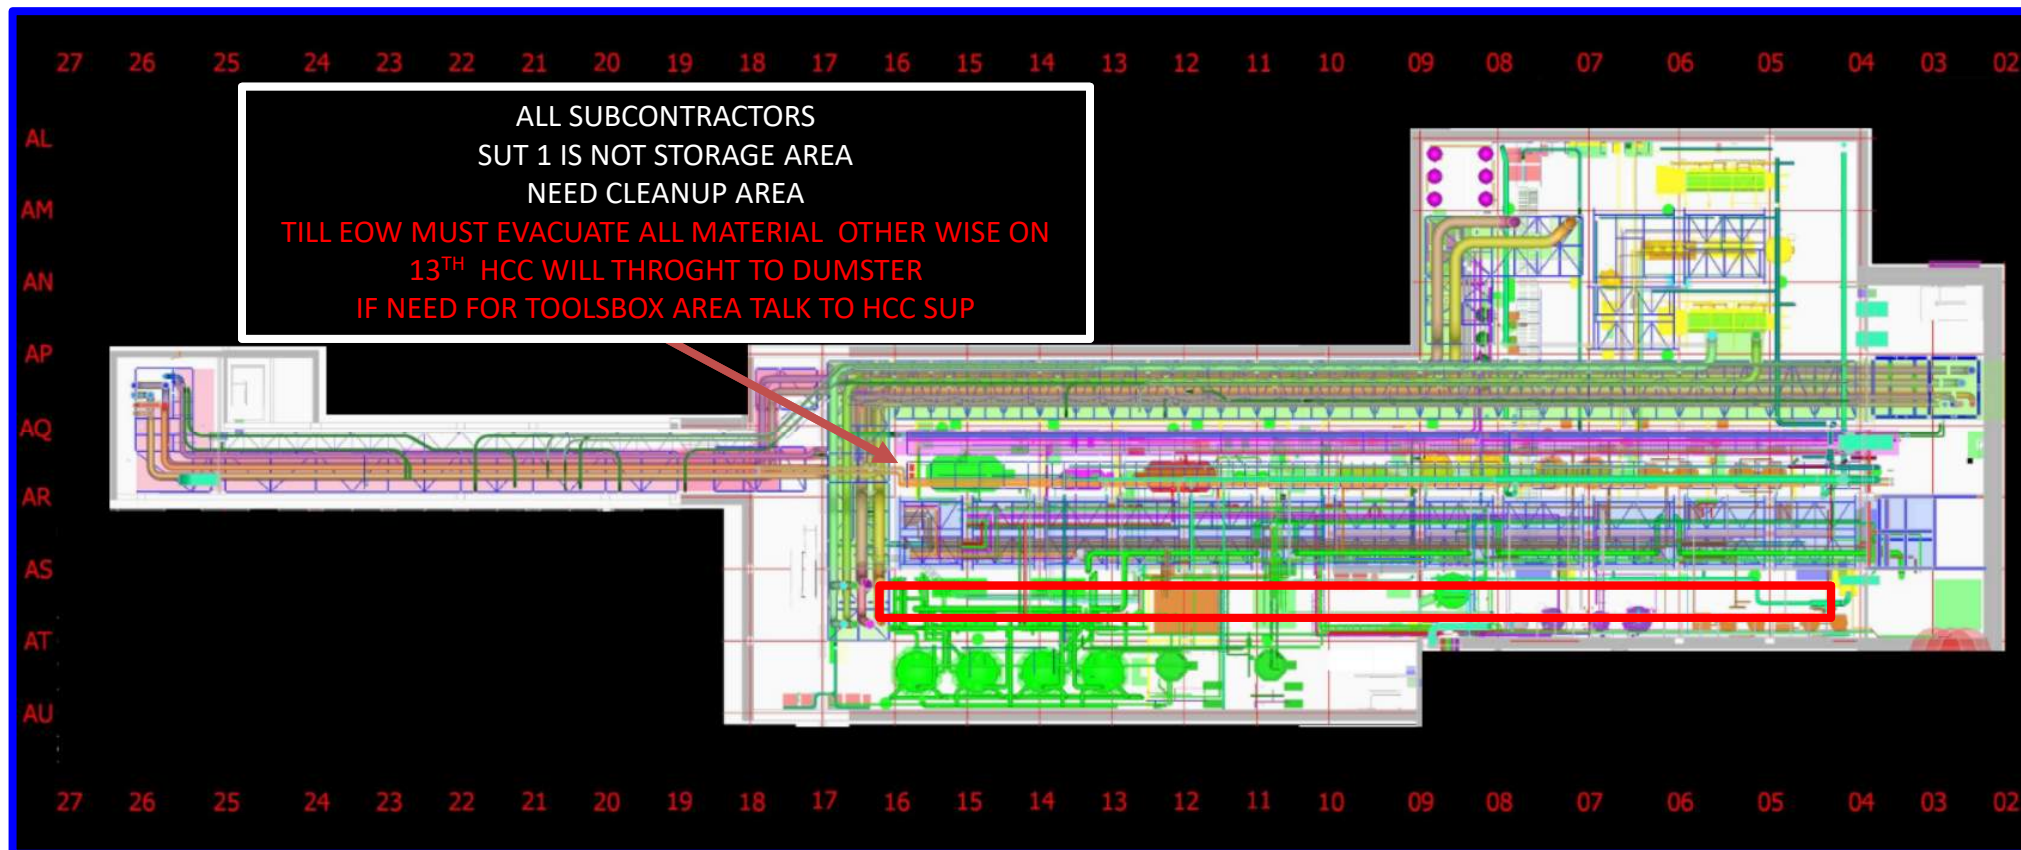






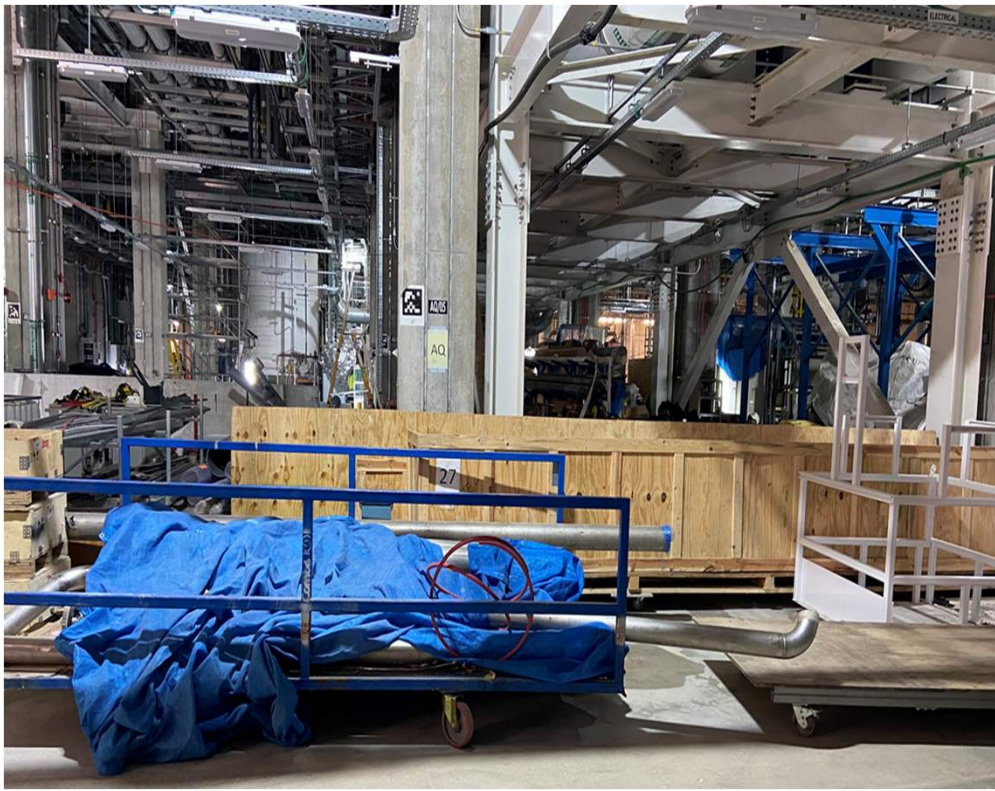

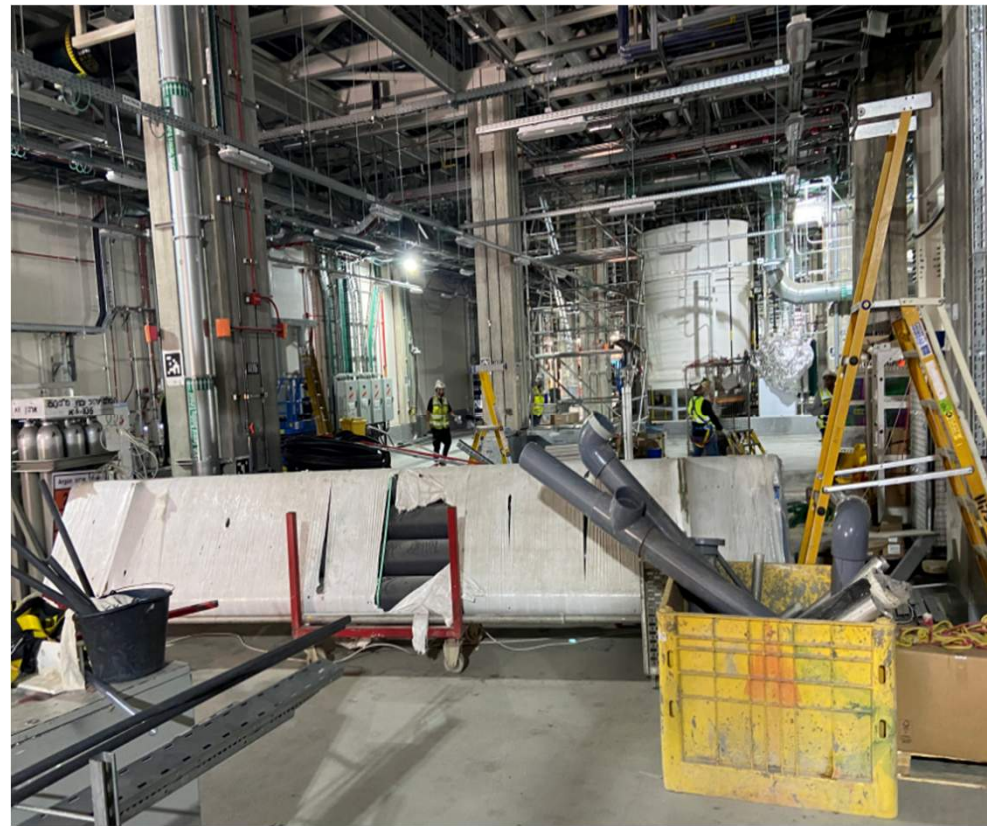

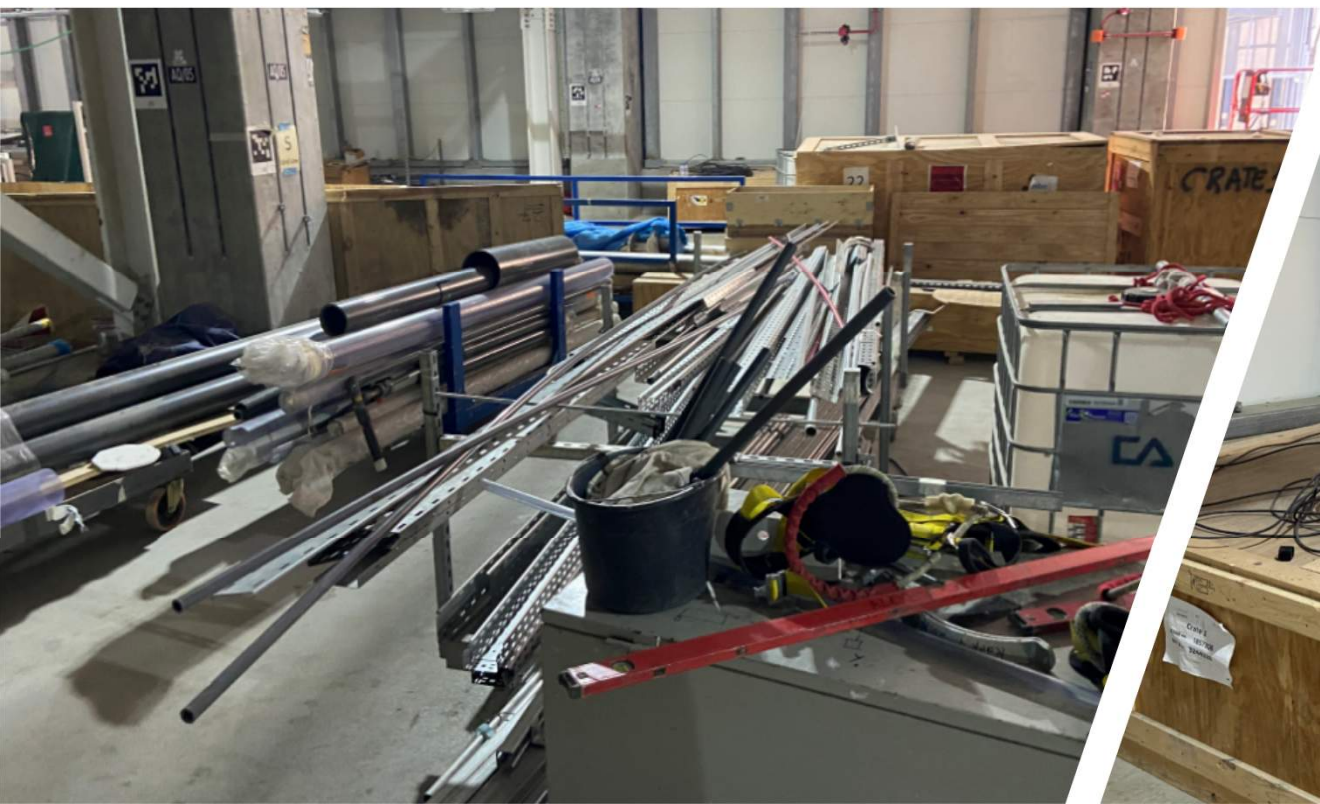


SUT 1 IS NOT STORAGE AREA

**NEED CLEANUP& EVACUATE ALL MATERIALS &
TOOLBOXES**


**TILL EOW 10TH MUST EVACUATE ALL MATERIALS,
OTHER WISE ON 13TH HCC WILL THROGHT
UNAPPROVED STUFF TO DUMSTER!!**

**EVERY TOOLBOX OR MATERIALS MUST BE
APPROVED - TALK TO HCC SUP- IBRAHIM**

SUBFAB BUILDOUT MOD 1

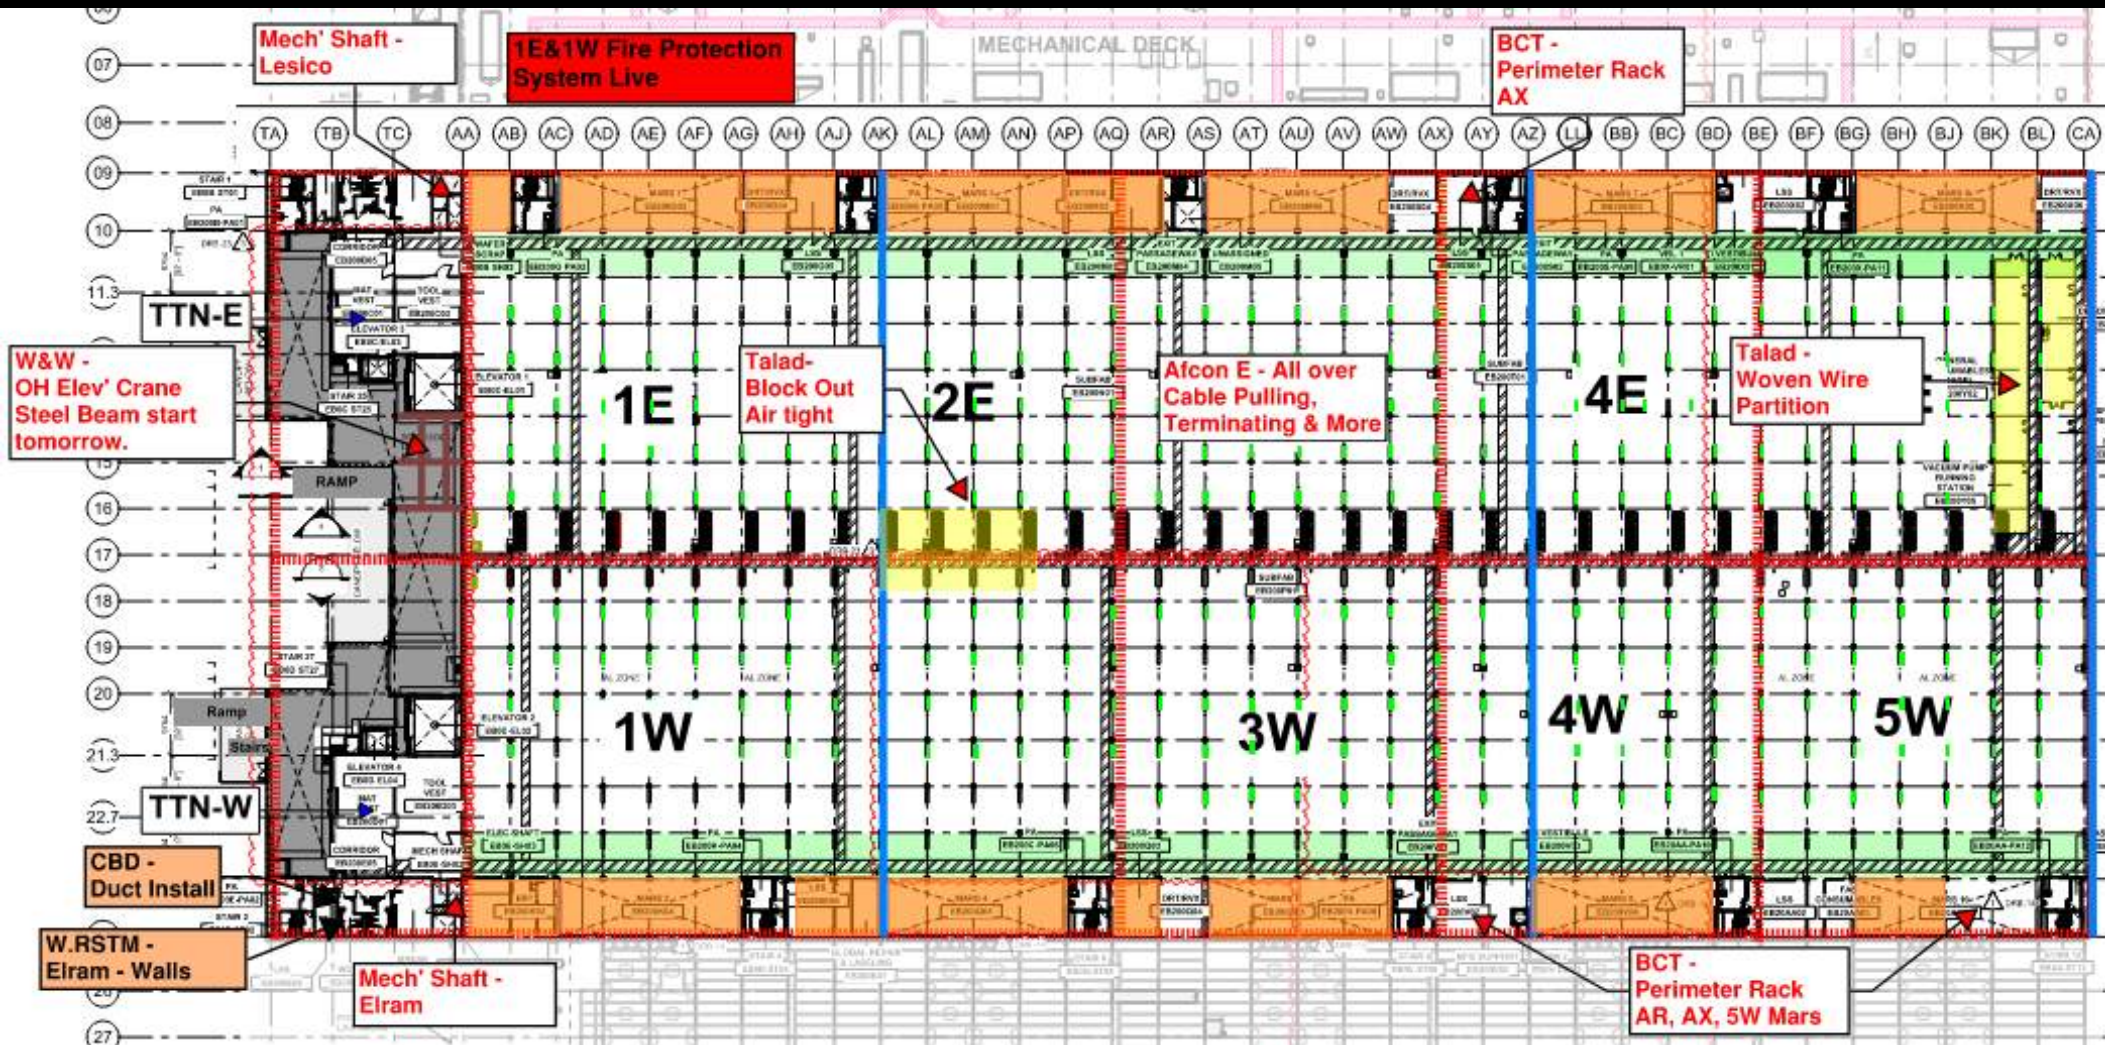


W&W Elev' Crane Beams Apr9-10.


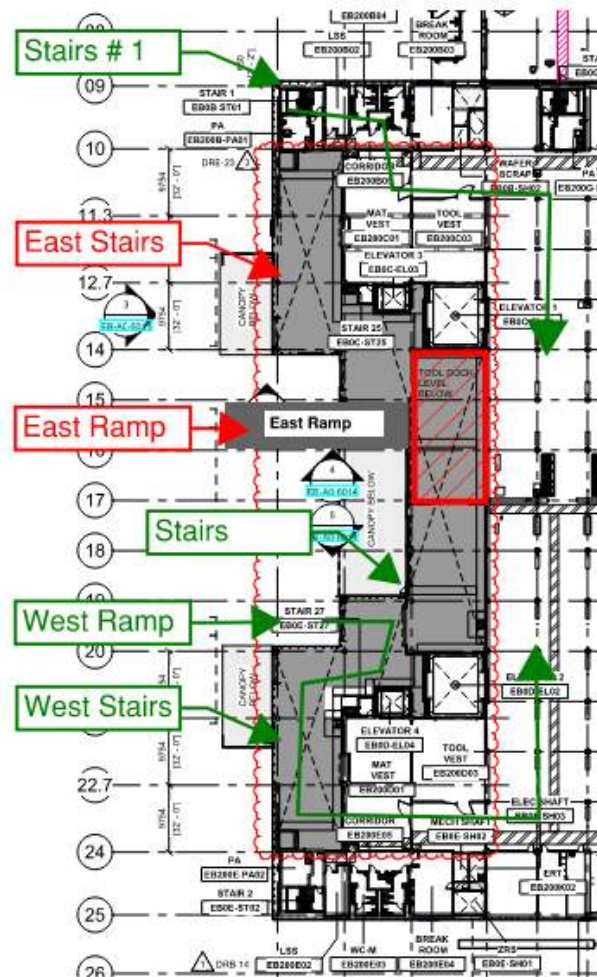


The floor plan shows a complex layout of rooms and corridors. Key features include:

- Vertical Zones:** 1E, 2E, 3E, 4E, 5E (top) and 1W, 2W, 3W, 4W, 5W (bottom).
- Horizontal Zones:** 1E, 2E, 3E, 4E, 5E (left) and 1W, 2W, 3W, 4W, 5W (right).
- Construction Progress:**
 - Apr 20 MARS 4E
 - Jun 8 MARS 5E
 - Apr 6 MARS 3W
 - May 11 MARS 4W
 - Jun 15 MARS 5W
- Blocked Areas:**
 - 3W LSS Room Blocked
 - Stairs #8 Blocked all week SF only
- Other Labels:** TTN-E, TTN-Dock Level, TTN-W, SHORING INSTALLED, VACUUM PUMP RUNNING STATION, CR DECK BUILD, TA, TB, TC, AA, AB, AC, AD, AE, AF, AG, AH, AJ, AK, AL, AM, AN, AP, AQ, AR, AS, AT, AU, AV, AW, AX, AY, AZ, LL, BB, BC, BD, BE, BF, BG, BH, BJ, BK, BL, CA.

Lesico Pressure Test Tomorrow

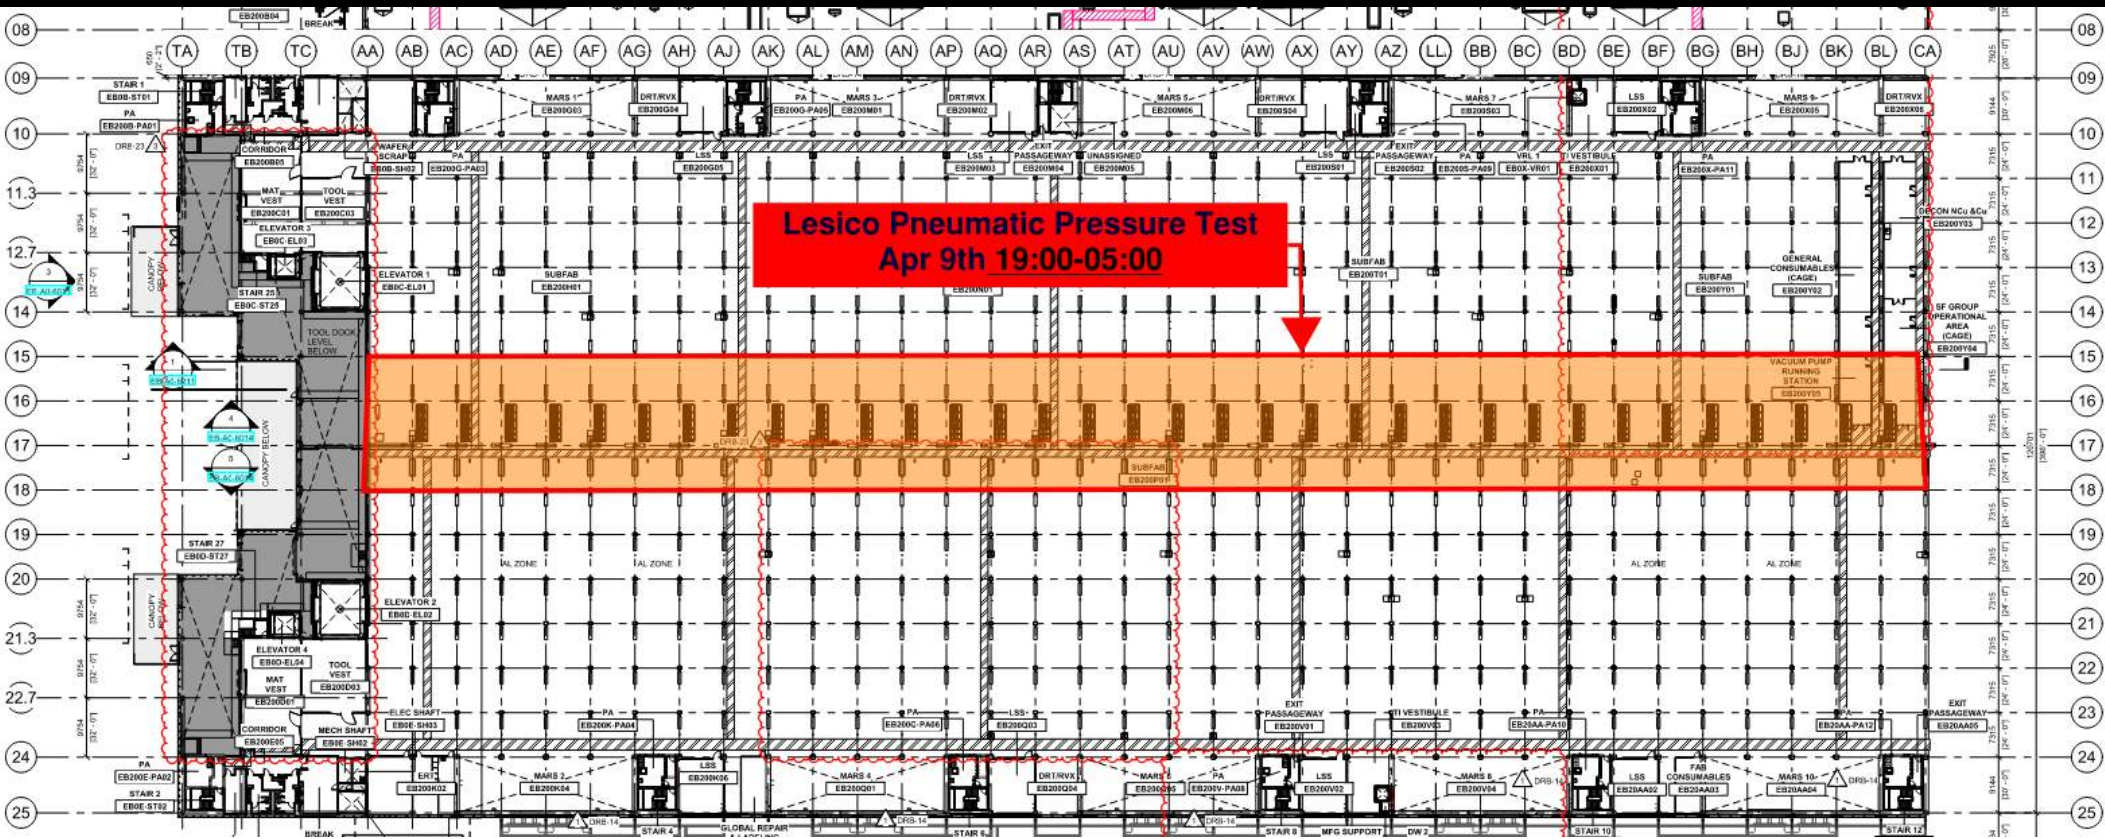

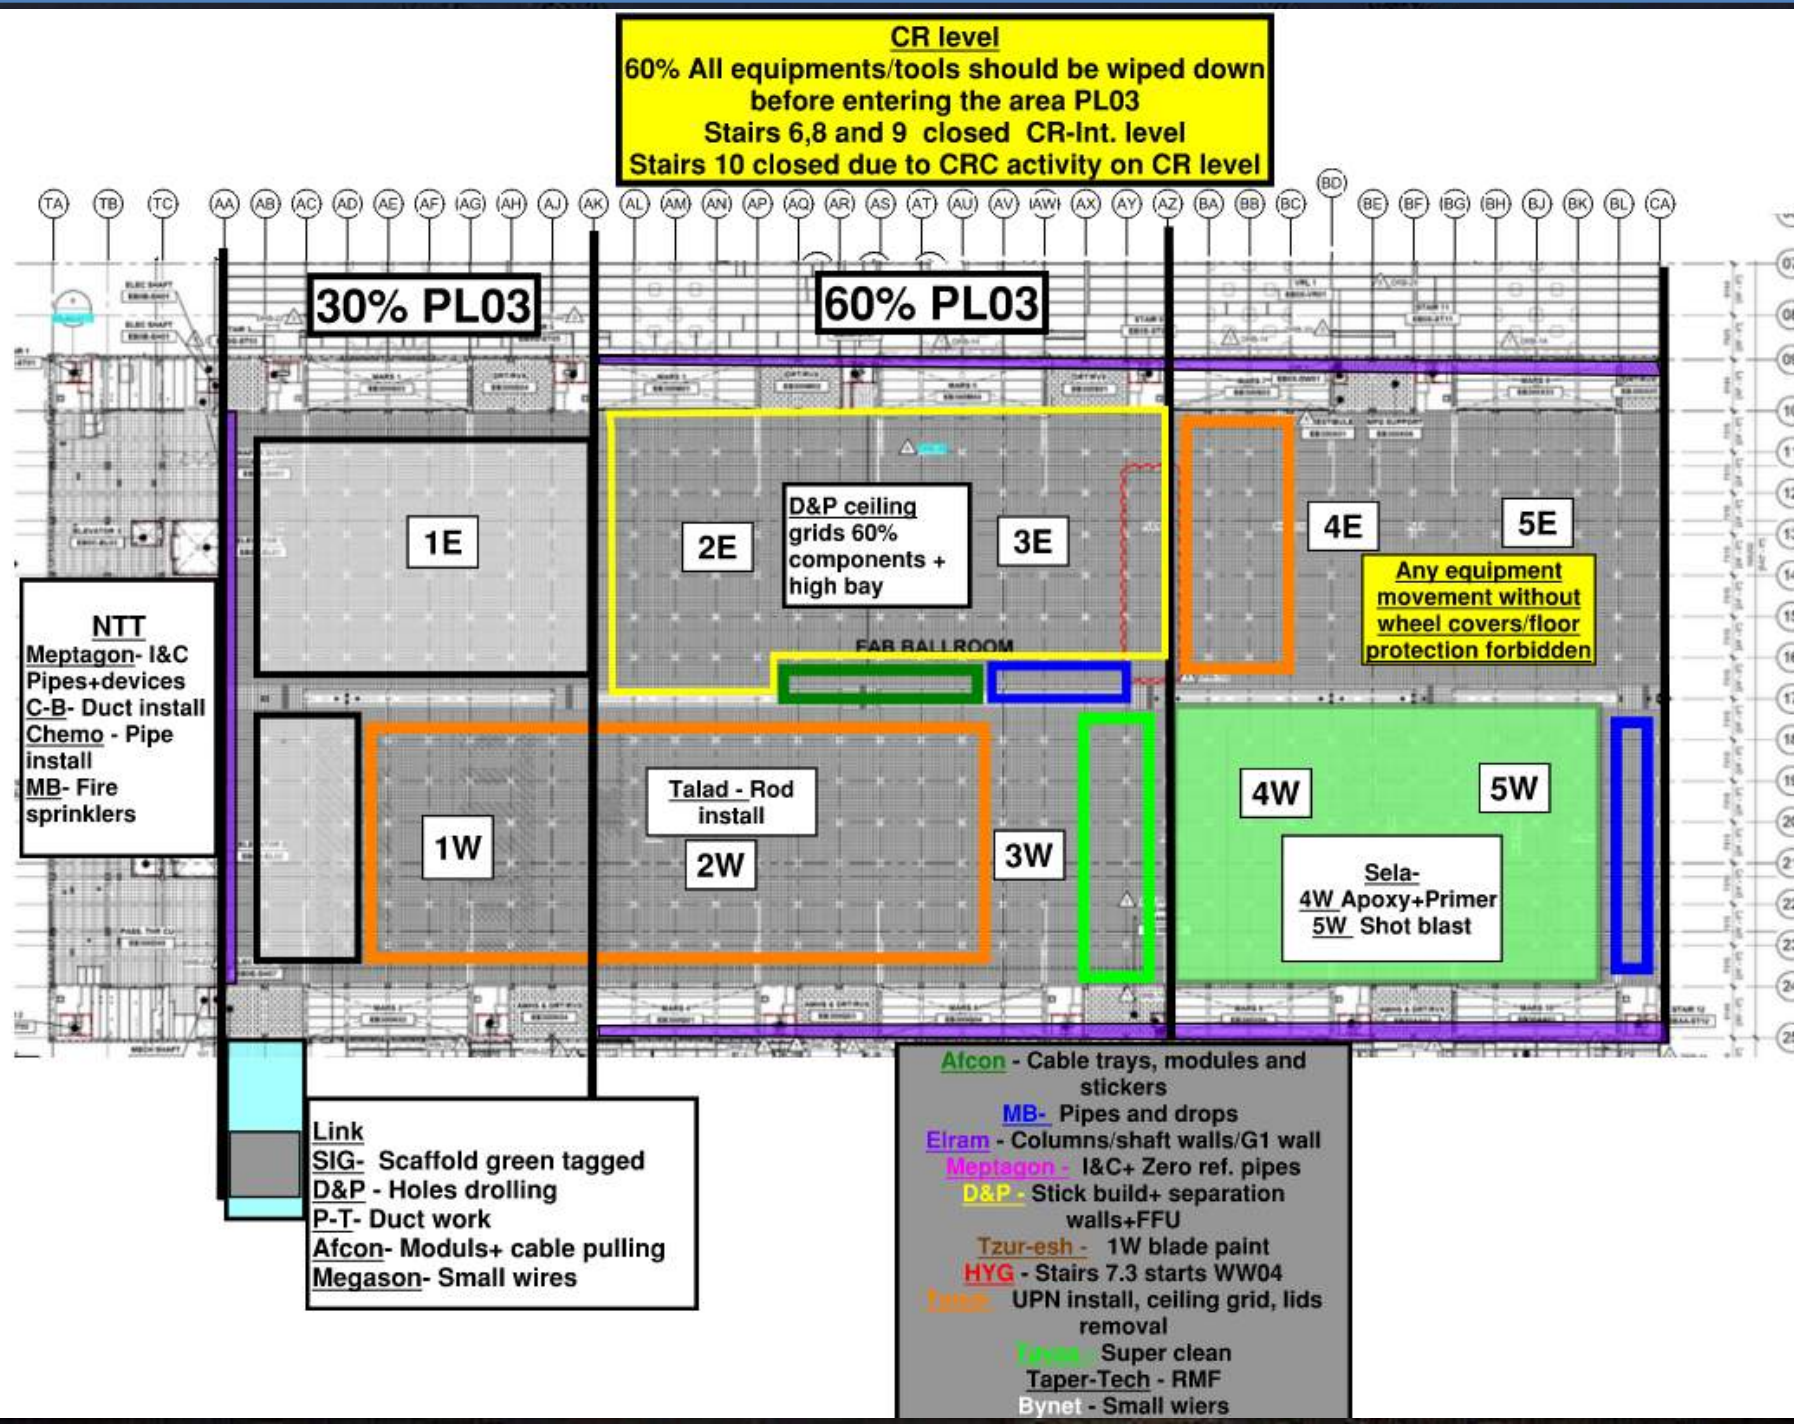




Meptagon- I&C


Do not move carts/ stage material without plywood




30%

60%

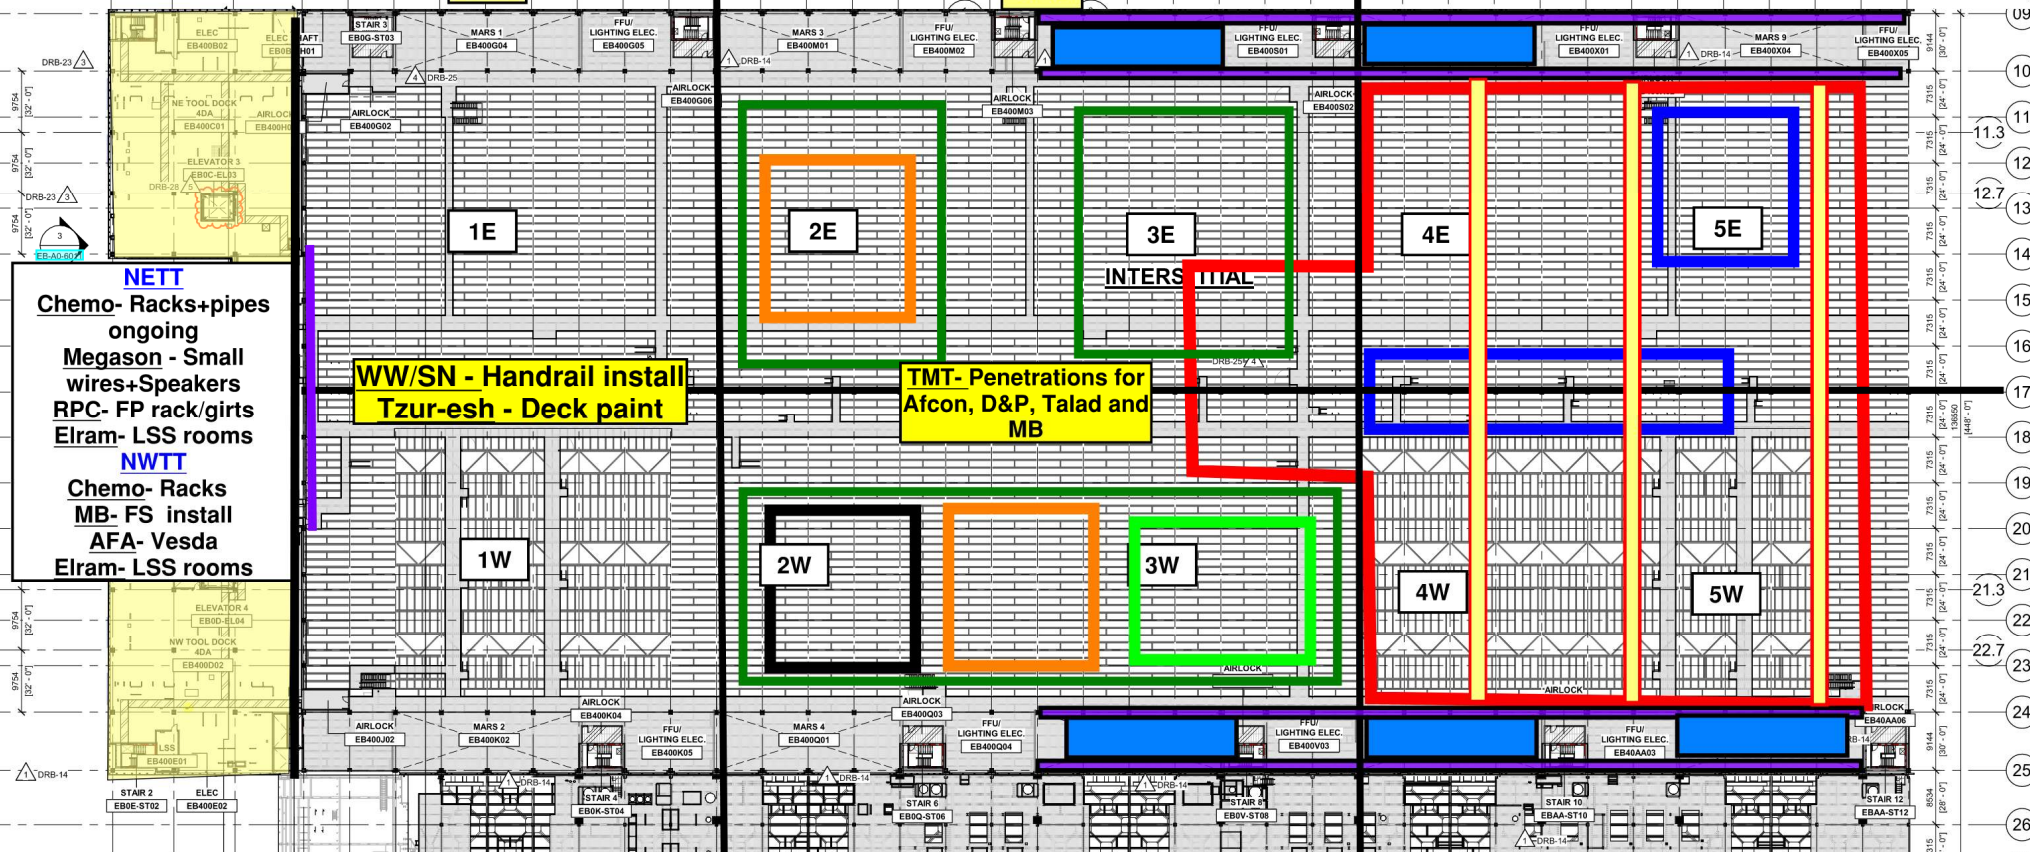

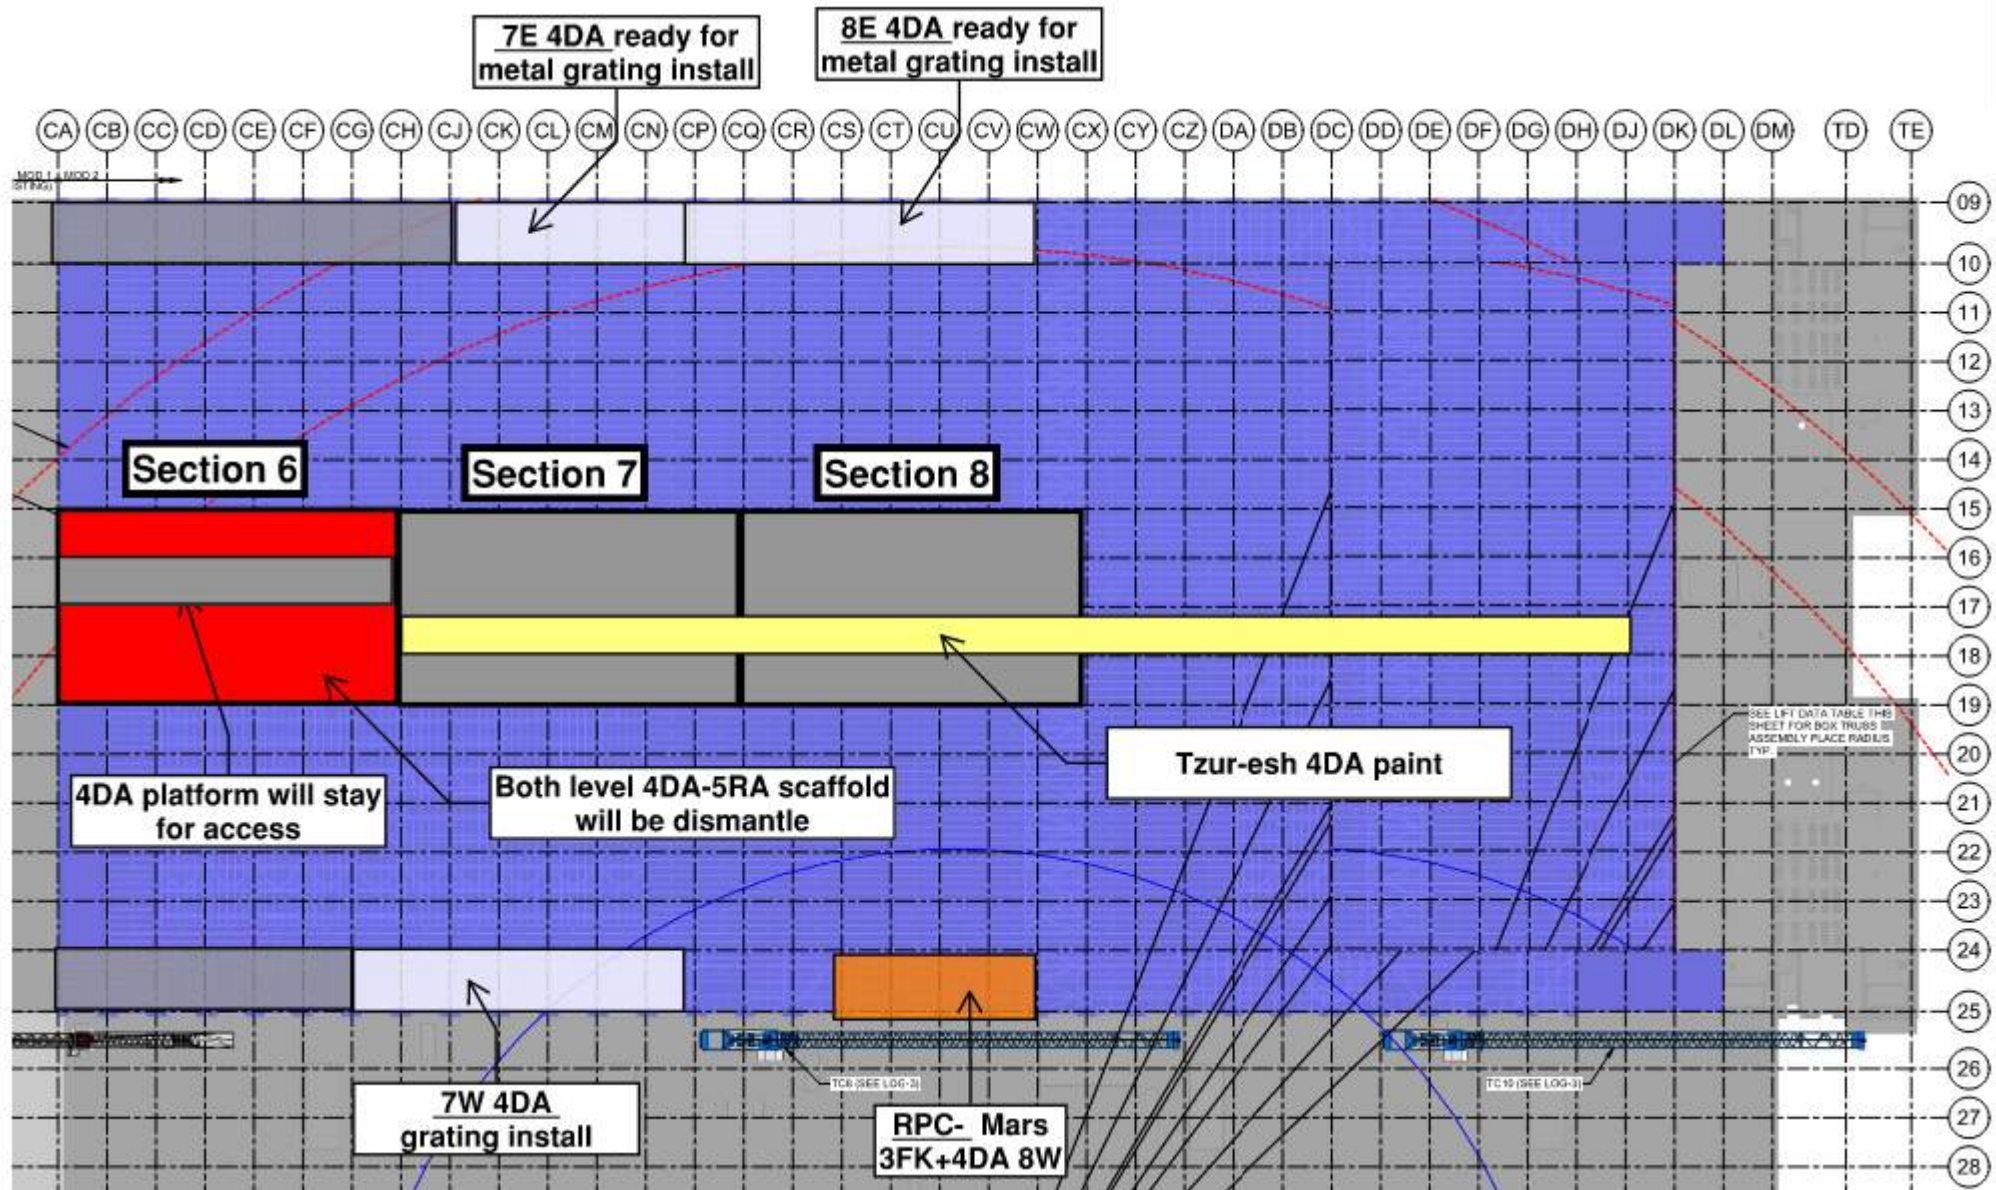



HOFFMAN CONSTRUCTION COMPANY



Afcon



Wall of Shame

D&P

60%



Afcon




D&P



Elram



Afcon




HOFFMAN CONSTRUCTION COMPANY




Wall of fame

Tapper tech



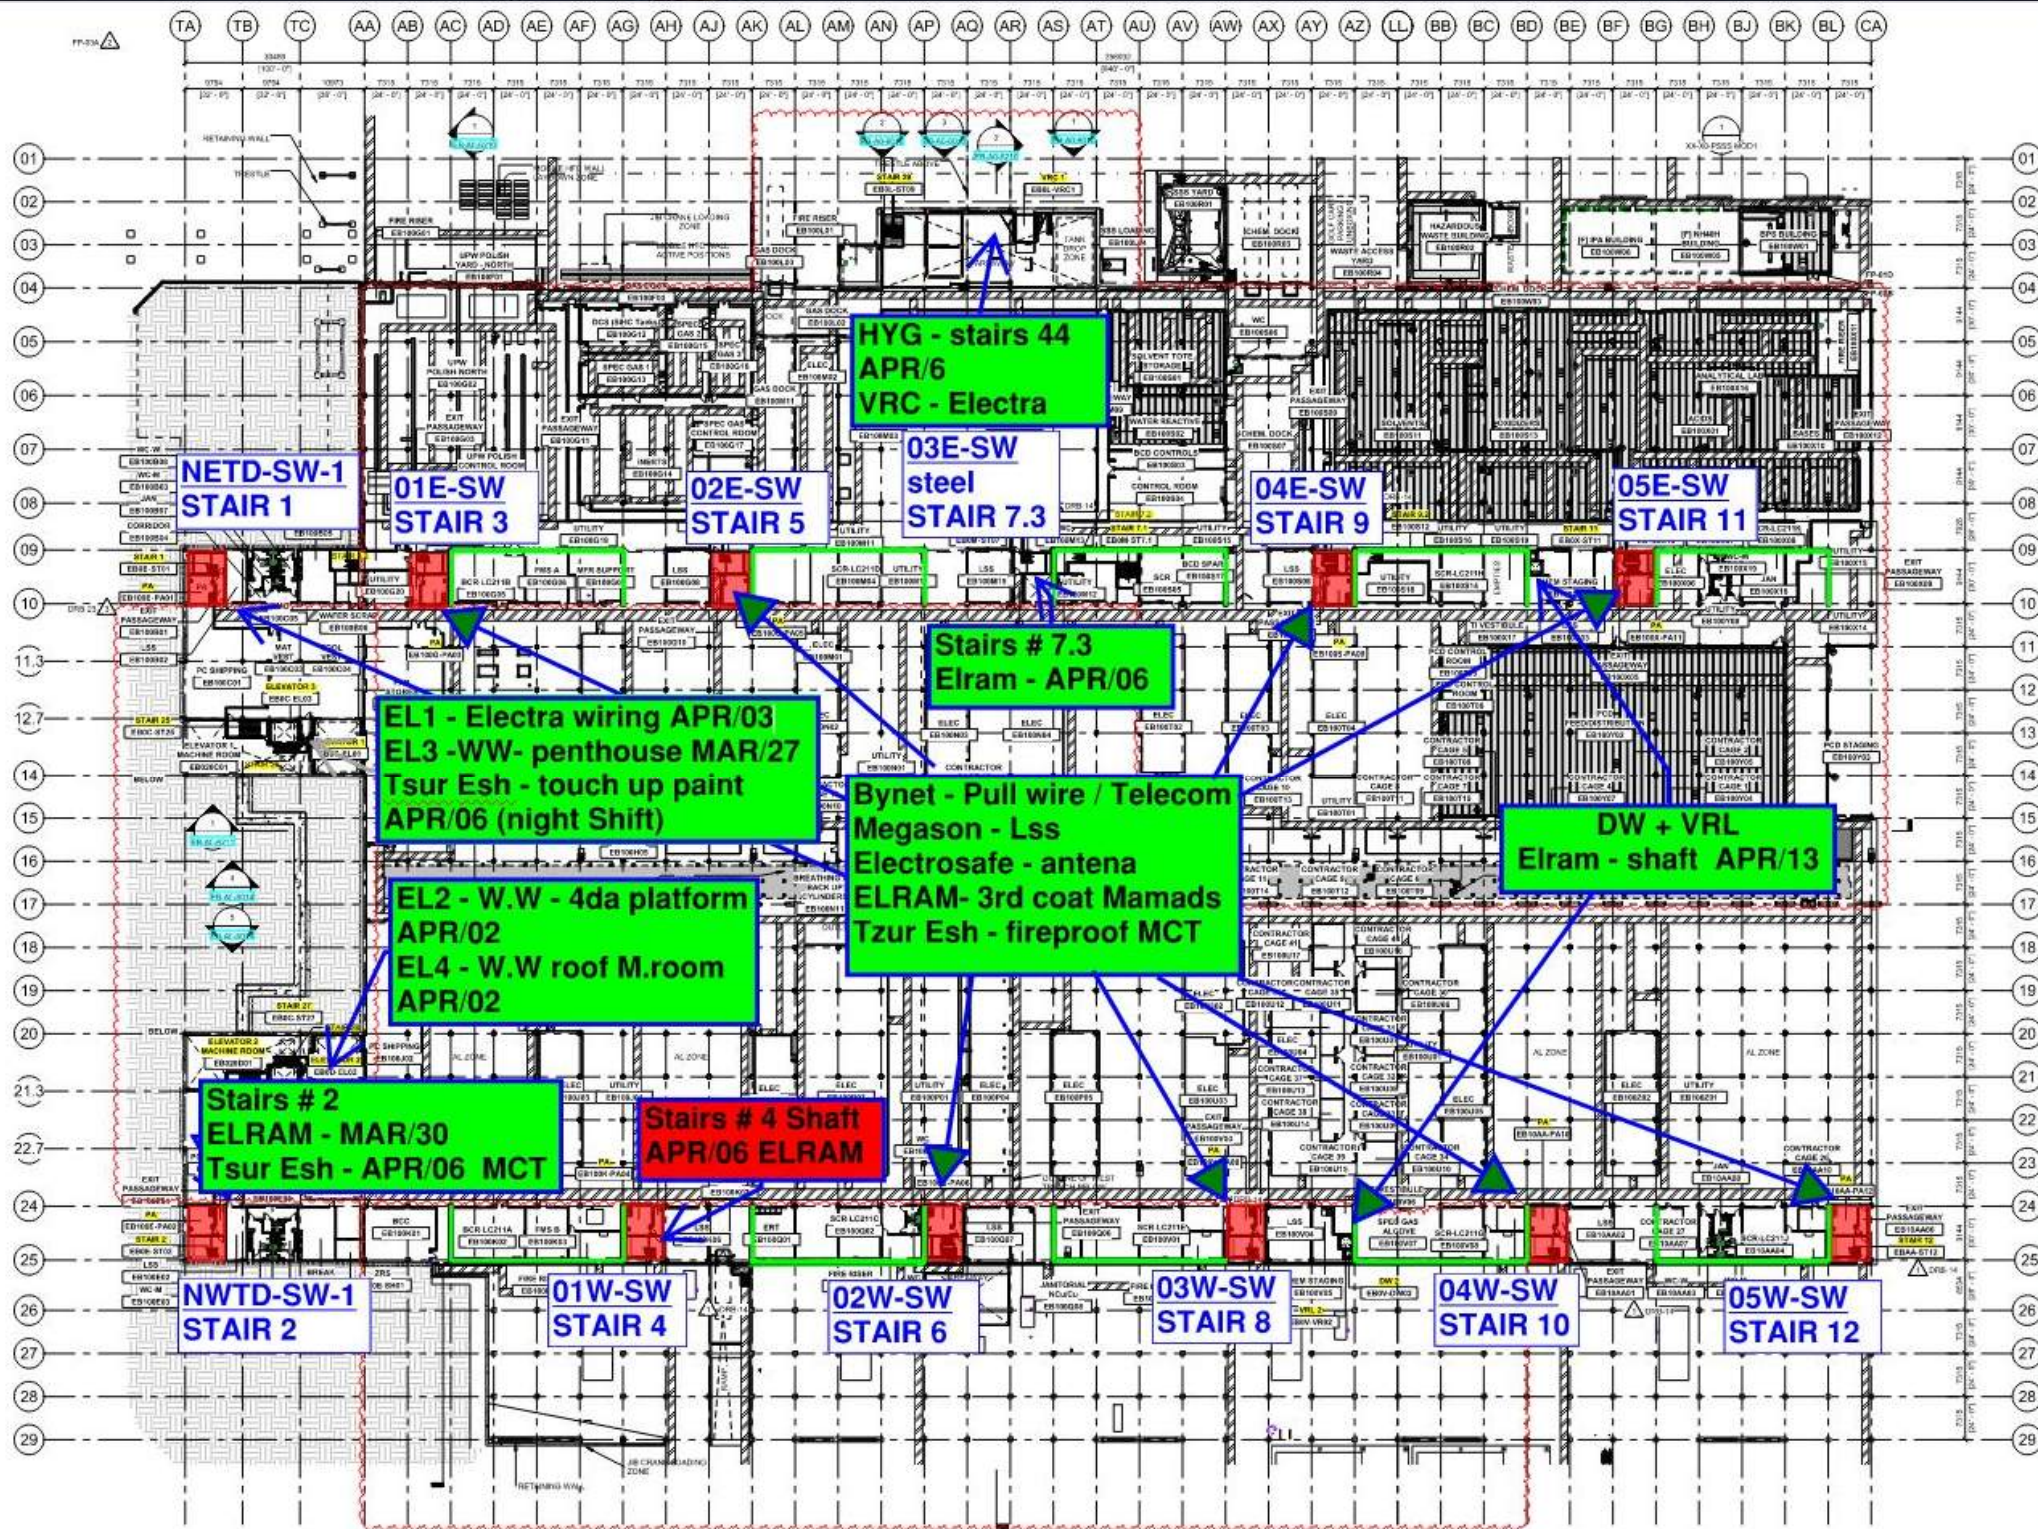

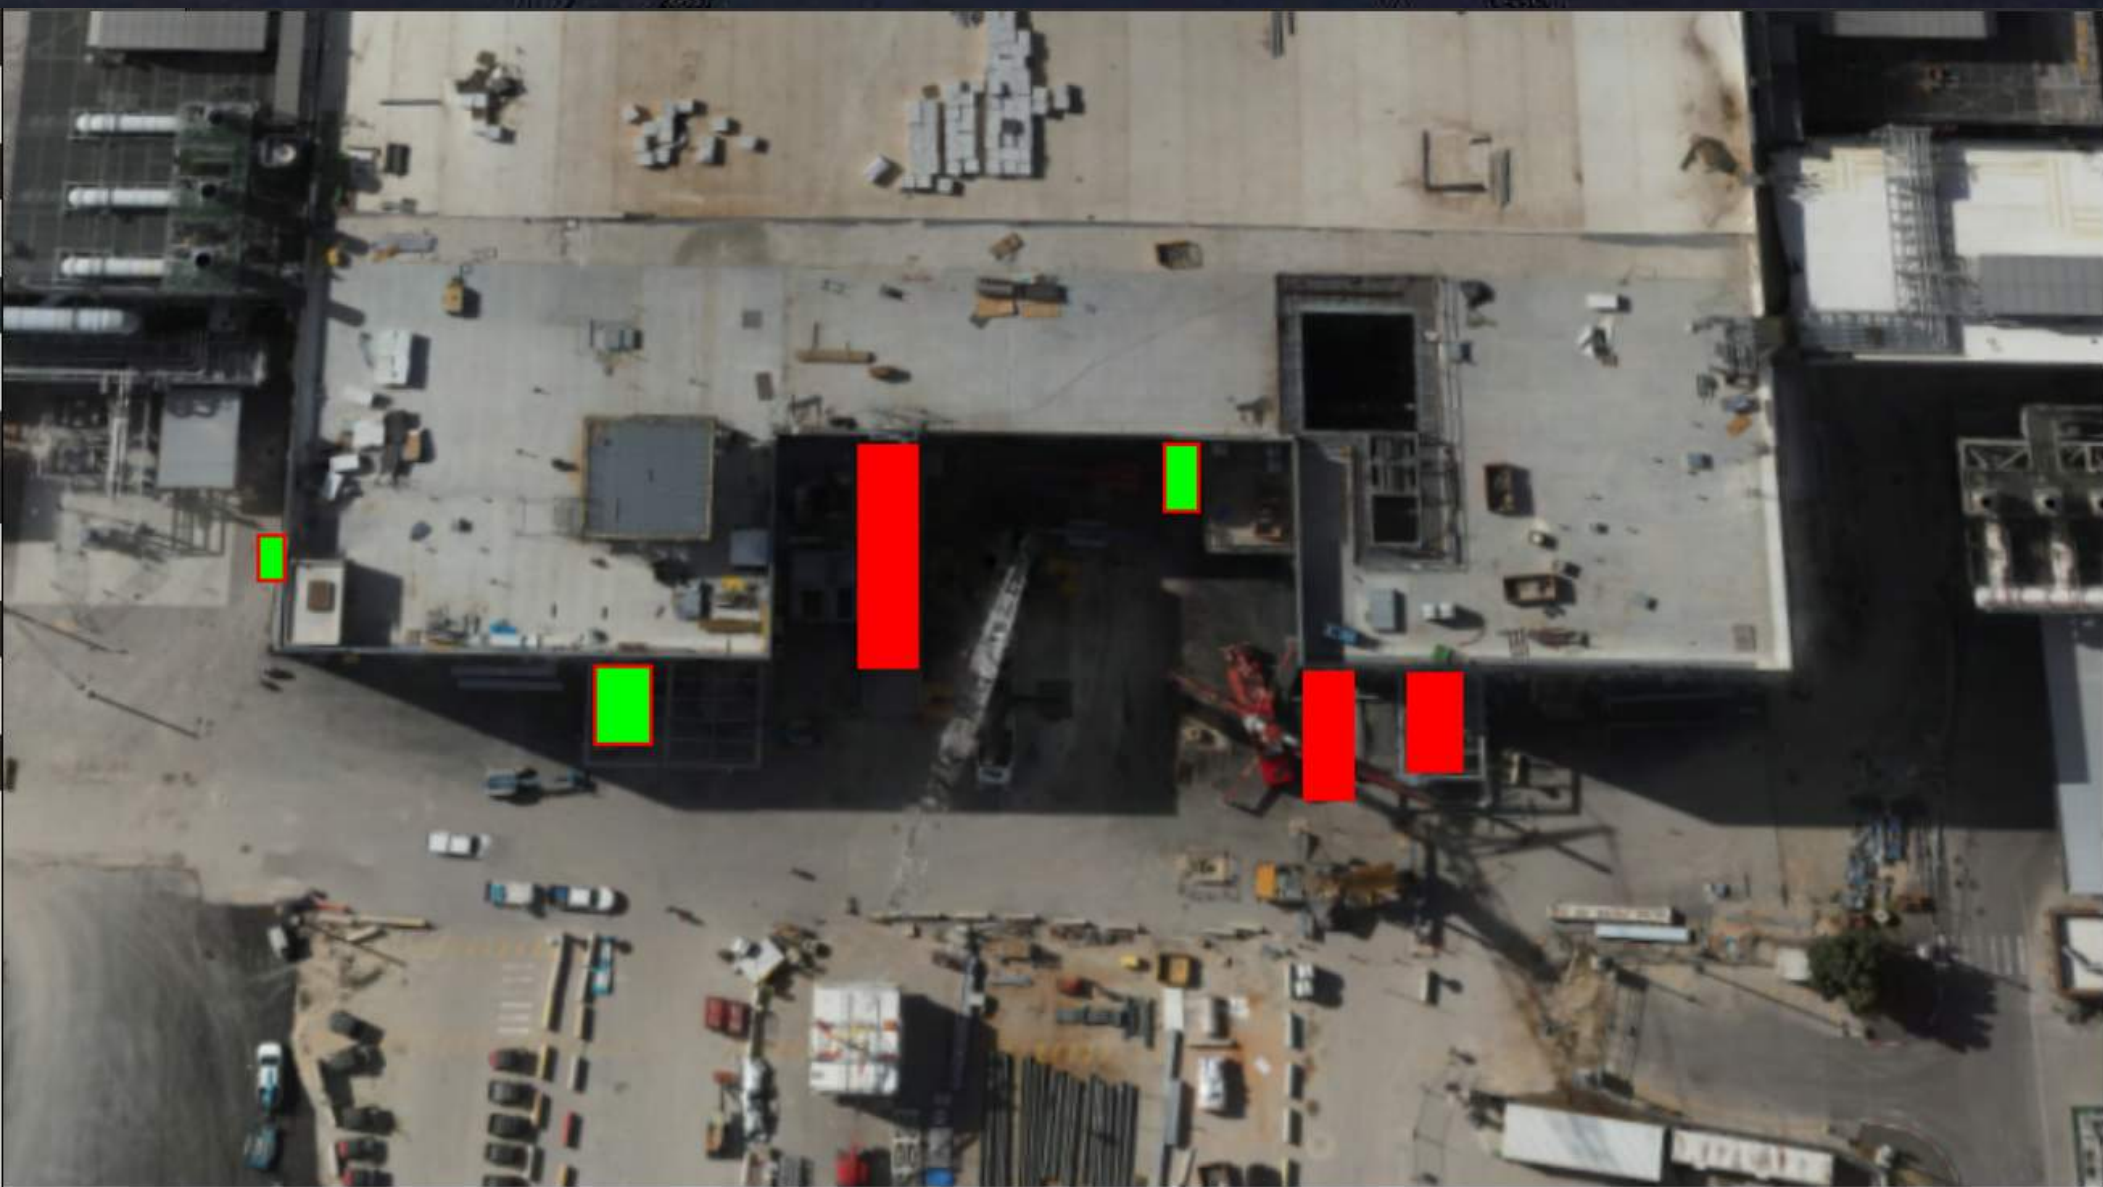



READY FOR GIRTS 

INSTALLING GIRTS 


READY FOR PANELS 

PANELS INSTALLED 

MOD 2 WESTSIDE GIRTS/SIDING




MOD 2 EASTSIDE GIRTS/SIDING

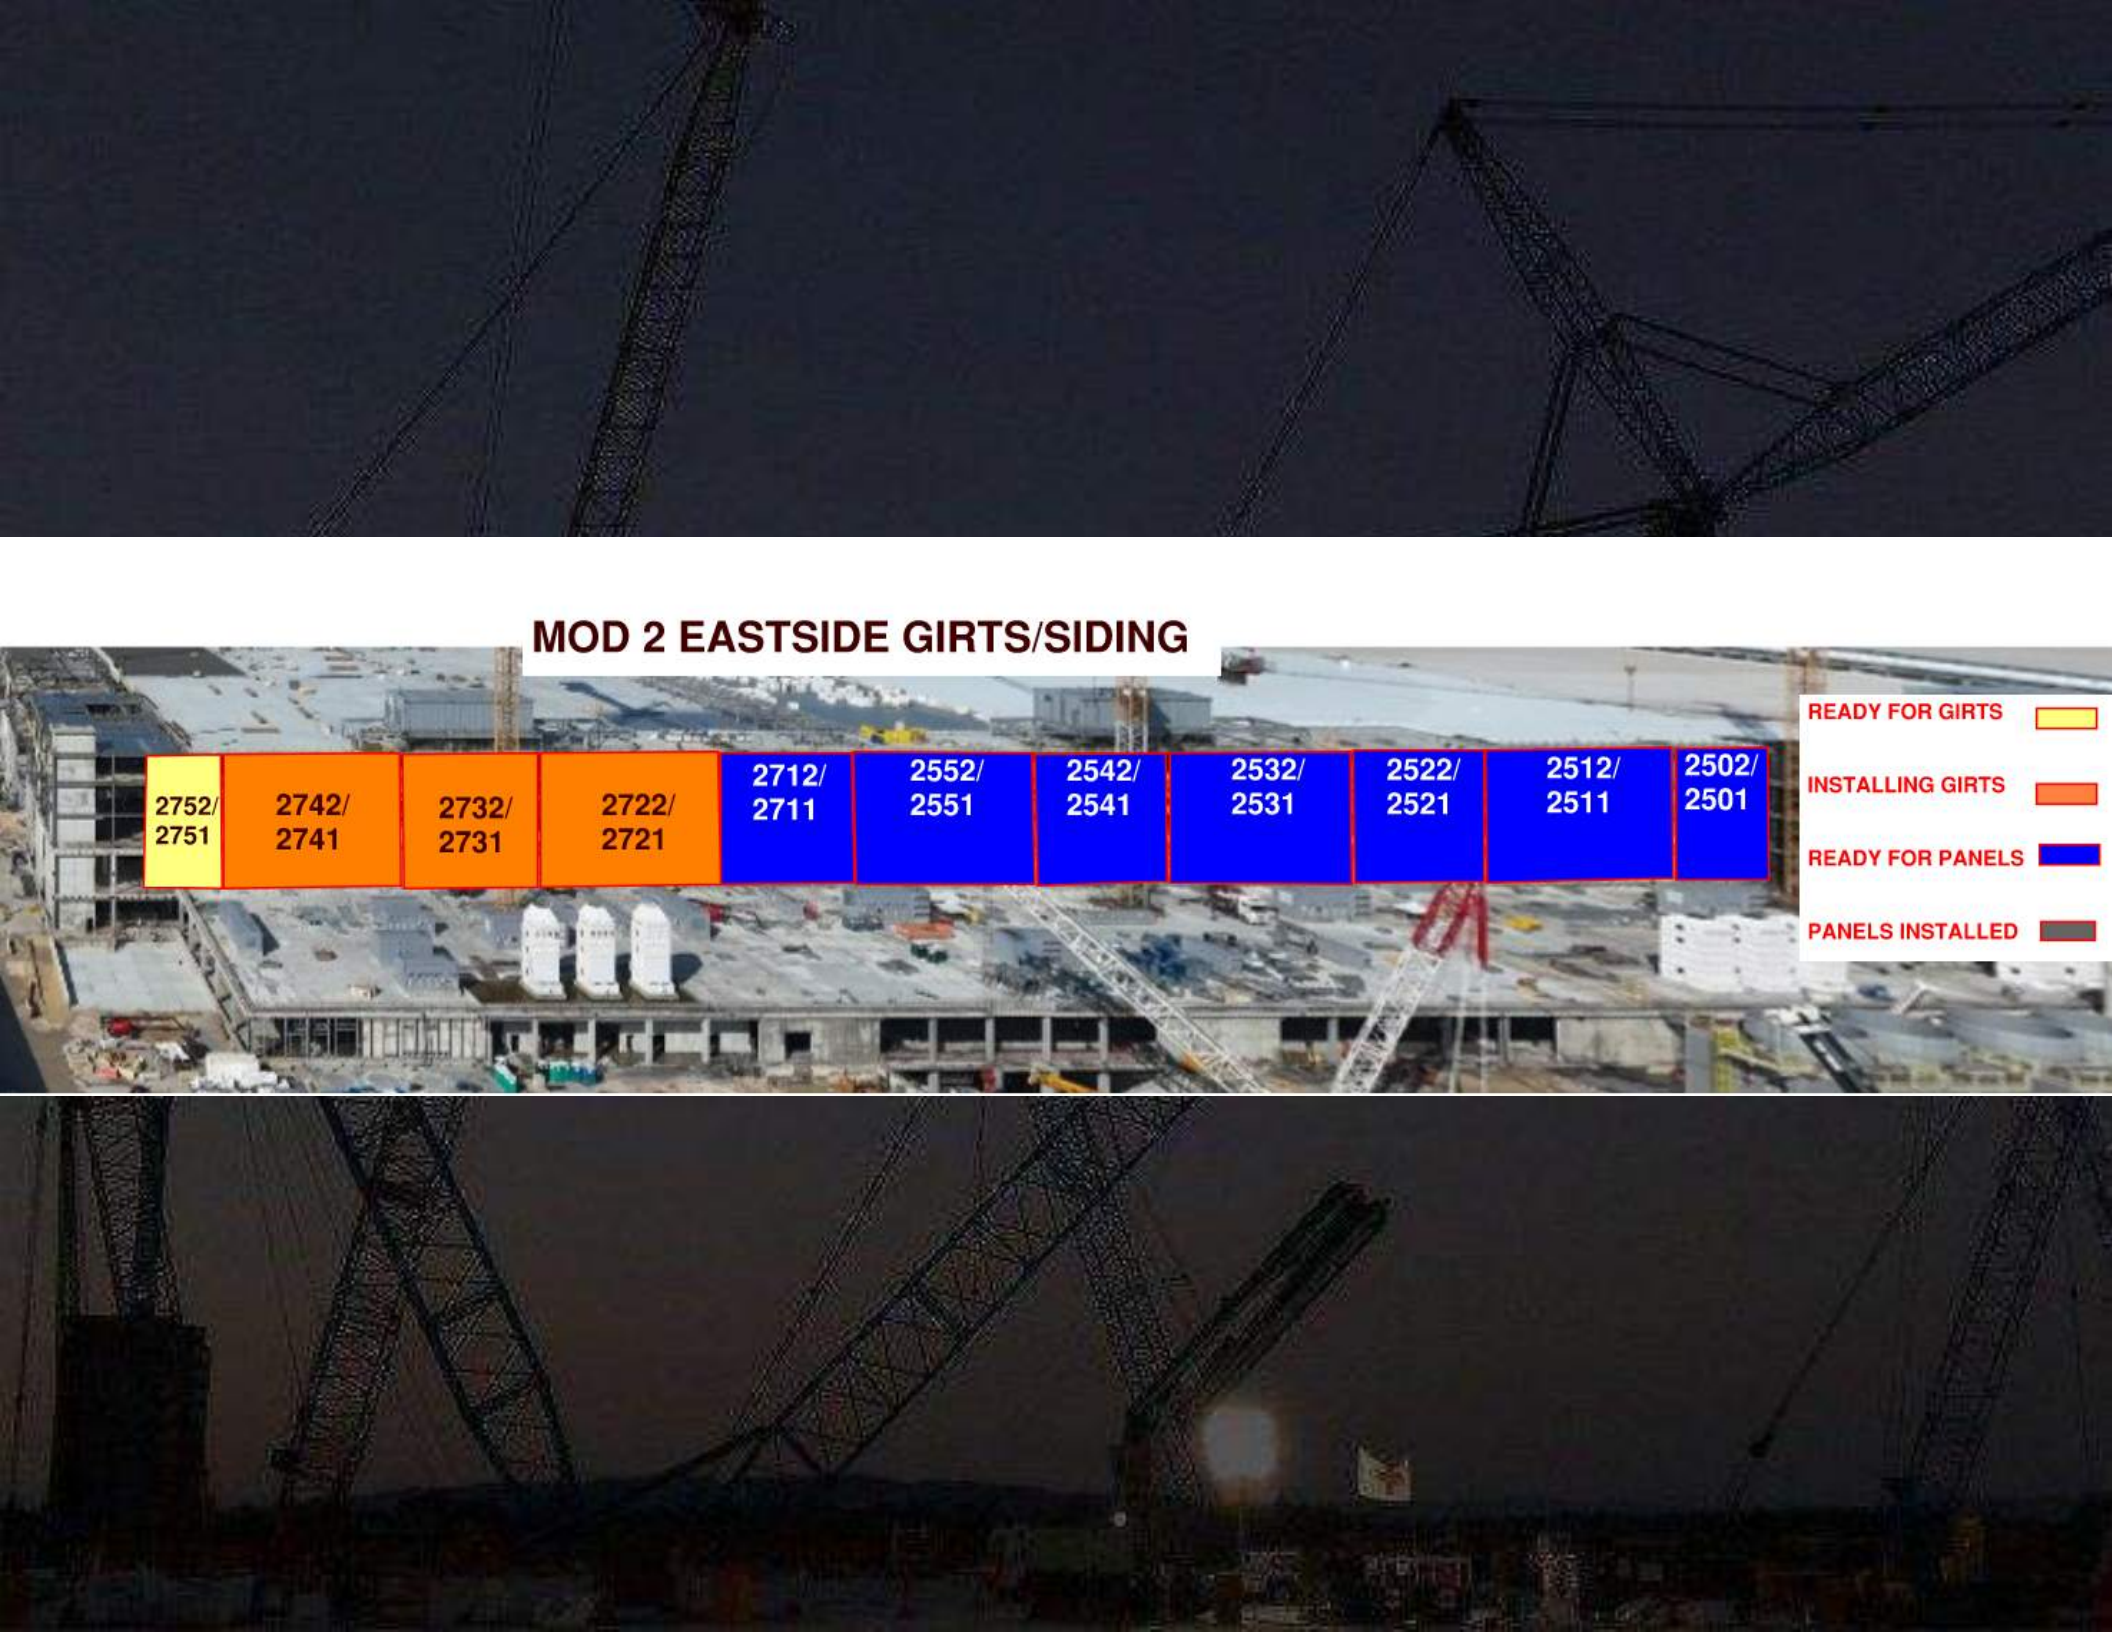

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------


READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

PSSS.1

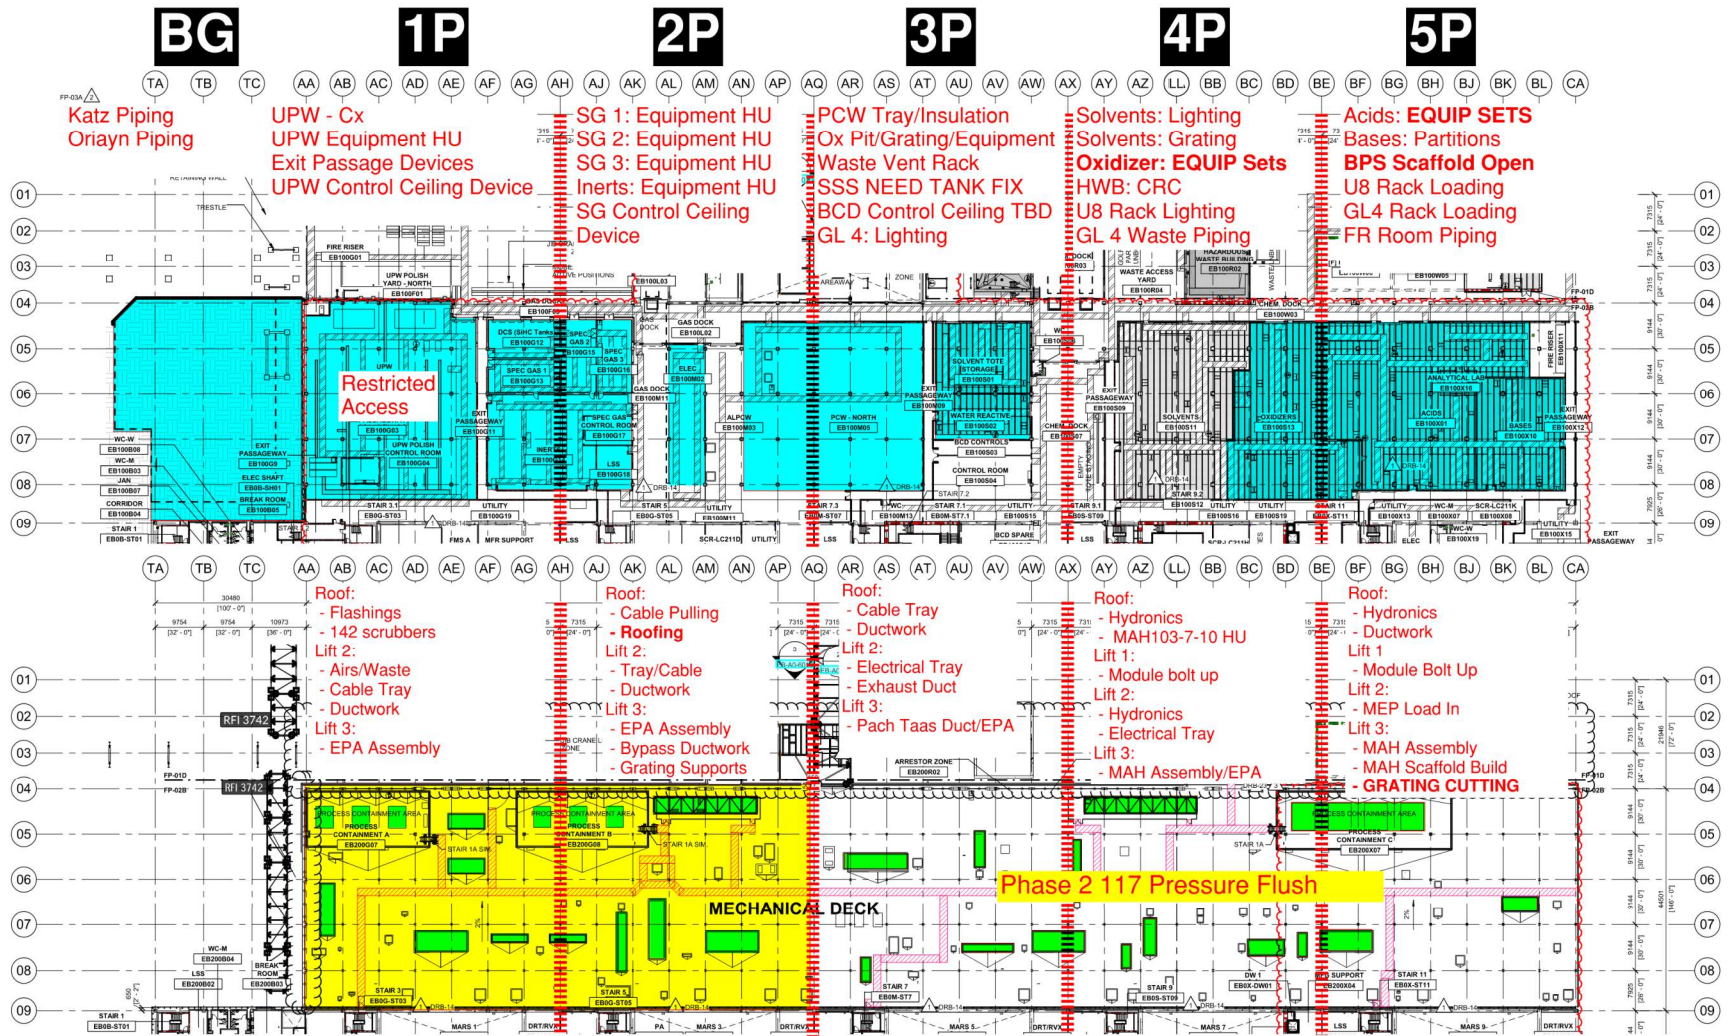


PSSS.2


Utility Level
1YA

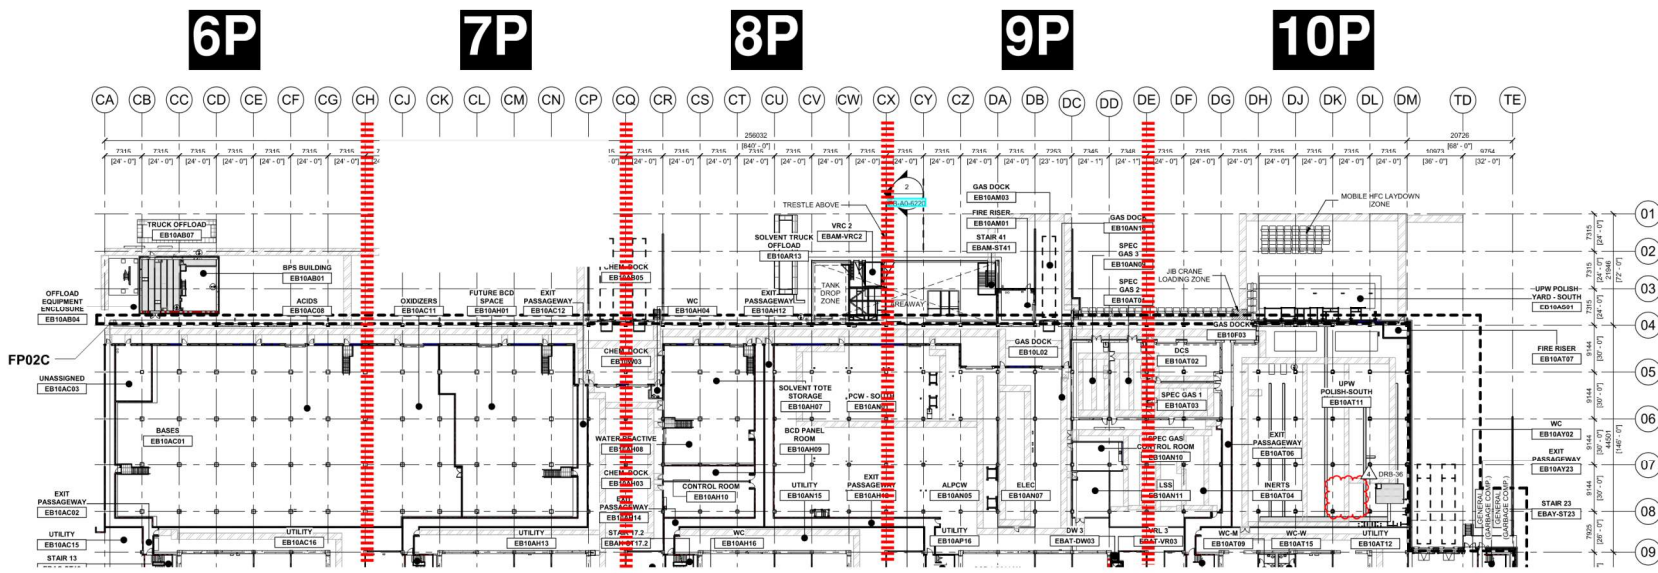

PSSS Roof
2SA

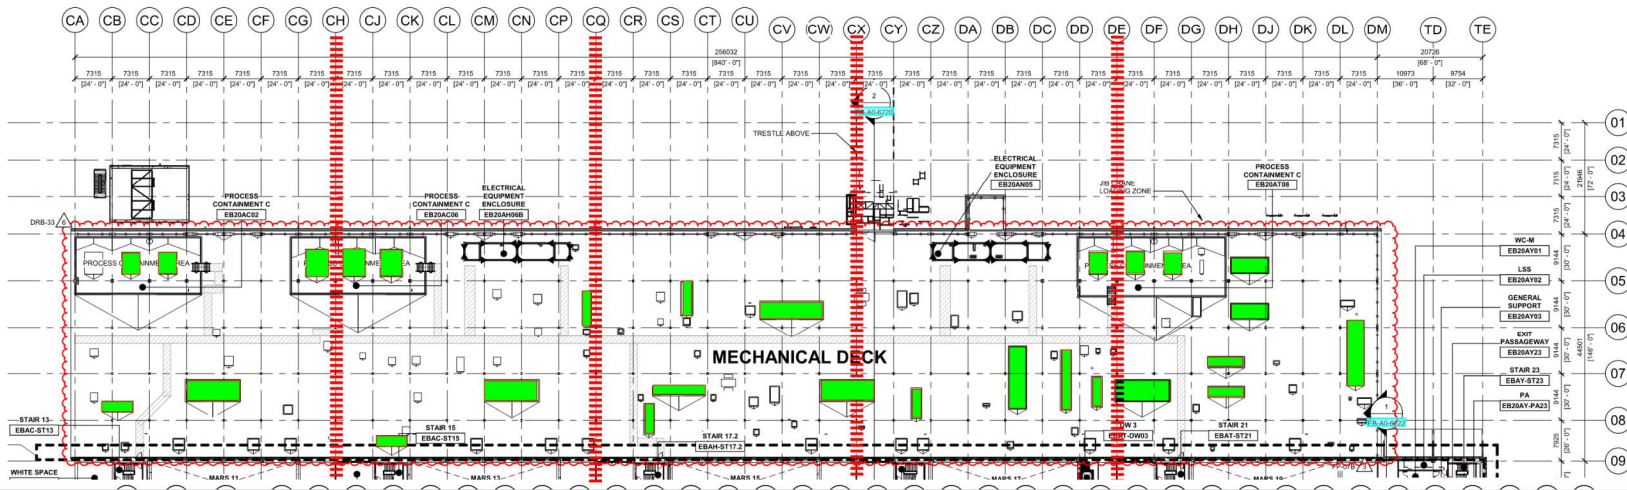

* Pach Taas - completion of spools and lindapters on UPN 138 * Pach Taas - working on connections of WP to modules	* Chemo - performing passivation on UPN 111 (UL + lift 2)	*Afcon - Installation of lighting and cable pulling	* ASD - erection of scaffold for VFD derains * W&W - welding connections on CA line for MOD2 steel * CB - working on small AH ducts.
---	---	---	--

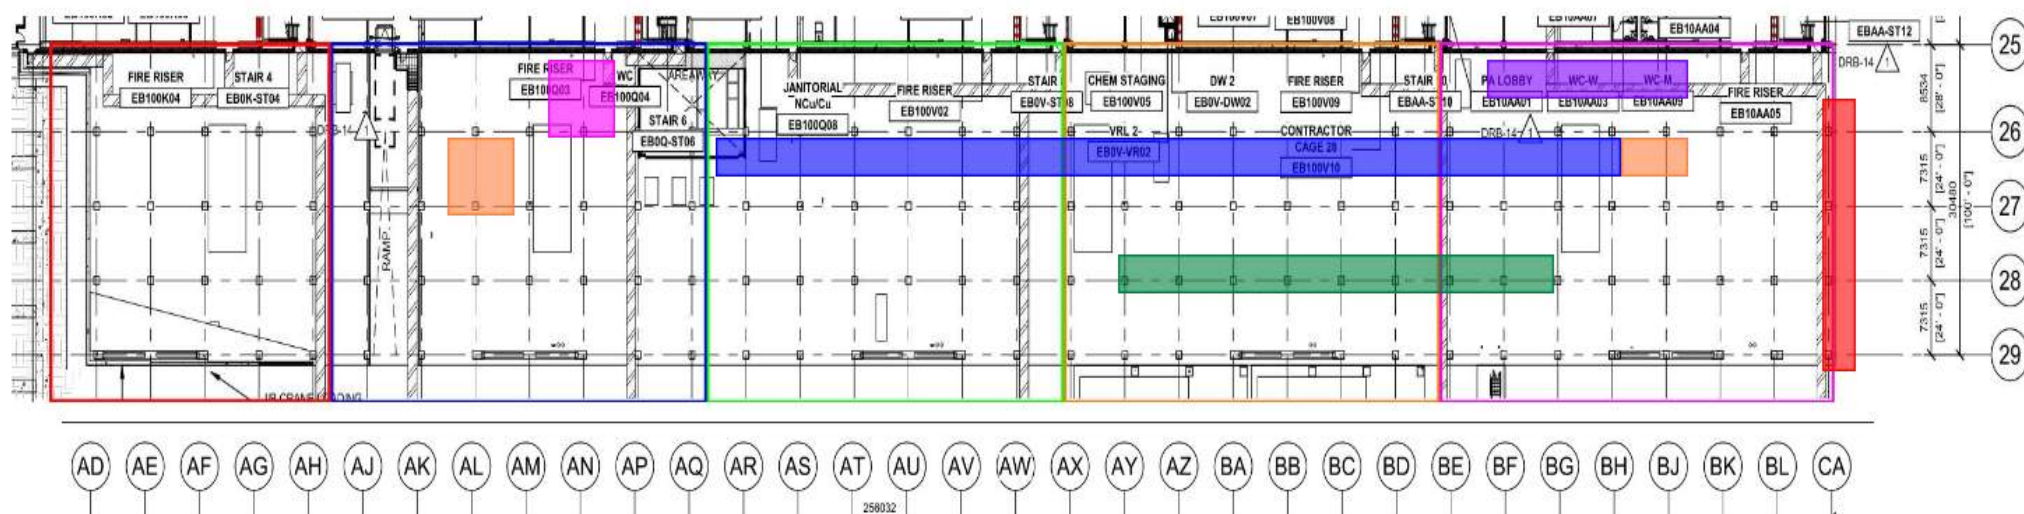


WJG – Lift 2

* Chemo - about to start restoration of UPN 113 once water test results are good
* Carmel Bidud - installing handrails to open planking for stiffeners

* Afcon - installation of trays to exhaust fans

* Chemo - continuing insulation
* SK - performing connections to MAH (later this week, scaffold will be turned to yellow tag)

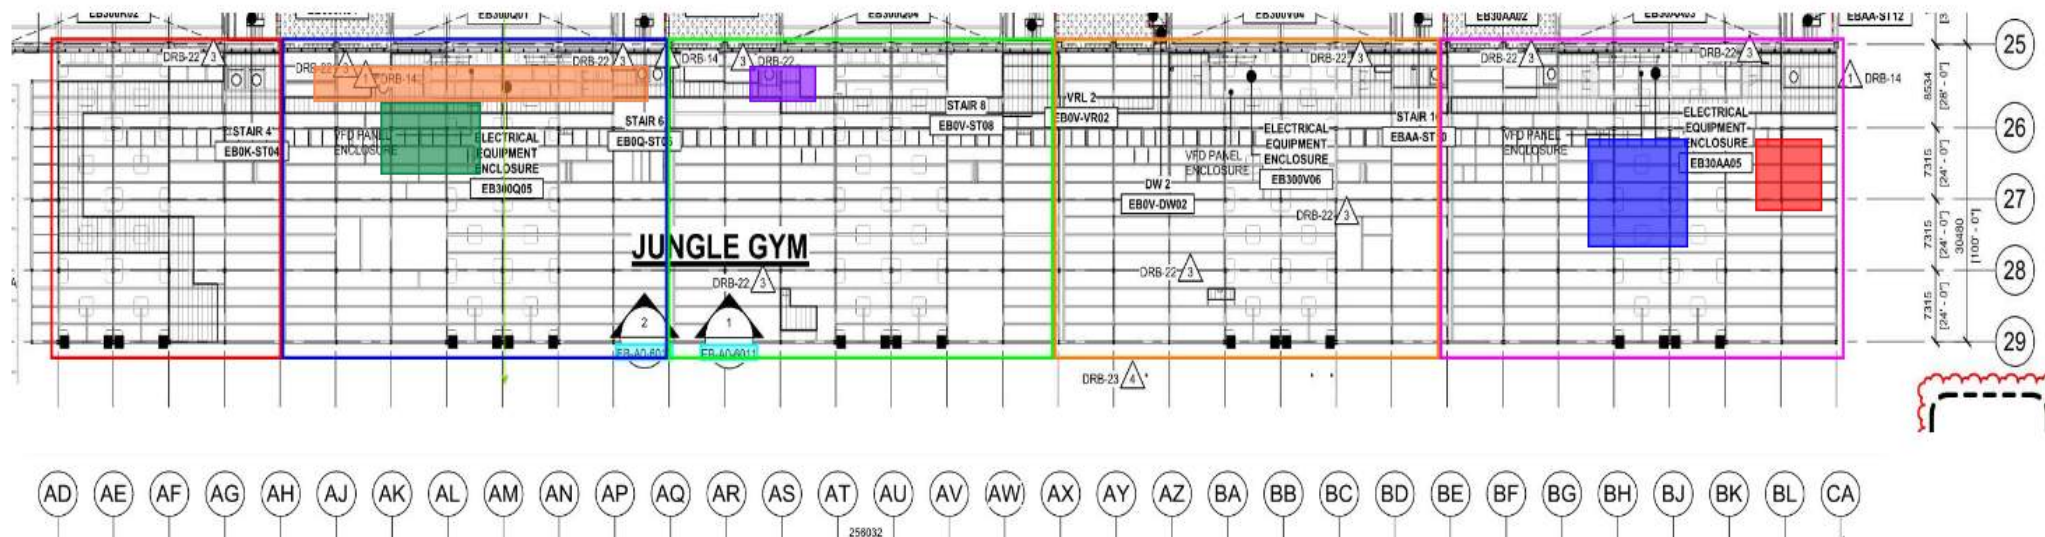

WJG – Lift 3

* Chemo - hoisting and installing 4J
MARS pipes

* SN - handrai installation and
penetrations




Crane logistics

Crane: 750 ton crane
moving south of RCTO
Tuesday 08/04/25






CUB 1 Ops Ready April 24

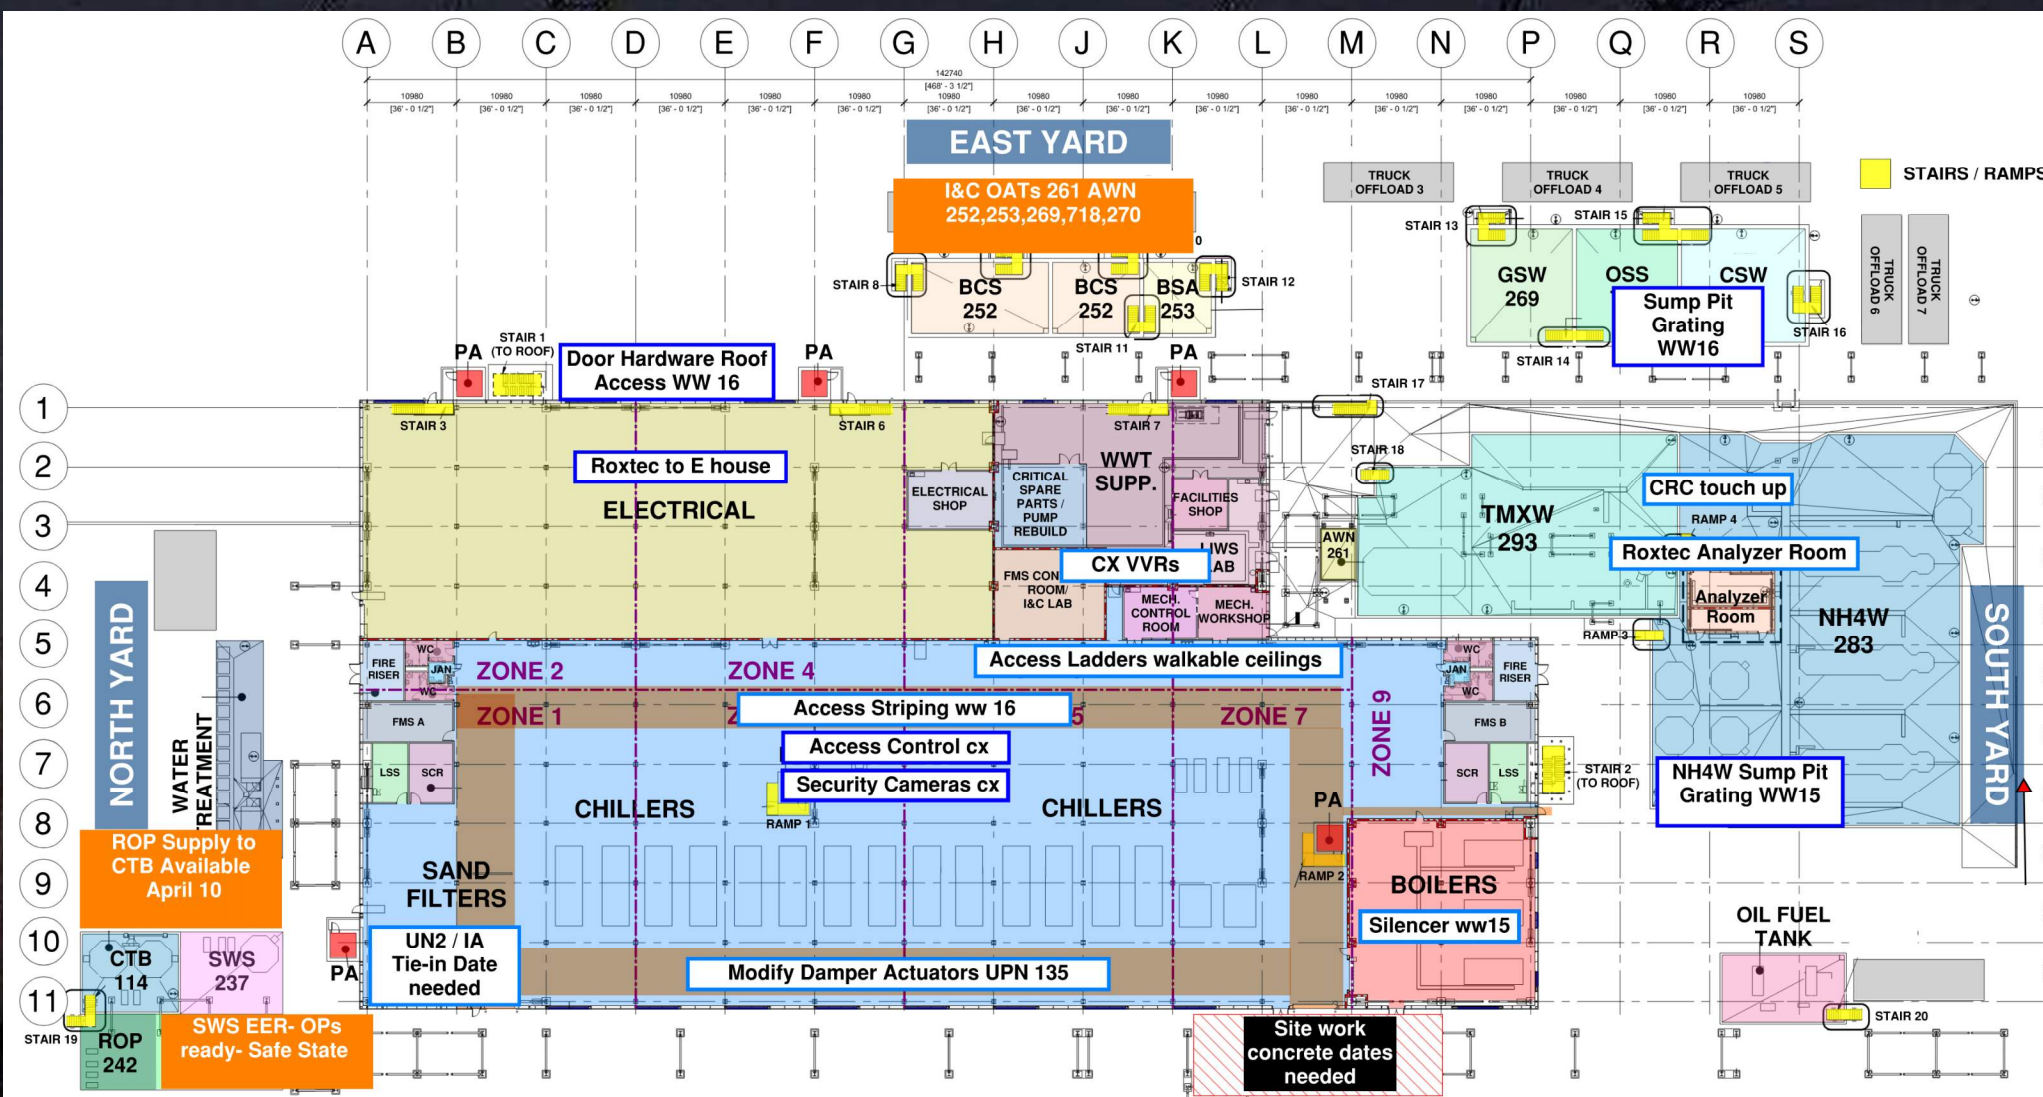


CUB 1 – EXTERIOR/ROOF




CUB 2- Load in & H&T

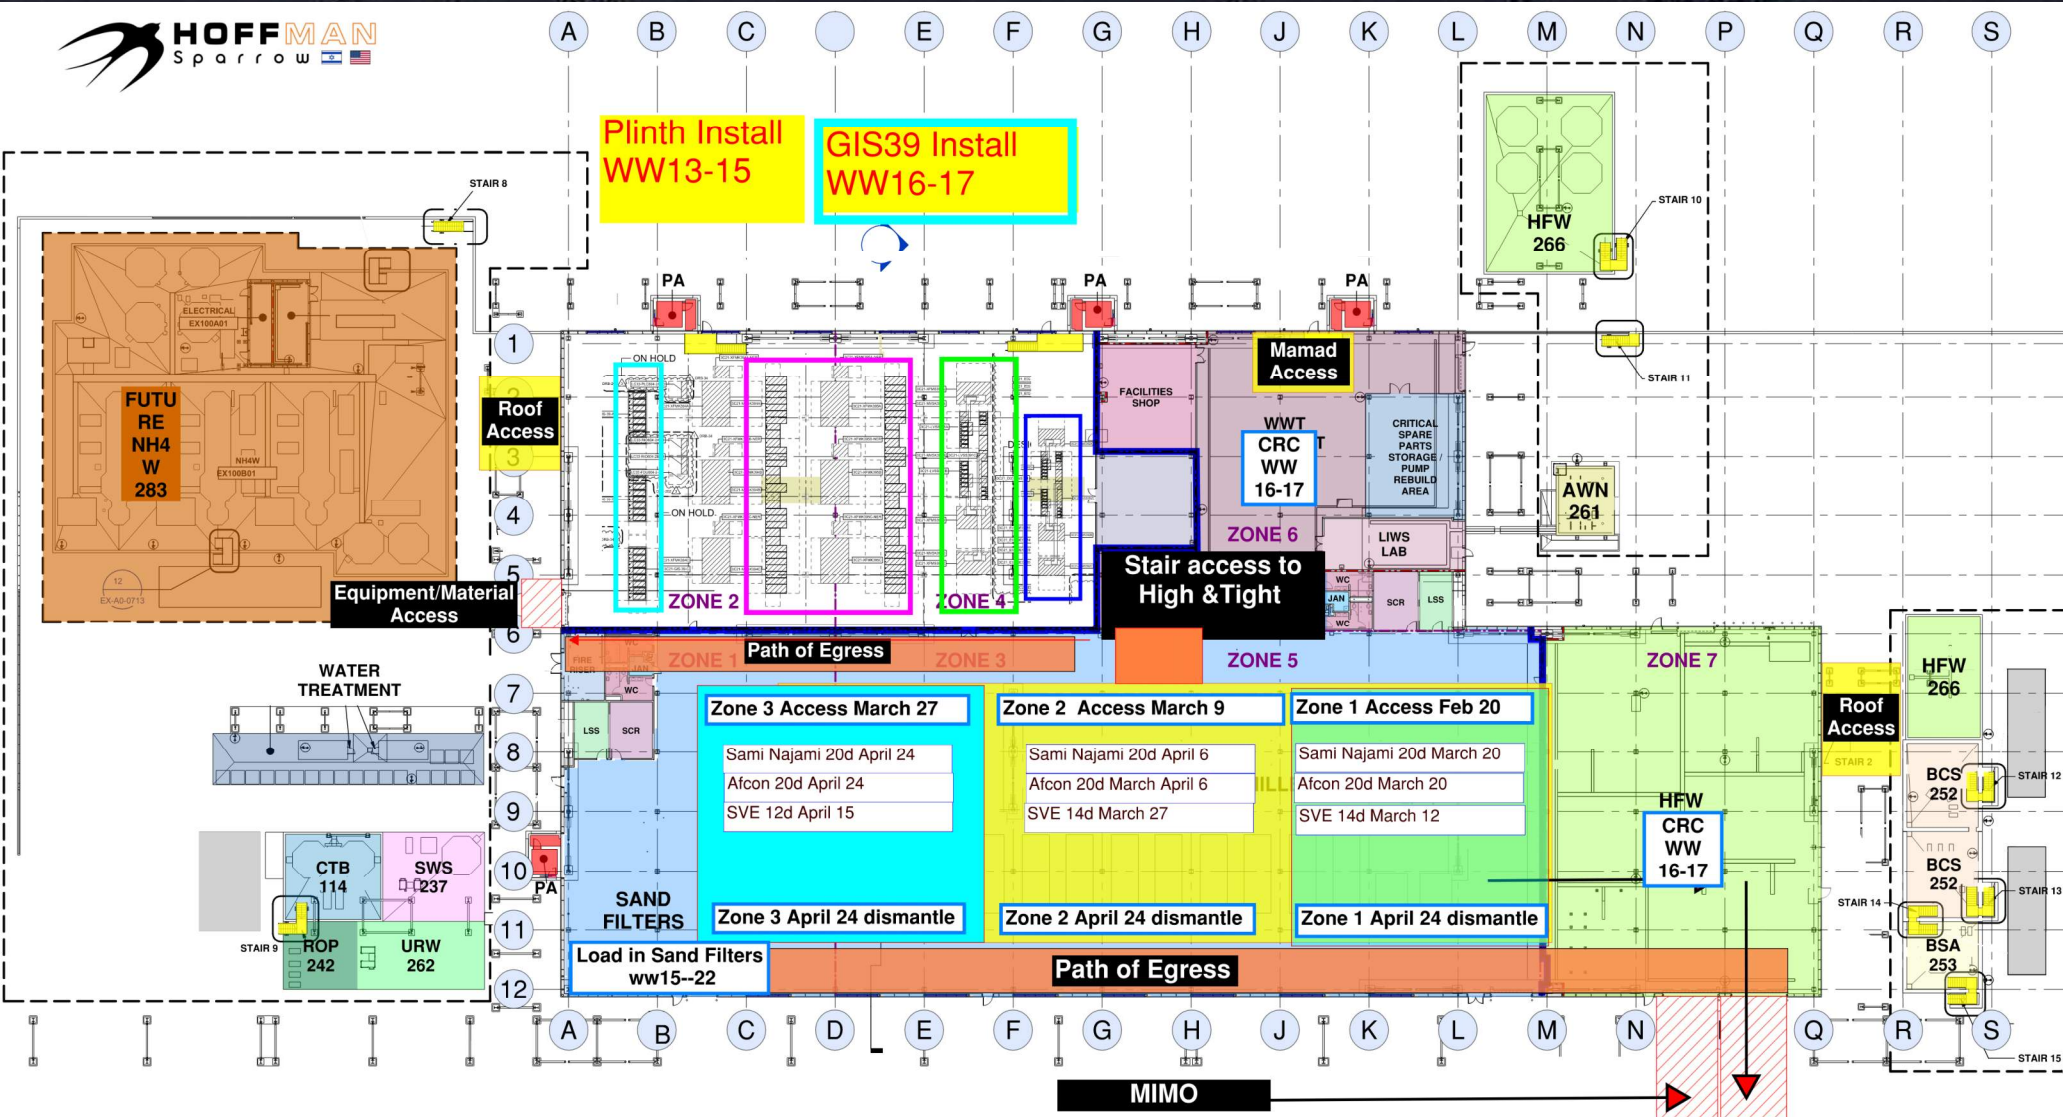


CUB 2- Trestles/Roof/Guardrails

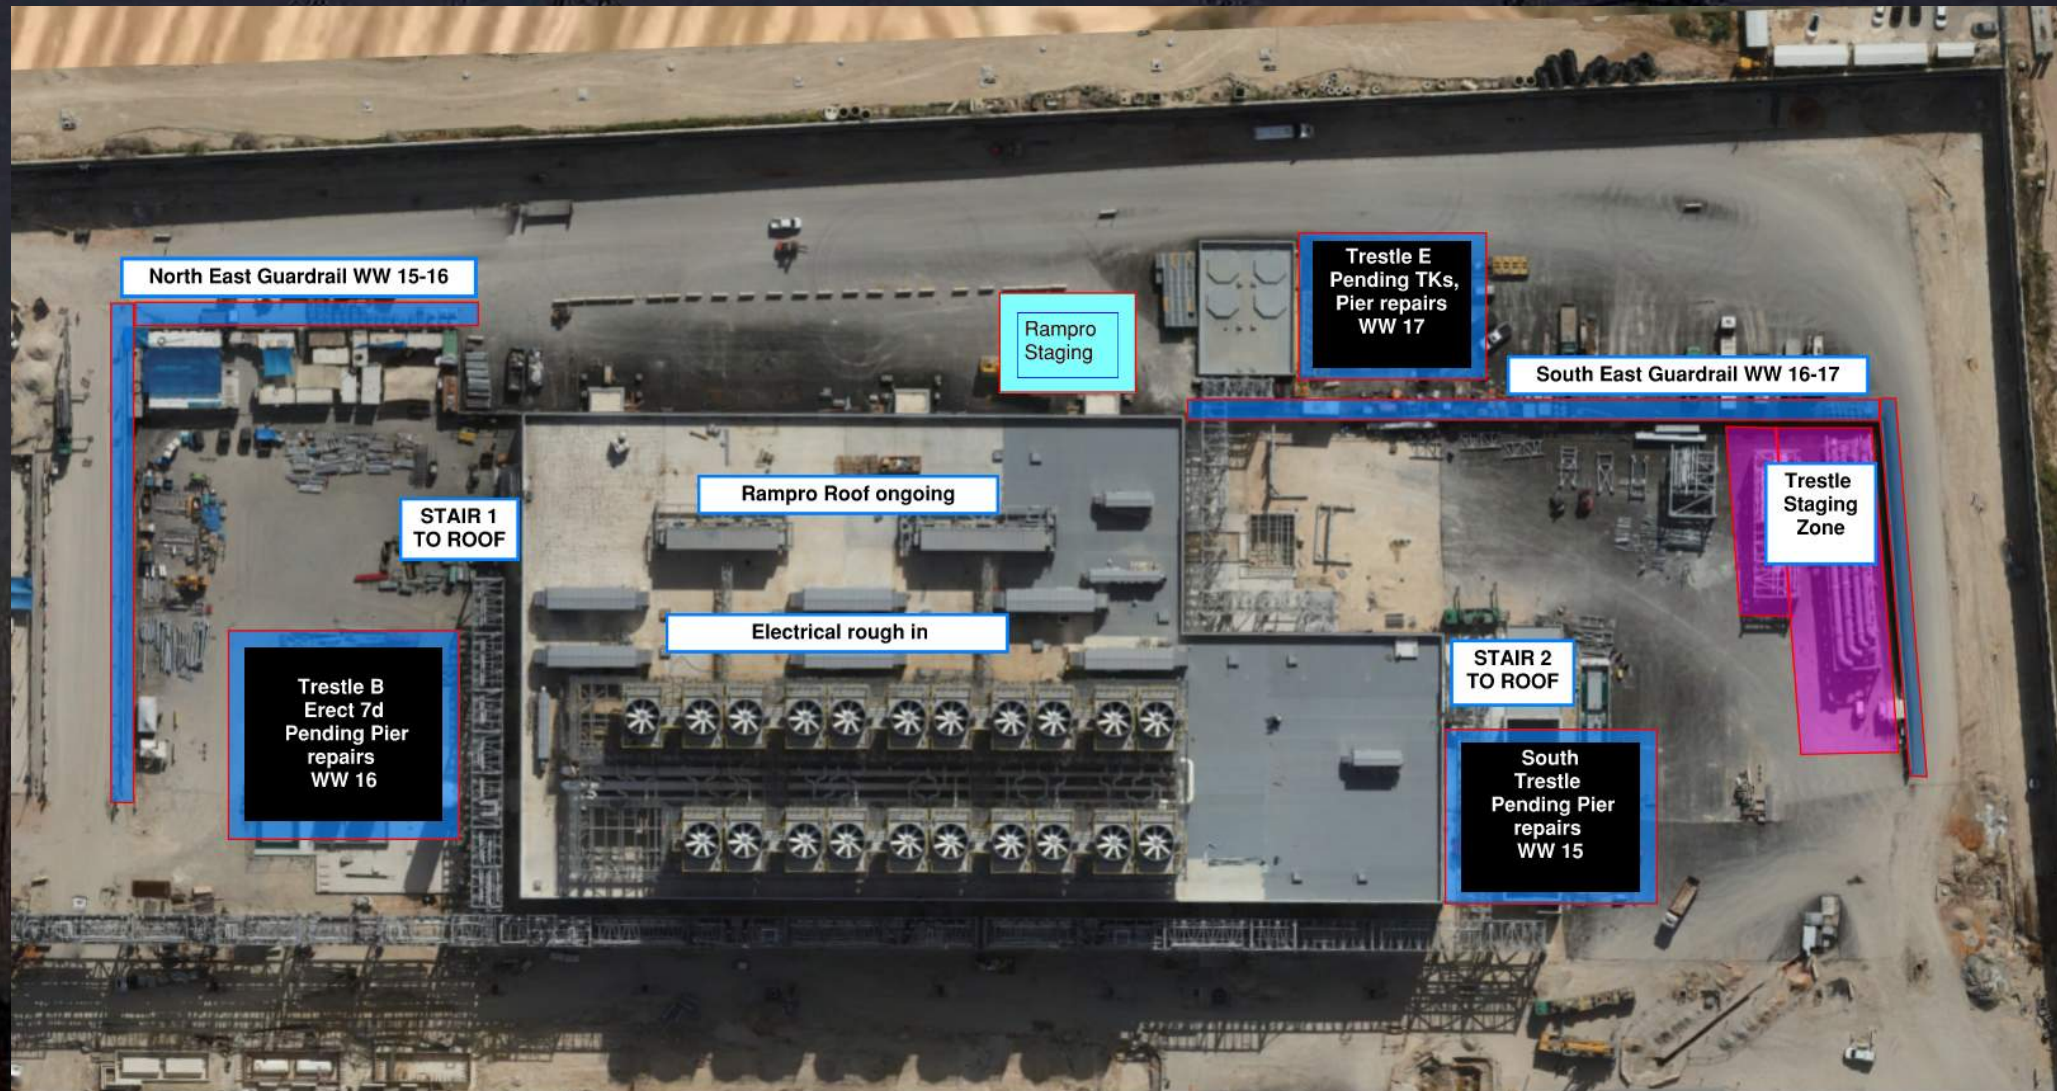



HOFFMAN CONSTRUCTION COMPANY

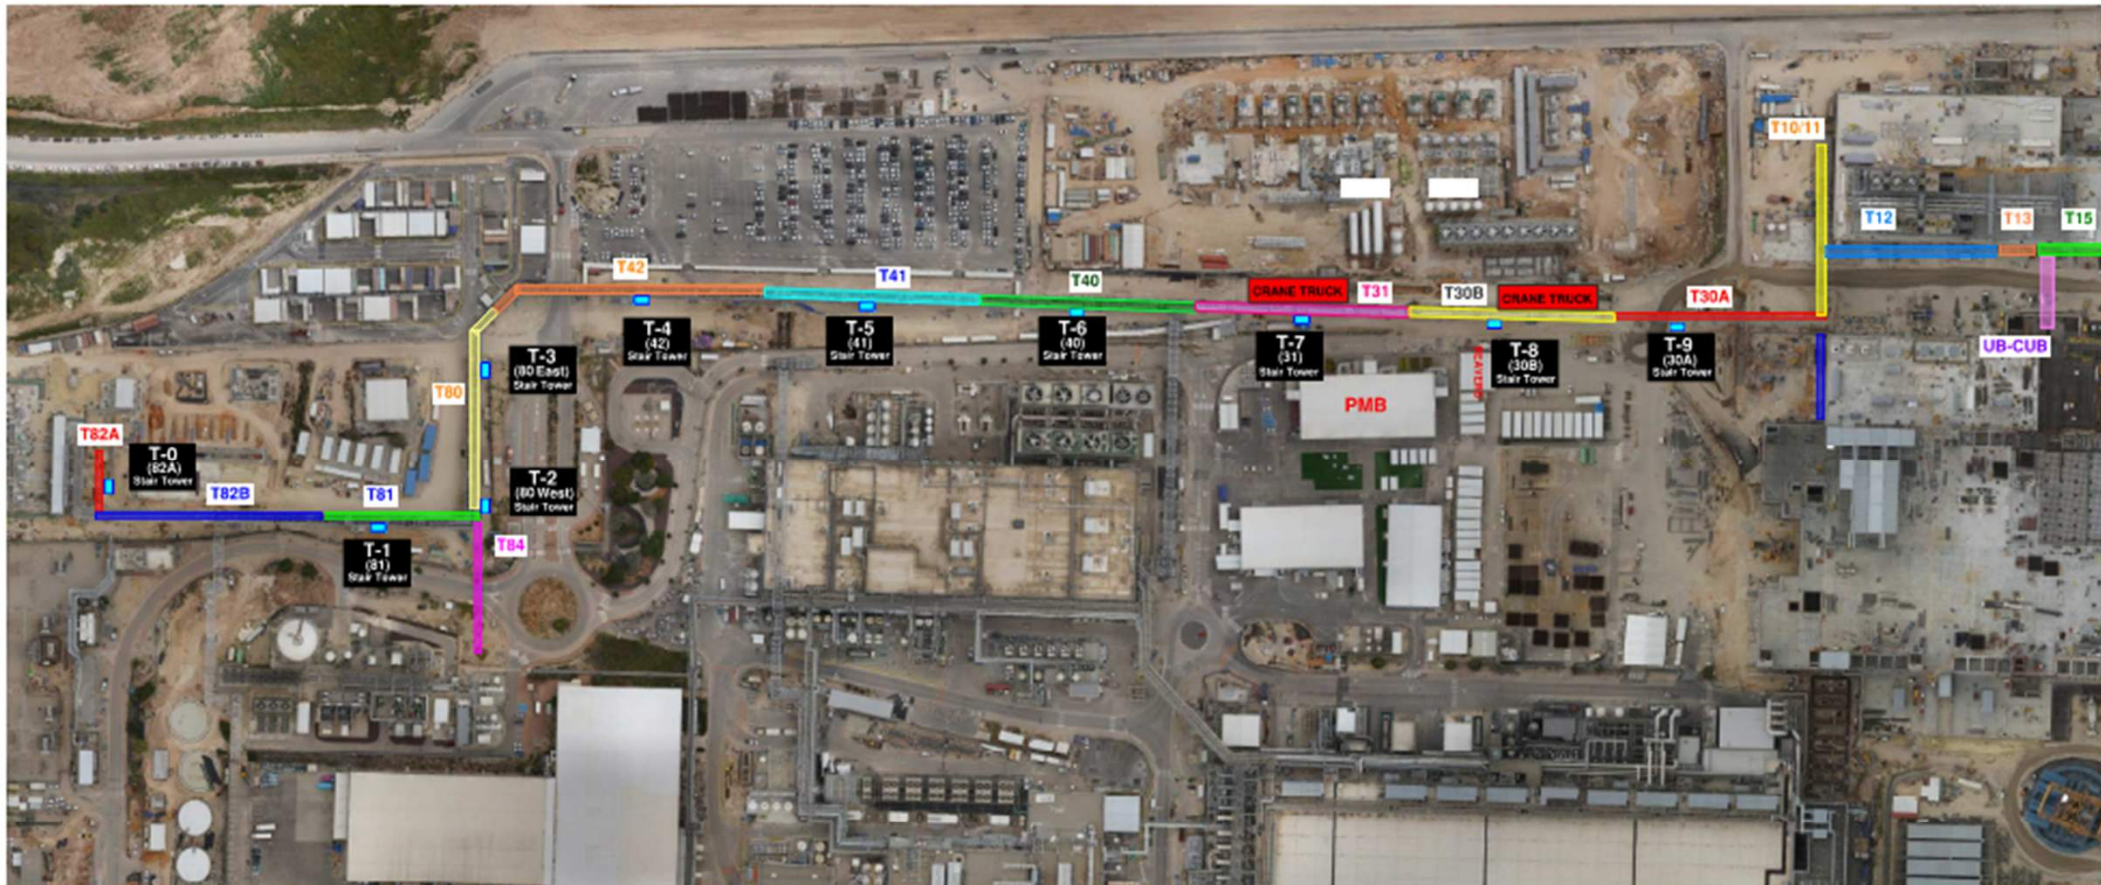




Daily Coordination Meeting

Site Logistics

North

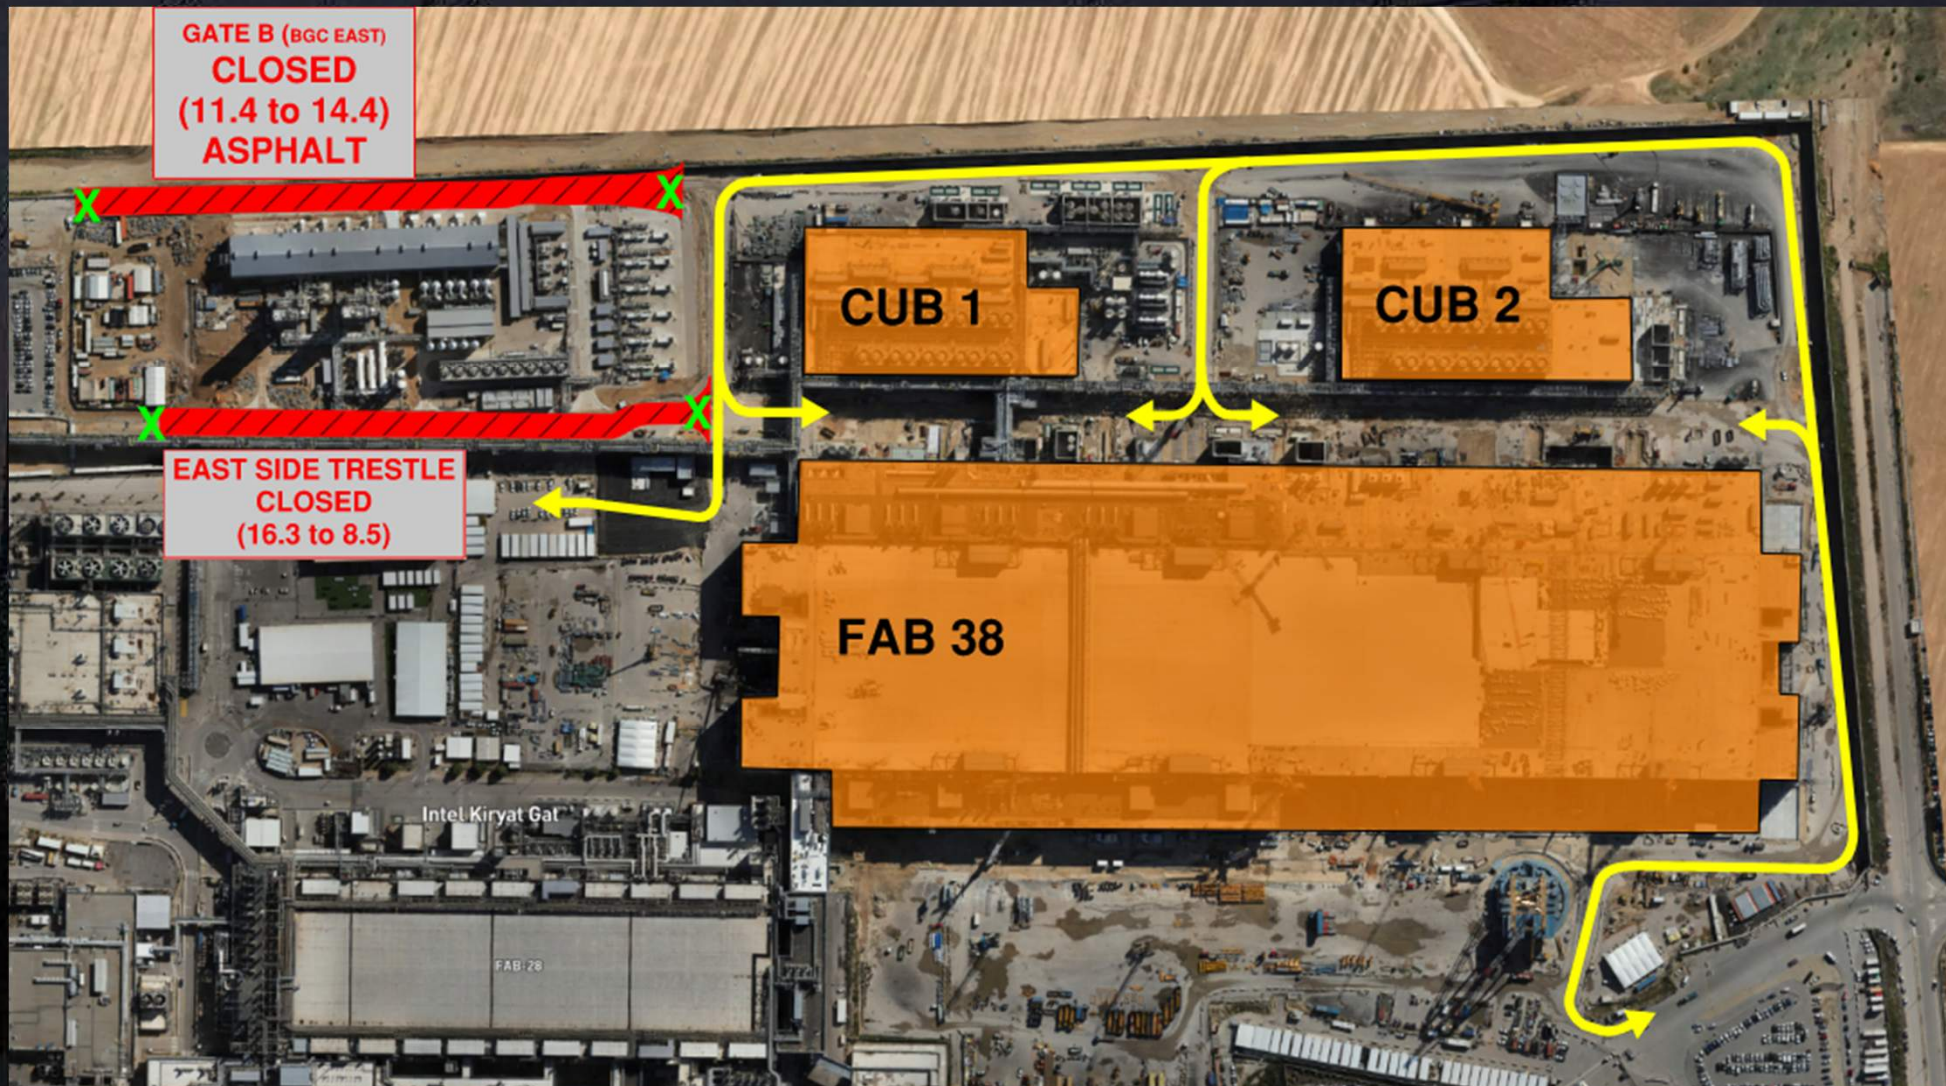




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting


Site Logistics
North

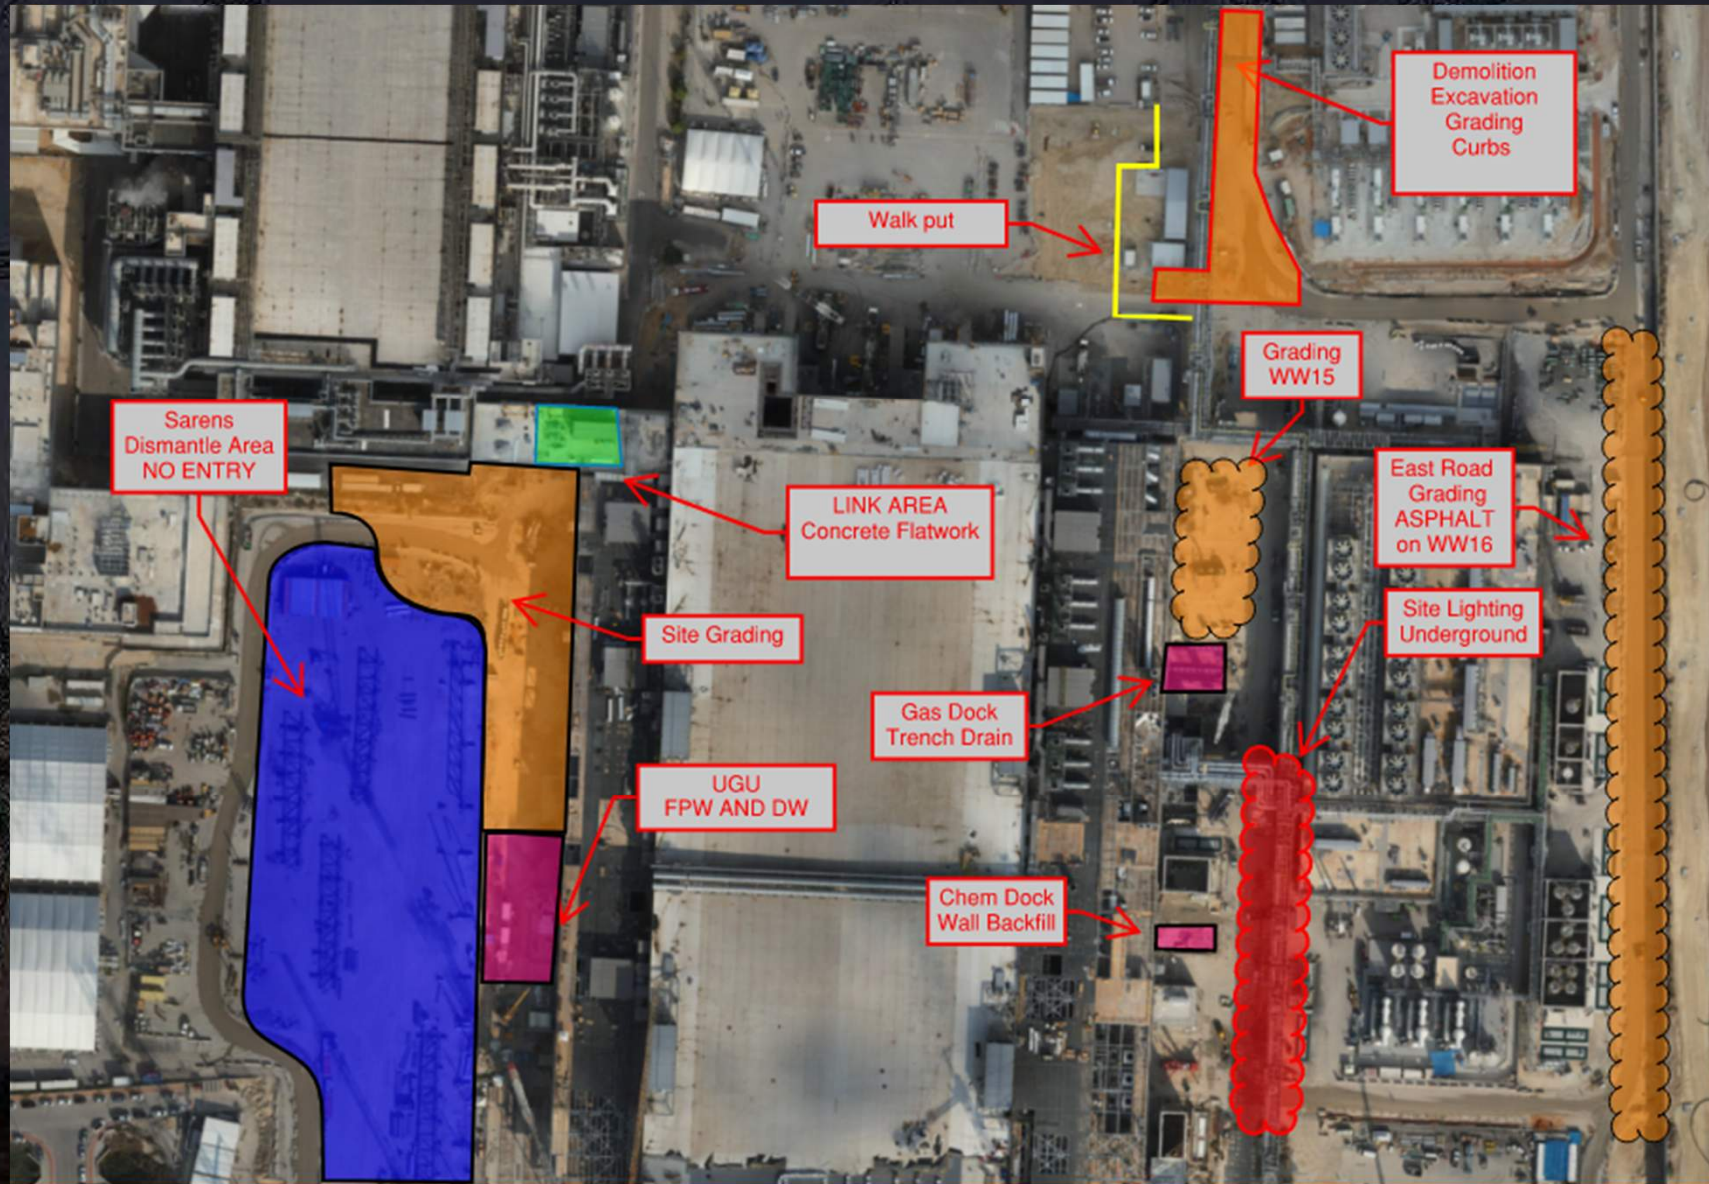



Daily Coordination Meeting

Site Logistics South

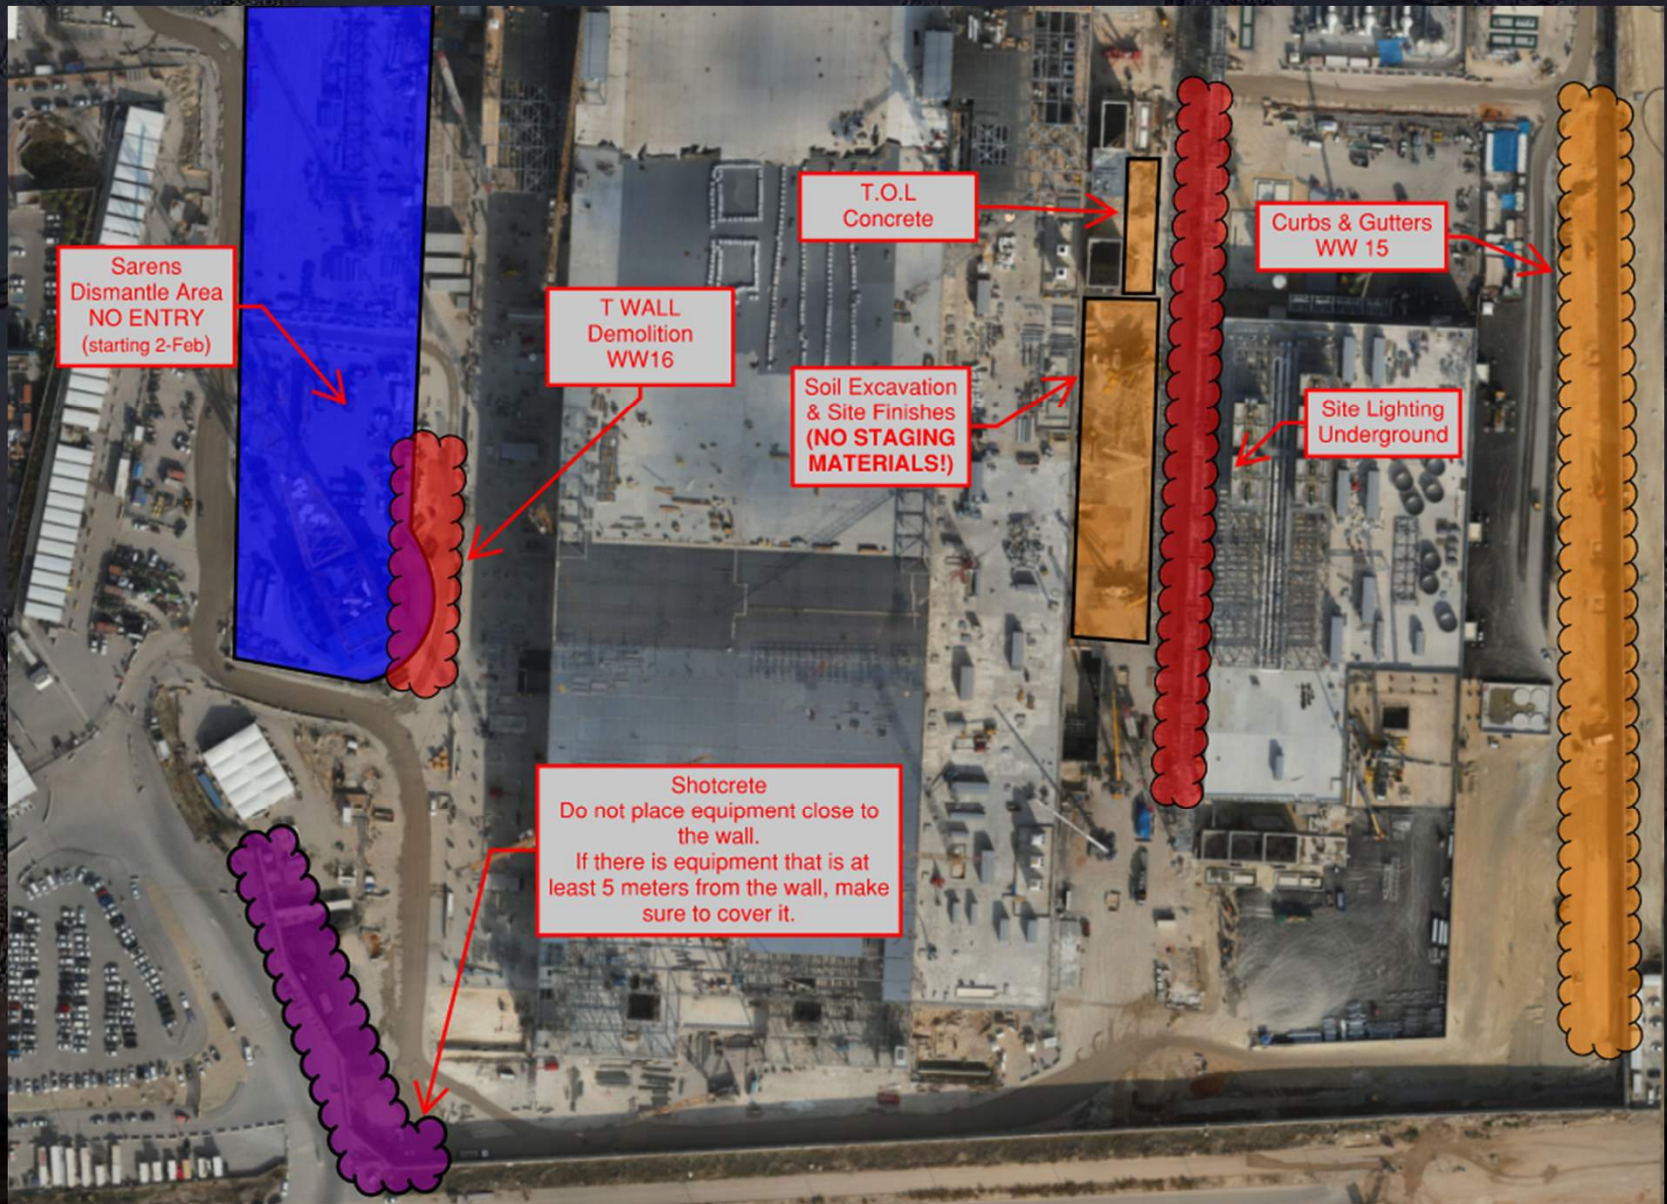



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)

■ LARGE
■ SMALL
■ BUILDING






HOFFMAN CONSTRUCTION COMPANY





Daily Coordination Meeting

WATER BOTTLE FILLING STATIONS

WATER BOTTLE FILLING STATIONS

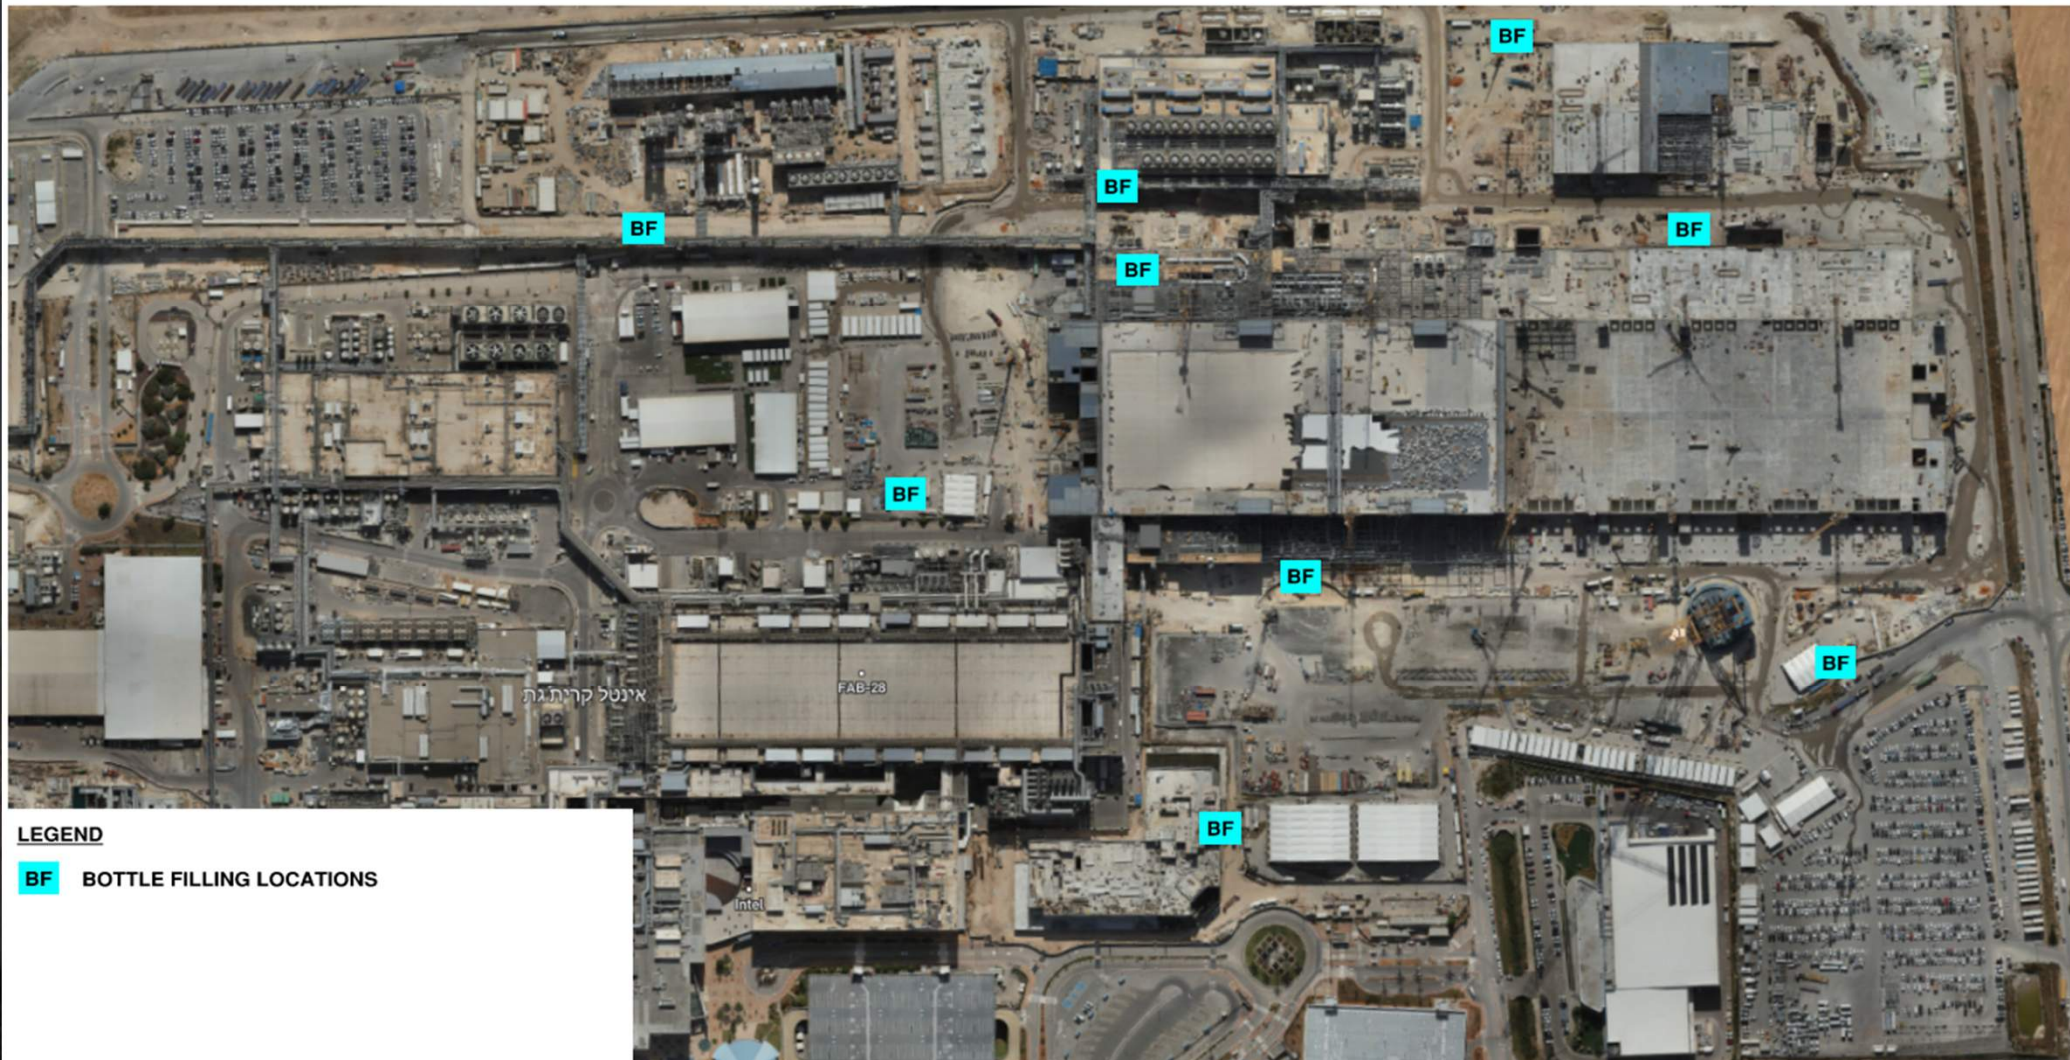

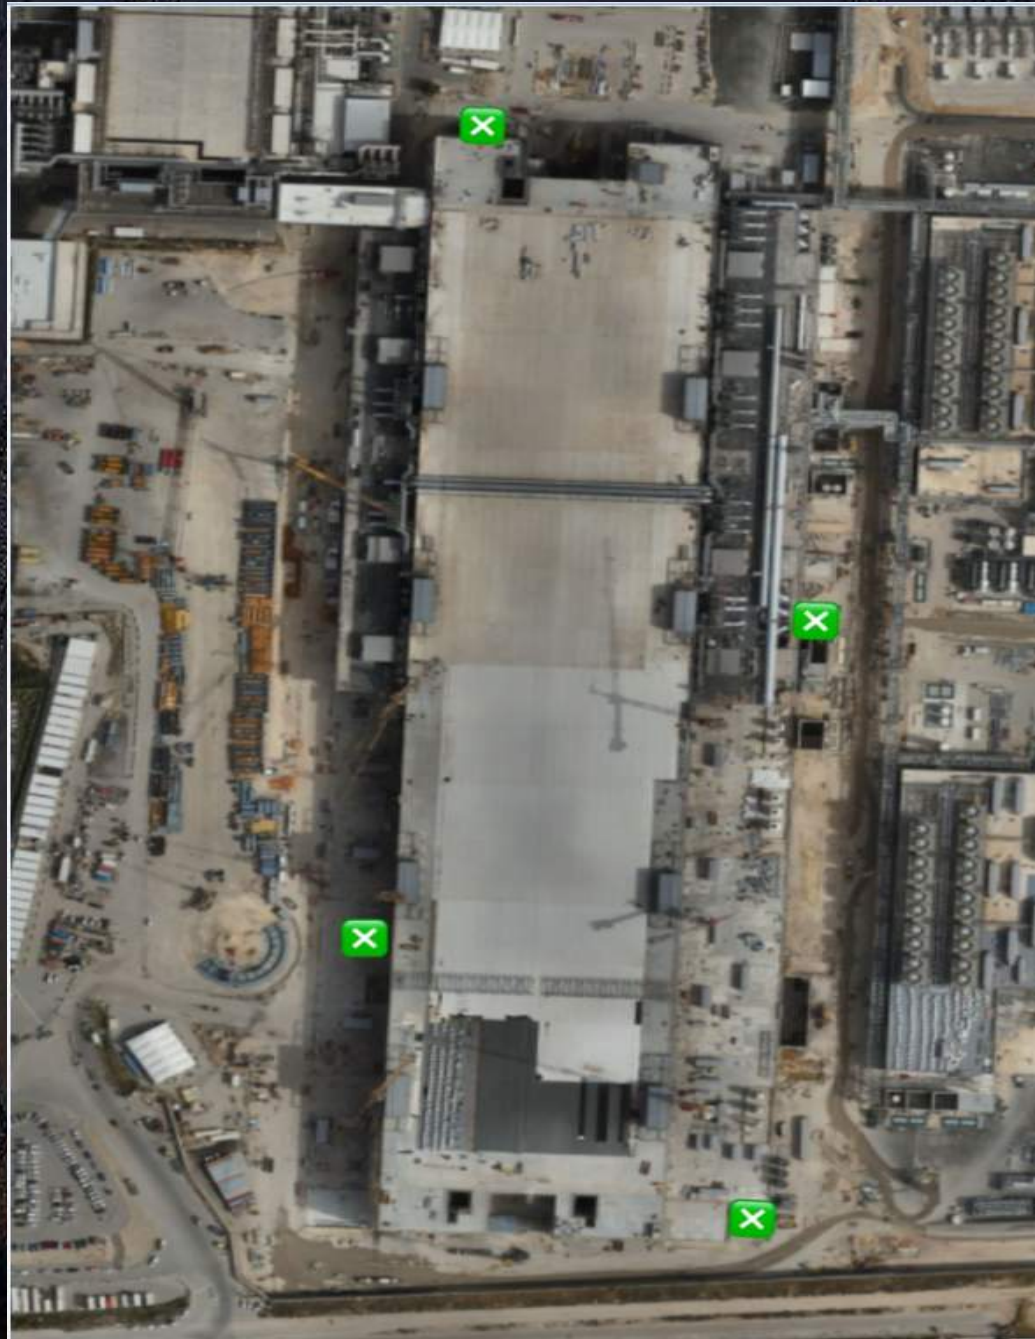

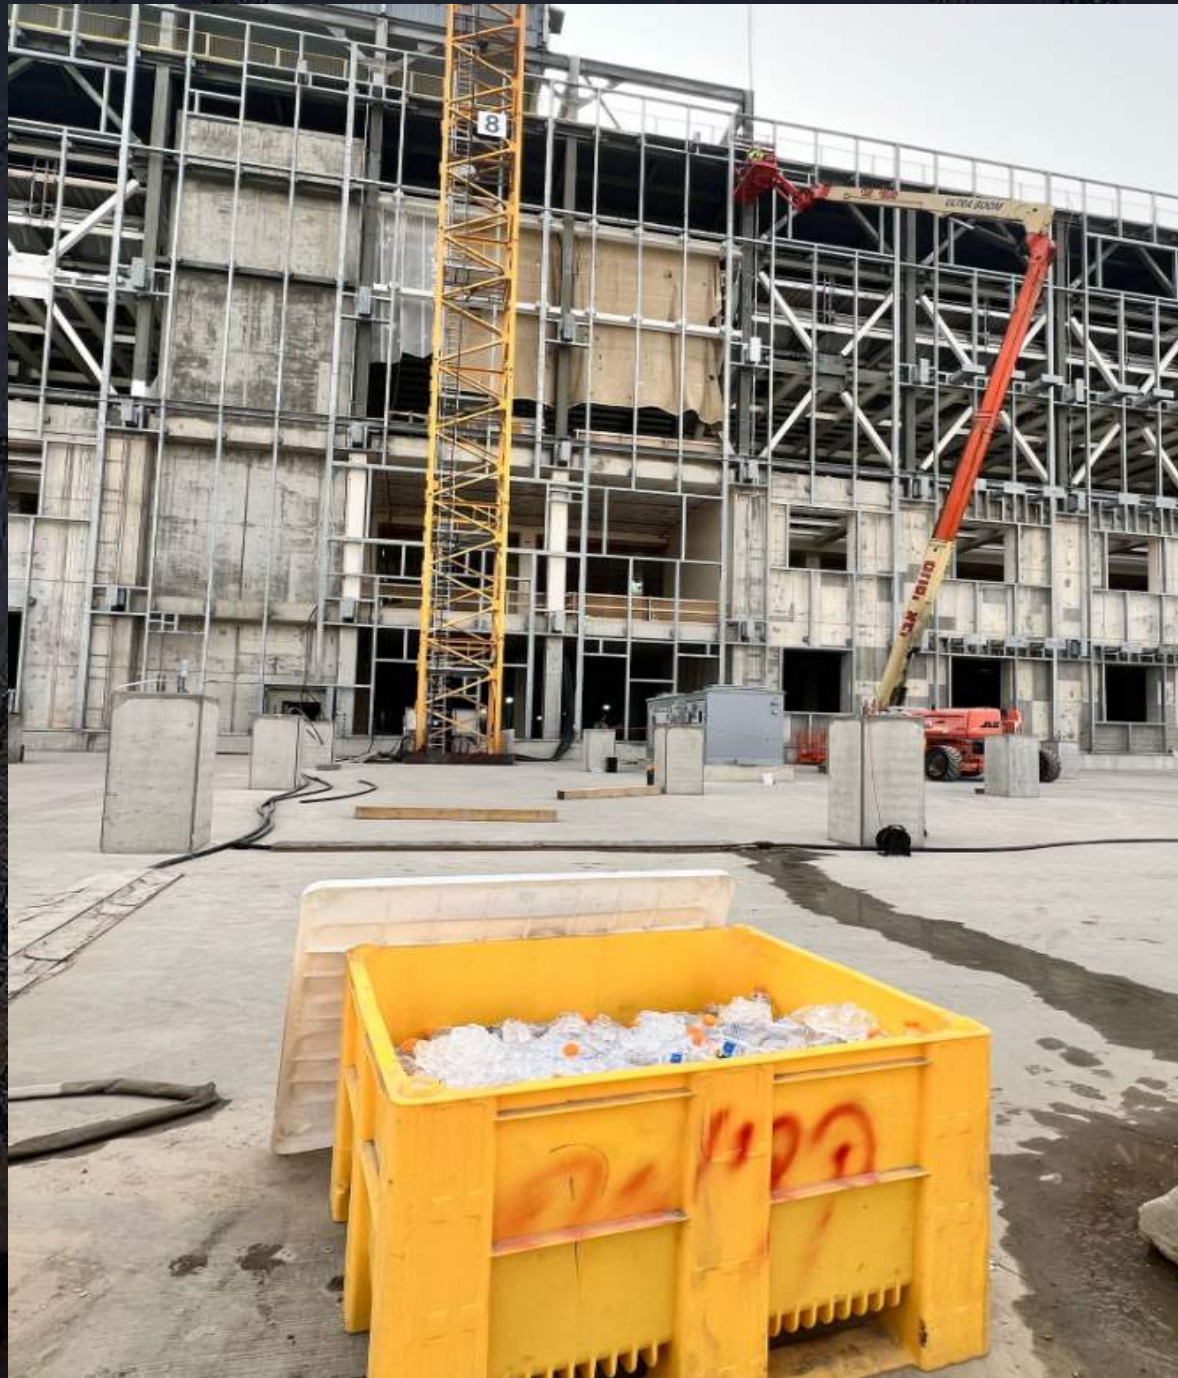

Change in personnel

With the upcoming holiday just like the last one we all need to make sure we have a plan for missing manpower. If you have missing supervision make sure you have a competent person filling the gap.



HCC/EHS Weekend Work- 04/04/2025

White Board Meeting in Beavers at 06:30

Superintendents

Jeremy Lee 052-6042279
Avinadav Ben Yehuda 052-8197360
David Jollands 052-3961675
Paschalis Papadopoulos 052-2168215
Leslie Kelly 052-6391546
Mark Keegan 052-3209679
Max P

CSA CM

Girum Abay - 052-2237784
Pauric Oreilly - 052-3571665

Crane

David Sofati

Cx

Evan Jaderlund 052.575.6048.+ 2 cx team

Safety

Afcon:
Safety: Steven Shartho – 0559129333
Foreman: Mantu Singh – 0559116973

SK:
Safety: Majdi Abu Amra – 0546192581
Foreman: Marcelo – 0542072784

Sami Najami:
Foreman: Sorov Das – 0552837973
Safety: Amir Okev - 0502942941

Subcontractor Weekend Work- 04/04/2025

FAB

Clean Room

Utility level/ SUT

Sami Najami

Foreman: Anuar [0526084897](tel:0526084897)

Ehs: Wasam 0509828381

Afcon electrical

Ehs Steven [0559129333](tel:0559129333)

Foreman Perdit [0552742935](tel:0552742935)

Subfab

- Afcon E
 - SF Mod1 & TTNE&W
 - Team leader: 0559648722

Subcontractor Weekend Work- 04/04/2025

PSSS

Sami Najami

Foreman: Walter Fischel – 052-5319705

Ehs: Wasam 0509828381

WJG

Sami Najami

Foreman: Walter Fischel – 052-5319705

Ehs: Wasam 0509828381

Subcontractor Weekend Work- 04/04/25

CUB

Cx team: Evan Jaderlund 052.575.6048.+ 2 people from cx.

Trestle

Sami Najami steel crew-

Supervisor: Adeeb Asslay 052 601 7477

Safety: Aviram Shriki 050 905 9920

QC: Saleh Shabaneh 054 222 0995

Foreman:Walter Fischel – 052-5319705

Safety: Wisam 050 928 8381

Site

Daily Coordination Meeting



14:00 Sign In
