

Daily Coordination Meeting




Daily Coordination Meeting

General Topics:


- **Weekend Work**
- **Holiday Week next week – Red Flags**
- **Remain Focused on the Little Things**

[illegible]


SUT 38.1 LEVEL

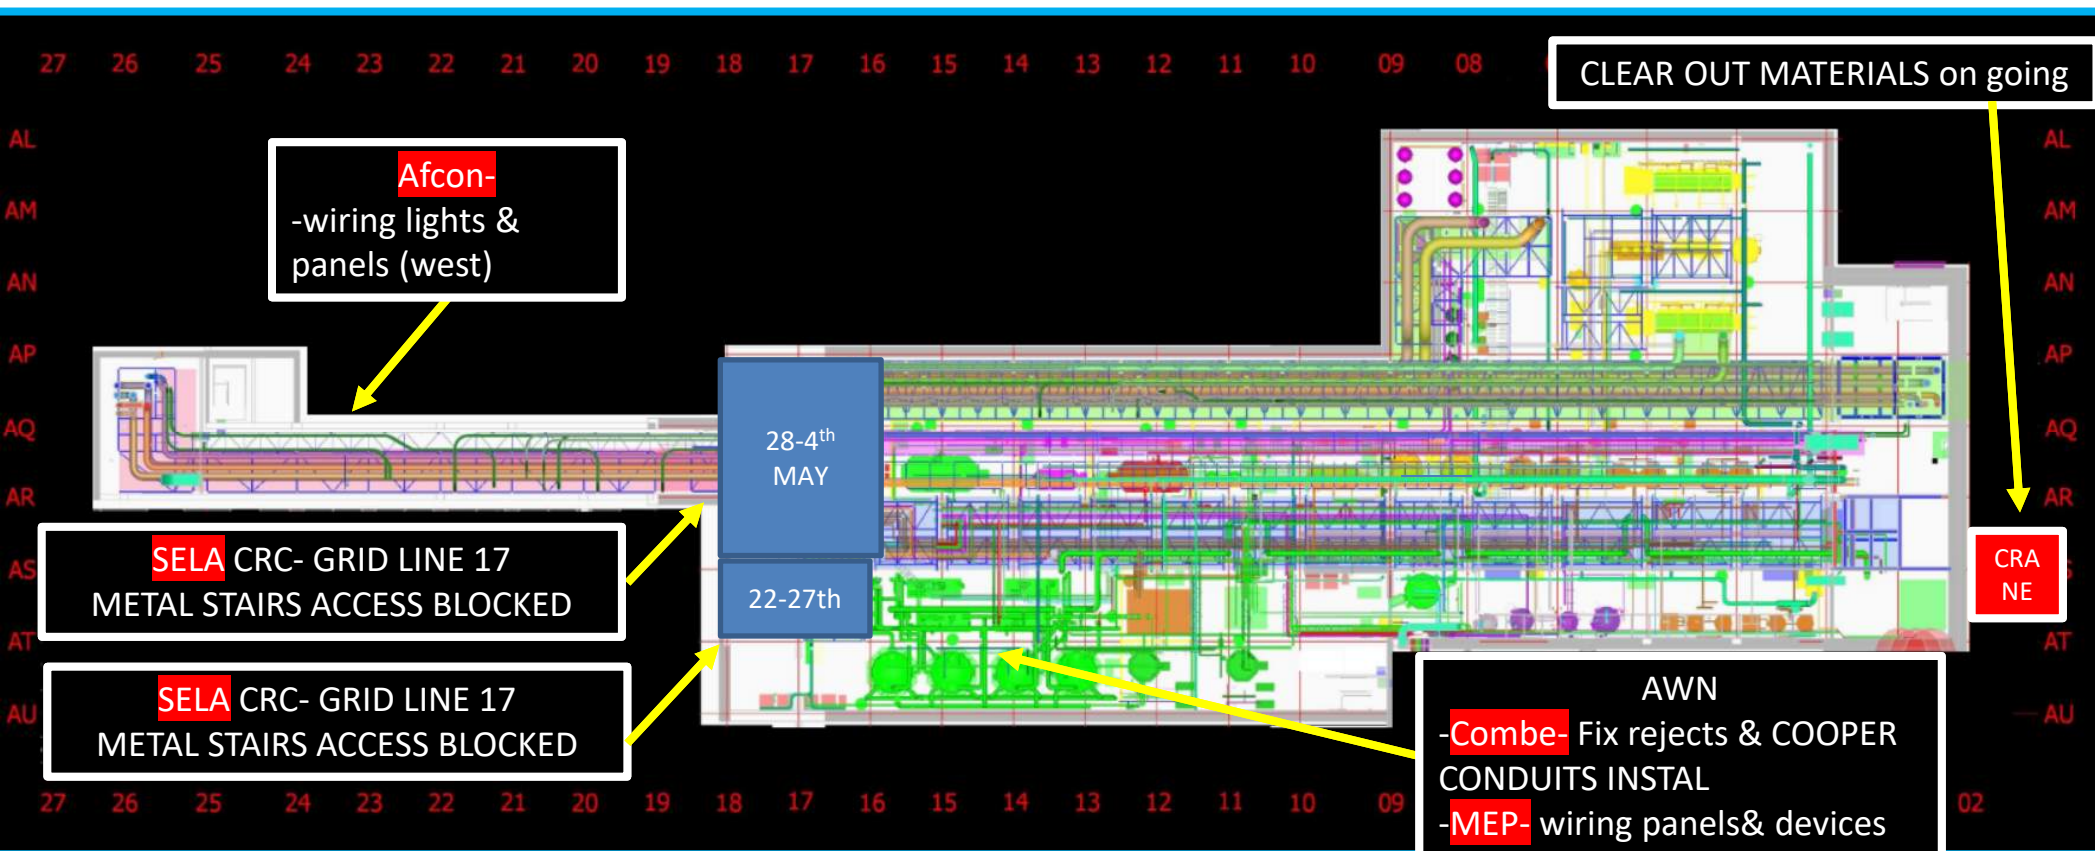


sut 1 crc sequence		
SEQUENCE	start date	completion date
1	done	
2	27.4	7.5
3	8.5	19.5
4	19.5	29.5

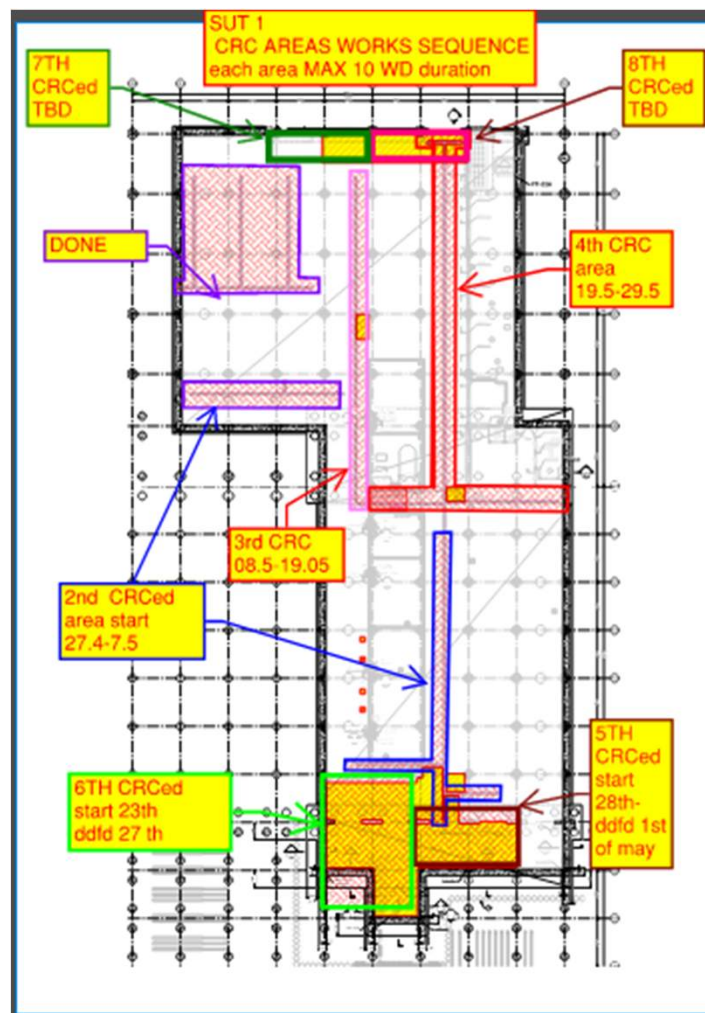



SUBFAB BUILDOUT MOD 1

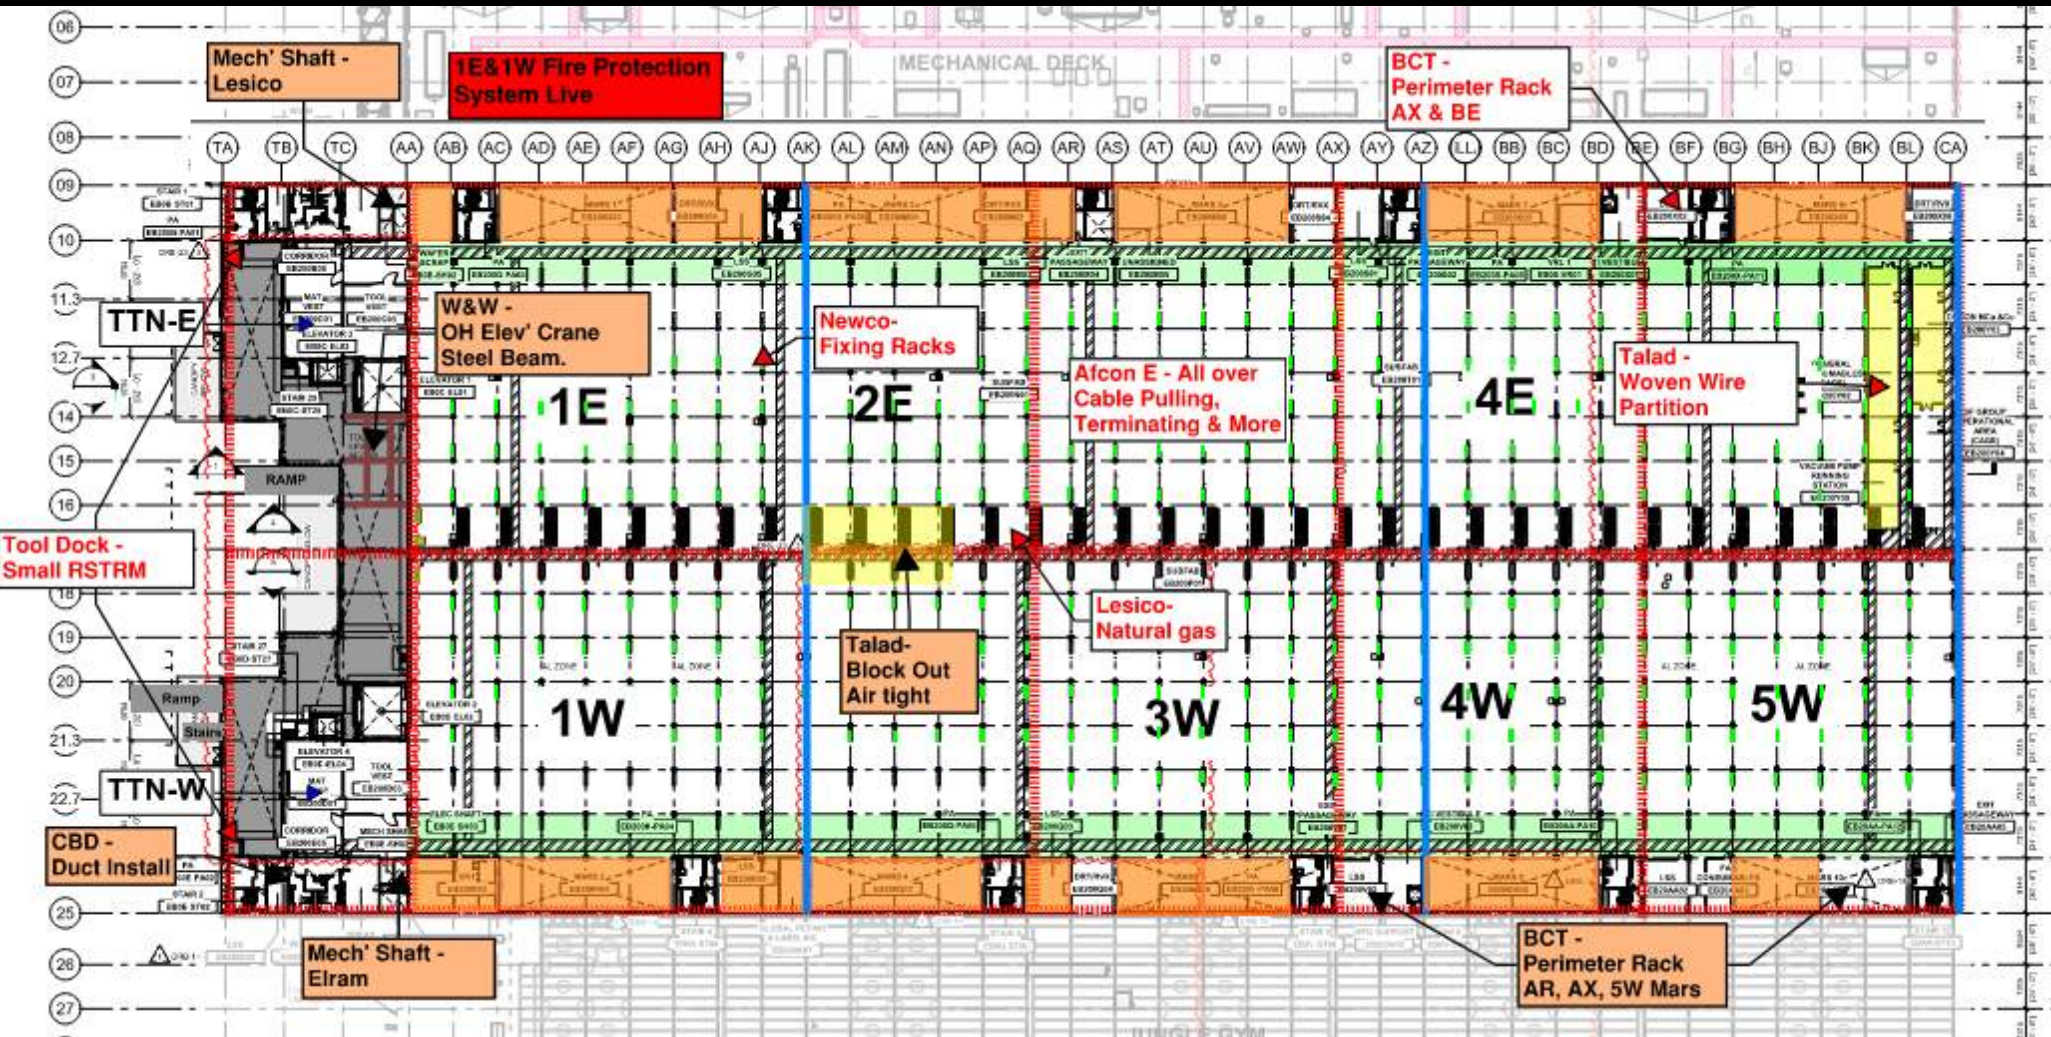


BCT/Lesico Pressure Test Tomorrow

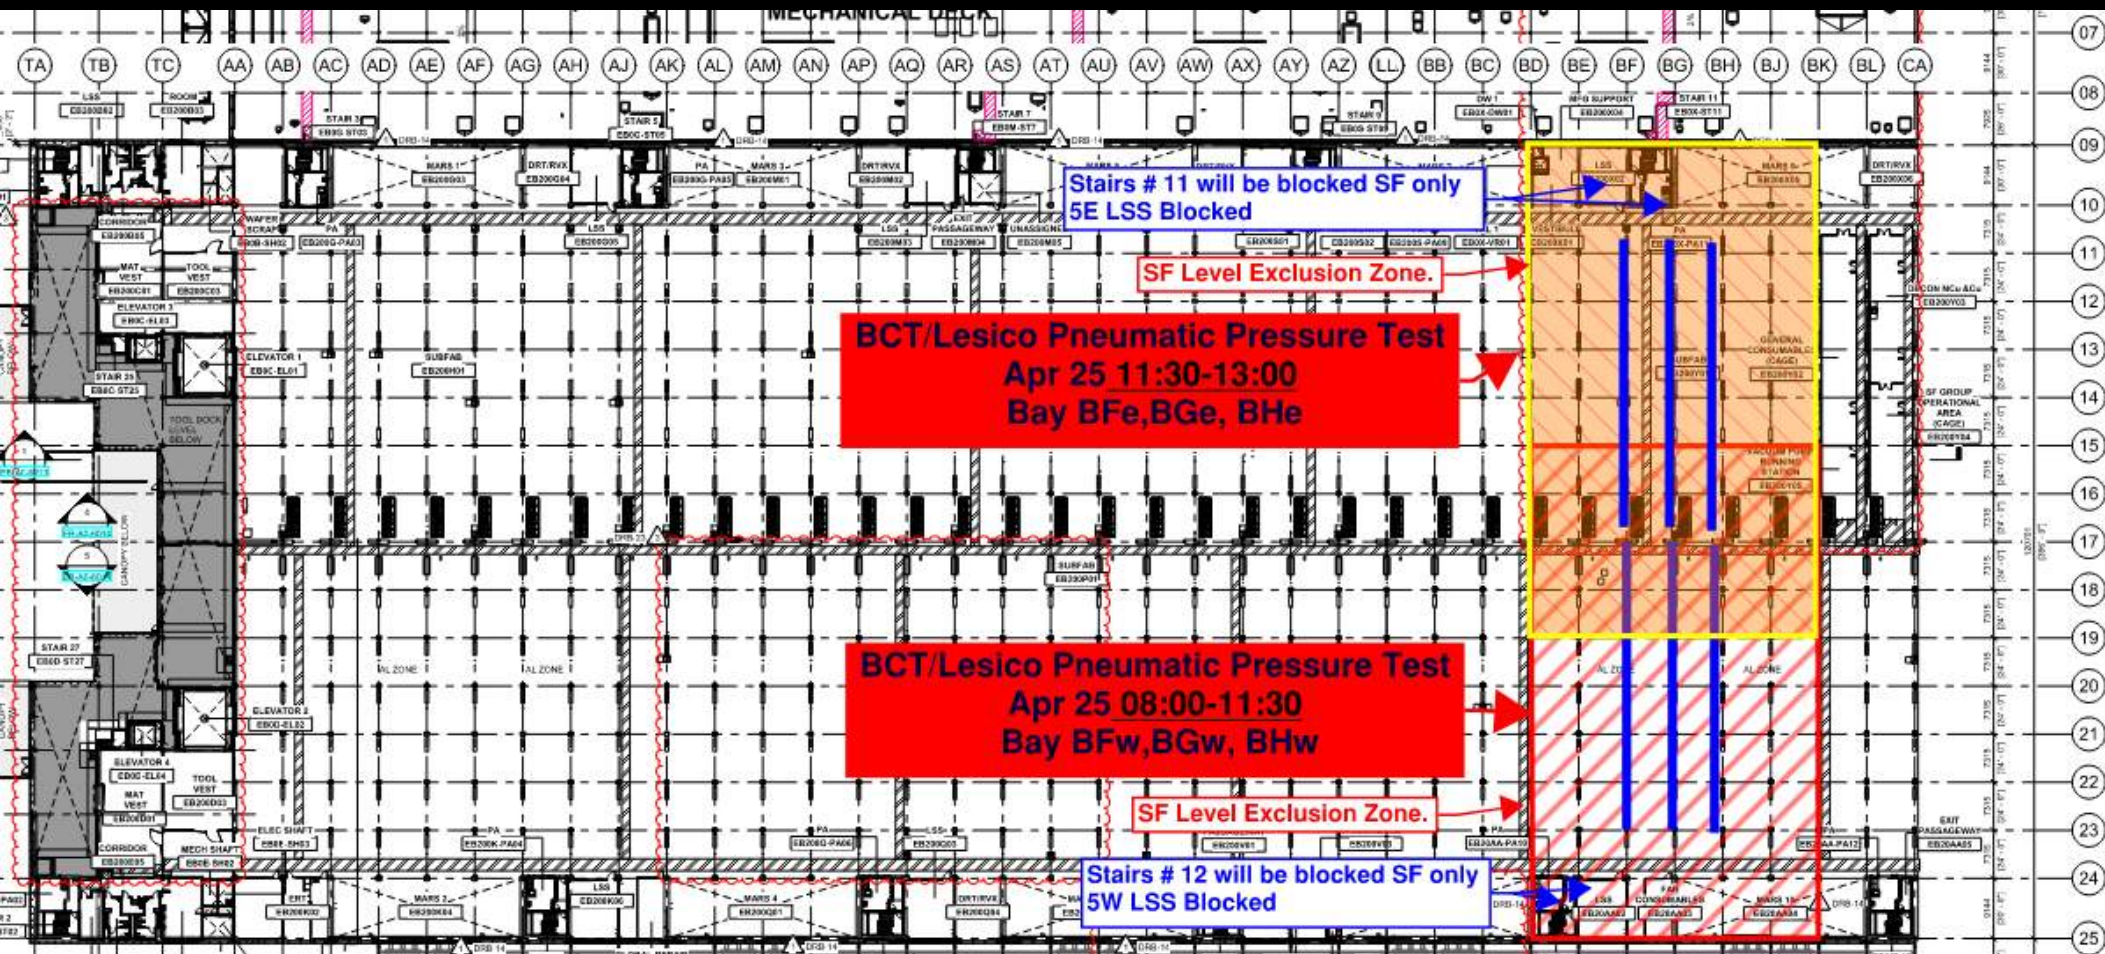

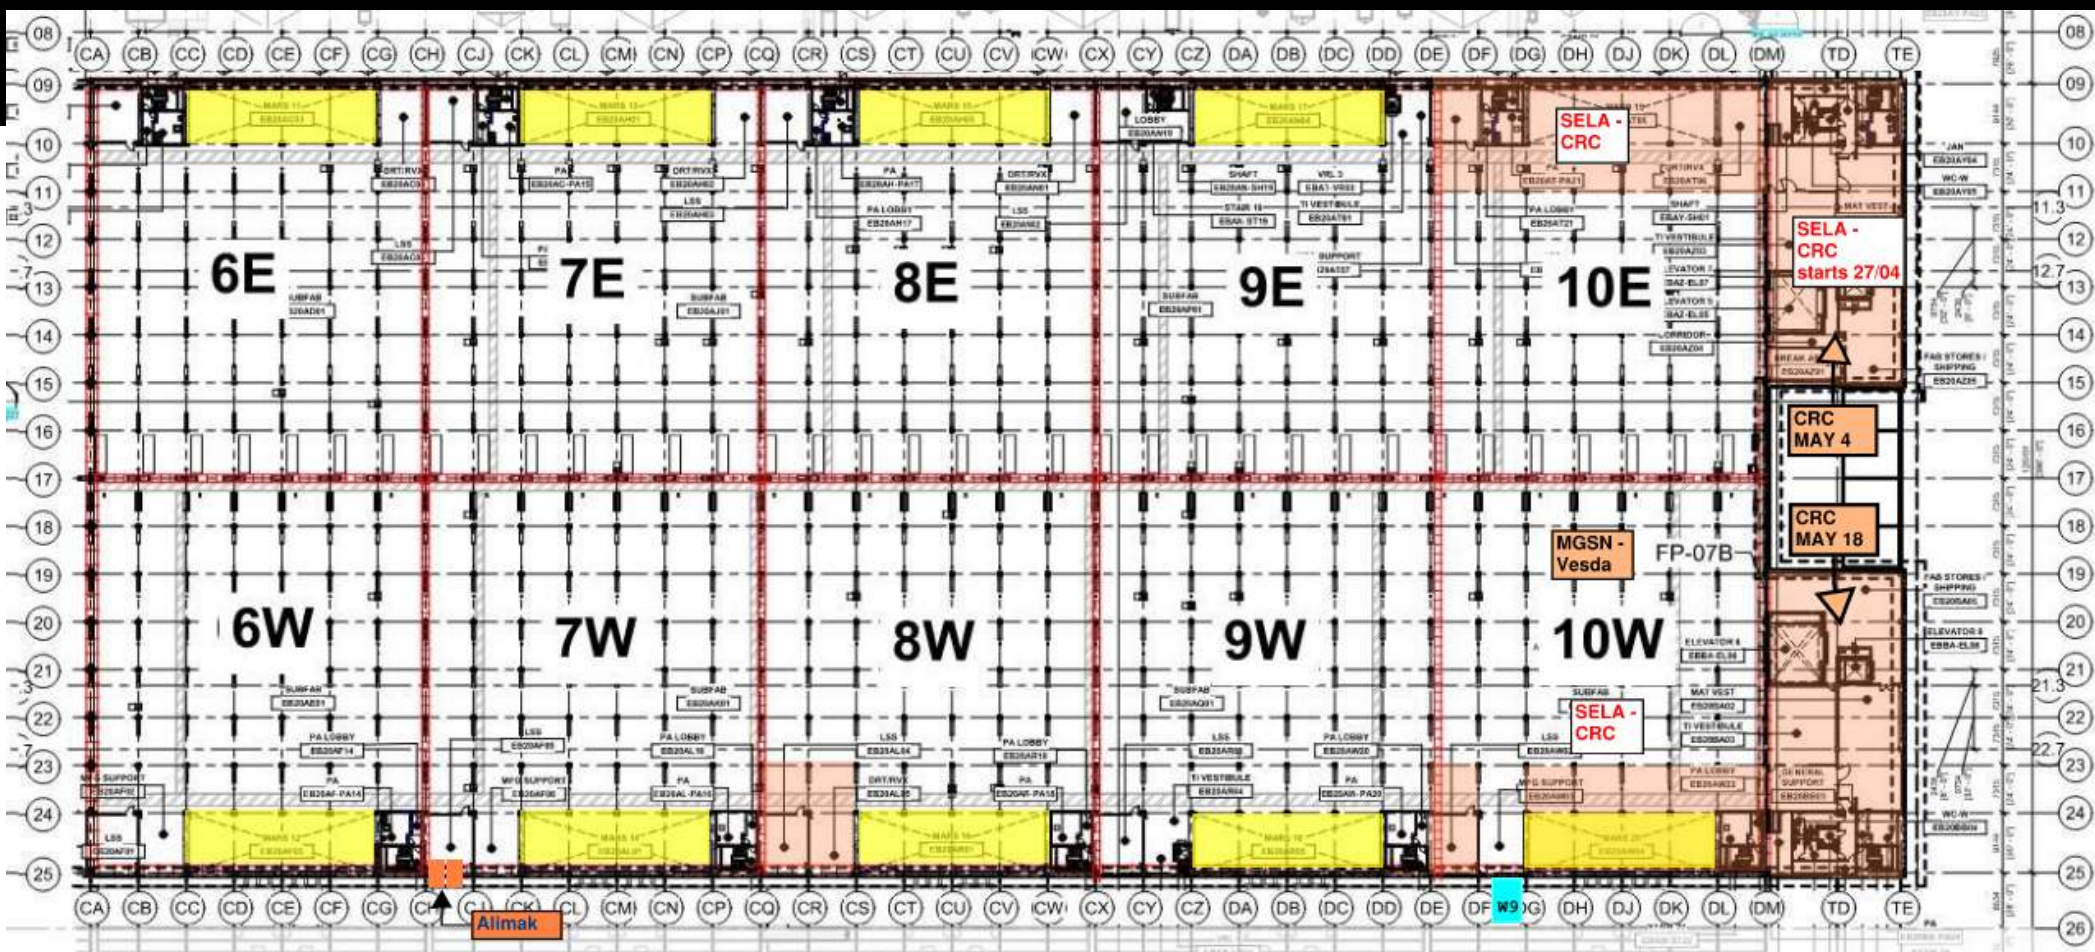

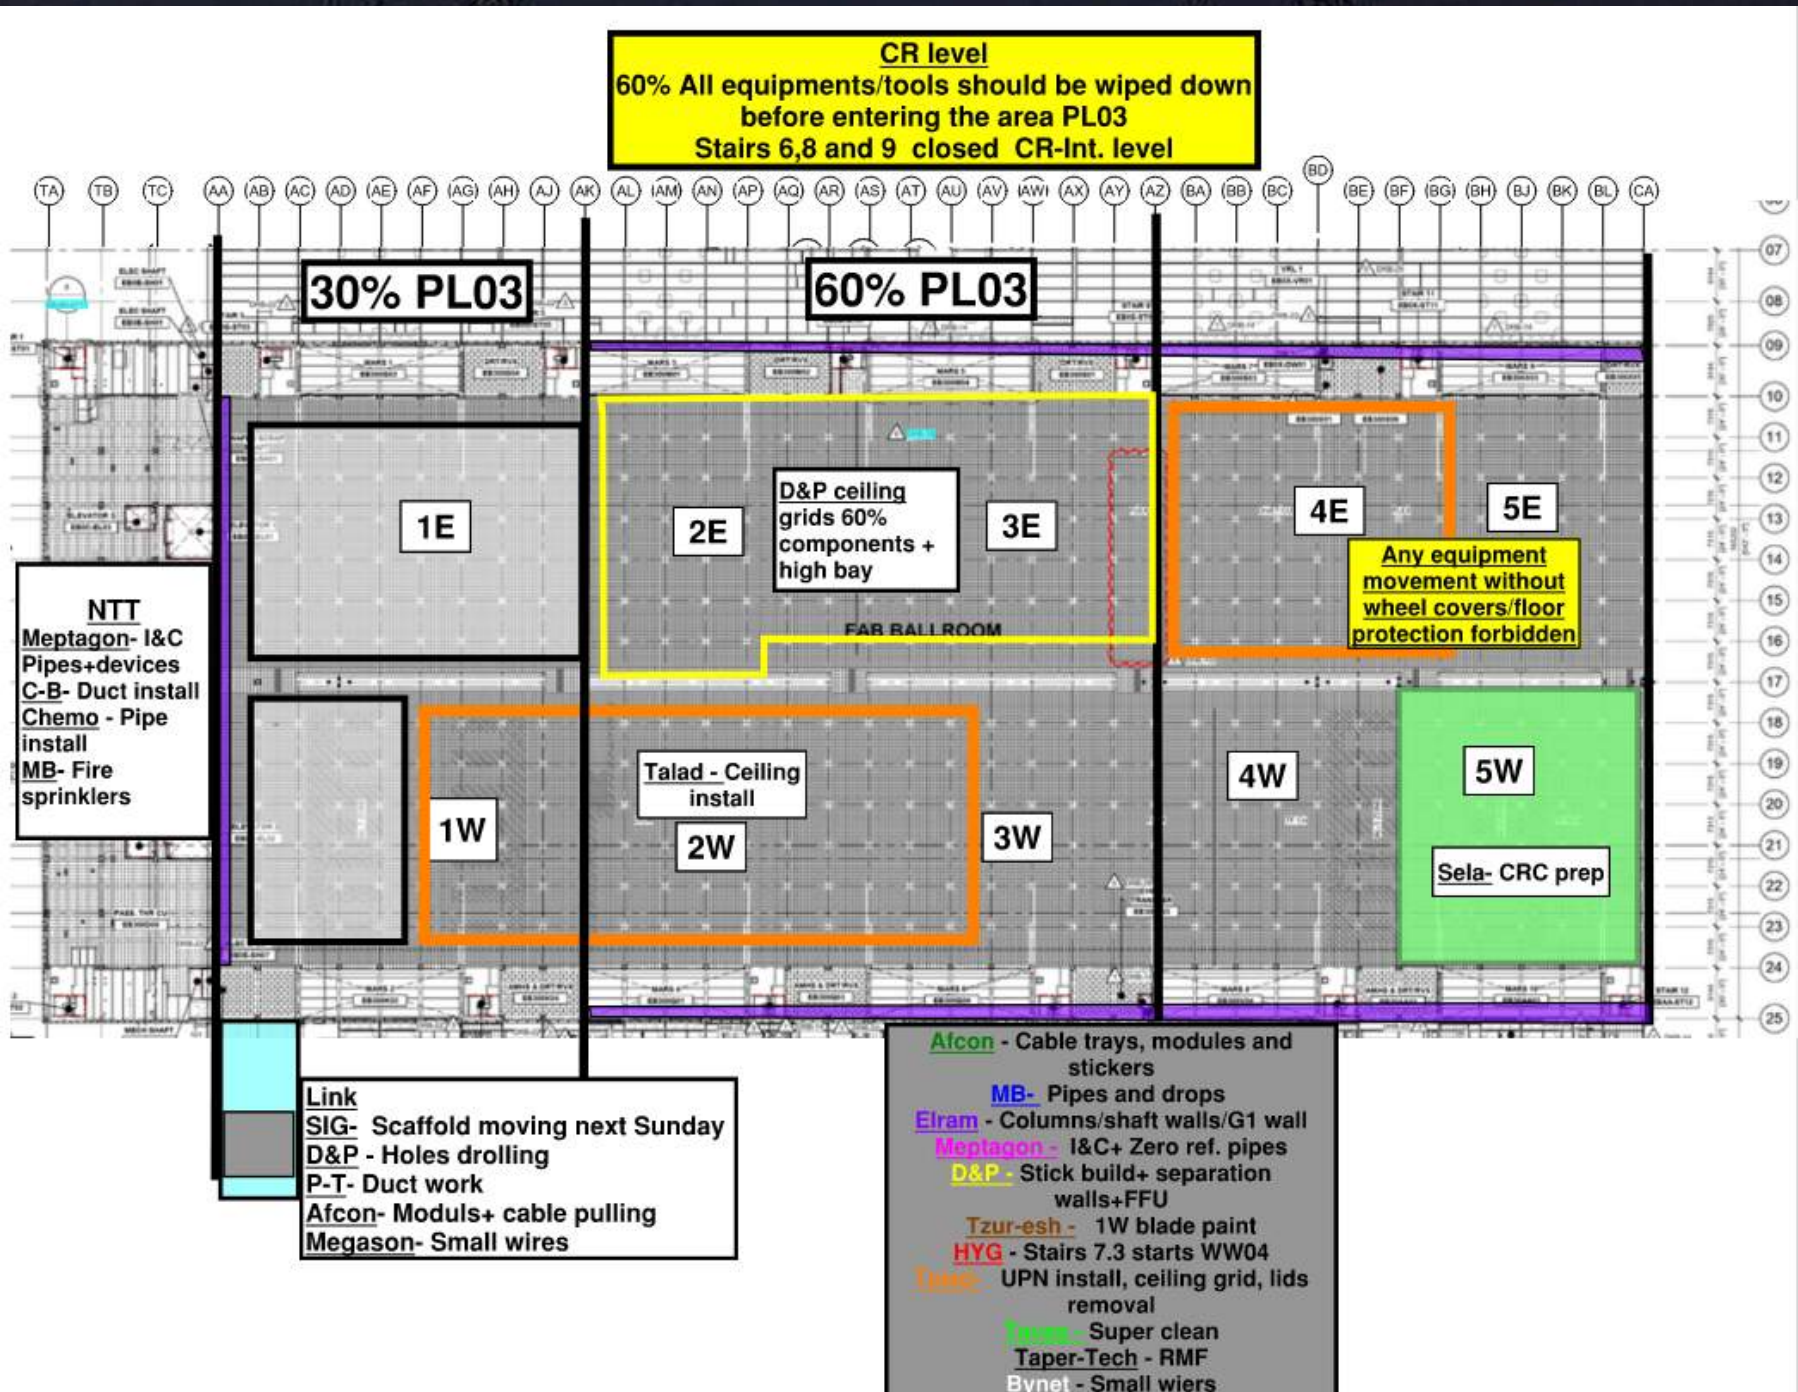



JIB CRANE LIFTING ZONE

Afcon - Cable trays, modules and stickers

MB - Fire sprinklers

Elram - Gypsum/G1 wall

Chemo - Skids and pipes

SK - IA pipes

Tzur-esh - Paint+ touch ups

WW - Cat walk

RPC - 4DA/5DA FP

Tavas - Super clean

Bynet - Communication weirs

Megasone - Speakers

Meptagon - I&C

Int. level


Walk on FRP is approved.

Do not move carts/ stage material without plywood

TA TB TC AA AB AC AD AE AF AG AH AJ AK AL AM AN AP AQ AR AS AT AU AV AW AX AY AZ BA BB BC BD BE BF BG BH BJ BK BL CA

30%

60%



NETT

Chemo- Racks+pipes ongoing

Megasone - Small wires+Speakers

RPC- FP rack/girts

Elram- LSS room

NWTT

Chemo- Racks +pipes


MB- FS install


AFA- Vesda


Elram- LSS room

WW/SN - Handrail install


TMT- Penetrations for Afcon, D&P, Talad and MB

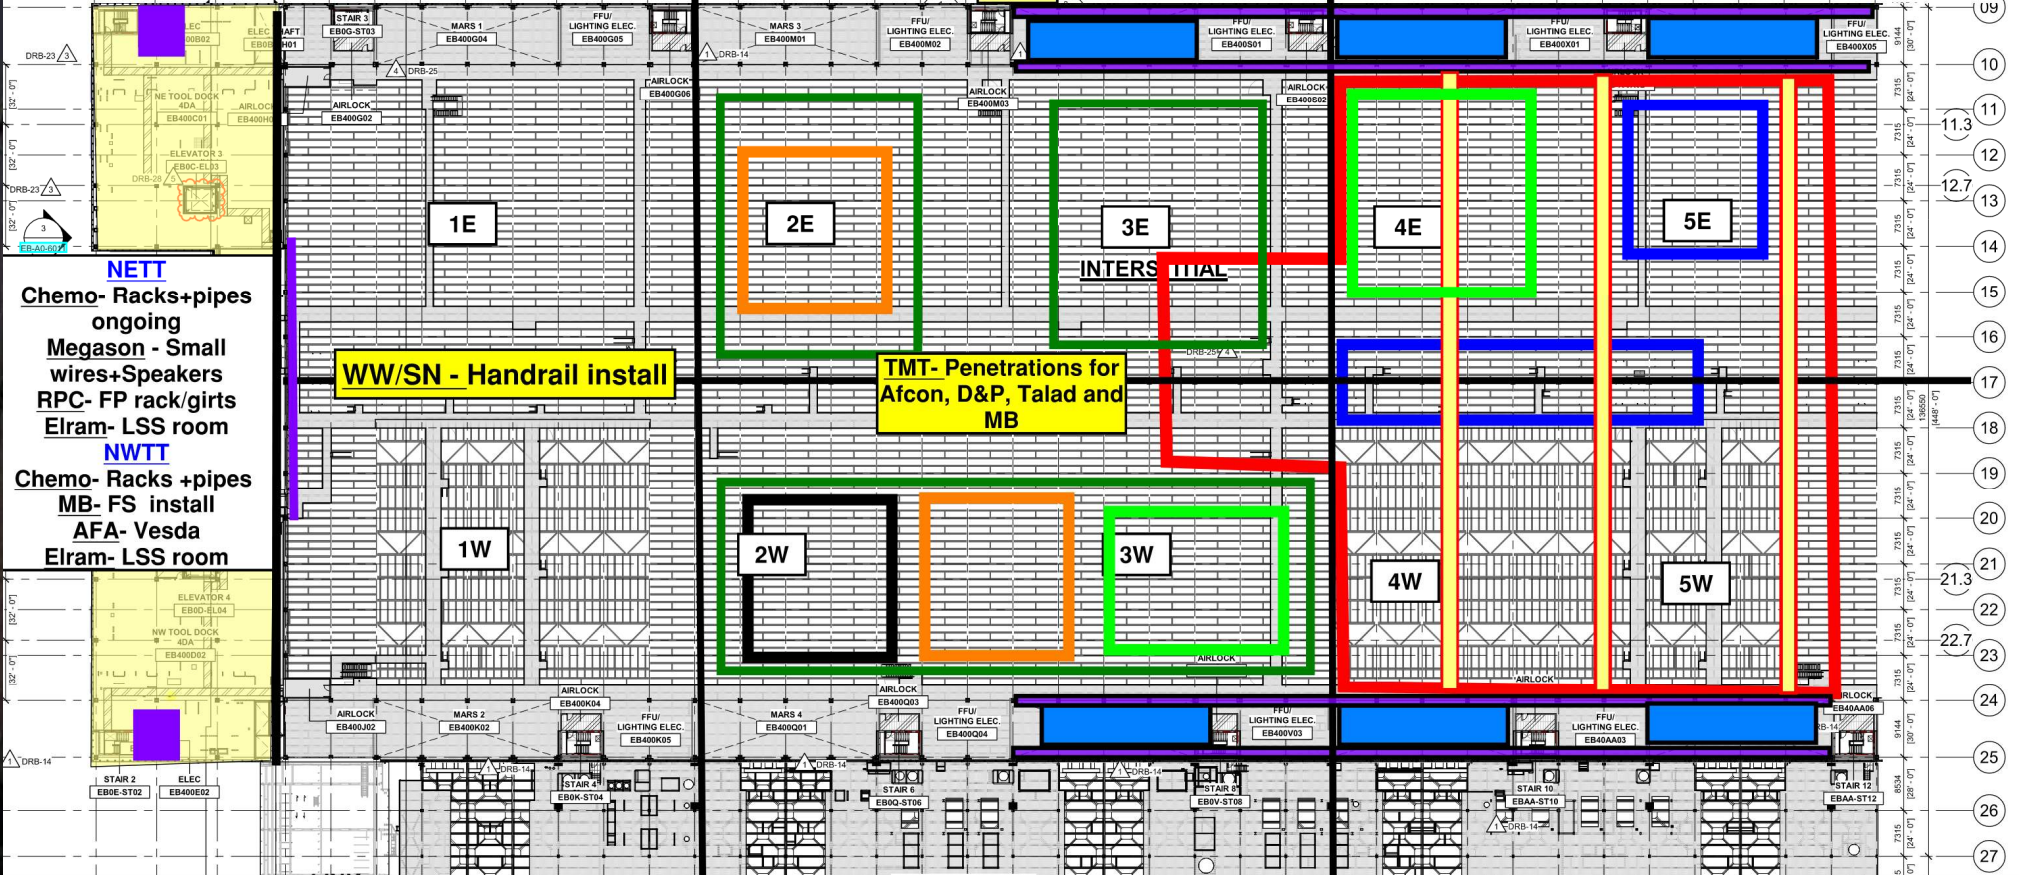

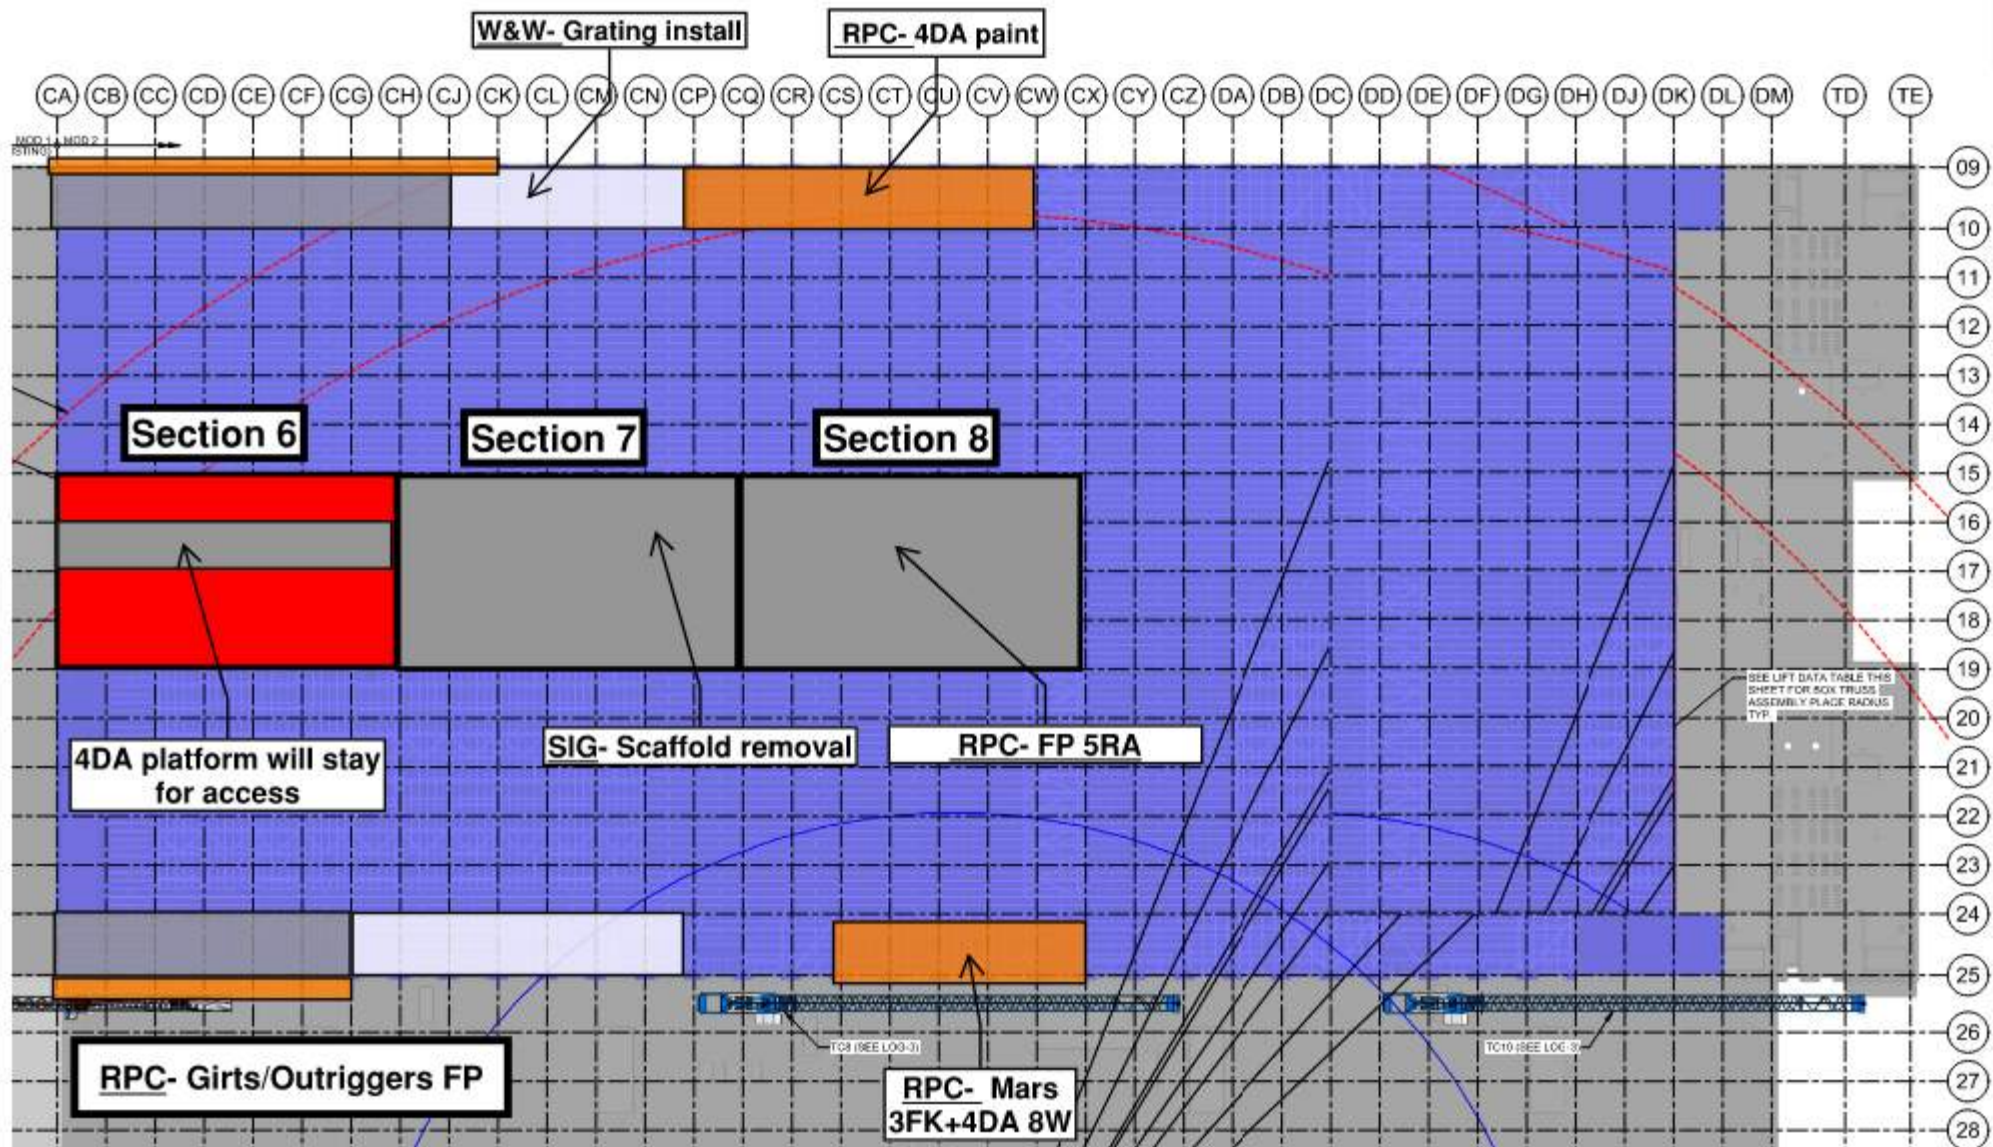


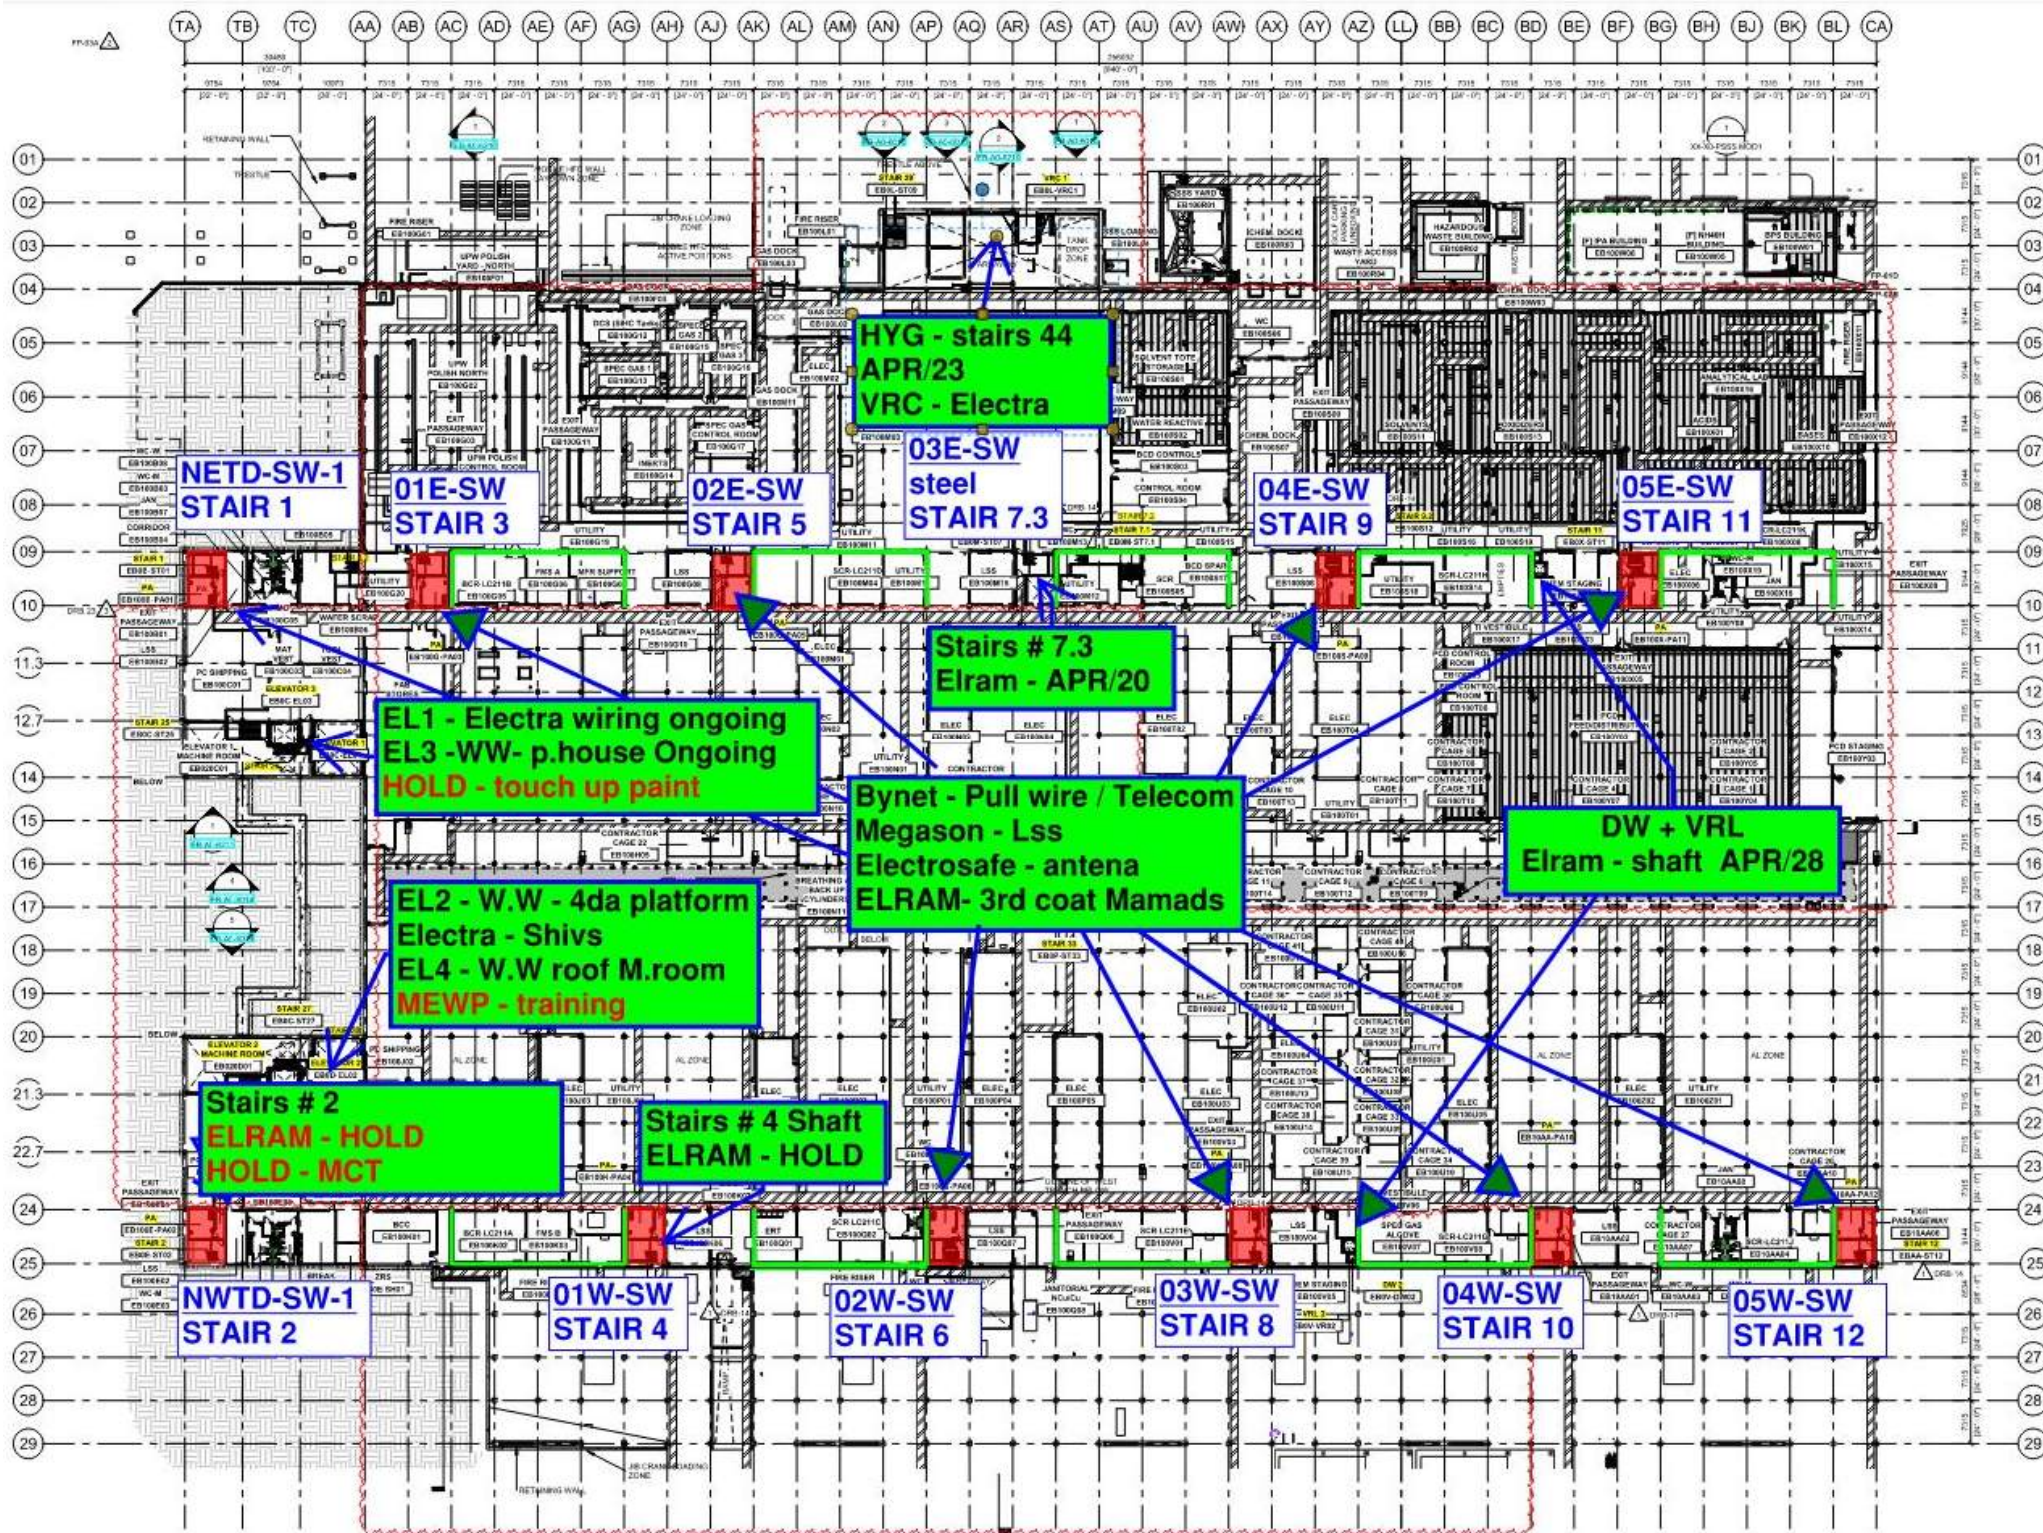

Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

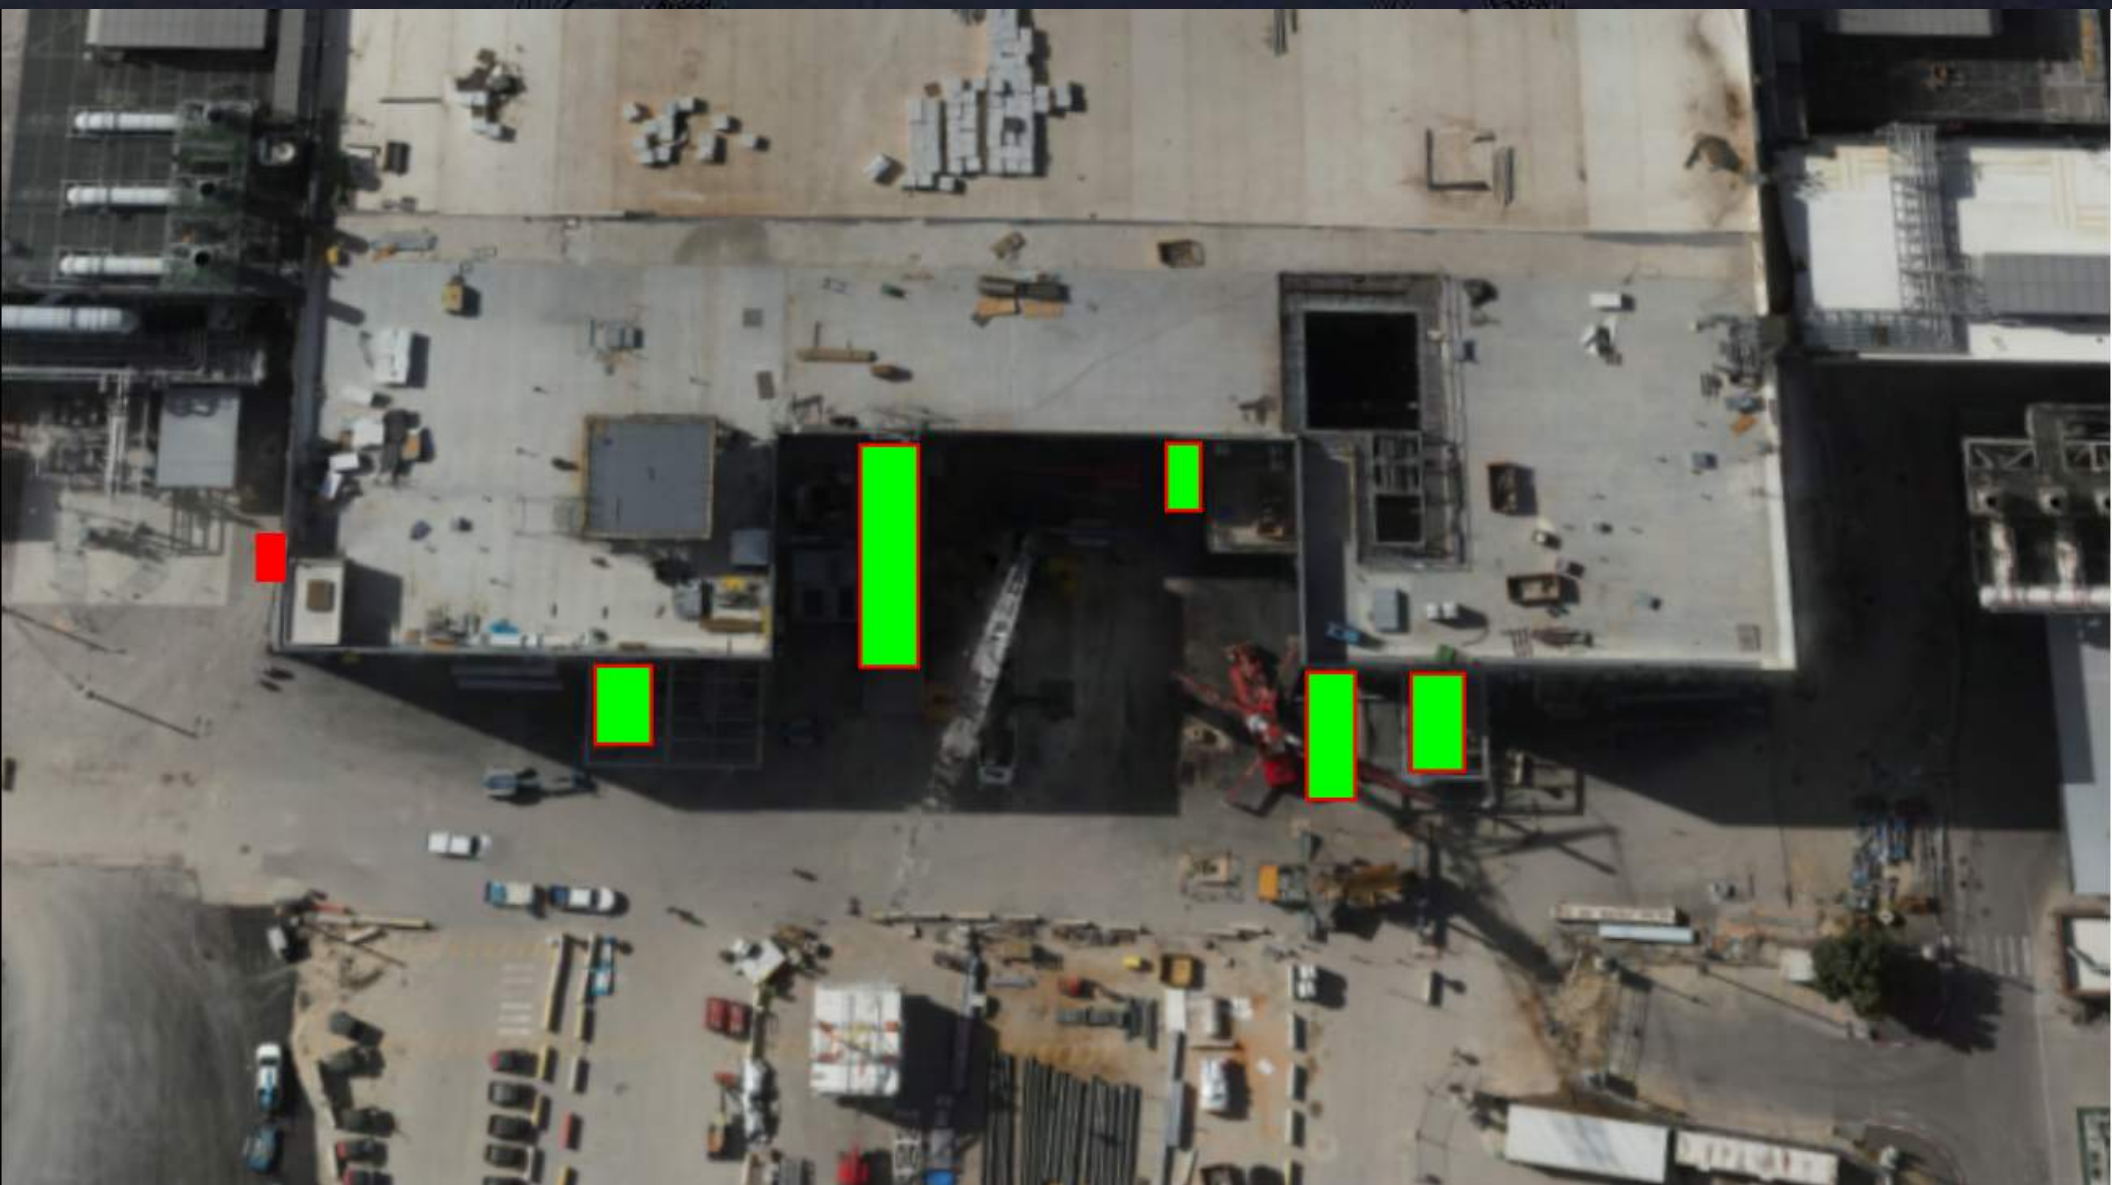


MOD 2 WESTSIDE GIRTS/SIDING

- READY FOR GIRTS
- INSTALLING GIRTS
- READY FOR PANELS
- PANELS INSTALLED

2602/ 2601	M I M O	2612/ 2611	MIMO 2622/ 2621	2632/ 2631	2642/ 2641	2652/ 2651	2812/ 2811	2822/ 2821	2832/ 2831	2842/ 2841	2852/ 2851
---------------	------------------	---------------	-----------------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

MOD 2 EASTSIDE GIRTS/SIDING

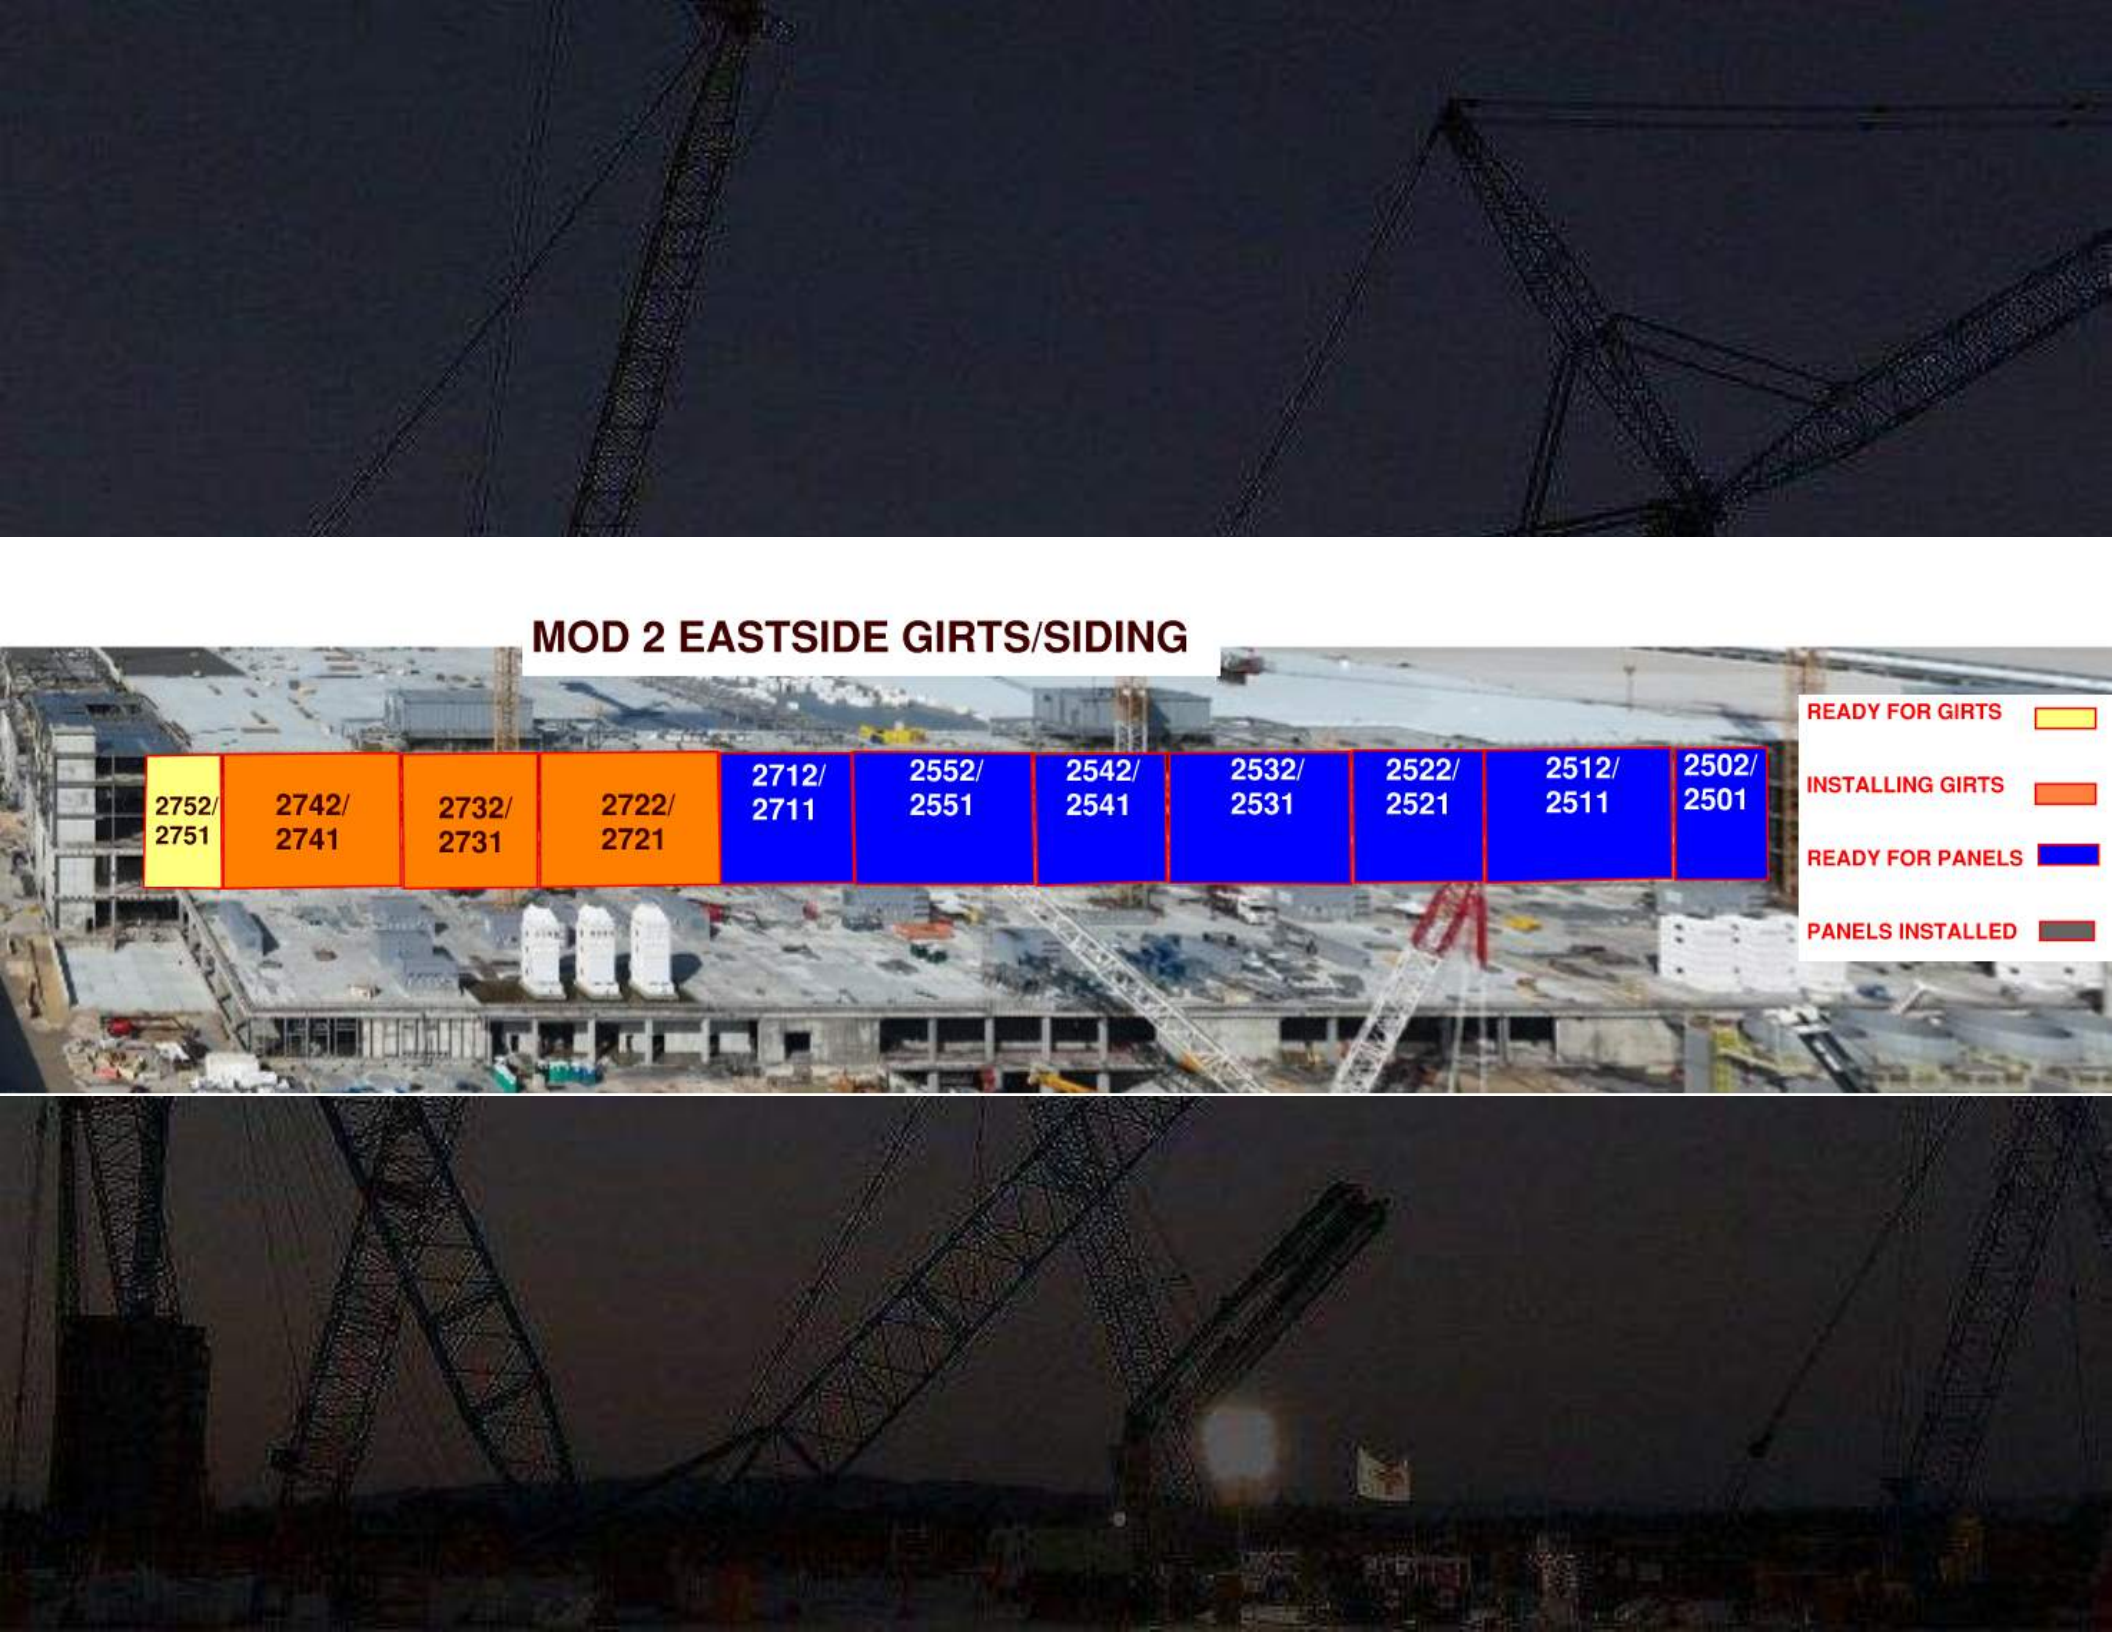


2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

PSSS.1


Utility Level
1YA

PSSS Roof
2SA

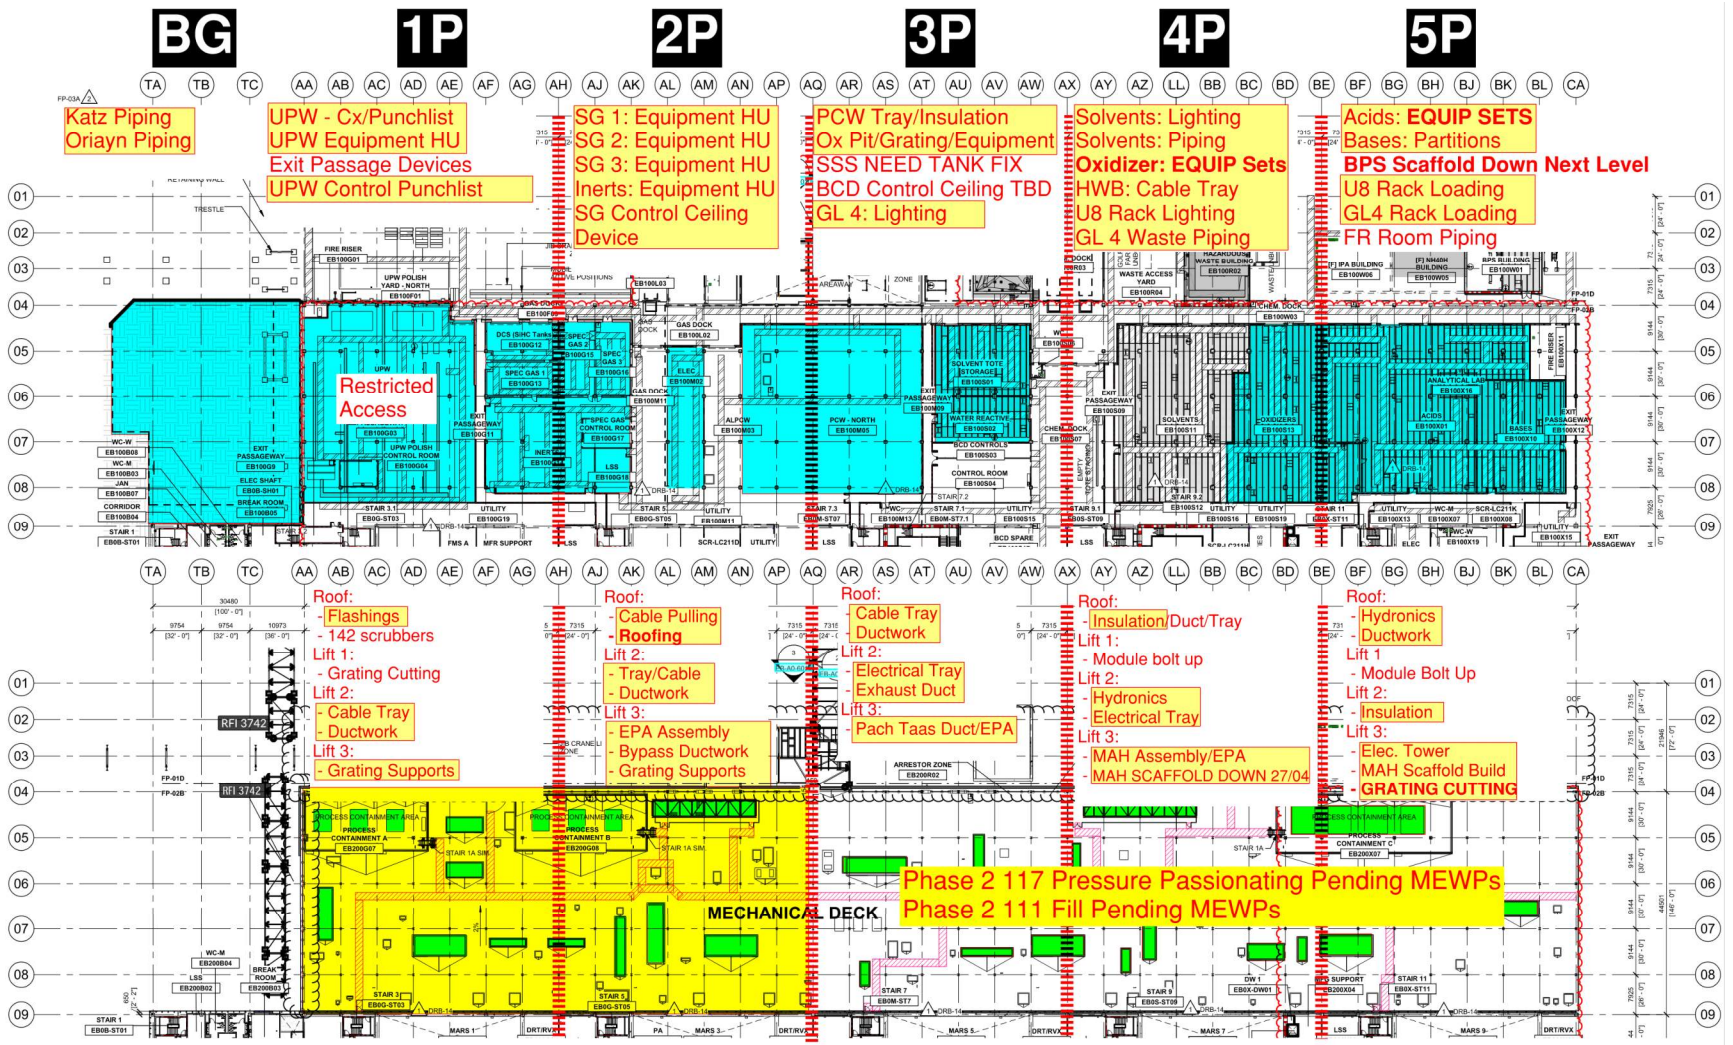


PSSS.2

Utility Level
1YA

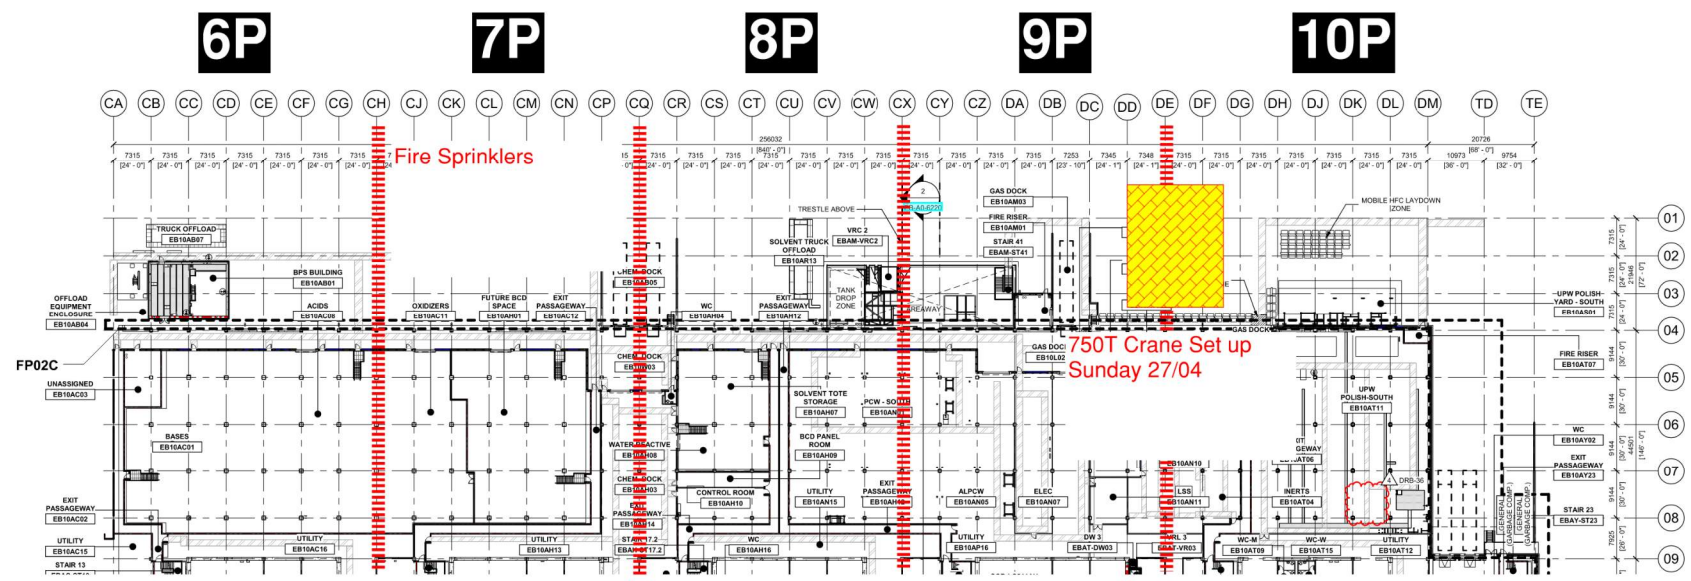


PSSS Roof
2SA

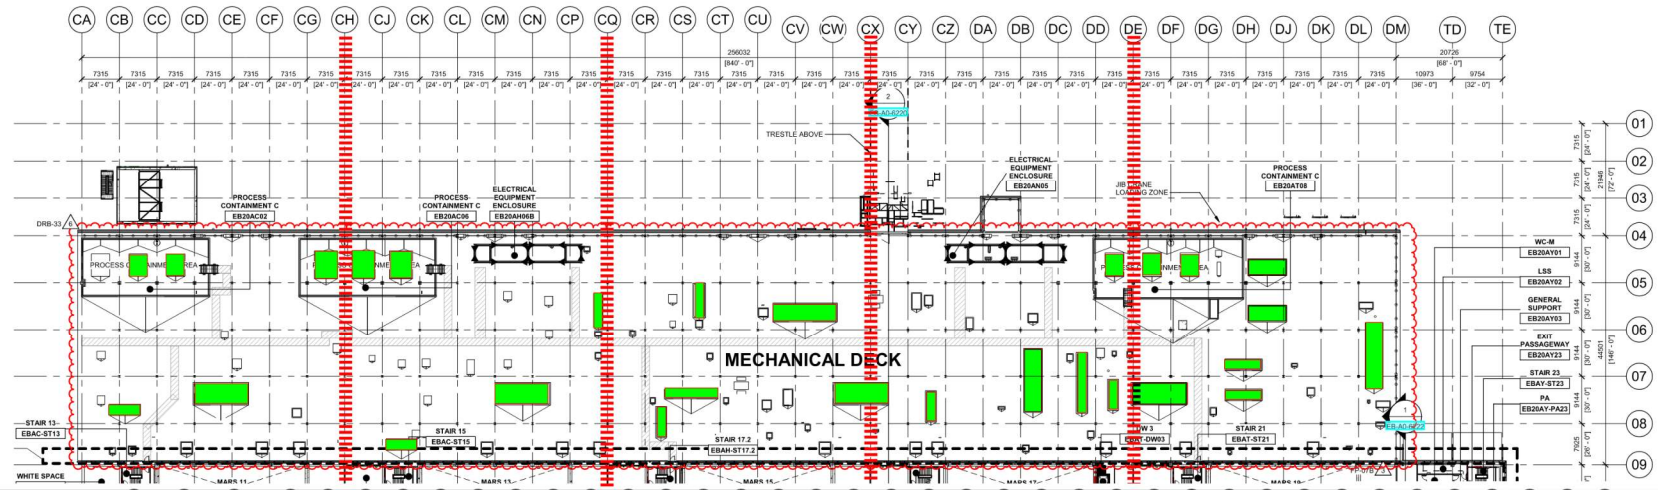


PSSS Pressure Tests

PSSS Roof
2SA

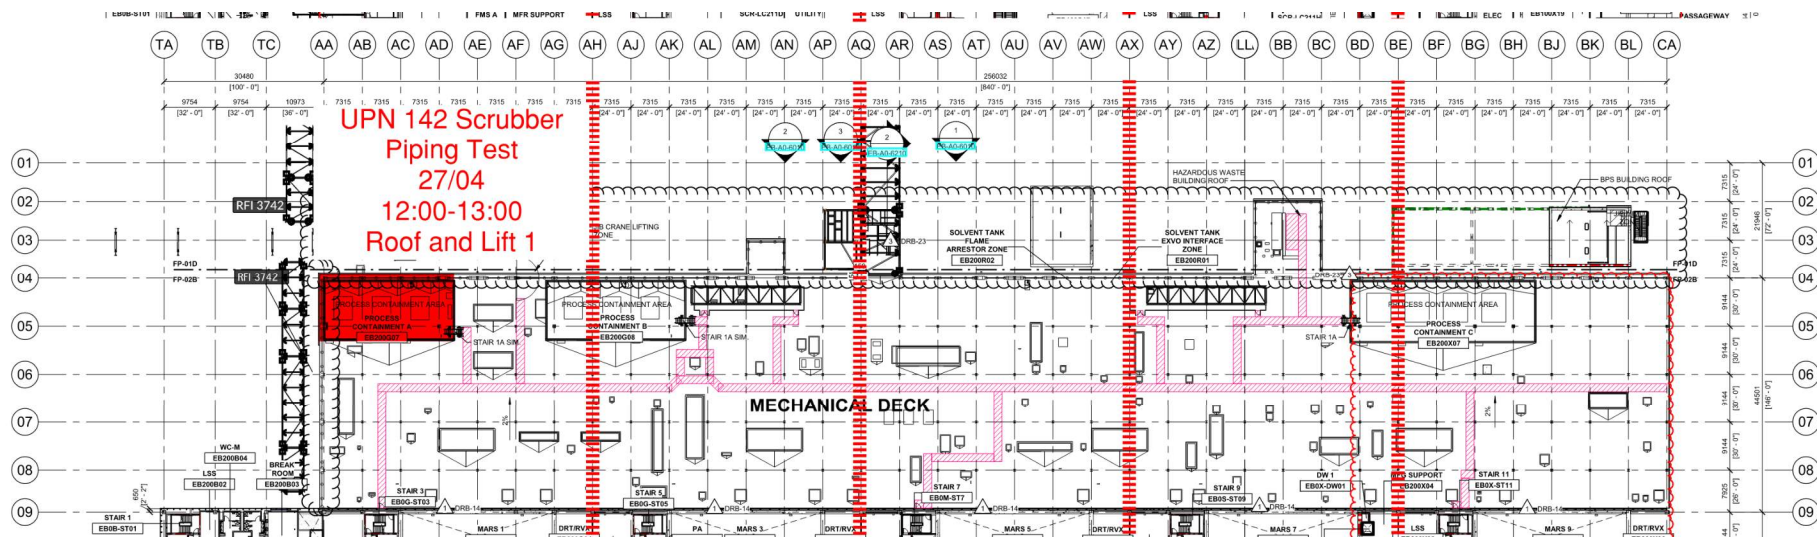

BGY GN2 Purging

21st-27th
continuous
noise
BGY West
Canopy
Closed

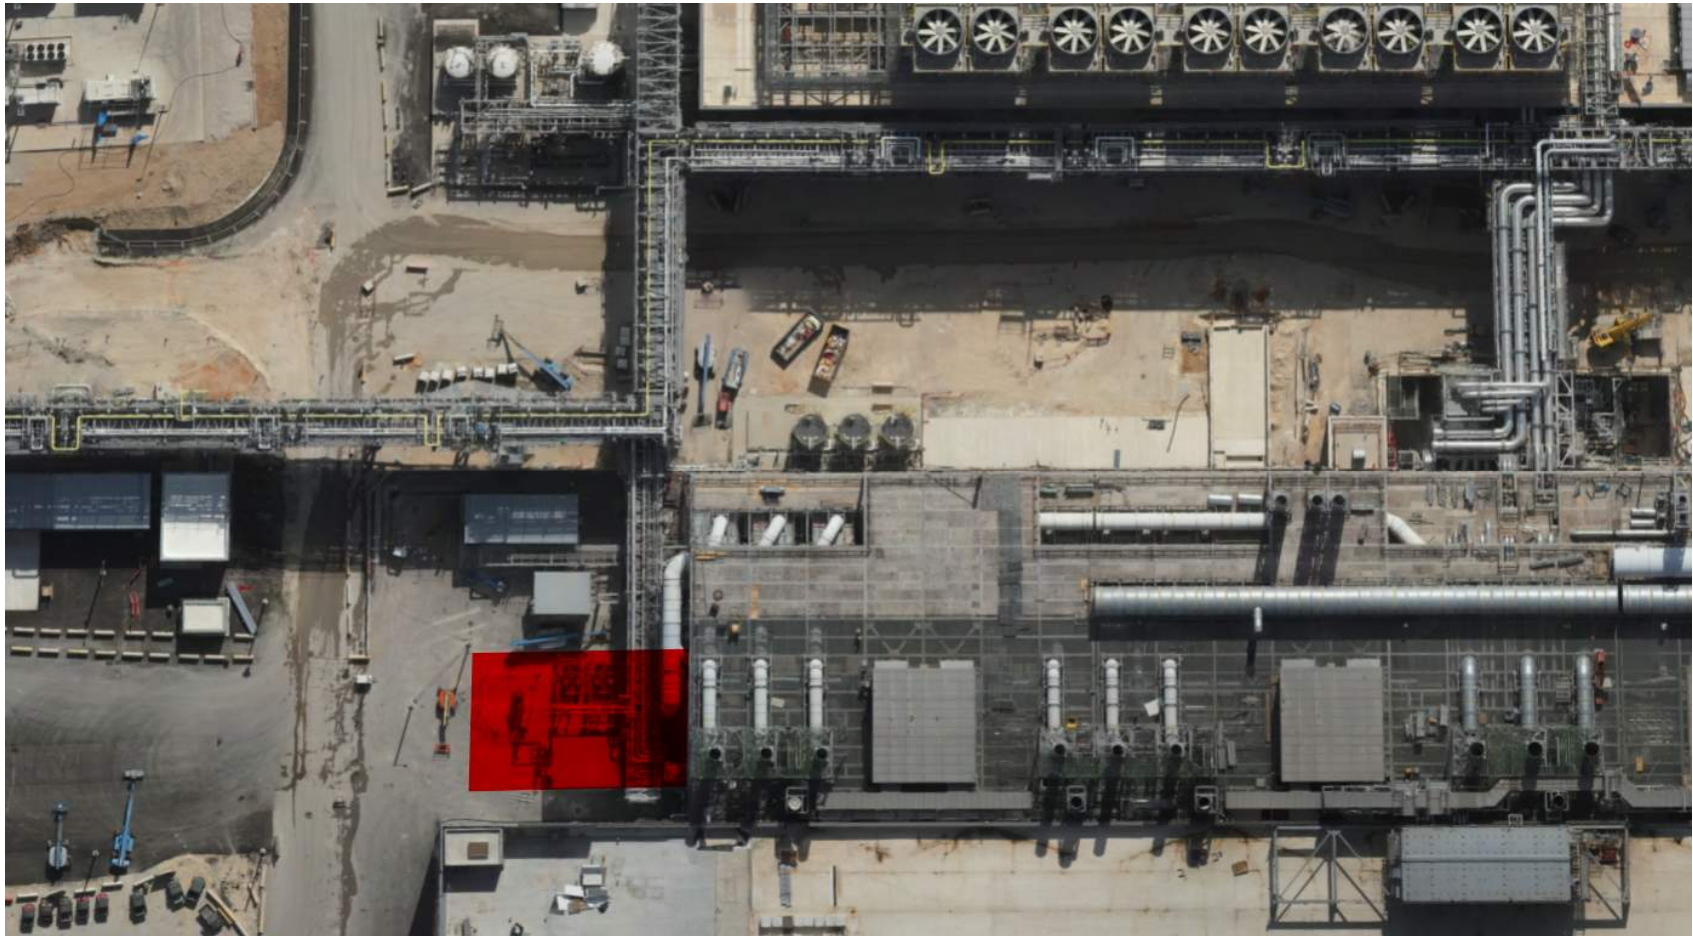


WJG – UL

* Carmel Bidud - erection of scaffold for flashing measurements and installation.

*Lesico - welding and grouting pipe support

* W&W - welding connections to MOD2 on CA line

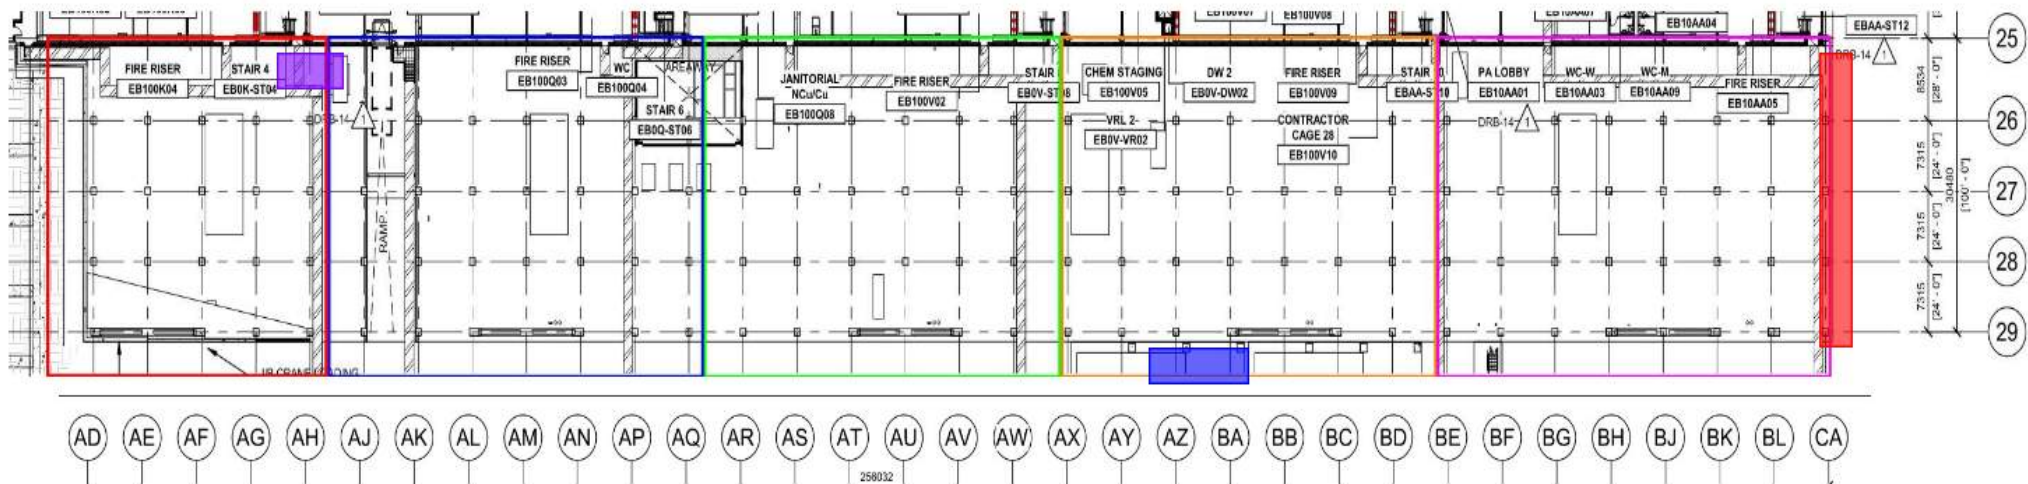




WJG – Lift 2

* Taper tech - fixing planking after stiffeners installation
* Chemo - continuing insulation

* Taper tech - opening planking for stiffeners installation

* Chemo - working on connections OF upn 117 AND 111 to MAH 101-7/8

* Afcon - installation of cable tray underneath MAH and doing cable pulling to VFD + working inside VFD

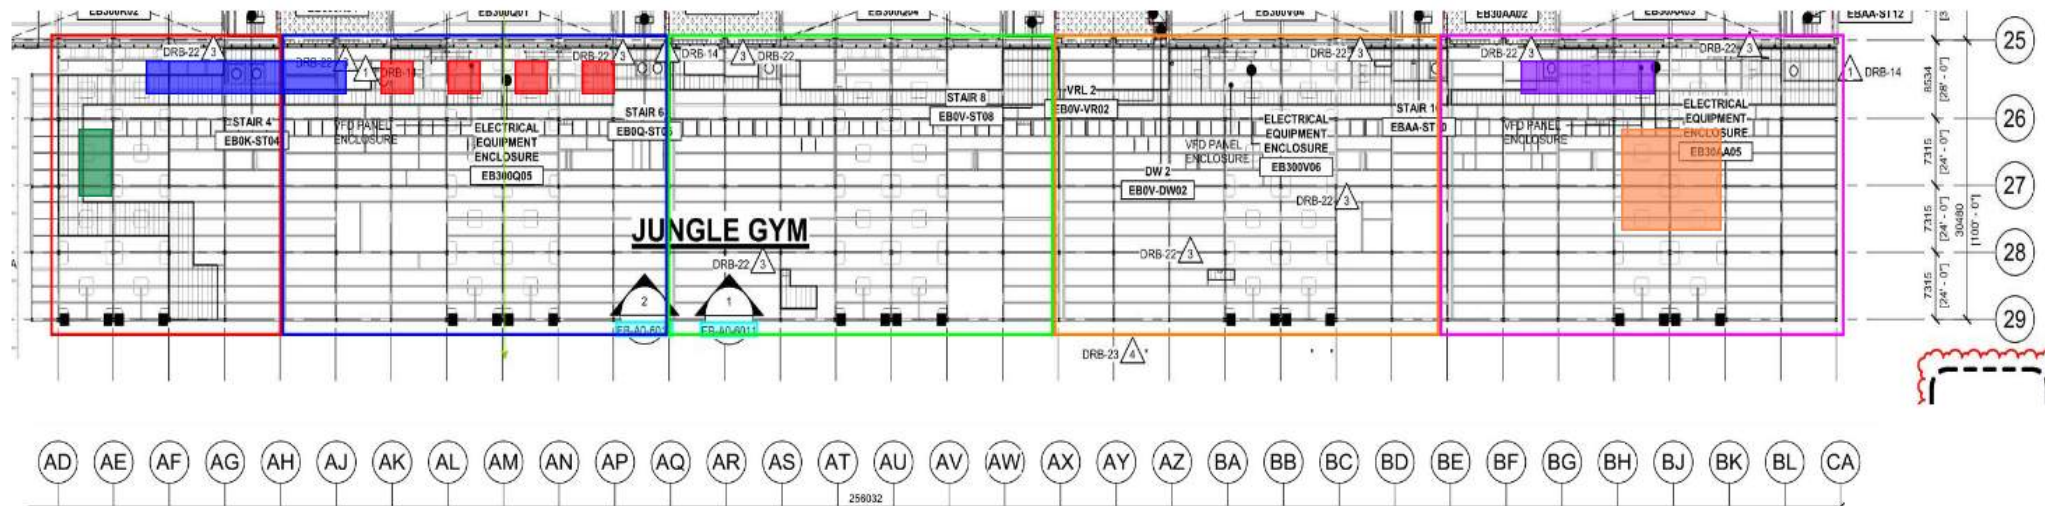


WJG – Lift 3

* SN - installing and welding penetrations supports

* Taper tech - performing planking penetrations and removing ramps for permanent handrails
* SN - handrails installation




MEWP Scheduled for Intel inspections
April 22:
BARZEL 3144
BARZEL 2784
BRAND 3667
BRAND 3731
BRAND 1843

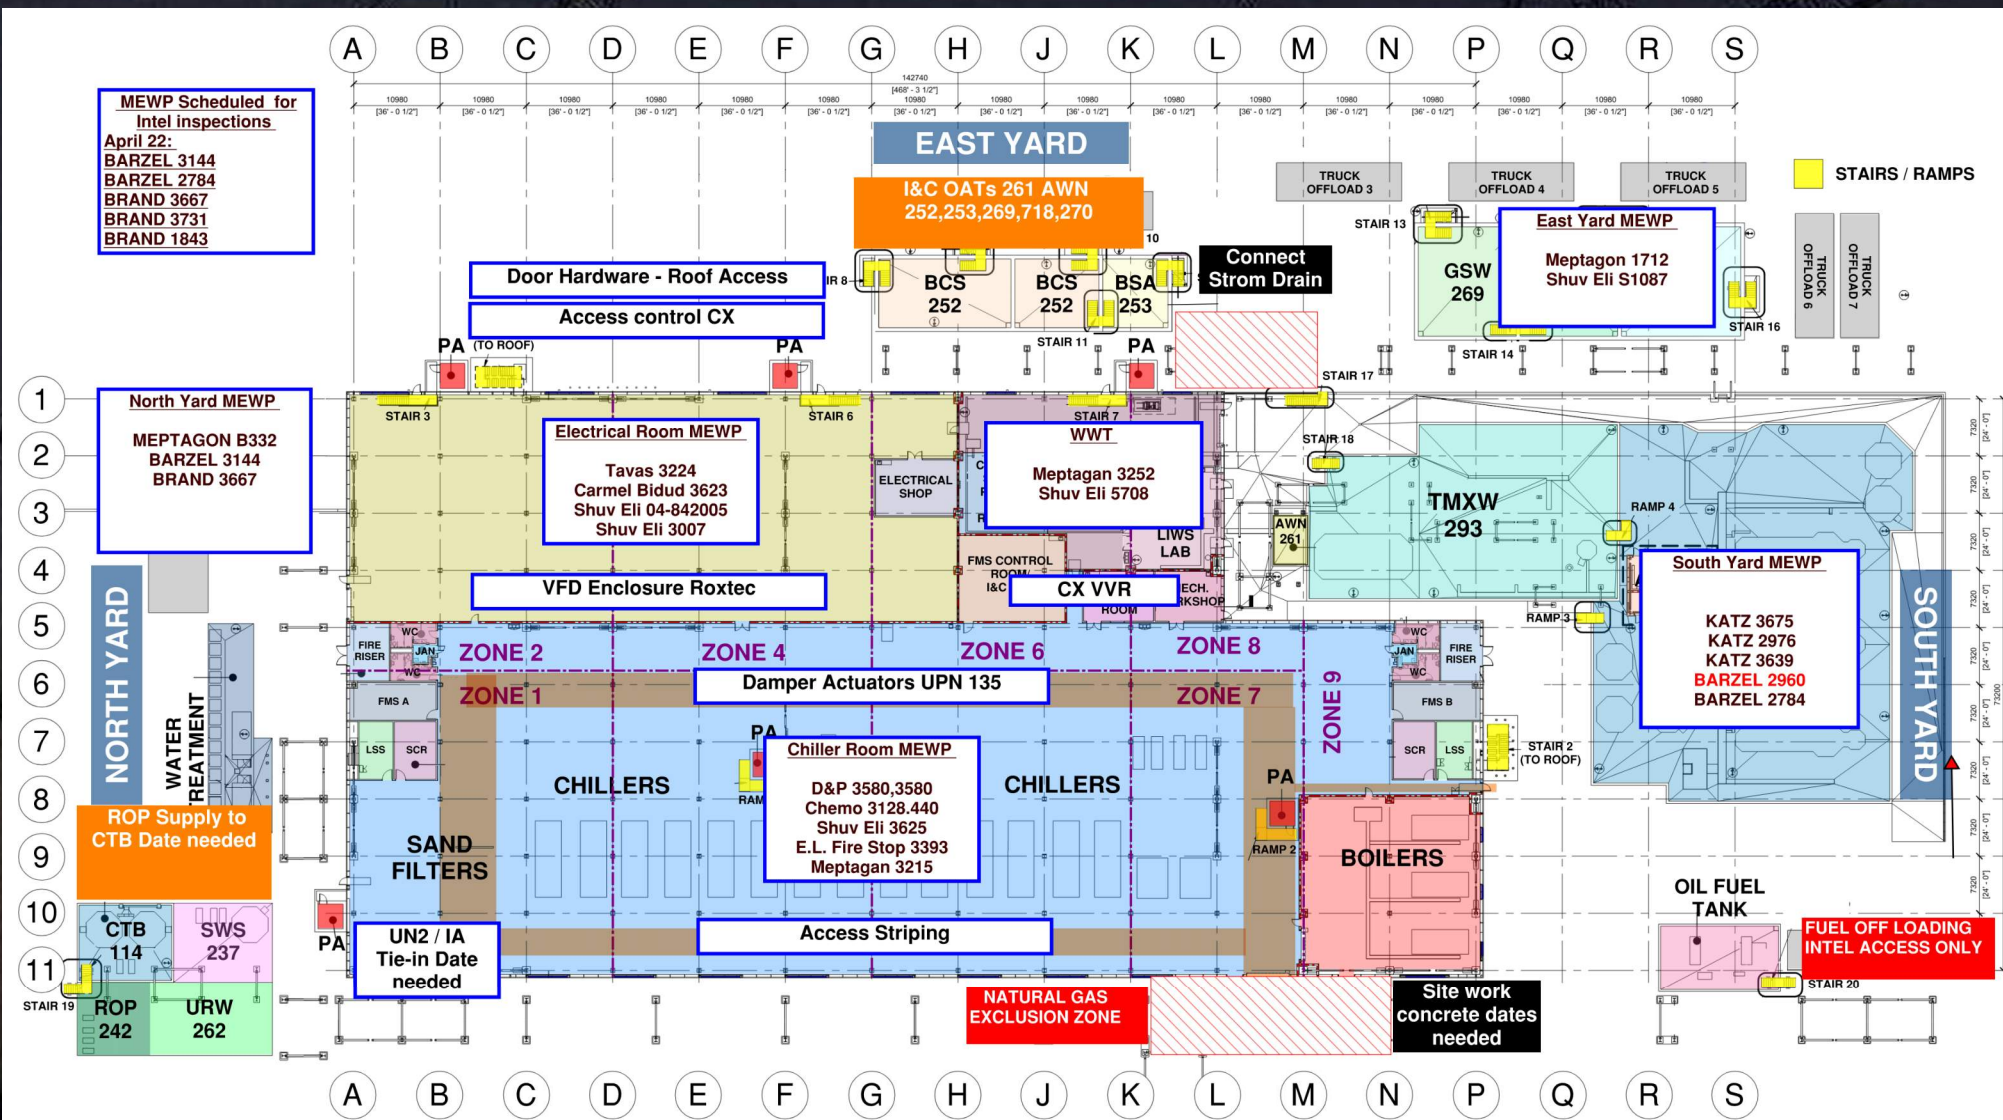



CUB 1 – EXTERIOR/ROOF

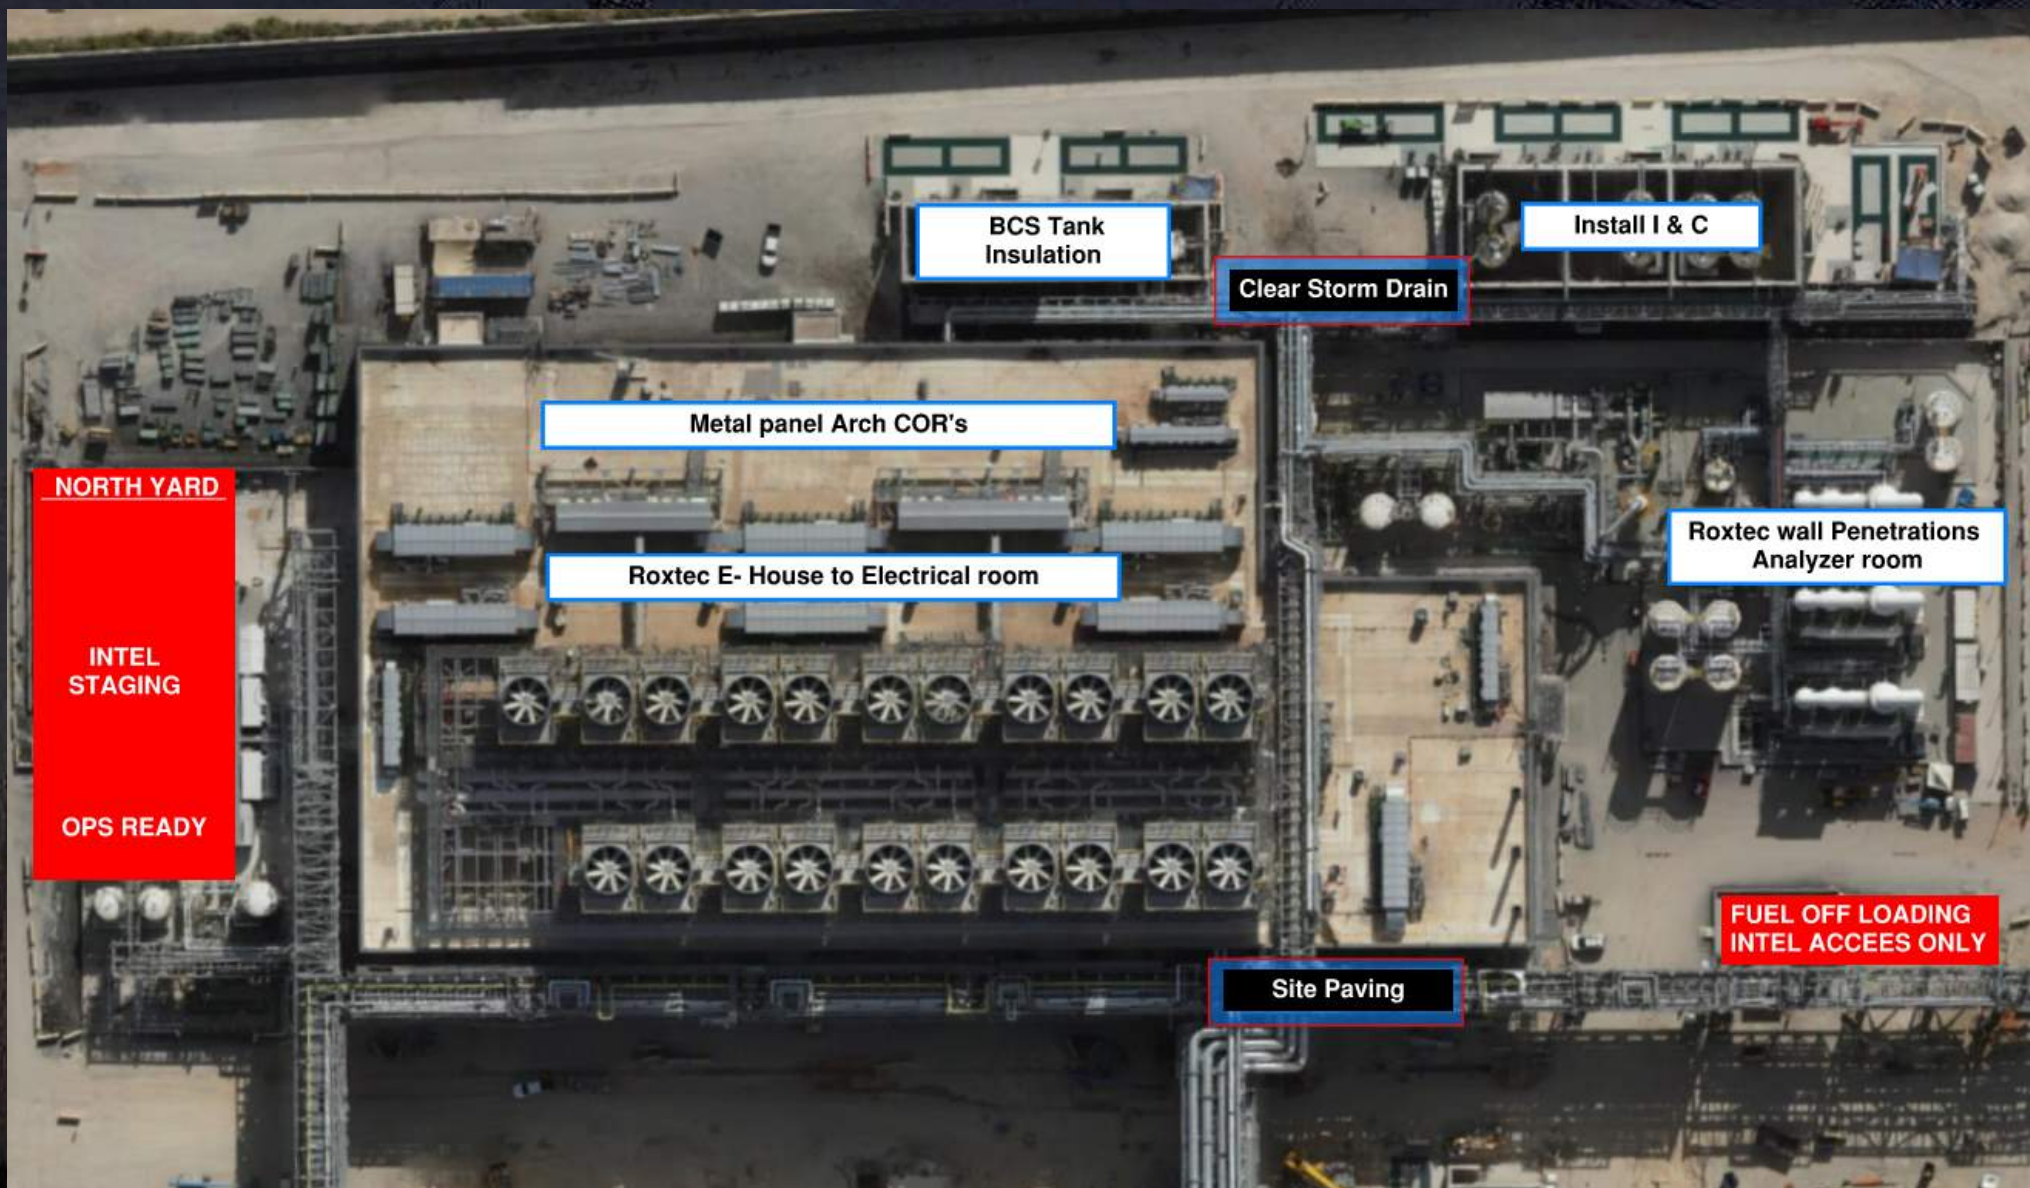

CUB 2- Load in & H&T



**Plinth Install
WW17-18**

**GIS39 Install
WW18-19**

**MEWP Scheduled for
Intel inspections
April 22:**
BRAND 1843

Chiller RM MEWP
Chemo-3451,354,3123,2688,1883,3270,176809,1023,3600,
2291,3148,176817. HR179,HR179.
SK - 176918,3730
KATZ-358
Sami-768,2718
D&P-2696,3495

Electrical RM MEWP
Shuv Eli - 1600,1519
Sami-4740,3751
D&P-2786,3622

HFW MEWP
Chemo - 176912, 3445
KATZ - 176812, 749
Shuv-Eli - 176788
D&P - 1013, 2696
AFCON 3810

North Yard MEWP
BRAND 1843
BRAND 1704

**Roof
Access**

**Equipment/Material
Access**

**Mamad
Access**

**Stair access to
High & Tight**

**AWN
261**

**WWT
CRC
WW
17-18**

Zone 3 Access March 27
Sami Najami 20d April 24
Afcon 20d April 24
SVE 12d April 15

Zone 2 Access March 9
Sami Najami 20d April 6
Afcon 20d March April 6
SVE 14d March 27

Zone 1 Access Feb 20
Sami Najami 20d March 20
Afcon 20d March 20
SVE 14d March 12

Zone 3 April 24 dismantle

Zone 2 April 24 dismantle

Zone 1 April 24 dismantle

Zone 7

**HFW
266**

**CRC
WW
16-17**

**Roof
Access**




**HFW
266**

**BCS
252**


**BCS
252**


**BSA
253**

MIMO

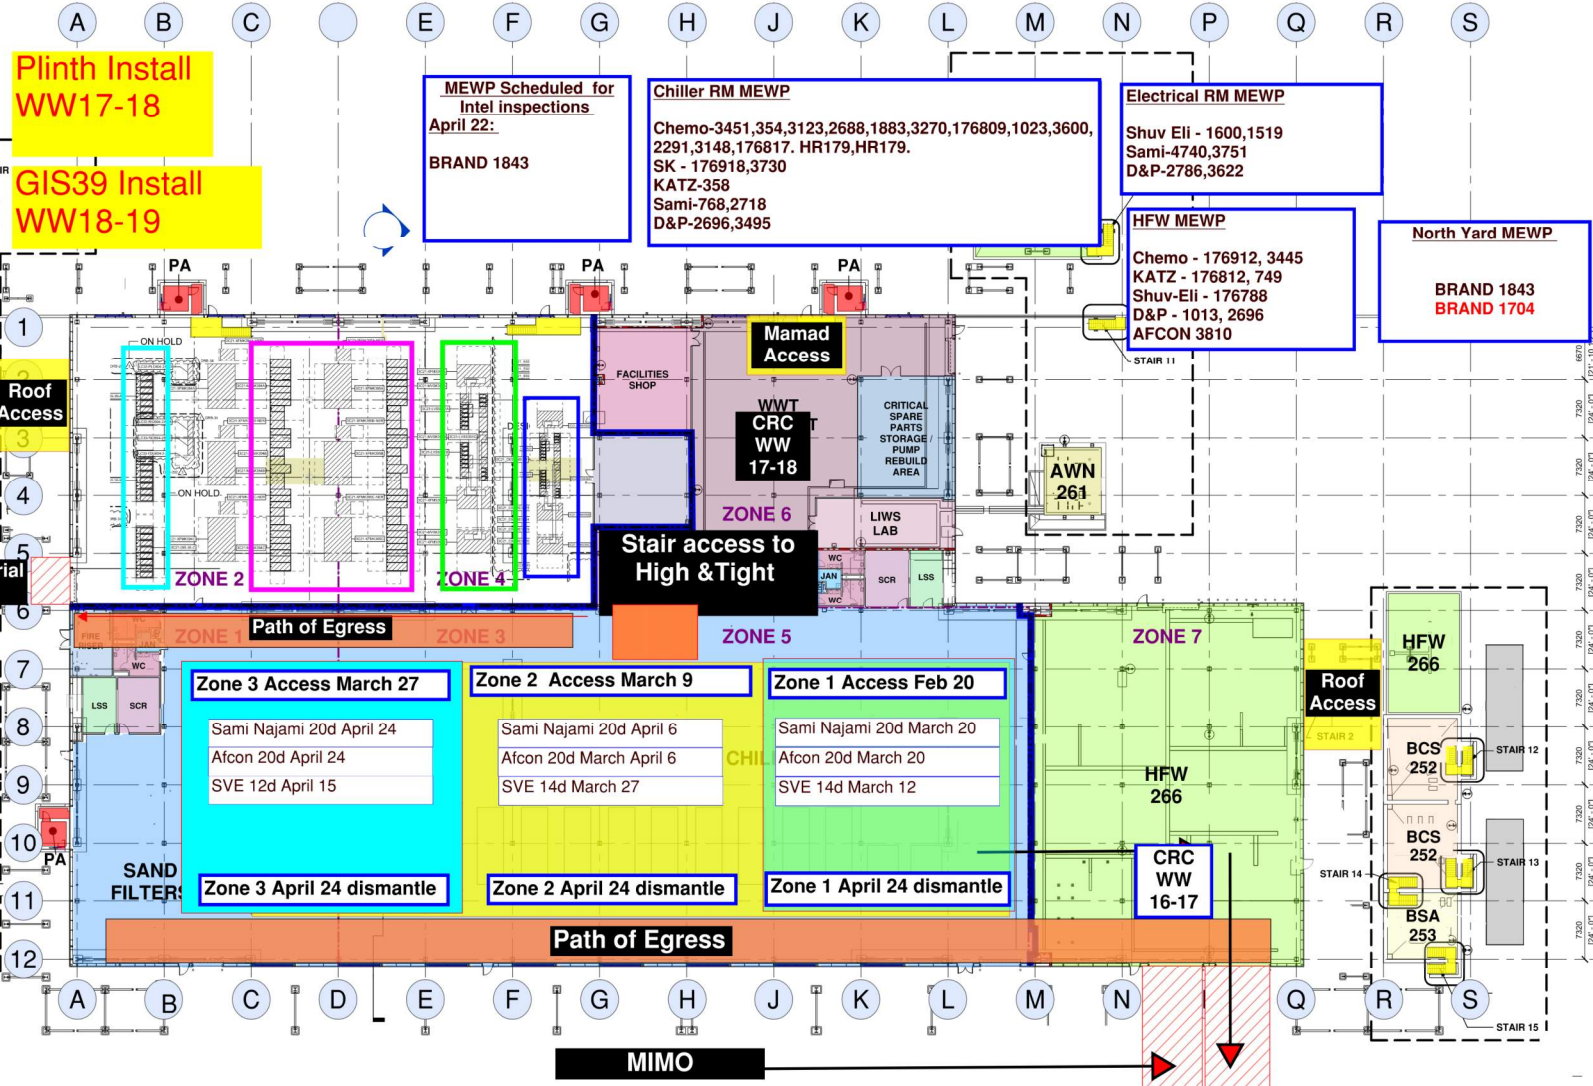



CUB 2- Trestles/Roof/Guardrails

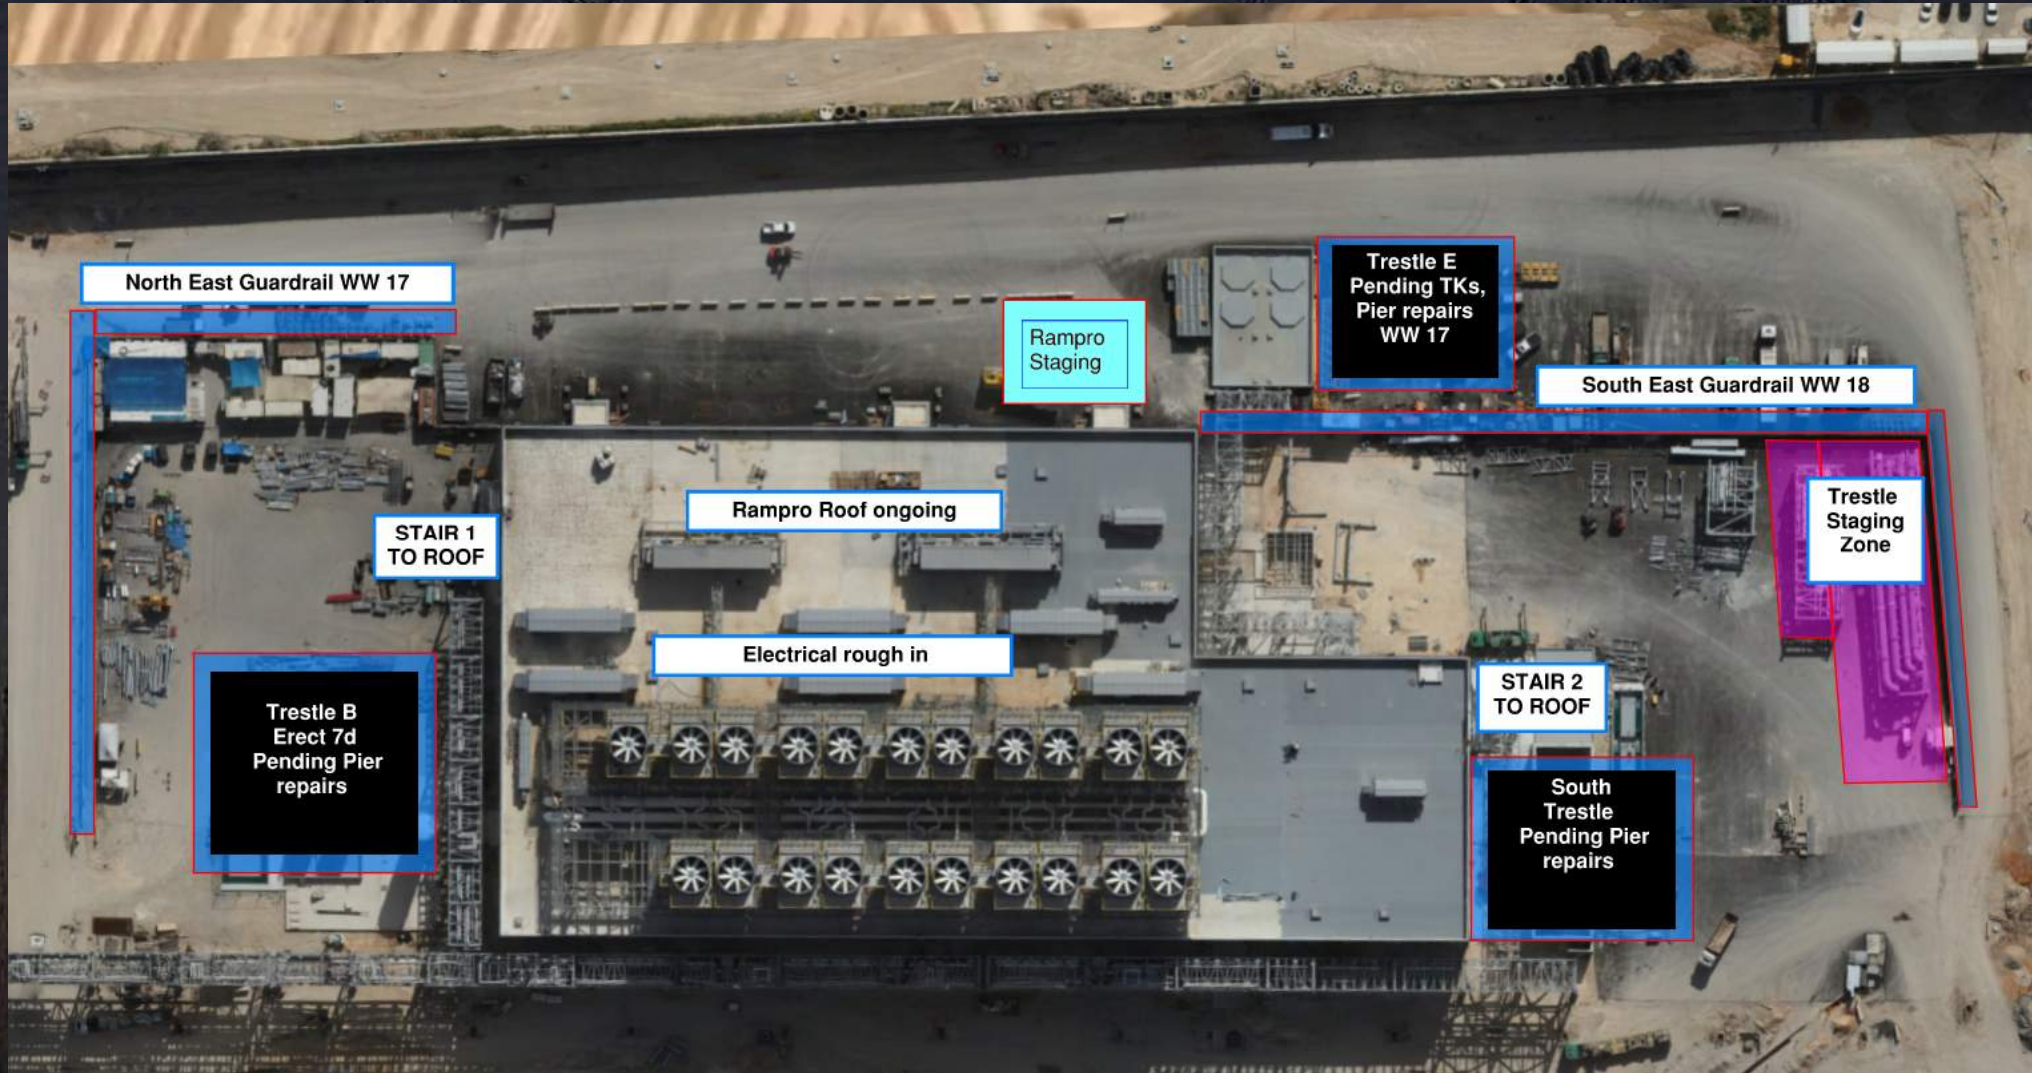



HOFFMAN CONSTRUCTION COMPANY

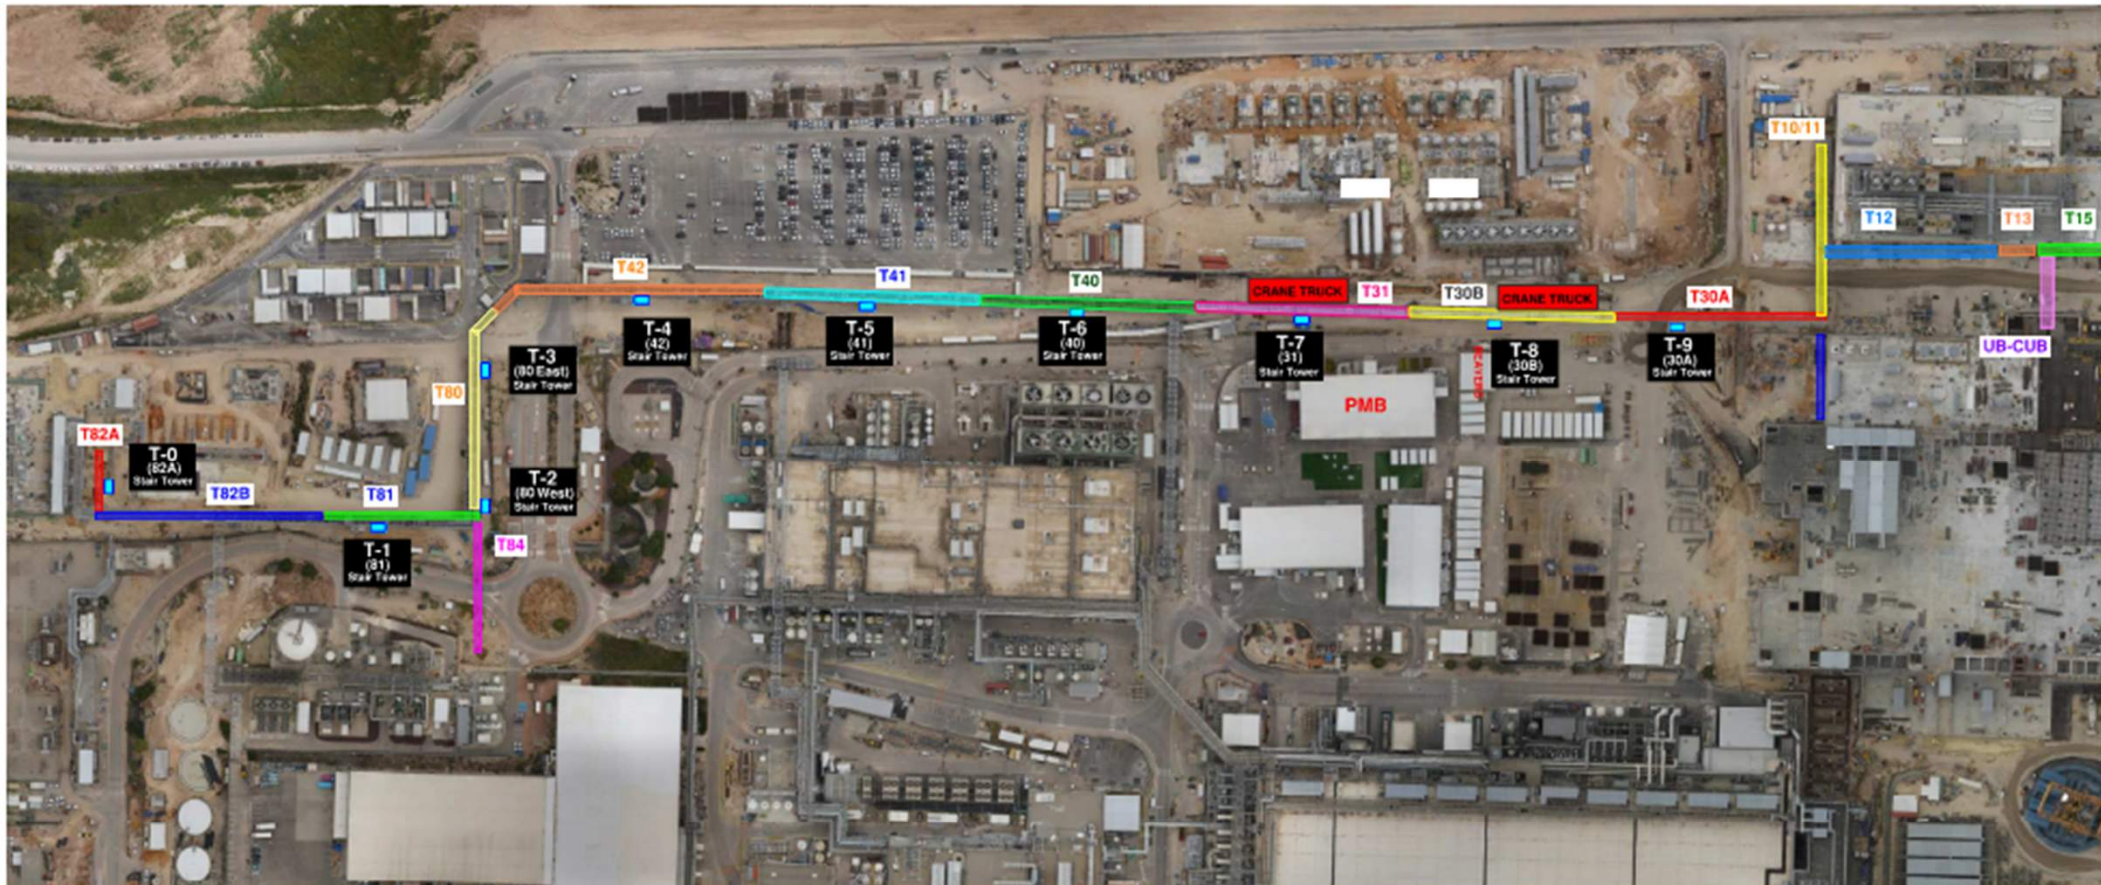

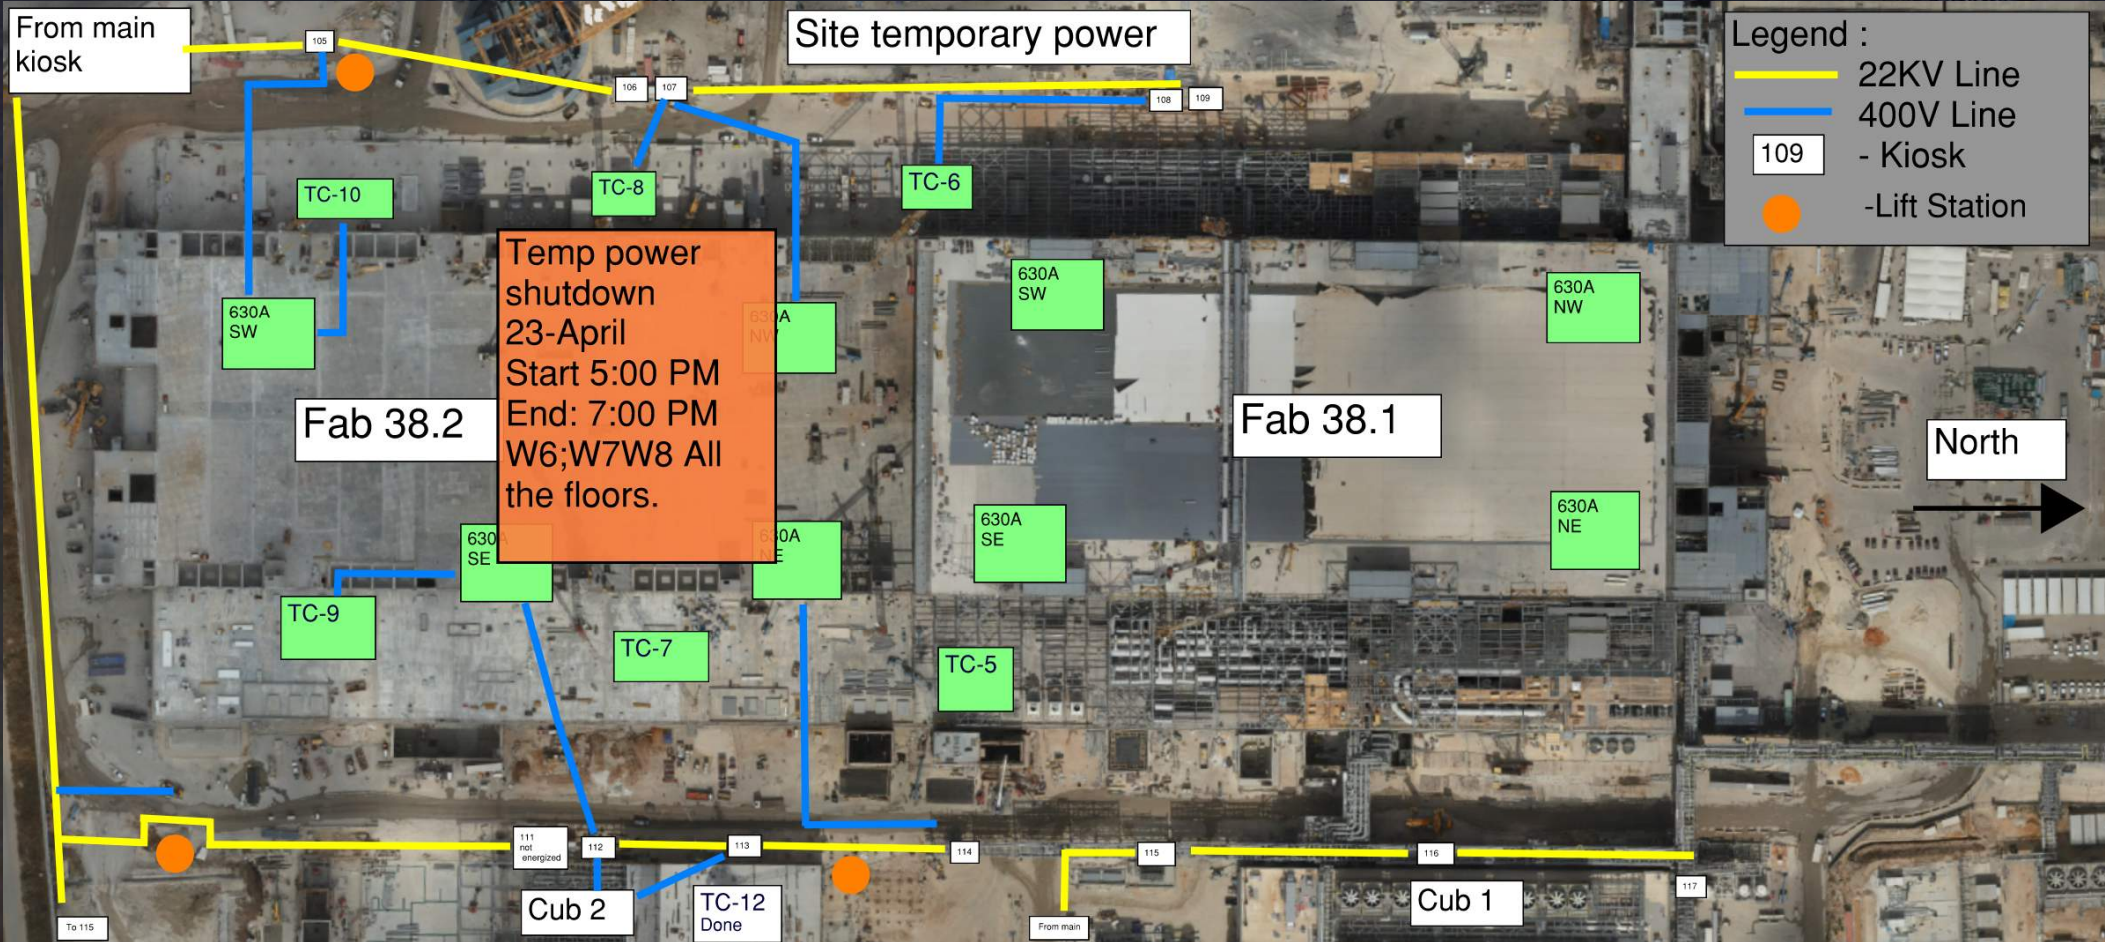




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

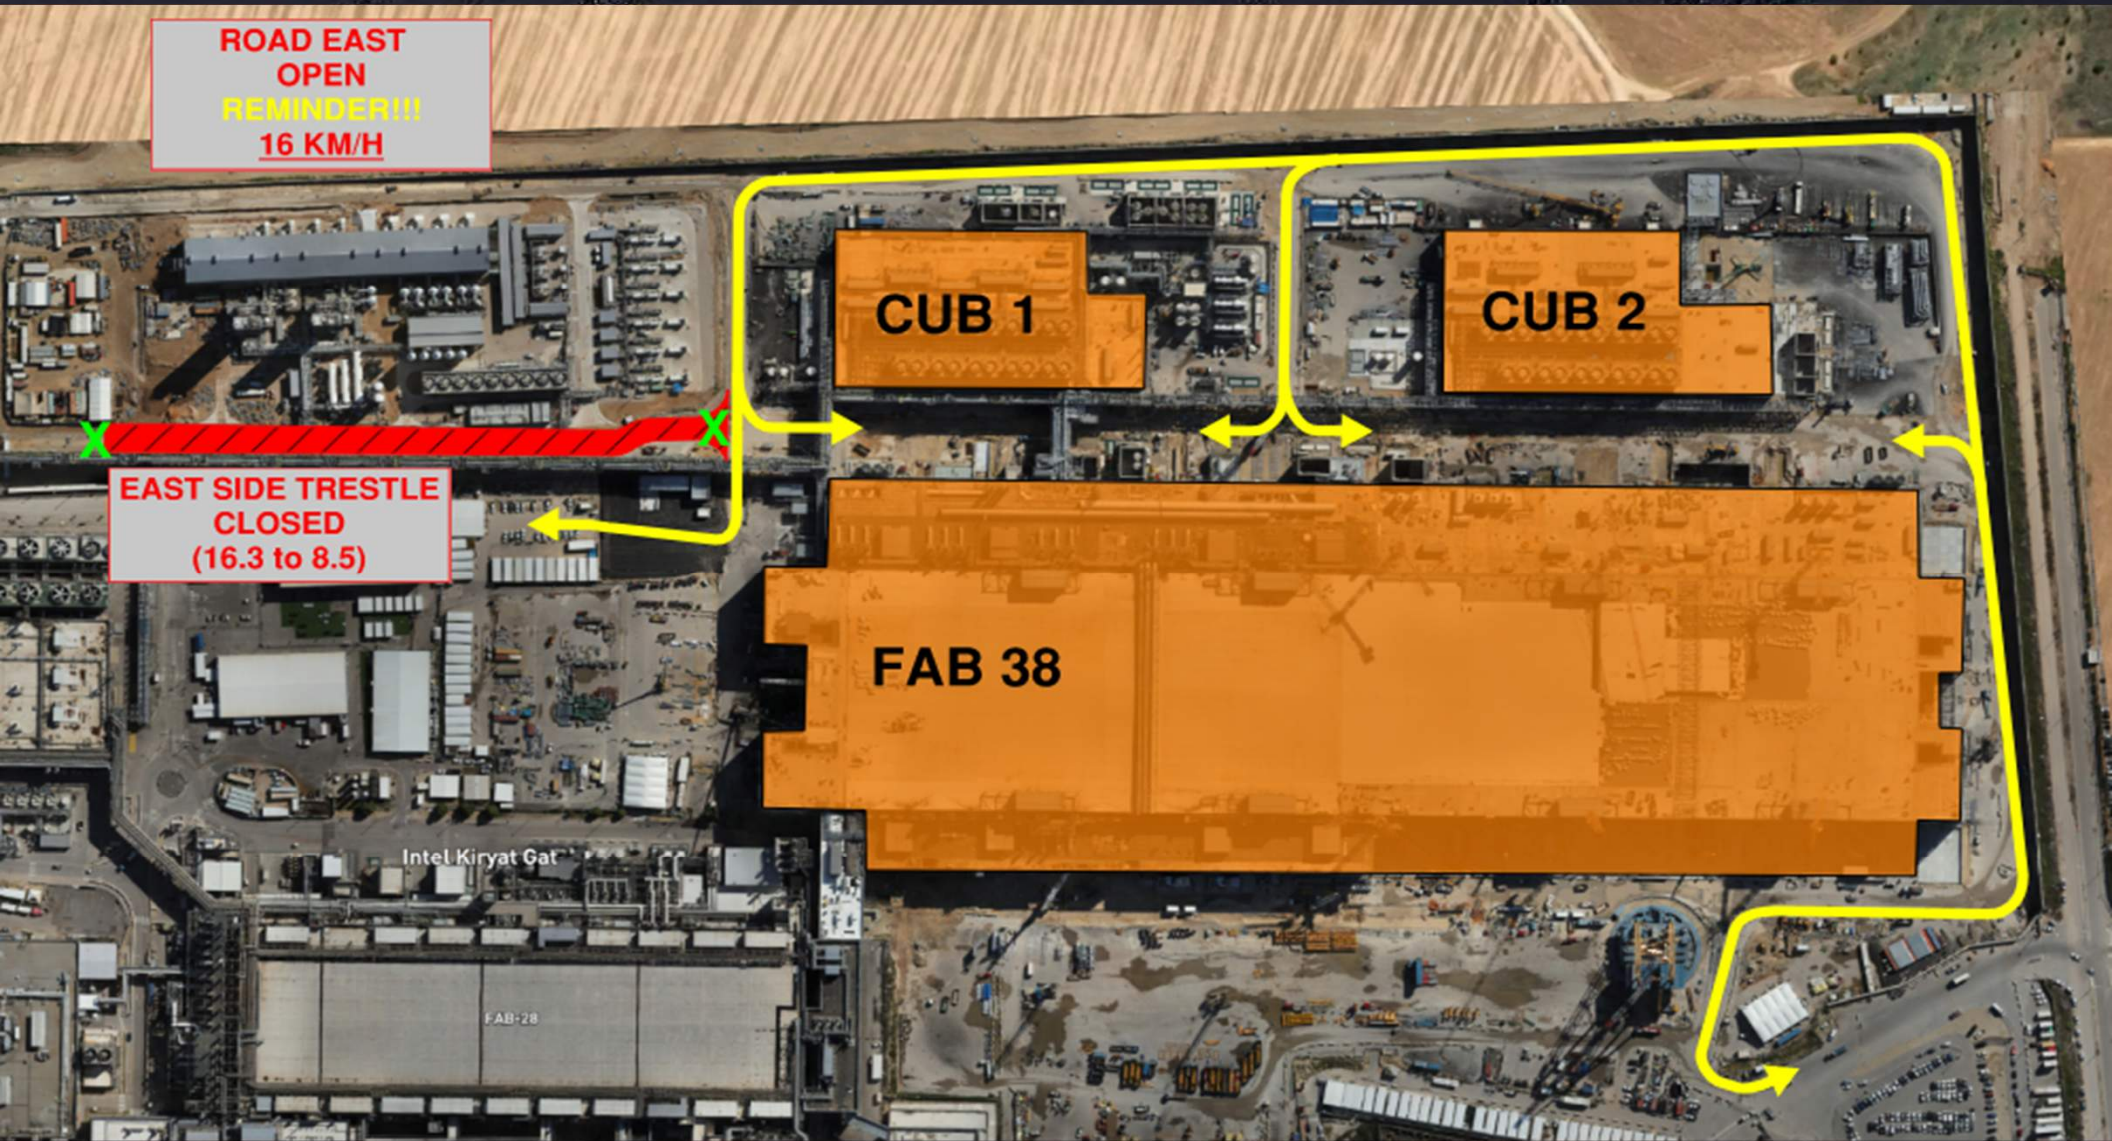



Daily Coordination Meeting


Site Logistics: North





Daily Coordination Meeting

Site Logistics: South

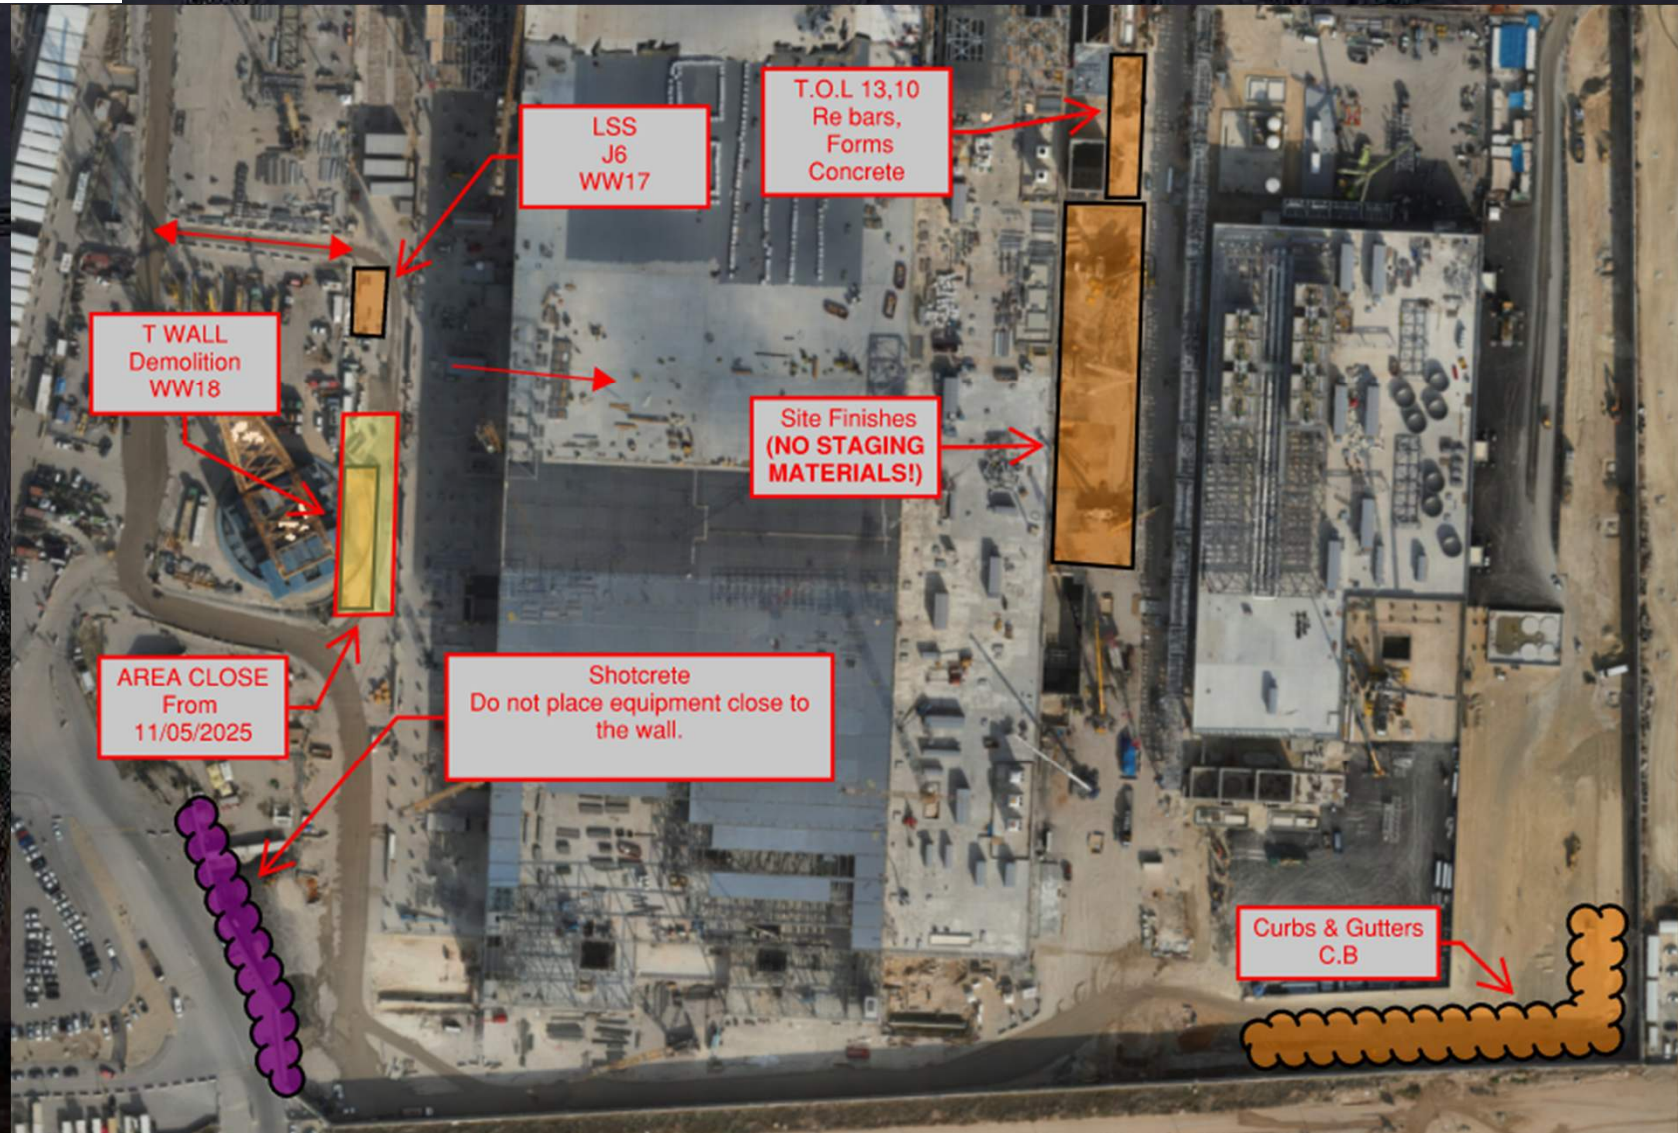



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

MAMAD Locations

MAMAD LOCATIONS (19-March-2025)

■ LARGE
■ SMALL
■ BUILDING






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

WATER BOTTLE FILLING STATIONS

WATER BOTTLE FILLING STATIONS

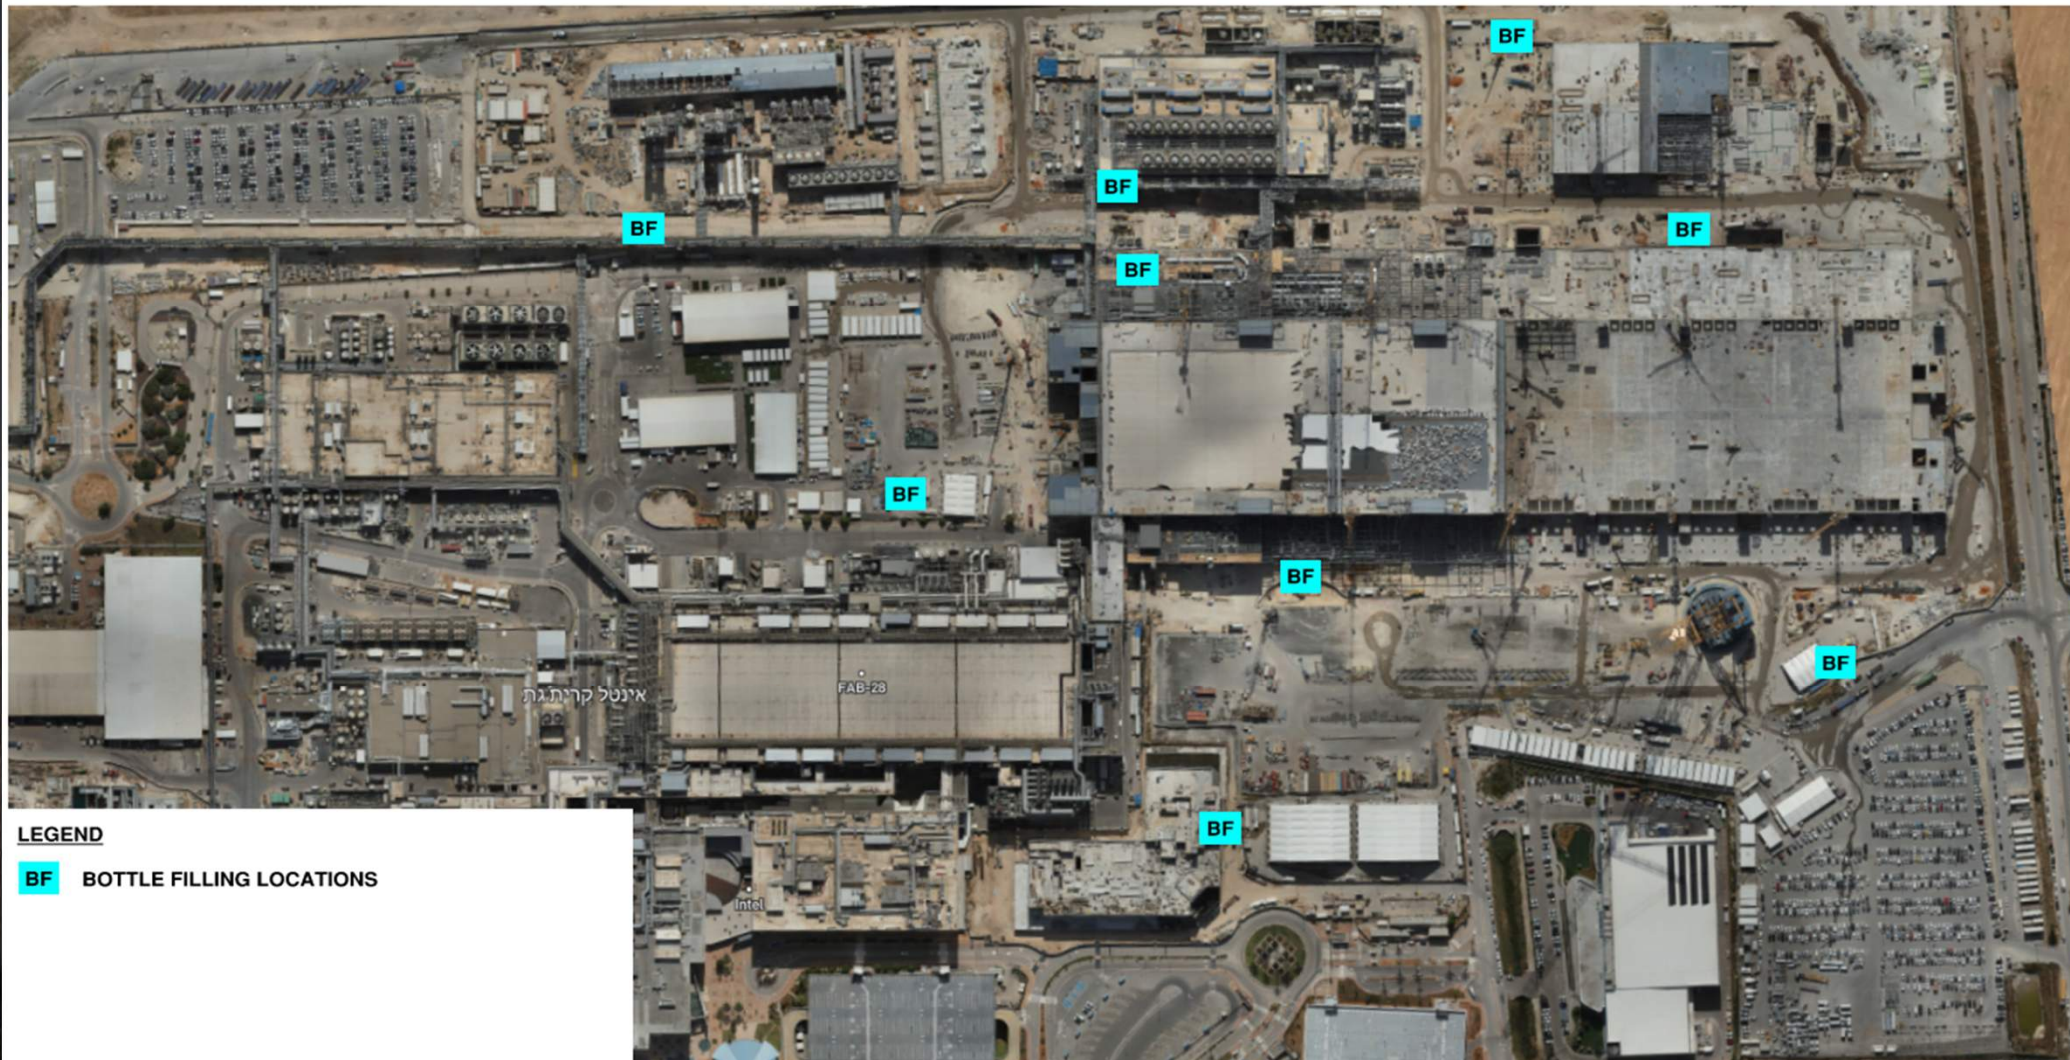


LEGEND


BF BOTTLE FILLING LOCATIONS



HOFFMAN CONSTRUCTION COMPANY

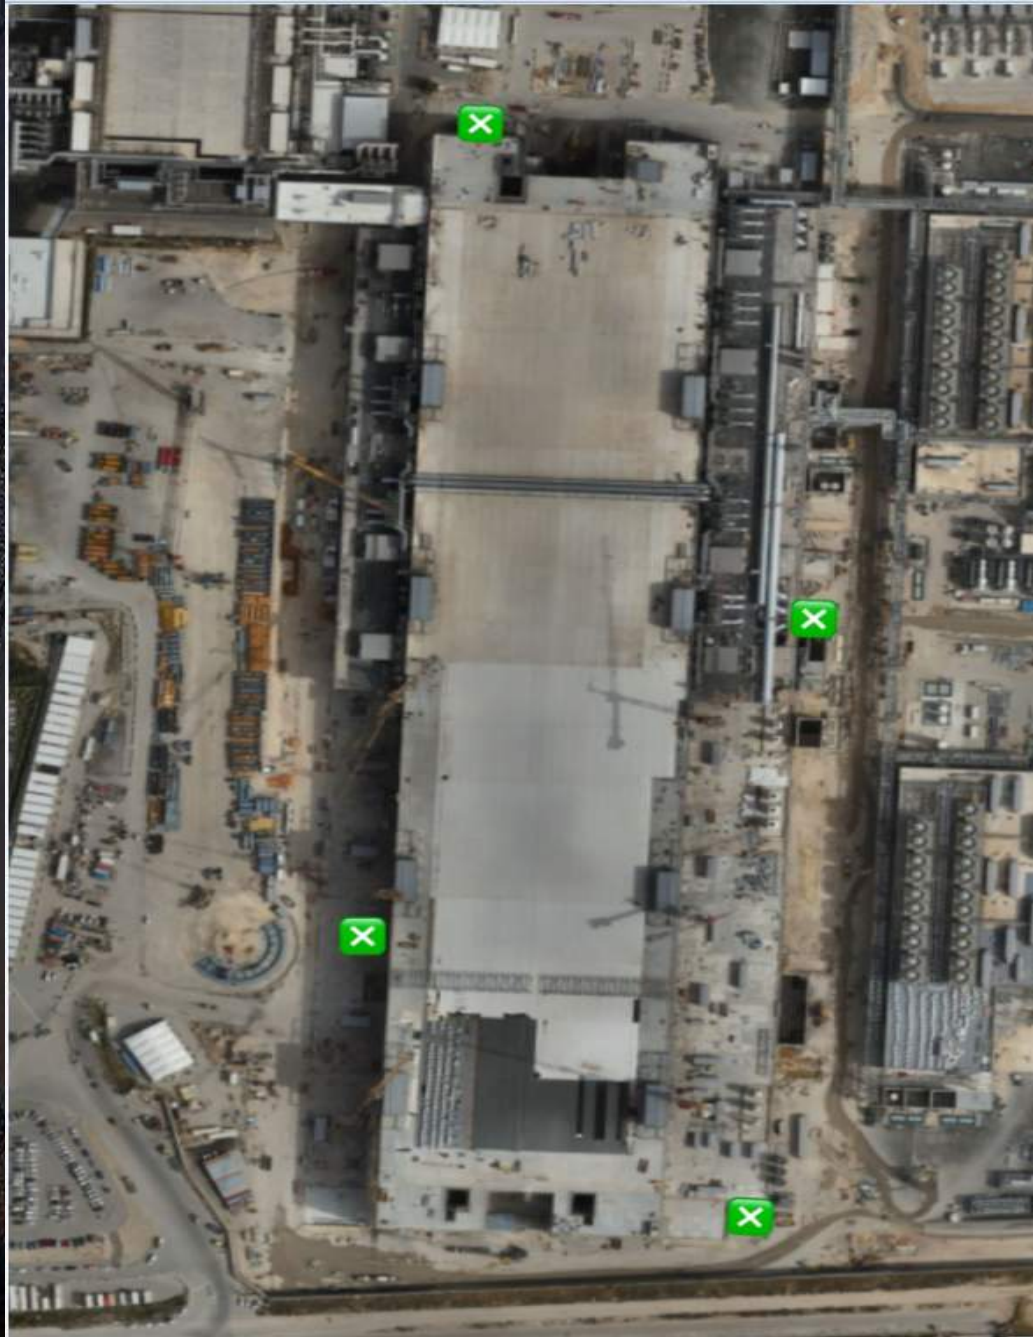

Fall protection plan

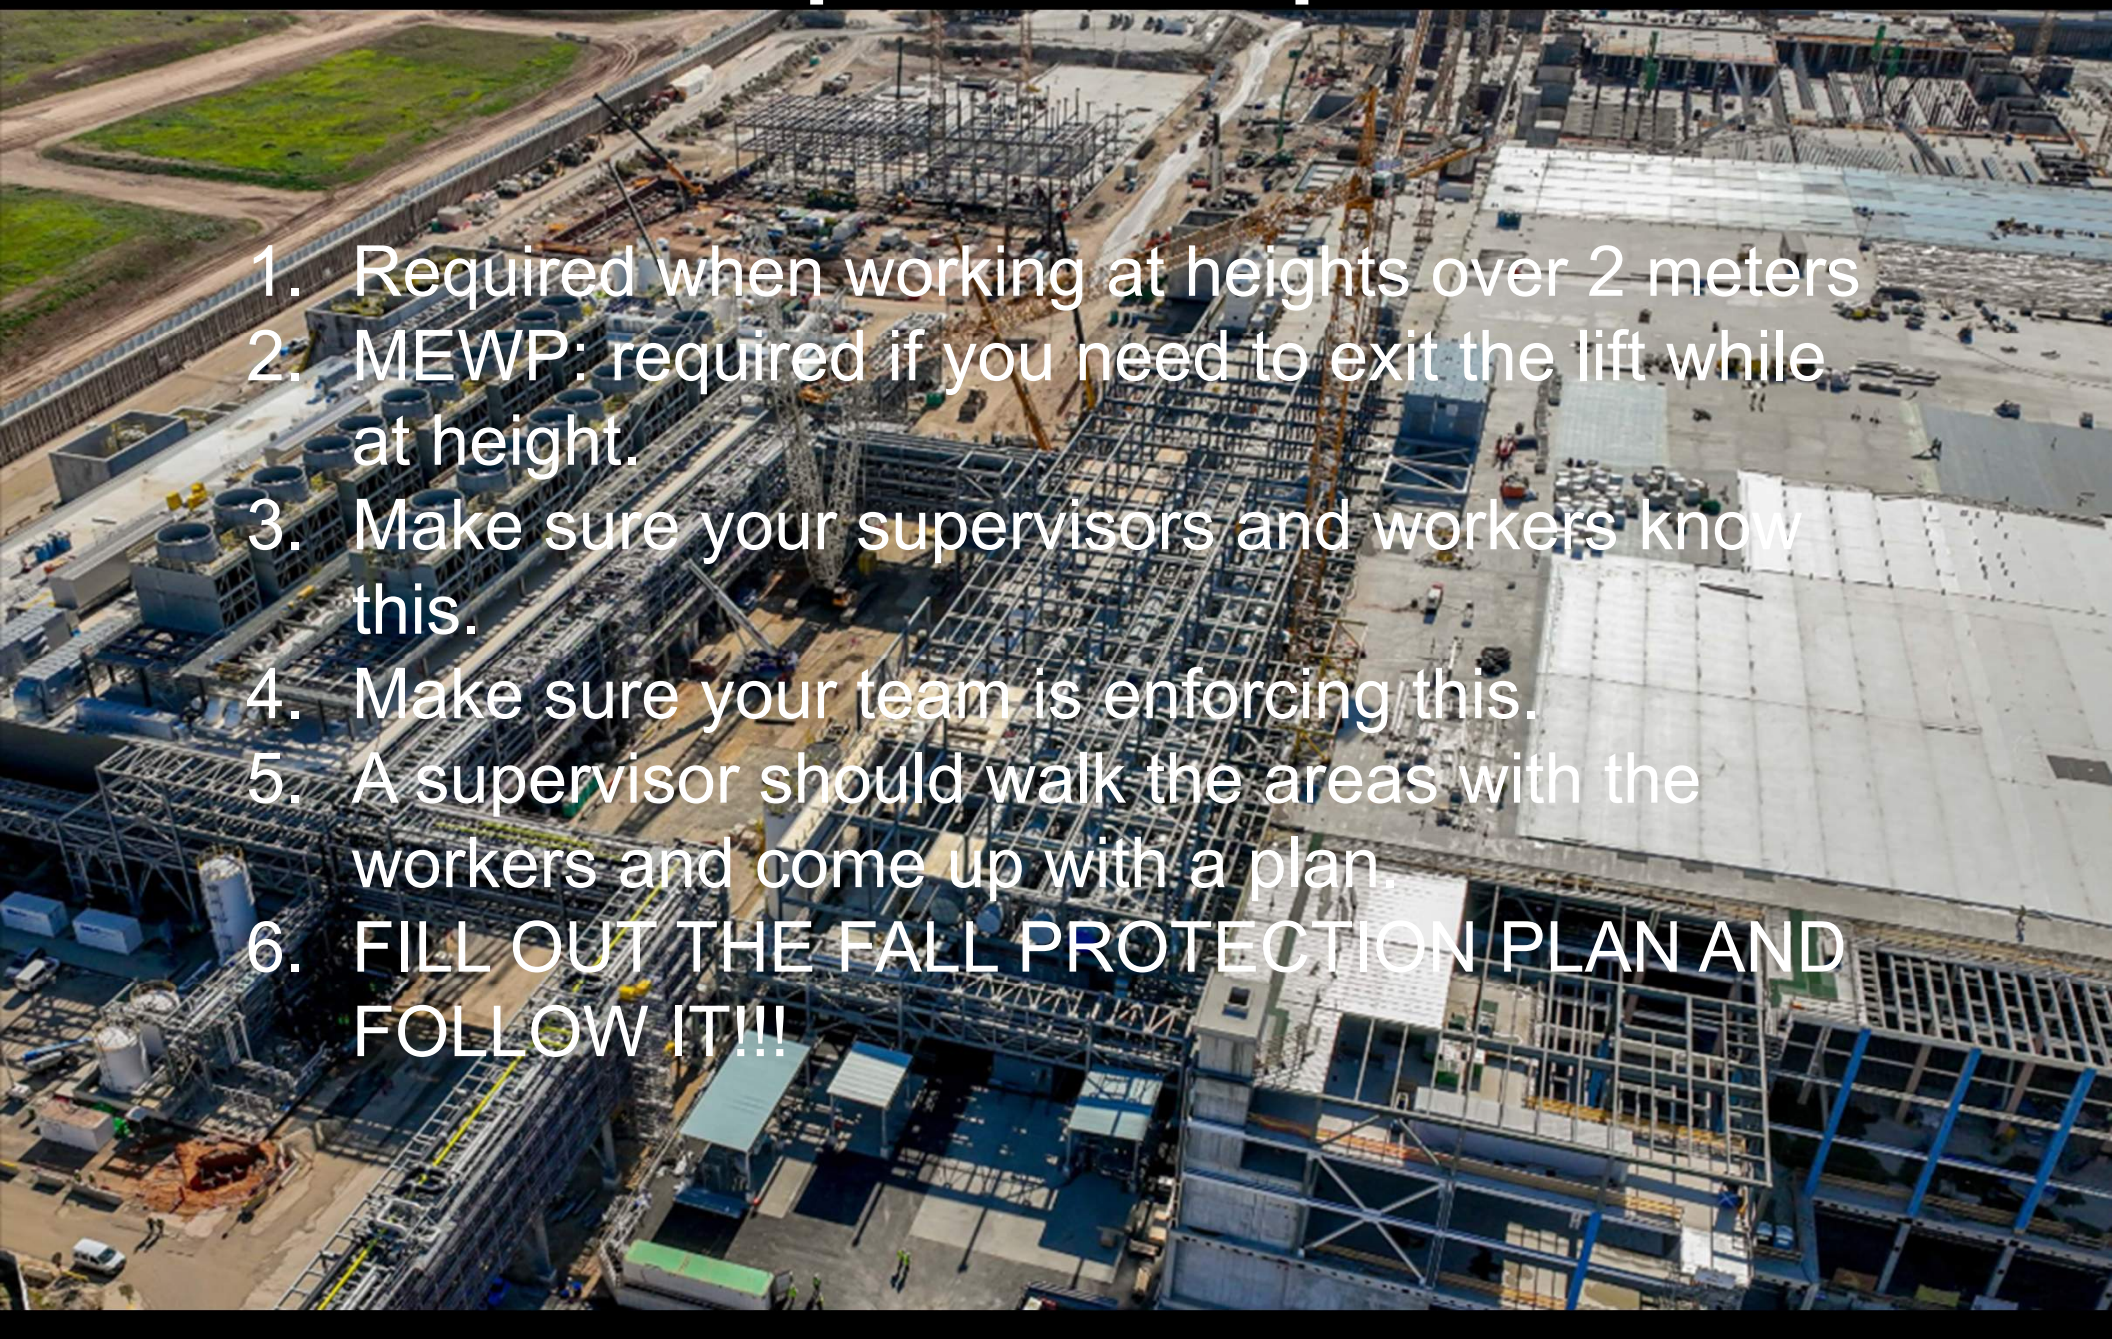- 
1. Required when working at heights over 2 meters
 2. MEWP: required if you need to exit the lift while at height.
 3. Make sure your supervisors and workers know this.
 4. Make sure your team is enforcing this.
 5. A supervisor should walk the areas with the workers and come up with a plan.
 6. **FILL OUT THE FALL PROTECTION PLAN AND FOLLOW IT!!!**

HCC/EHS Weekend Work- 25.04.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Sandefer -052-3440752

Ziv Srur - 053-2712258

Yakov Alon - 052-4671271

Leslie Kelly - 052-6391546

Michael Ohehir- 052-4168879

CSA CM

Dana Chelly - 052-4729048

Idan Dahan - 052-5949702

Pablo Irizarry - OSM CM

Abhilash-Parameswaran - 052-6938827

MEP

Cx

Cranes

Safety

- Safety Foreman- Adir Elmakayes- 054-7254767 Adir-Elmakayes@Hoffmancorp.com
- Safety Assistant- Husam Natasheh- 053-2478114 Husam-Natasheh@Hoffmancorp.com
- Safety Professional - Muhamad Halila-052-4060554

Subcontractor Weekend Work- 25.04.2025

FAB

SNJ – Liran – 052-8939558

Utility Level / Roof / Stair Shaft

Afcon electrical

EHS Steven [0559129333](tel:0559129333)
FOREMAN Perdit [0552742935](tel:0552742935)

Subfab

- Lesico -5E,5W Pressure test
 - Foreman- Gabriel 0549892929
 - Safety – Michael Gasri 0526060223
- Afcon-E – All over Mod1
 - Foreman – Avi Eli 0526008487
 - Safety – Stefan Shabto 0559129333
- Megason – TTN,MOD2
 - Foreman – Israel 0526869393
 - Safety- Idan 0539281172

• Clean Room

- Talad – 20- 1W ceiling work and popout (EHS Maty 0504887477, Super Igor 0544509386)
- Chemo- 55- coil fitup in mar 5e and 5w including ttnw for piping and racks (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2- mod 1 CR (Ravid 0507111588, Roni 0542496363)
- Tavas – 10 guys Cleanroom clean Maintenance 1-2E/1-2W (Supervisor 0526055908, EHS 0523140571)
- Sig – 17- scaffolding in mod 2(EHS Beni 0506232032, Super Shmulik 0549205966)
- W&W 25 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Walter - 0525319705)
- Afcon – 20 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pulling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Rolling Plains – 21- Fireproof prep and coating mod 1 and 2 (Super oleg 0542689370 , EHS MARCOV 0546596857)
- Sela- 8- CRC prep and coat mod 1 5W

Subcontractor Weekend Work- 25.04.2025

PSSS

Afcon Electrical – Cable Tray and Cable Pulling /BCD UL and 4&5P Roof & Lift 2

- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333

W&W – Grating Supports 1P Lift 3, Grating Alignment Lift 3, Lift 3 handrail, MOD2 Girts

- Foreman – Willie 052-6145521
- Safety –

WJG

W&W

Safety: Tony Abu Nassar – 0507870320

Foreman: Walter -0525319705

Subcontractor Weekend Work- 25.04.2025

CUB

Sela CUB 1 walk path painting:

Noam - 0508184590

Sergey - 0526650046

Sami Najami CUB 2 internal test:

Husein - 052-6917461

Aviram - 050-9059920

Chemo Aharon (maybe)

Dudu - 0509808846

Gabi - 0504327005

Trestle

SNJ:

Piping and steel

15 People - pipes

30 People - steel

Safety – wisam

0509828381

Team leader - Muchless

0528341298

Team leader – adeeb aseely

0526017477

Site

Olizki - curb stone, grading, clean up

Daily Coordination Meeting



14:00 Sign In
