

Daily Coordination Meeting




14:00 Sign In

Daily Coordination Meeting

General Topics:

- Fab power today @ 16:00
- Weekend work

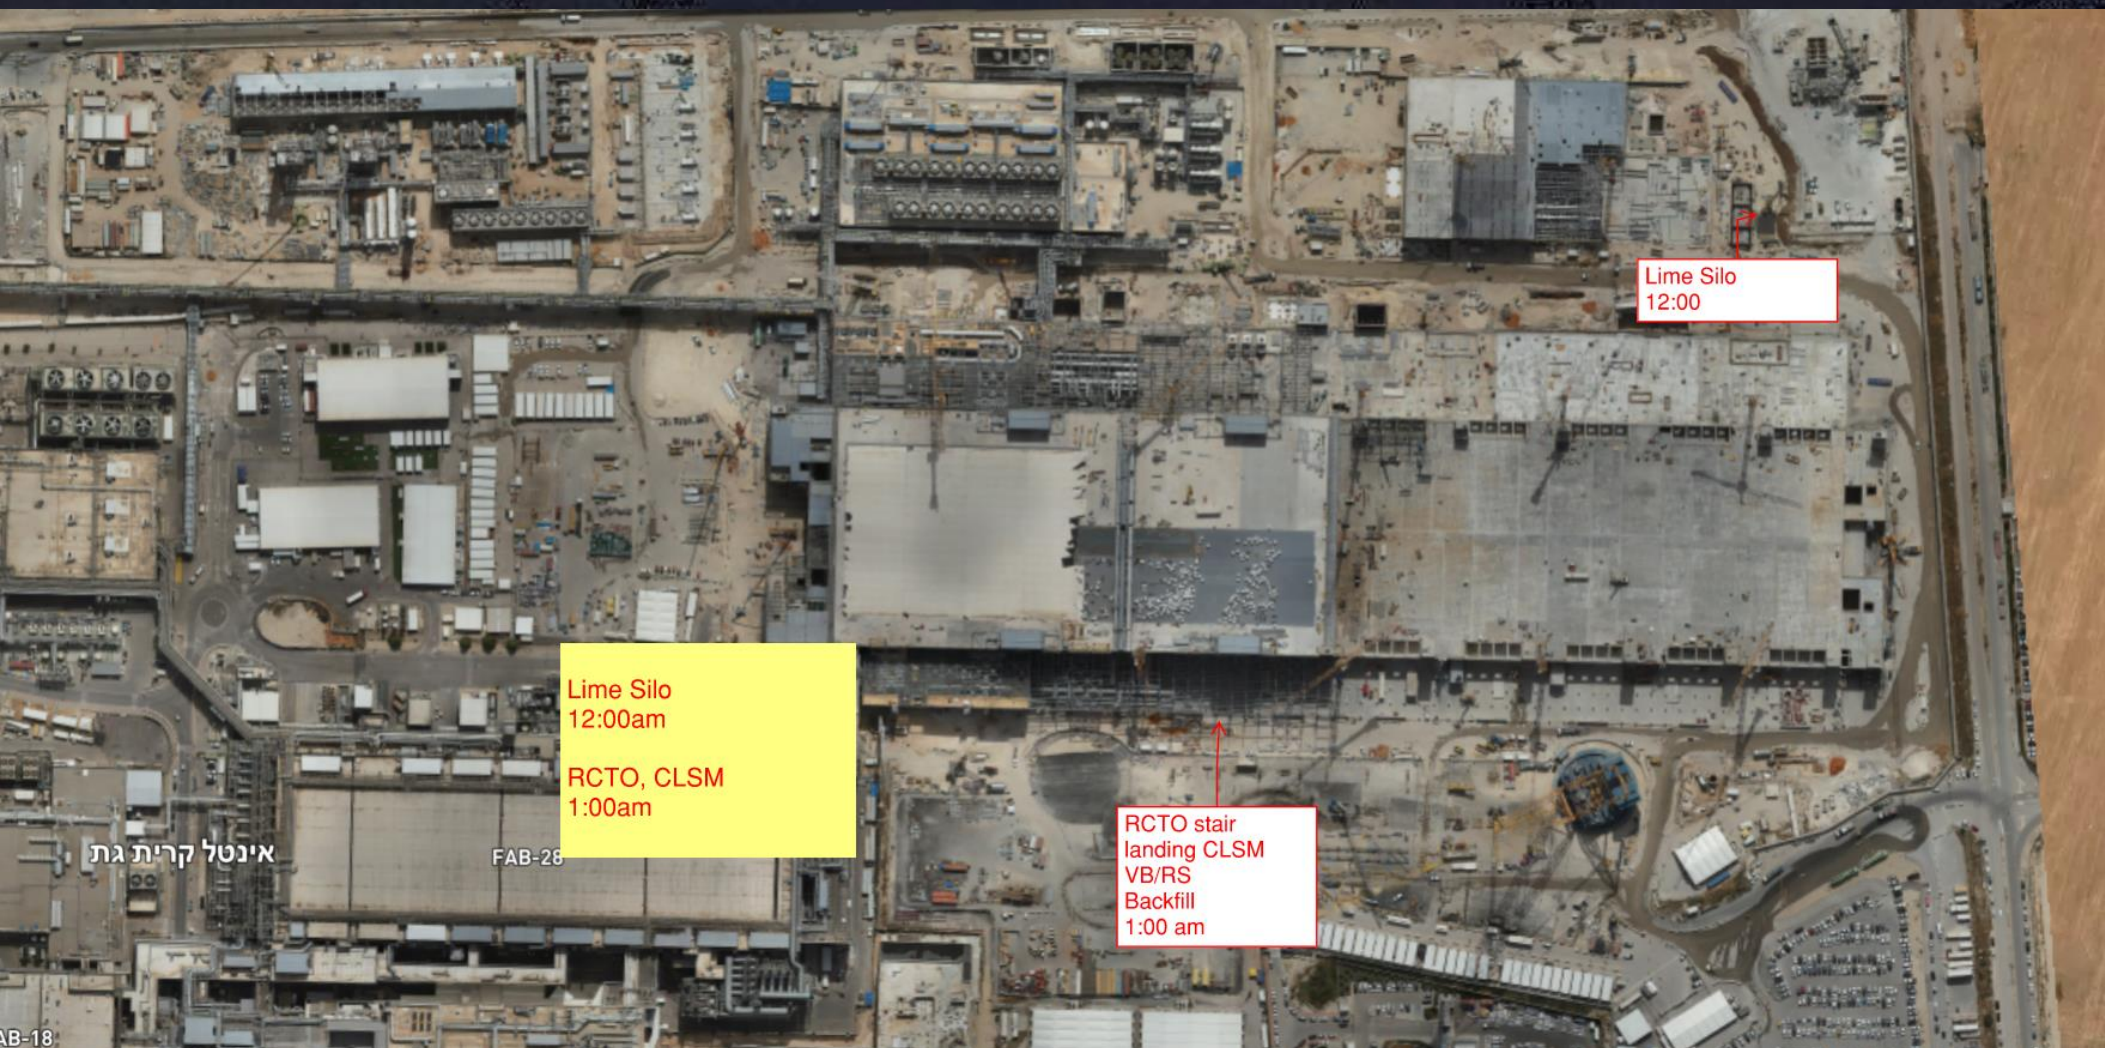

Lime Silo
12:00

Lime Silo
12:00am
RCTO, CLSM
1:00am

RCTO stair
landing CLSM
VB/RS
Backfill
1:00 am


אינטל קרית גת

FAB-28


AB-18




UTILITY LEVEL MOD1

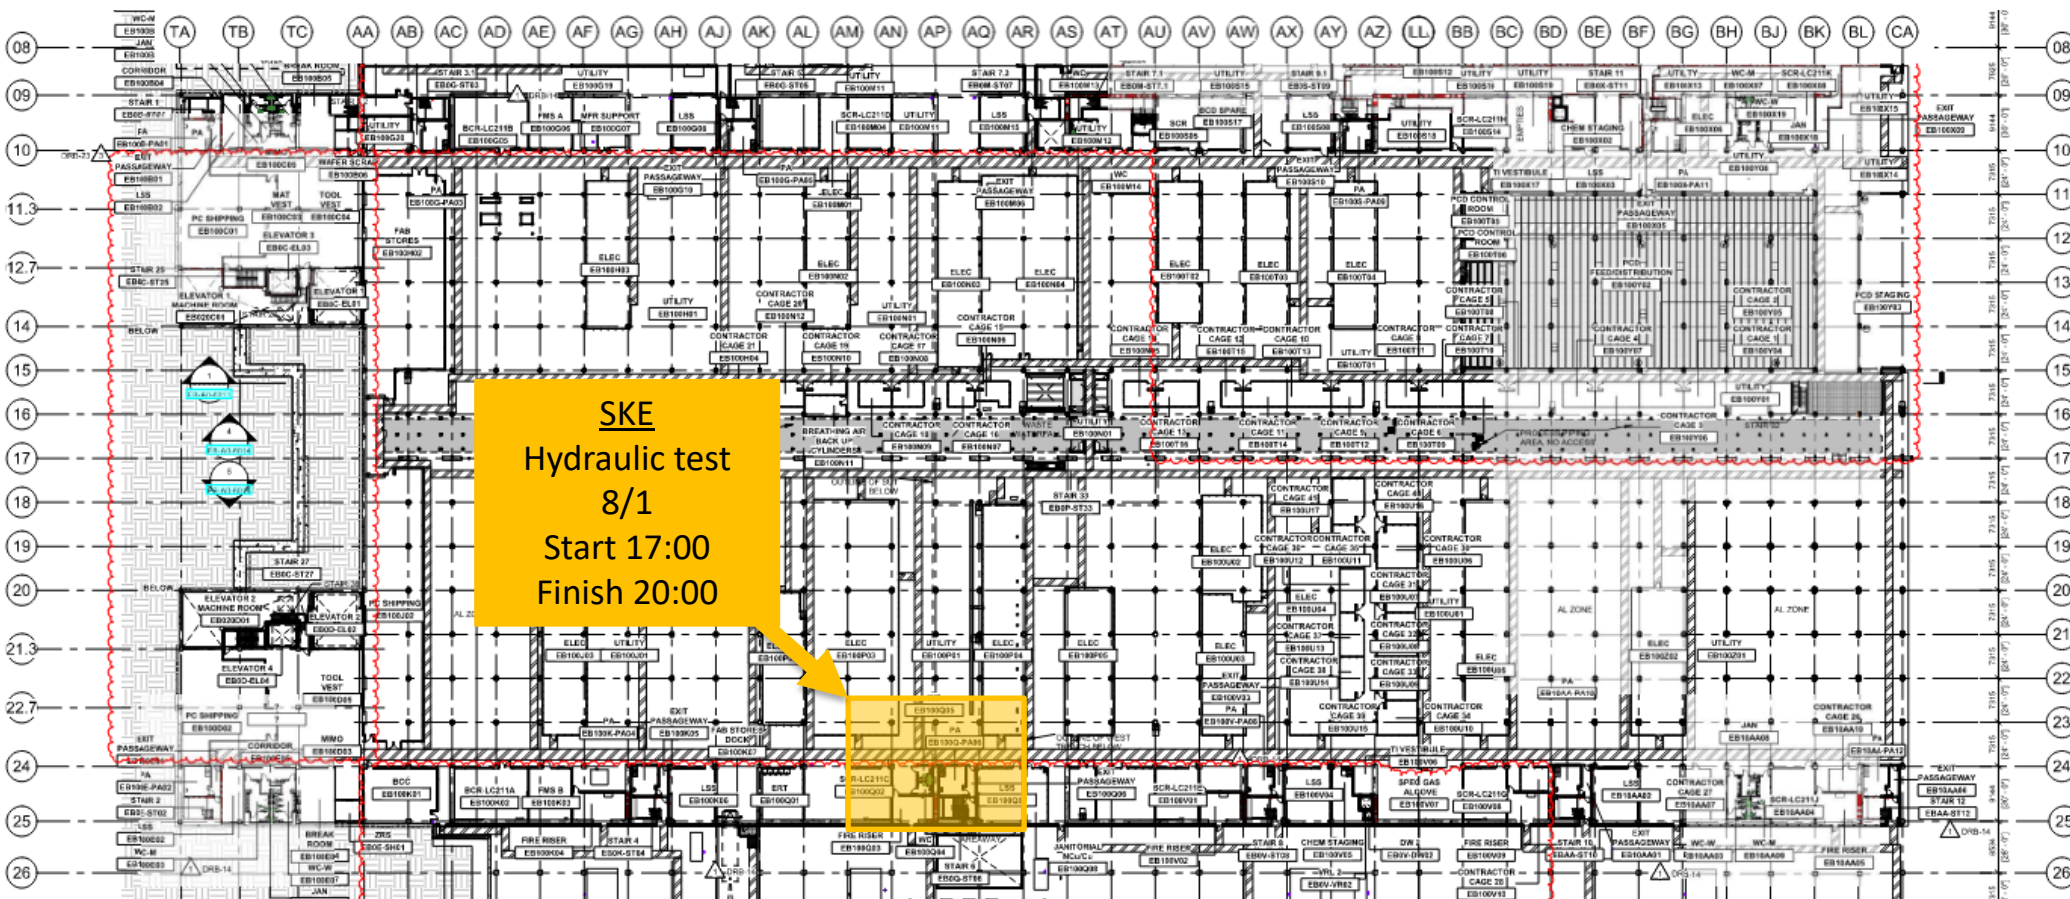

UTILITY LEVEL MOD1

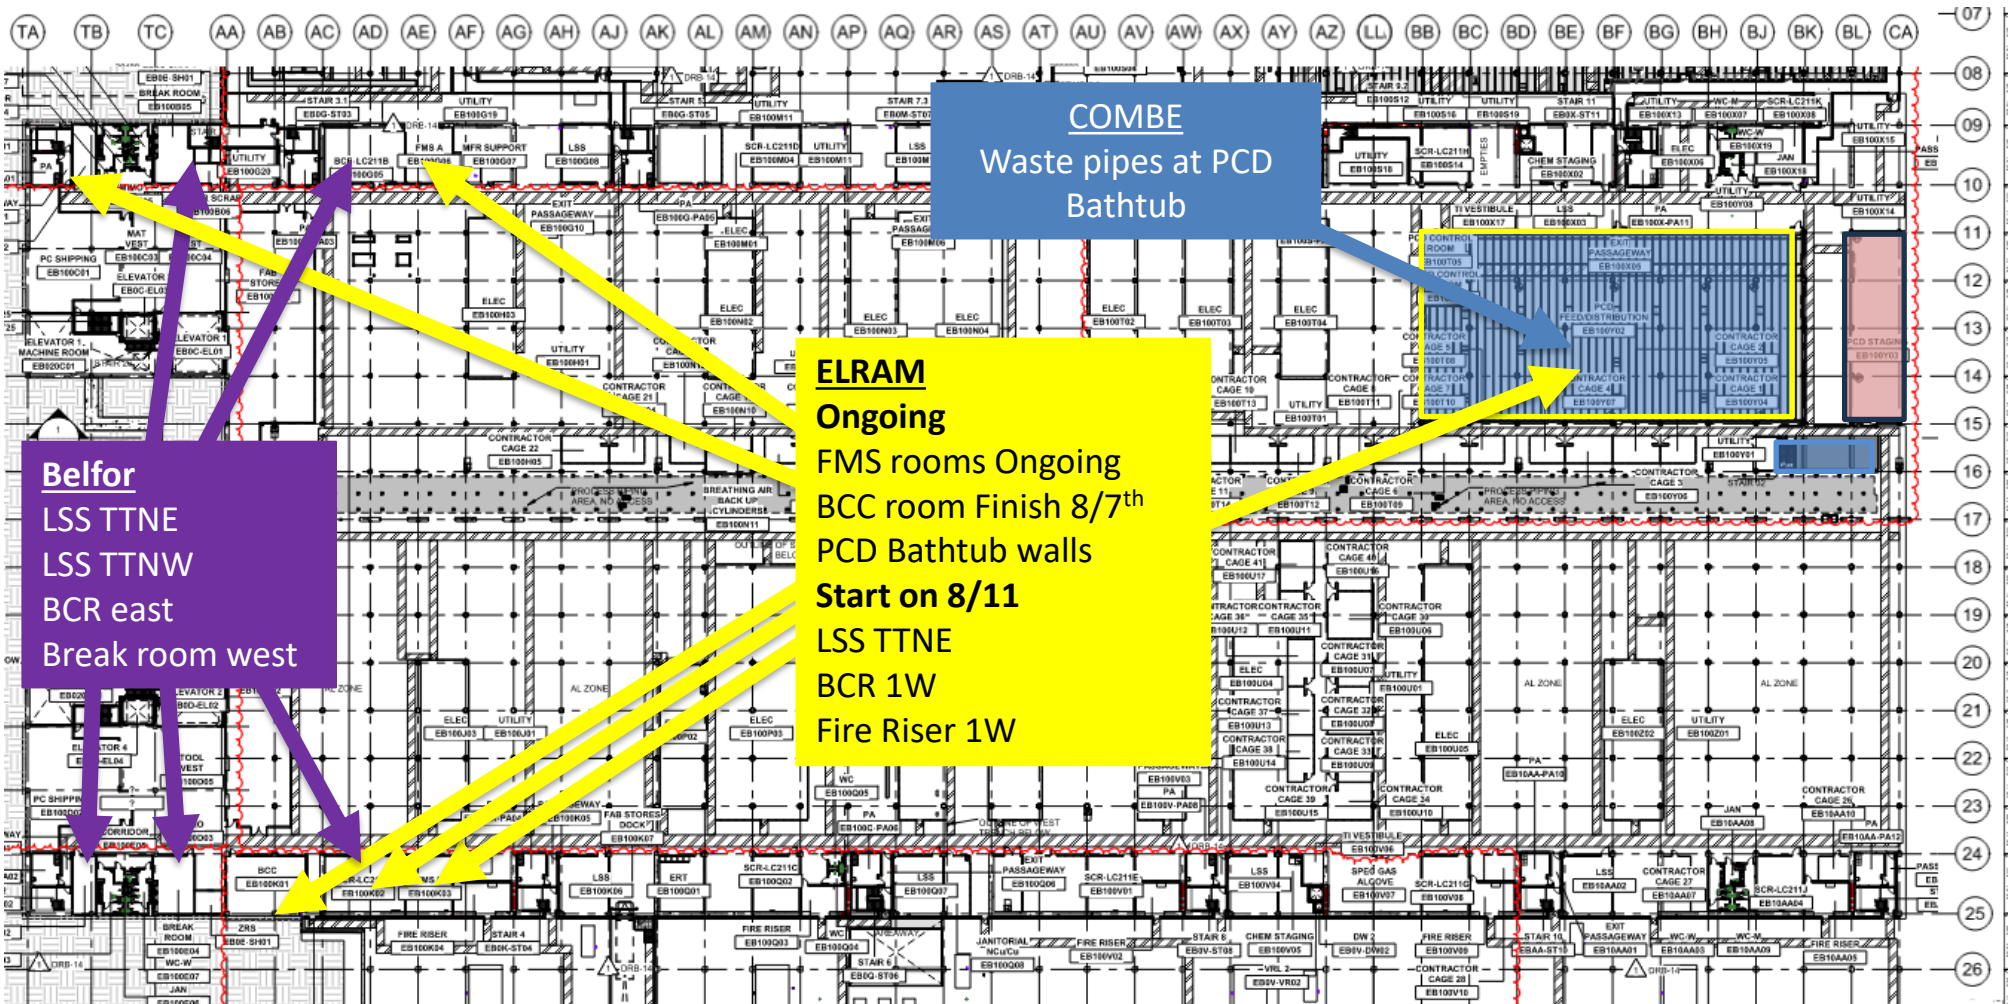


UTILITY LEVEL MOD2

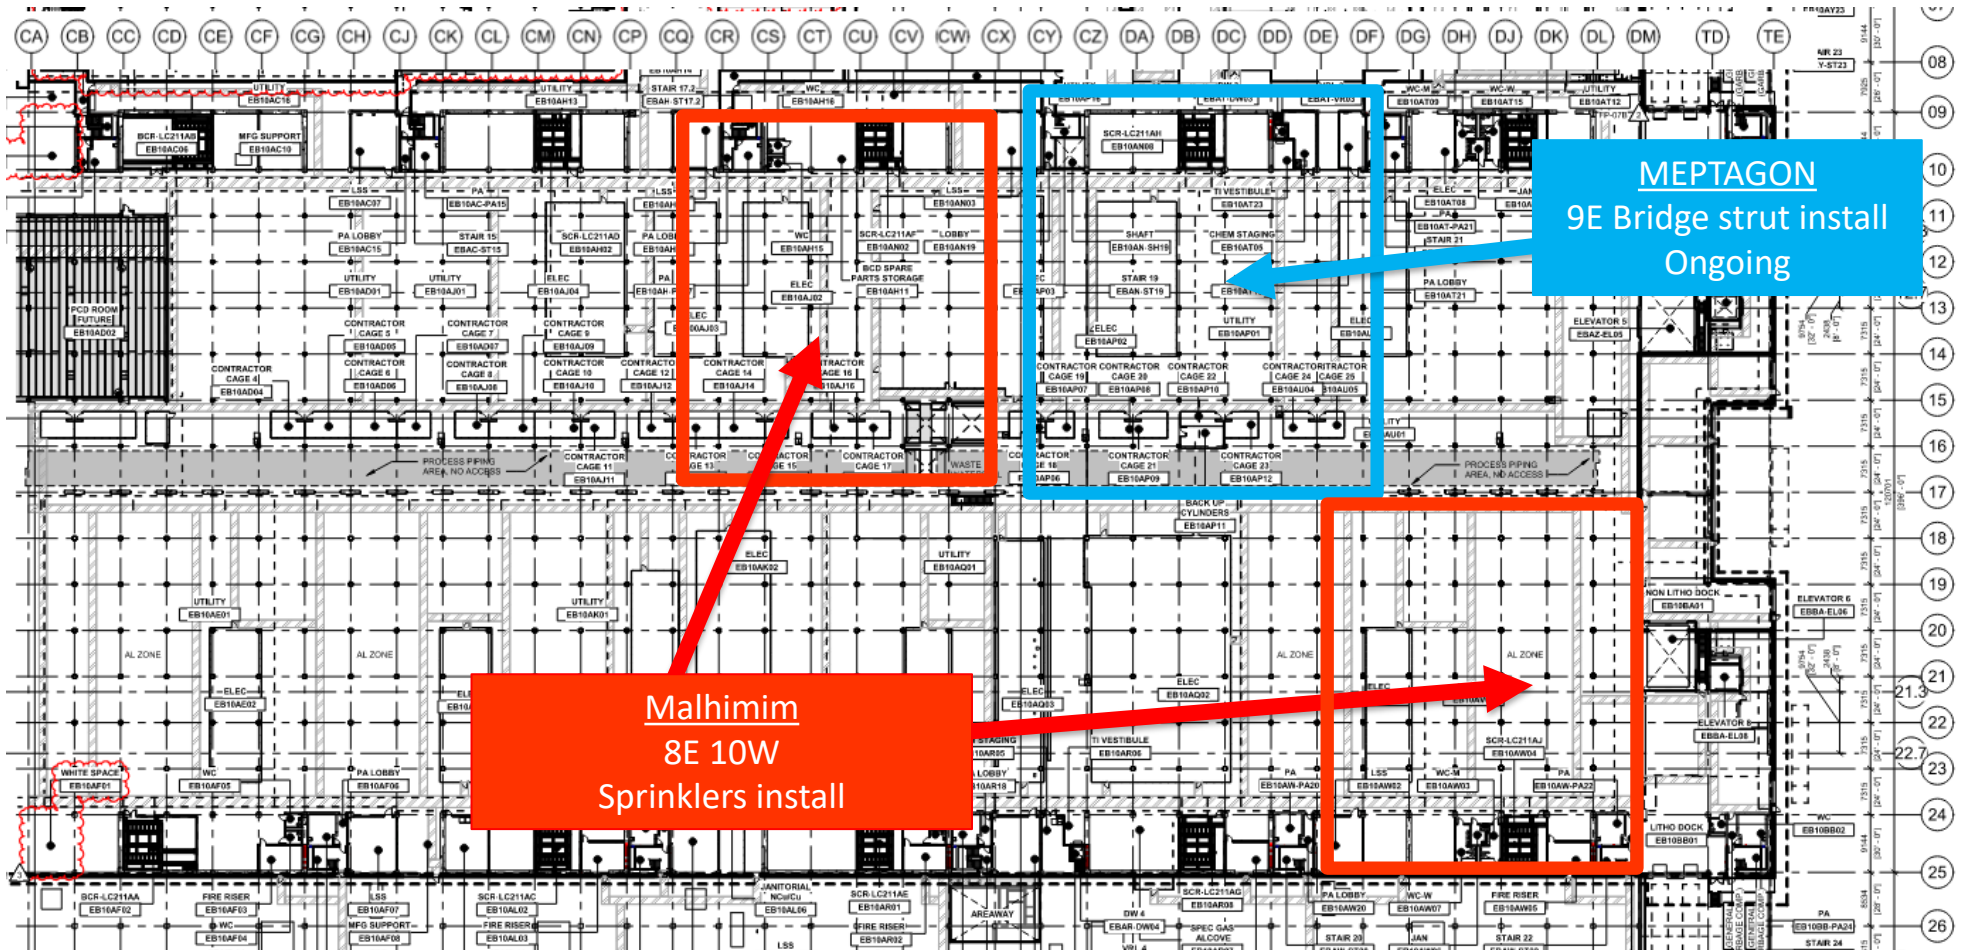




SUT 38.1 LEVEL

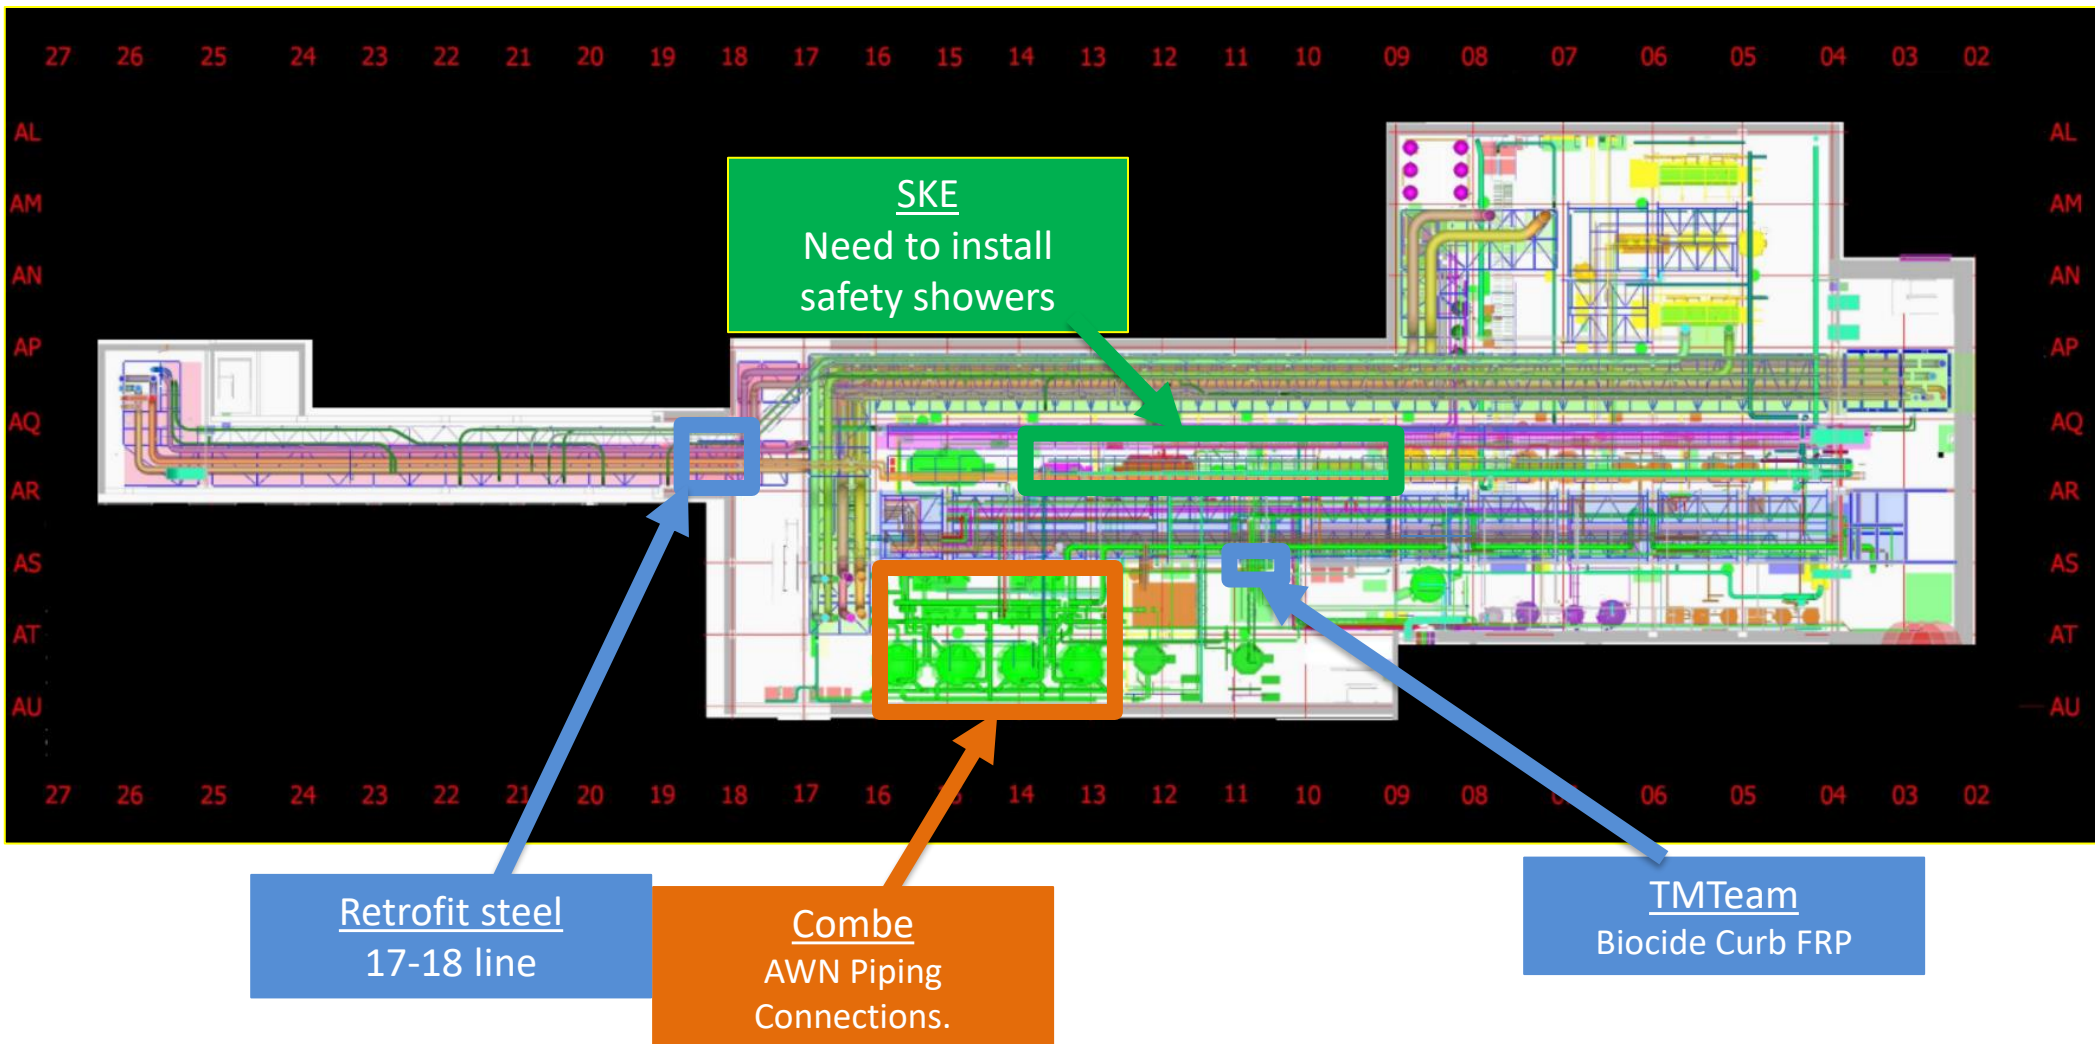



SUT 38.2 LEVEL

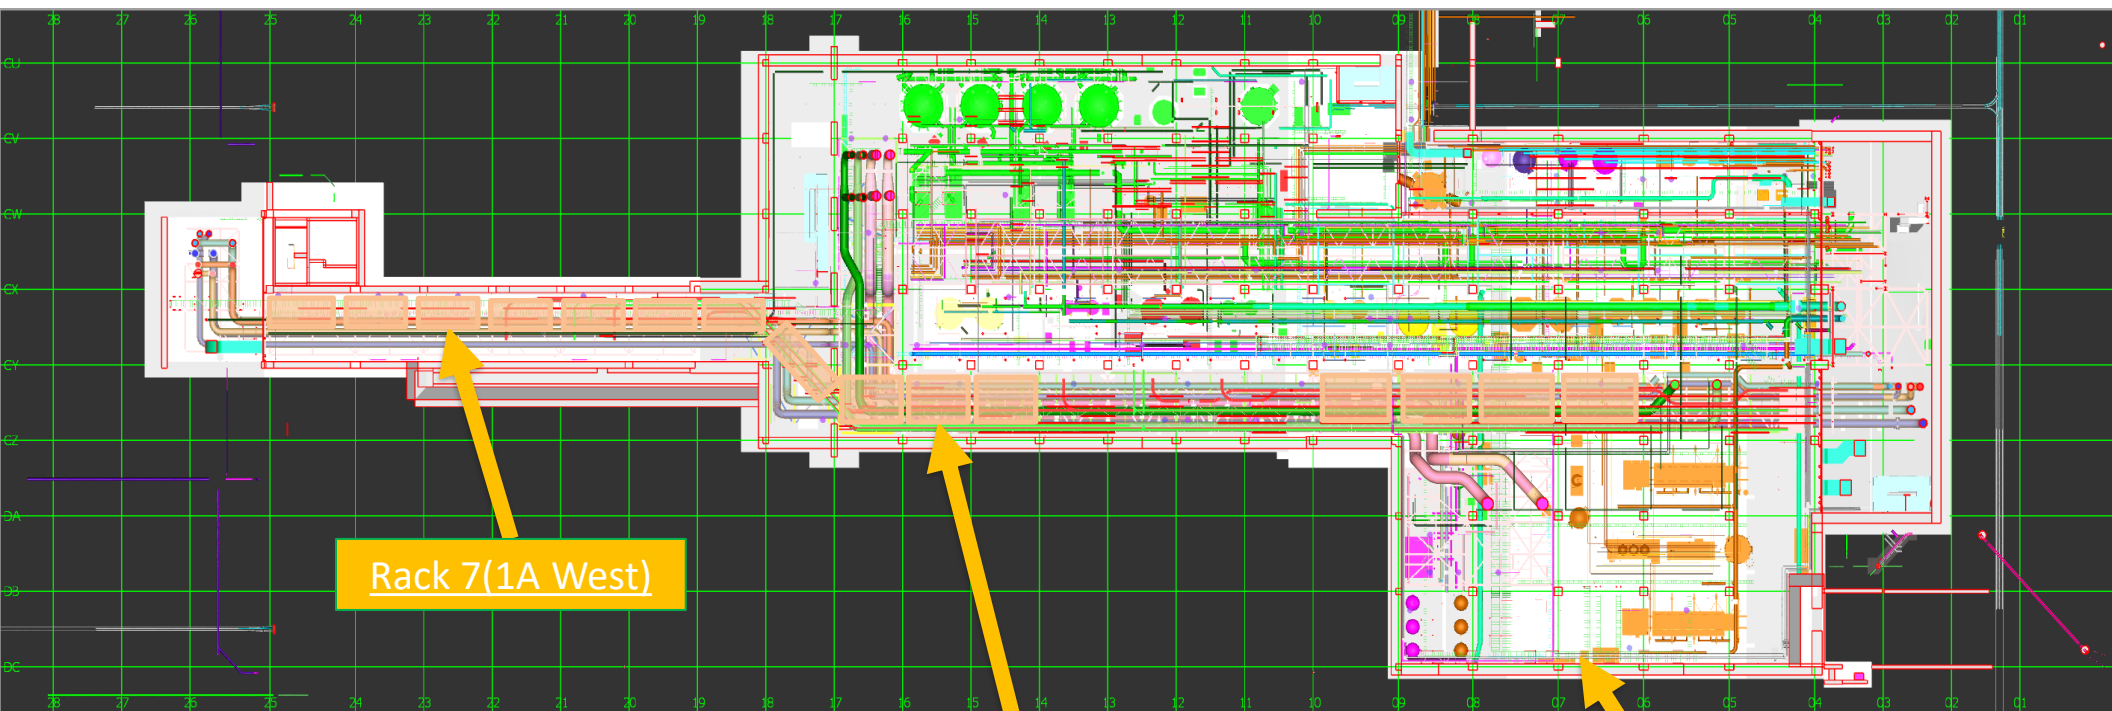

Rack 7(1A West)


1A Rack
Lifting

8 Rack


SKE
H&T
CRW
Move-In date ?

Vesda
H&T

SUBFAB BUILDOUT MOD 1

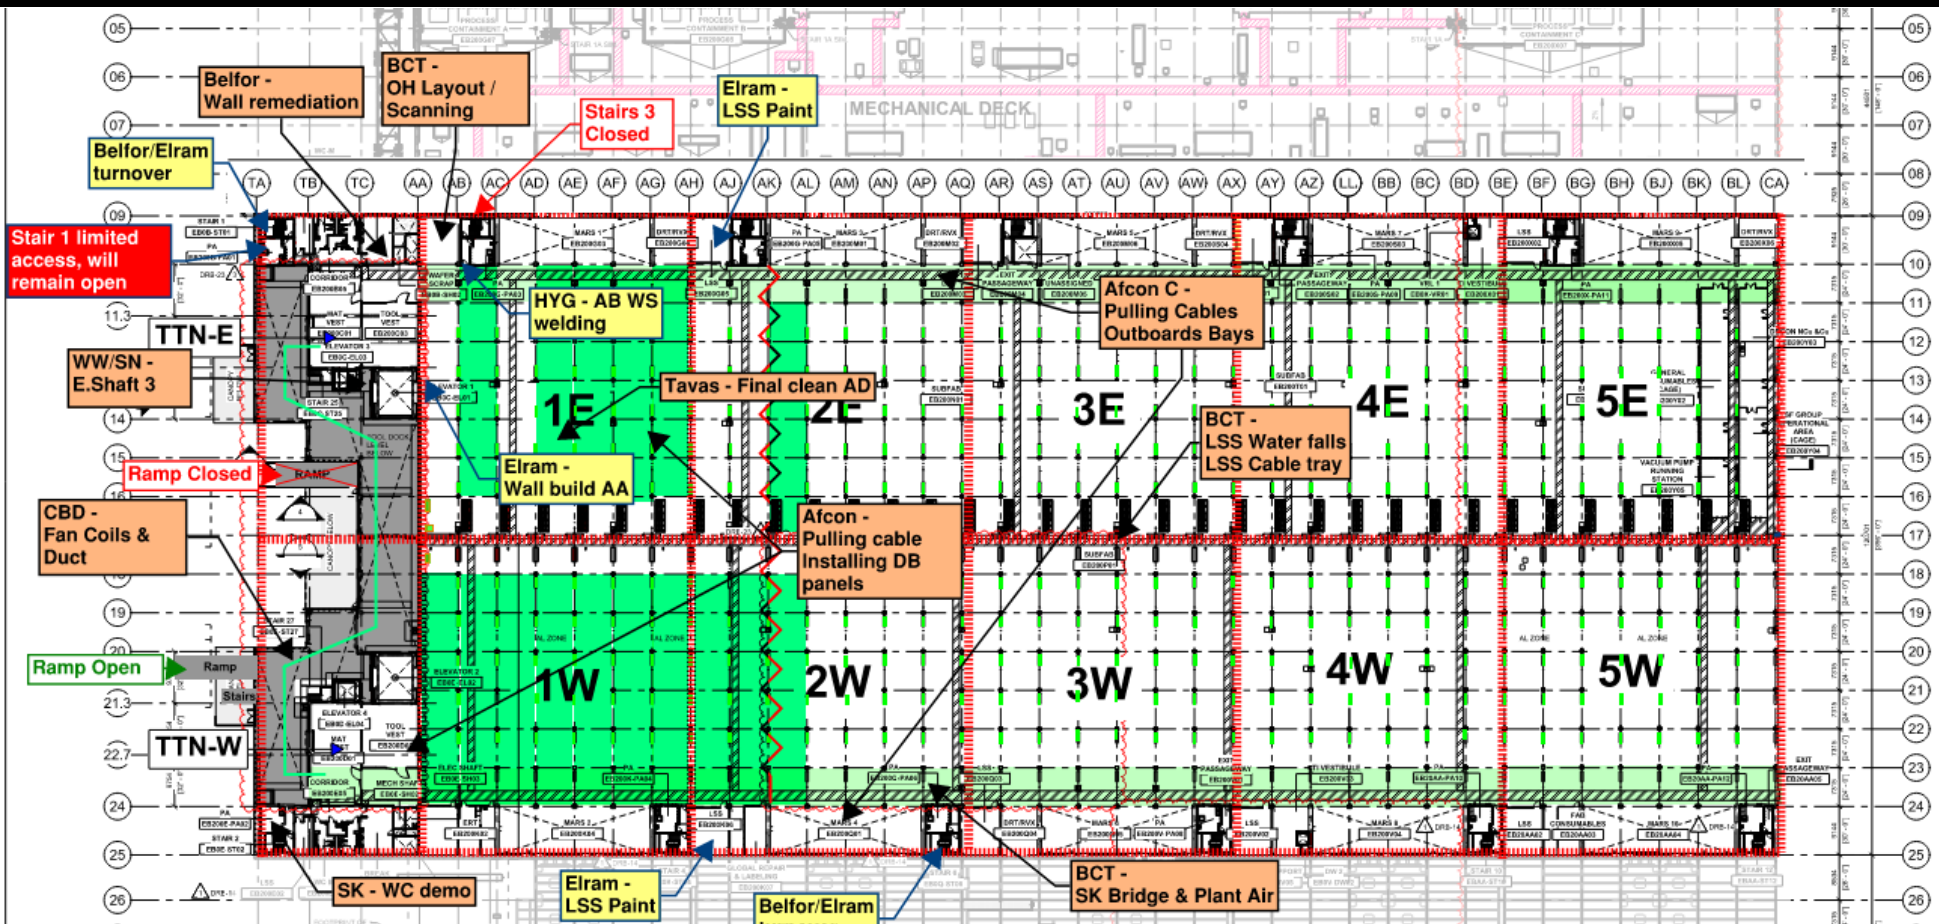

SUBFAB BUILDOUT MOD 2

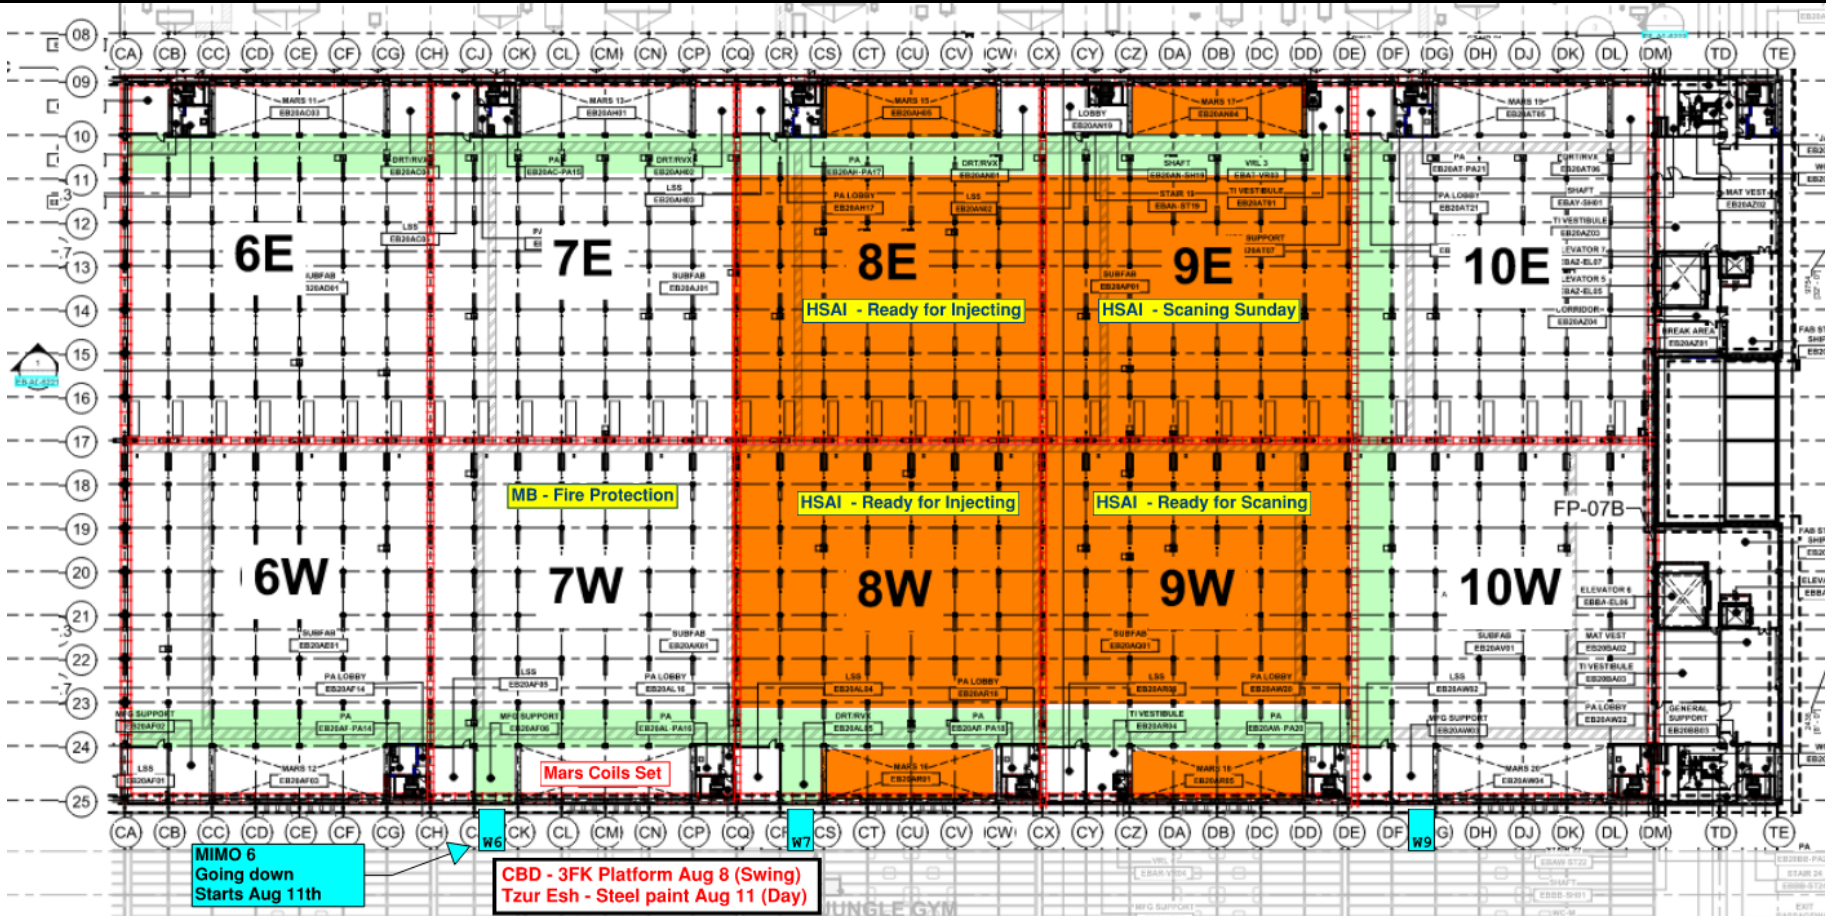


CRC Beauty Cote Work Plan.


Be well prepared to protect CRC


1. Nothing touches the floor, All must be on wheels.
2. Carts & MEWPs wheels must be replaced with a cleaner type (White).
3. Always have protective sheets/board on site to use for cover areas.
4. Damaging CRC will cause unnecessary and painful expenses to your company.



**1W South
Starts Aug 11**


**1W North
Ongoing**

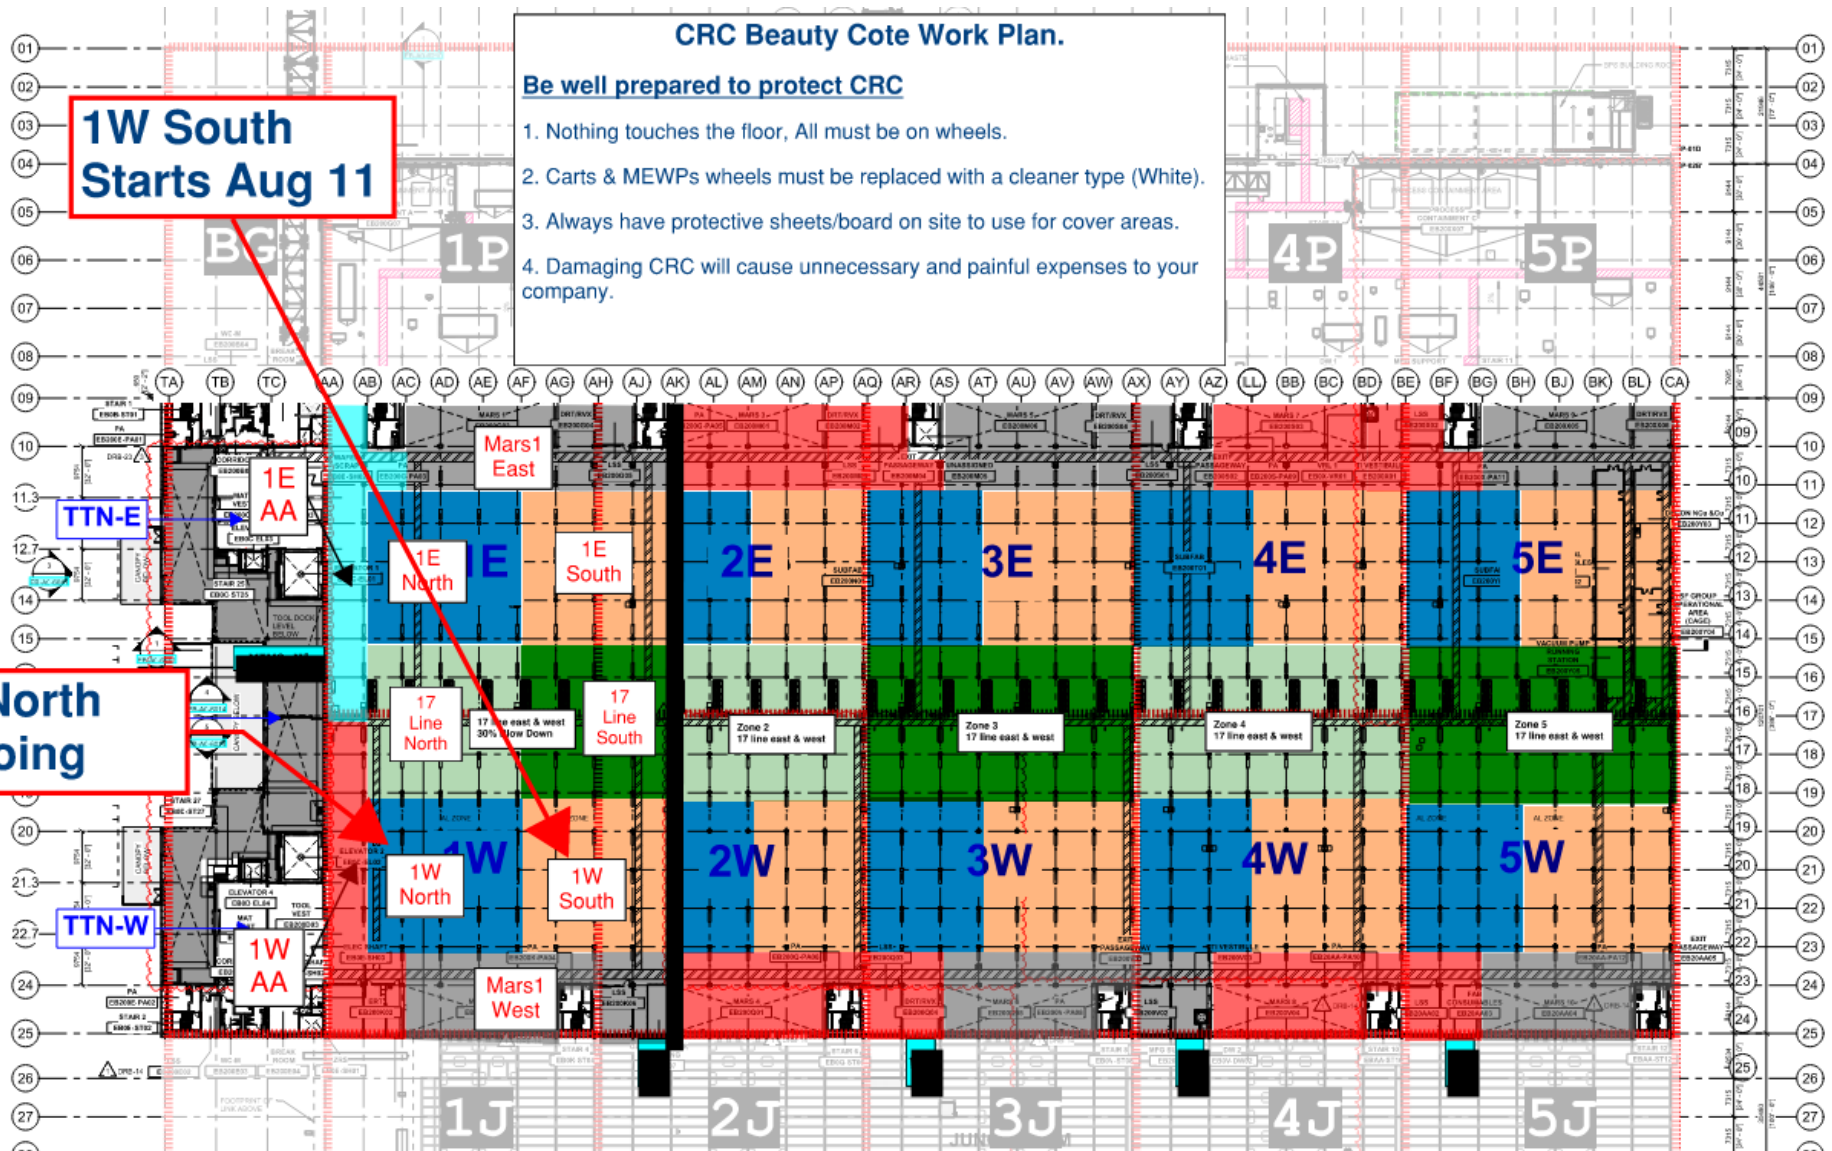


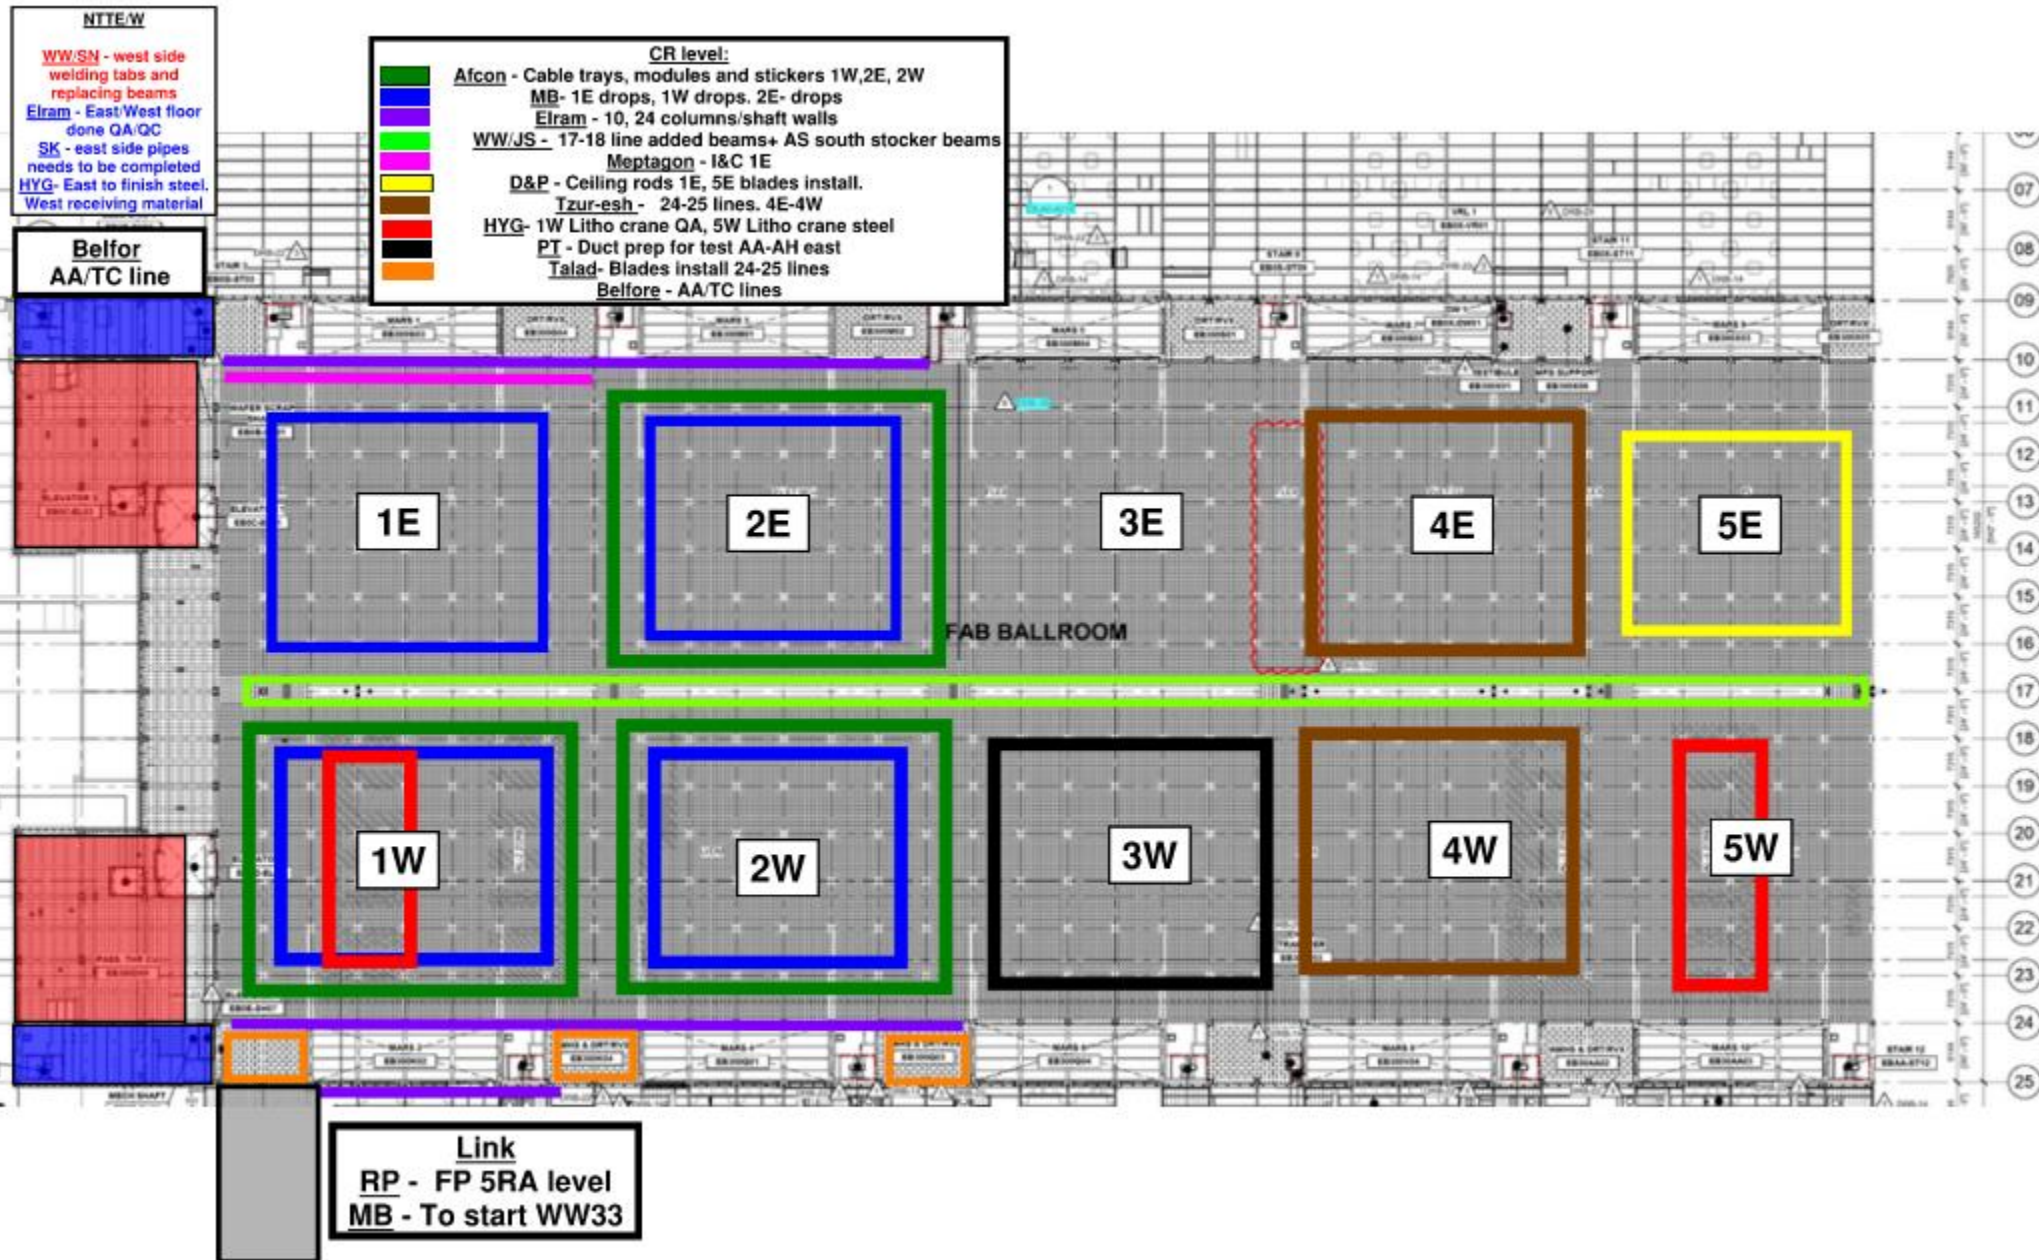


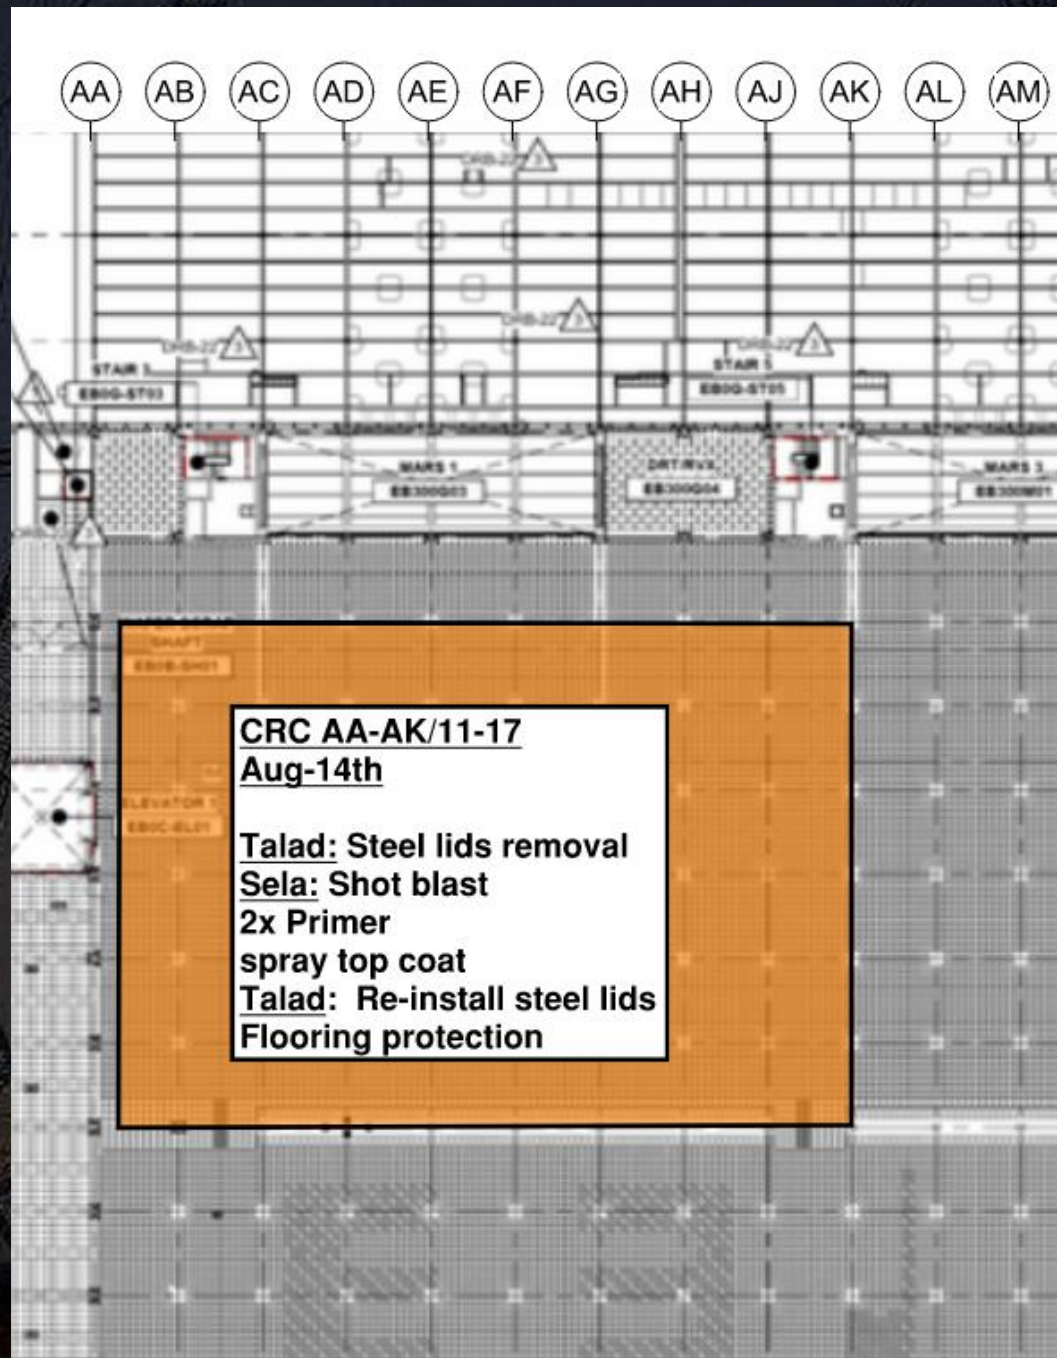


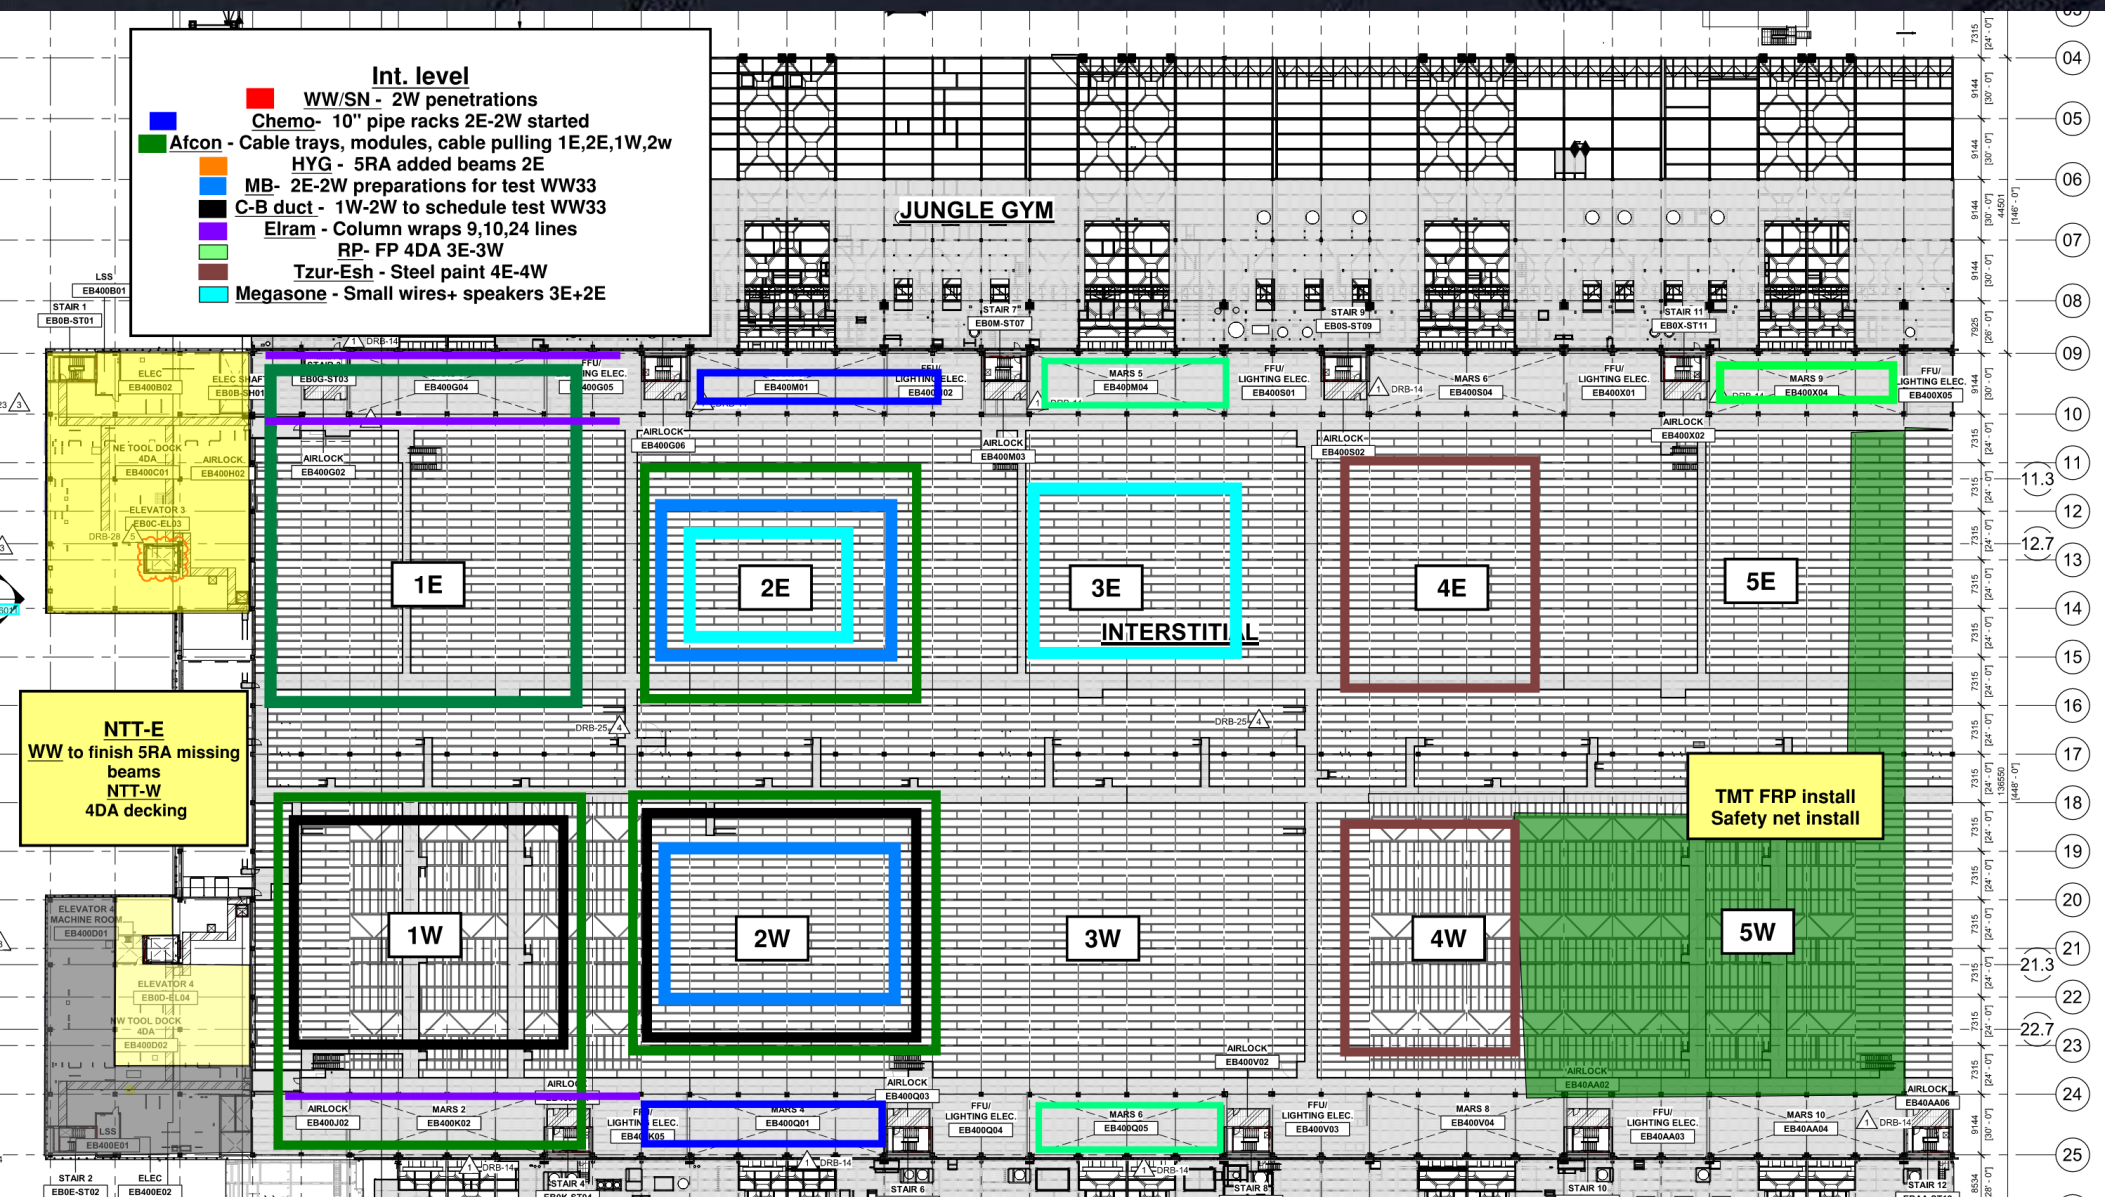

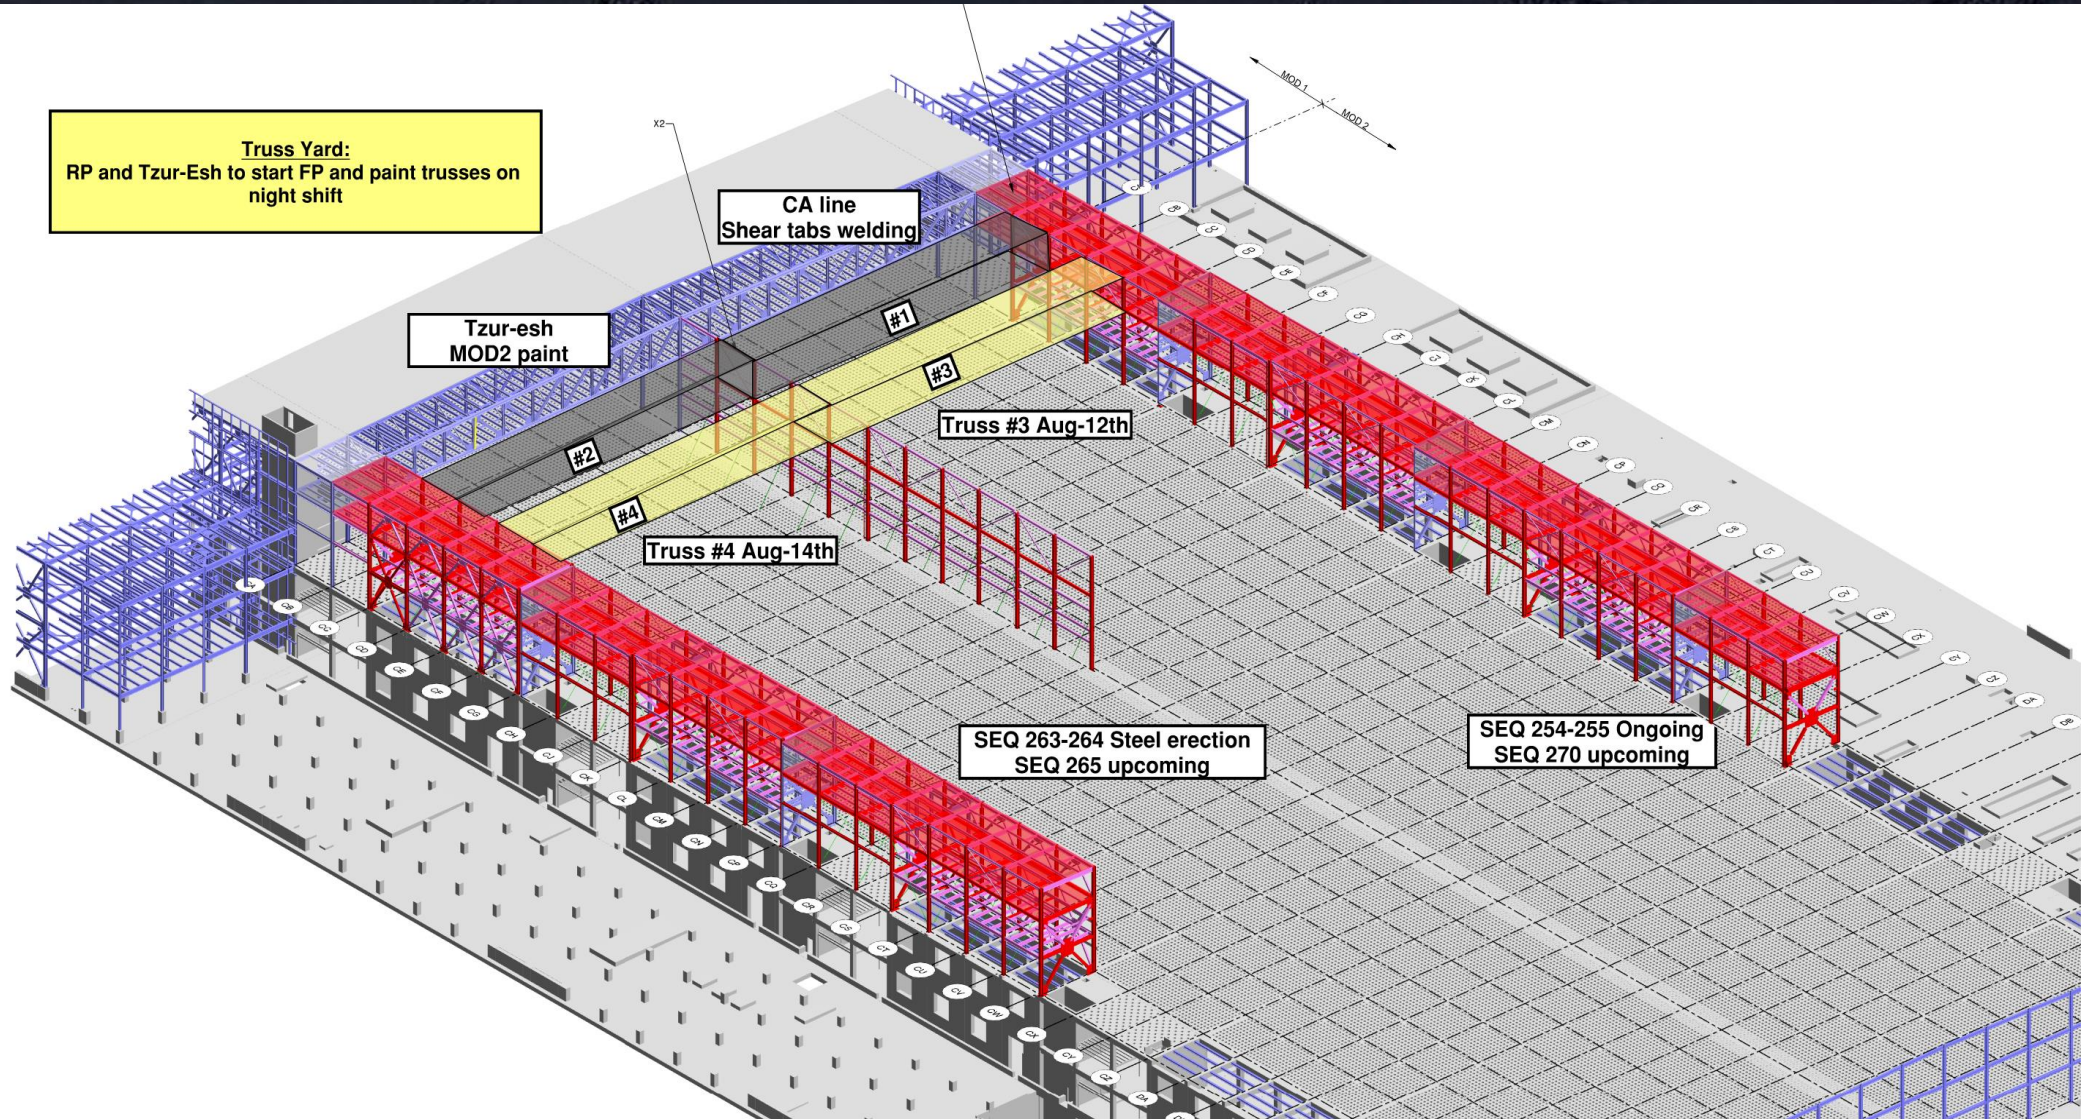


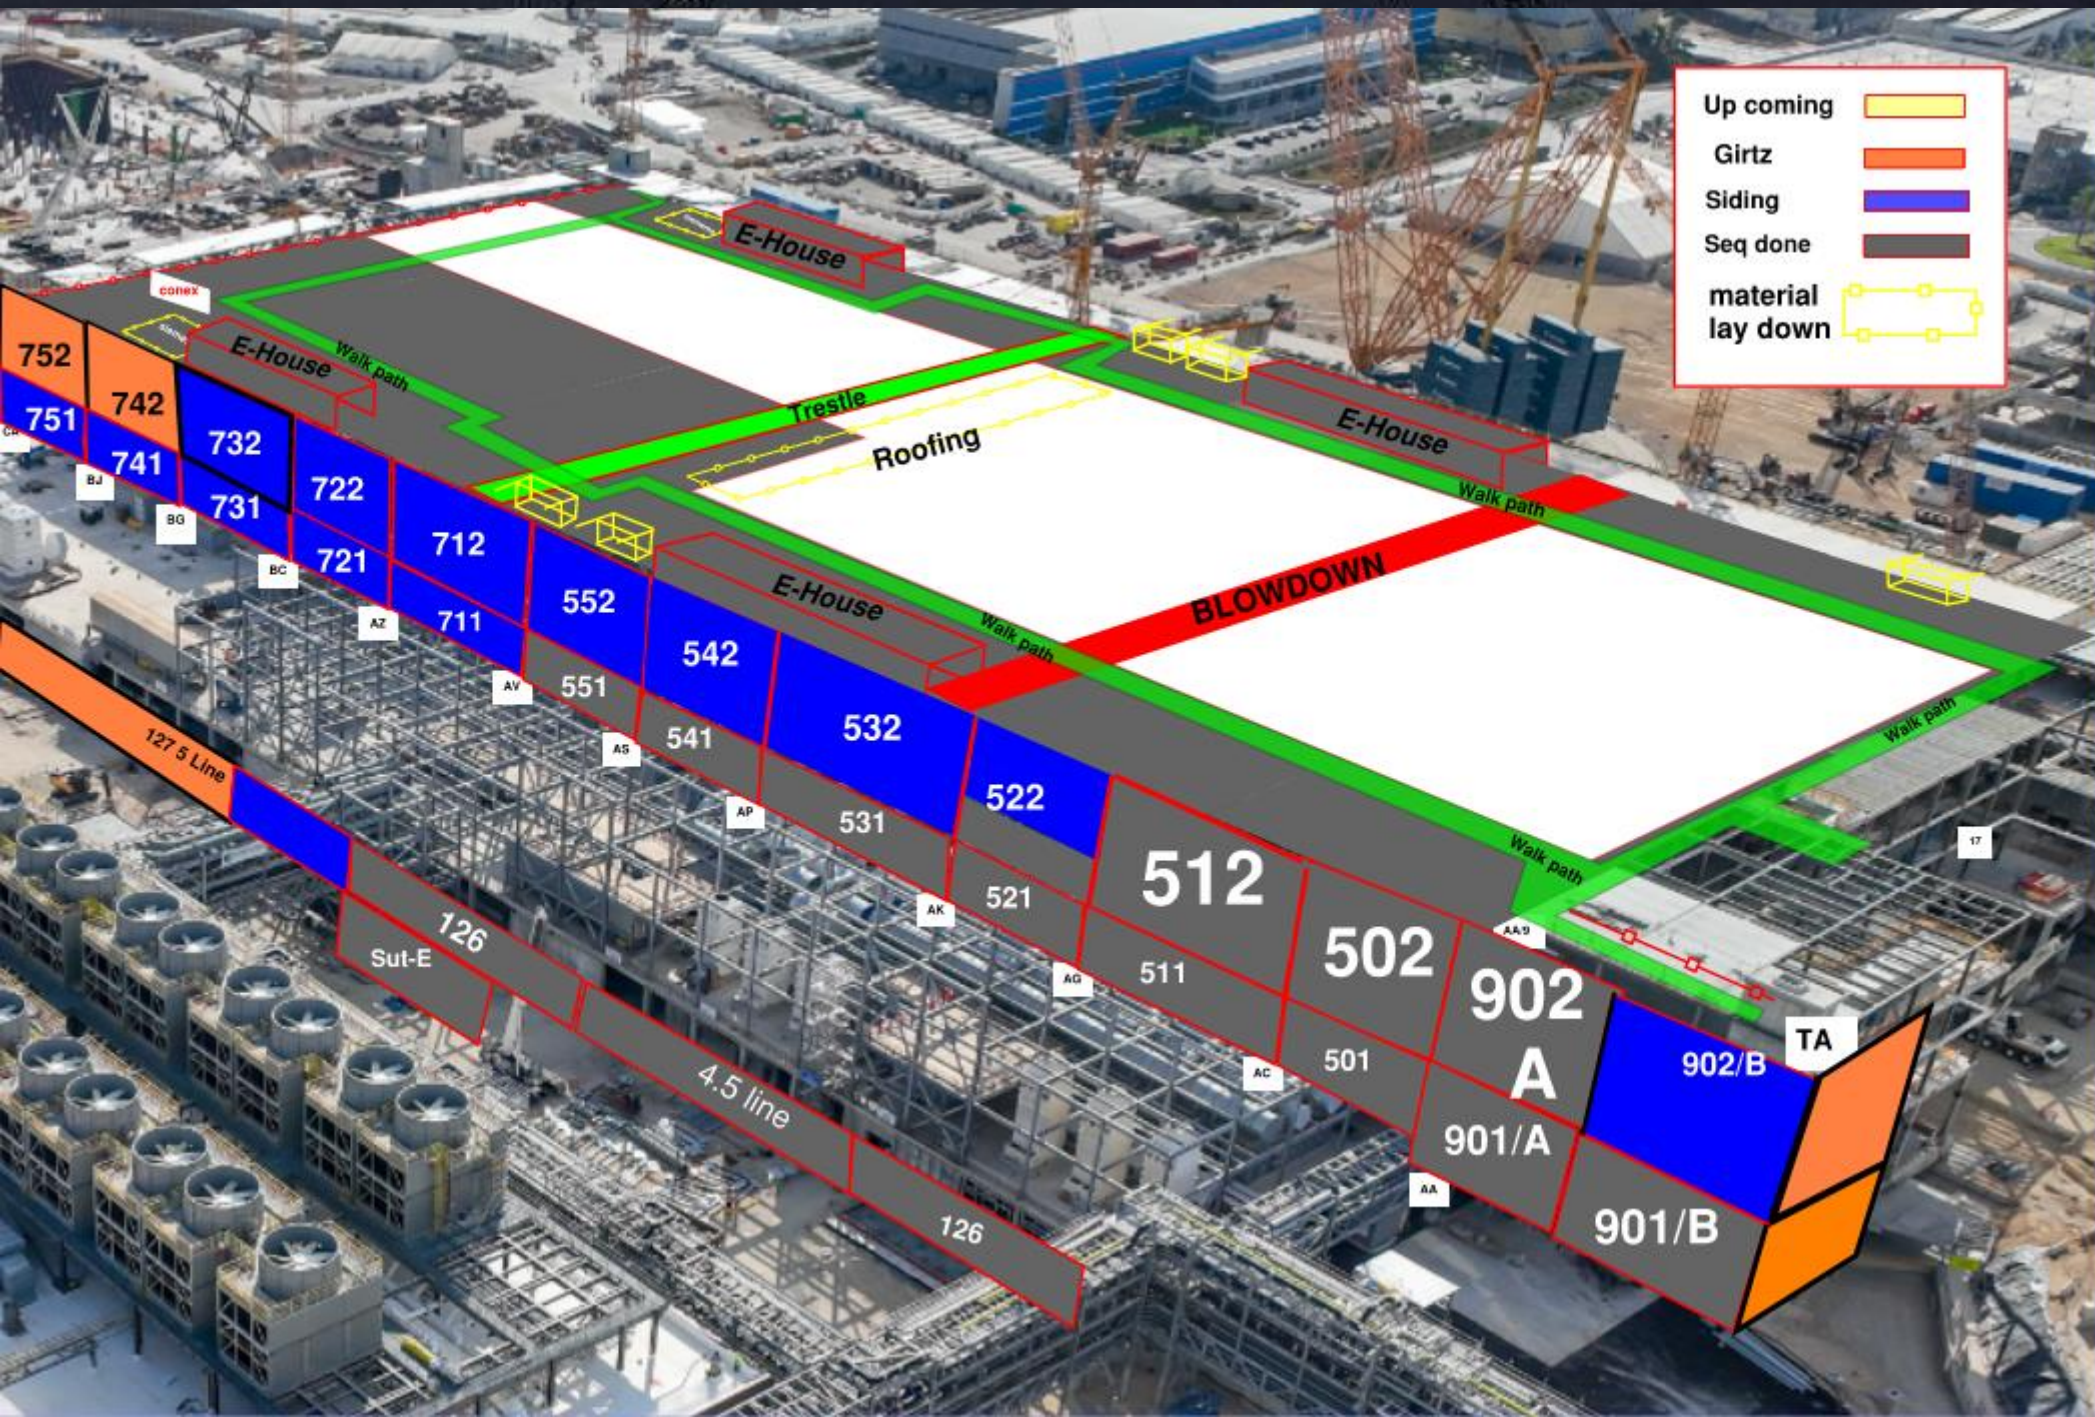

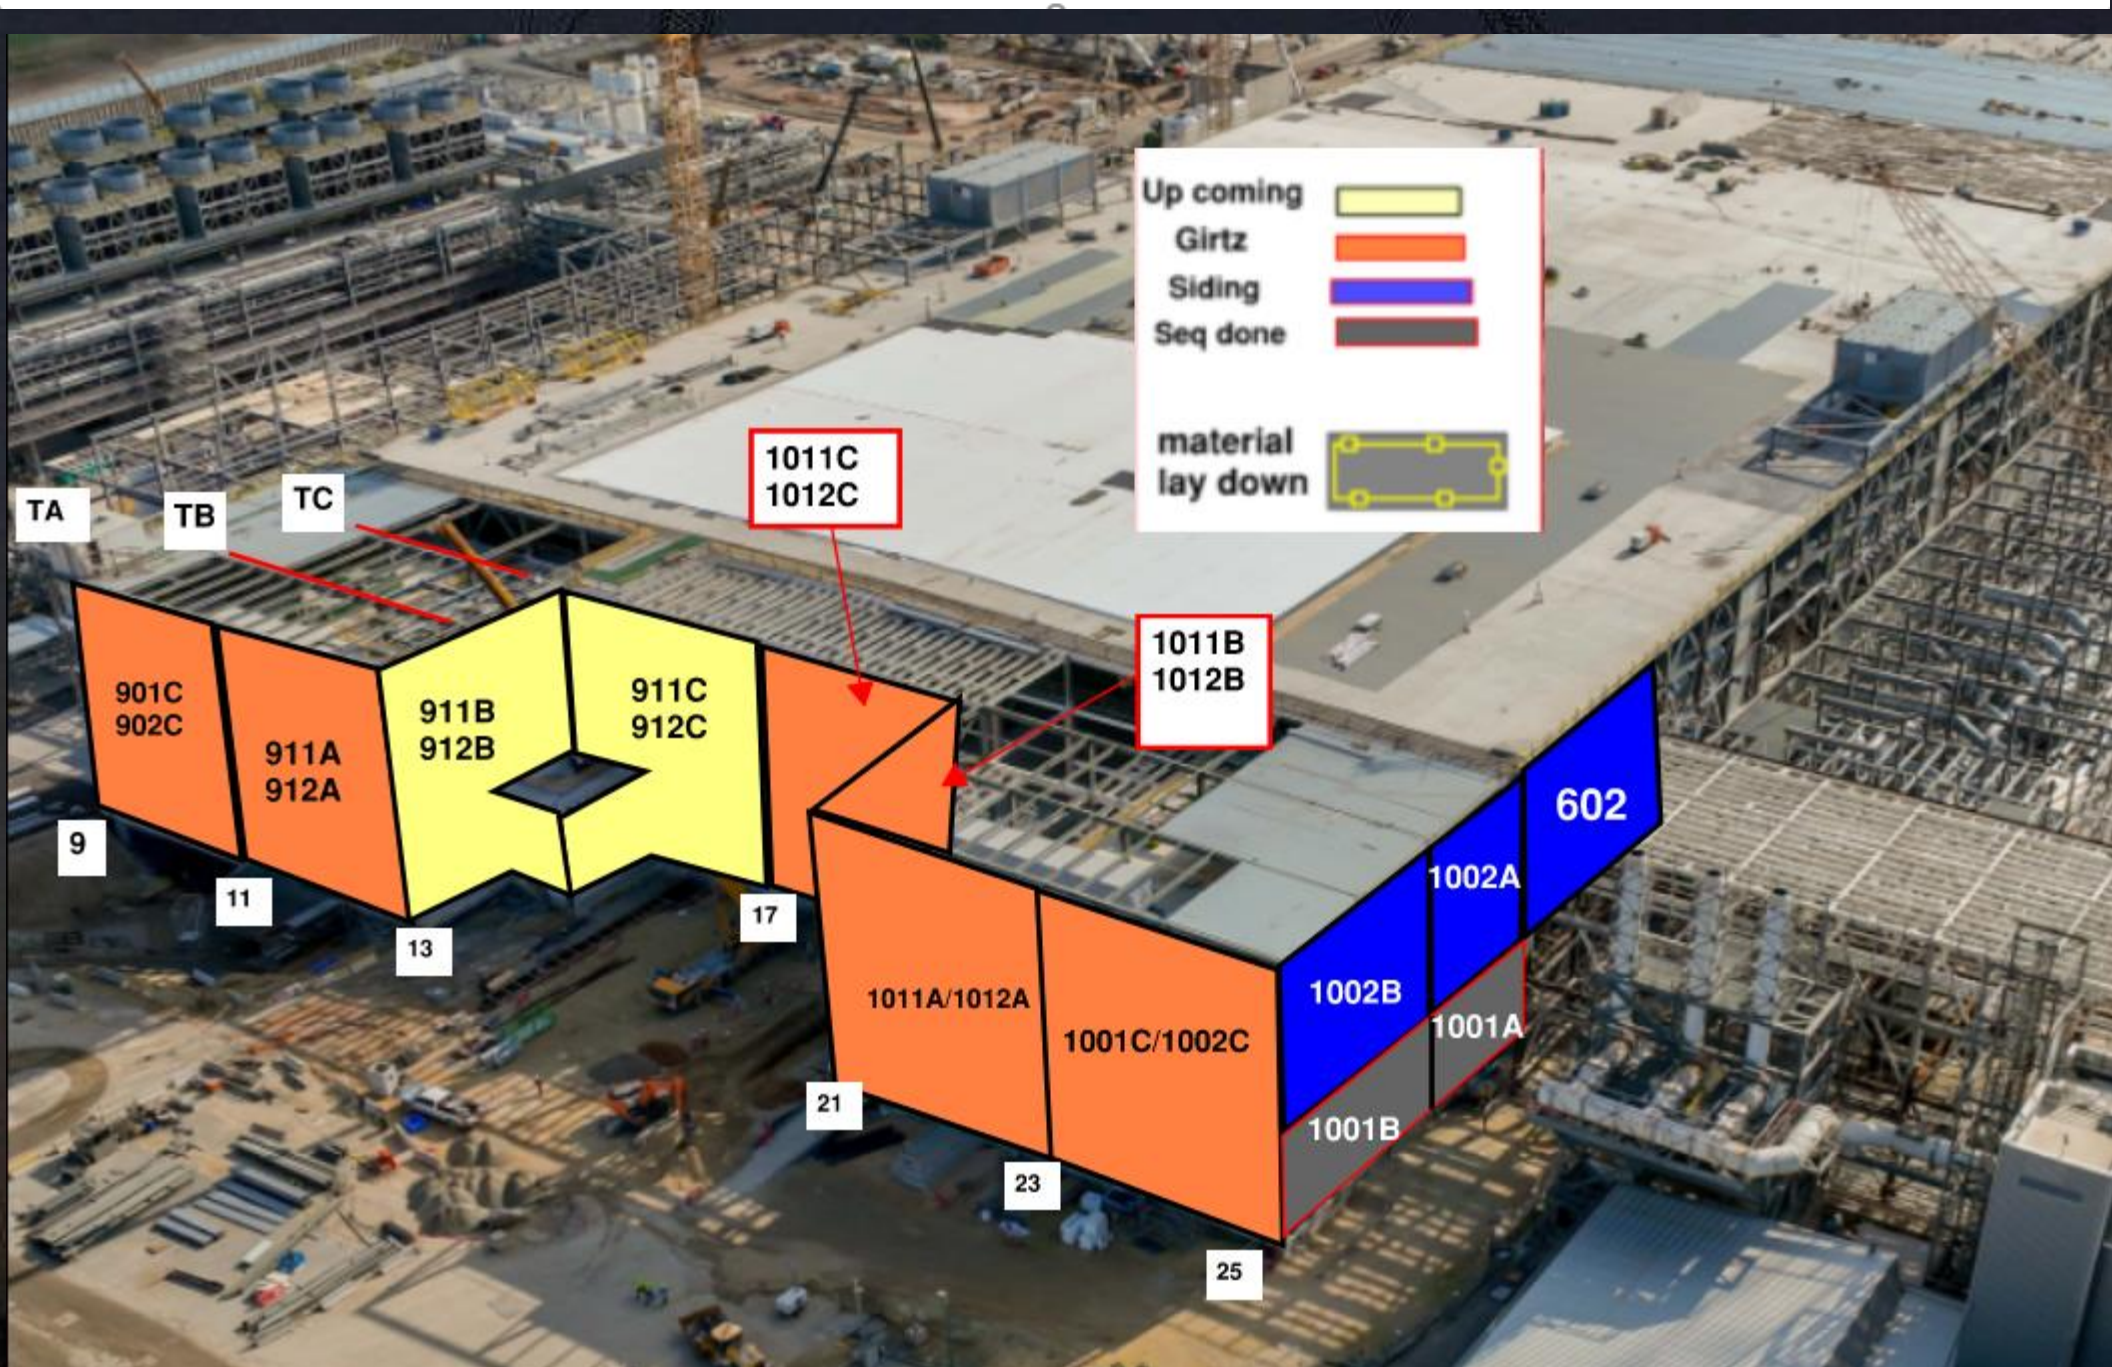

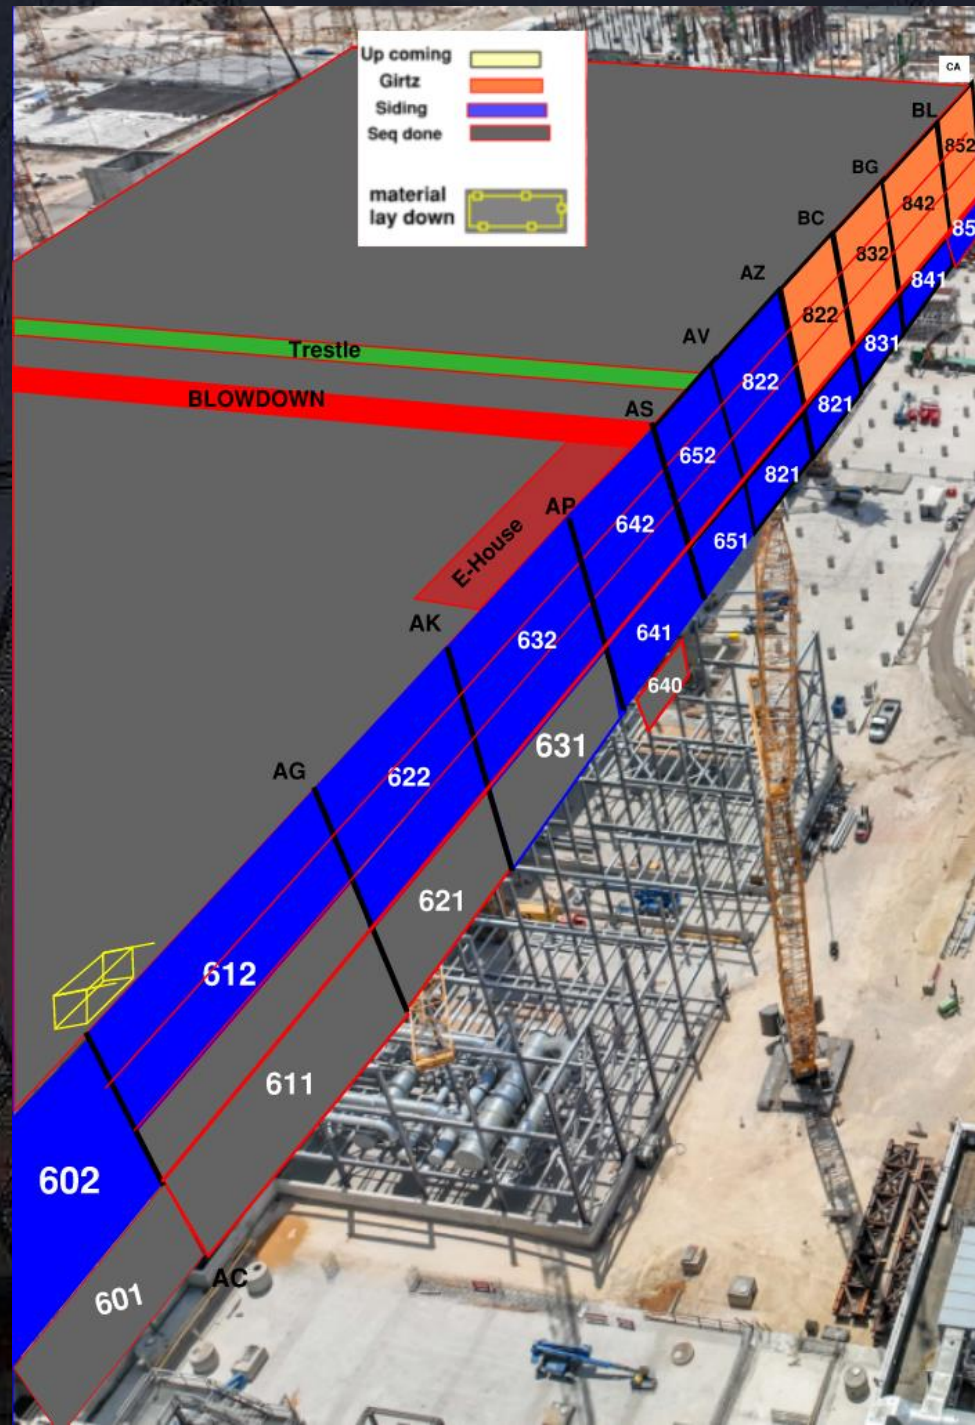

Utility Level 1YA

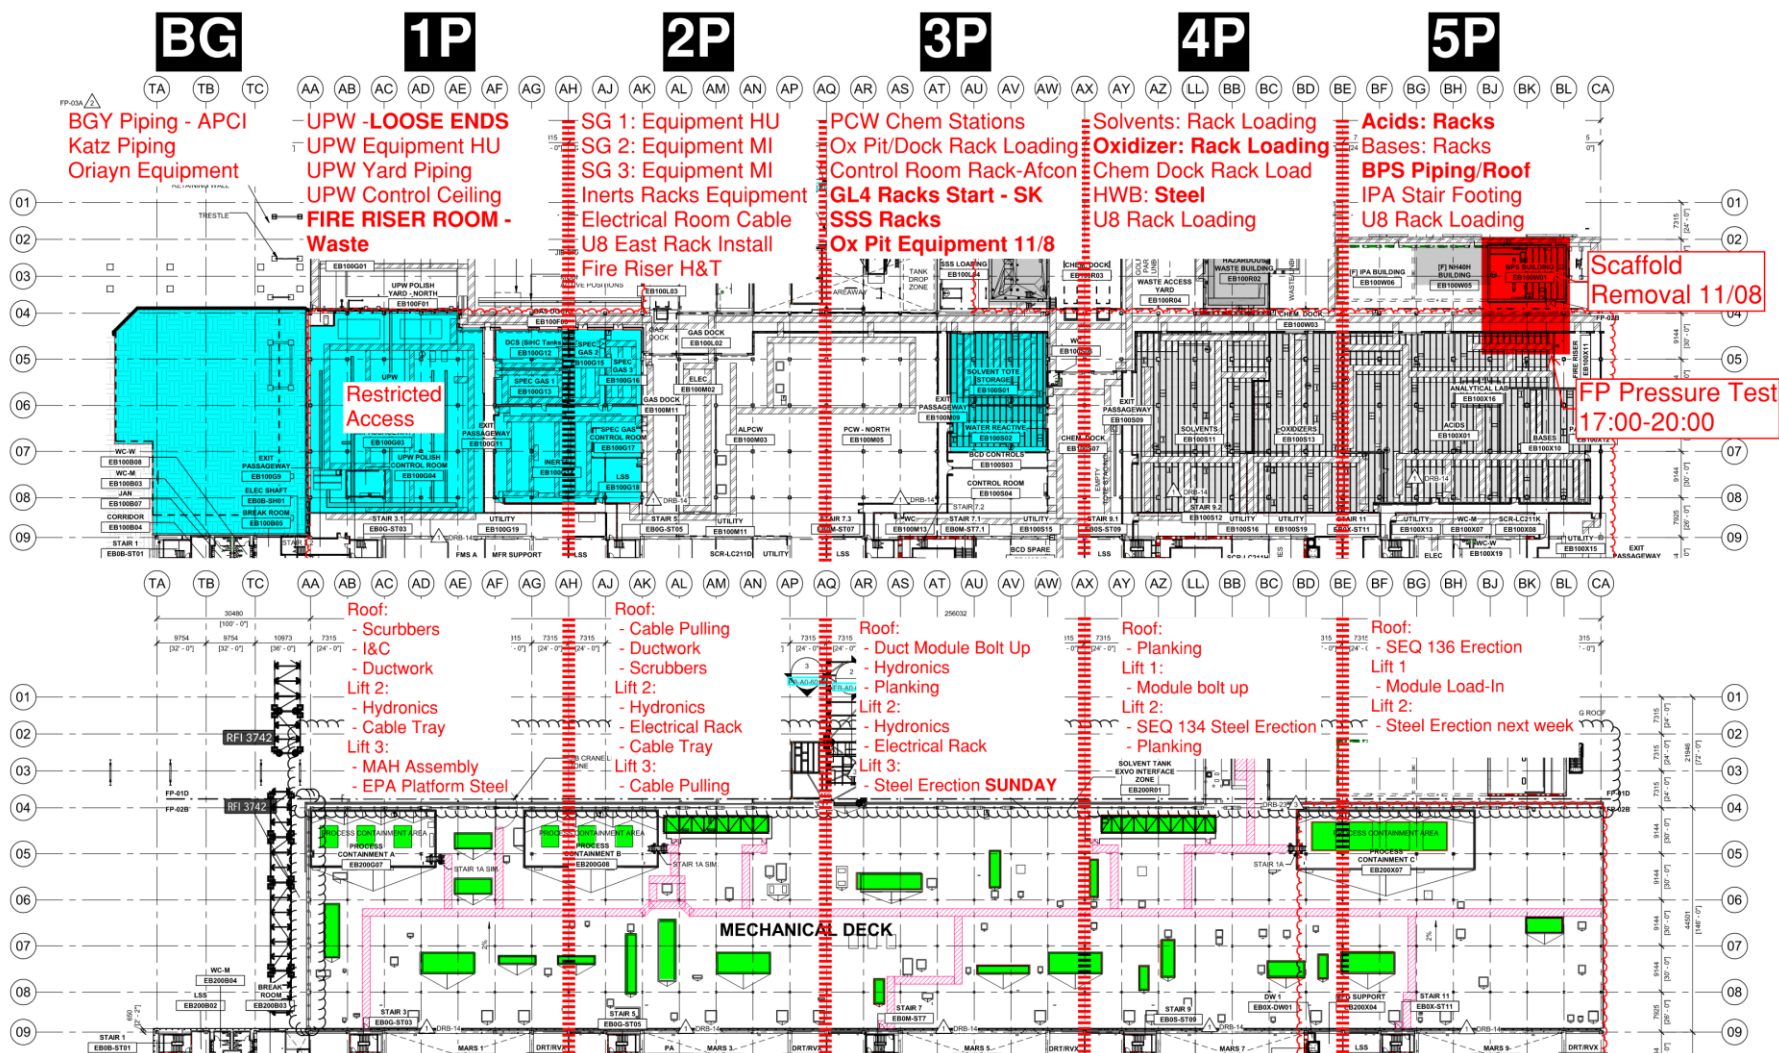


Utility Level 1YA

PSSS.2

10P


Utility Level

1YA

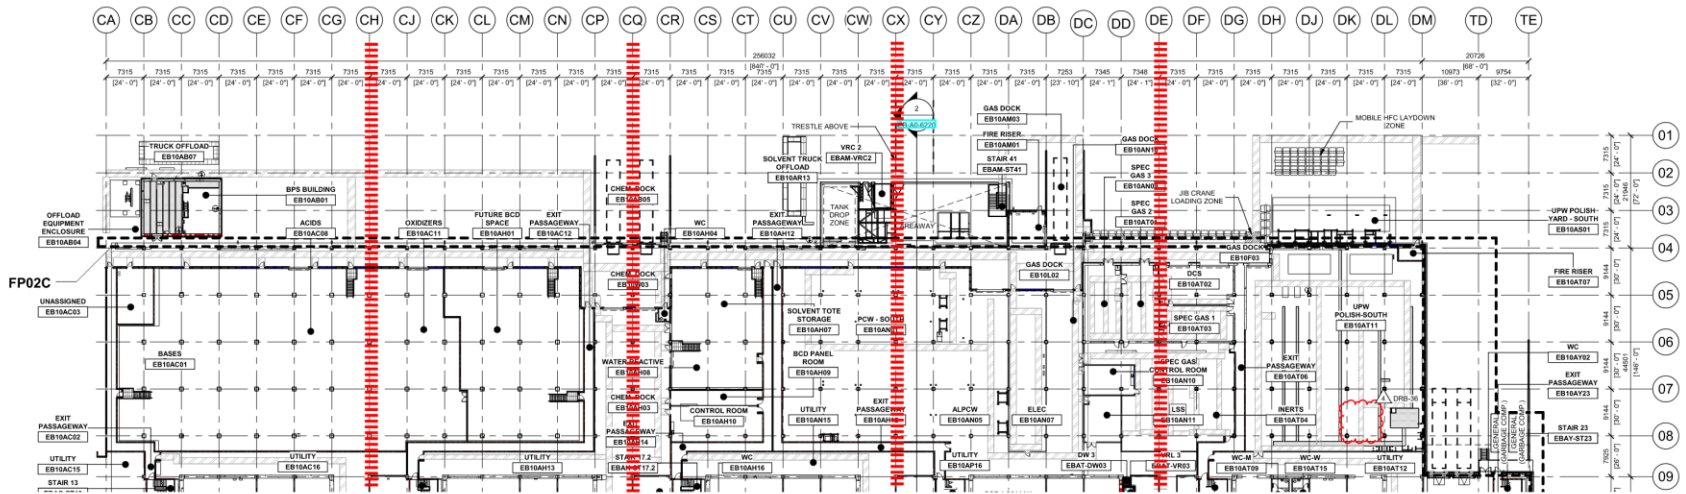


PSSS Roof 2SA

AHU Delivery 08/06

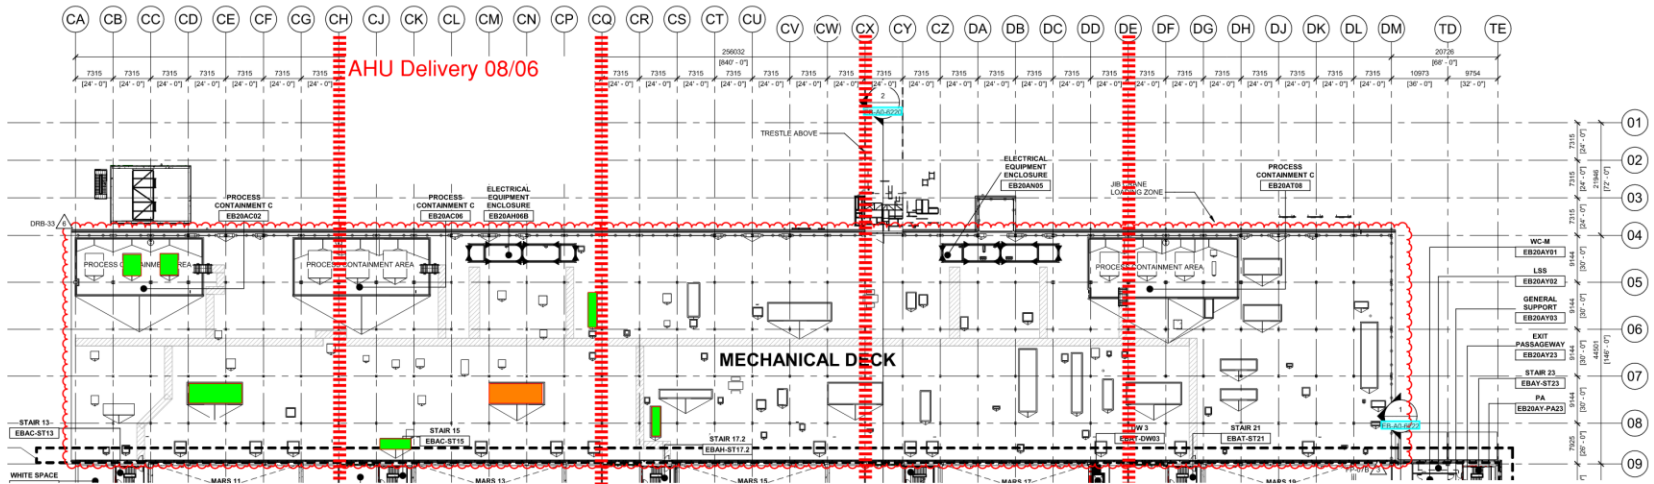




WJG 01J, 02J LIFT 2 & 3

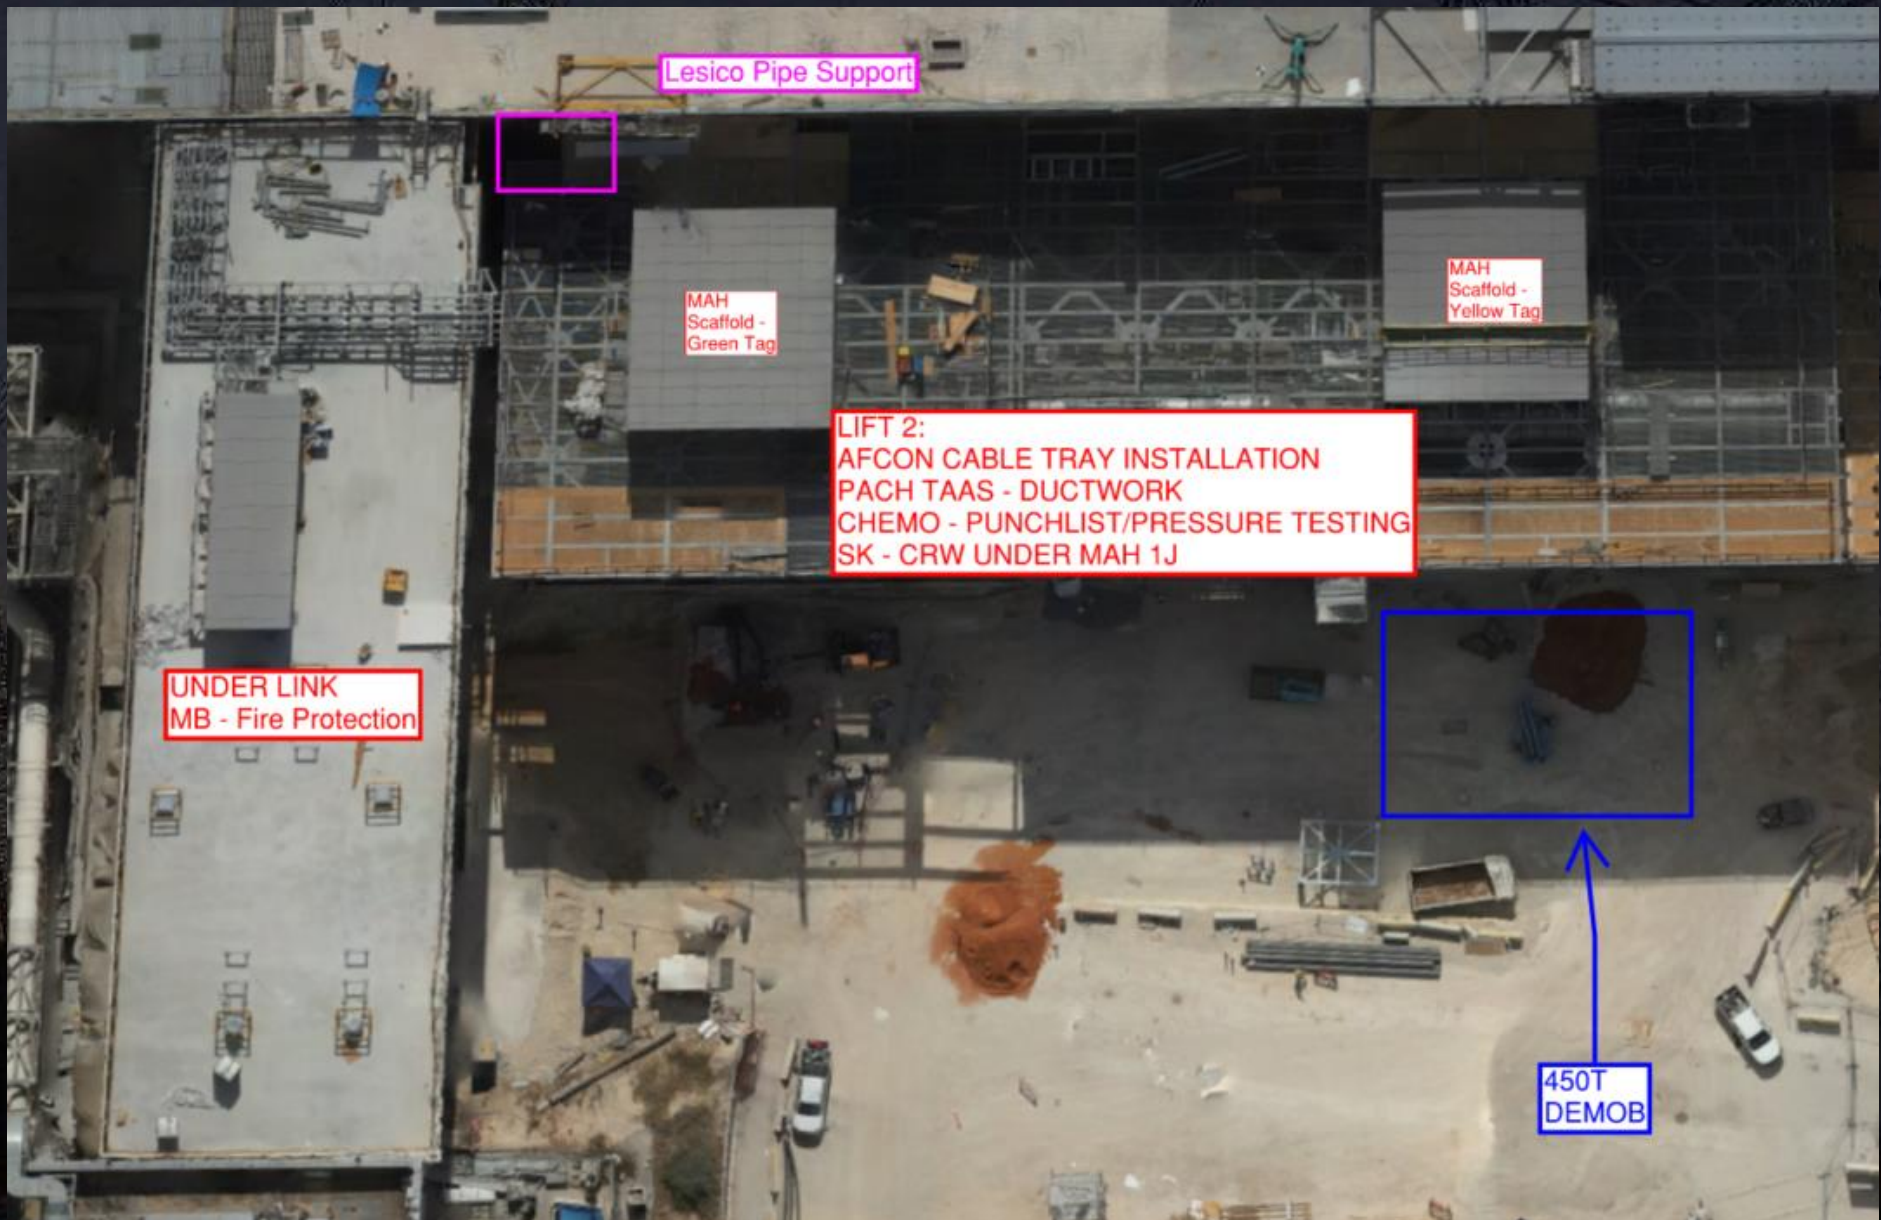



WJG 03J, 04J, 05J LIFT 2 & 3

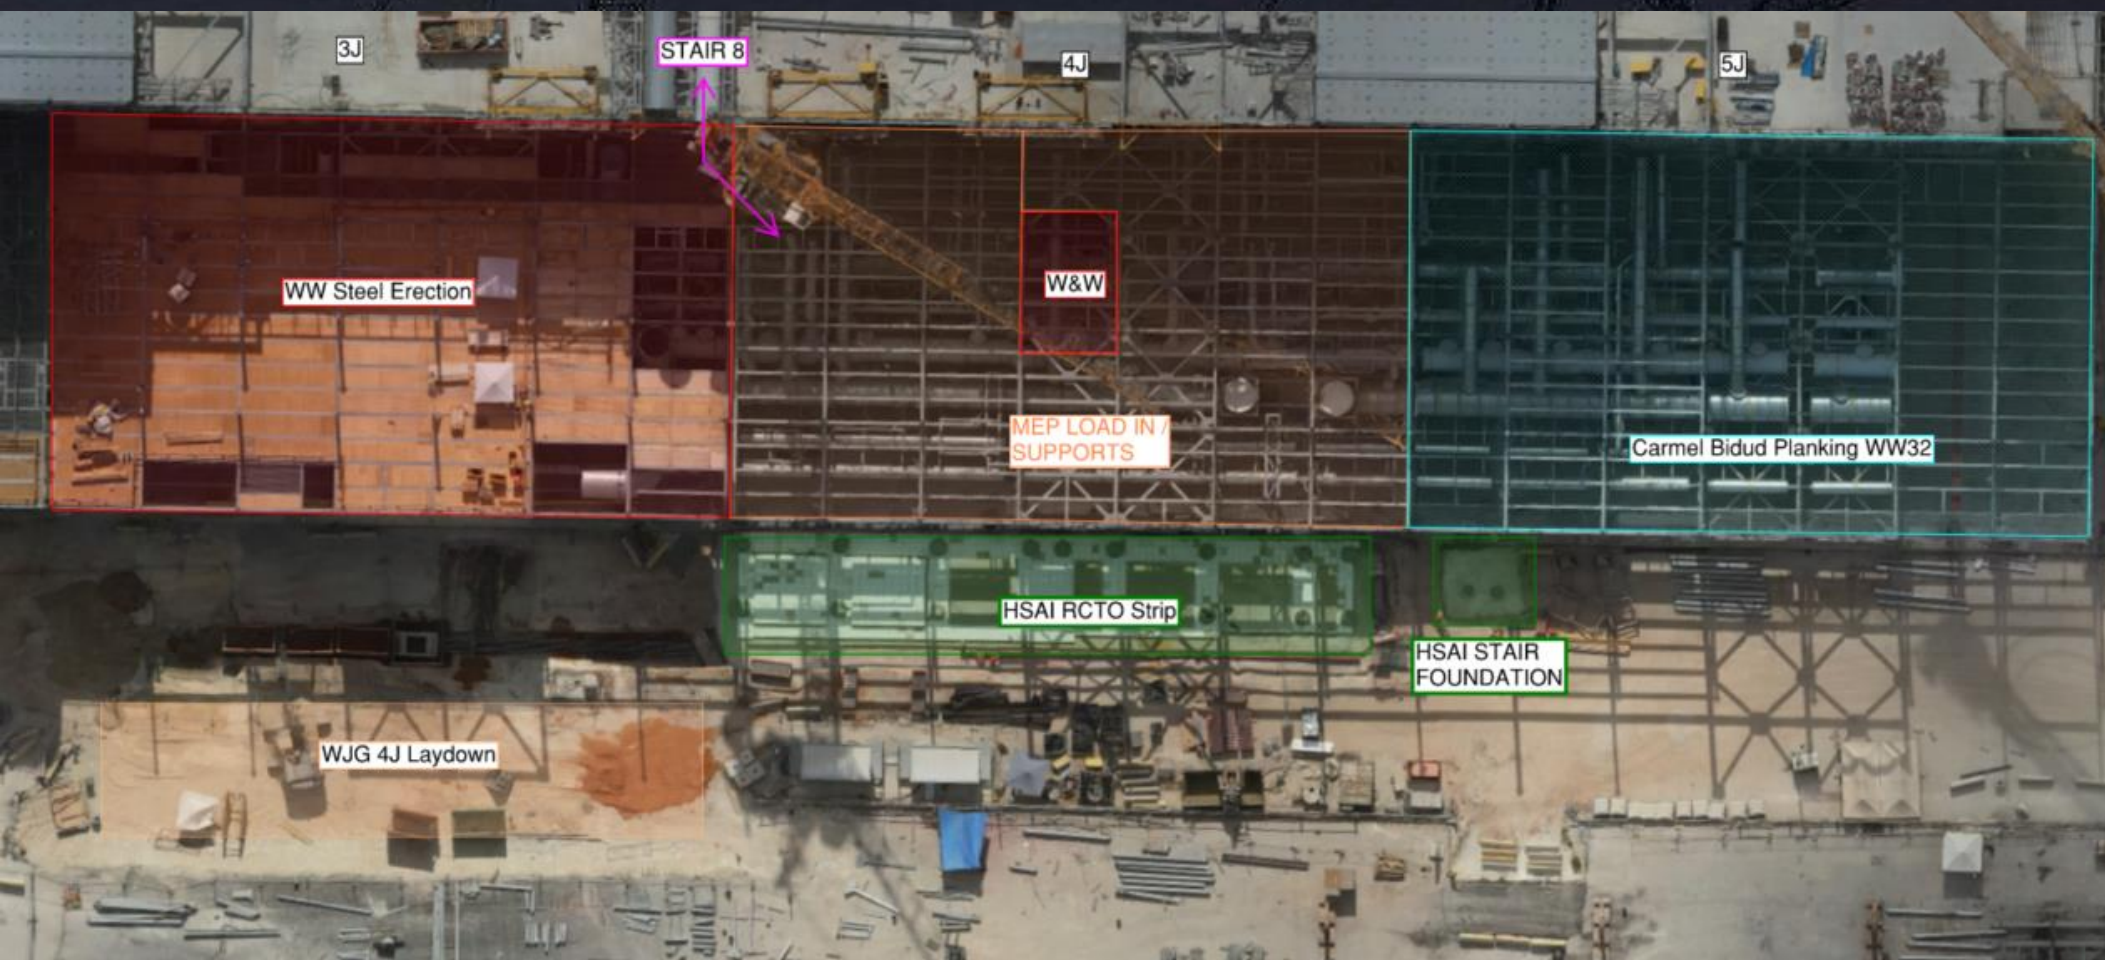




WJG UTILITY LEVEL BUILD OUT

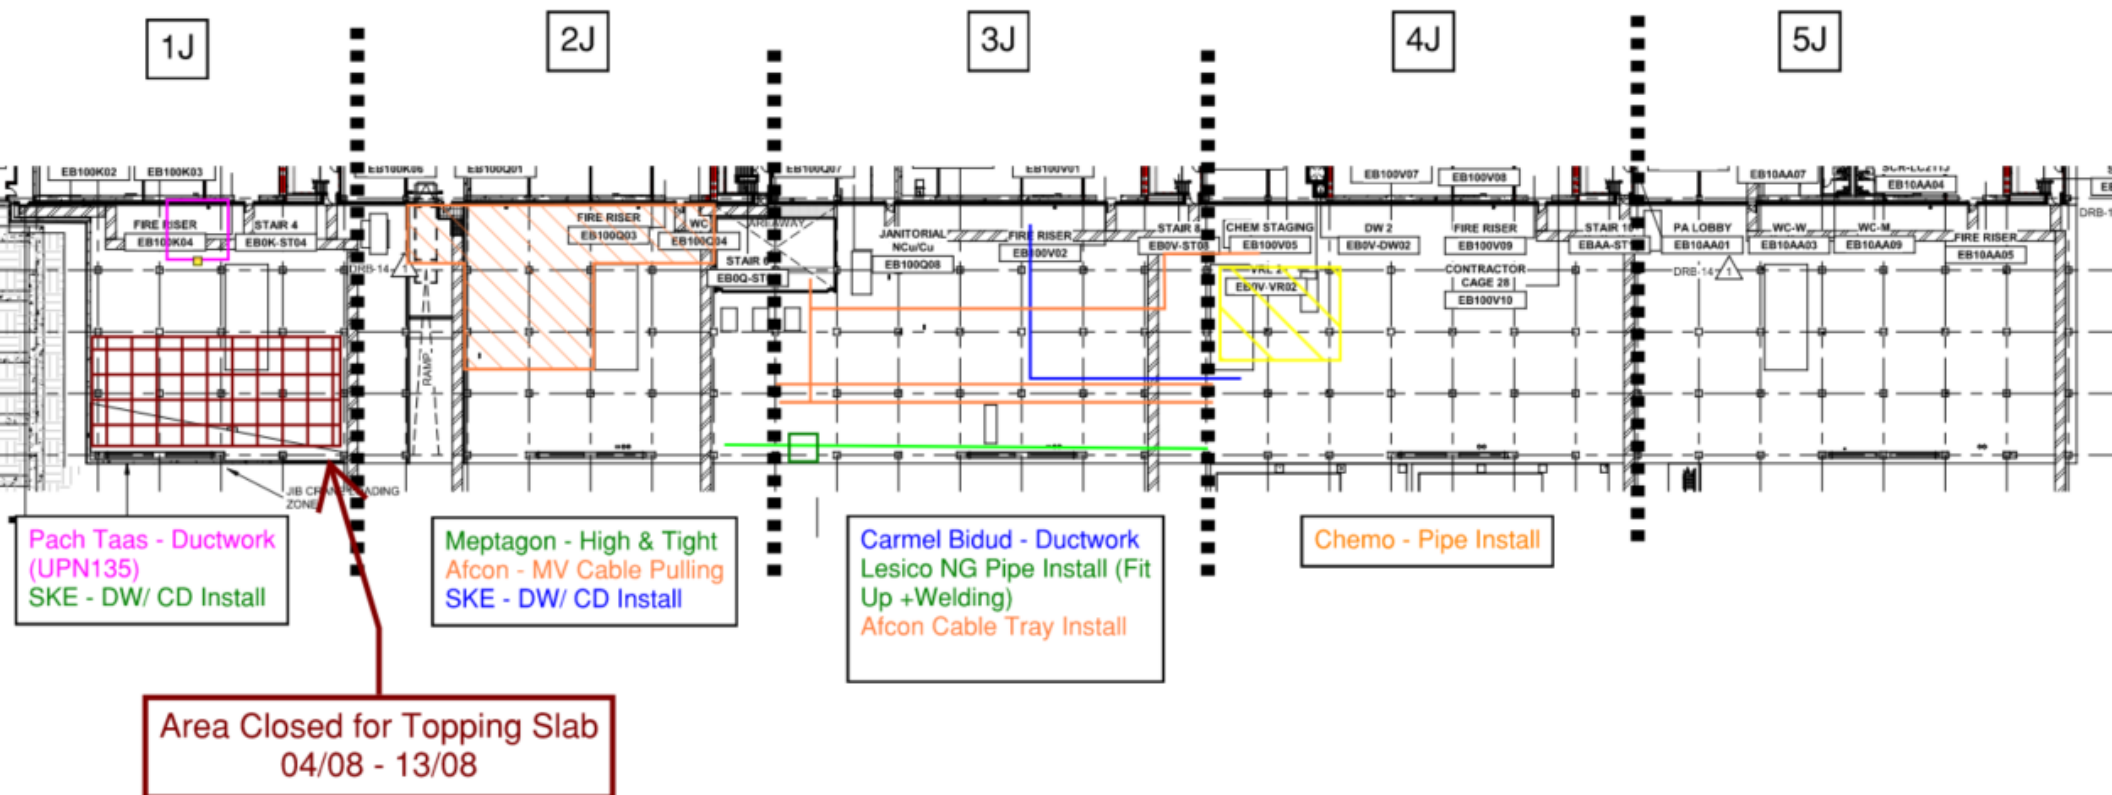


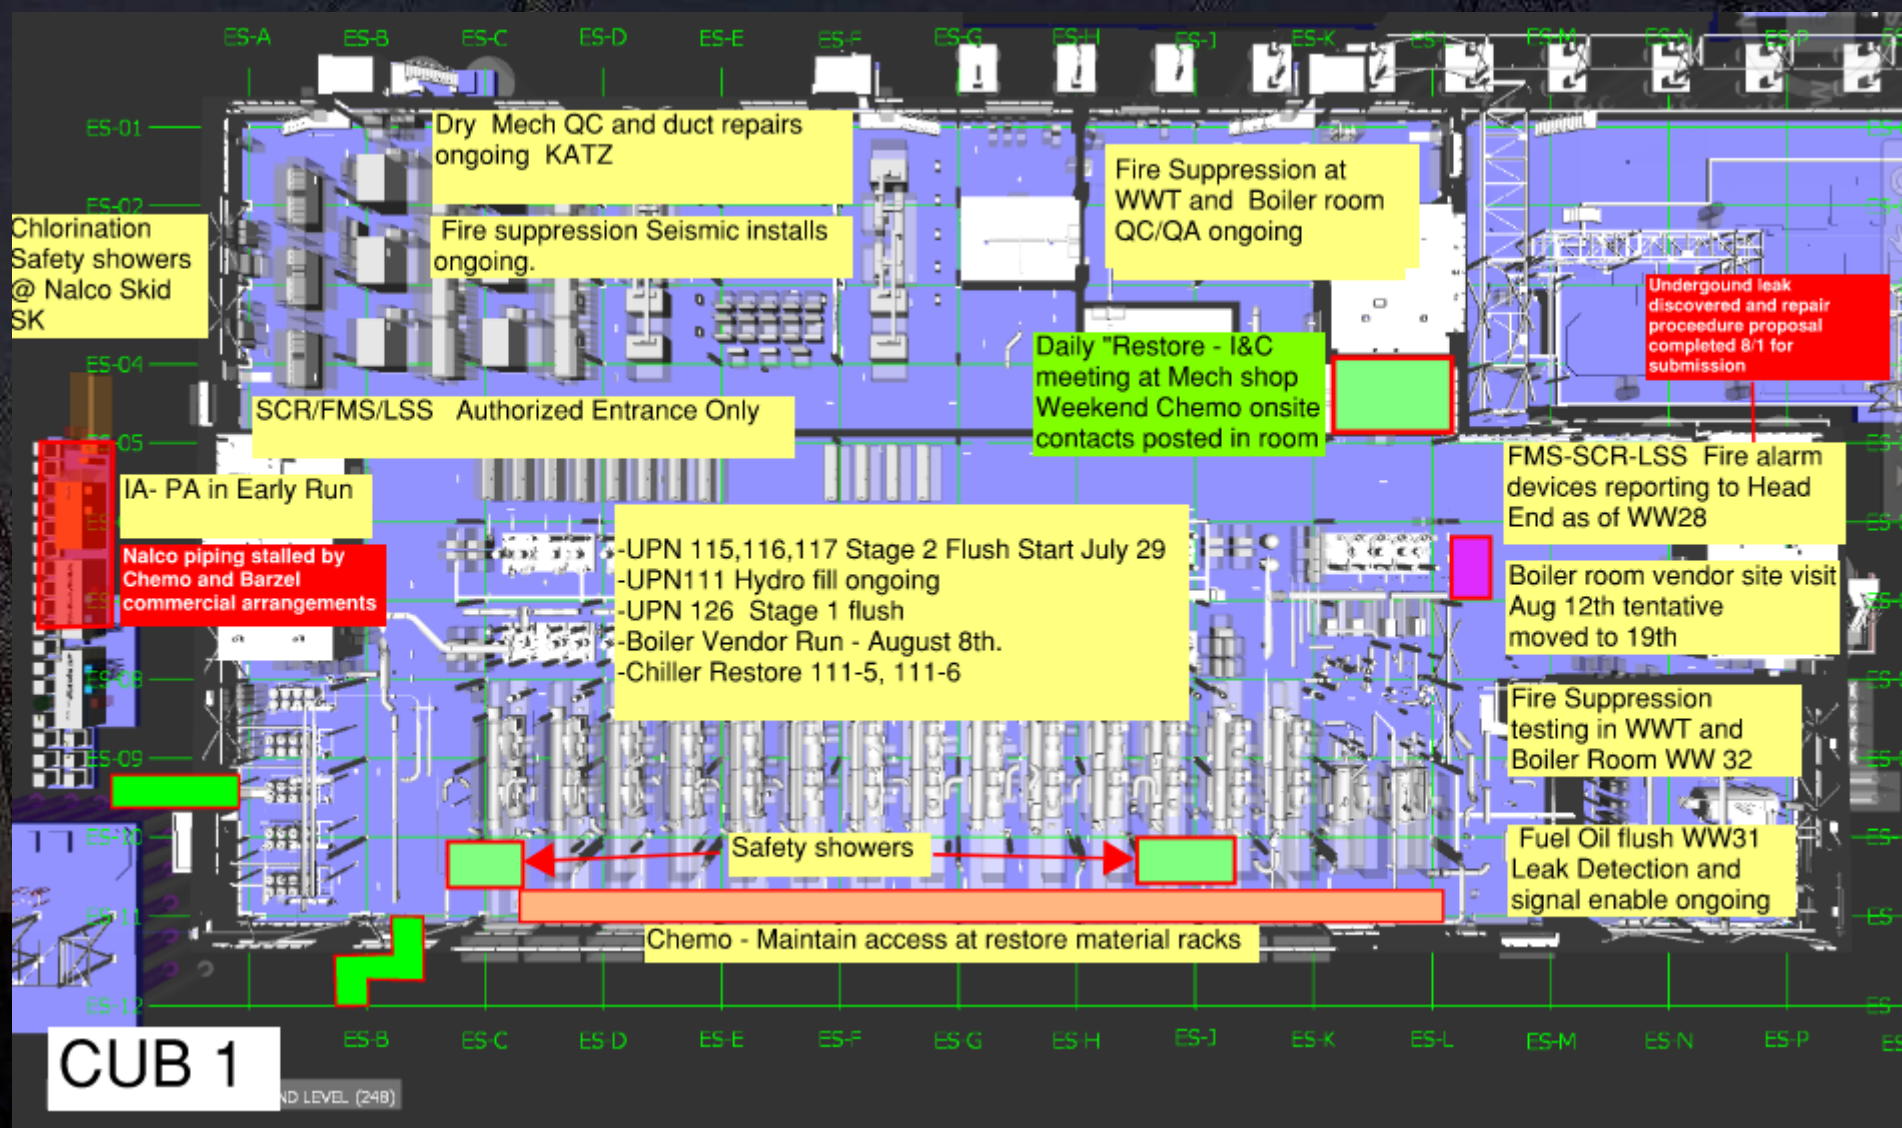


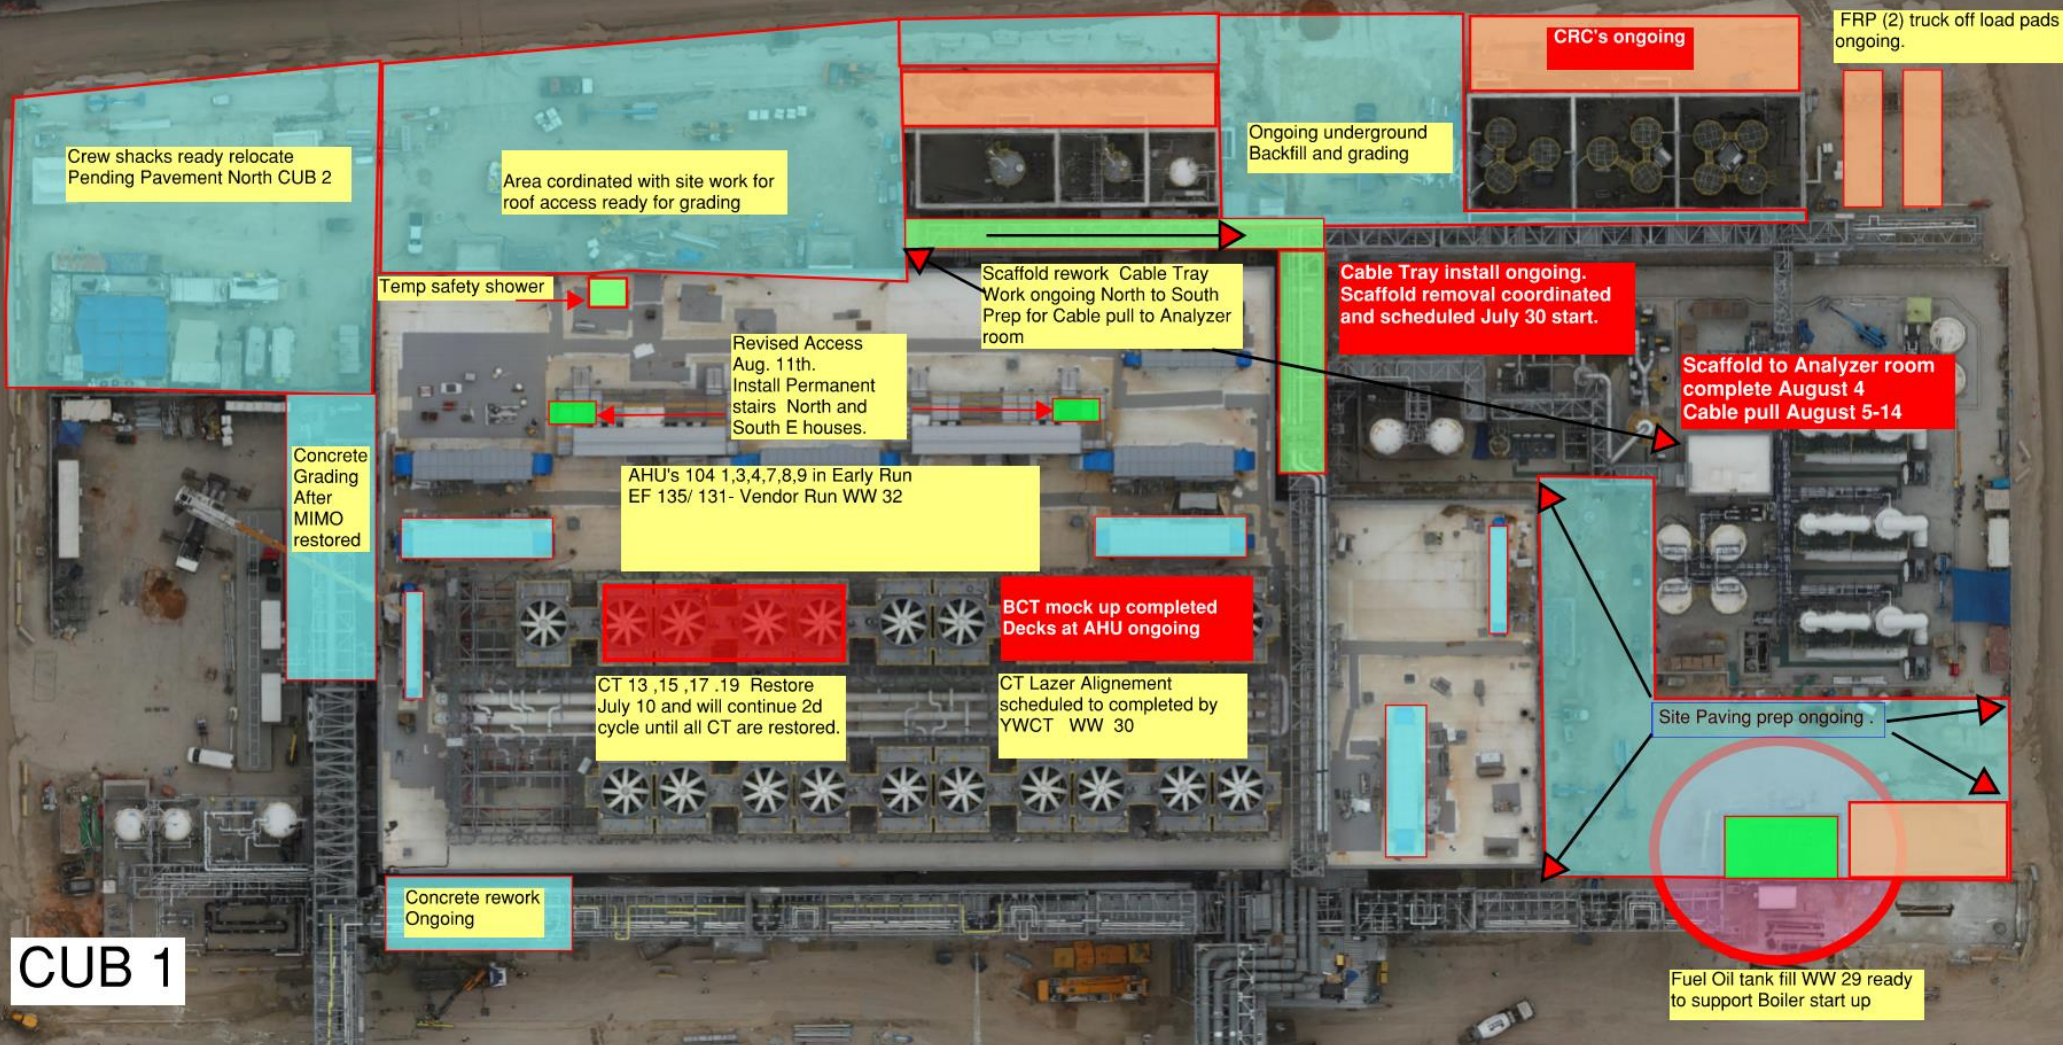




HOFFMAN CONSTRUCTION COMPANY

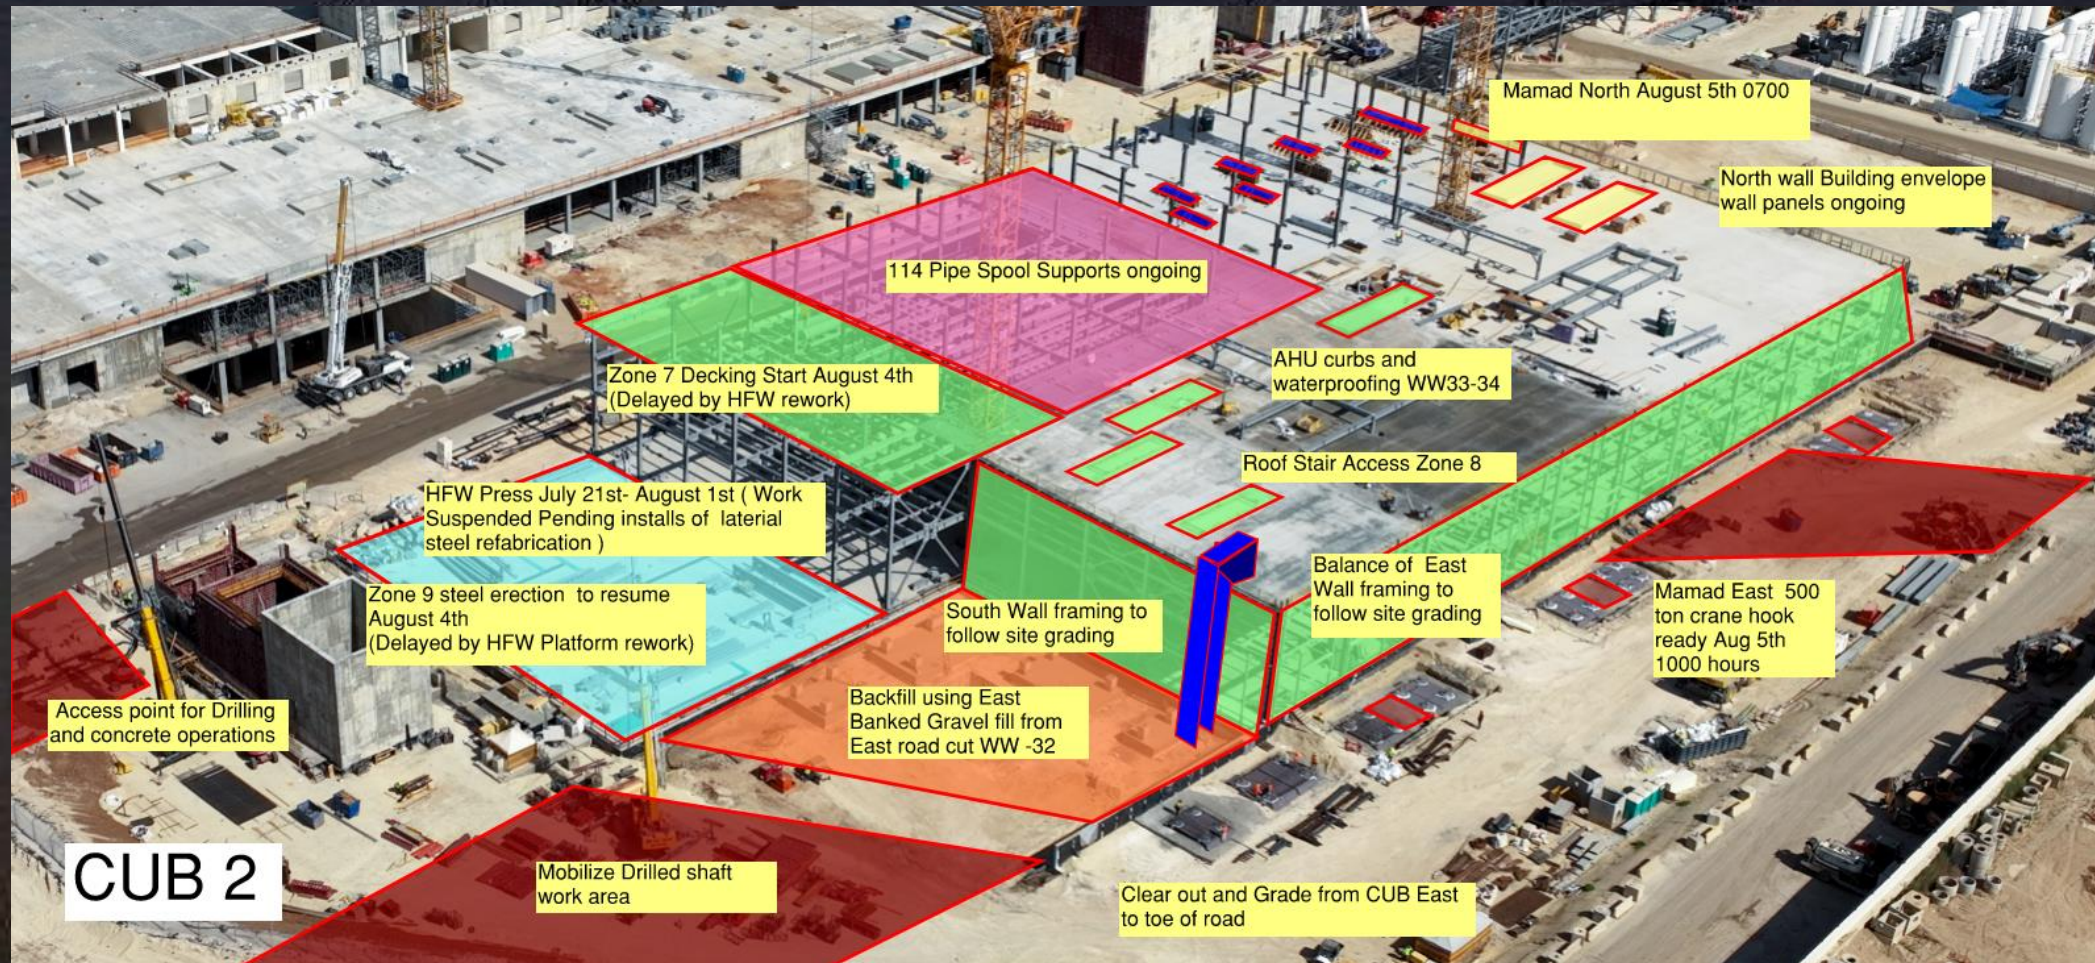

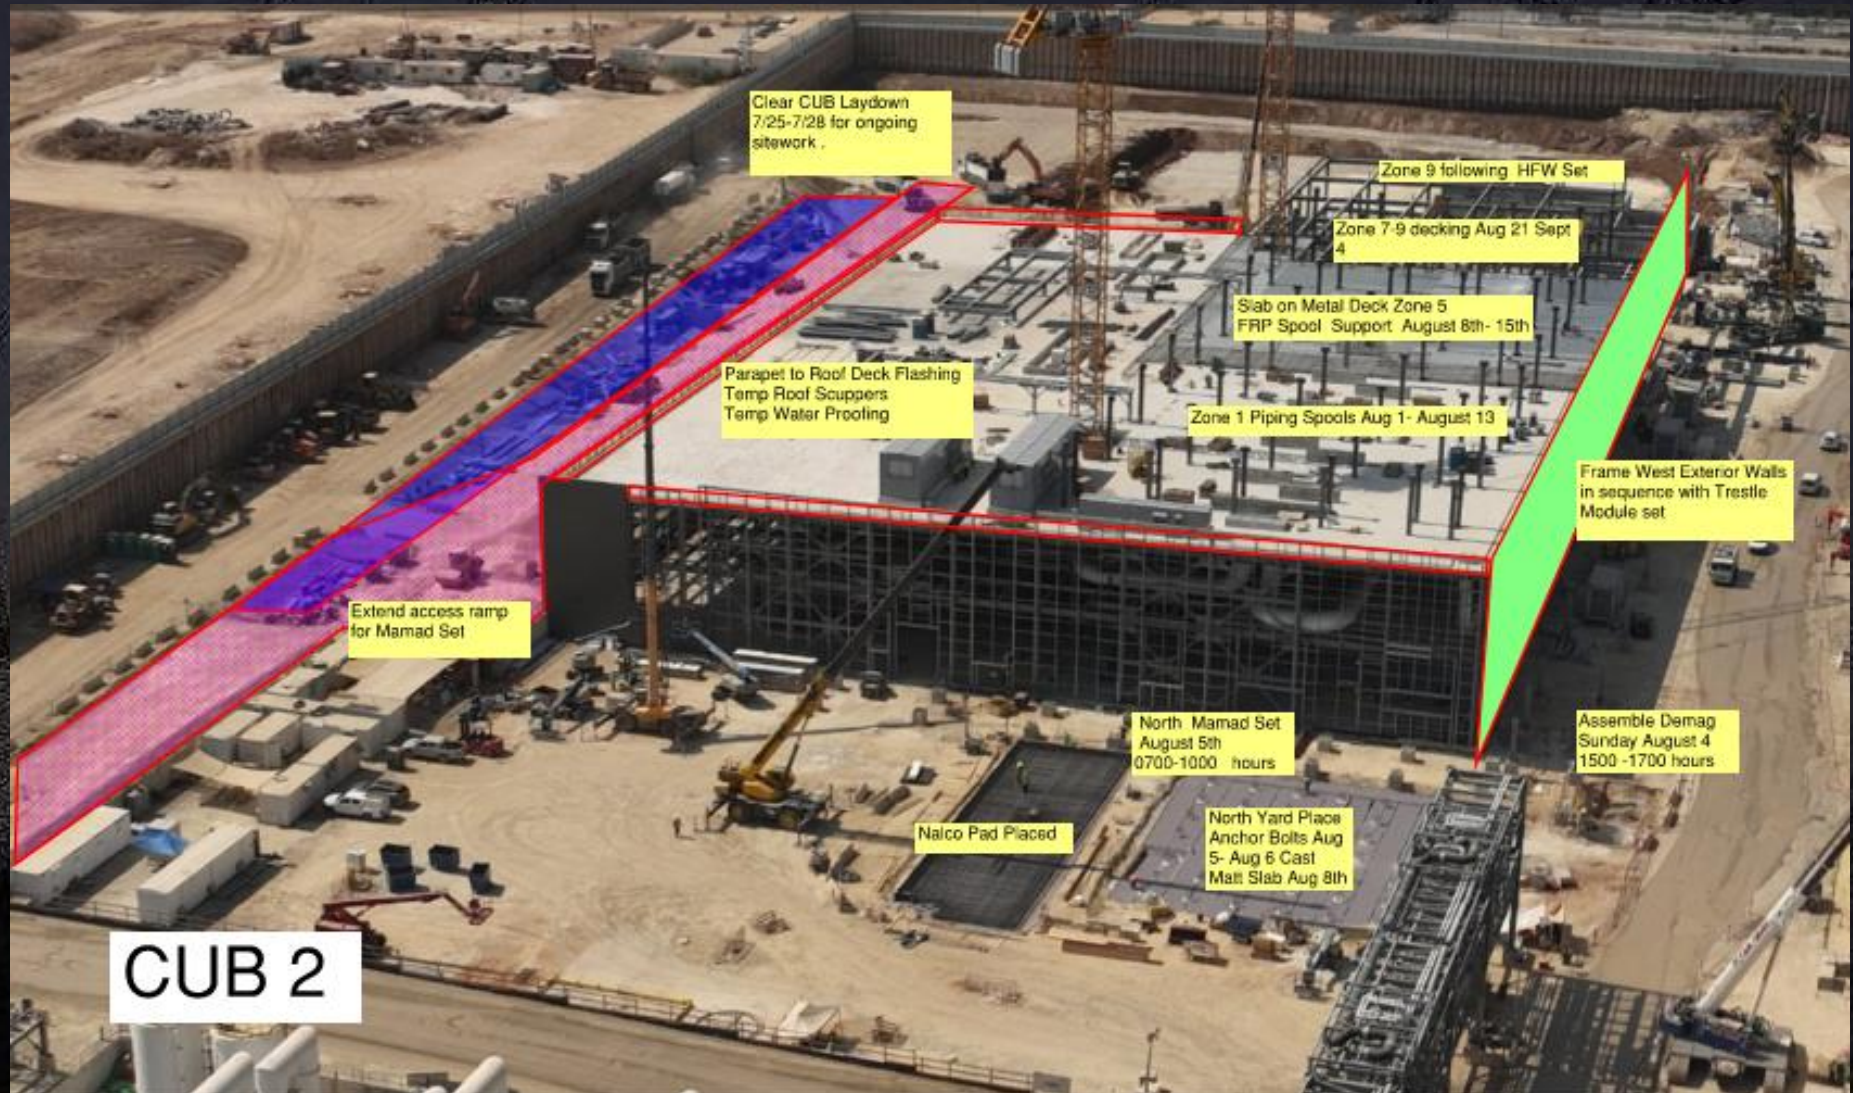

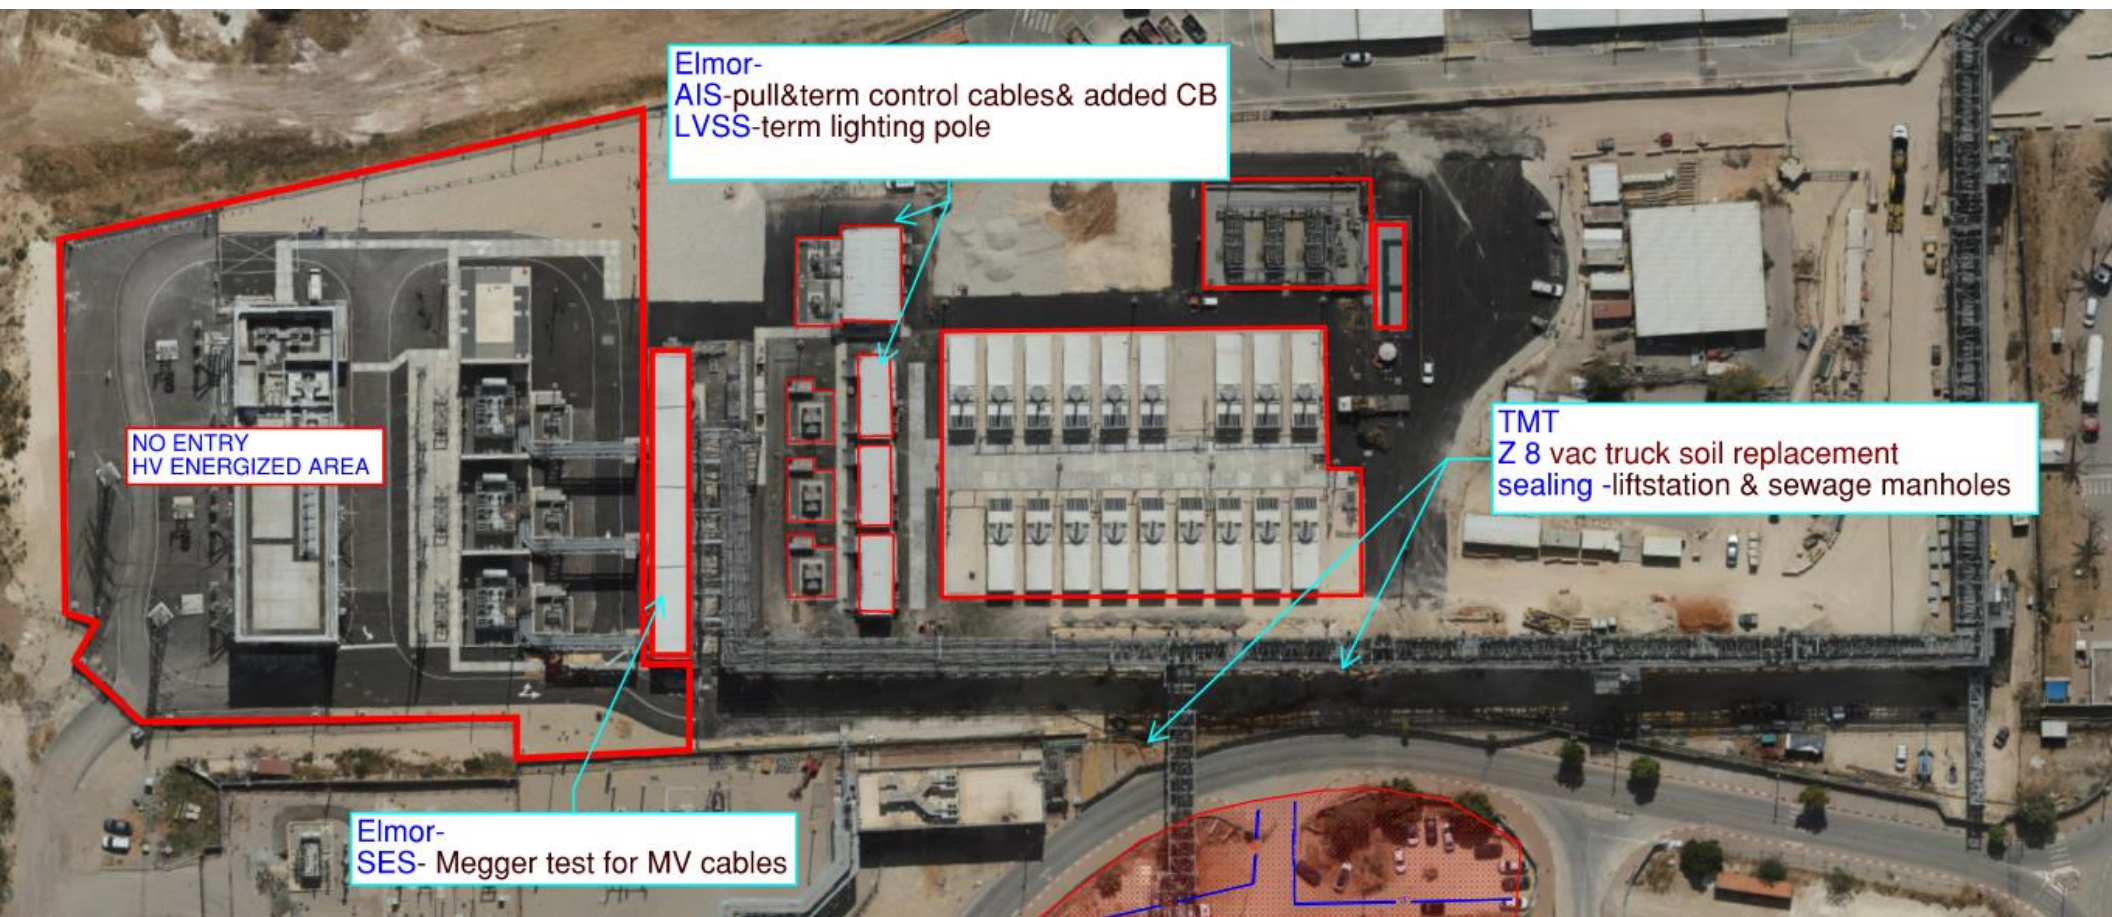


NO ENTRY
HV ENERGIZED AREA

Elmor-
AIS-pull&term control cables& added CB
LVSS-term lighting pole

Elmor-
SES- Megger test for MV cables

TMT
Z 8 vac truck soil replacement
sealing -liftstation & sewage manholes

FAB GIS PERMENENT POWER
AUGUST 8TH 4PM.

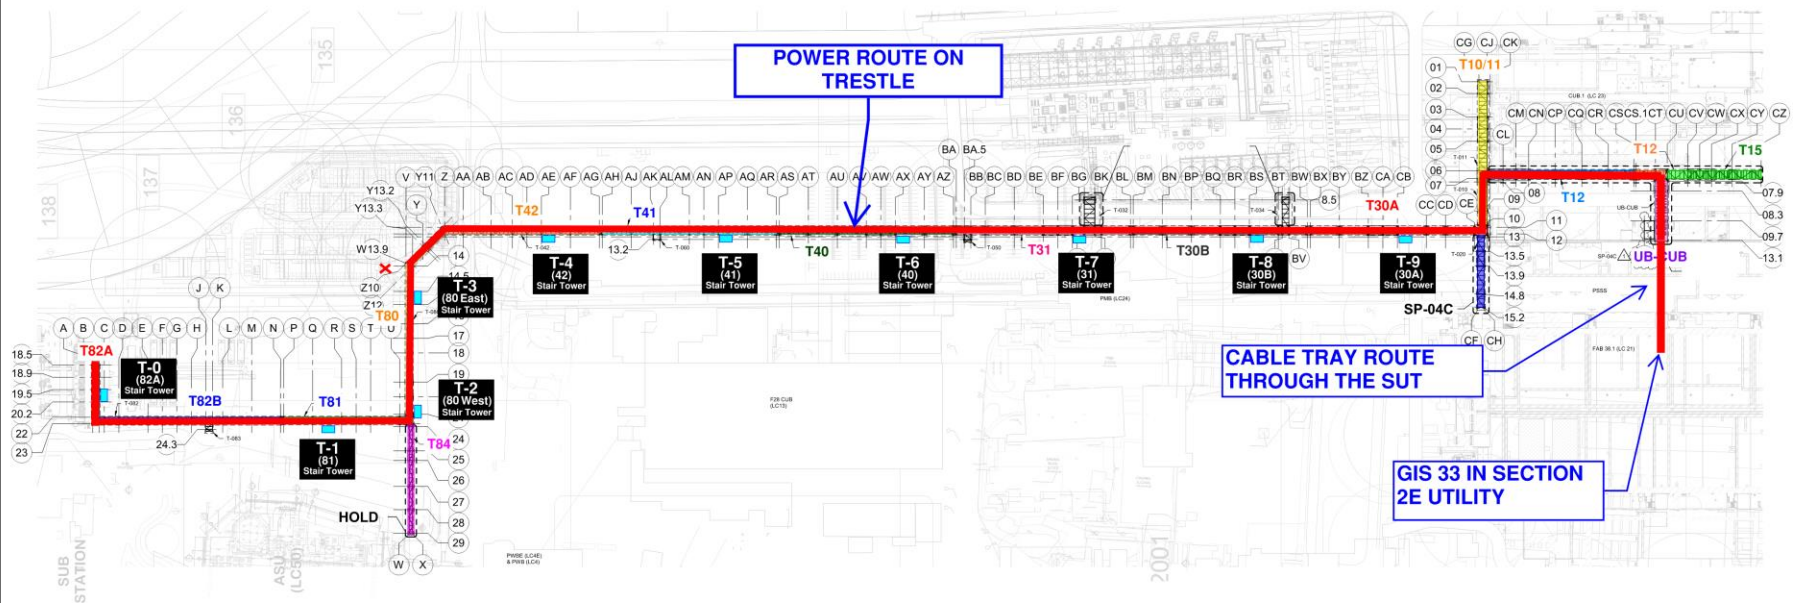



Trestle - MOD 2 Steel erection

T-17 Lvl 1

August 14

August 11

August 13

August 18

August 15


August 8

August 12

#3

#1

#2

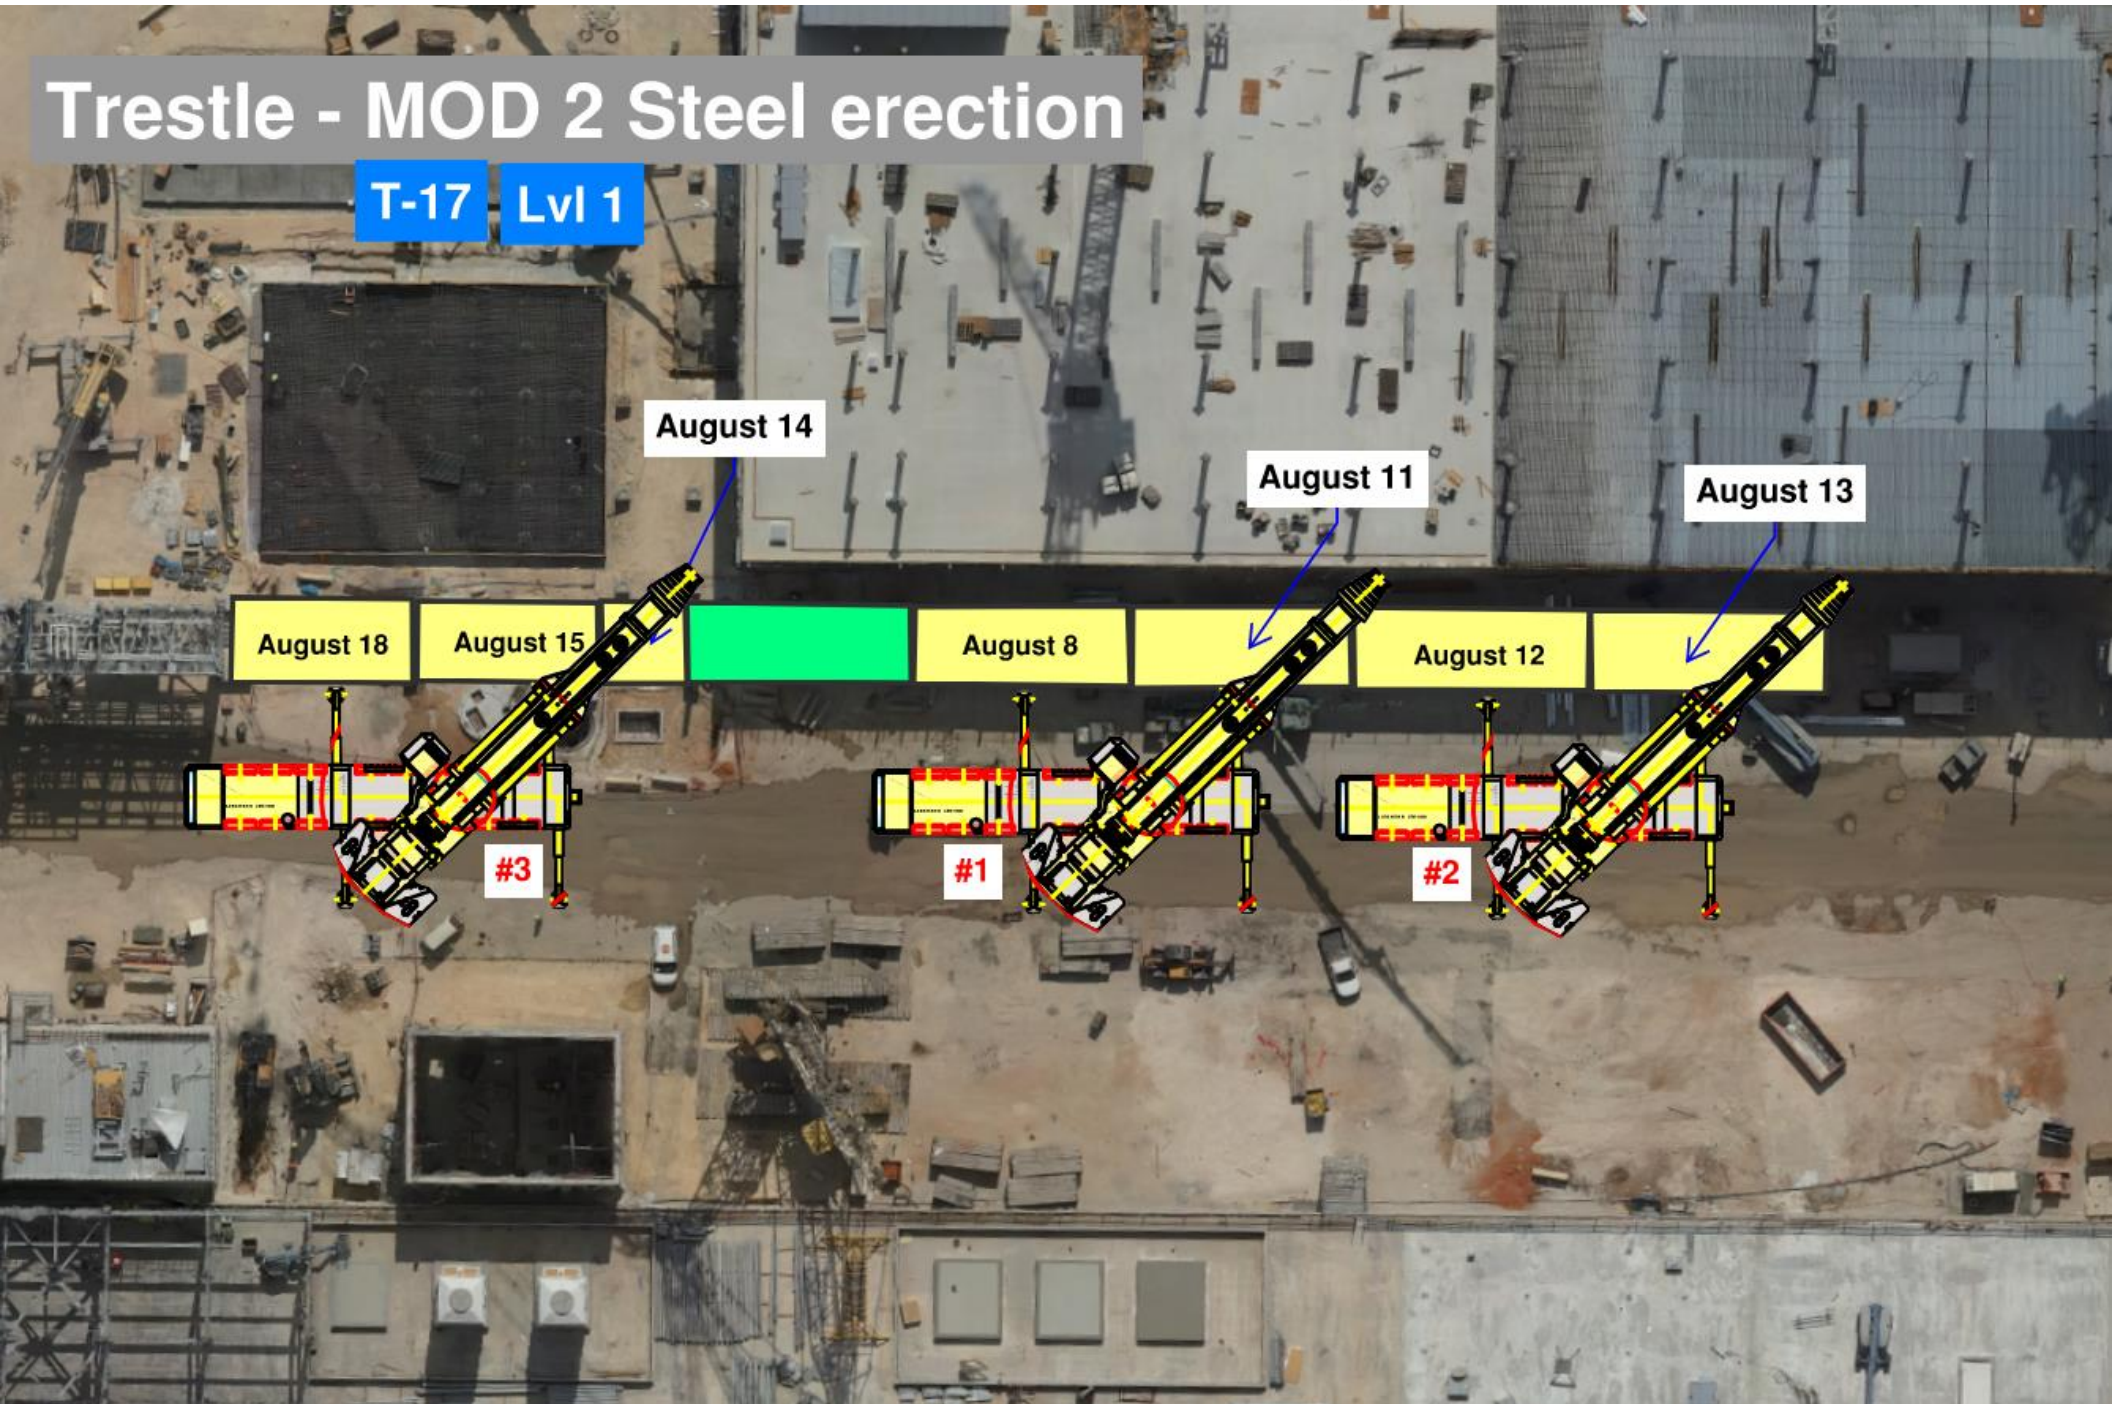

Trestle - MOD 2 Steel erection

T-17 Lvl 2

August 19

August 25

August 27

August 21

August 20


August 22

August 26

#1


#2

#3

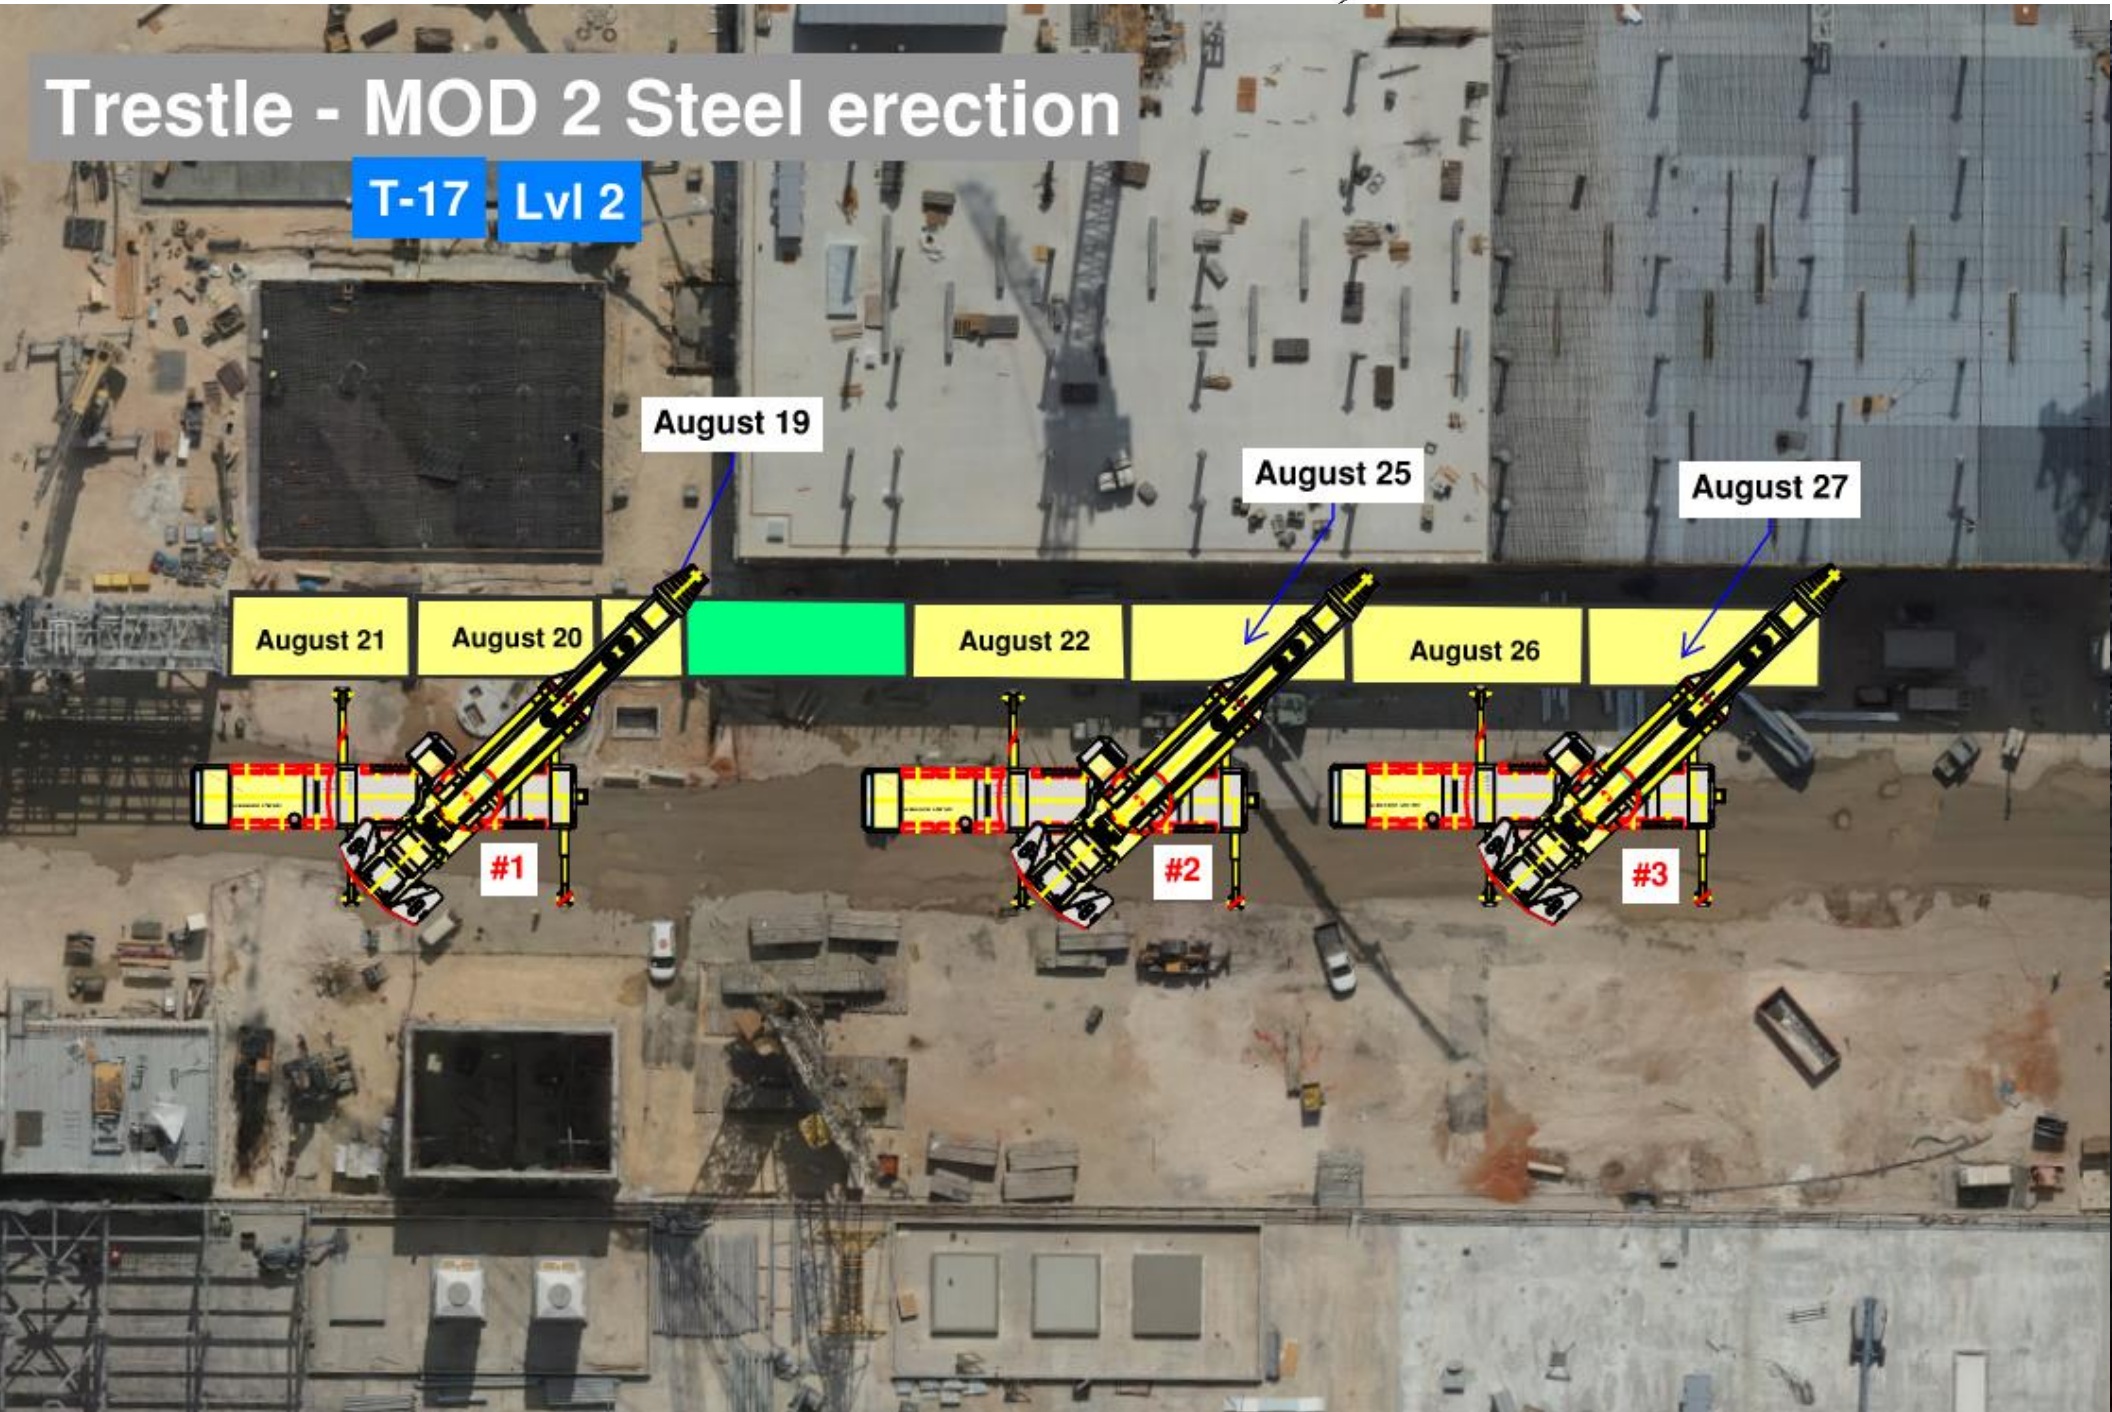


BSGS



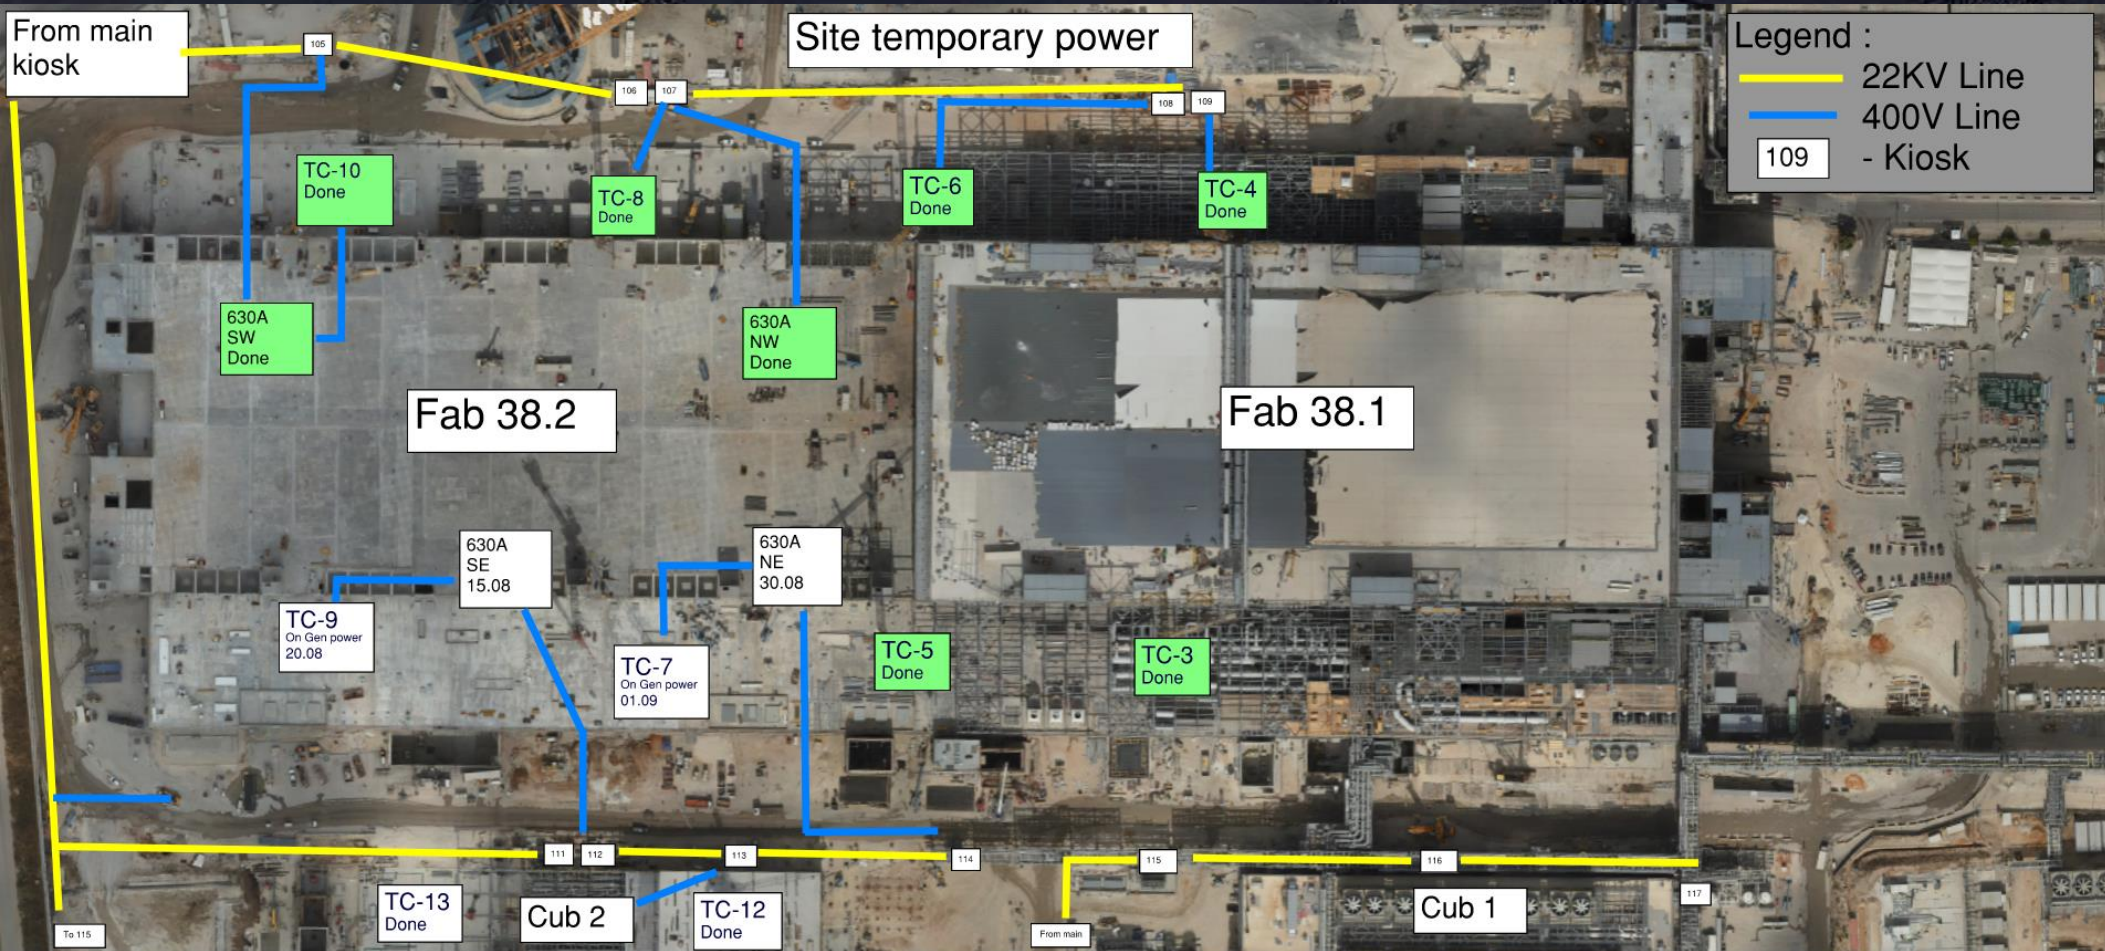

Daily Coordination Meeting


Site Logistics
North Gate B

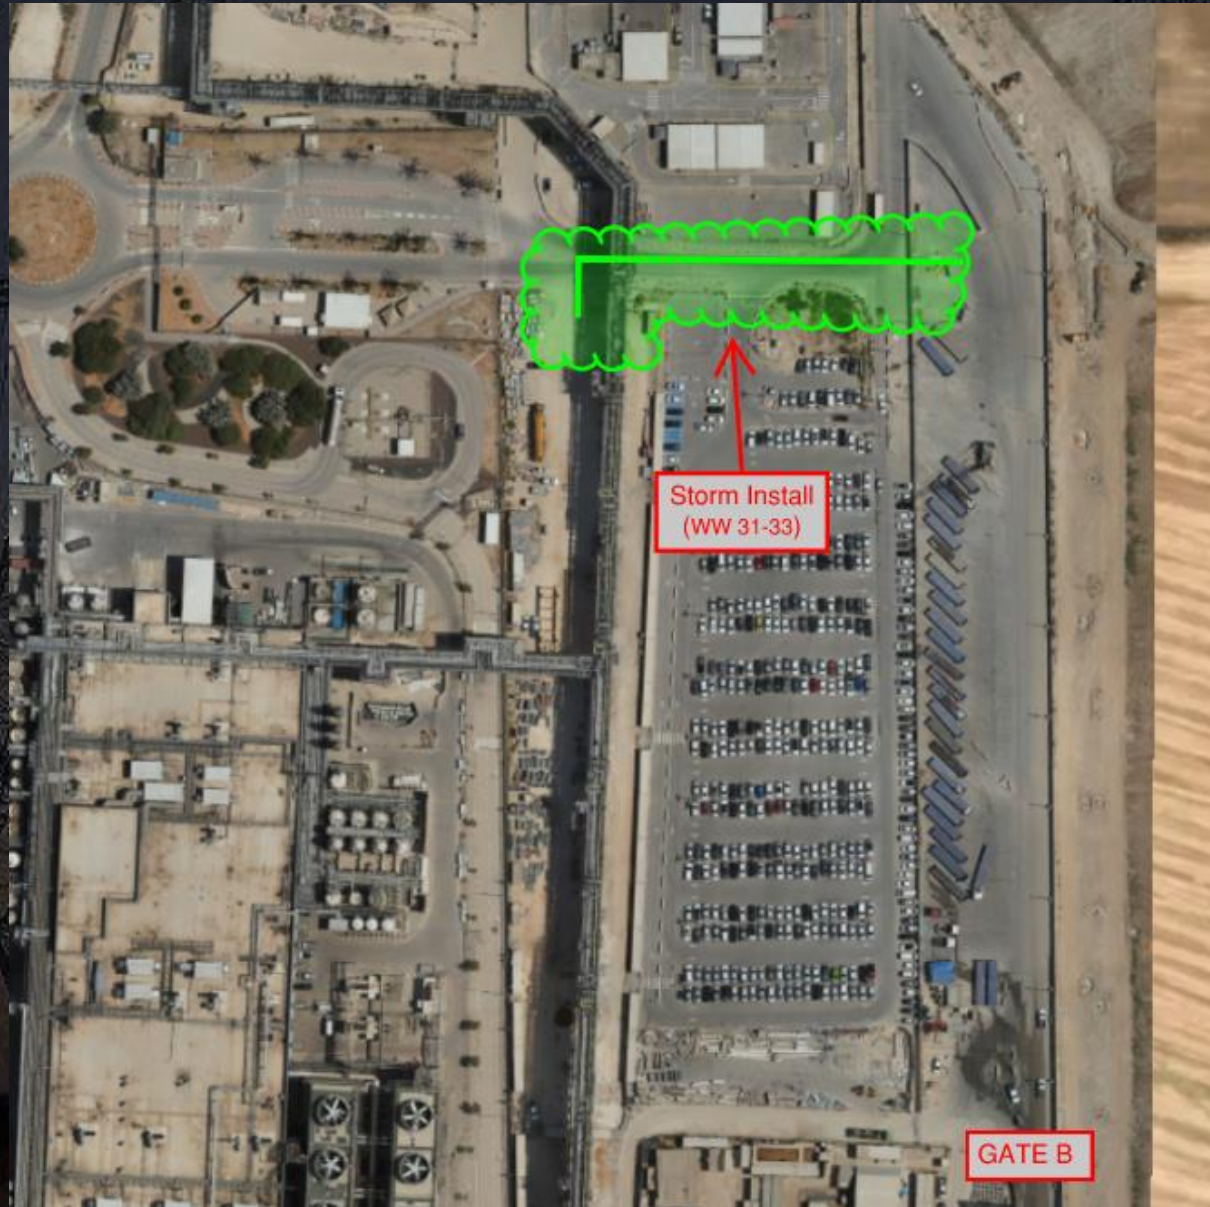

Daily Coordination Meeting

Site Logistics

Traffic Plan

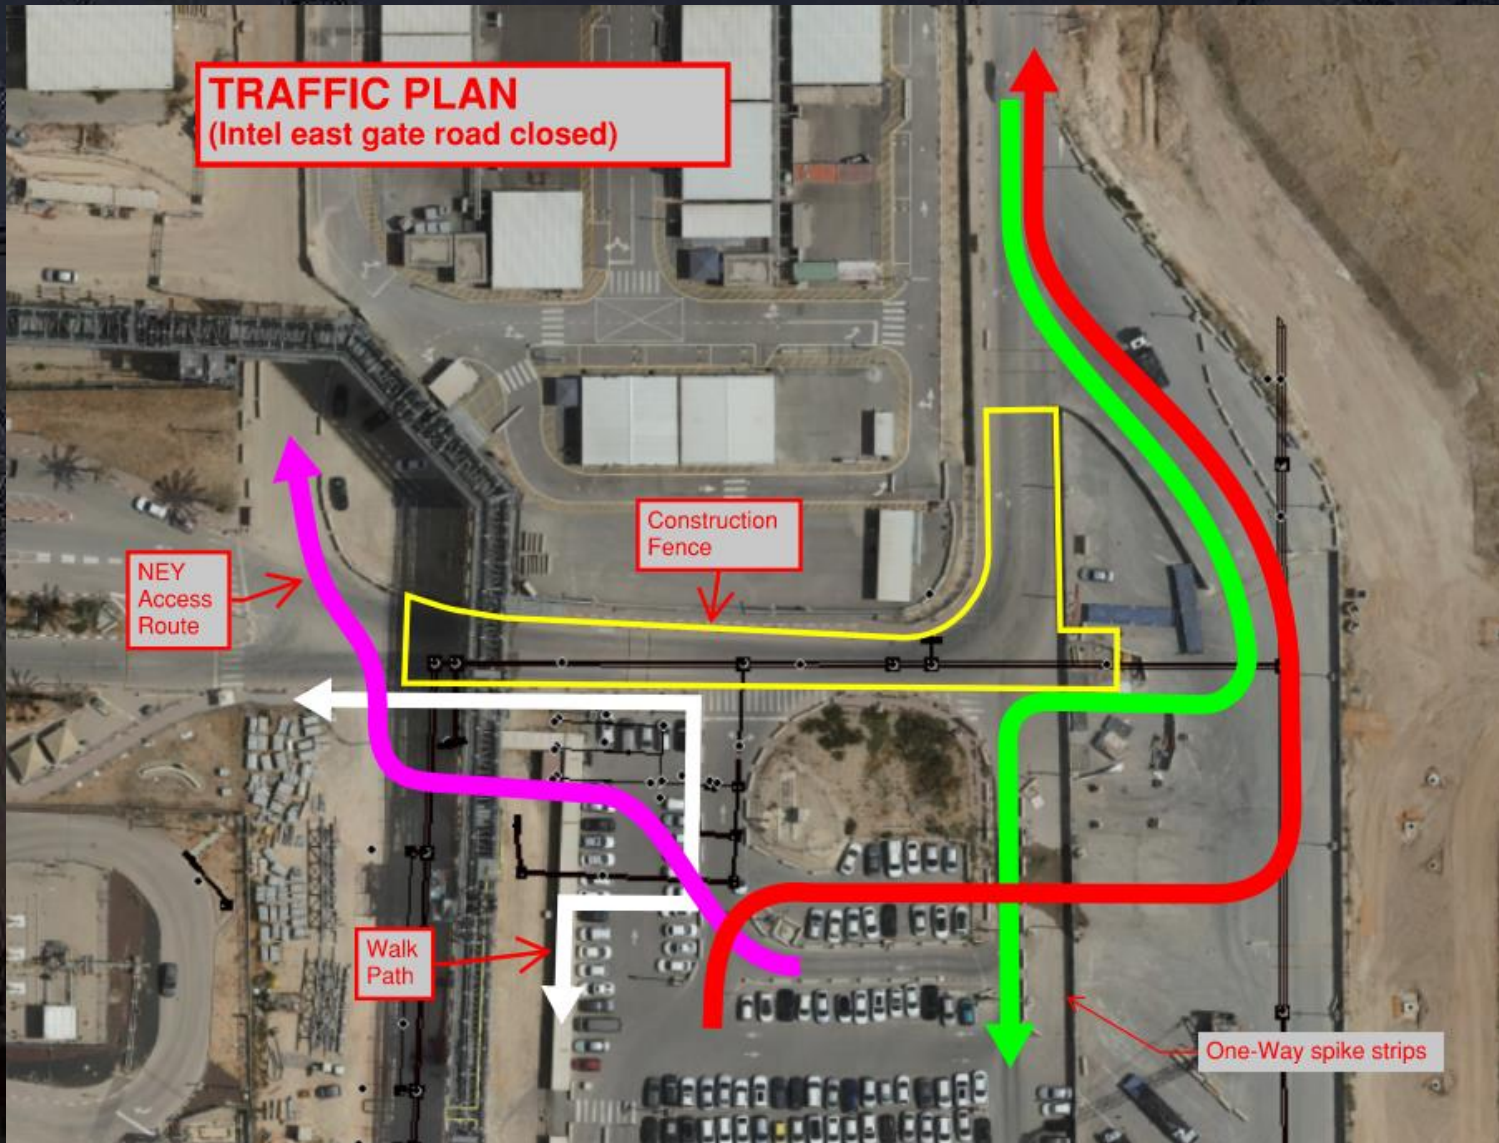




Daily Coordination Meeting

Site Logistics


North

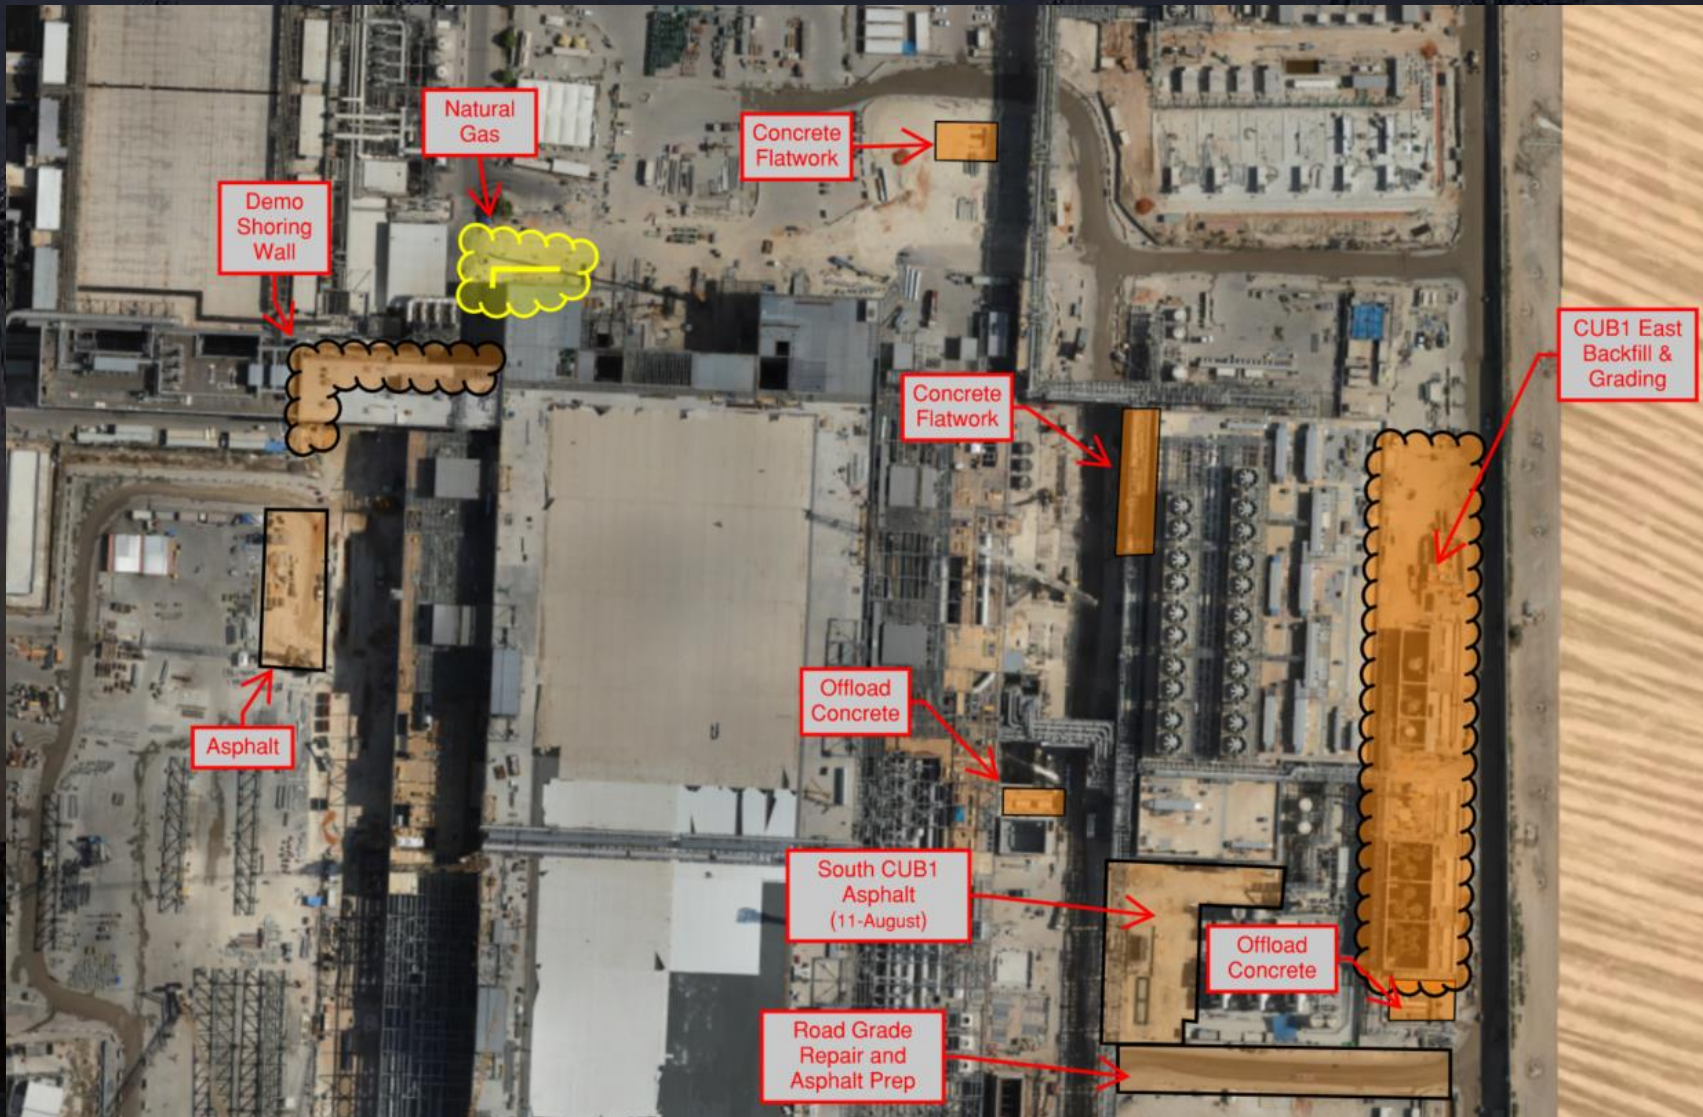

Daily Coordination Meeting

Site Logistics

South

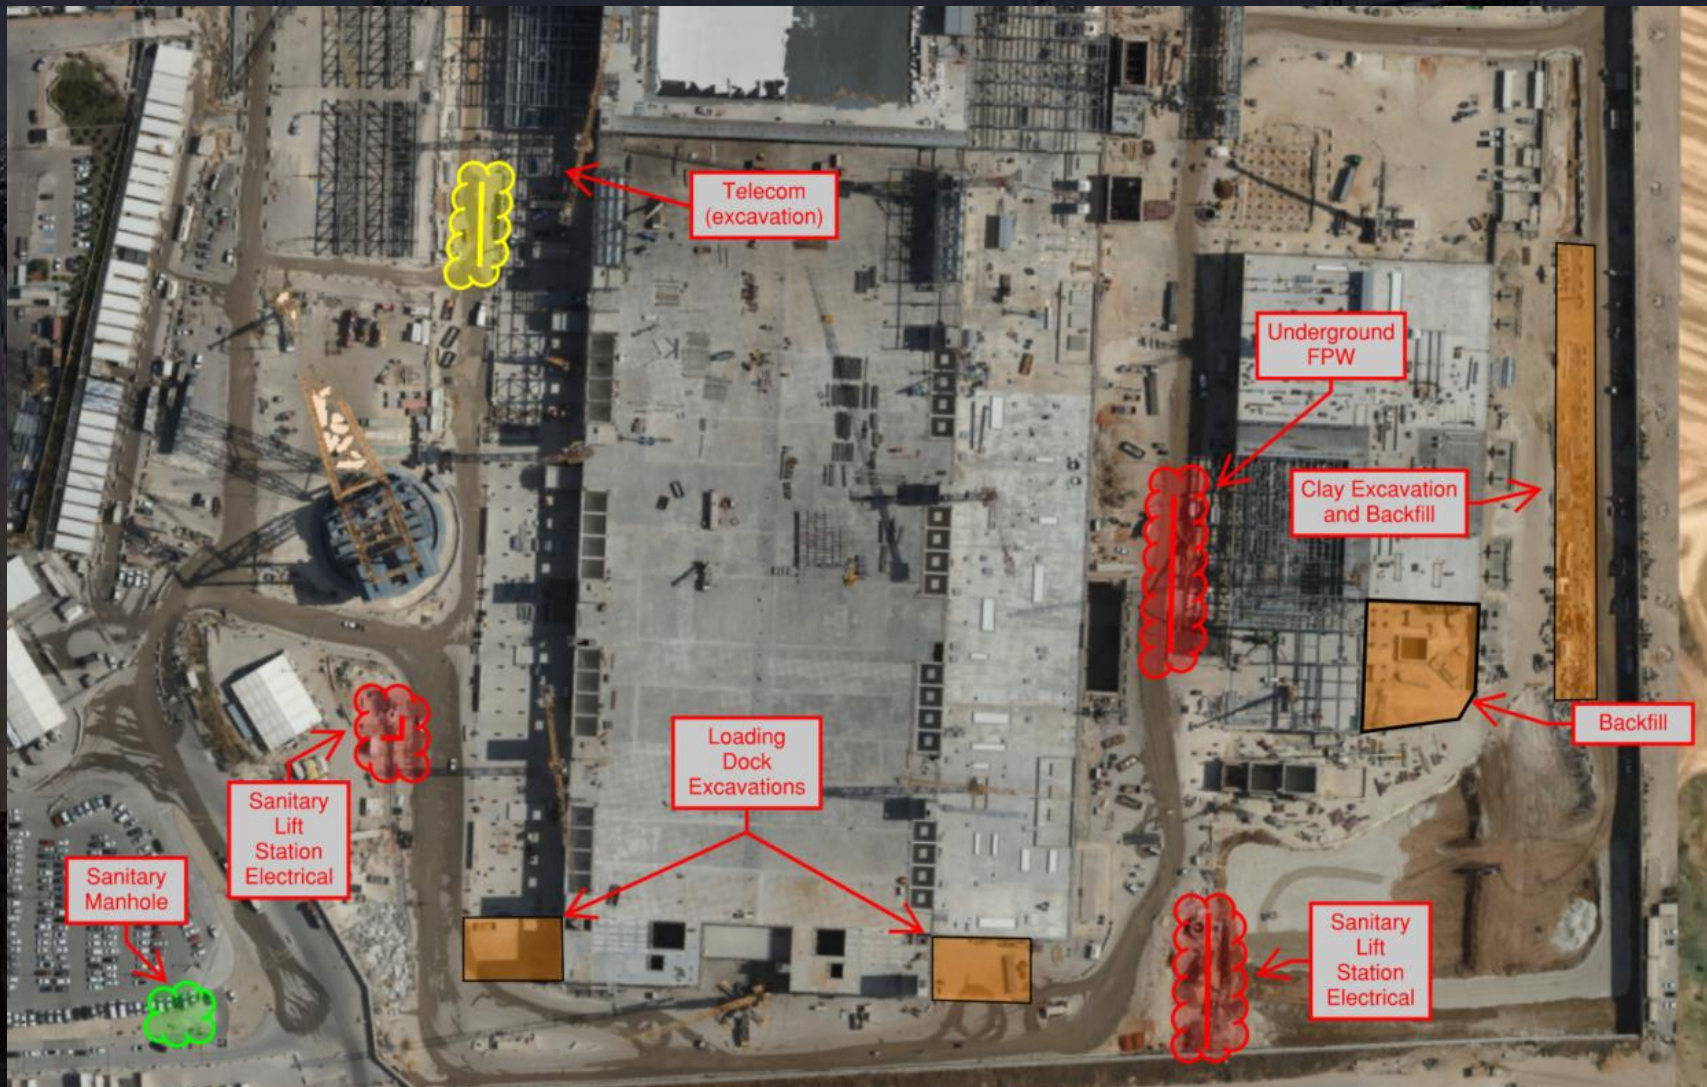

Daily Coordination Meeting

Site Logistics
BUGGY PARKING



GOOD PARKING



**GET YOUR
BUGGY
STICKERS**

- Must have a whip
- Must have a company name
- Must have a shakalaka




BAD PARKING




Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

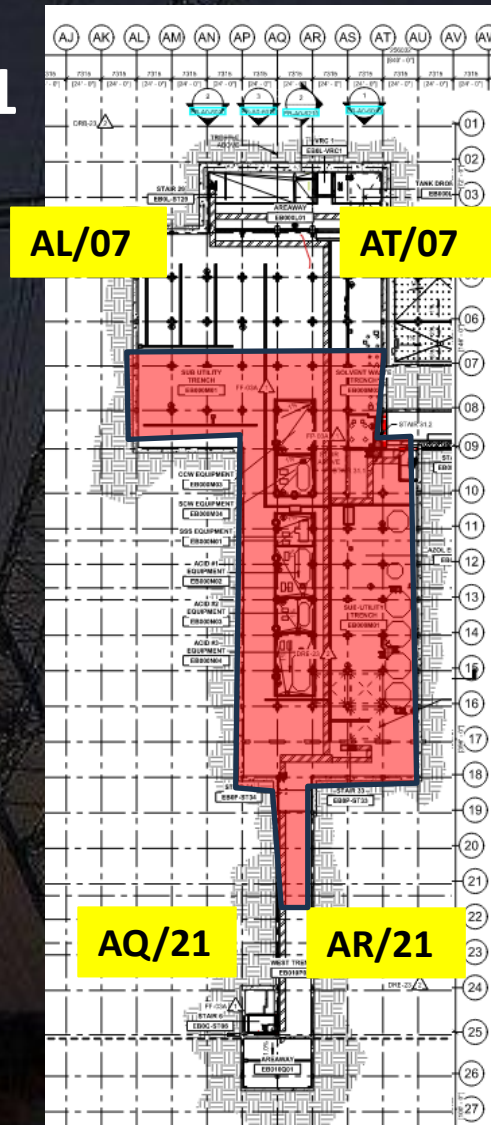


SUT2

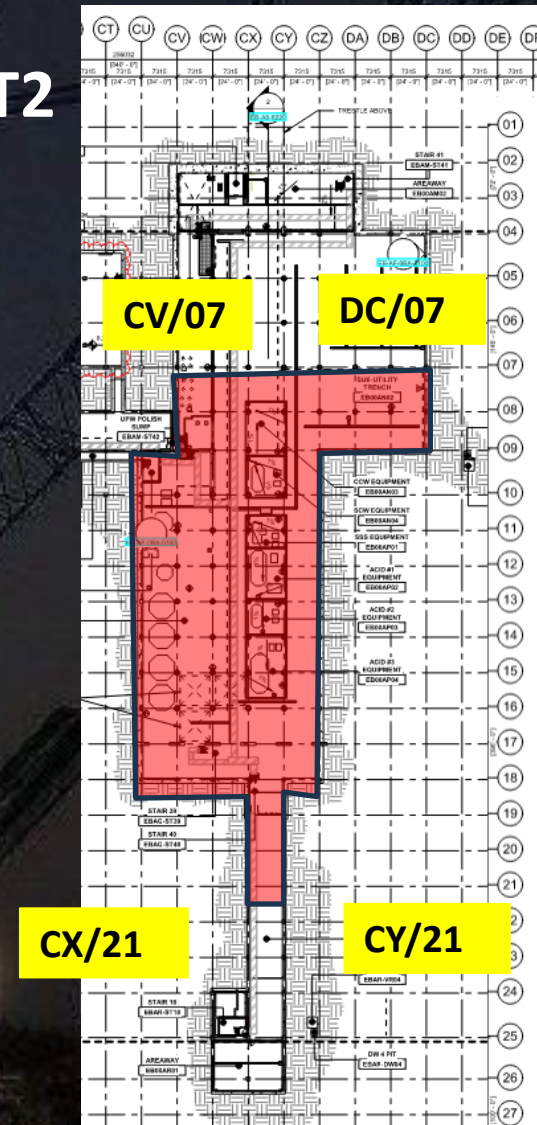

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

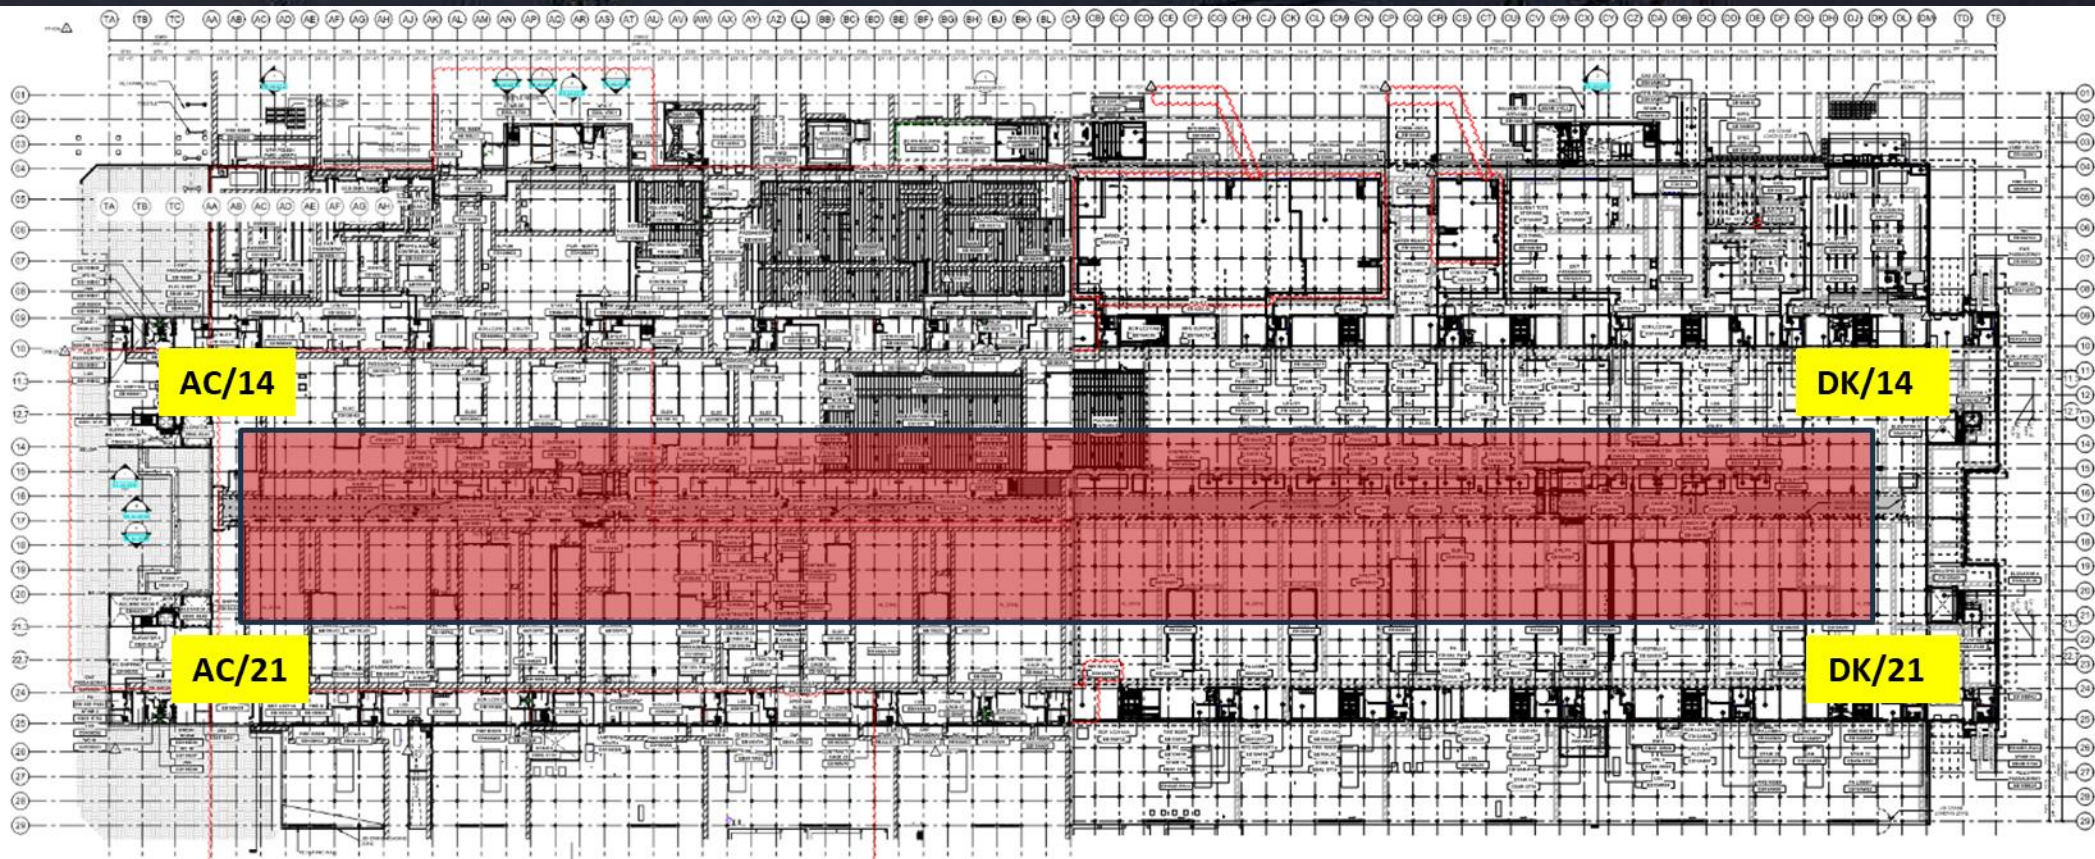



Daily Coordination Meeting


Site Logistics - Protected Areas (Subfab Level)

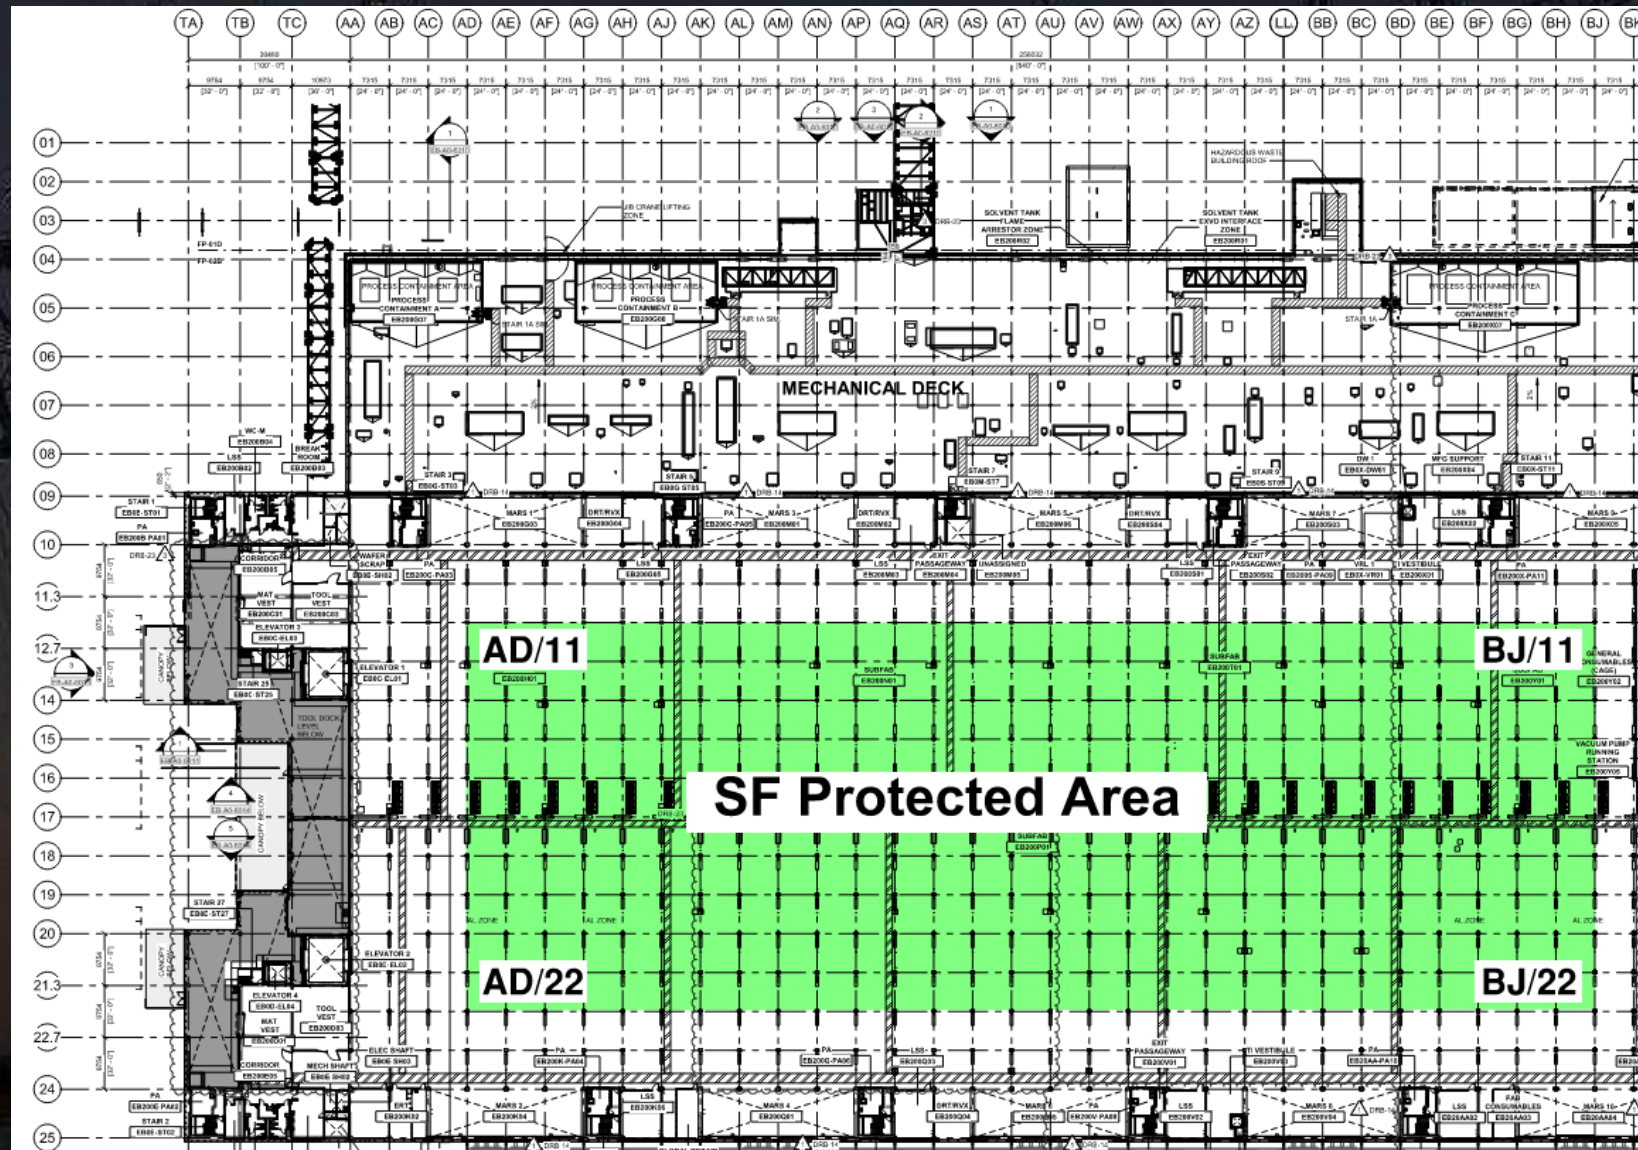

Daily Coordination Meeting

Site Logistics


Protected Areas

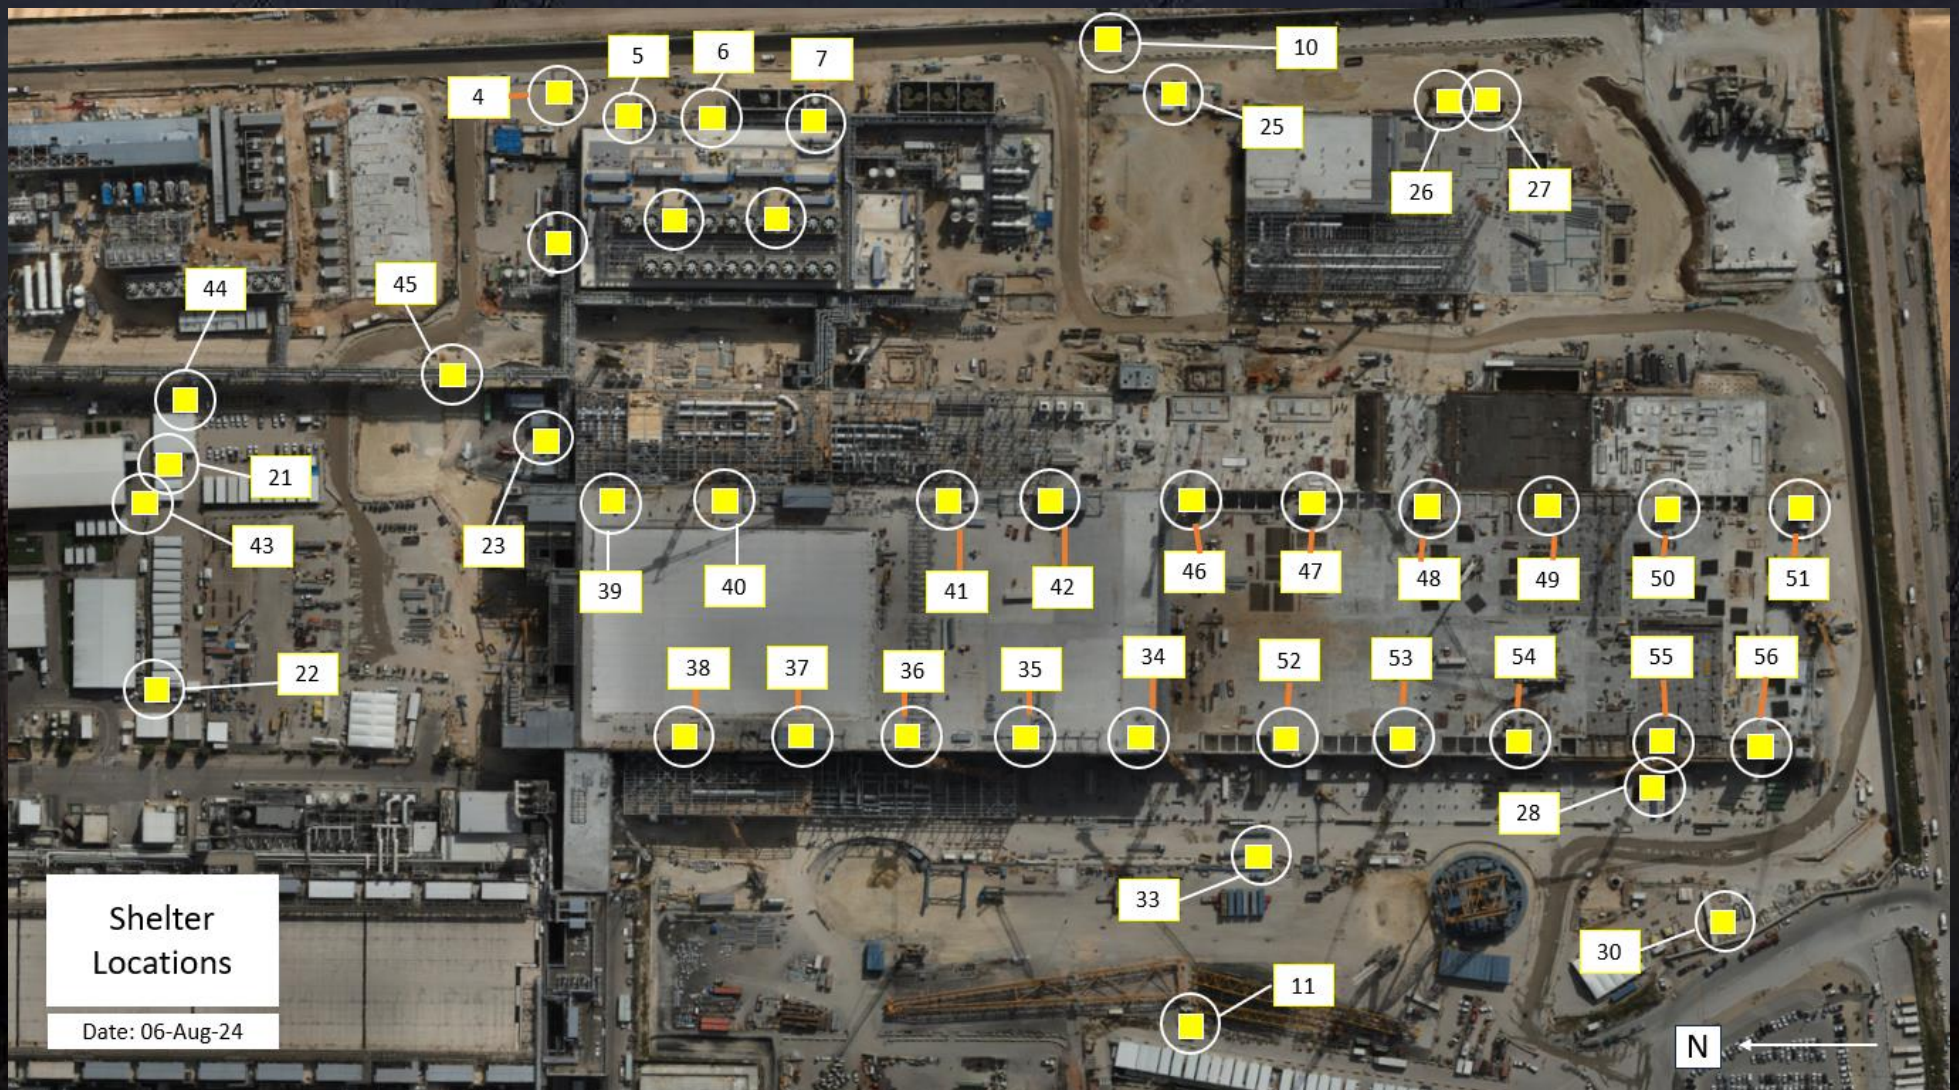

Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

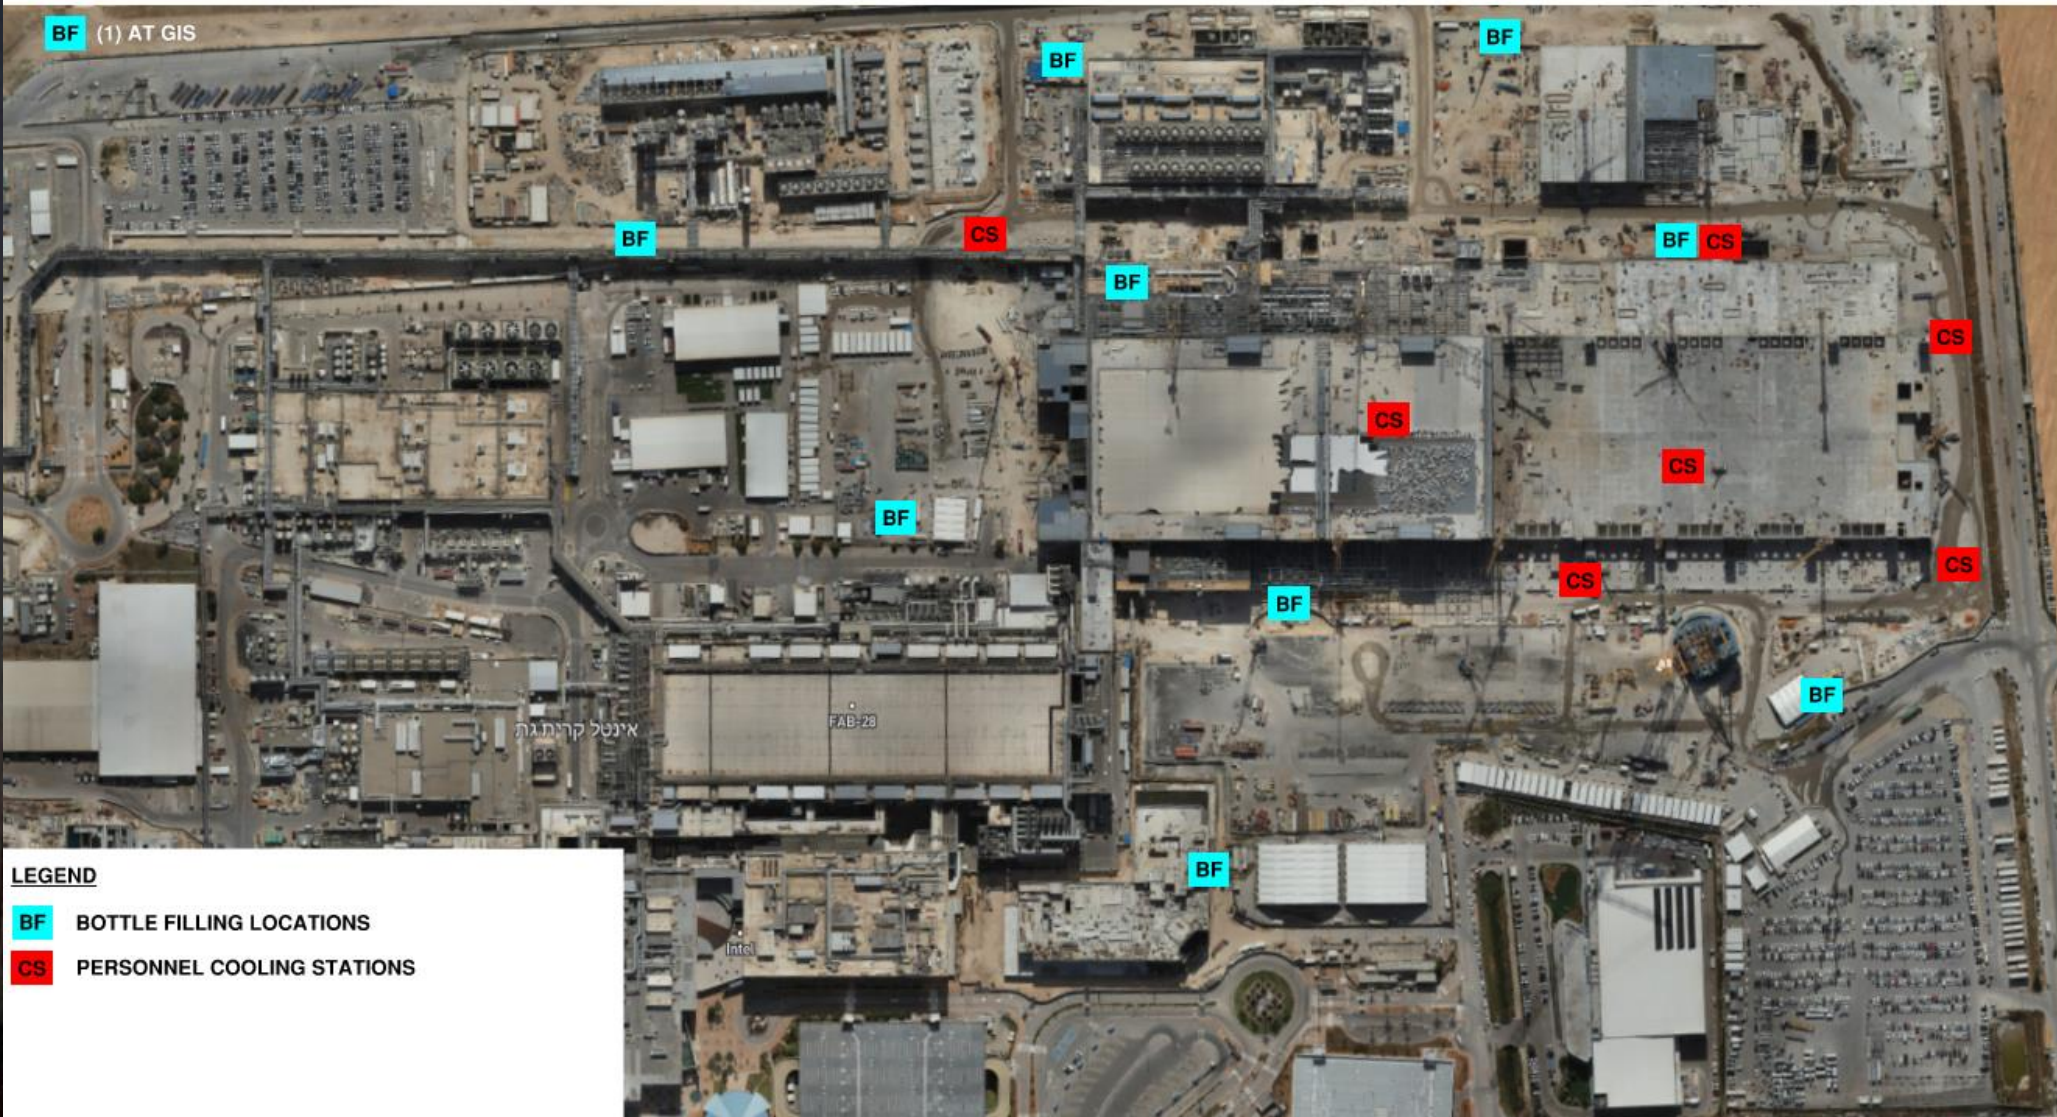

Back to Basics

- We aren't going to be able to successfully execute our higher risk activities unless we ensure that we have a solid foundation.
- We've focused a lot on some elements of the basics this week.
- The foundation of the safety of our people are all the "little" things that are too often overlooked.
- When you are out in the field look to make sure each of your crews have the foundation to have a safe and successful outcome



Heat Index- August 11th

	temperature (°F)															
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
50	81	83	85	88	91	99	103	108	113	118	124	131	137			
55	81	84	86	89	93	97	101	106	112	117	124	130	137			
60	82	84	88	91	95	100	105	110	116	123	129	137				
65	82	85	89	93	98	103	108	114	121	128	136					
70	83	86	90	95	100	105	112	119	126	134						
75	84	88	92	97	103	109	116	124	132							
80	84	89	94	100	106	113	121	129								
85	85	90	96	102	110	117	126	135								
90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127										
100	87	95	103	112	121	132										

 Caution
  Extreme Caution
  Danger
  Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In

HCC/EHS Weekend Work- 09.08.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Michael Carpenter 052-7583027
- Avinadav Ben Yehuda 052-8197360
- Oscar Macias 052-4845469
- Eyad Abd Al Wely 052-3287236

CSA CM

- Aharon Fahima 052-5970136
- Leonid Khomich 053-2722138

MEP

- Boris Gruman 054-7886568
- Ken Power 052-2531428
- Shmuel Rosenberg 052-3878052
- Simon Garton 052-2770953

CX/QA

- Raymond Griffin 052-6941063

Cranes

- Maksym Panov 055-9181086

Safety

- Safety Foreman- Nadav Alfasi- 052-5115772 Nadav-Alfasi@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Officer - Arkady Gerber-050-6851432 Arkady-Garber@Hoffmancorp.com

Subcontractor Weekend Work- 09.08.2024

FAB

- Dvir

Utility Level

- Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

- Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

- HYG

Ehs Salah 0507773119

Foreman Avishai 0503303939

- Carmel duct

Ehs Amit 0549249356

Foreman Aitan 0527053353

- Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

- Combe upw

Ehs; Michael 0525506596

Foreman; Edward 0526419894

- Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Clean Room

- Rolling Planes:

Lead – Codrin : 054.6594273

Safety – Ovidiu Iacob: 054.6993648

- Afcon:

Lead – Lok: 055.9652398

Safety – Pradeep: 055.2742935

- W&W/Sami Najami:

Lead – Dave Wehr: 052.6156276

Safety – Tony: 050.7870320

- Chemo:

Lead – Mr. Winai Sirimat: 052.8090588

Safety – Lotem: 054.4477112

- Elram:

Lead – Eliezer Bonillo

Safety – Shlomo Amar:

- Talad:

Lead – Hen Asulin

Safety – Marcelo Zekcer: 052.3540242

Subfab

- Malchimim Badarom – DRB rework –

Michael – 053-437-7846

- BCT / Yishay – OSM lighting –

Idan – 052-667-4453

- Afcon – Pulling cable / install cable tray –

Raz – 054-683-8626

- Pach Taas – Perimeter room install –

Tomer – 050-767-0585

- HYG – Stair 3 –

Saleh – 050-777-3119

PSSS

- Pach Taas – Module bolting PSSS Roof and Lift 2

Foreman – Vadim – 052-6229005

Safety – Offek – 050-7838486

- W&W – SEQ 131,134,136, and 2P Scrubber Grating

Foreman – Willie – 052-6145521

Safety – Gary Lambert – 1-405-833-8910

- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2

Foreman – Charles – 055-2740190

Safety – Stevan – 055-9129333

- Chemo A. – PSSS Roof and Lift 2

Foreman – Maor – 050-955-9071

Safety – Rotem – 054-447-7112

- SK Engineering – GL4 Racks

Foreman – Marcela – 054-5210133

Safety – Marzuke – 054-447-7112

- Carmel B – BPS & Roof

Foreman – Haitem – 052-7053353

Safety – Amit – 054-9249356

- Combe UPW – UPW Room

Foreman – Boris – 054-8346412

Safety – Abed – 052-5148747

- Katz – BCD Racks/Delivery

Foreman – Sergey – 054-7501845

Safety – Ofer – 054-6756690

- HSAI – BIPA & MOD2 Stripping

Foreman – Dave – 052-4121028

Safety – Sam – 052-5259268

Siding

- SNJ FAB

Liran T. 052-6533558

Barak B. 053-3003902

Subcontractor Weekend Work- 09.08.2024

WJG

- W&W – Steel Erection 3J

Foreman: Chris Isaac – 052 588 3215

Safety: Moshe 054 801 2959

- Afcon – 3J UL Cable Tray, 2J Lift 2 Cable Tray

Foreman: Sarat 055 274 0190

Safety: Pradeep 055 274 2935

- Pach Taas: 1J UL, 2J Lift 2 Module Bolting

Foreman: Nuriel 054 901 2343

Safety:

- Chemo: 3J & 4J Lift 2 Piping

Foreman: Stav 054 717 5157

Safety: Rotem 054 447 7112

Site

- Olizki – Sweepers and water trucks & concrete forming

Supervision = Shimon: 052-4702921

EHS = Ben: 052-4033565

- TM Team – Telecom CLSM backfill

Supervision = Rafi: 050-8723363

EHS = Alon: 054-7711469

Trestle

Sami Najami piping – T-30A, T-84, T-32 areas , 15 workers. (+Crane) Mohamad Abed: 0544984772.

Sami Najami Steel – SUT area , 4 workers. Hamada : 0543516972.

Sami Najami piping – T-41 area , 5 workers.

Sami Najami Steel – SUT area , 4 workers.

Sami Najami Foundations - West of CUB2 area, 9 workers.

Safety- ALON MATAN -0525098950

GIS/NEY

Temp Power

Maor Tzvi 052-422-7273 for 02.08.24

CUB

Chemo Aharon: CUB 1

Dudu - 0509808846

Leonid - 0548883878

Sami Najami: CUB 2

Husein - 0526917461

Alon - 0509895008

Meptagon I&C: CUB 1

Sergey - 0537981592

Jaybal - 0557767234

HSAI: CUB 2

S.K.E: CUB 1 TMXW

Marzuk - 0548830263

Marcelo - 0545210133

CUB HYDRO WATCH:

CHEMO AHARON:

24 HOURS FRIDAY-SATURDAY

ONSITE DAY SHIFT 0700-1900 TEE-0523911674

ONSITE NIGHT SHIFT 1900-0700 AUDDY-0529396530

EK 052 3623553 SUPERVISOR ON CALL

cub 2

East wall metal studs salama is the forman
