

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:


- Line of fire- incident Thurs



HOFFMAN CONSTRUCTION COMPANY




UTILITY LEVEL MOD2

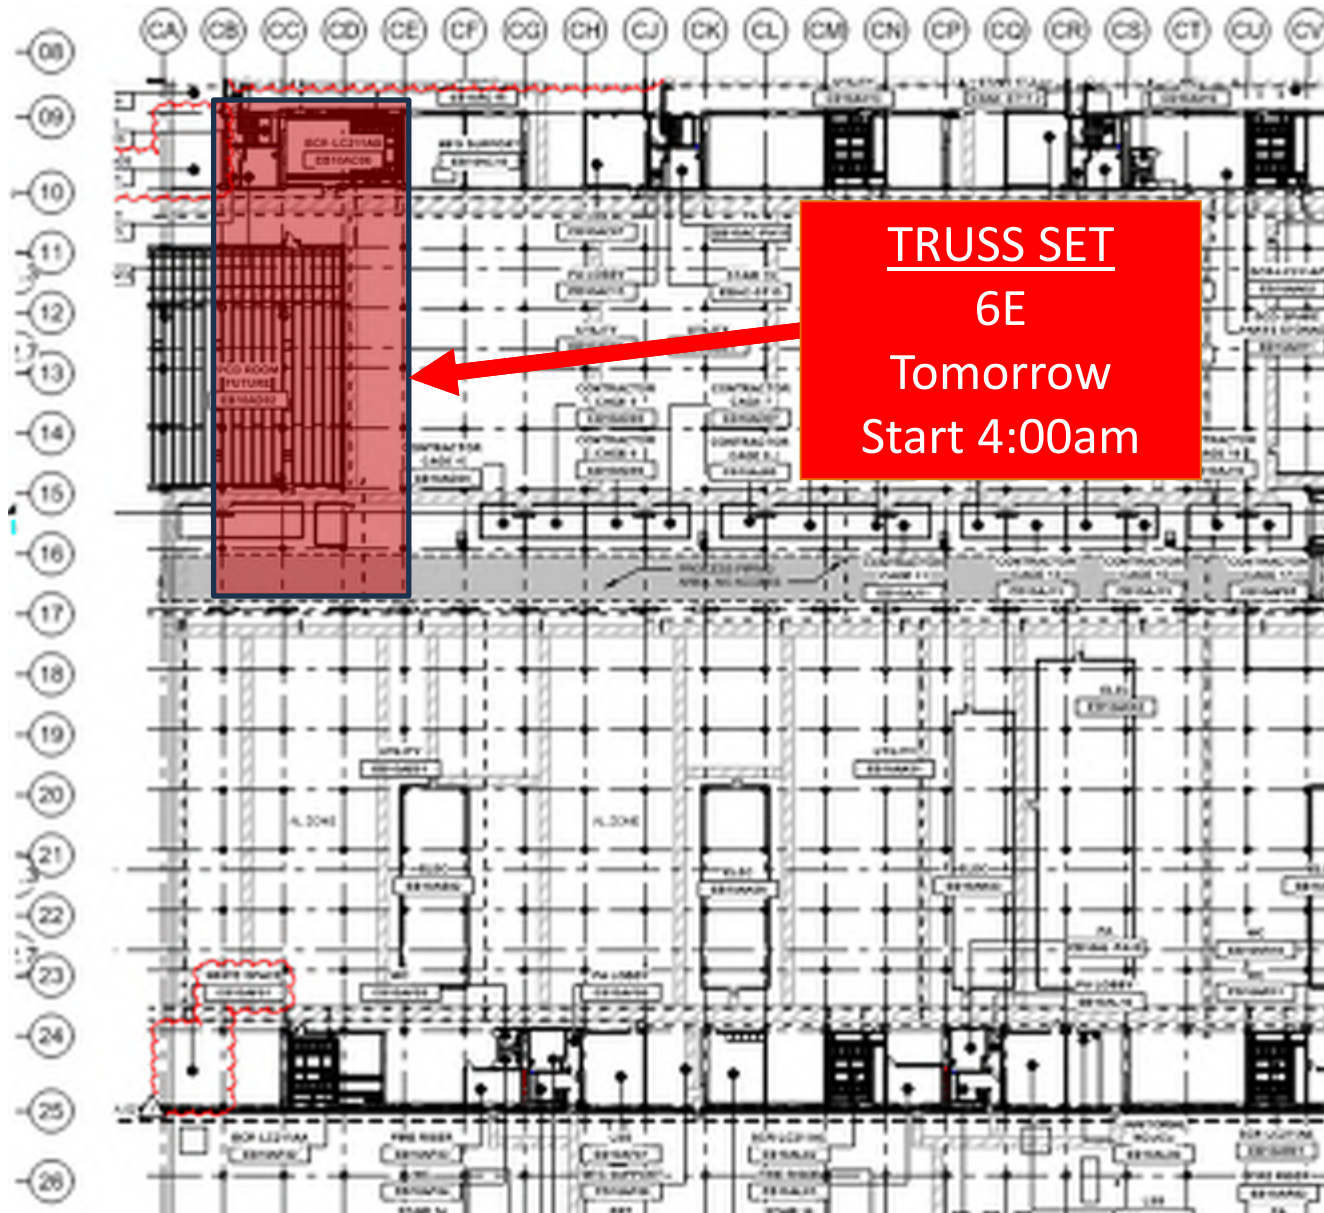





UTILITY LEVEL MOD1

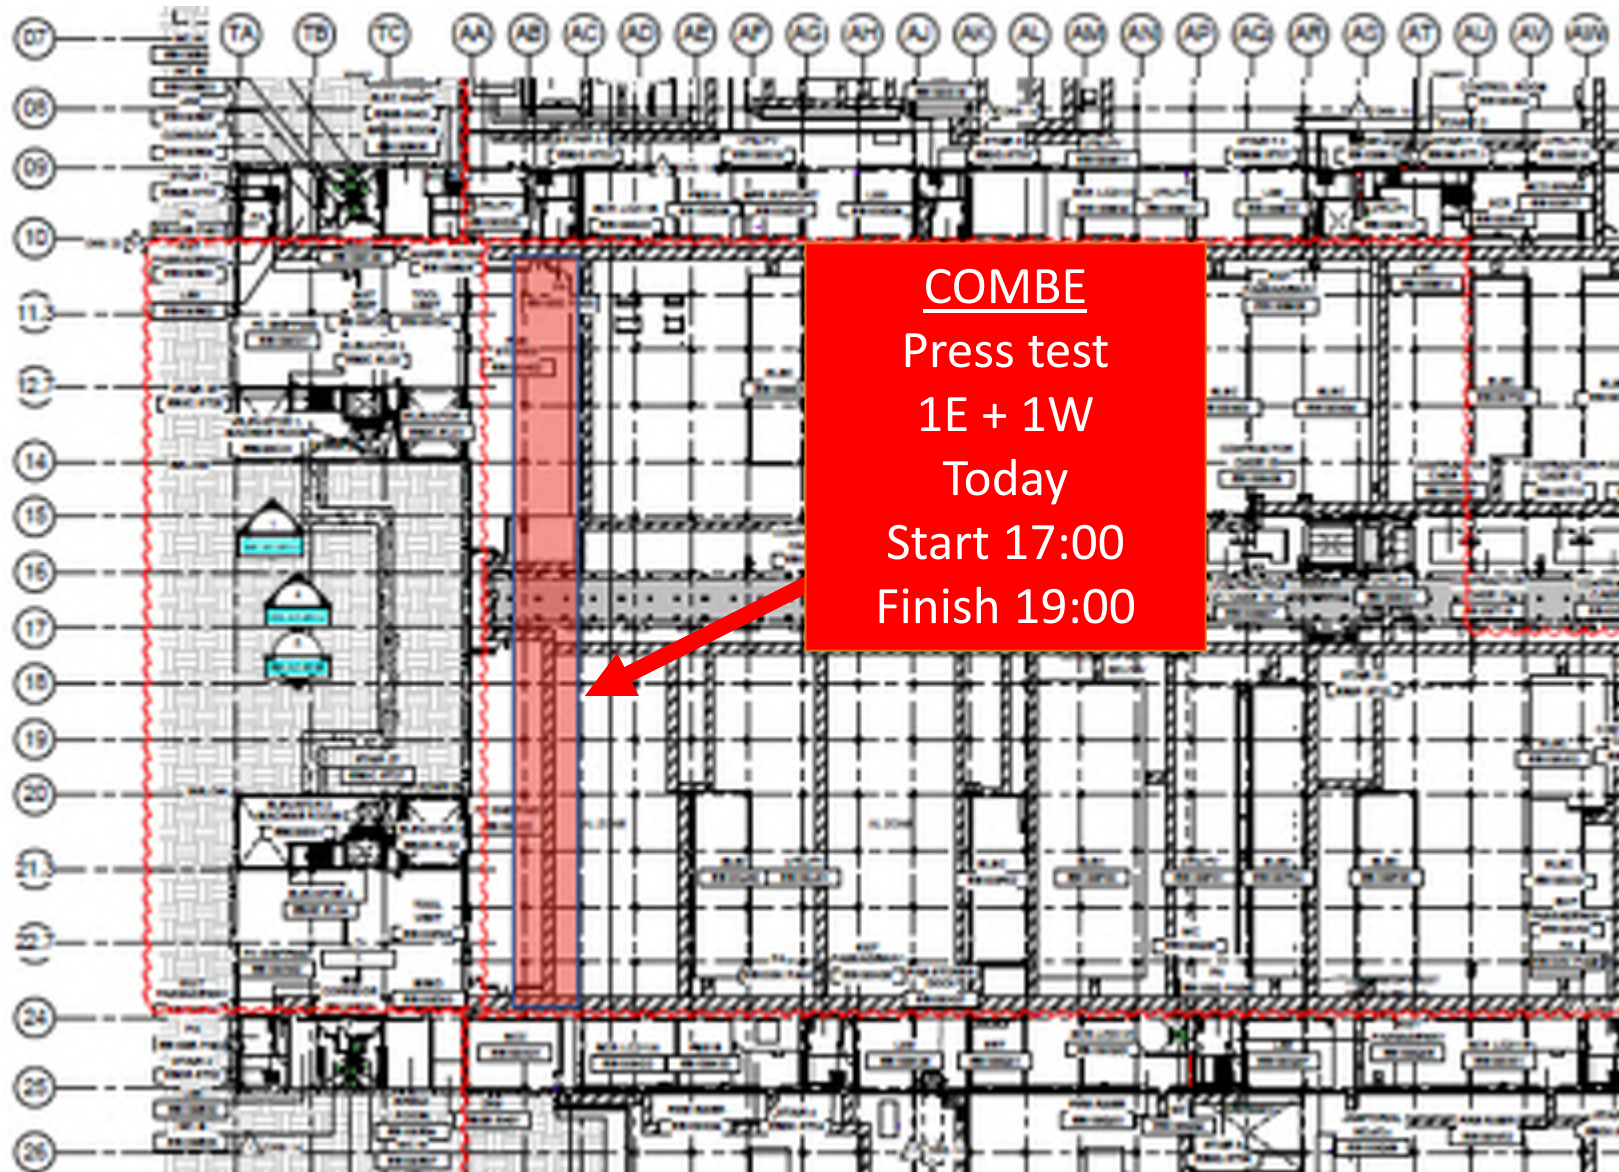


UTILITY LEVEL MOD1

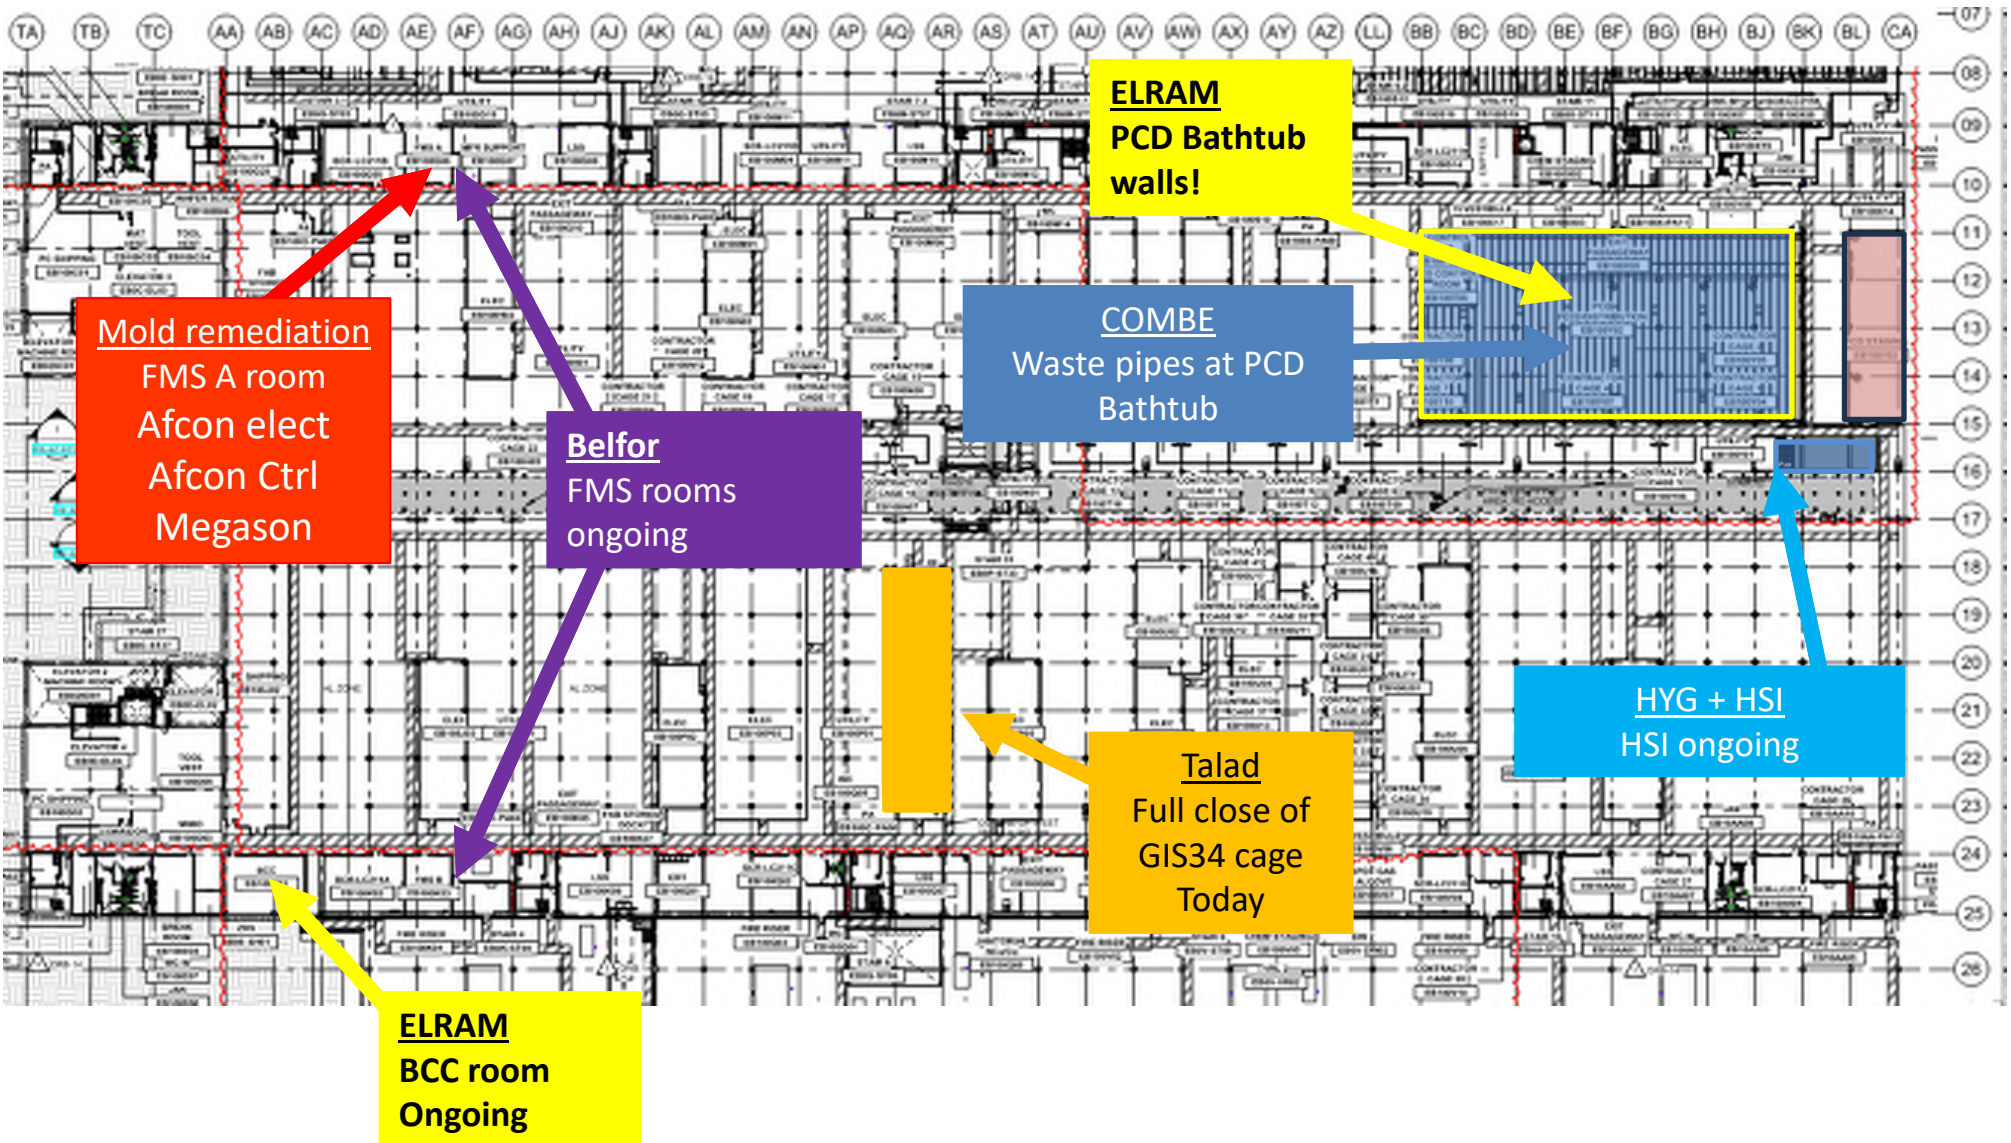

UTILITY LEVEL MOD2

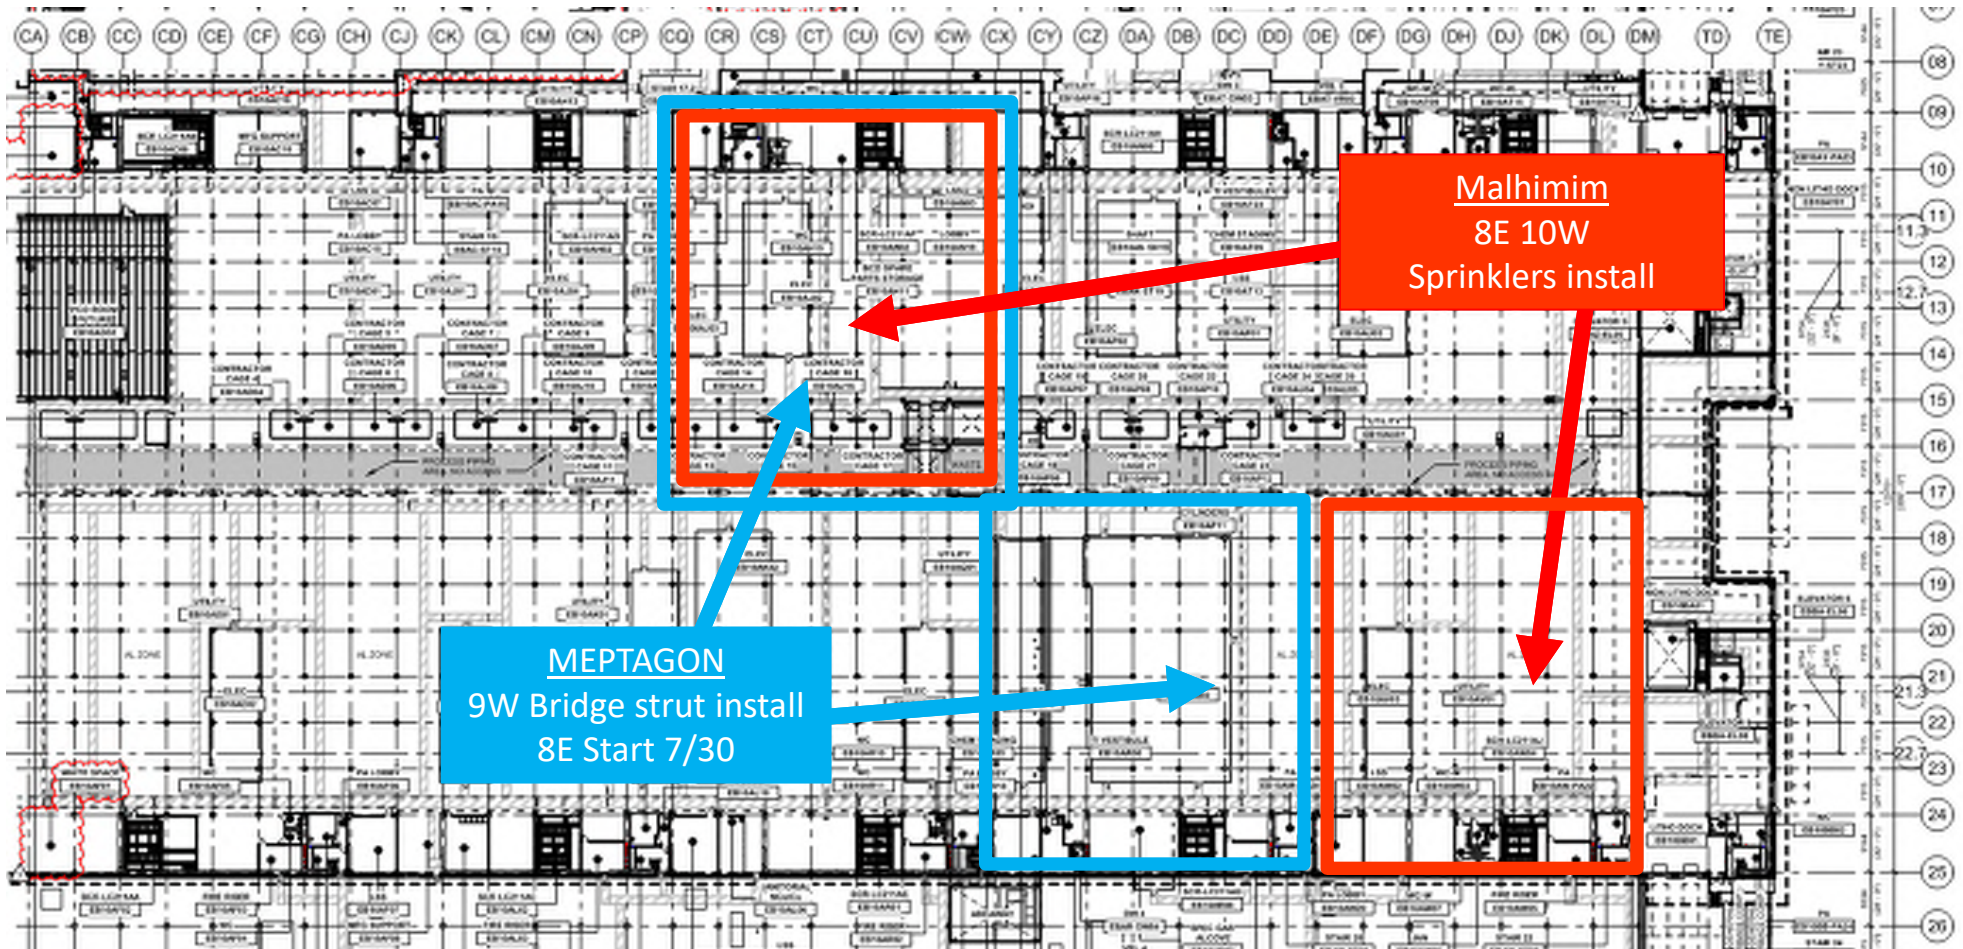


SUT 38.1 LEVEL

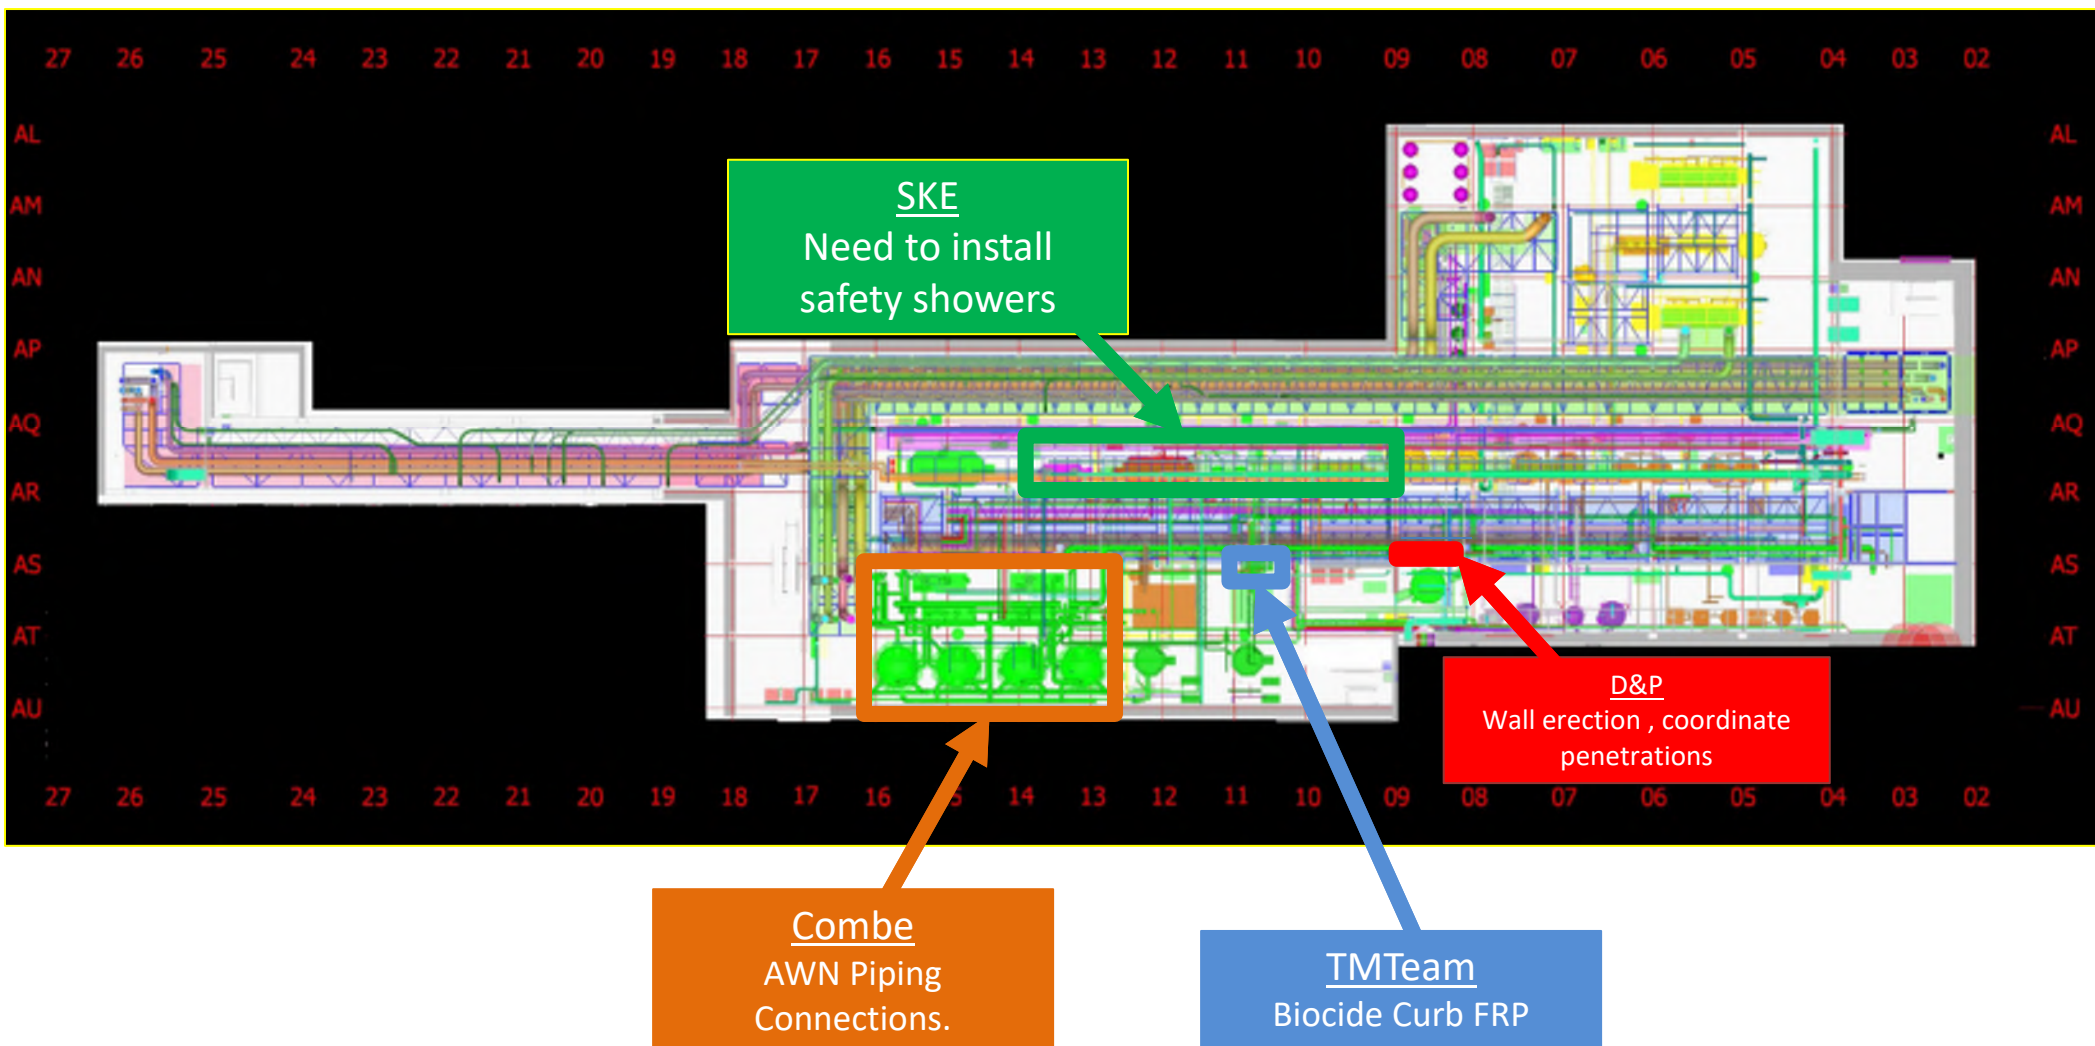





SUT 38.2 LEVEL

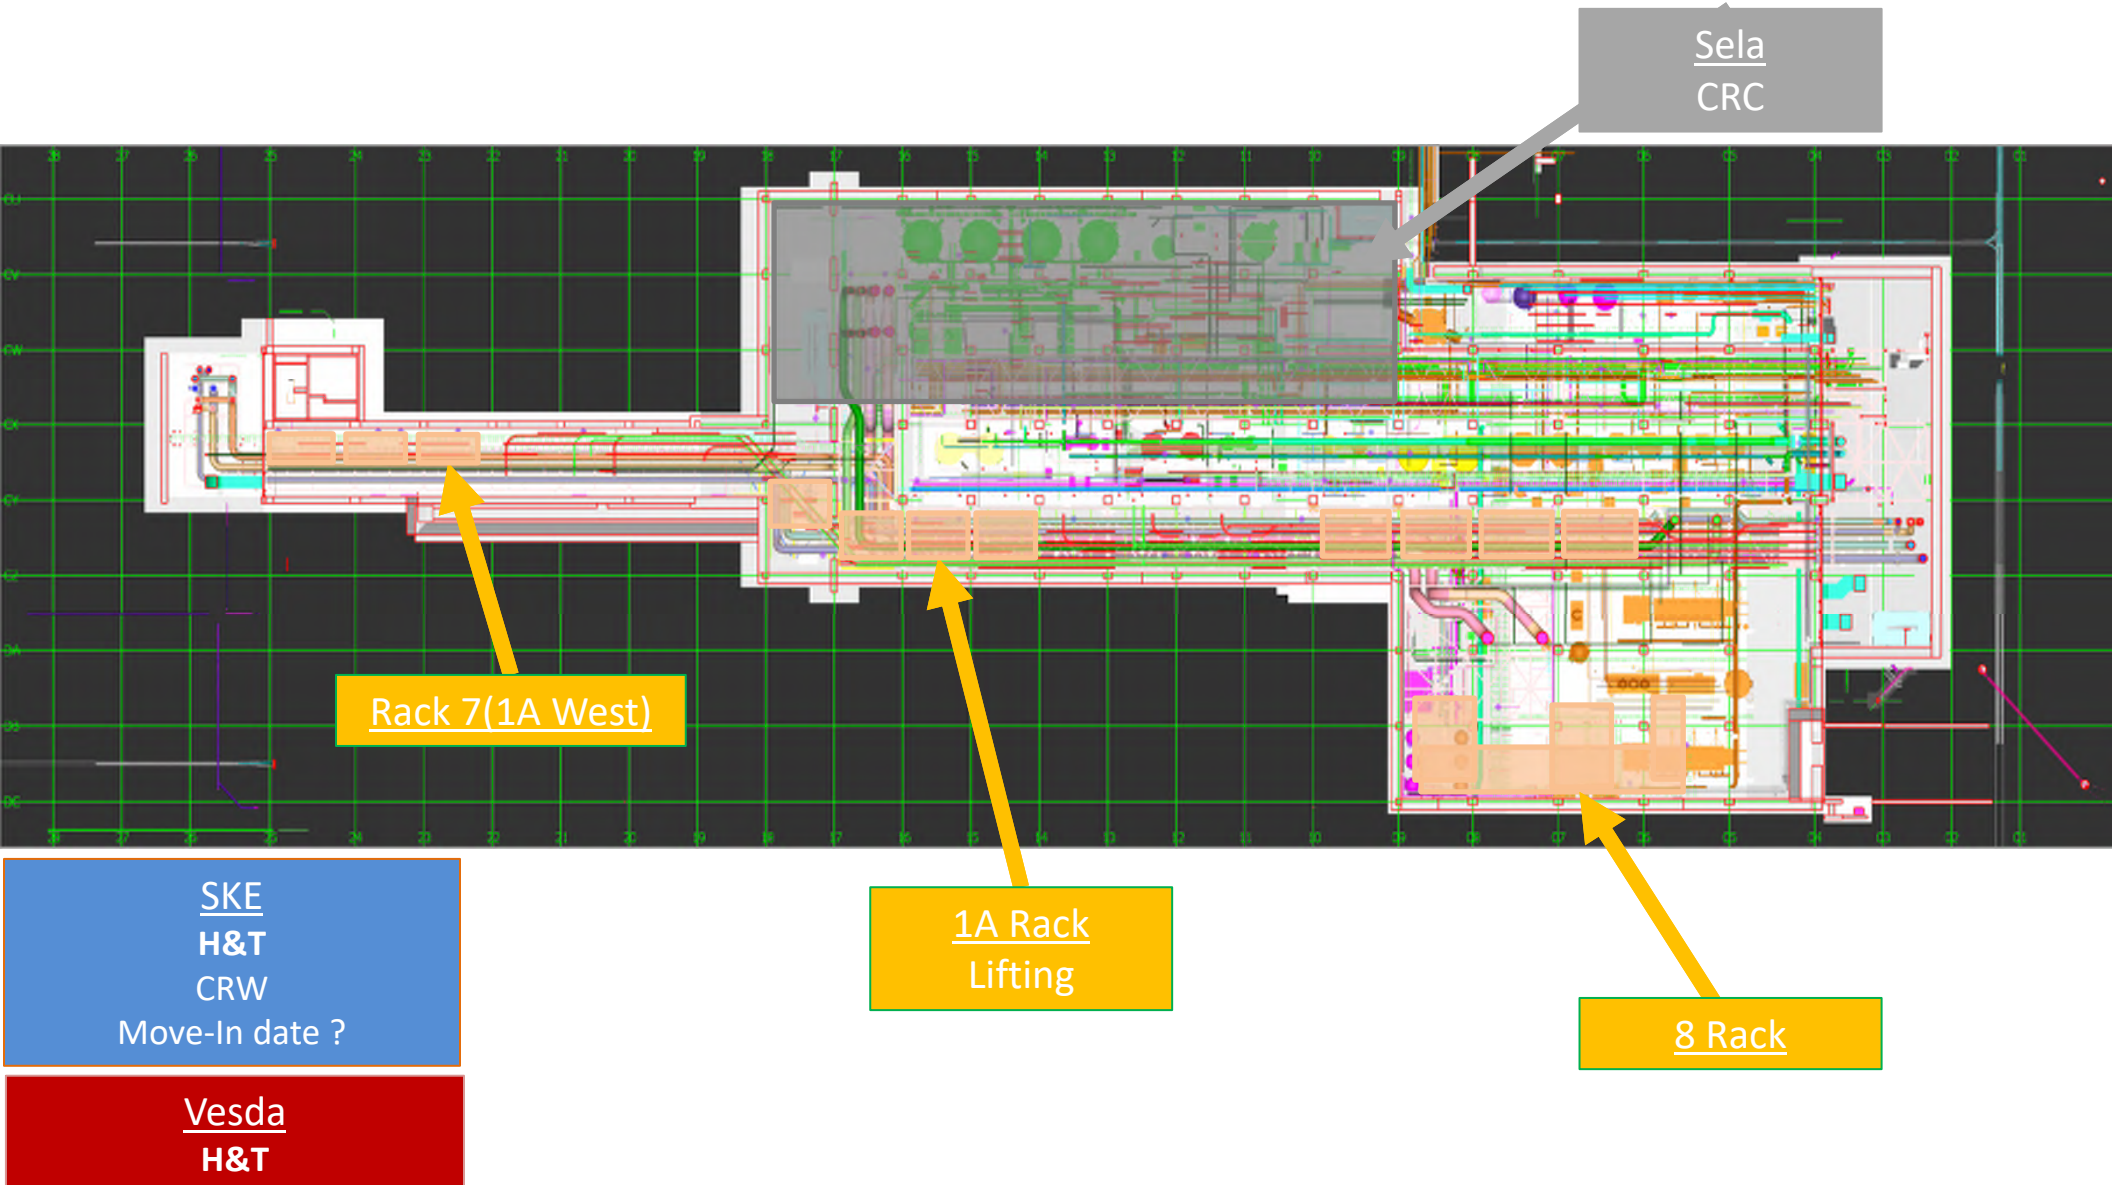

SUBFAB BUILDOUT MOD 1

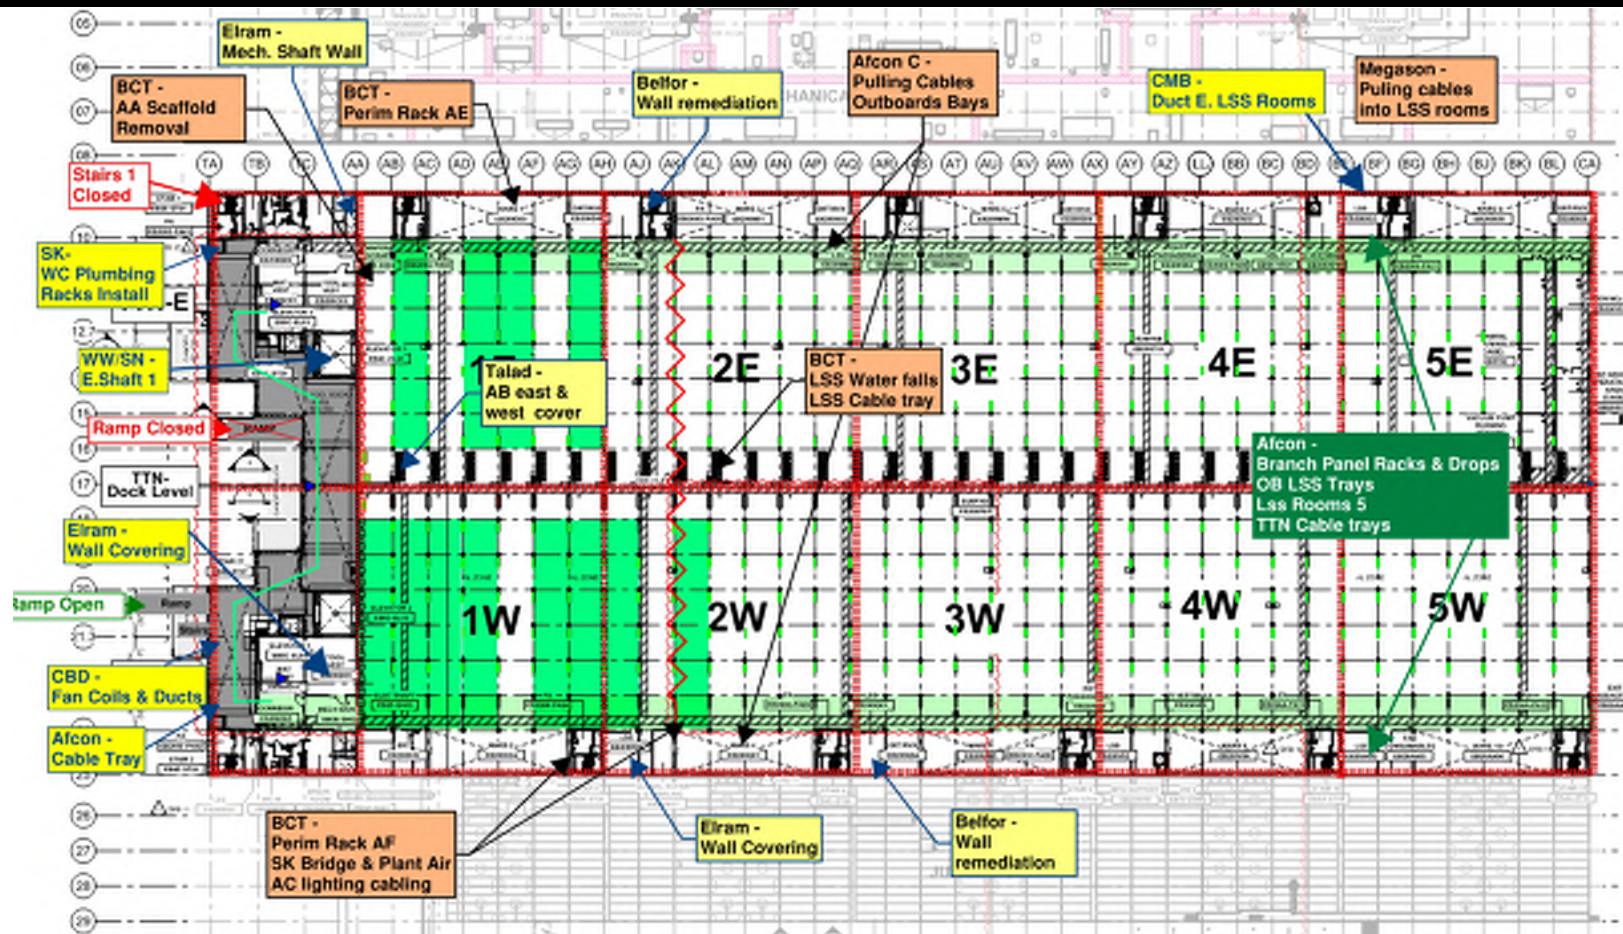


SUBFAB BUILDOUT MOD 2

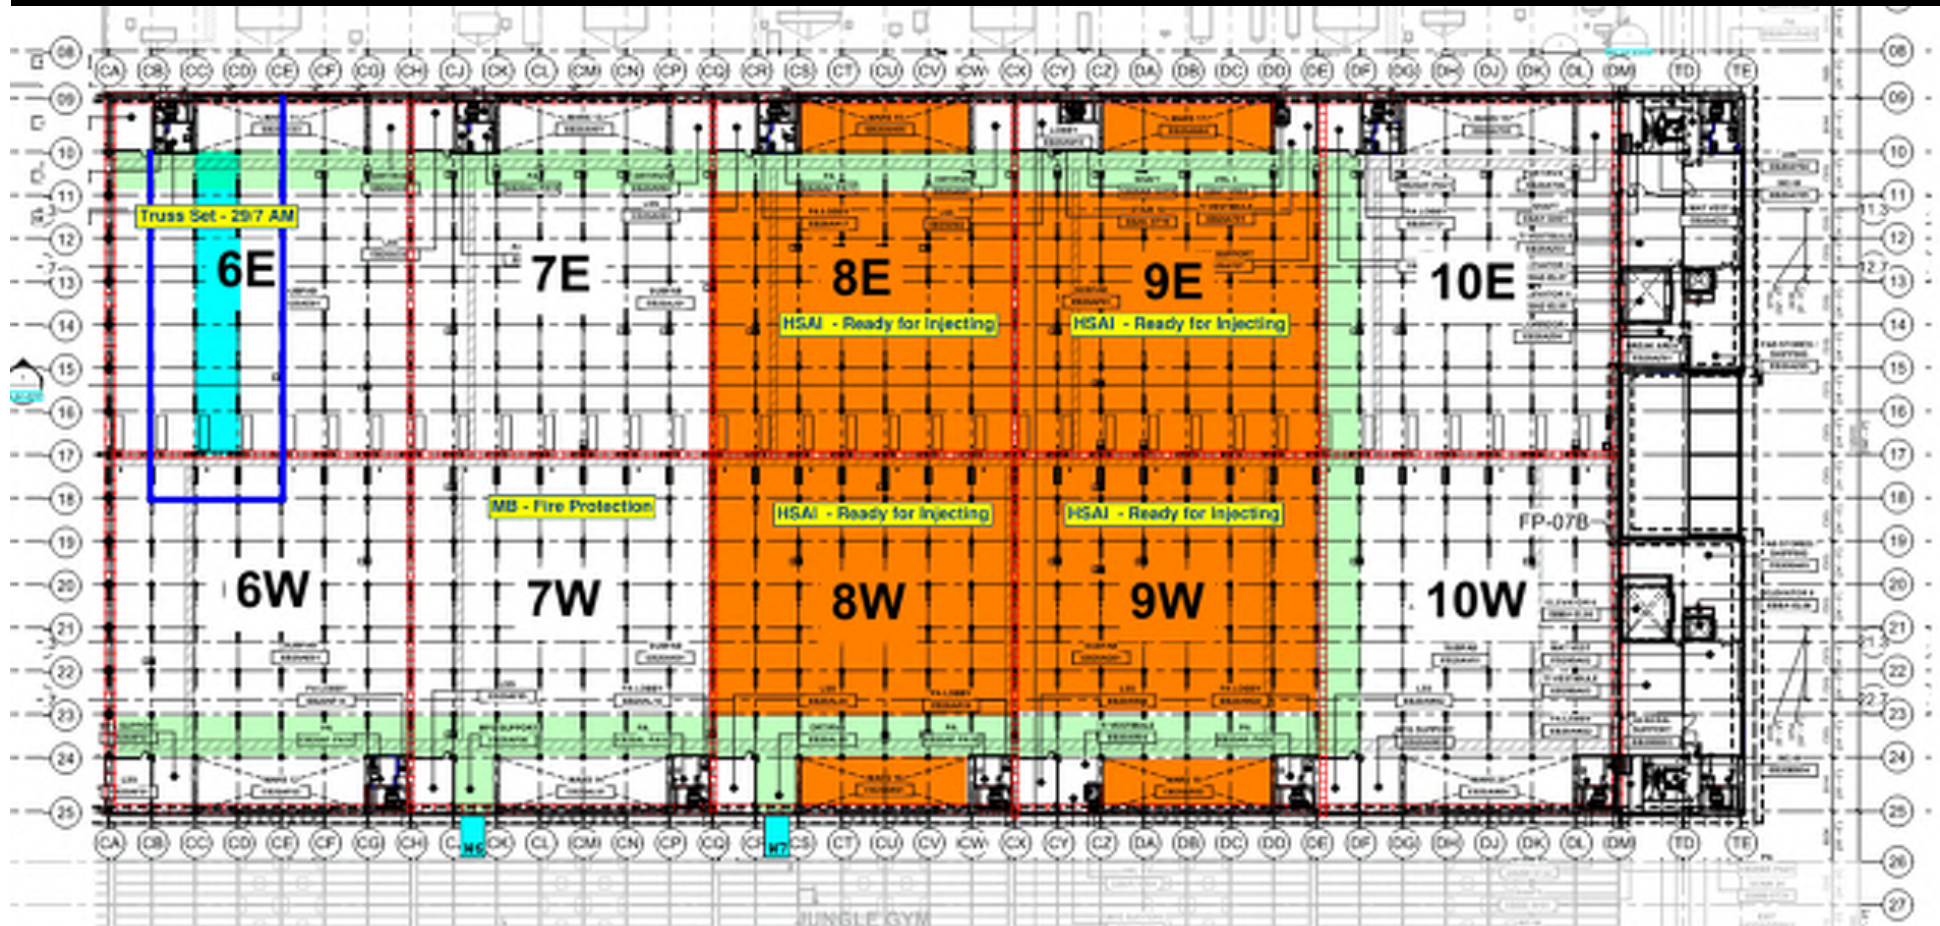



- CR level:**
-  **Access** - Cable trays, modules and stickers 1W, 2E, 2W
 -  **M3** - 1E drops, 1W drops, 2E-2W IFF
 -  **Items** - 10, 24 columns fix/wrap, 9, 25 line columns wrapping
 -  **Meplage** - Zero tolerance pipes 5E-5W, M/C preparations
 -  **D&P** - Ceiling rods 1E, 5E blades install
 -  **Tourish** - 24-25 lines, 4E-4W
 -  **HYG** - 1W Litho crane plates install, 5W Litho crane steel
 -  **PT** - Duct prep for test AA-AH east
 -  **Telad** - Seismic cables 1W,

**Before - 1W 25 line done
1E 9 Line Ongoing**

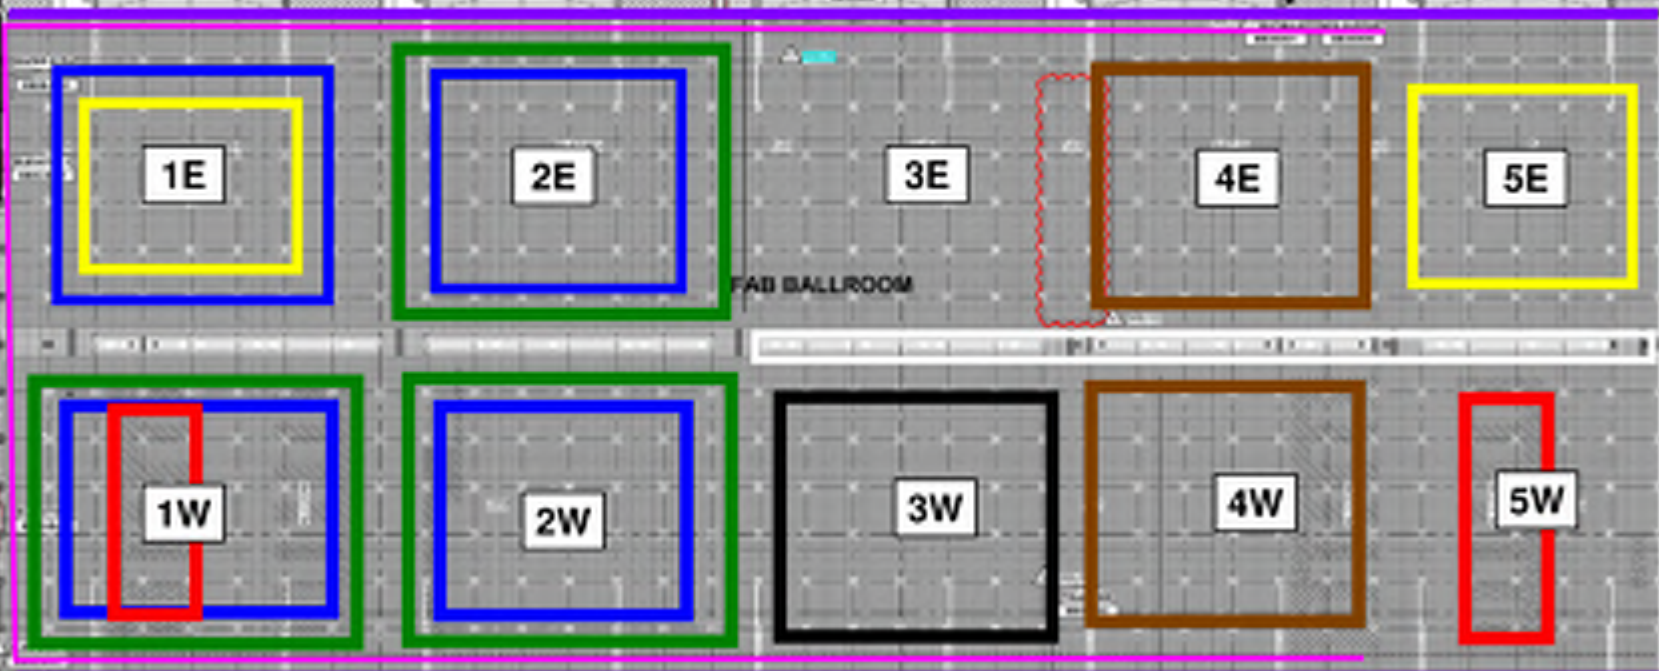



FAB BALLROOM


NEW


- WYSN** - west side welding tube and replacing beams
- East** - East/West floor done GA/GC
- SE** - east side pipes needs to be completed
- HYG** - East to finish steel, West receiving material


Link
RP - Fire proofing
D&P - Bolts torque

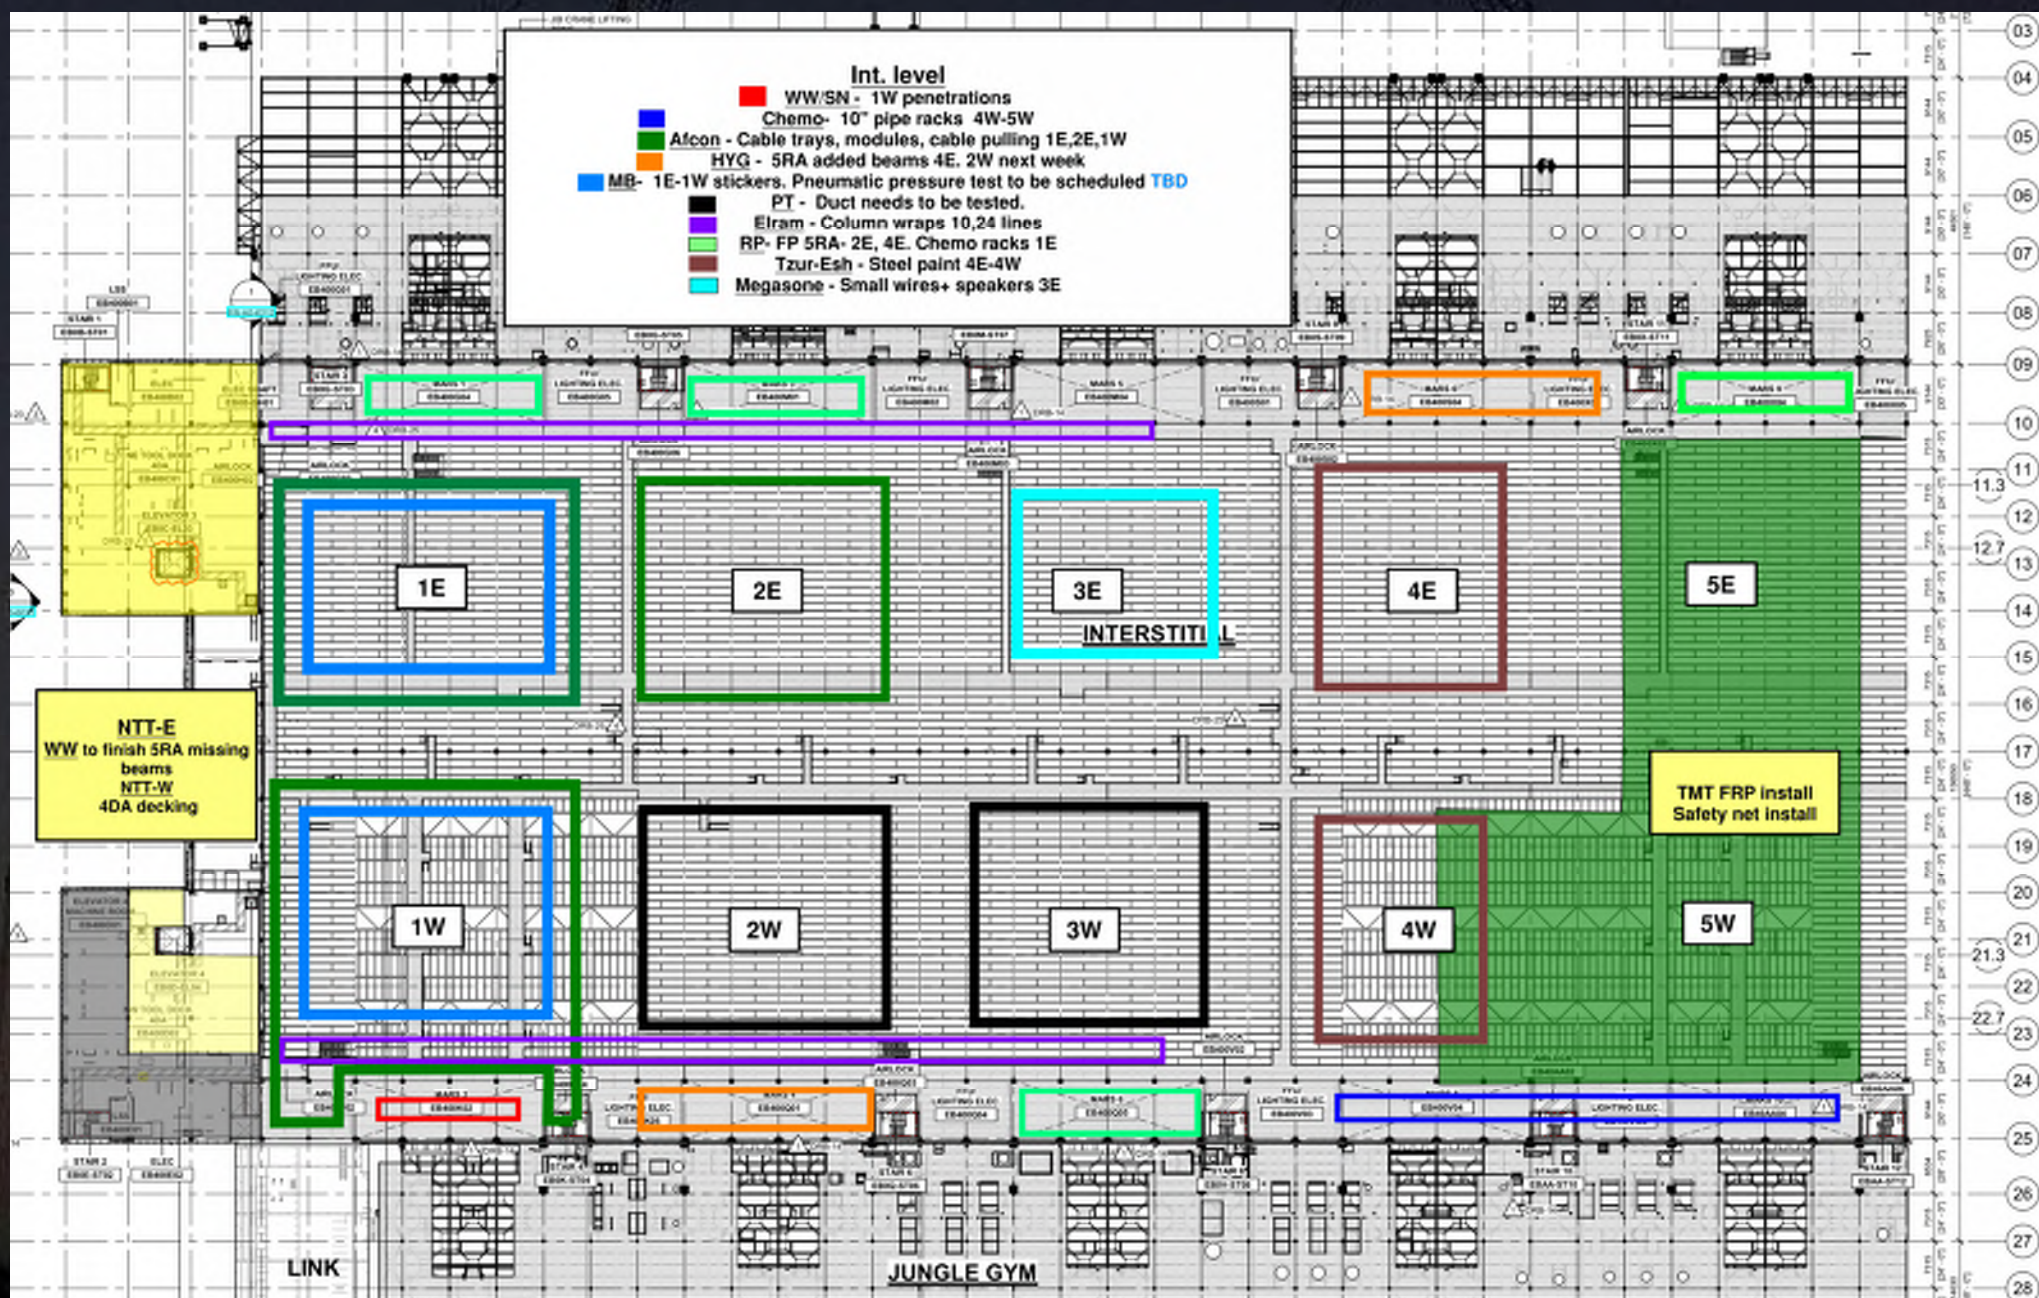


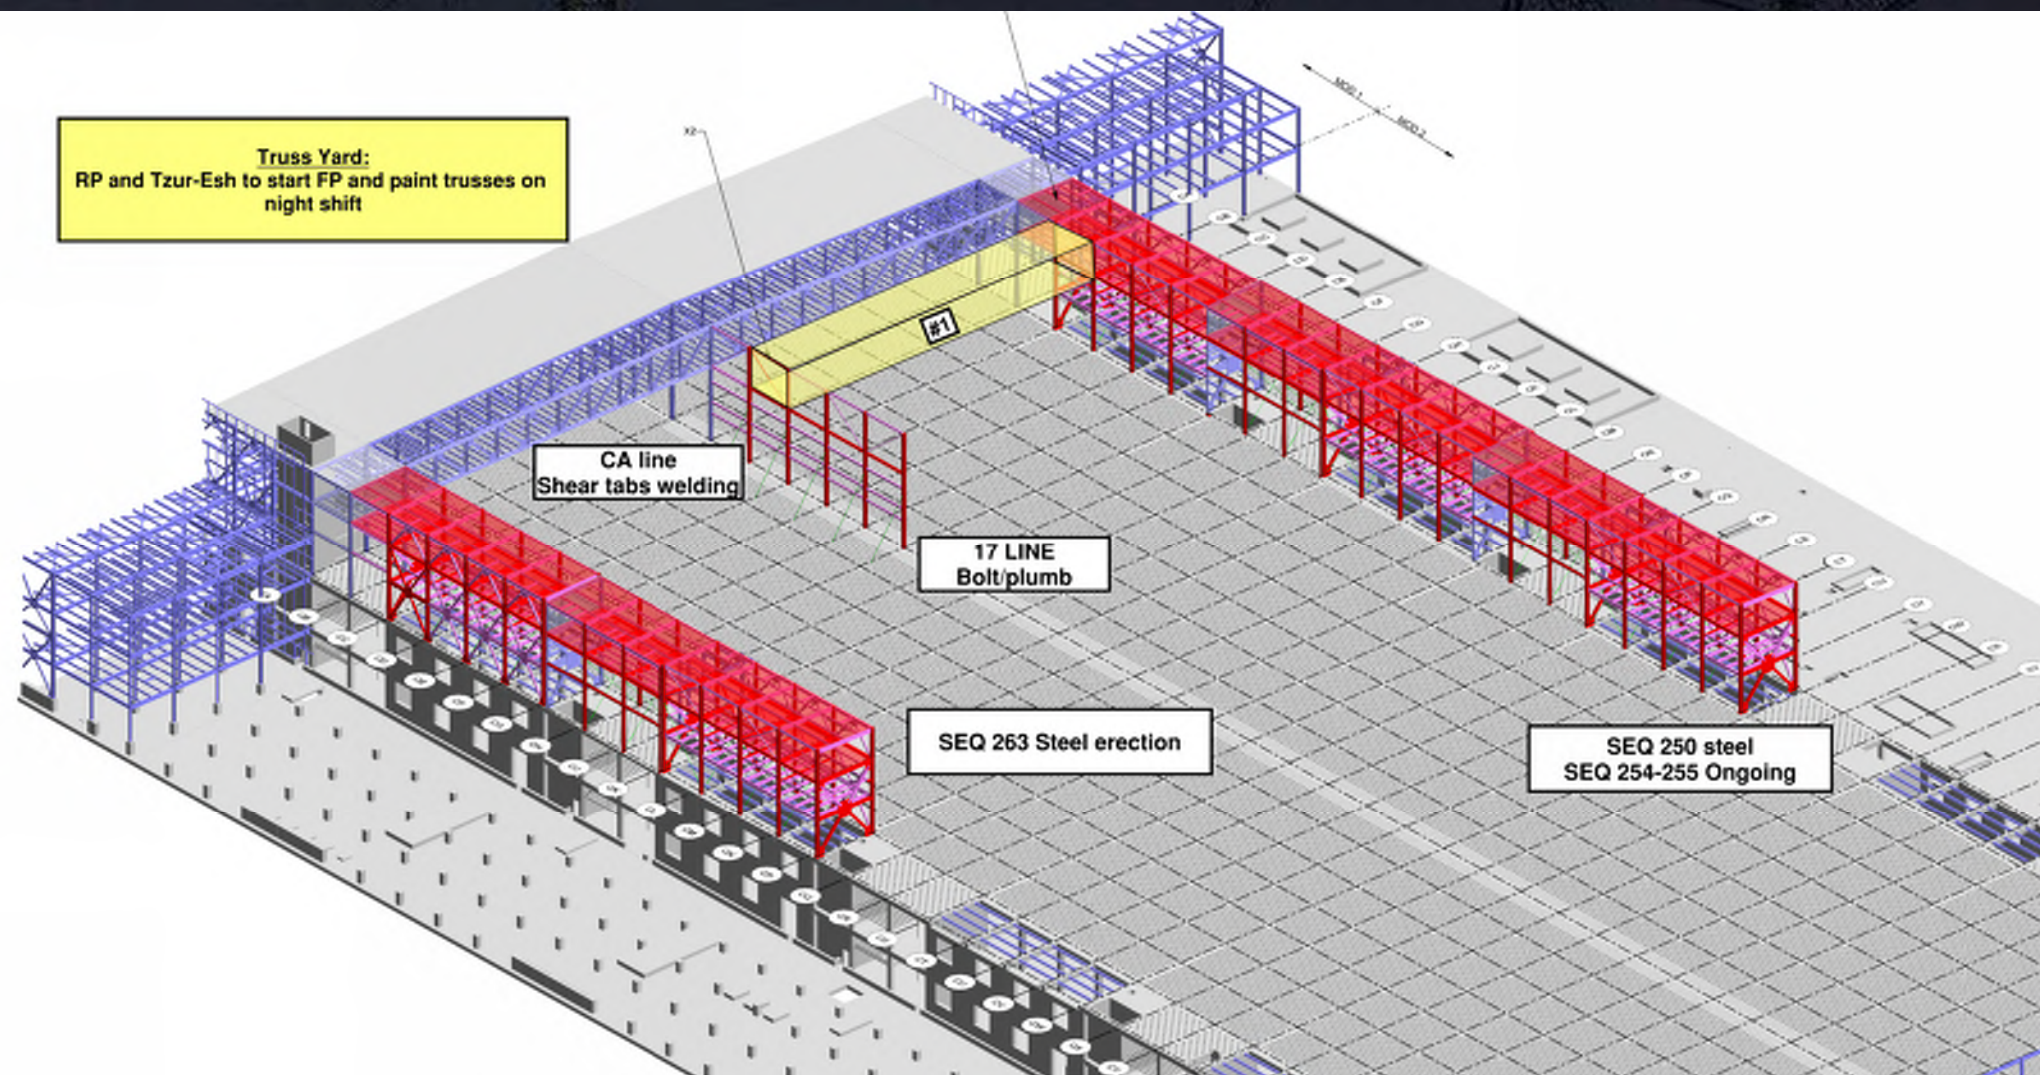

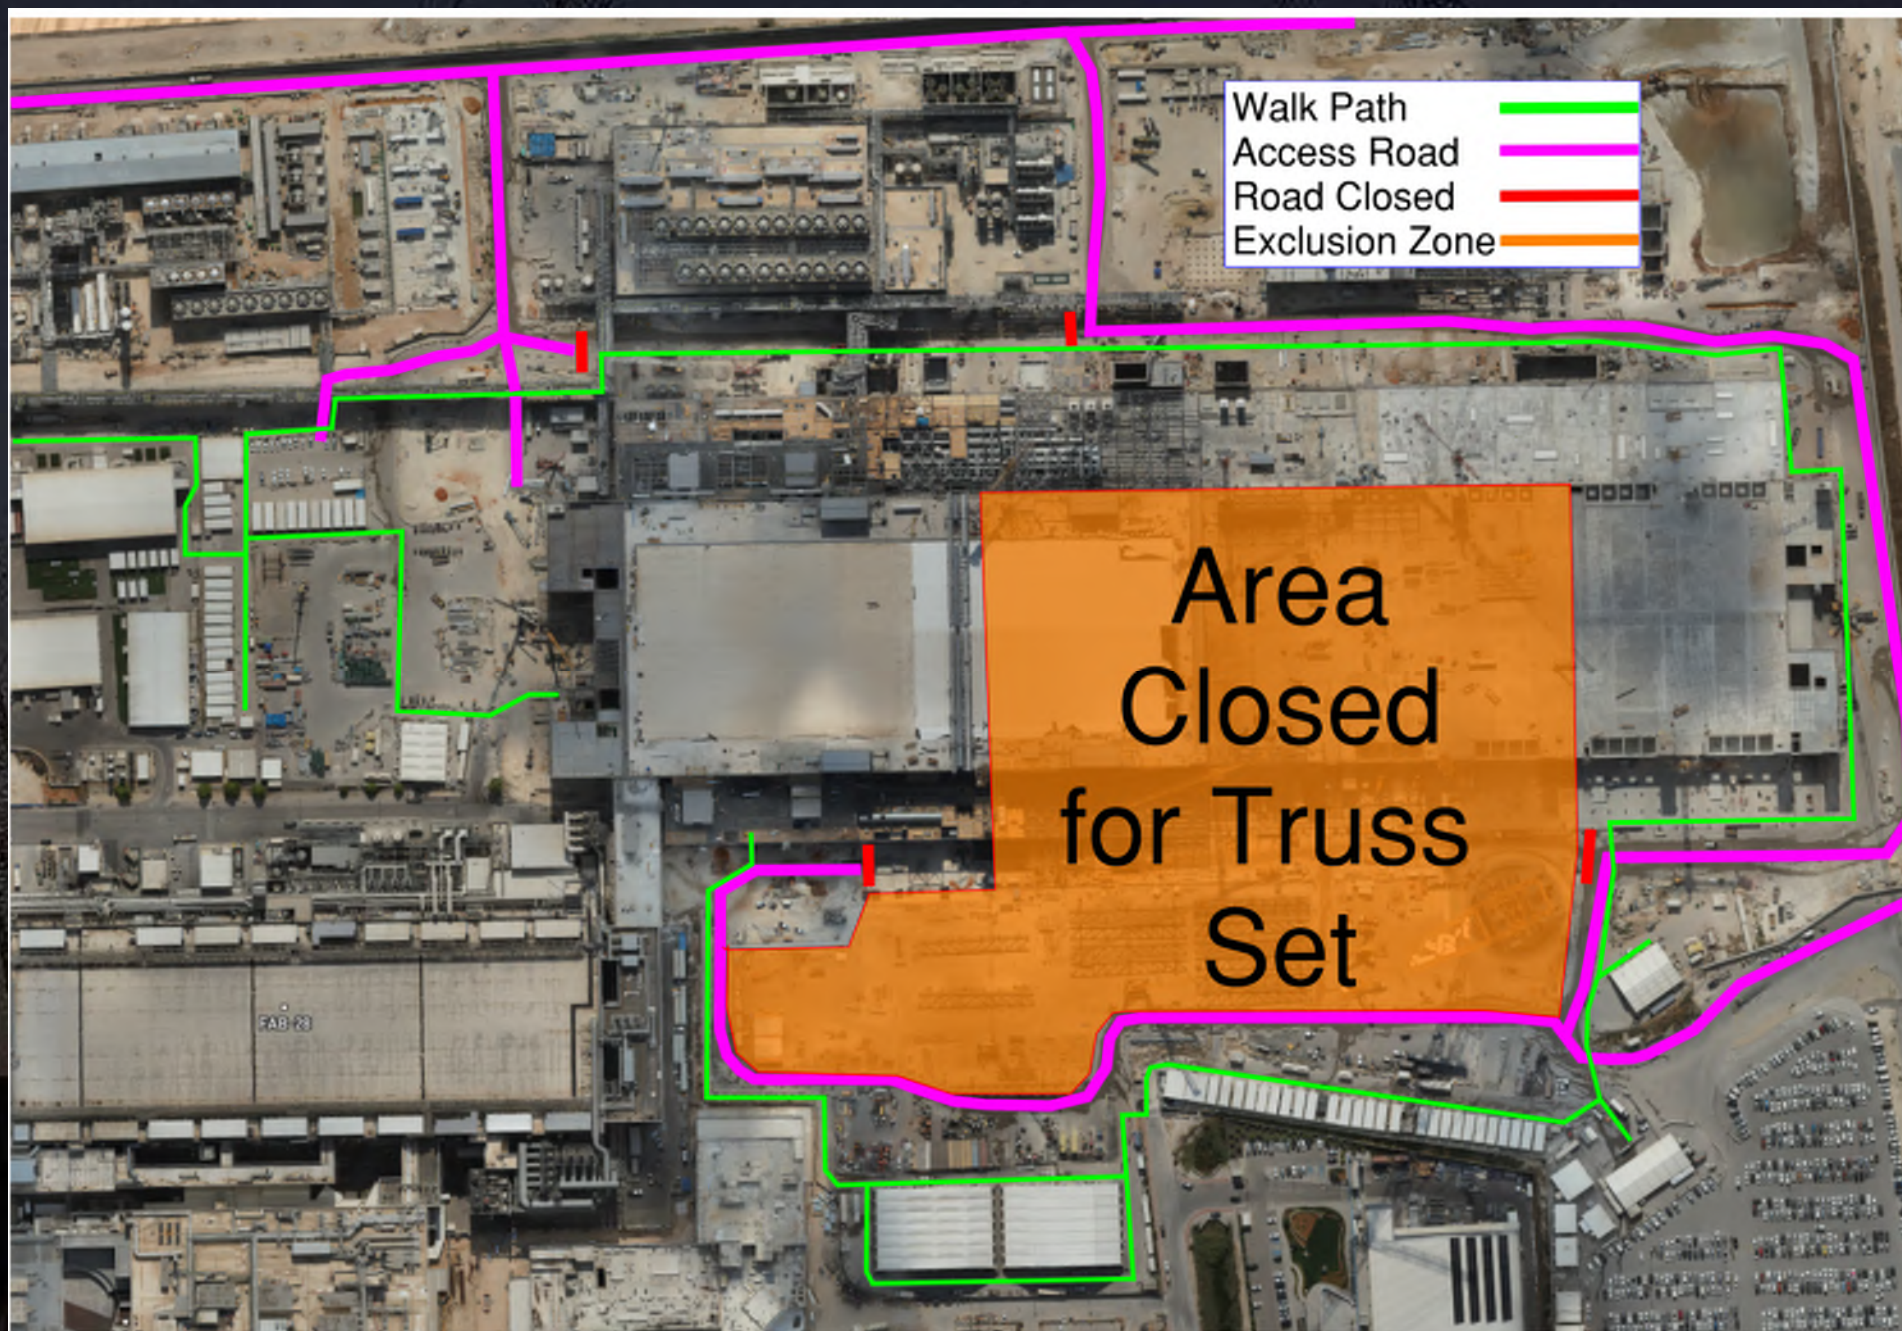

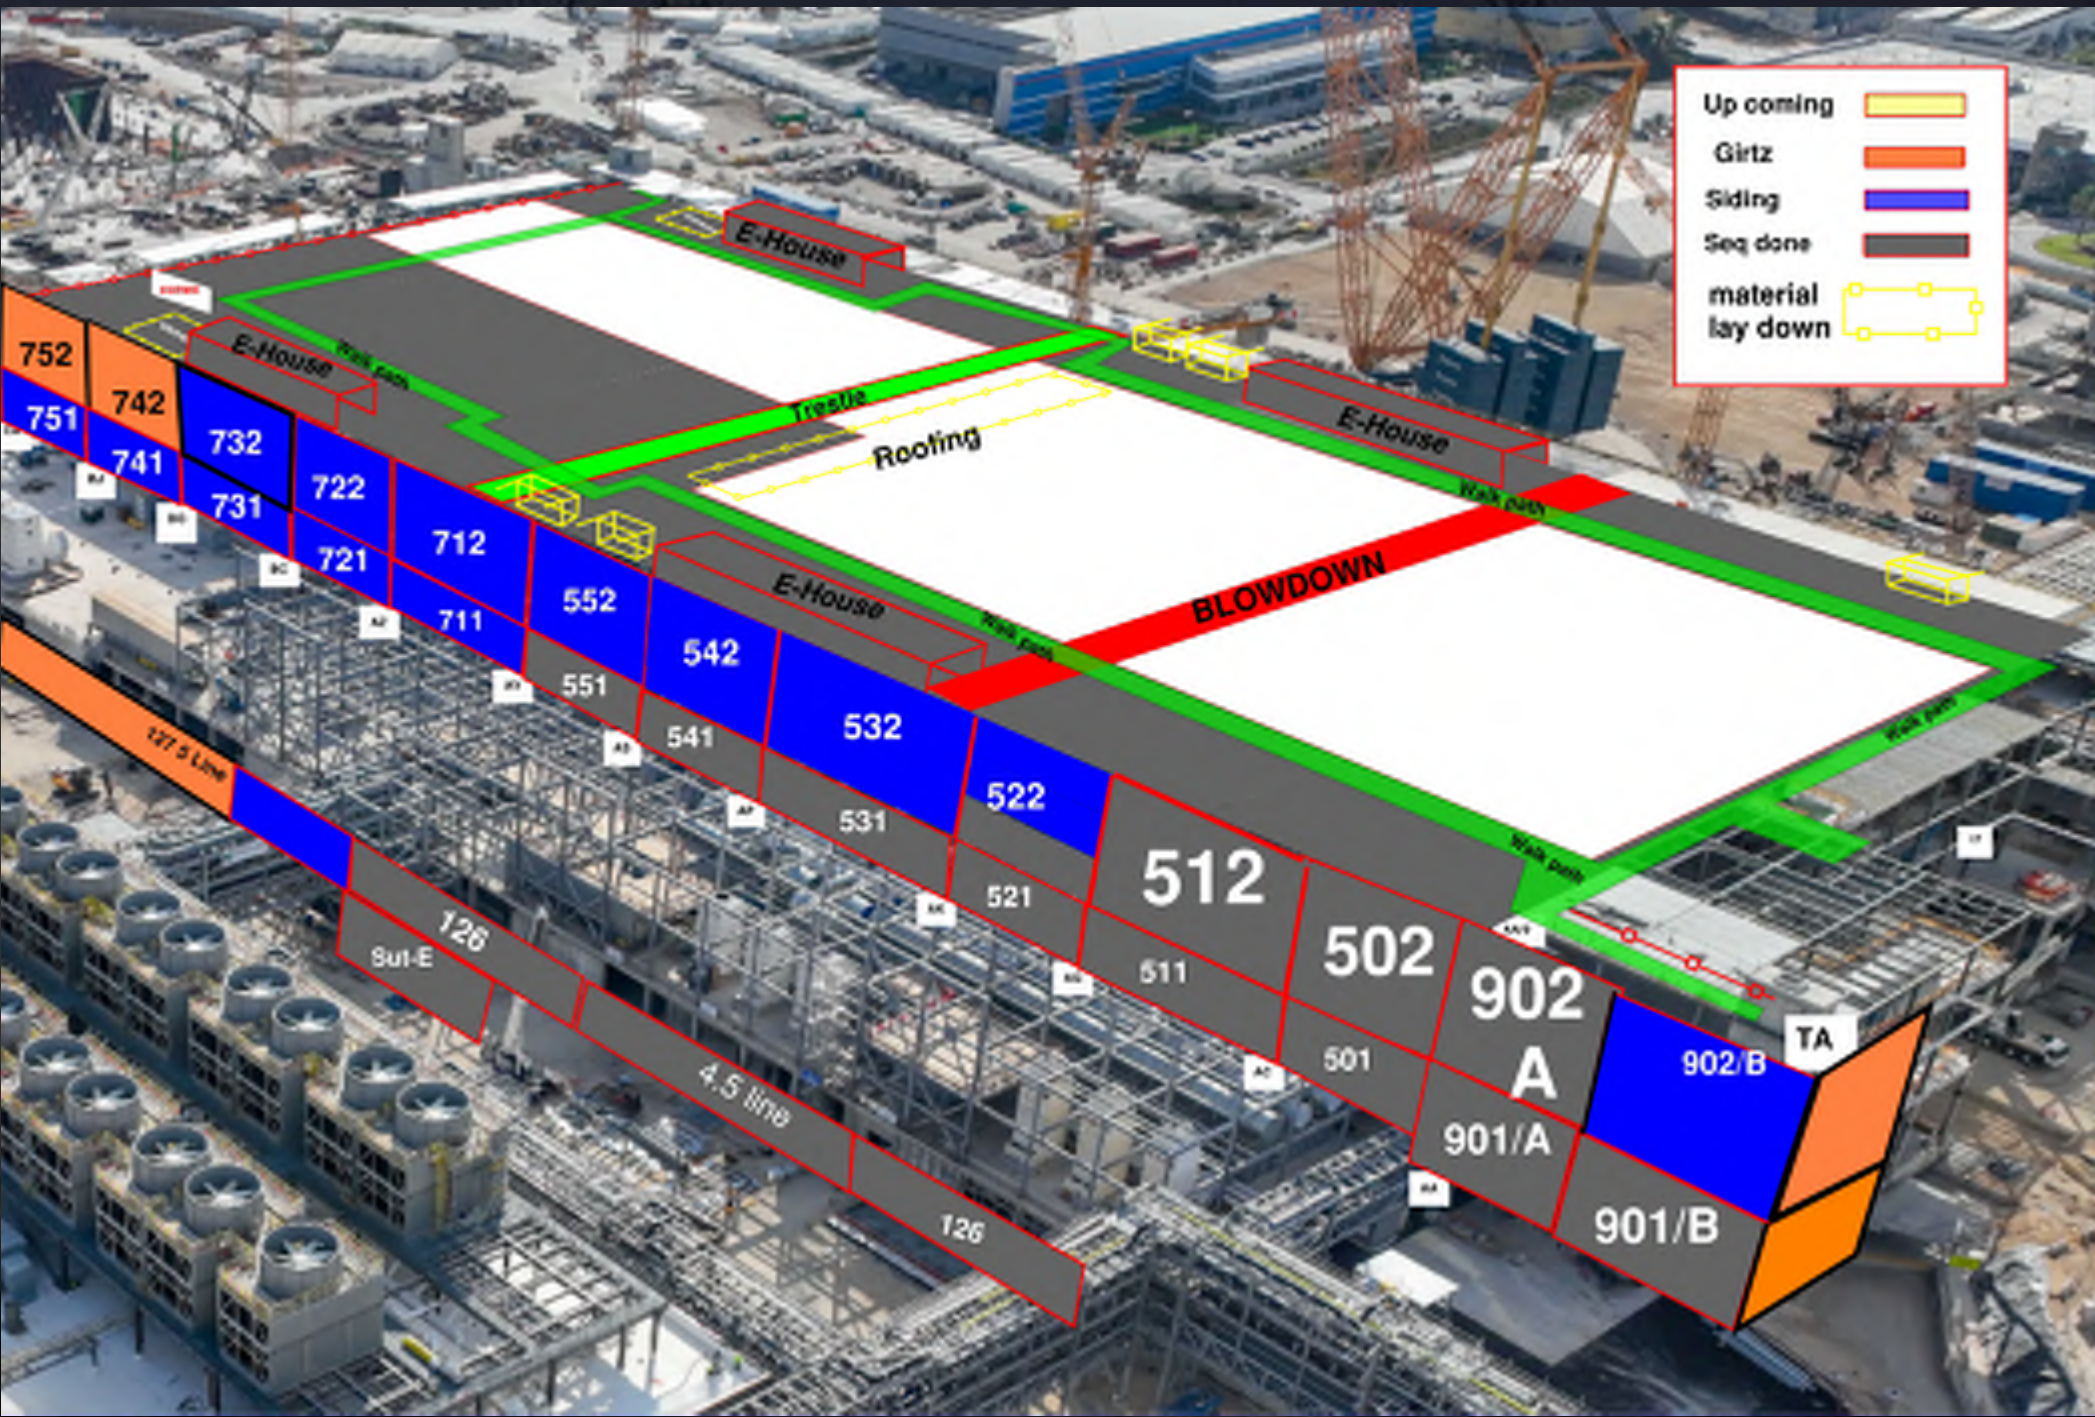

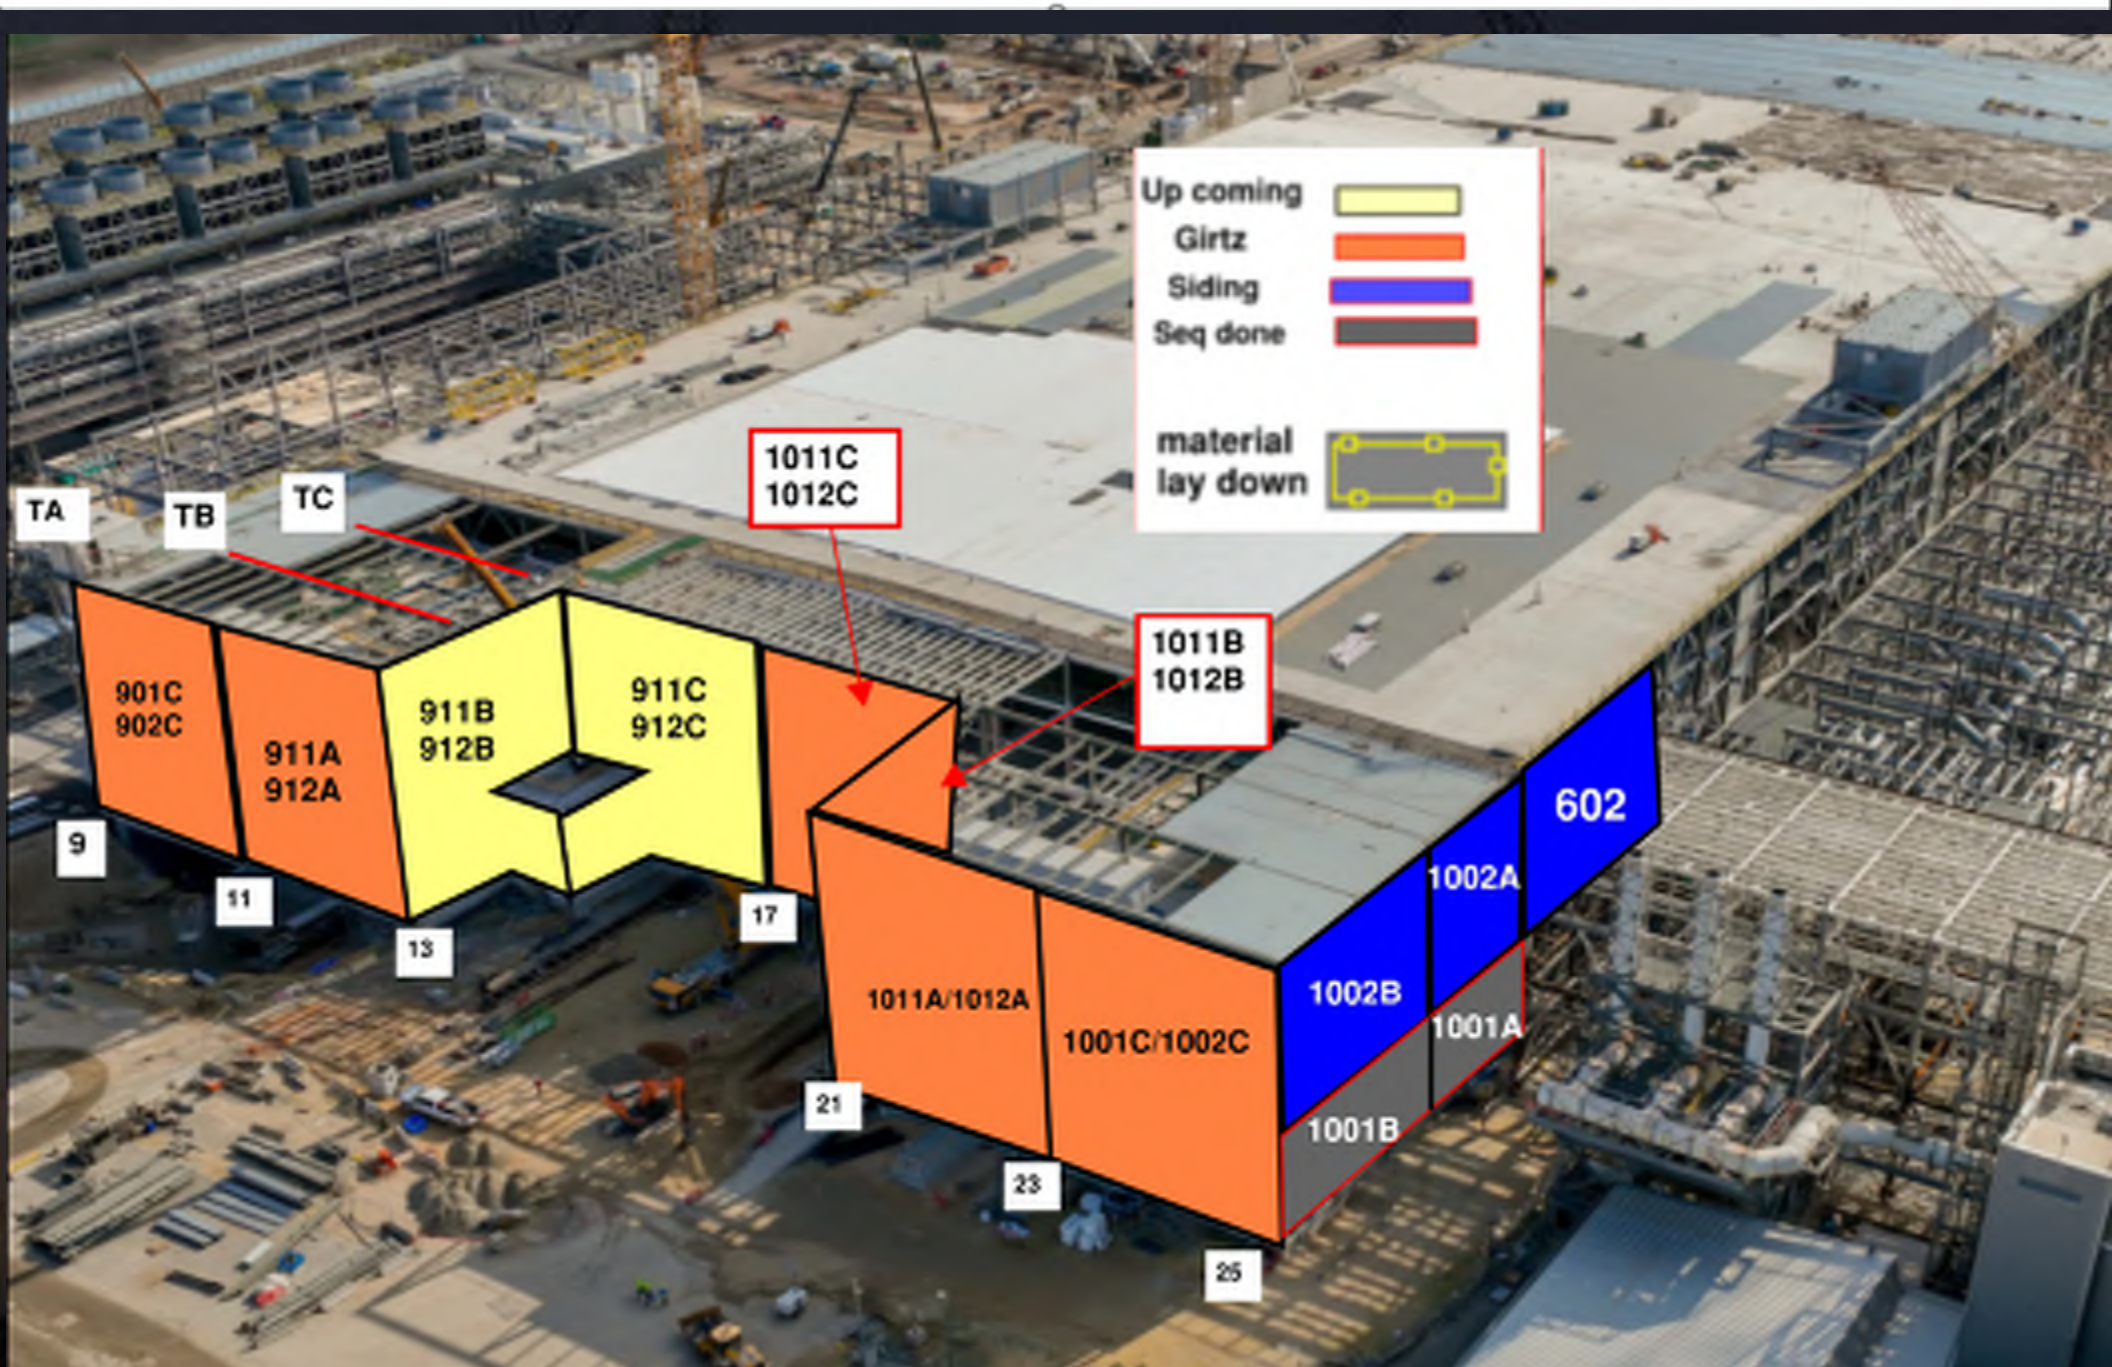


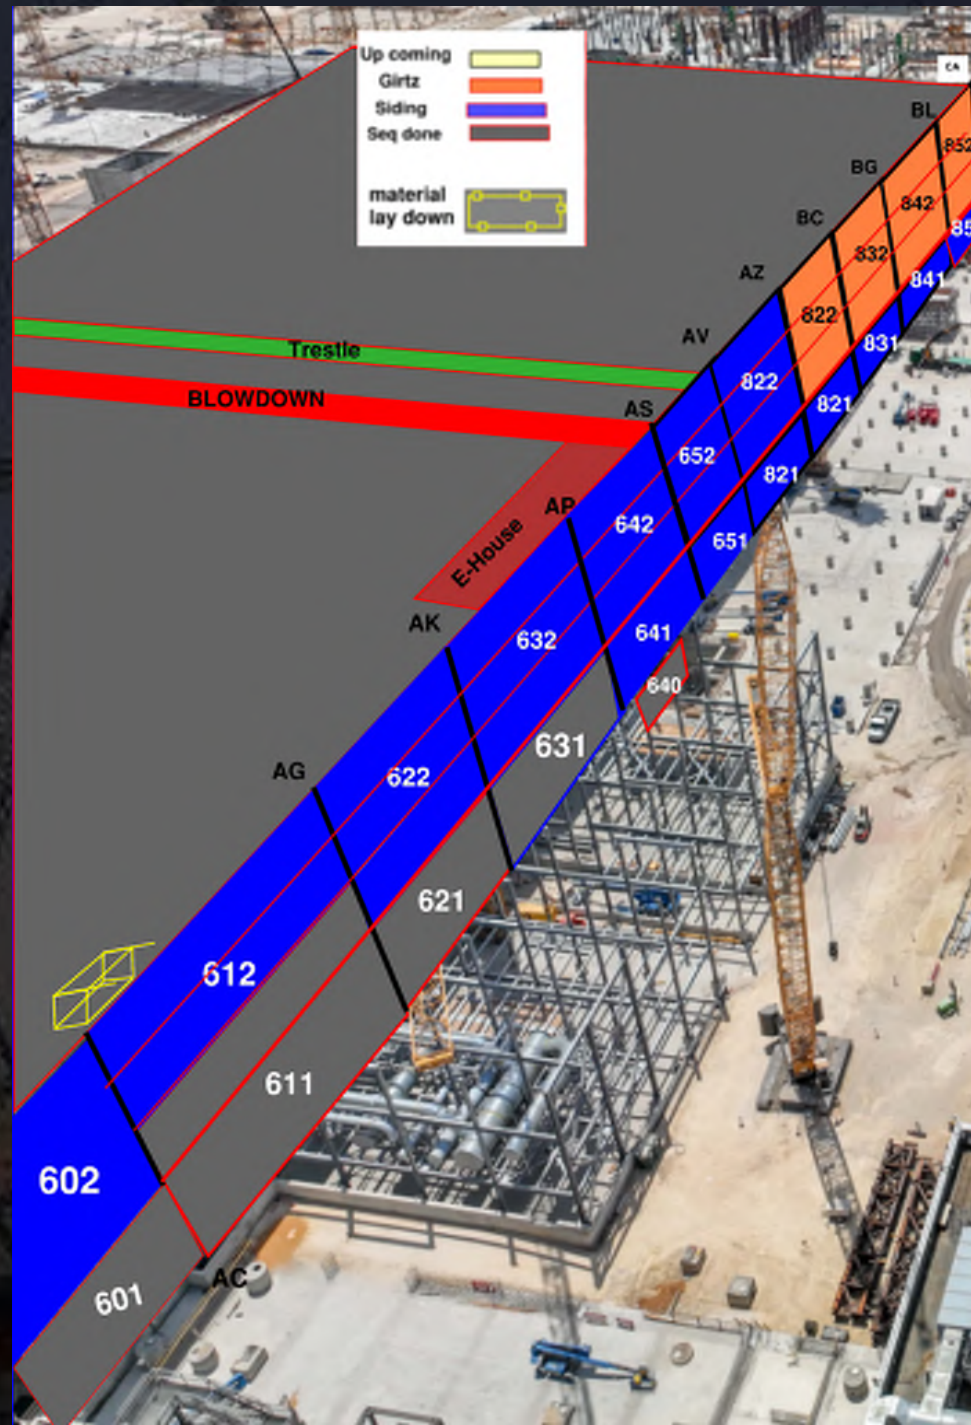

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

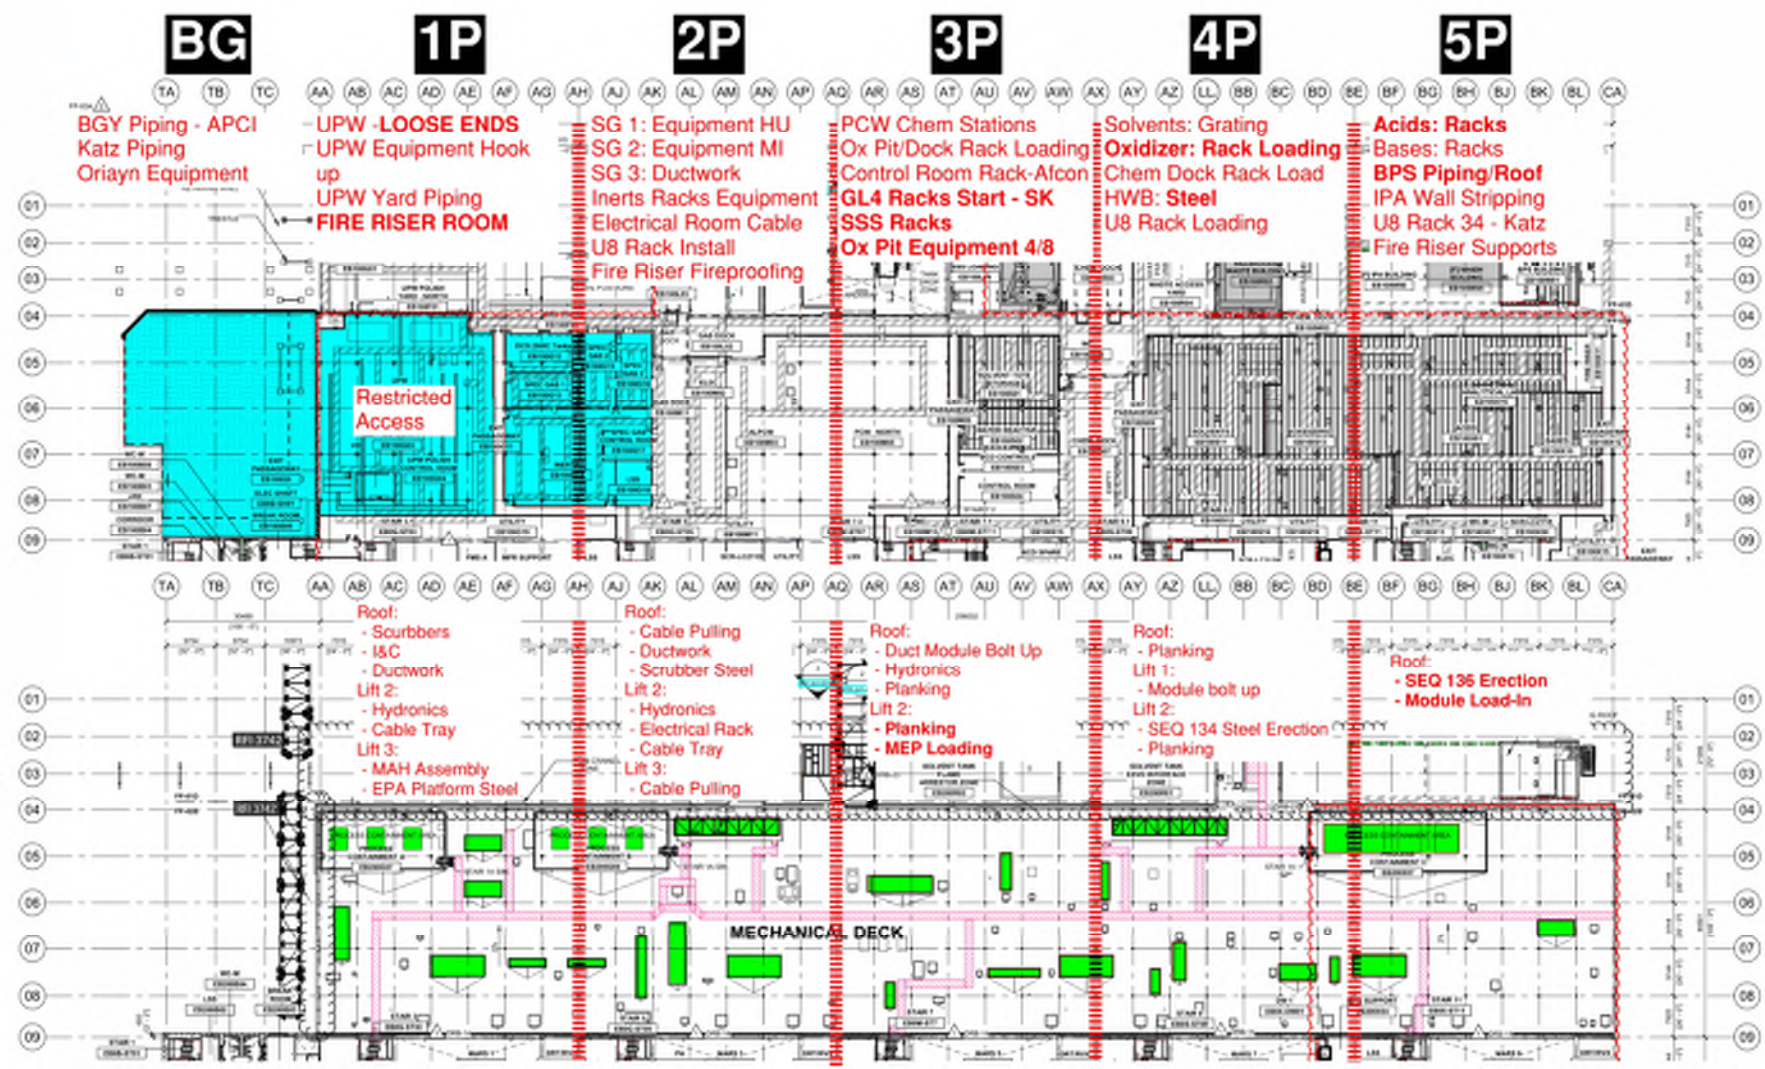

PSSS.2

Utility Level
1YA

PSSS Roof
2SA

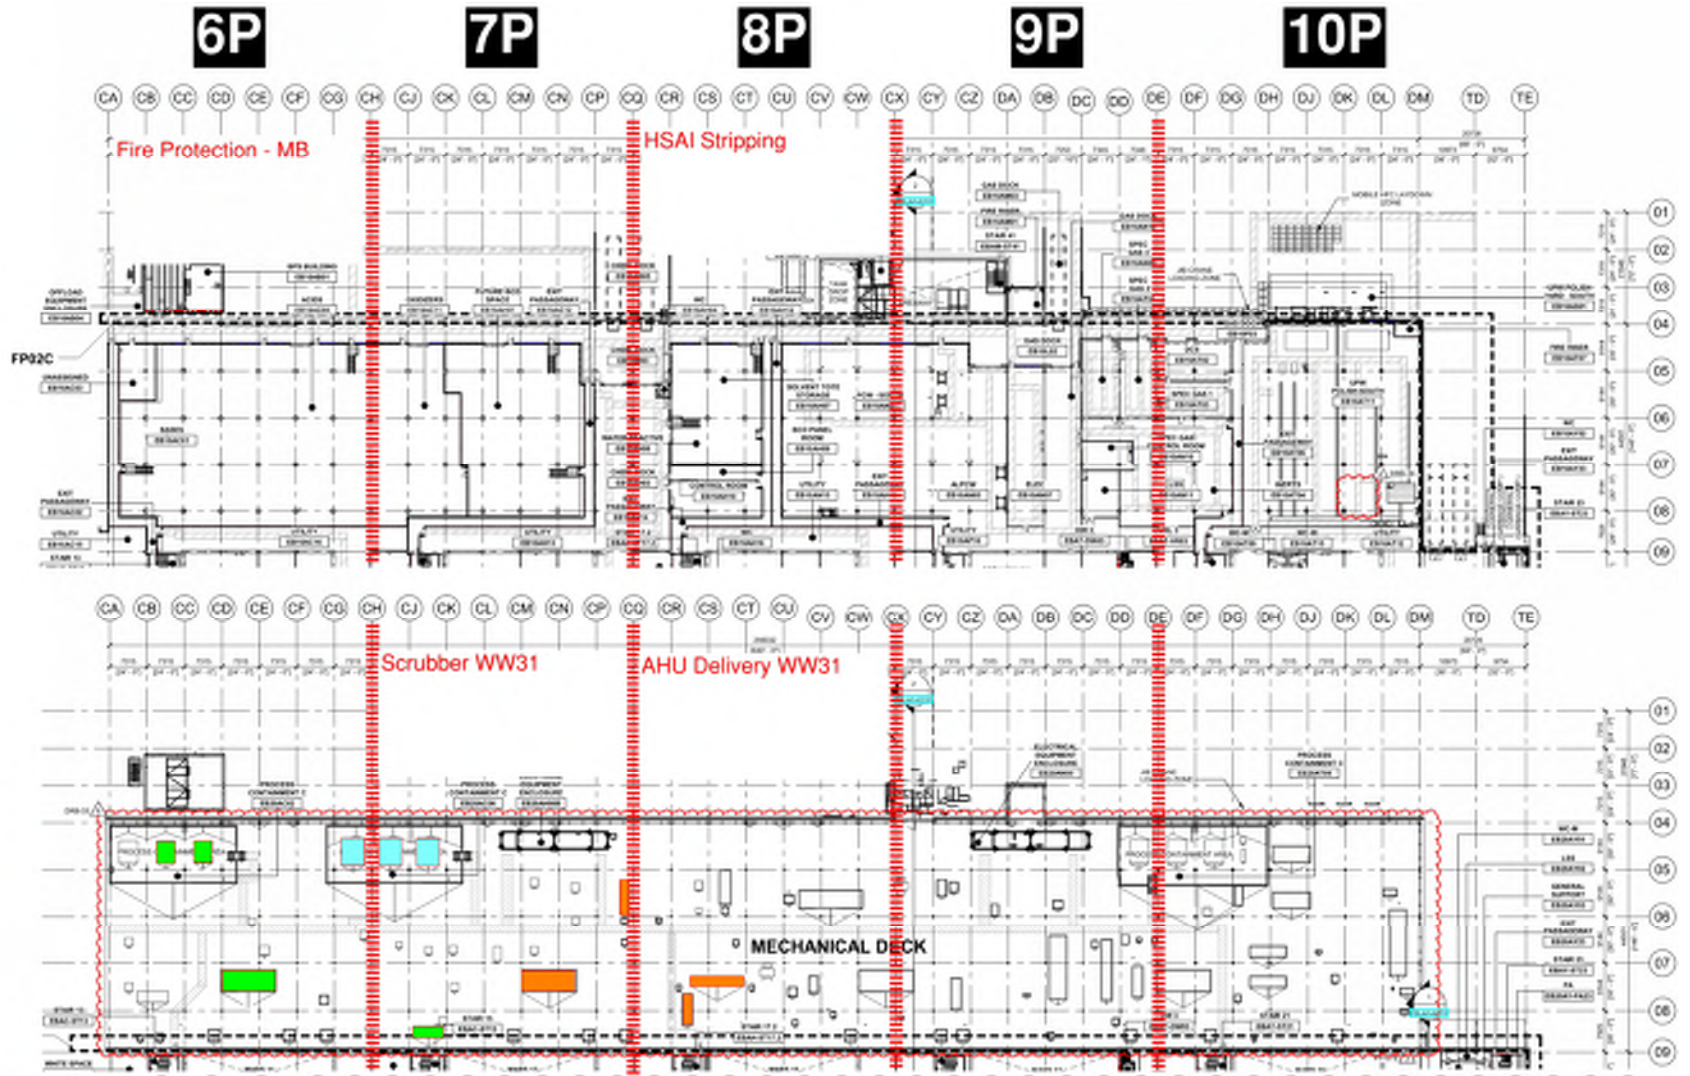




WJG 01J, 02J LIFT 2 & 3







WJG 03J, 04J, 05J LIFT 2 & 3

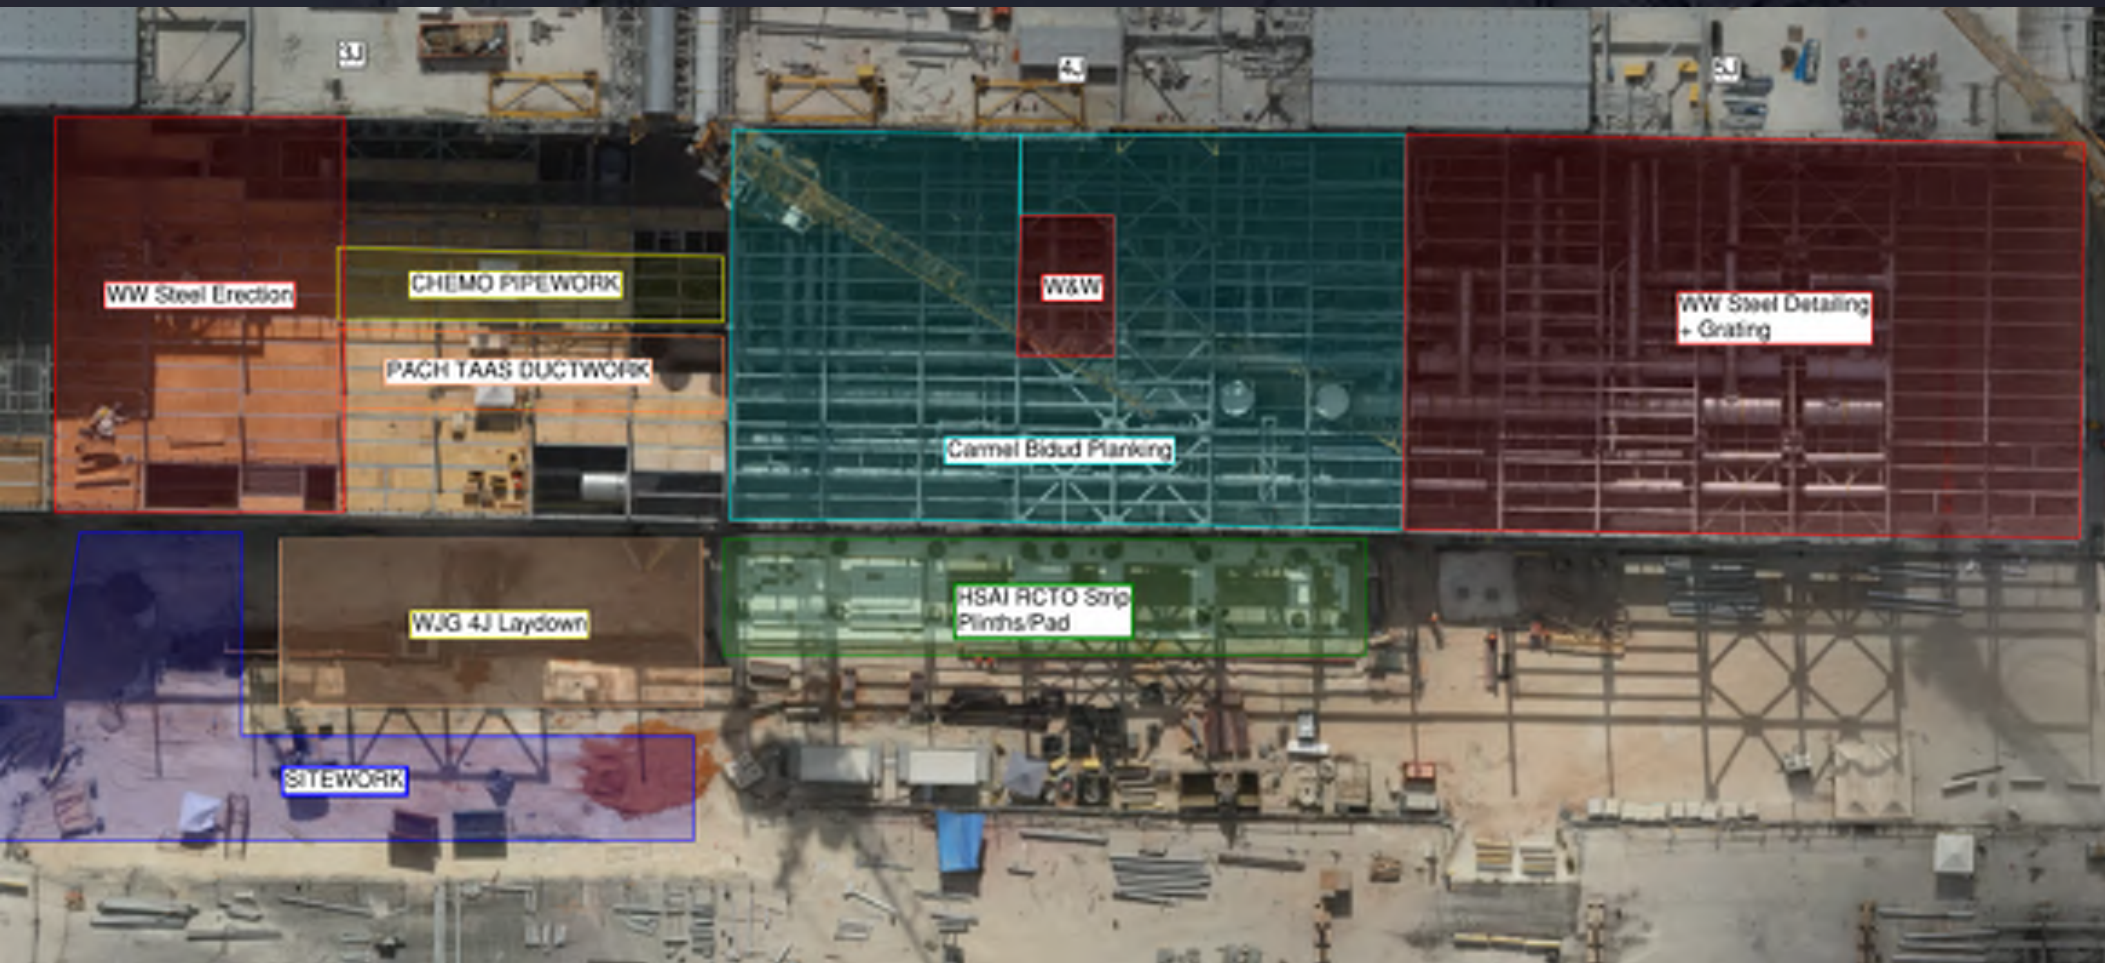






WJG UTILITY LEVEL BUILD OUT

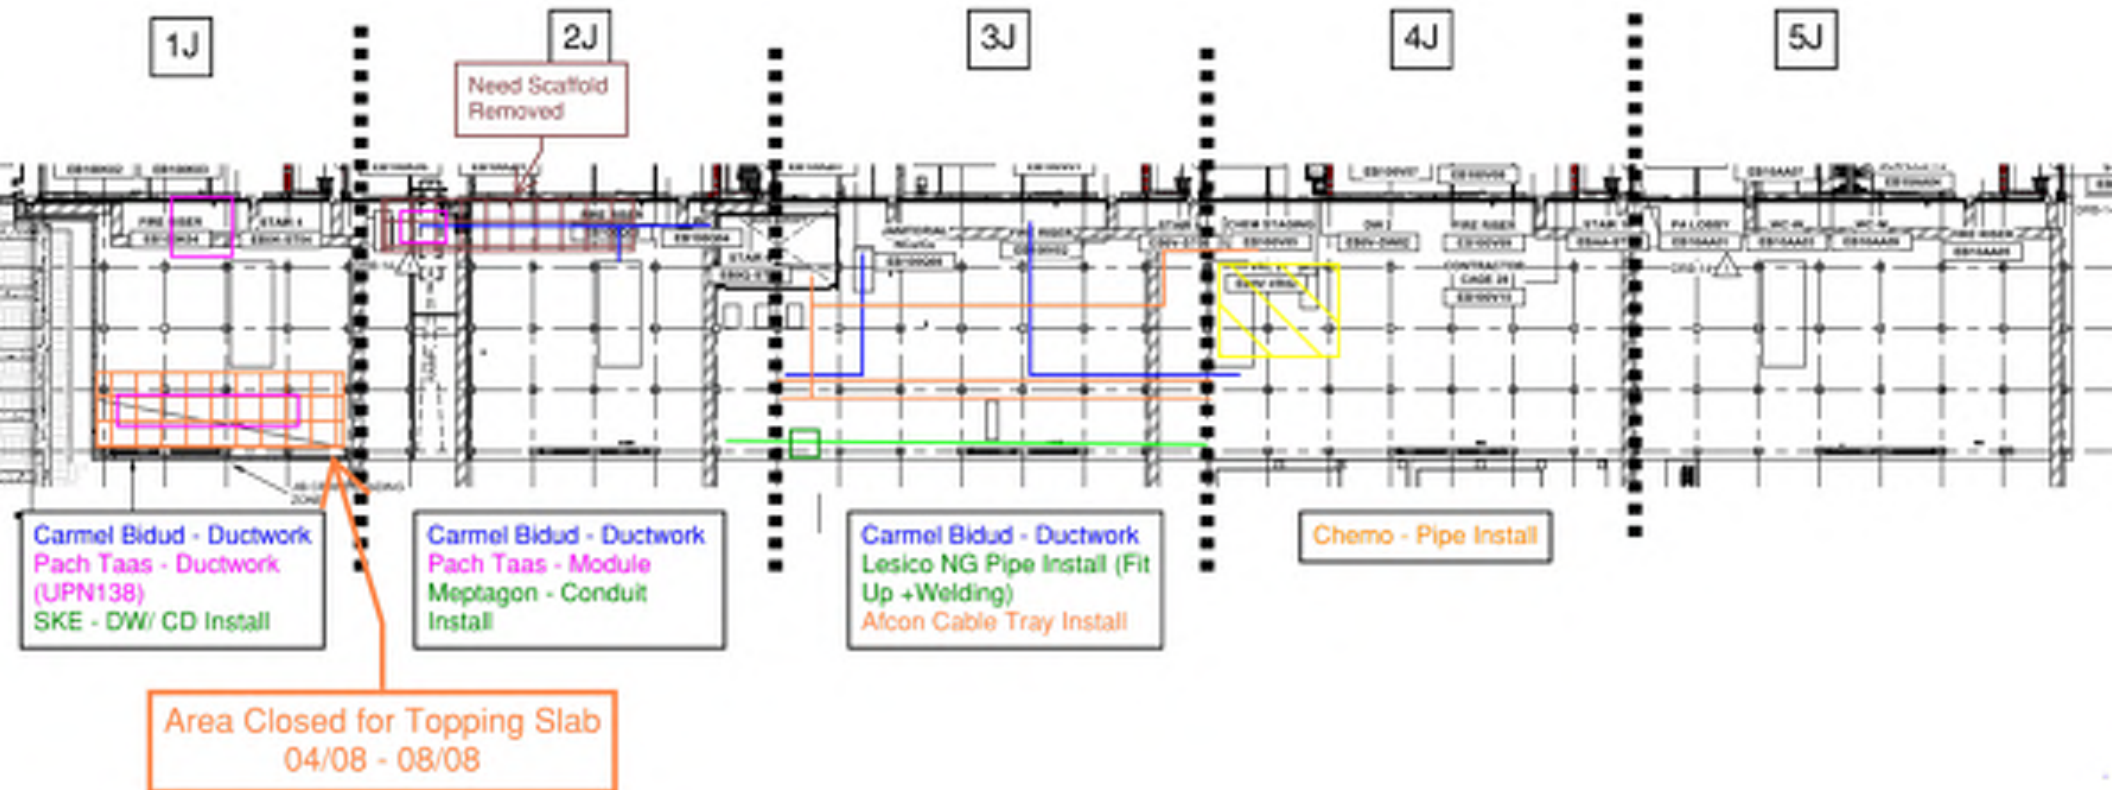


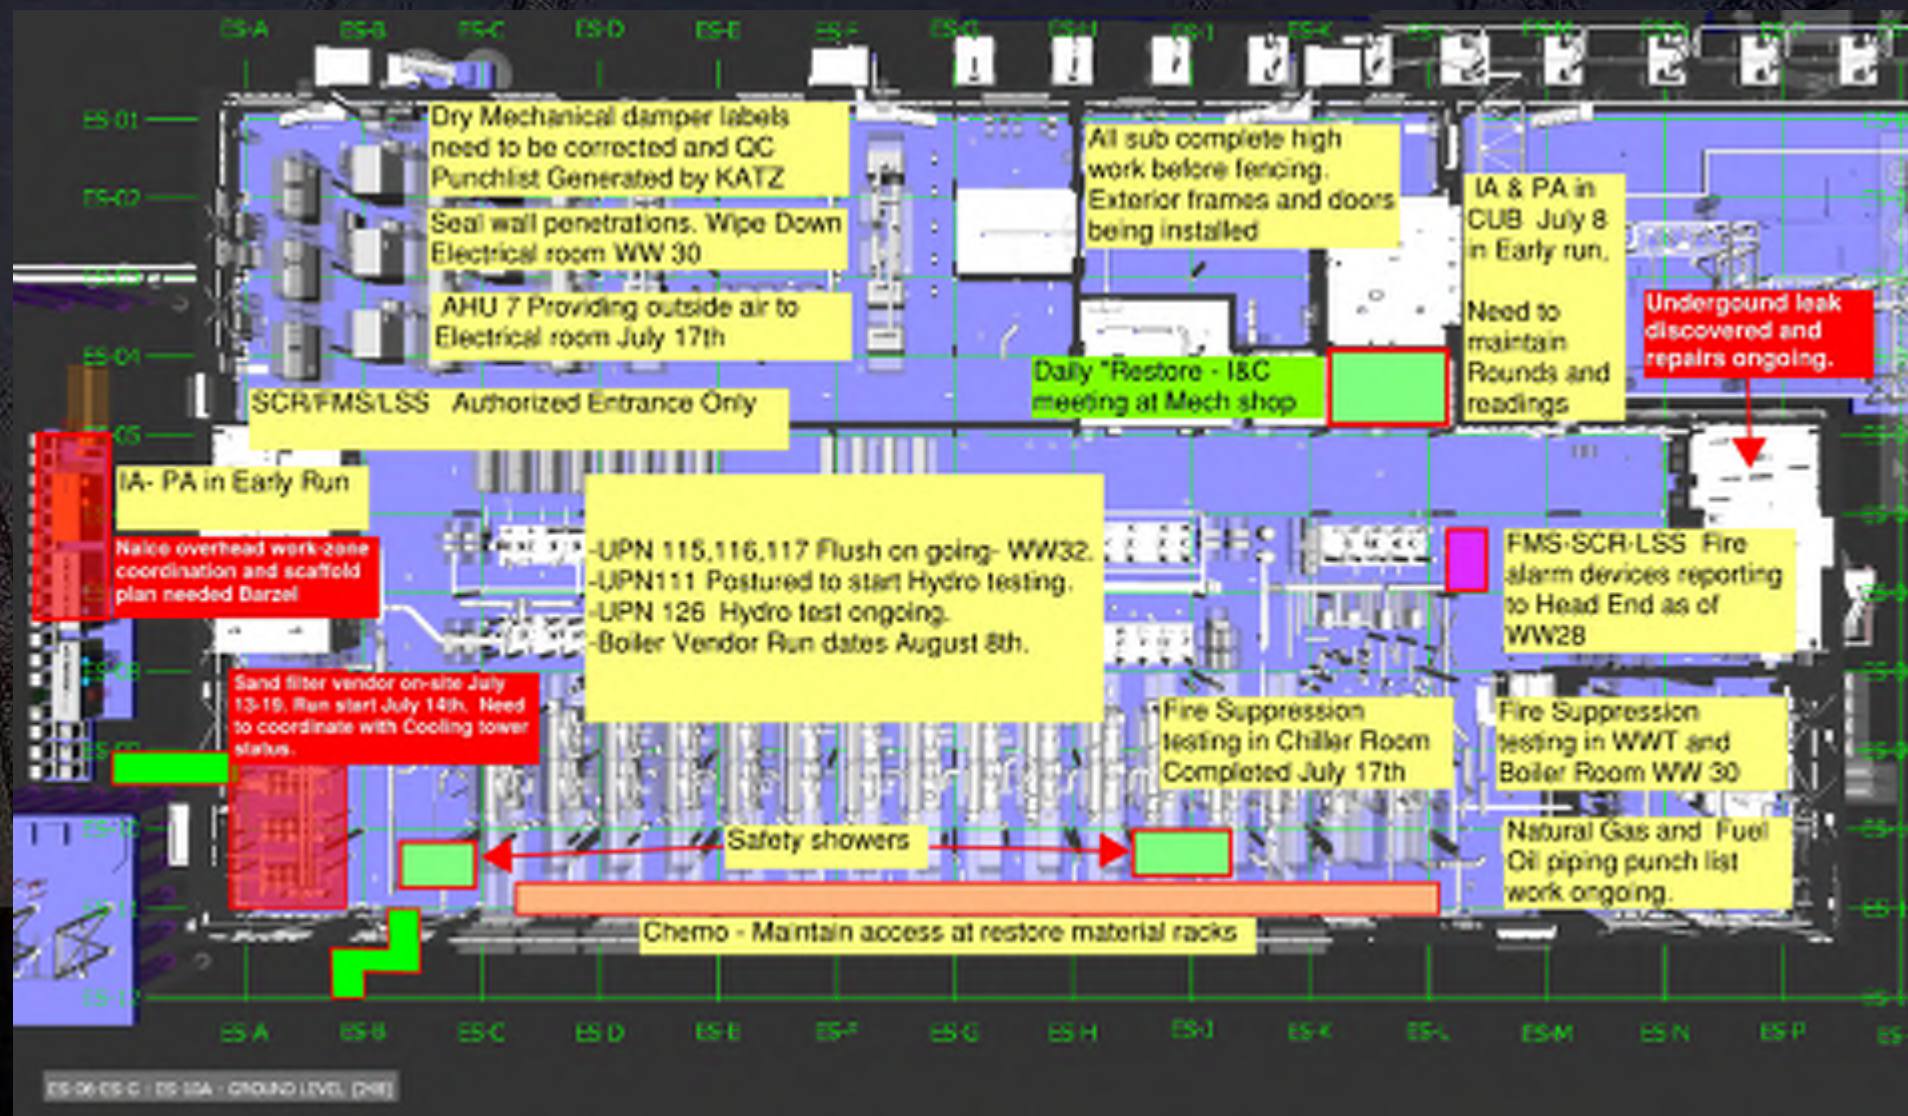

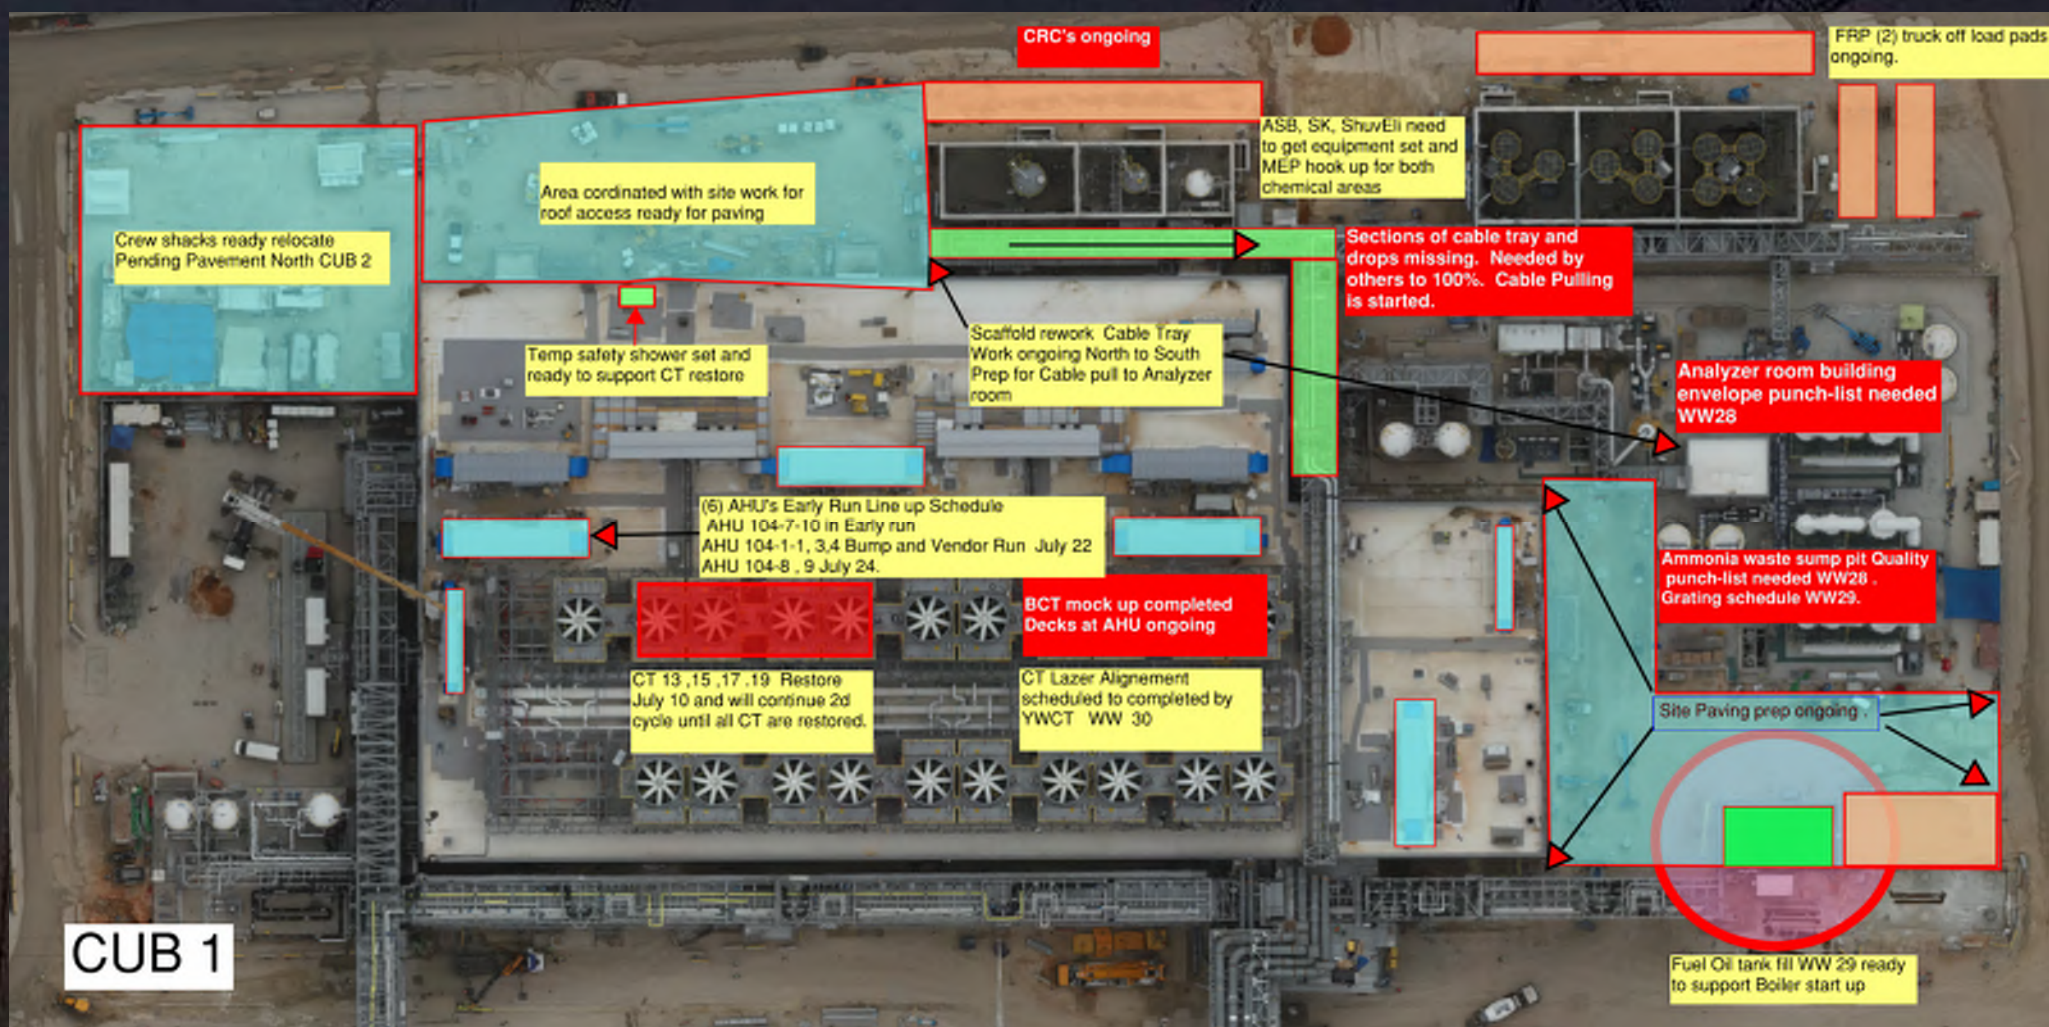

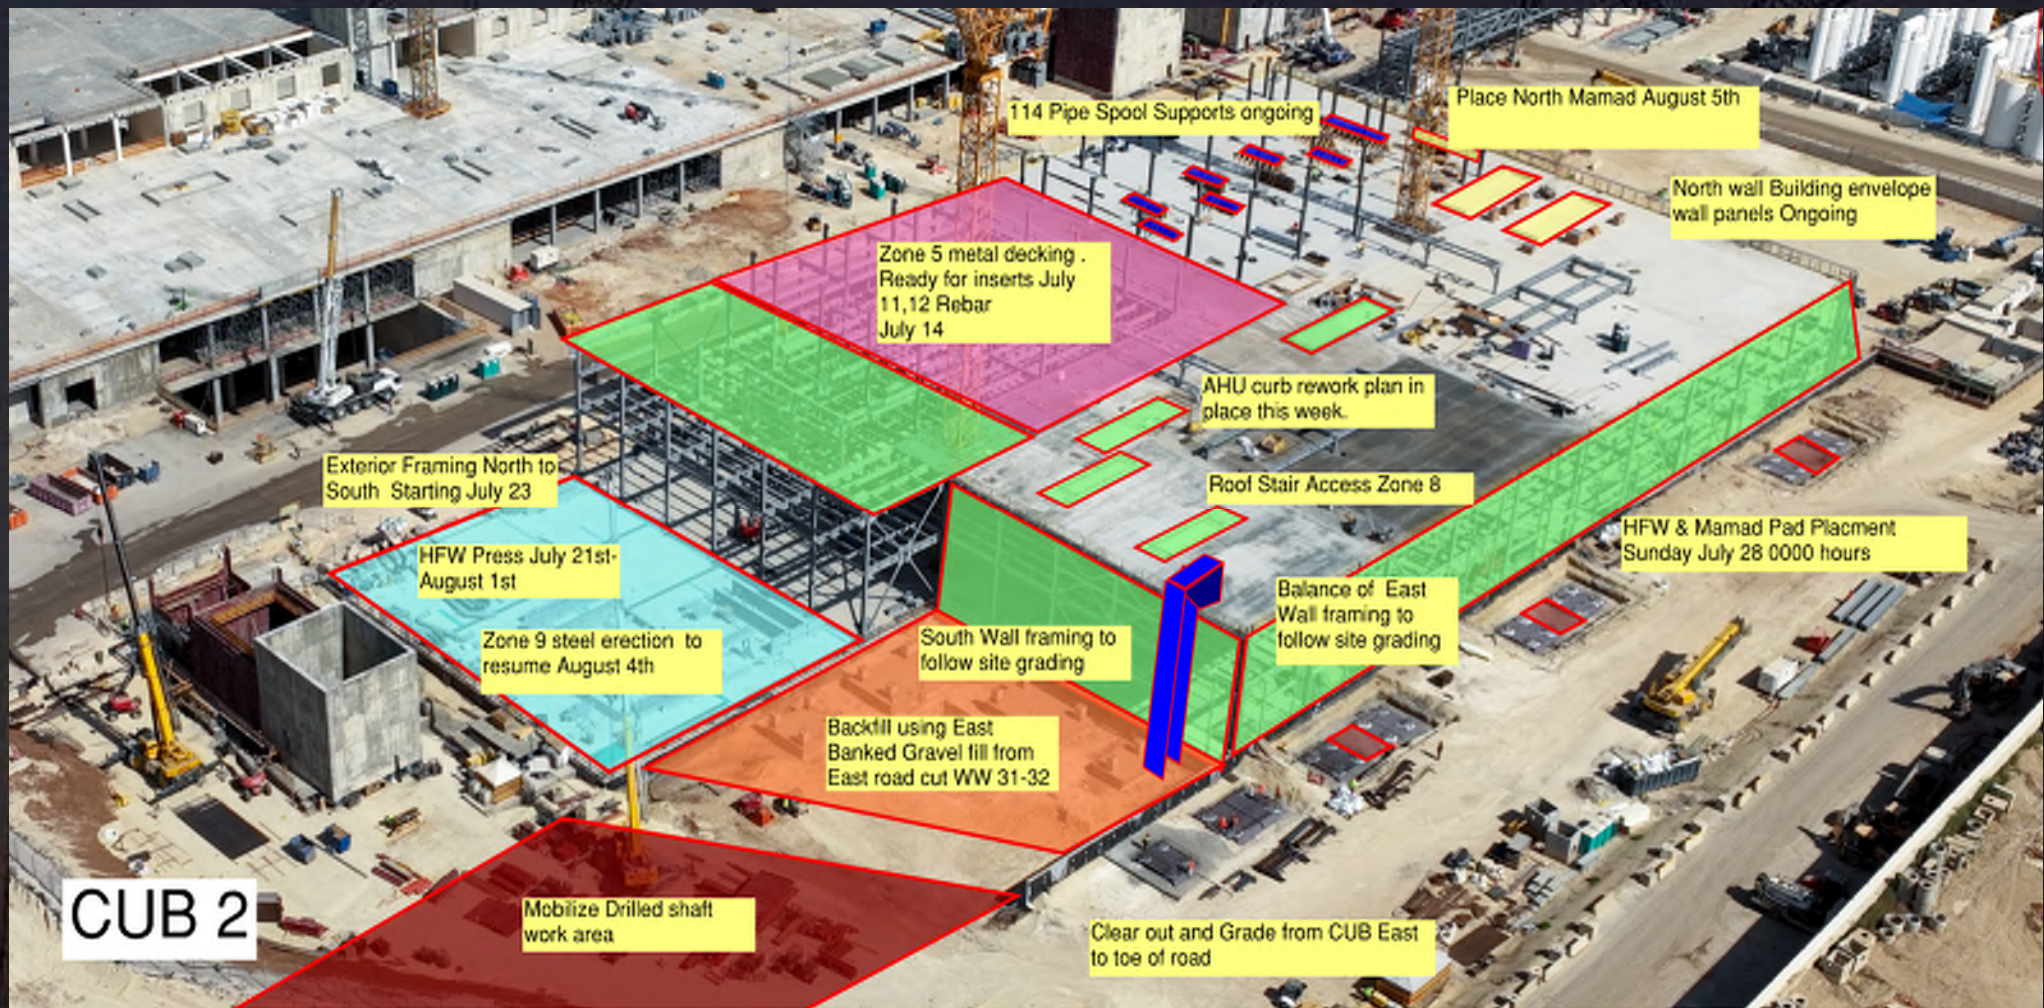

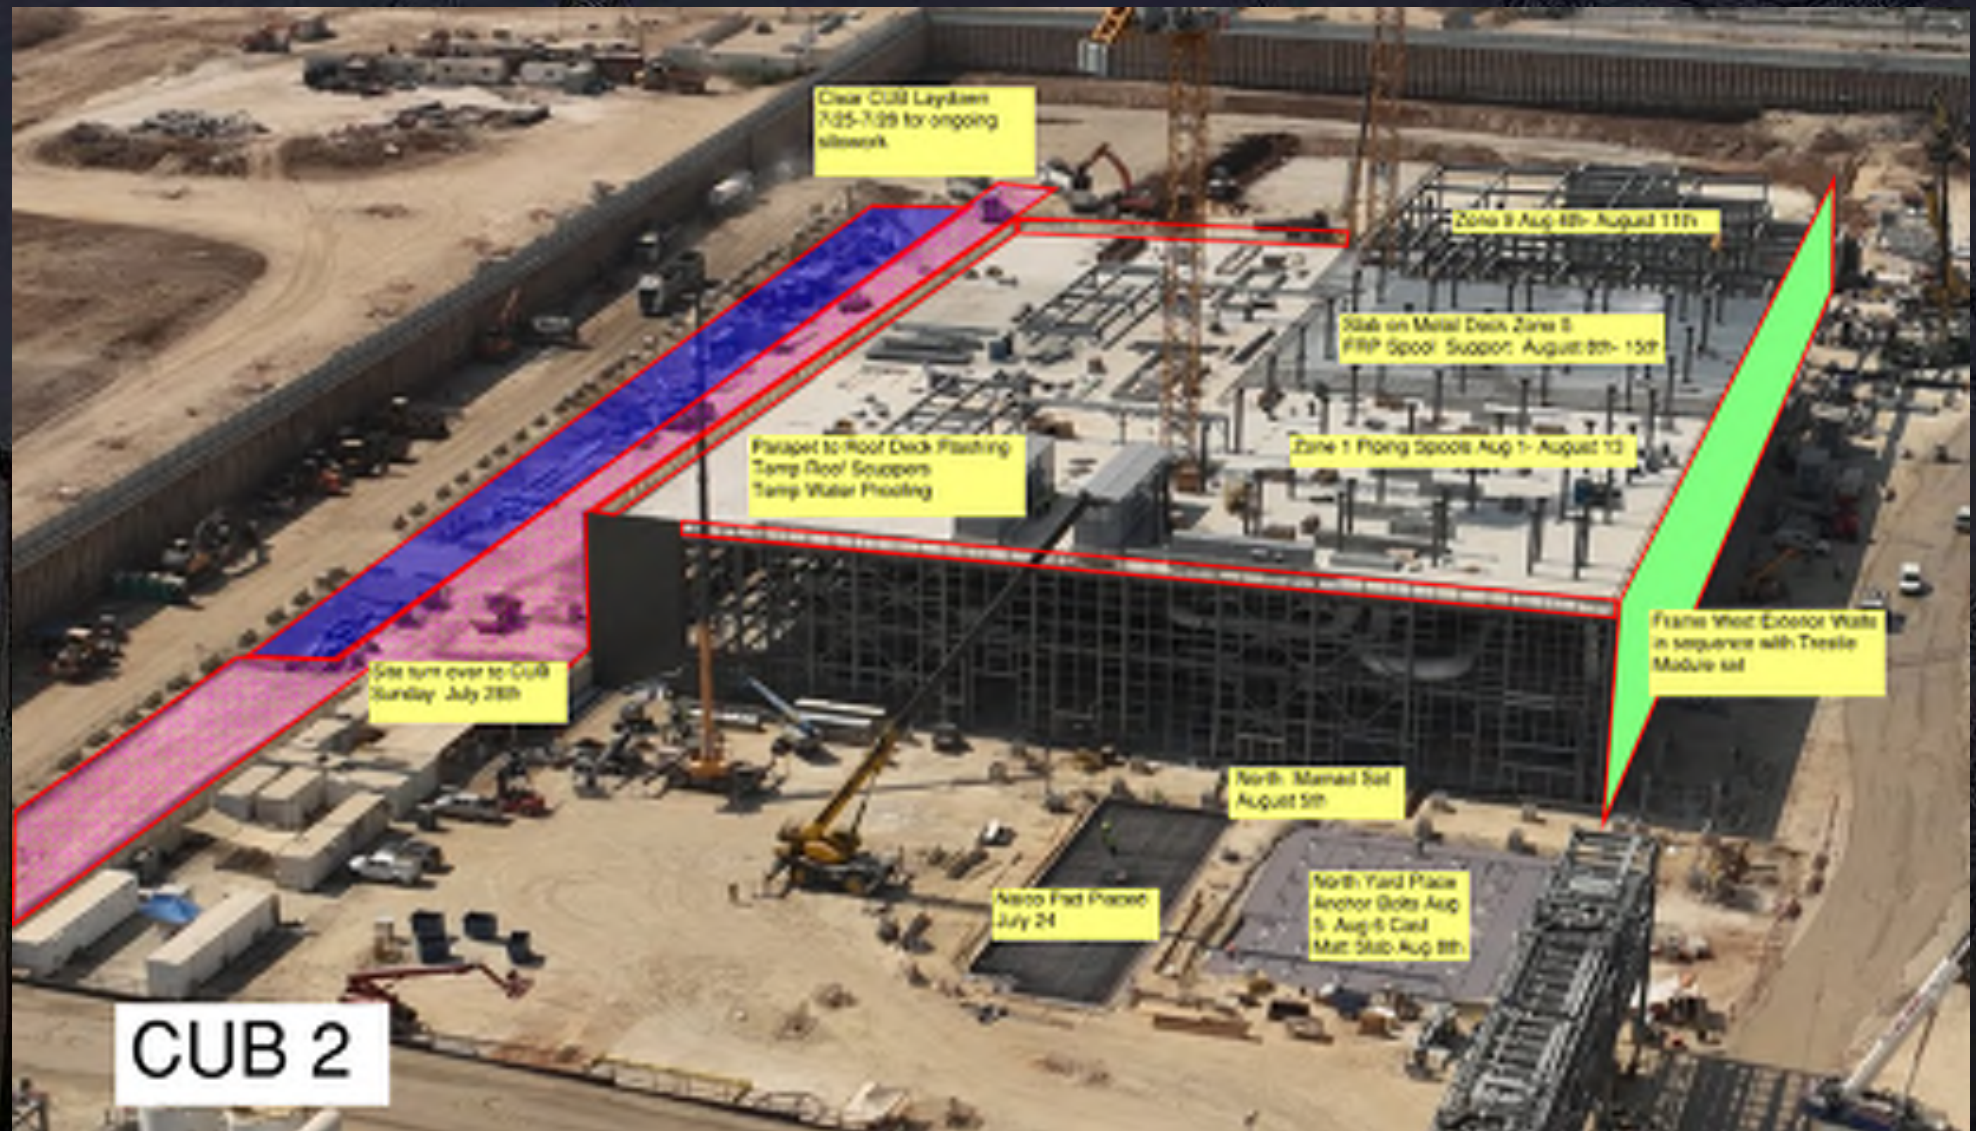

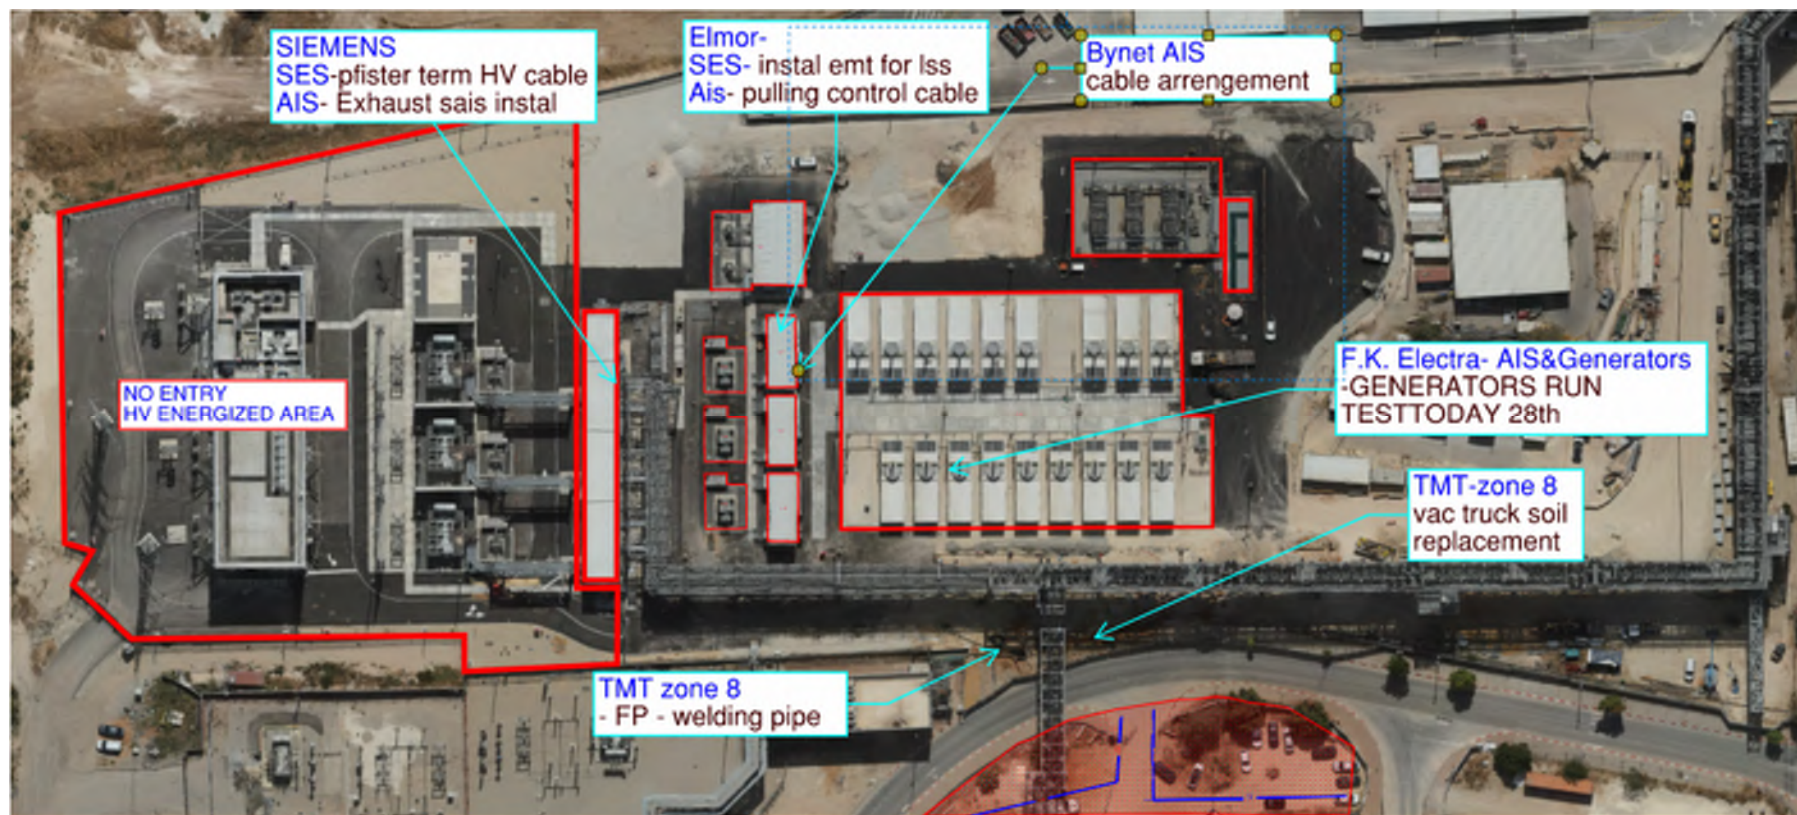





HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

T-17

Trestle - MOD 2 Steel erection

6-7 August

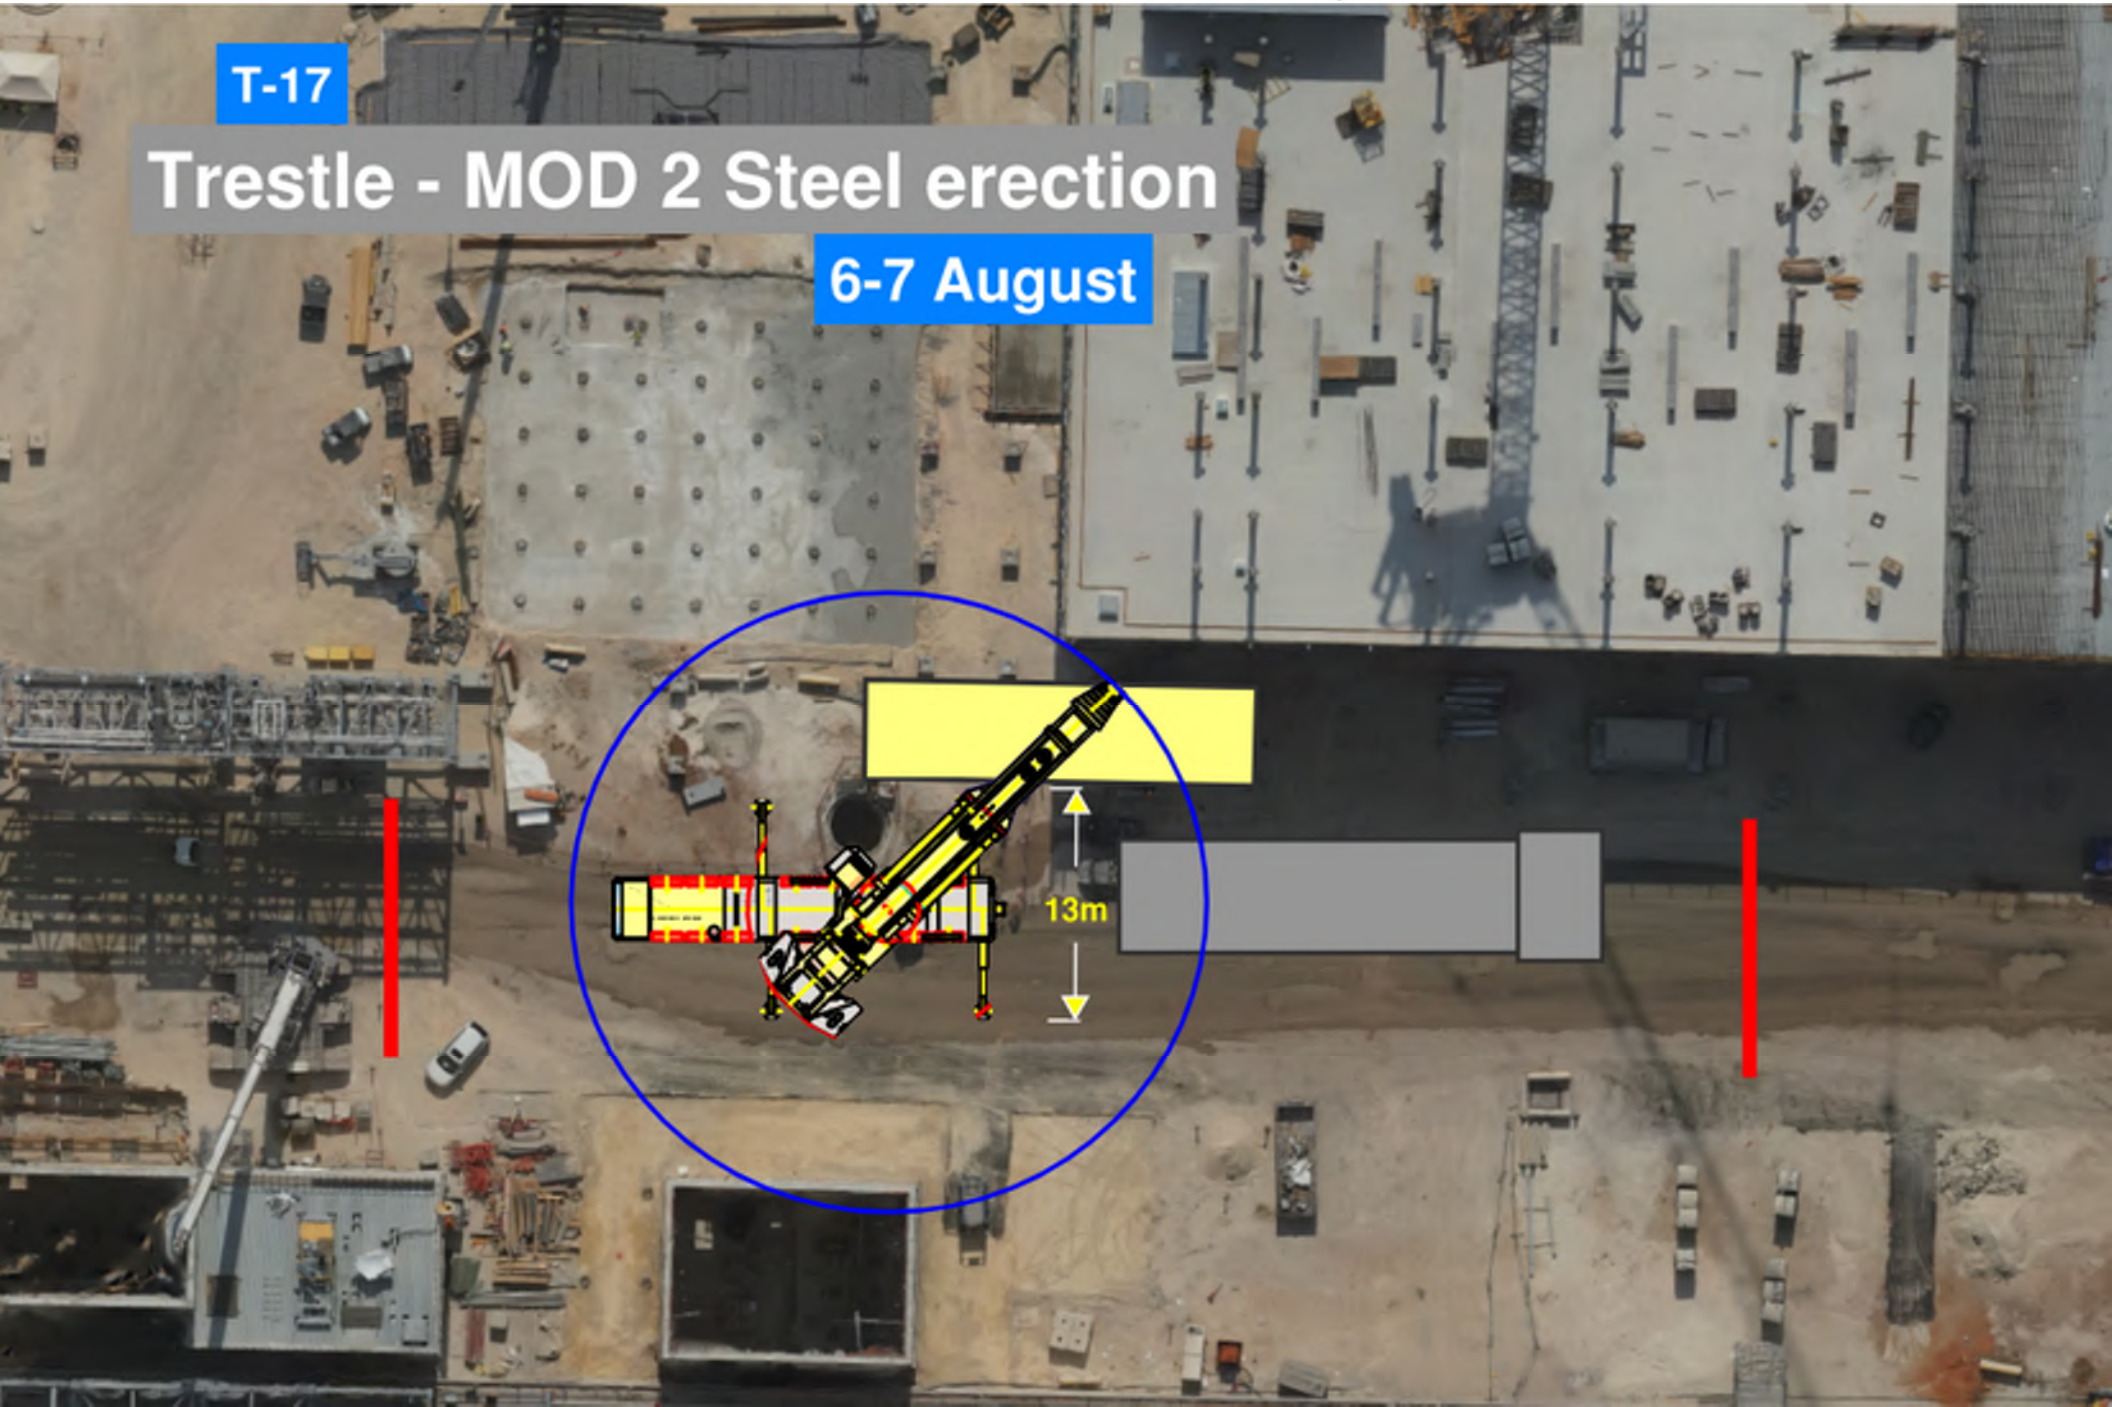




NDT radiography test at BGC vacuum tanks area

Spoter

Spoter

**Wednesday night July 28rd at
22:00 To
July 29th at 05:00 am.**

Daily Coordination Meeting

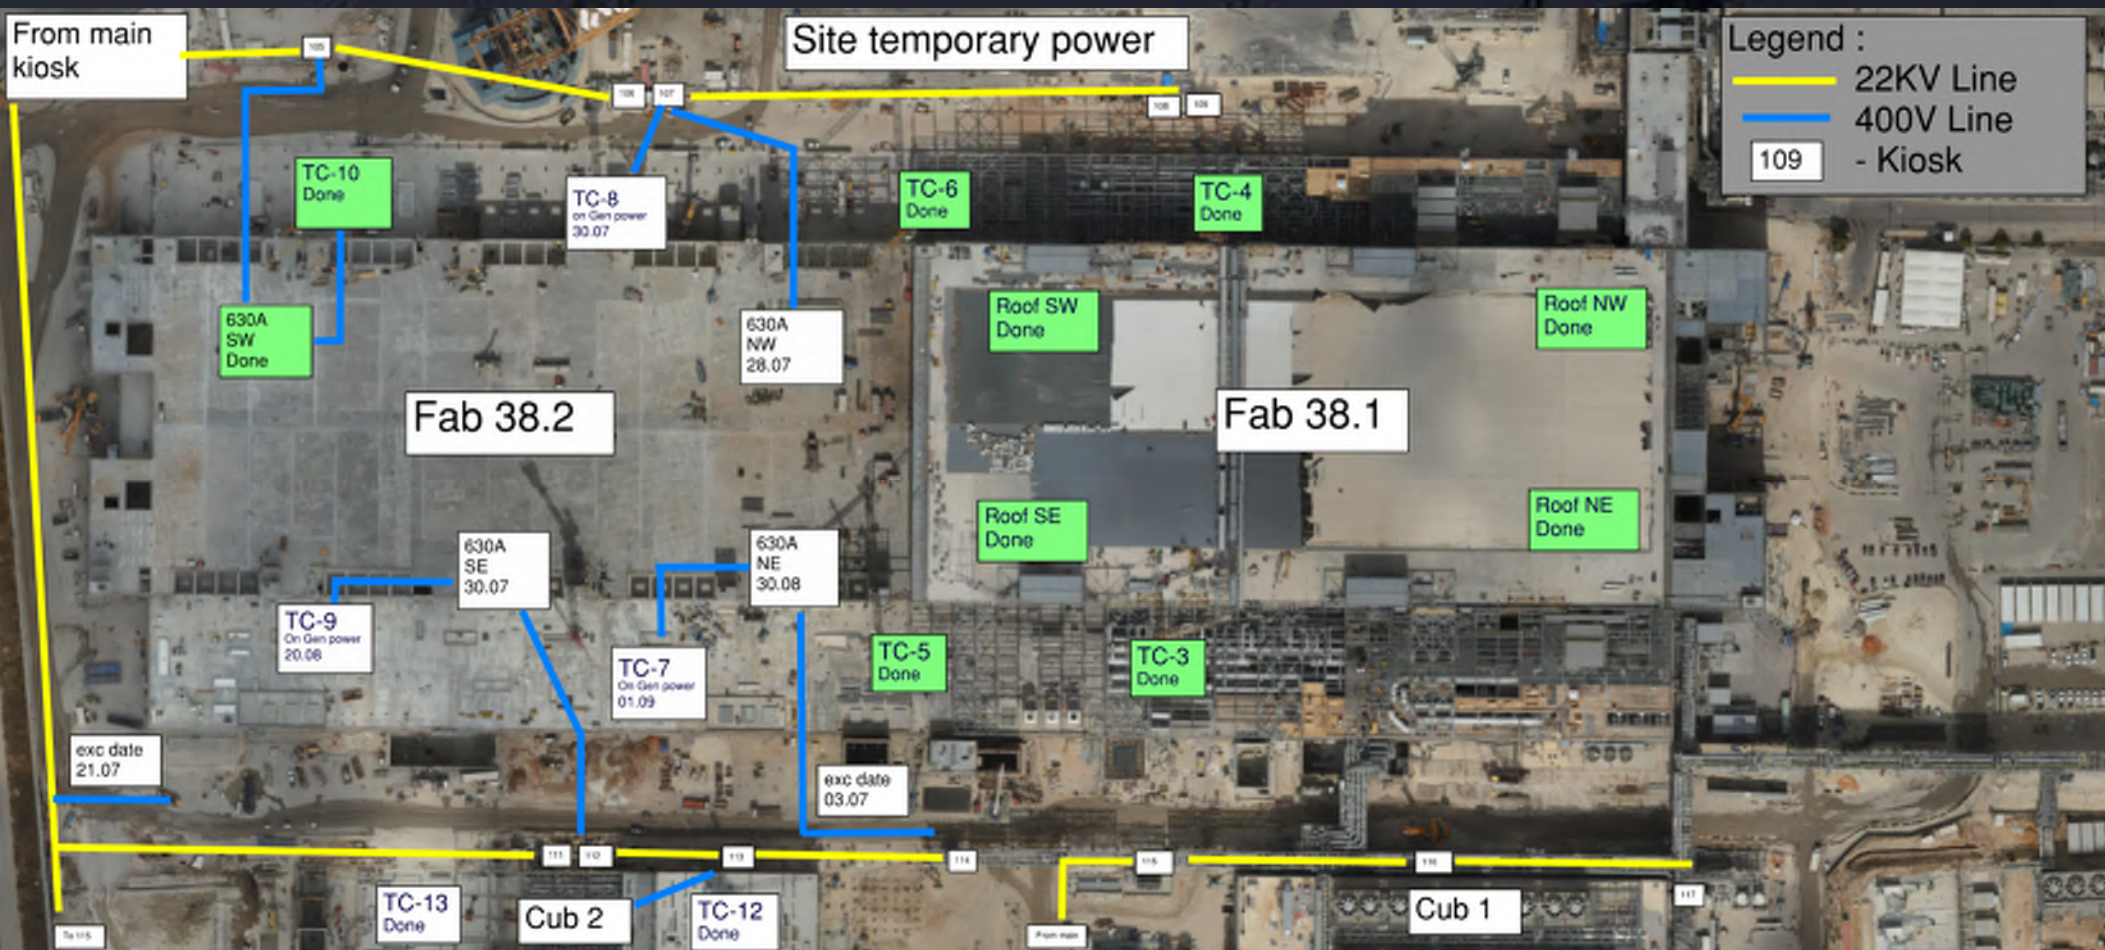



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Gate B






Daily Coordination Meeting

Site Logistics

Traffic Plan

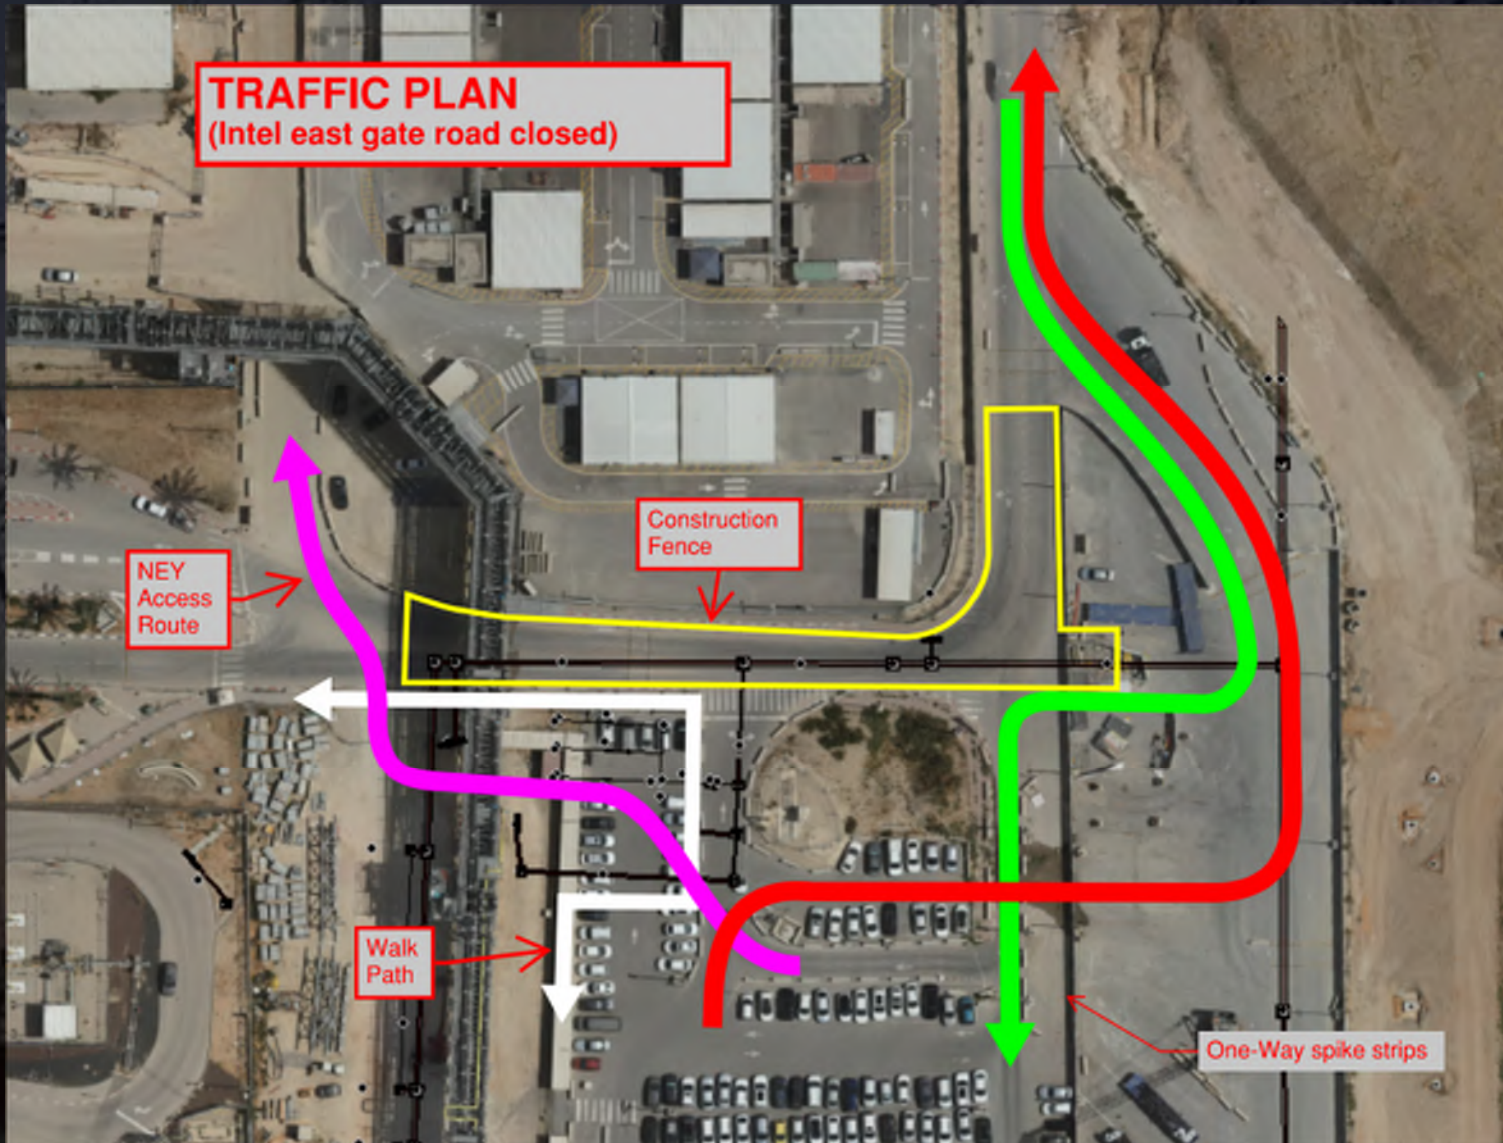




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North

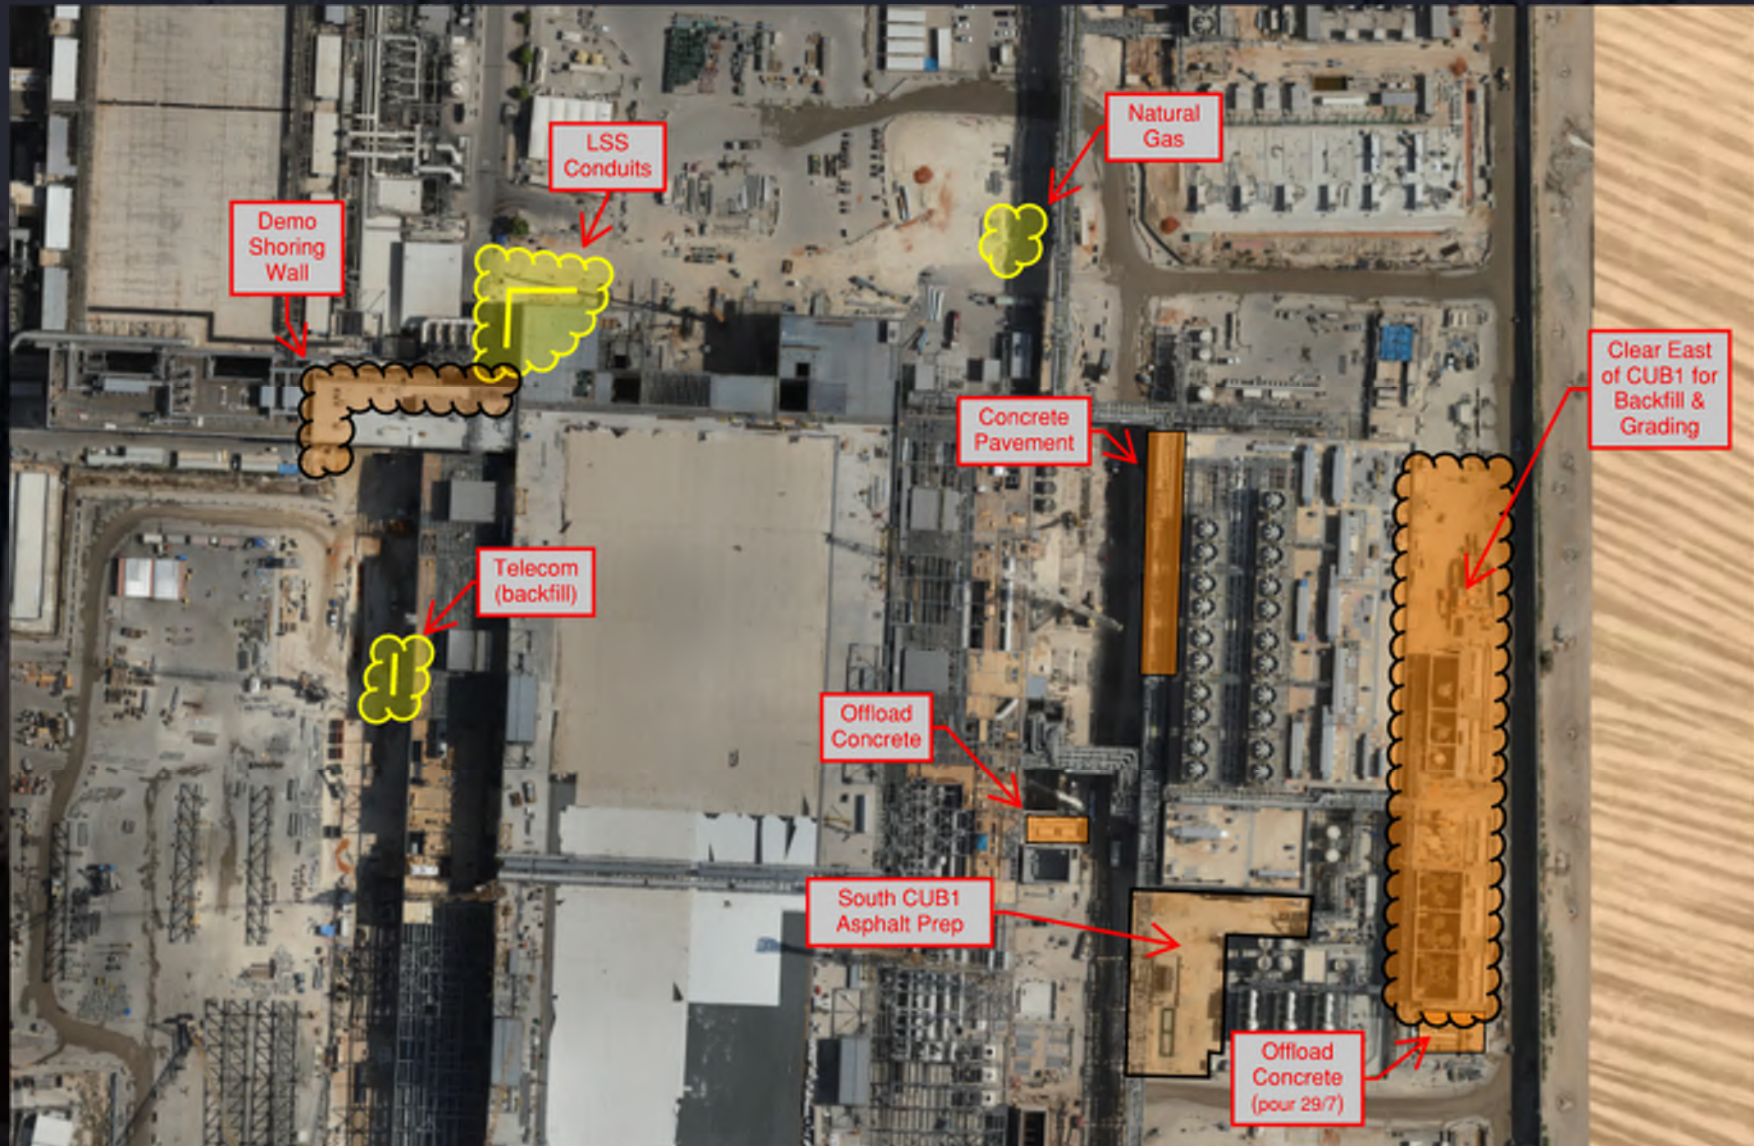



Daily Coordination Meeting

Site Logistics

South





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

SW Parking

Sanitary





Daily Coordination Meeting

Site Logistics


SW Parking



Daily Coordination Meeting

WATER BOTTLE FILLING & PERSONNEL COOLING STATIONS

BF (1) AT GIS

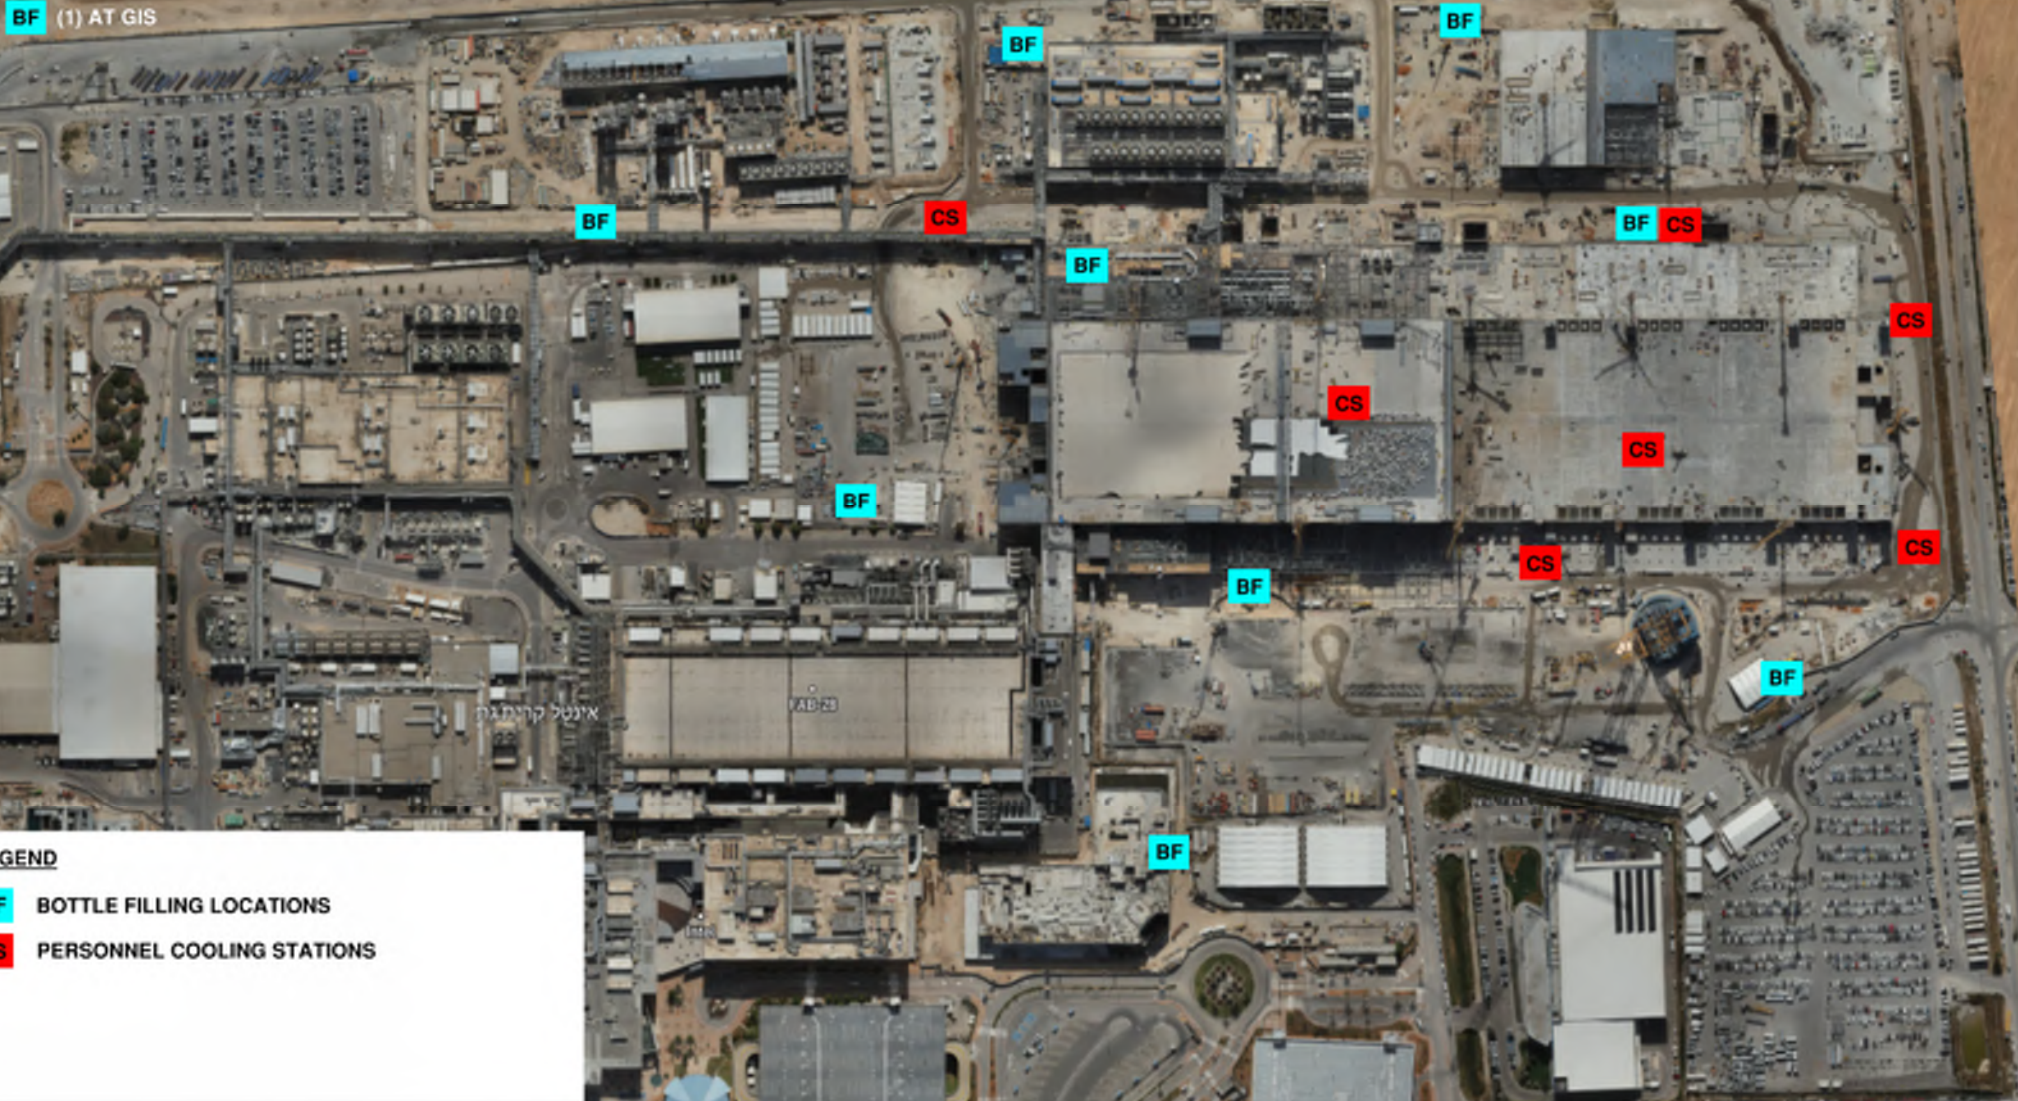

LEGEND


- BF** BOTTLE FILLING LOCATIONS
- CS** PERSONNEL COOLING STATIONS



Open CORs by Subcontractor

WW 29 – 479 CORs

WW 31 – 436 CORs

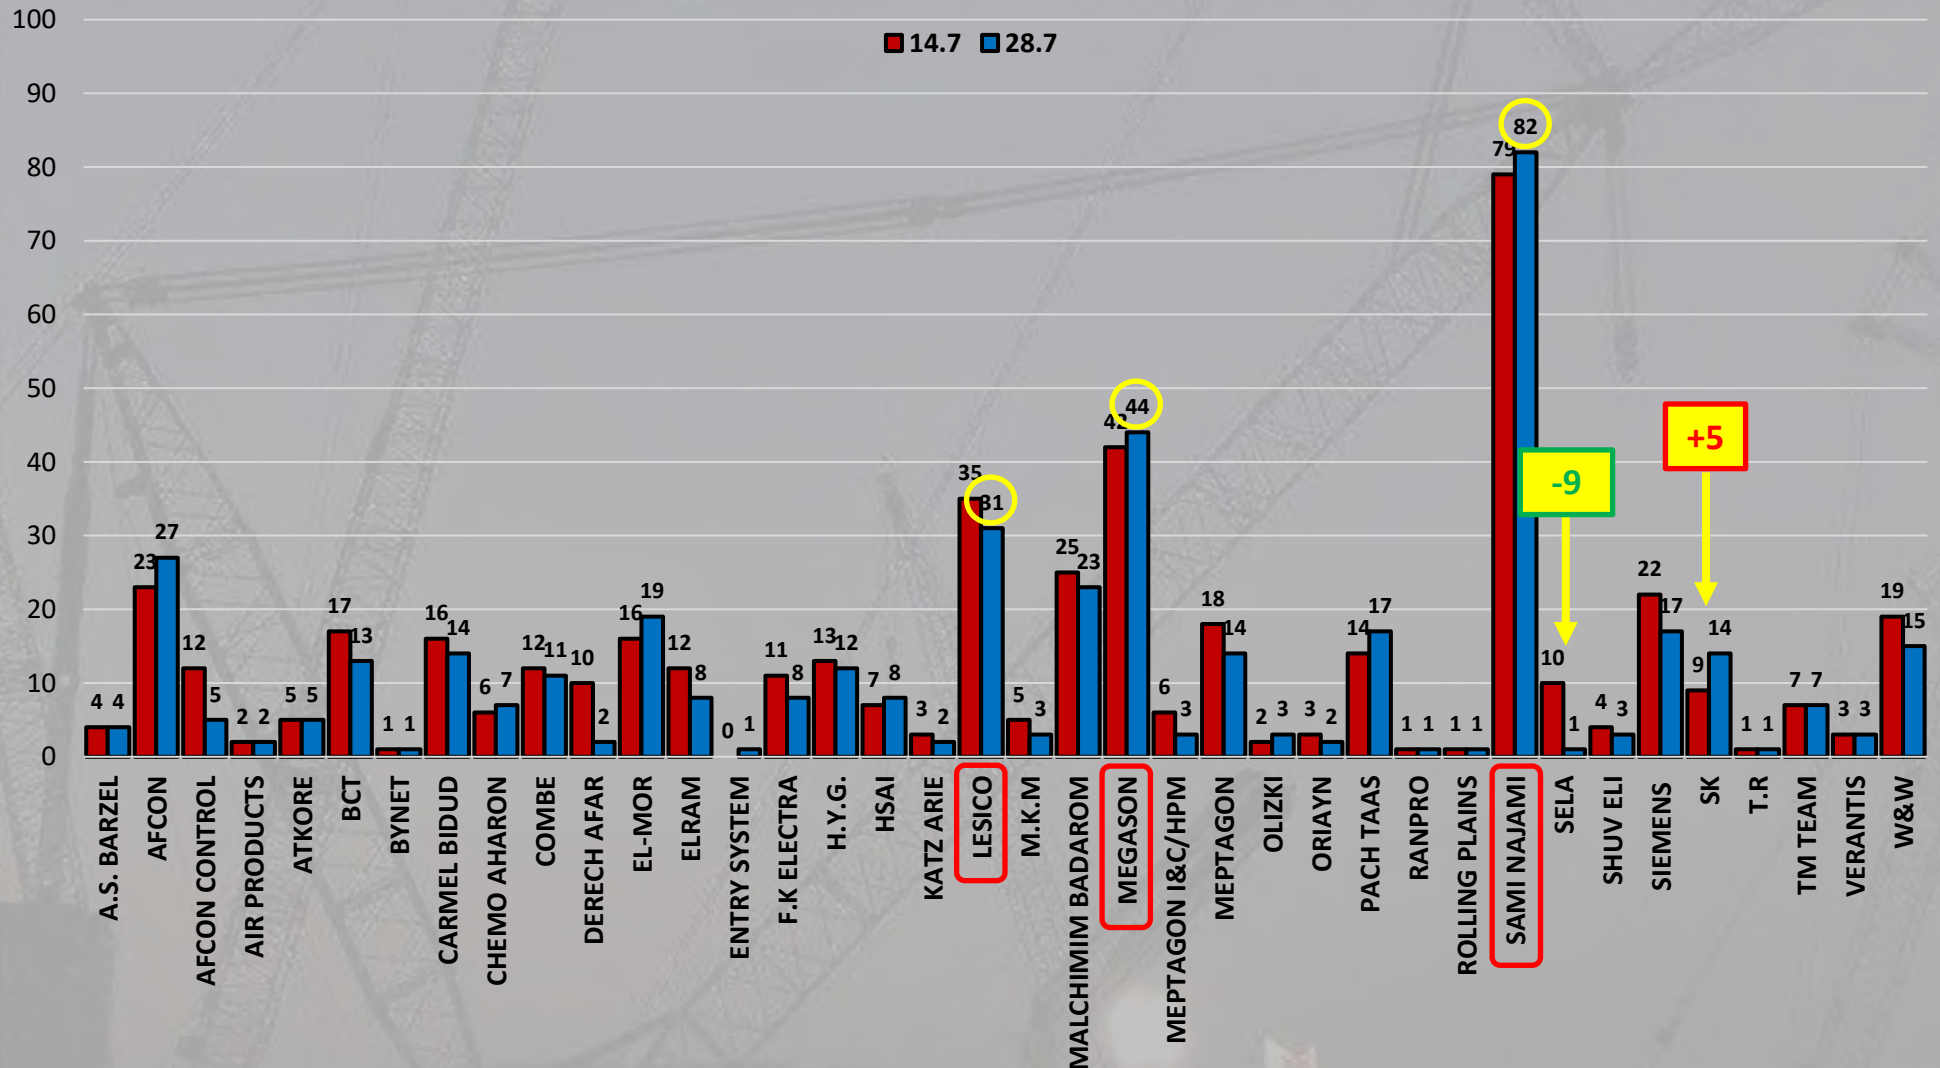




Overdue CORs by Subcontractor

WW 29 – 120 Overdue CORs

WW 31 – 132 Overdue CORs

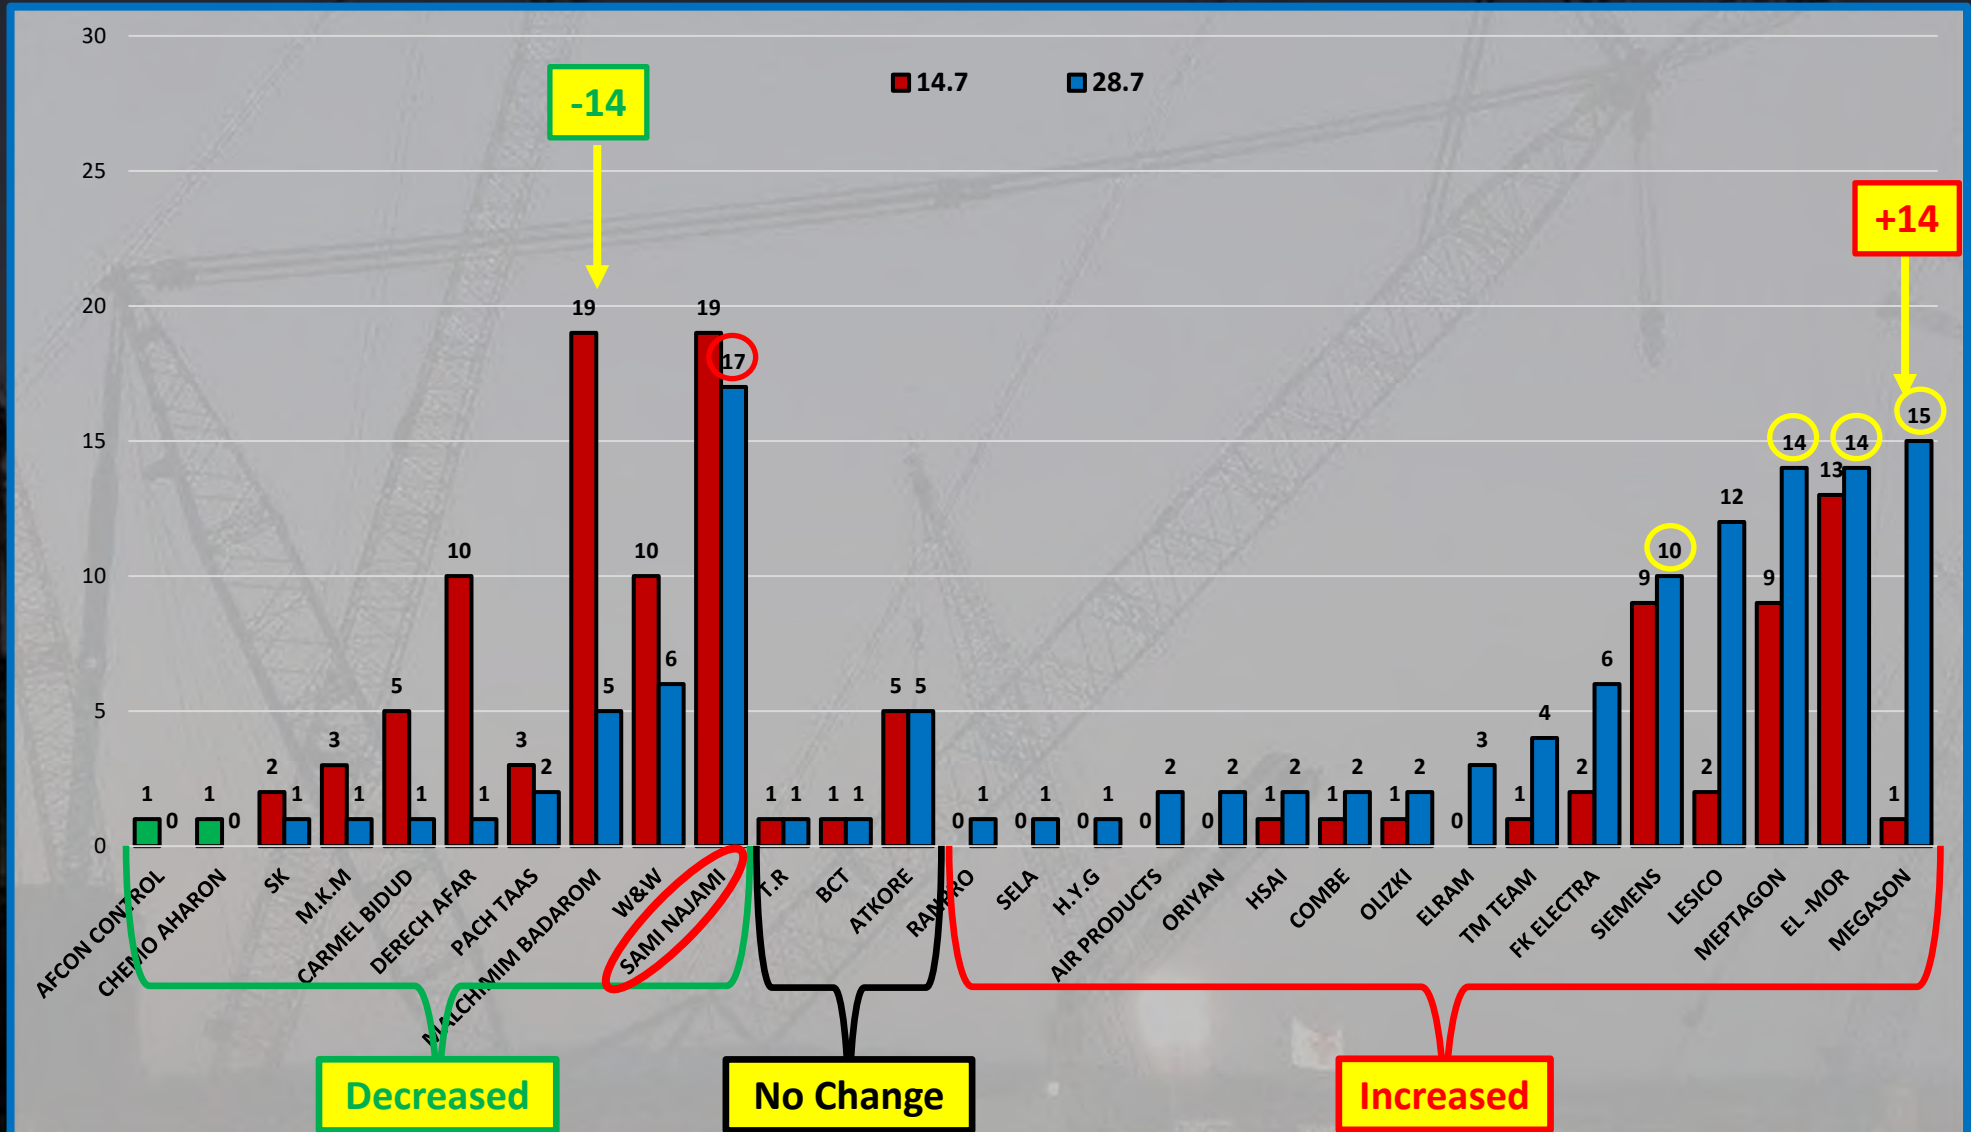

Mass Safety Meeting and Stretch and Flex

- Attendance to the MSM is required for all personnel working on the project.
- Today, we had hundreds of people hiding in their vehicles in the parking lot. This is not acceptable behavior, and we need your help communicating and helping ensure your workers are on time and present at the meeting.
- This is to ensure that everyone on site receives the safety information covered and helps us set the tone for the rest of the week.
- After the meeting, and before your workers begin their workday EVERY day, stretch and flex is required.
- Stretch and flex helps us wake up our minds and get our bodies ready for the work that we are doing each day.

Heat Index- July 28th

	temperature (°F)															
	80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
55	81	84	86	89	93	97	101	106	112	117	124	130	137			
60	82	84	88	91	95	100	105	110	116	123	129	137				
65	82	85	89	93	98	103	108	114	121	128	136					
70	83	86	90	95	100	105	112	119	126	134						
75	84	88	92	97	103	109	116	124	132							
80	84	89	94	100	106	113	121	129								
85	85	90	96	102	110	117	126	135								
90	86	91	98	105	113	122	131									
95	86	93	100	108	117	127										
100	87	95	103	112	121	132										

Caution
 Extreme Caution
 Danger
 Extreme Danger

Extreme Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



HCC/EHS Weekend Work- 26.07.2024

White Board Meeting in Beavers at 06:30

Superintendents

- Ethan Wolery 052-6041765
- Gilad Haziza 052-5984370

CSA CM

- Idan Dahan 052-5949702
- Nikol Loboda 052-3124965
- Andy Jollands 052-9659290

MEP

- Michael Ohehir 052-4168879
- Leslie Kelly 052-6391546
- Hillel Mashiah 052-6175084
- David Young 052-2241683

QA/Cx

Cranes

- Hadar Shem Tov 054-6693626

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978
- Safety Assistant- Husam Natasheh- 053-2478114
- Safety Professional – Anan Ragbe-058-7708886

Subcontractor Weekend Work- 26.07.2024

FAB

Utility Level

- Carmel raks
Foreman; Lucy 0506552488
Ehs; Michel 0542634700
- Combe upw
Foreman; Edward 0526419894
Ehs; Michael 0525506596
- Elram
Foreman: Shlomo 0545551702
Ehs: shy 0523632132
- Combe waste
Foreman: Denis 0525238504
Ehs: Michael 0525506596
- Chemo
Ehs lilach 0547886704
Forman sergey 0544659688
- Carmel duct
- Afcon electrical
- HYG

Clean Room

Subfab

- Carmel Bidud – AA scaffold removal
Ibrahim – 052-951-9833
- Afcon E – SF LSS Rooms. Avieli – 052-600-8487
- WW – Elev. Shaft 1

PSSS

- Pach Taas – Module bolting PSSS Roof and Lift 2
Foreman – Vadim – 052-6229005
Safety – Offek – 050-7838486
- W&W – SEQ 131,134,136, and 2P Scrubber Grating
Foreman – Willie – 052-6145521
Safety – Gary Lambert – 1-405-833-8910
- Katz – U8 Rack 7 Plate Install
Foreman - Polishchuk - 054-750-1845.
Safety – Ofer Ilsar - 054-675-6690
- Katz Piping – UPW Room
Foreman – Konstantin Tsib – 054-7861613
Safety – Ofer Ilsar - 054-675-6690
- Afcon Electrical – Cable Tray and Cable Pulling 1-4P UL and 1-2P Roof & Lift 2
Foreman – Charles – 055-2740190
Safety – Stevan – 055-9129333
- Combe UPW – UPW Room, UPW Yard, and Water Reactive Piping
Foreman – Eduard – 052-6419894
Safety – Michael – 052-6419894
- Chemo A. – PSSS Roof and Lift 2
Foreman – Maor – 050-955-9071
Safety – Rotem – 054-447-7112
- HSAI – BIPA & MOD2 Stripping
Foreman – Dave – 052-4121028
Safety – Sam – 052-5259268
- Carmel Bidud – 5P/U8 Rack 7 Ductwork & Roof Ductwork
Foreman – Hitim – 052-7053353
Safety – Michael – 054-2634700

Girts

Subcontractor Weekend Work- 26.07.2024

WJG

- Afcon
- W&W
- Pach Taas
- Chemo Aharon

Site

- **Derech Afar** – Sanitary lift station & sanitary underground install
Supervision = Raed: 054-2442030
EHS = Alex: 054-5403849
- **Olizki** – Sweepers and water trucks, truck offloads, concrete flatwork (PCC) & excavation
Supervision = Yossi: 052-2180485
EHS = Ben: 052-4033565

Trestle

- SN- Piping

CUB

- H.s.a.i
- Chemo
- Saminajami cub 2

GIS/NEY

TMT: •

Zone 8 Welding of fire fighting piping with the help of a crane

Zone 7+8+warehouse general cleaning and hot work in favor of a concrete floor 1*1

Manager - Ido Deus 050-866262
