

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Trestle Testing Impacting Friday PMB Parking
- Weekend Work




East area way Pour 1
4:00 am

Int'l Airport Gat

FAR-26

Int'l

UTILITY LEVEL MOD1

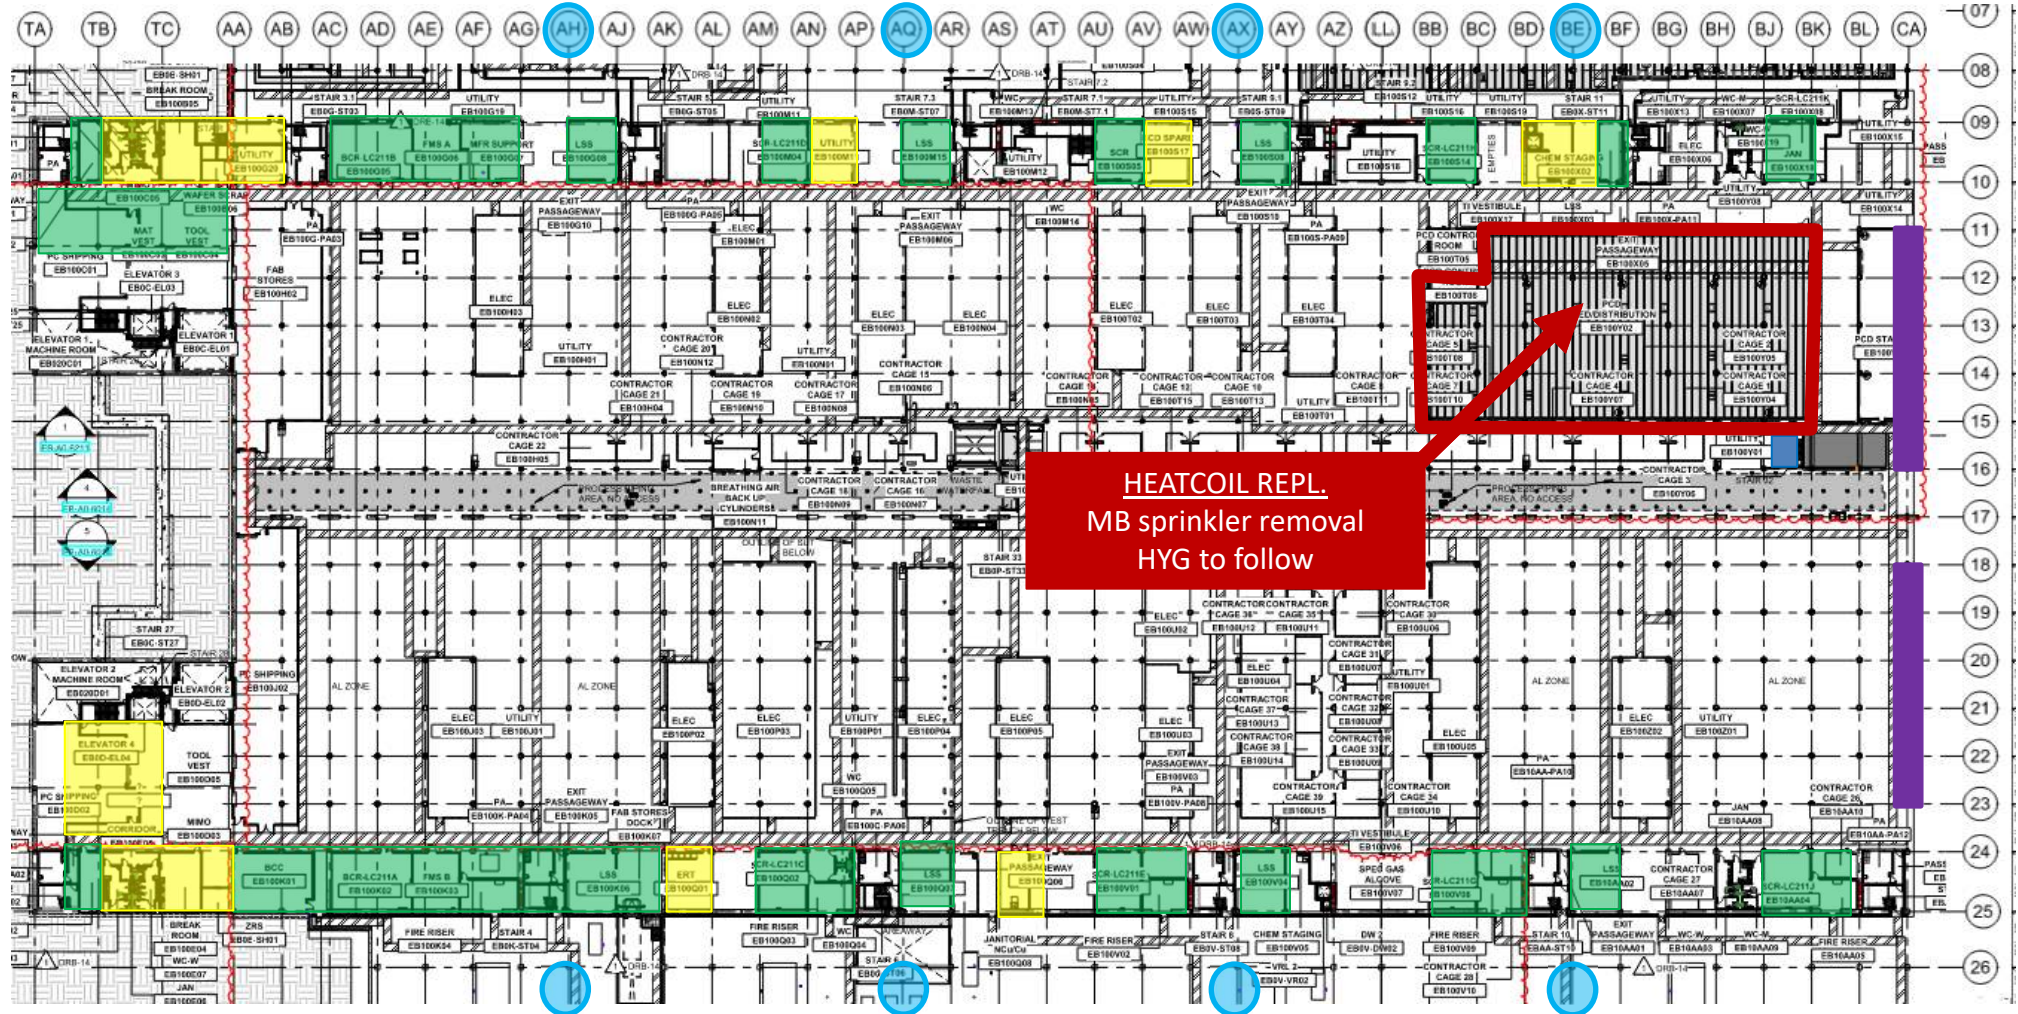


ELRAM
Drywall install


MEP+Electrical
Ready for re-install



UTILITY LEVEL MOD2

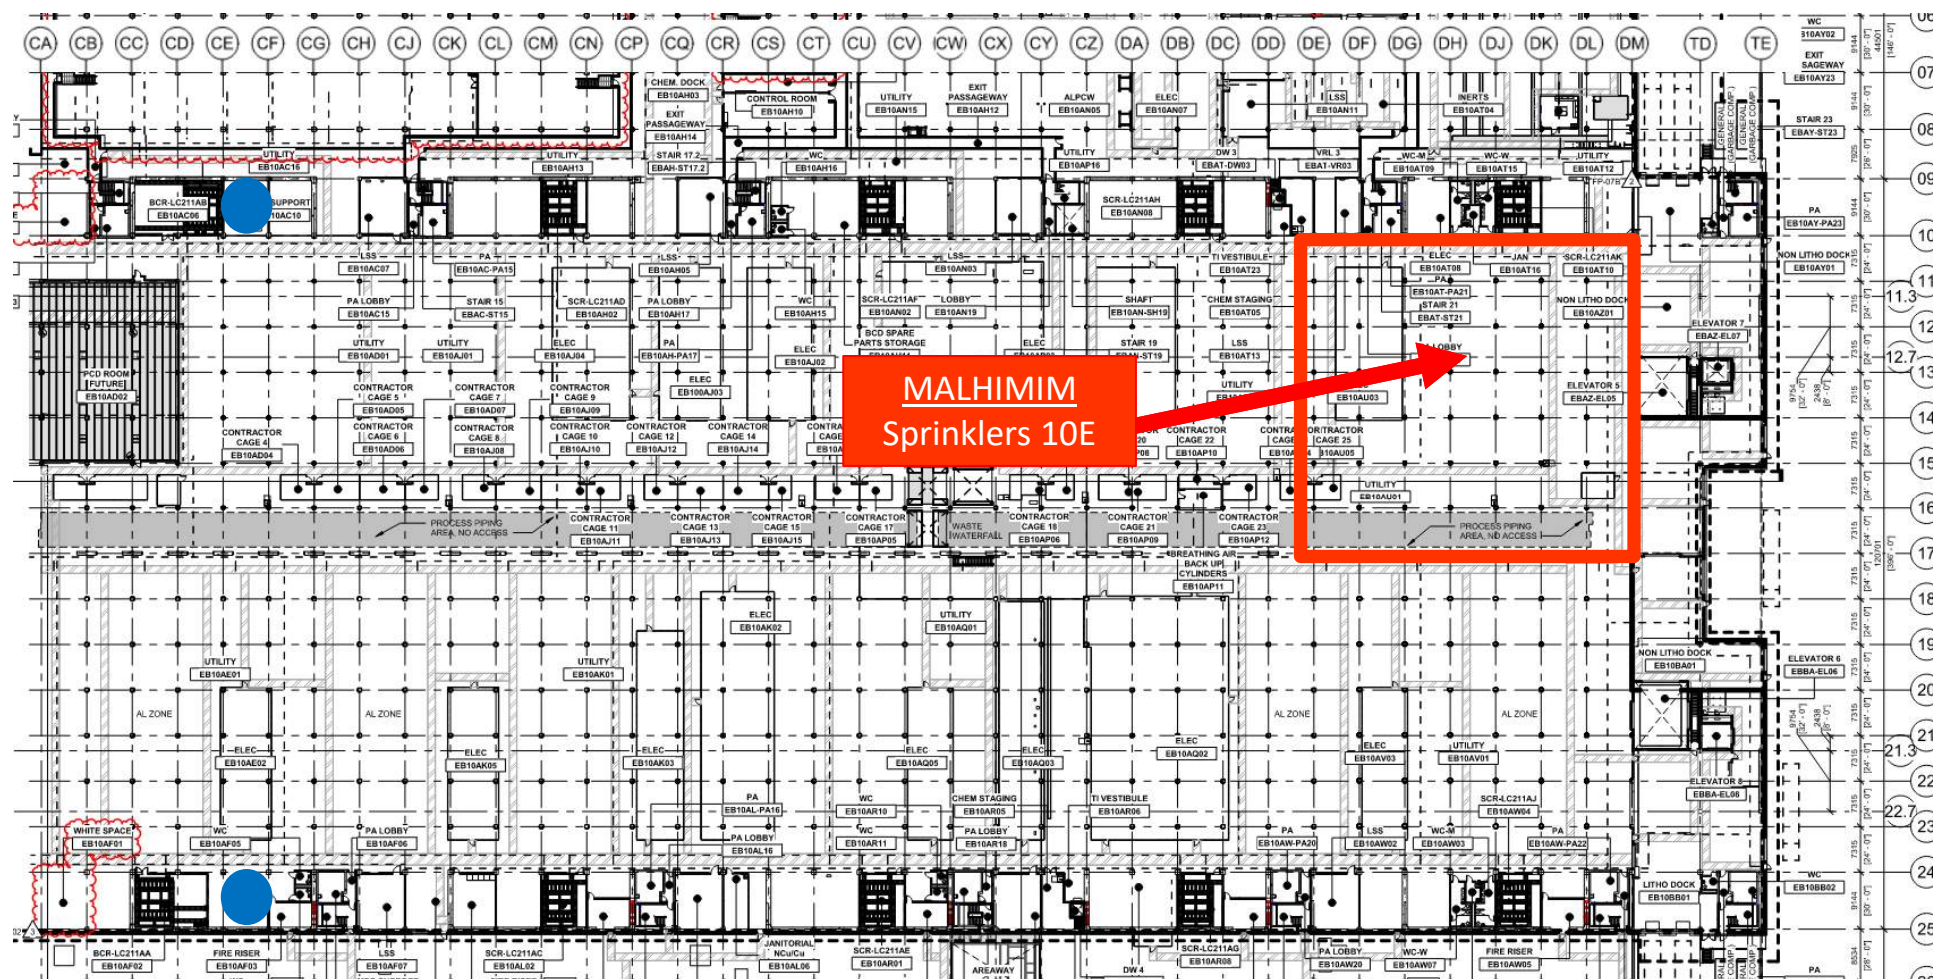


SUT 38.1 Accesses& Egress

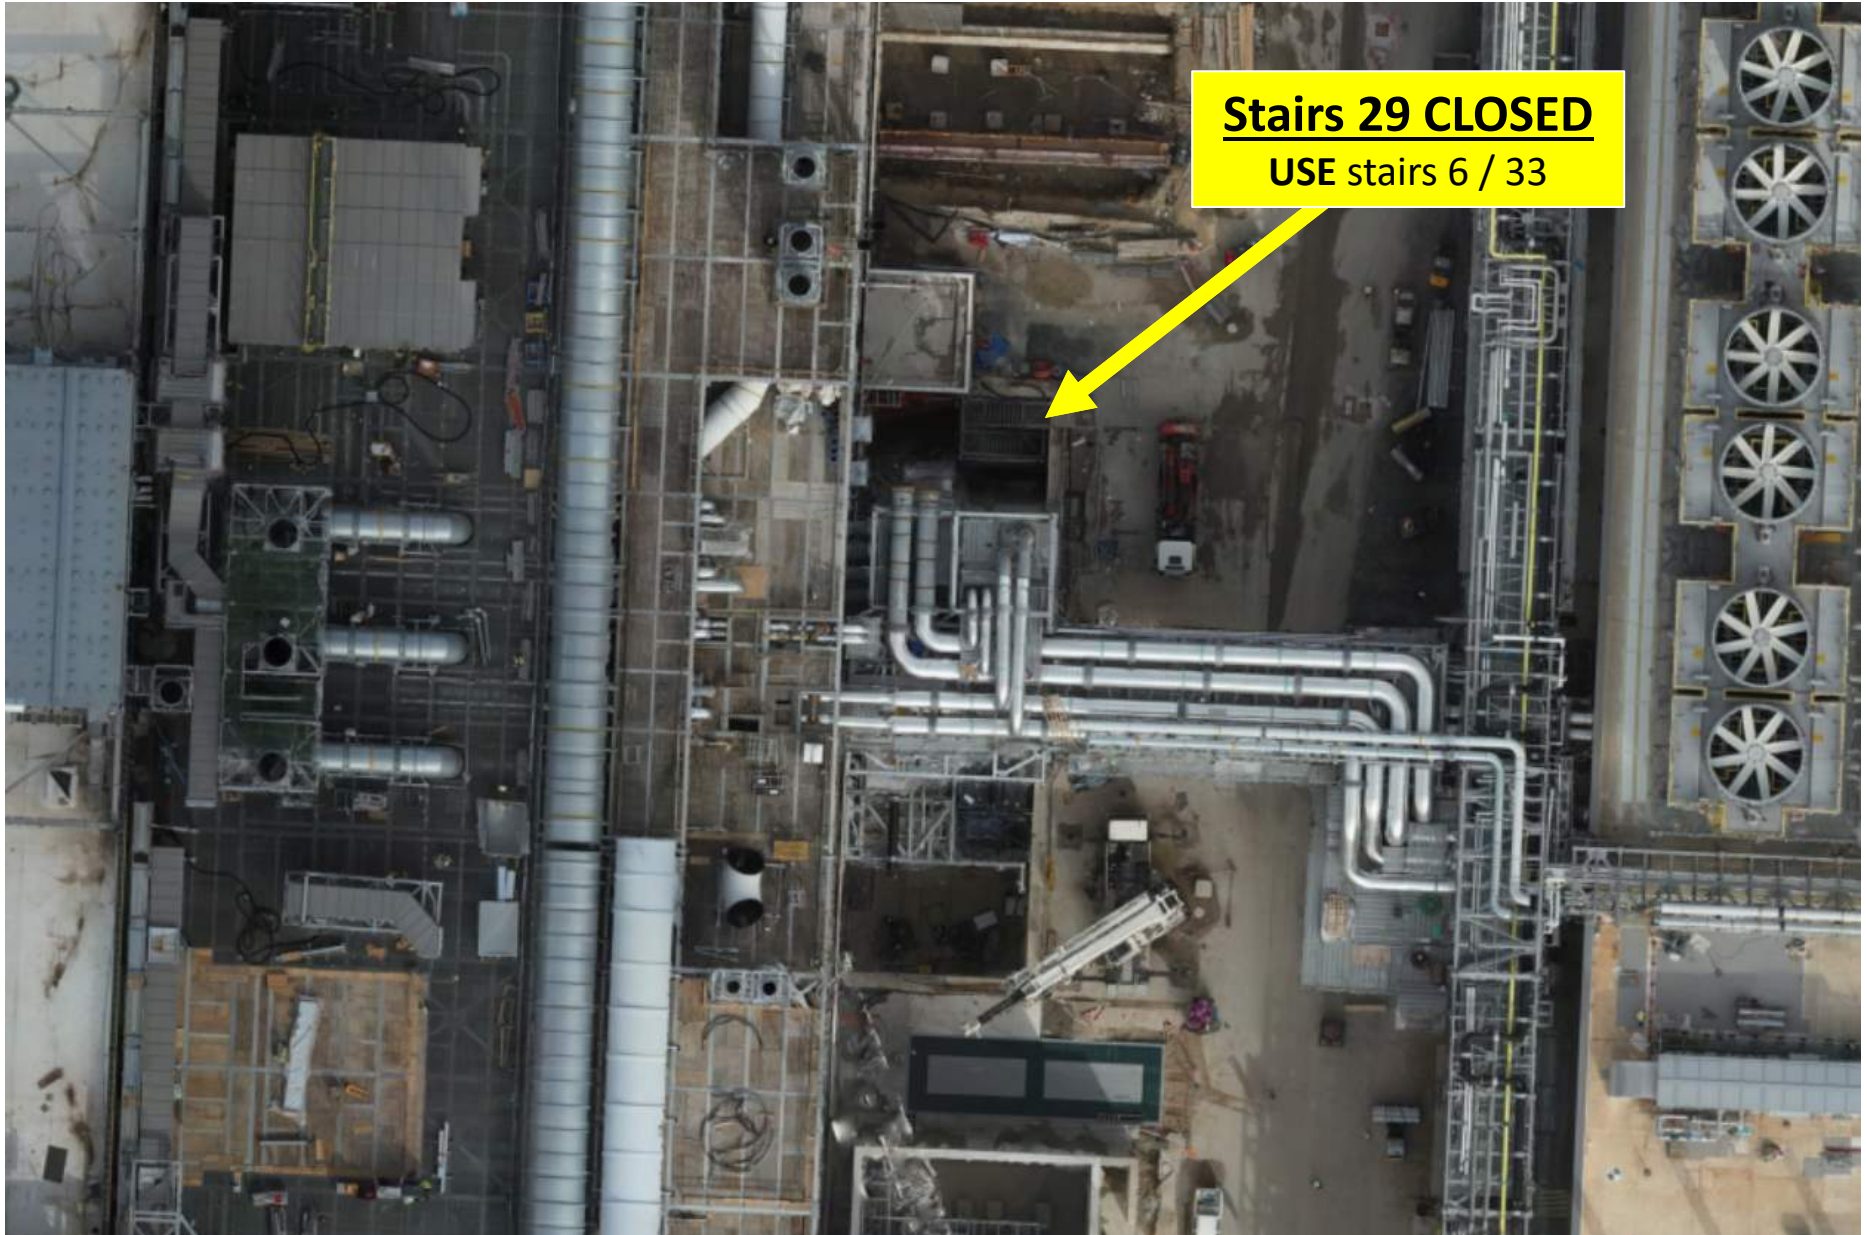

SUT 38.1 LEVEL

Stairs 29 CLOSED

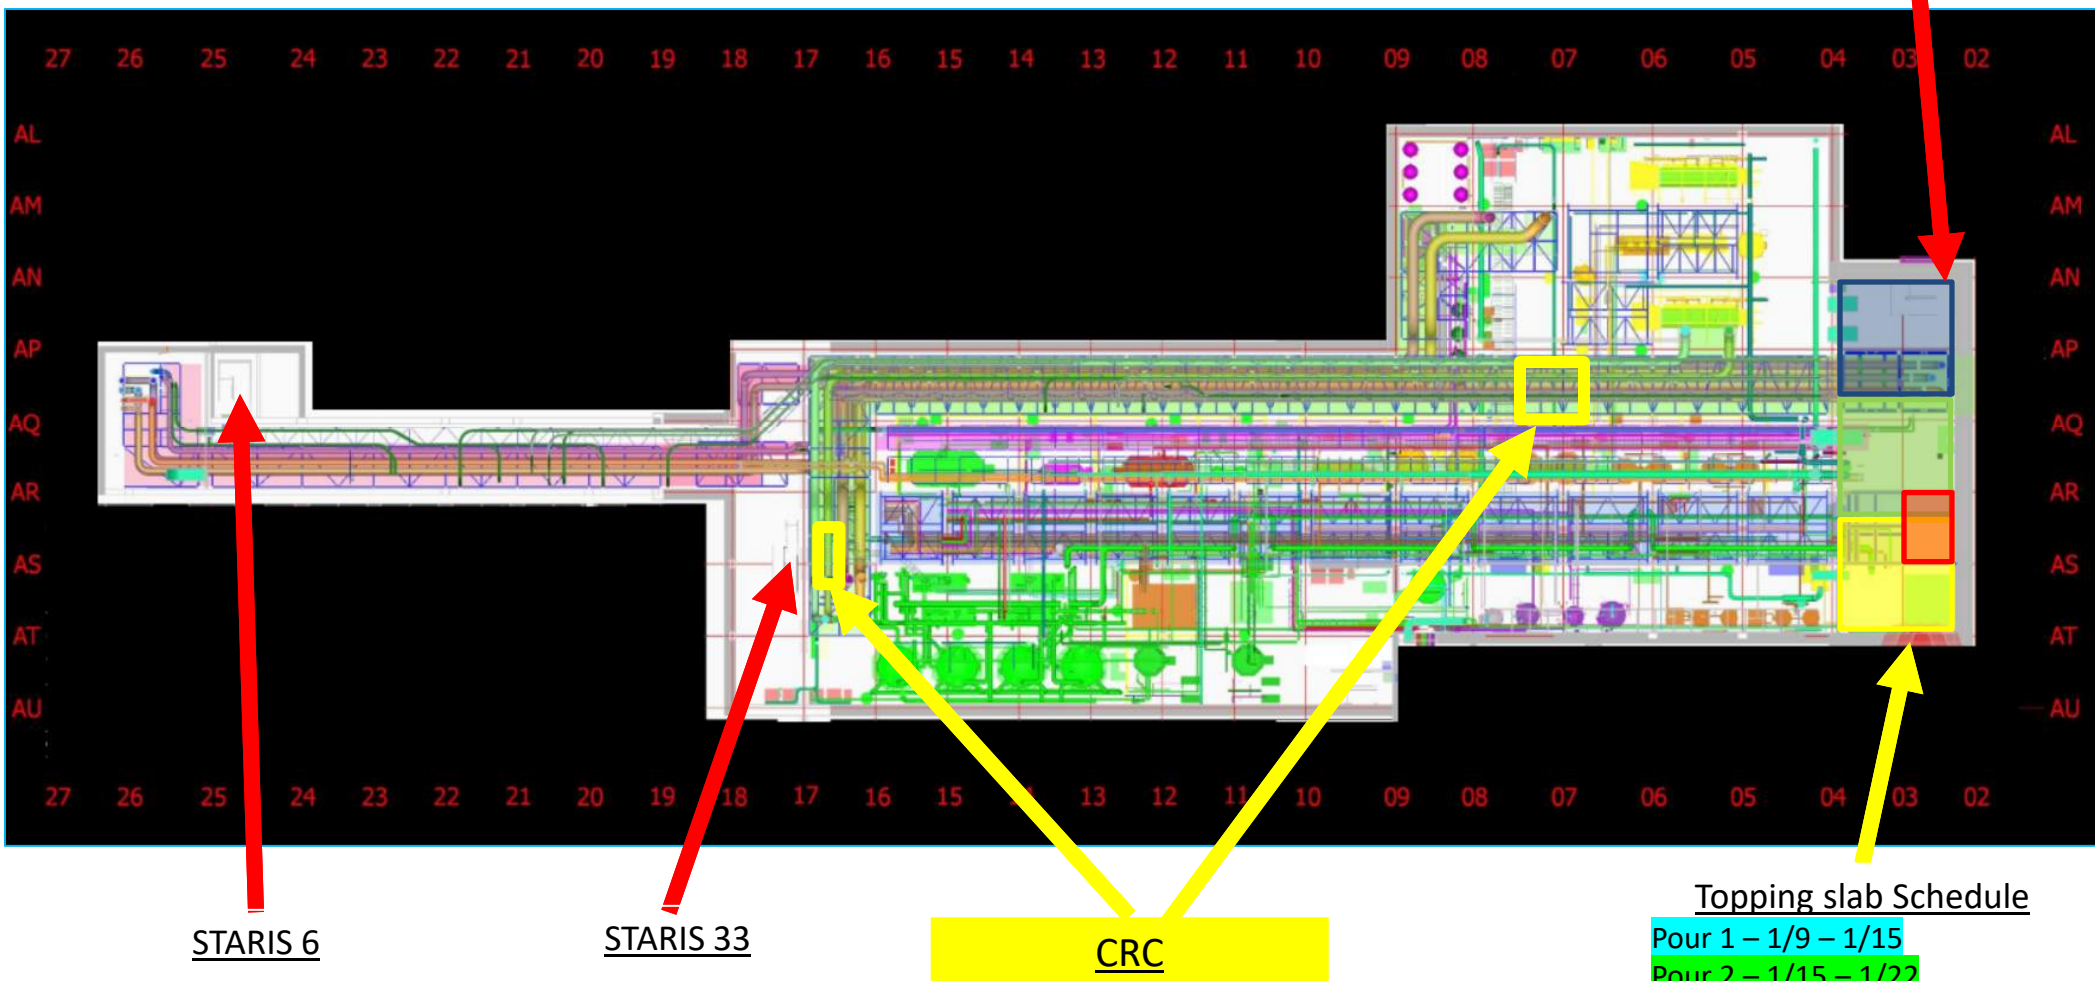





HOFFMAN CONSTRUCTION COMPANY




SUT 38.2 LEVEL

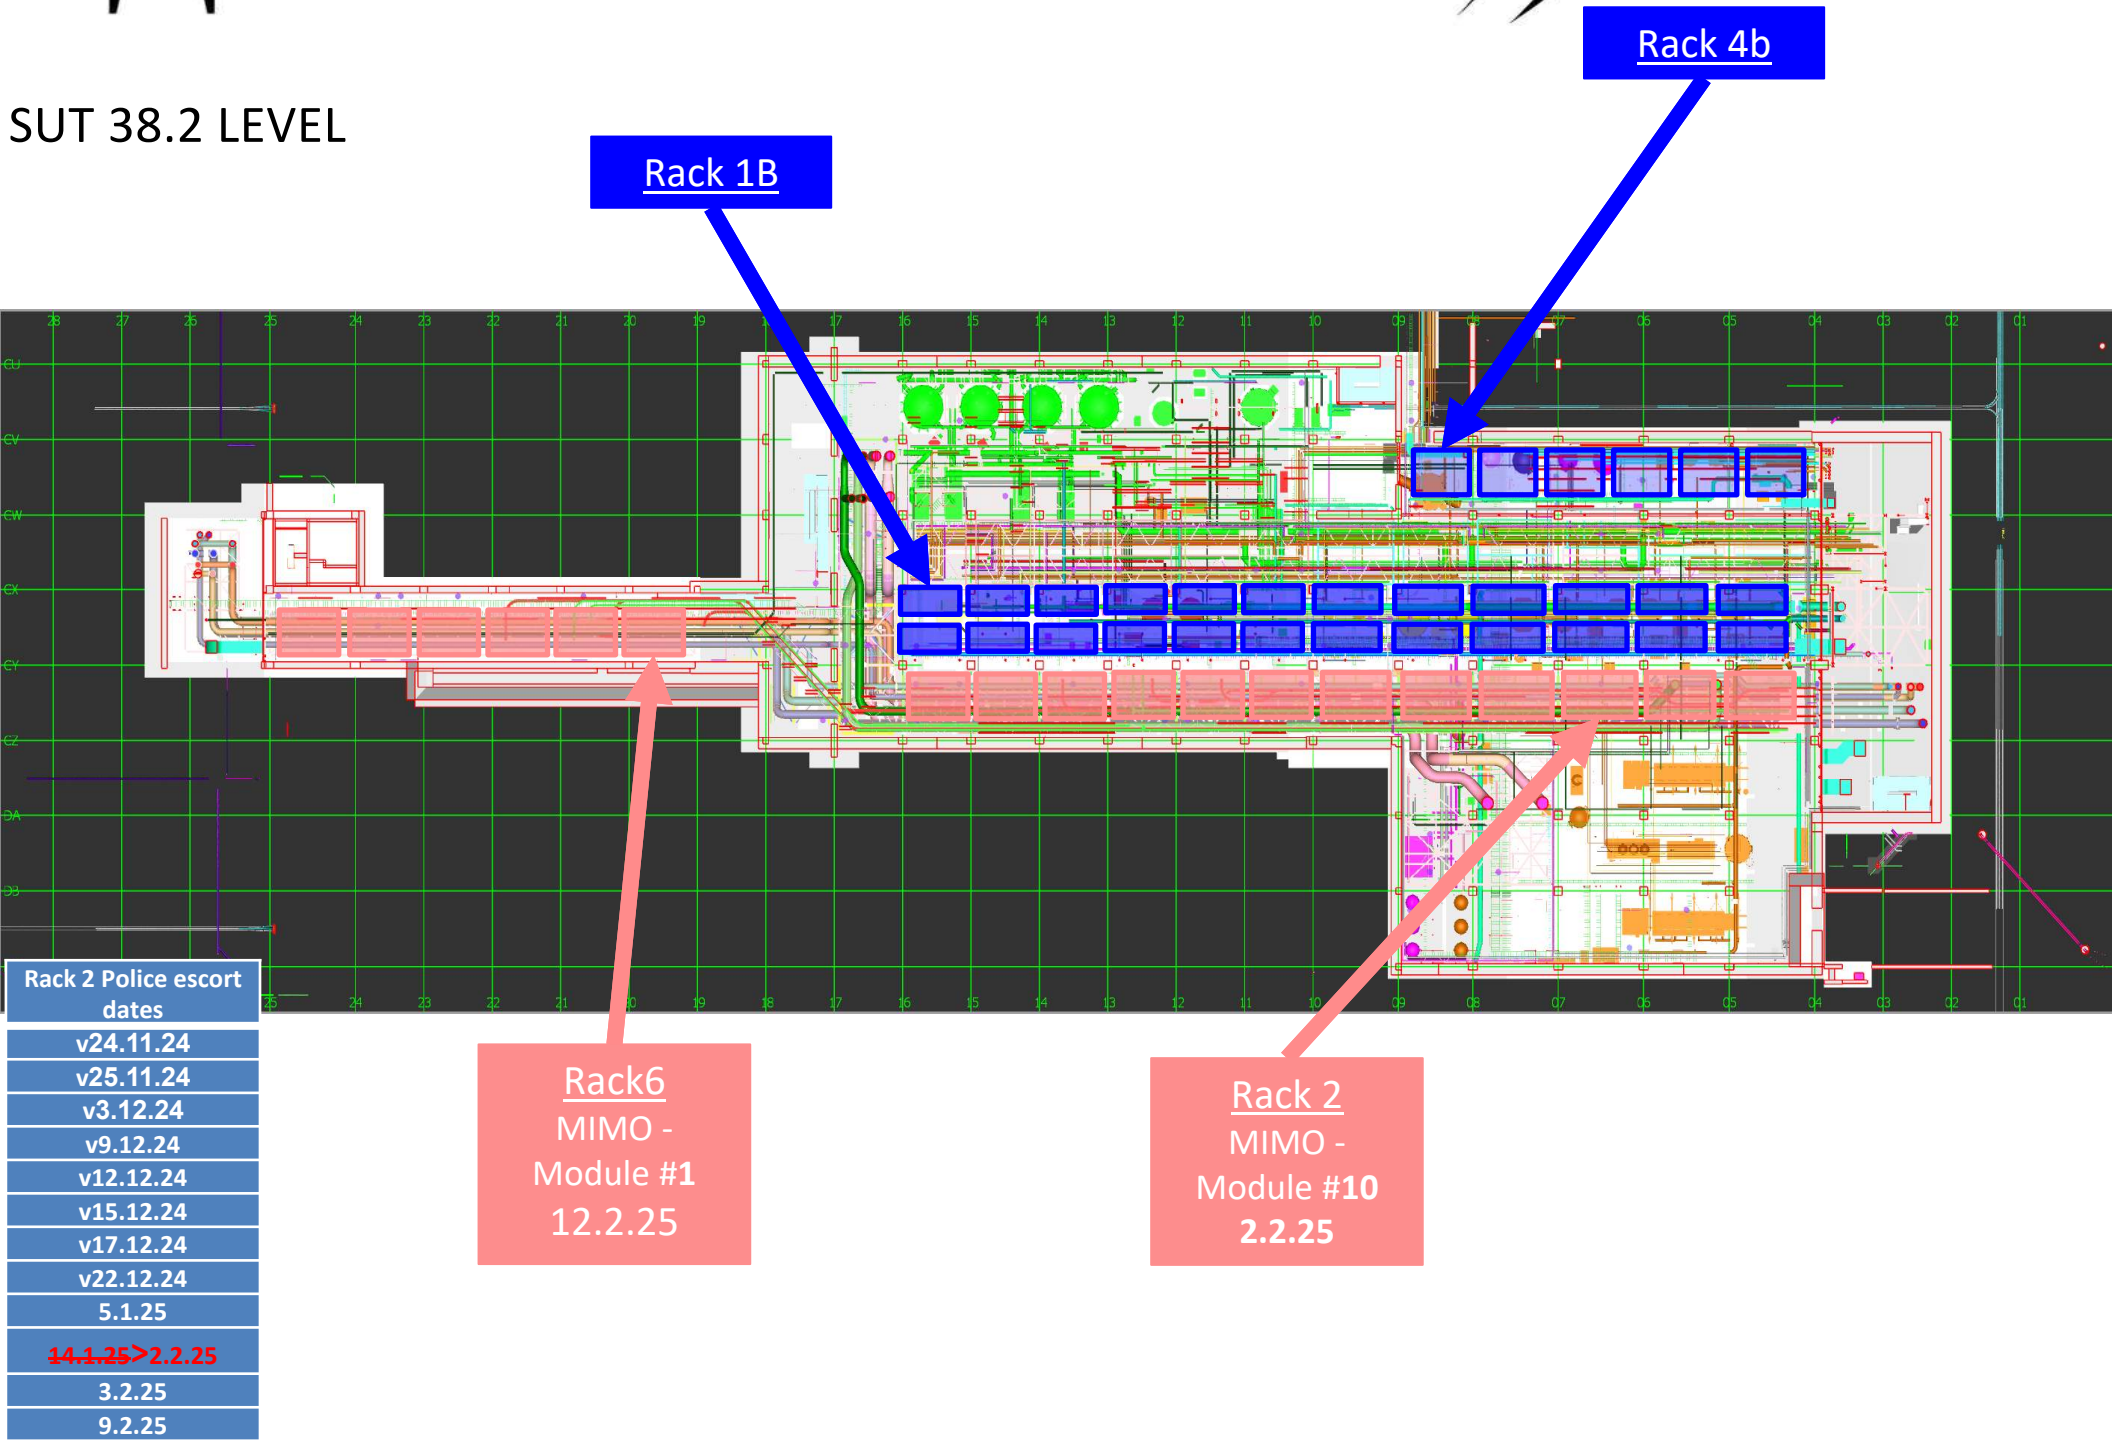


SUBFAB BUILDOUT MOD 1

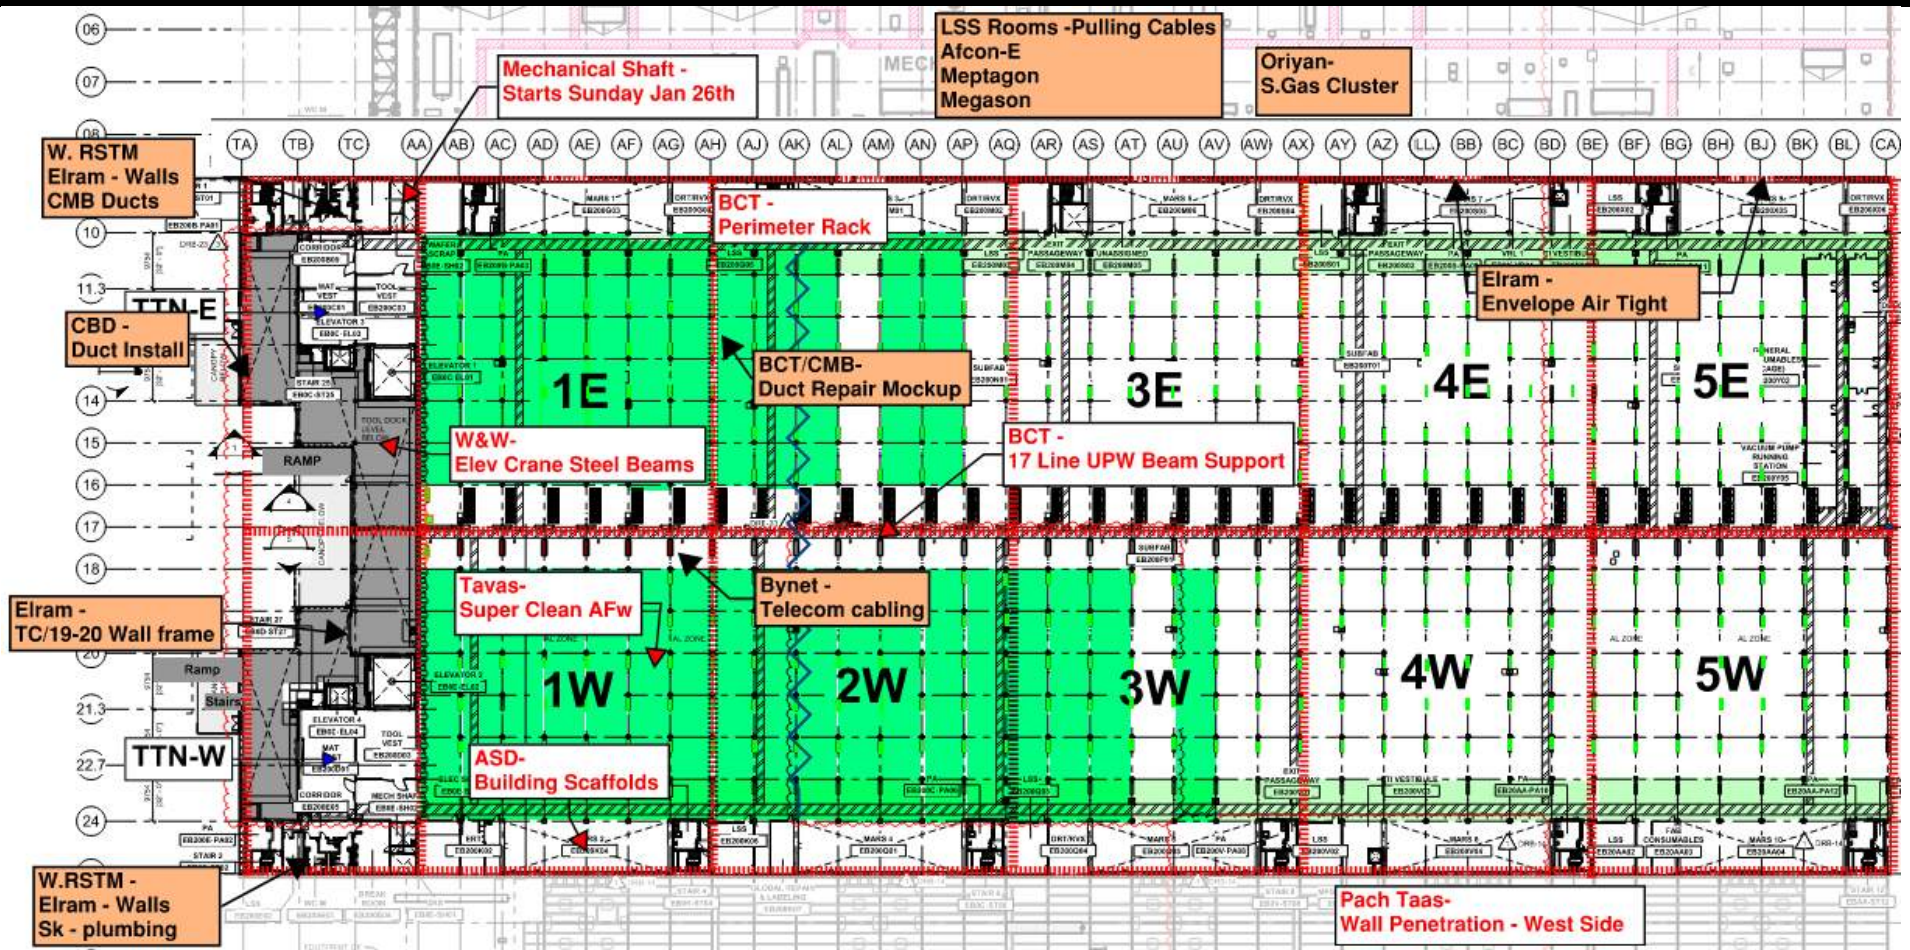


SUBFAB CRC TOPCOAT

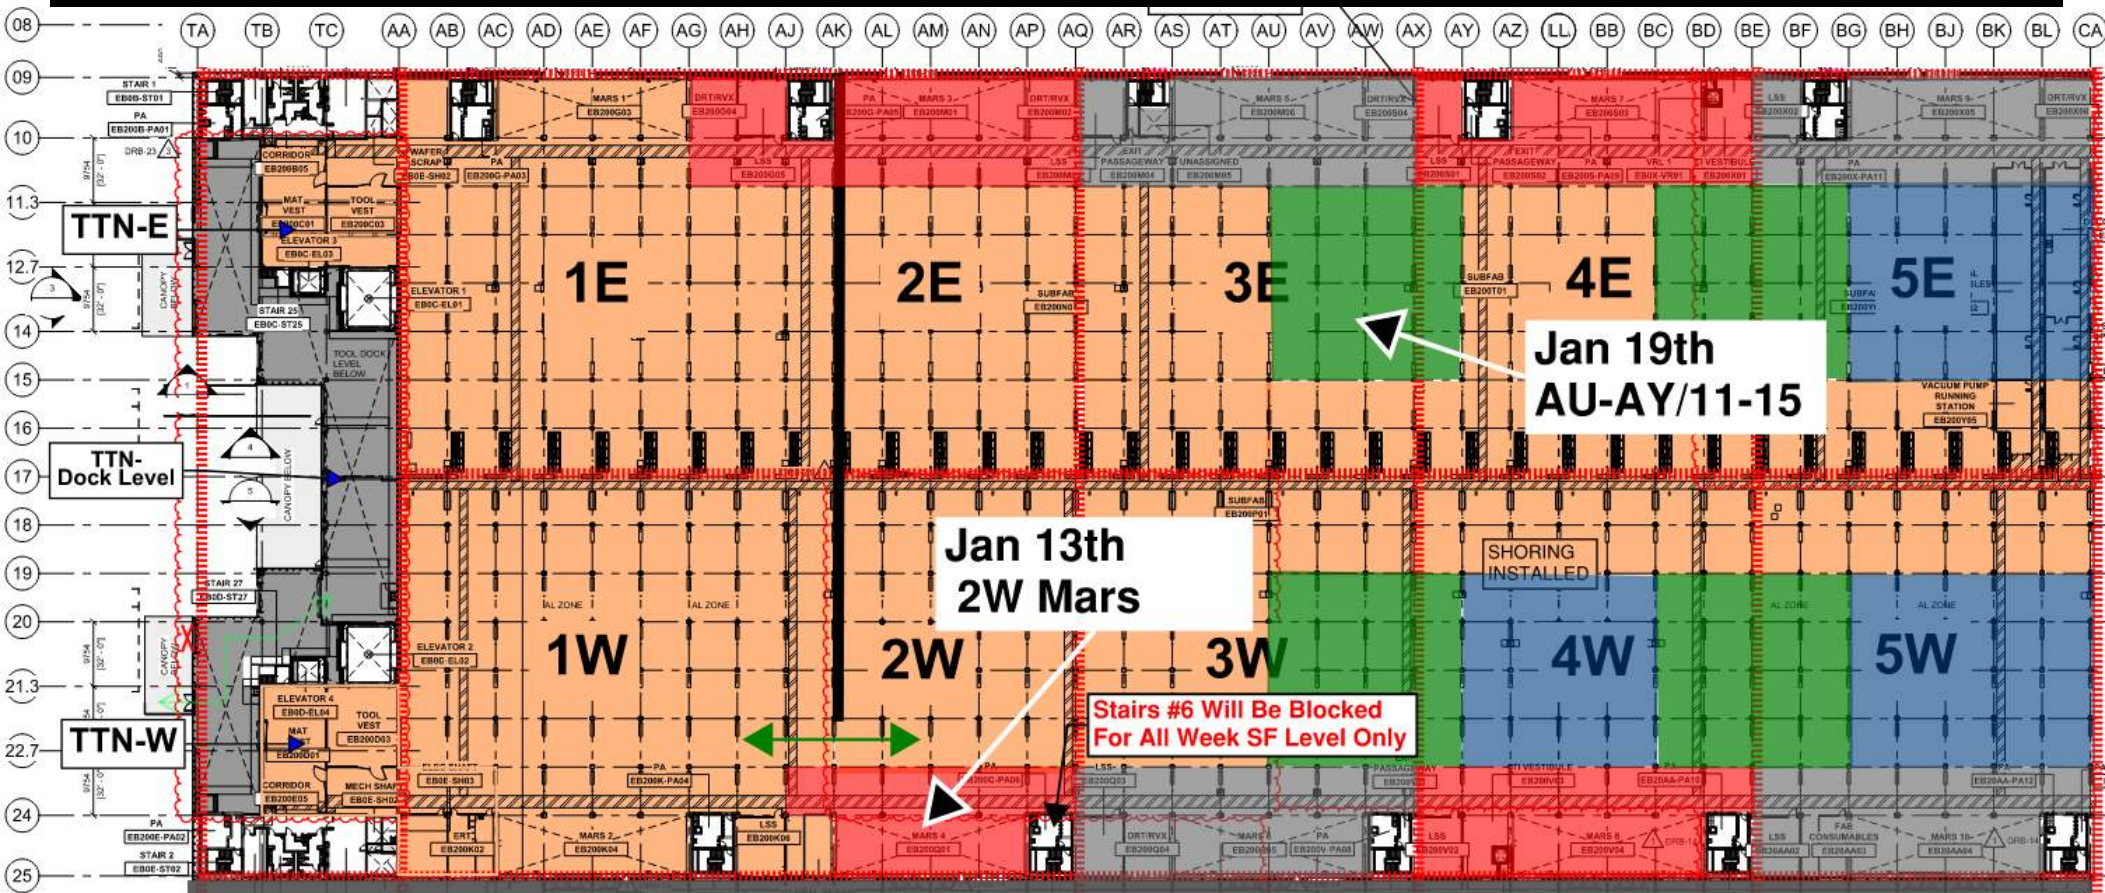



BCT Pressure Test Sunday

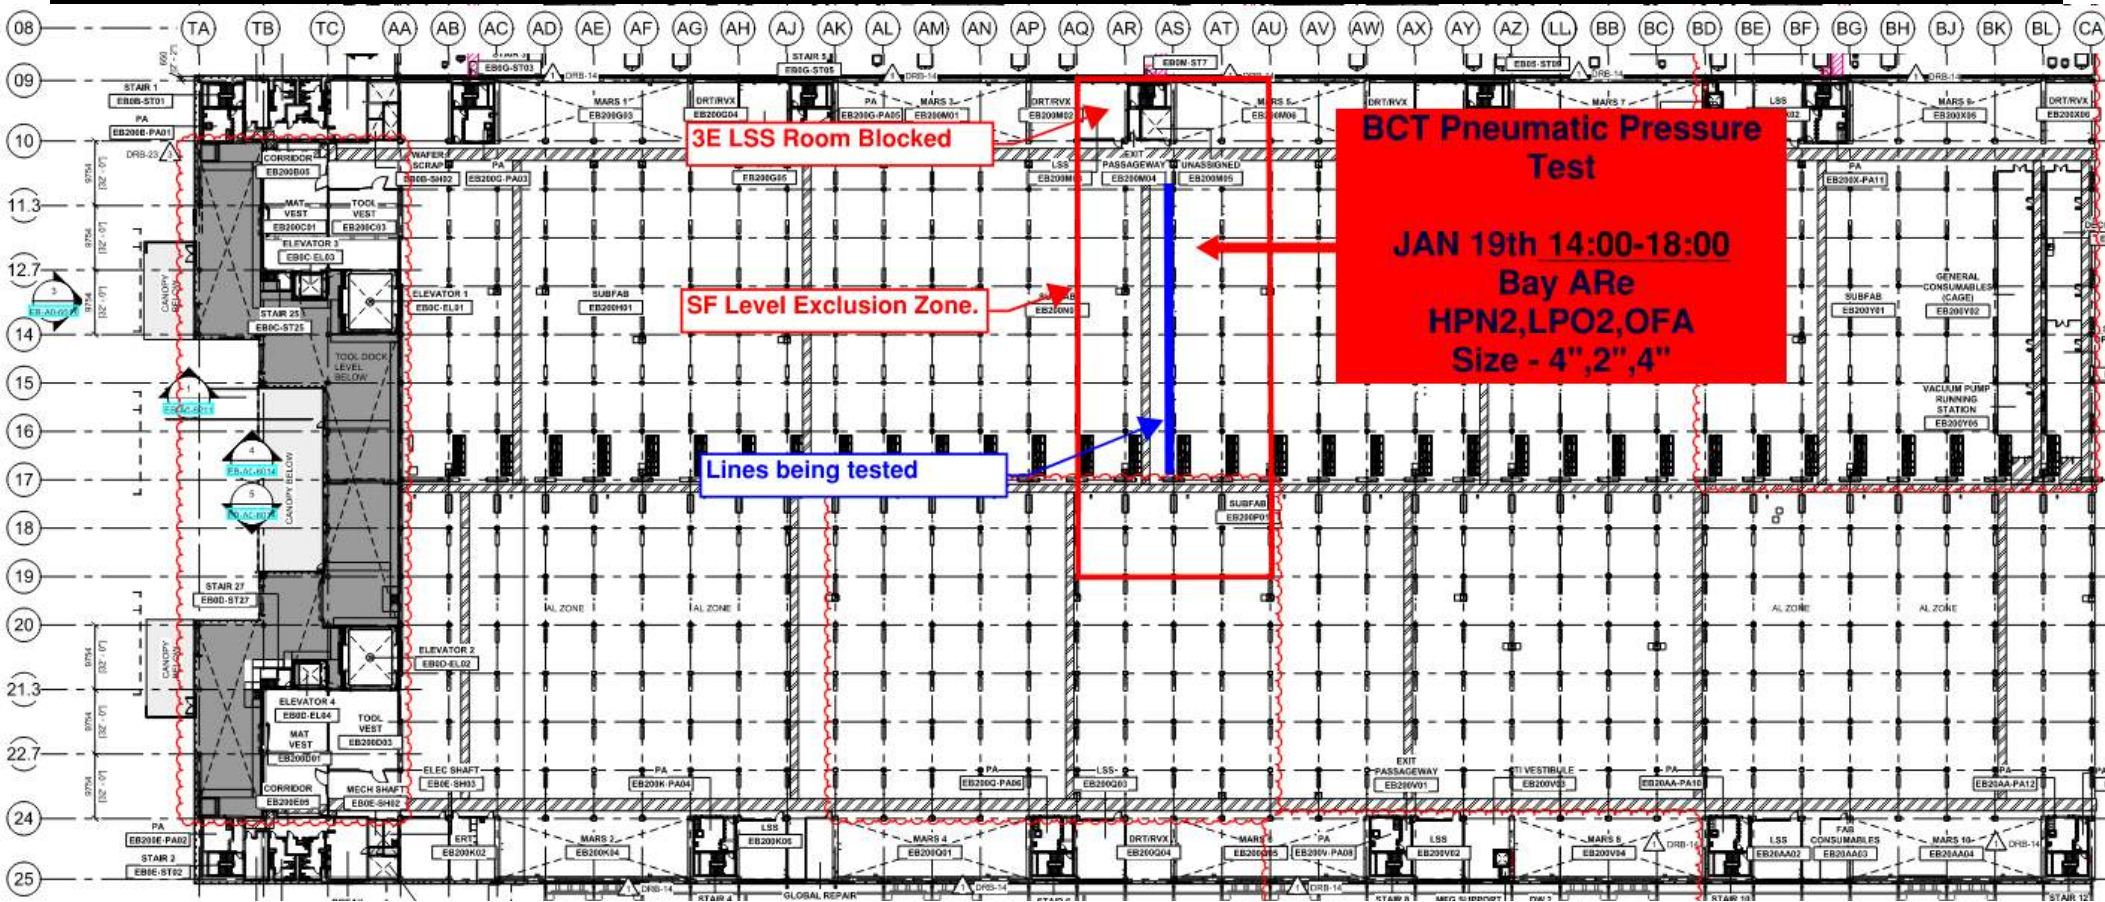


SUBFAB BUILDOUT MOD 2

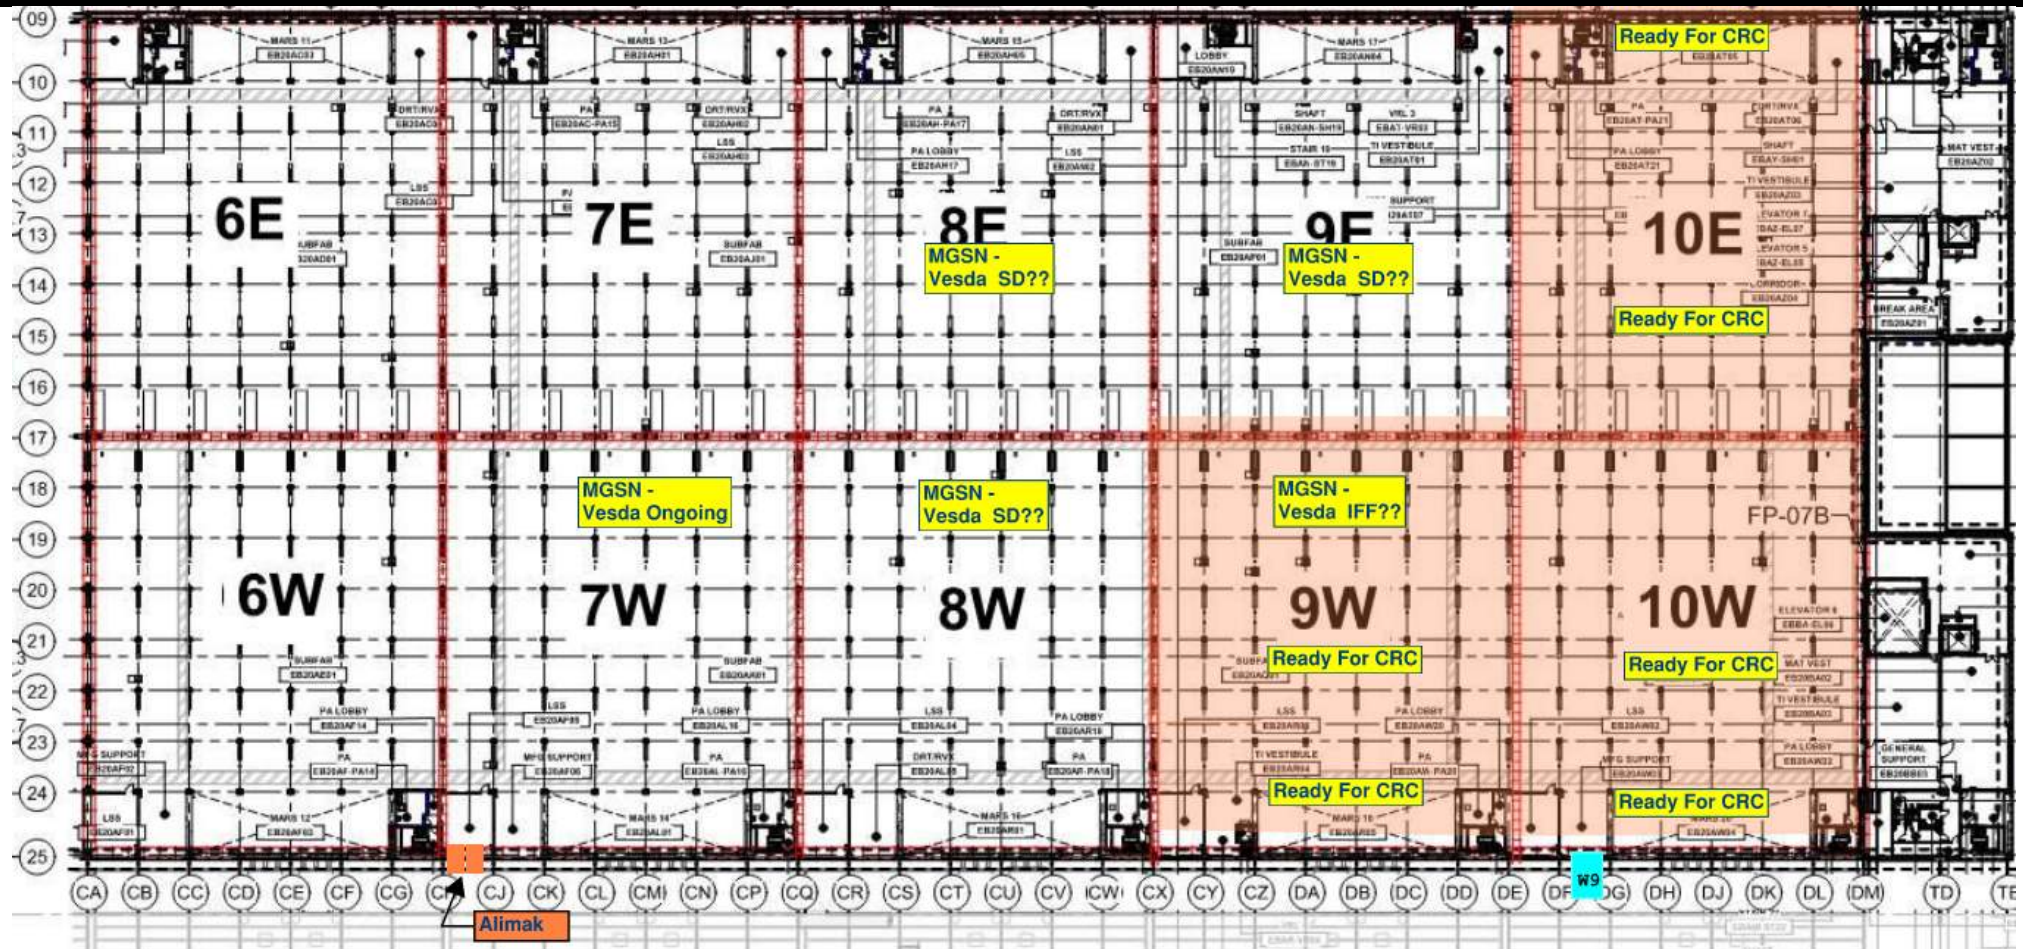

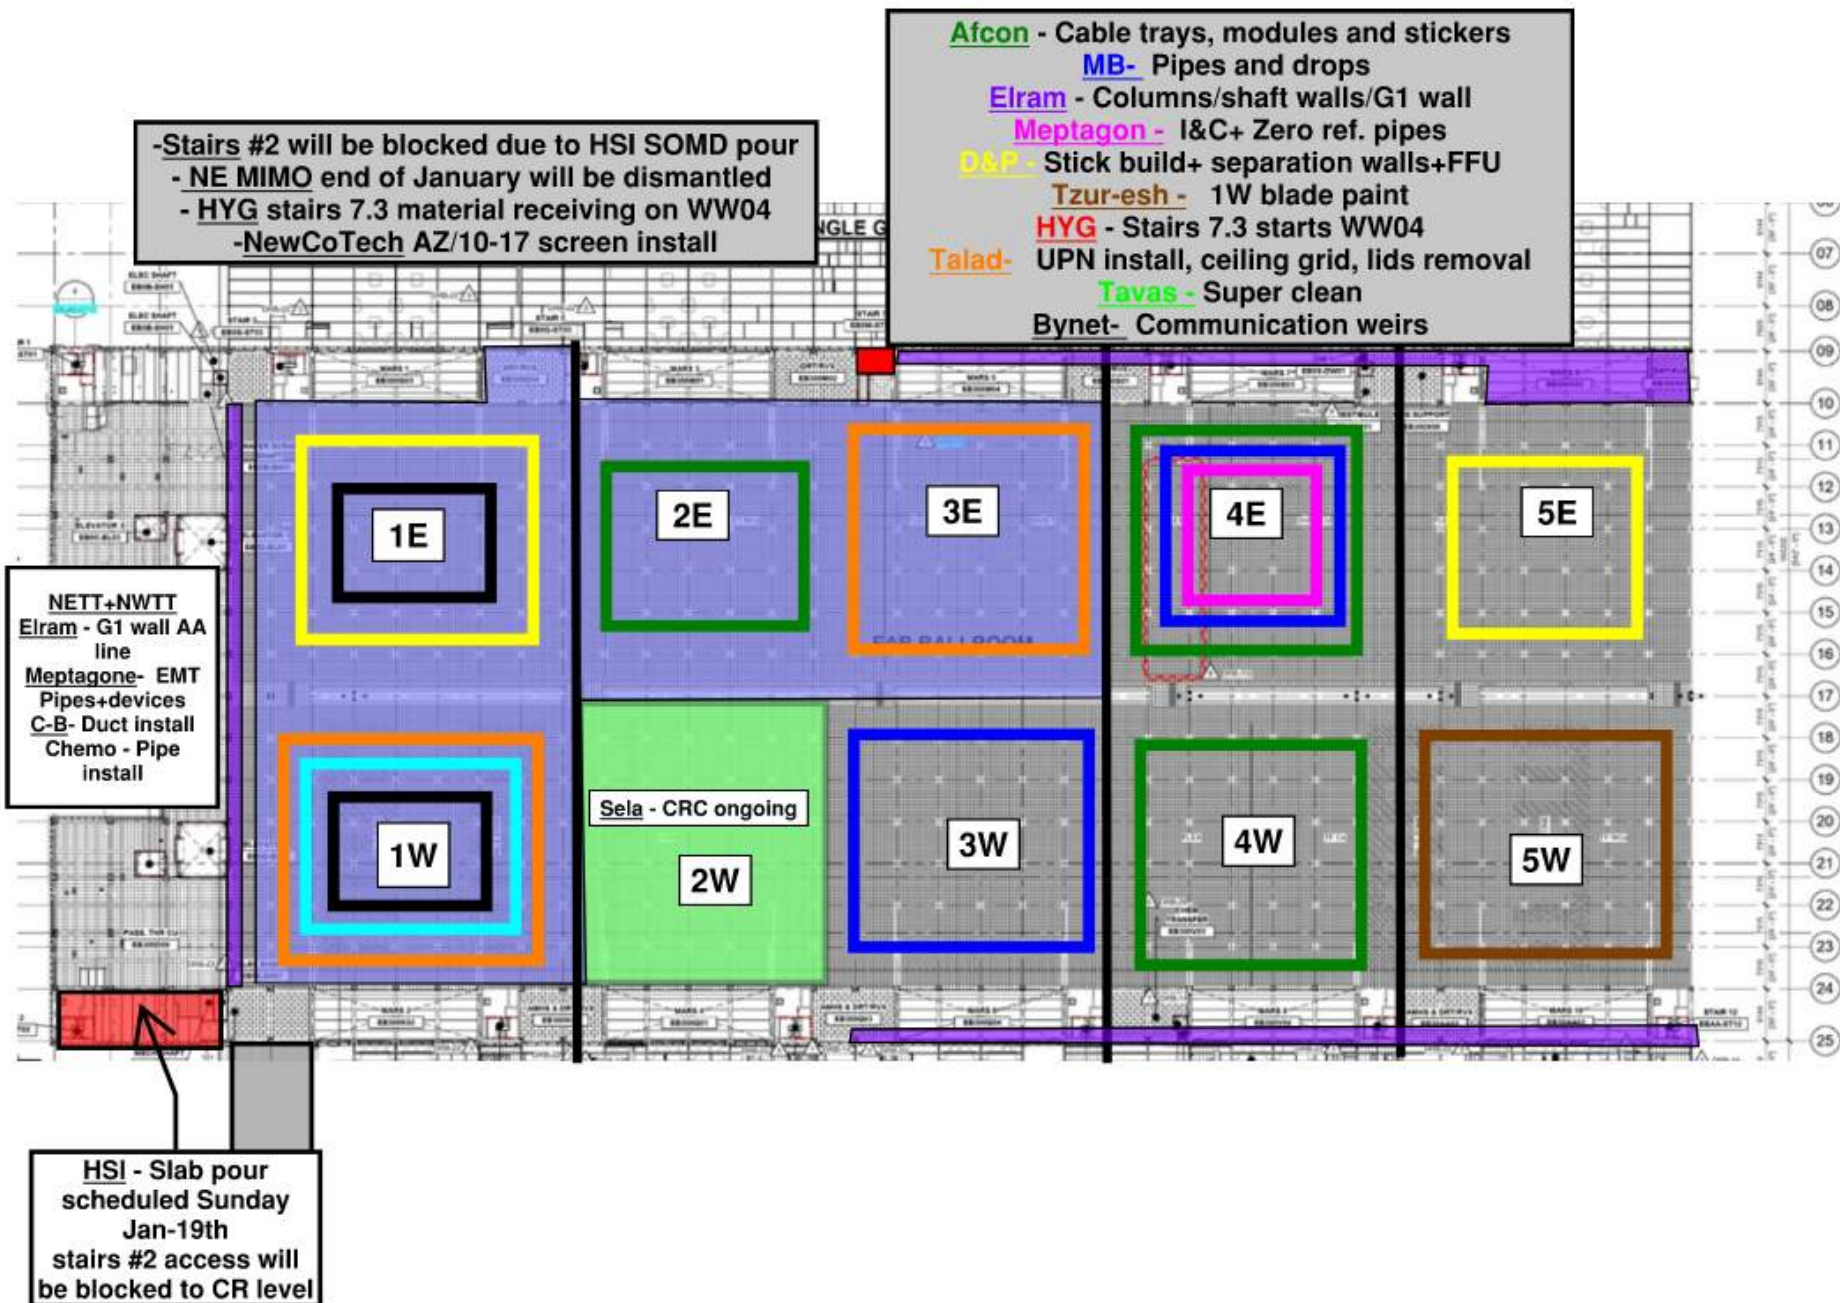

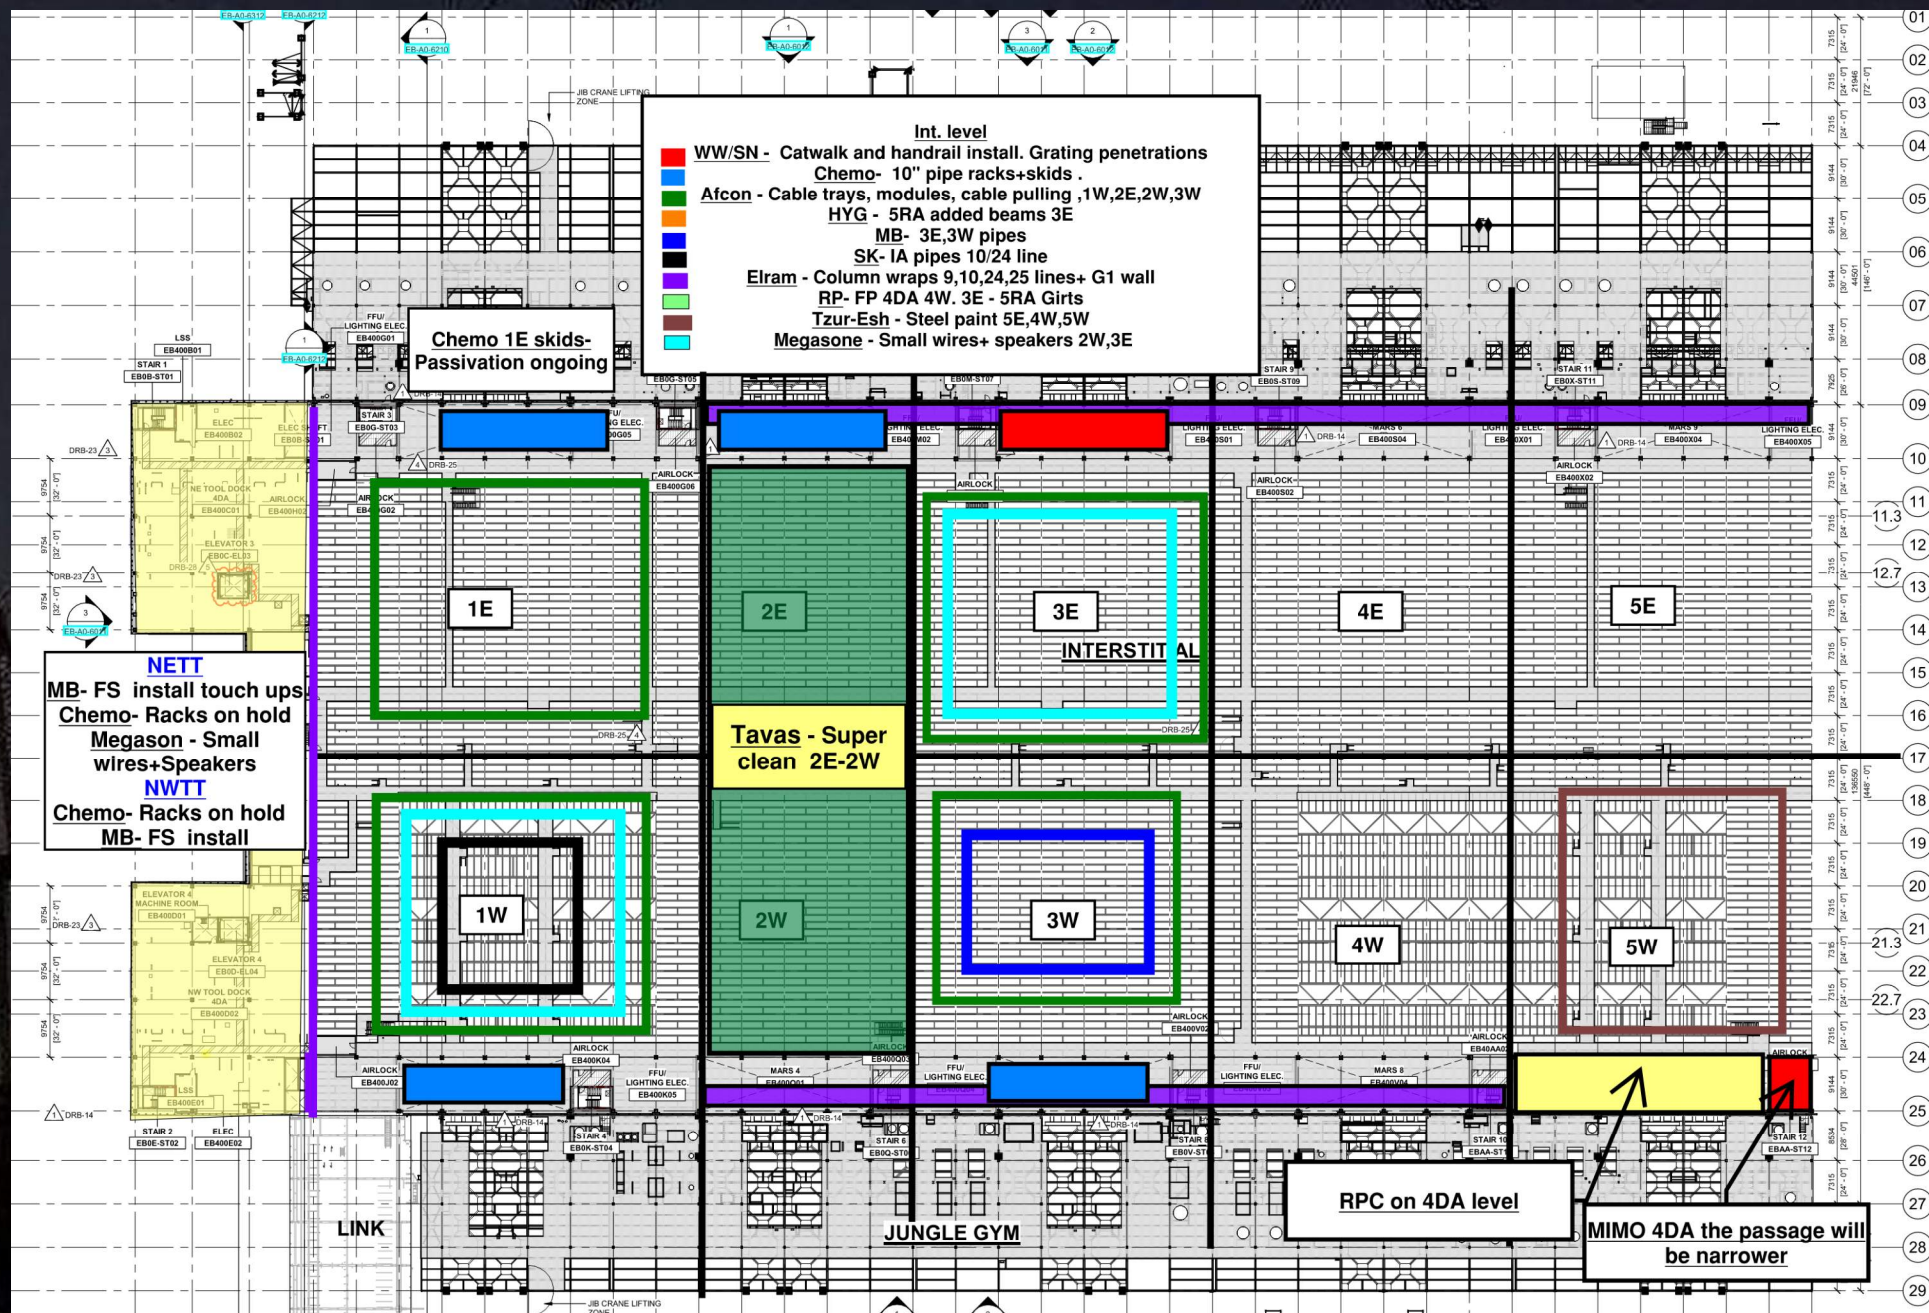


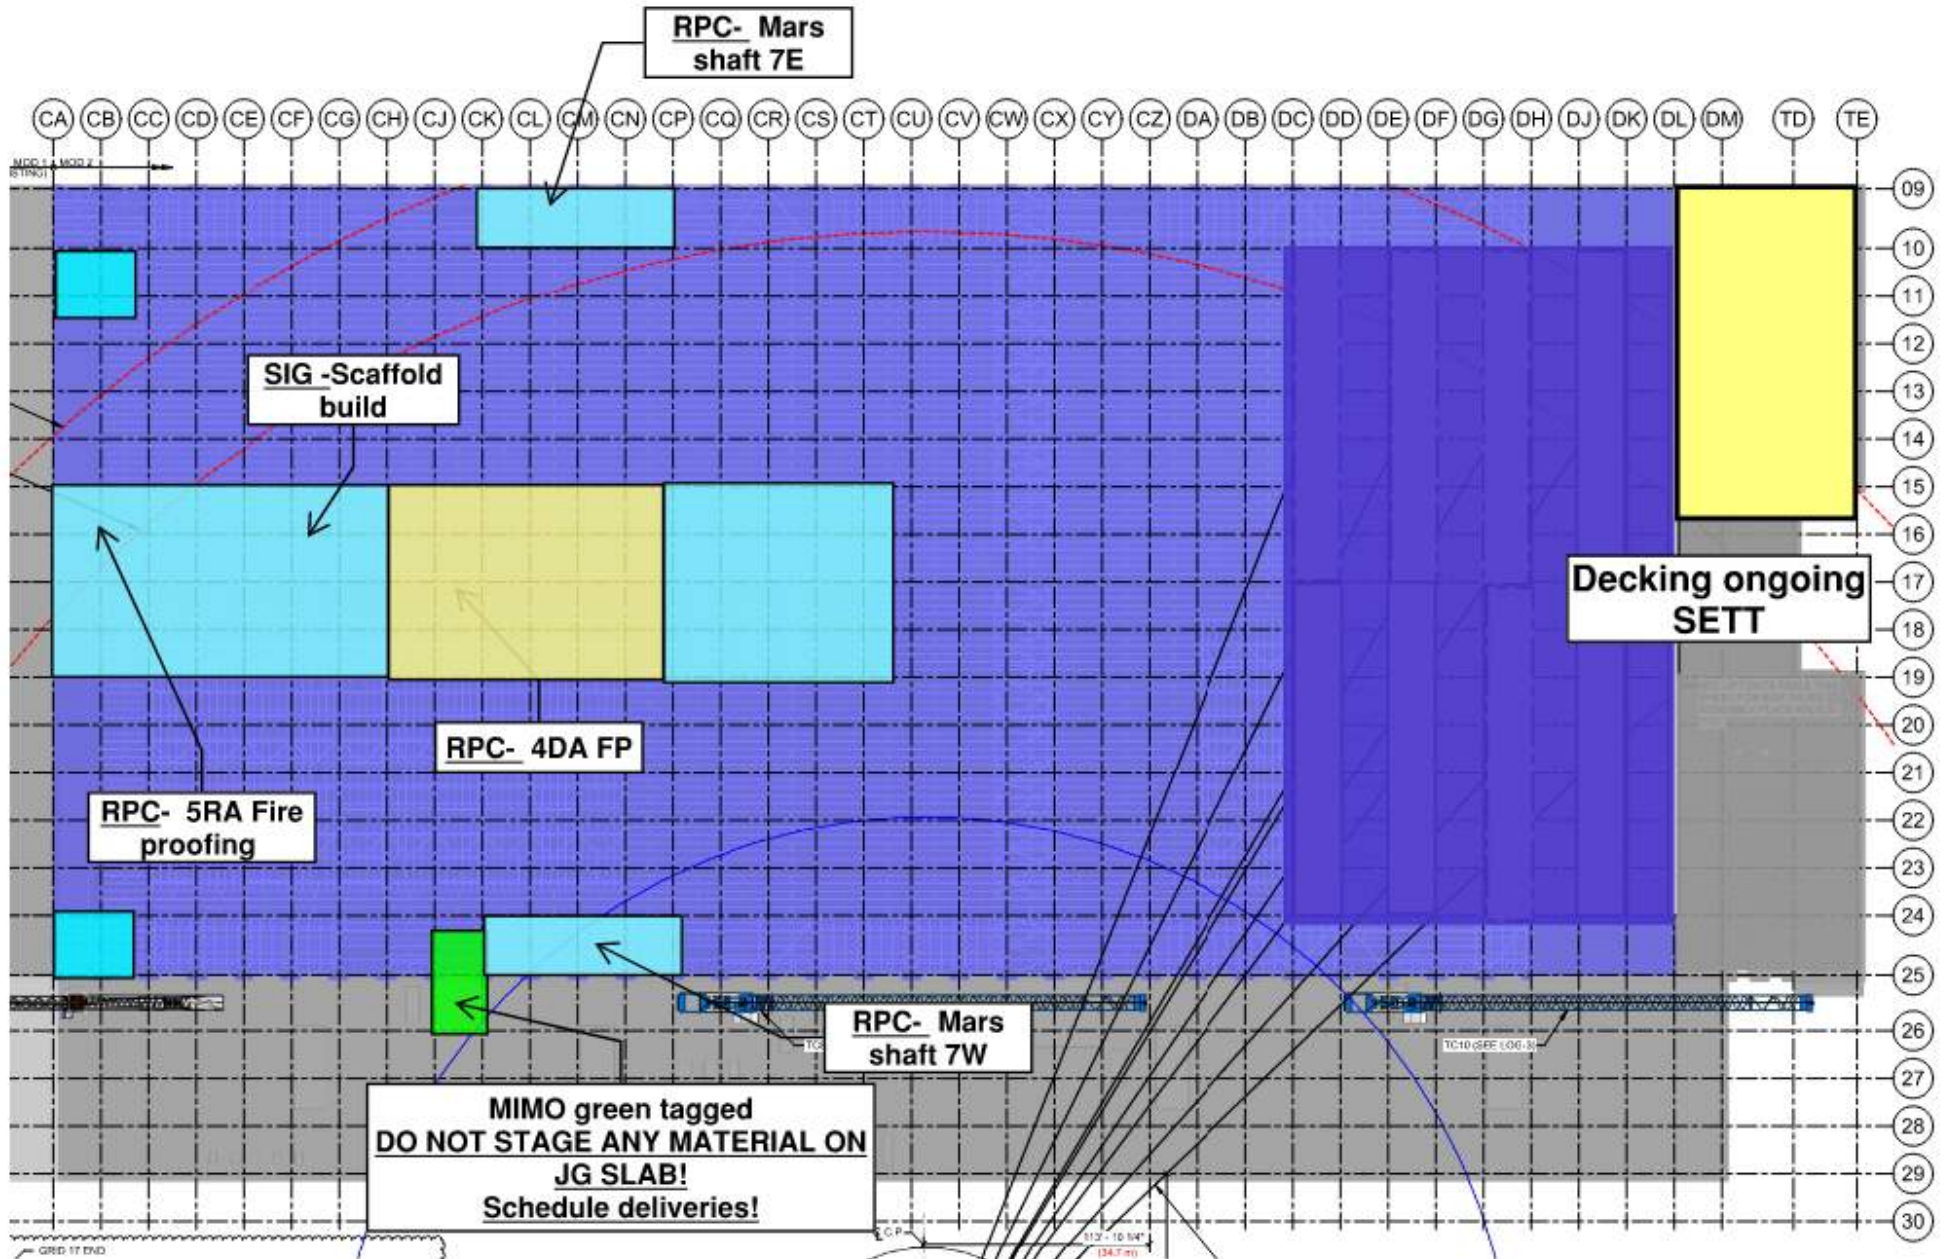

Mod 2 E House Roof
Picks.
Jan 14th @ 4:00 AM
Jan 16th @ 4:00 AM

Area to be
Closed for
Swing

Condensed
Barricade
for Bolting.

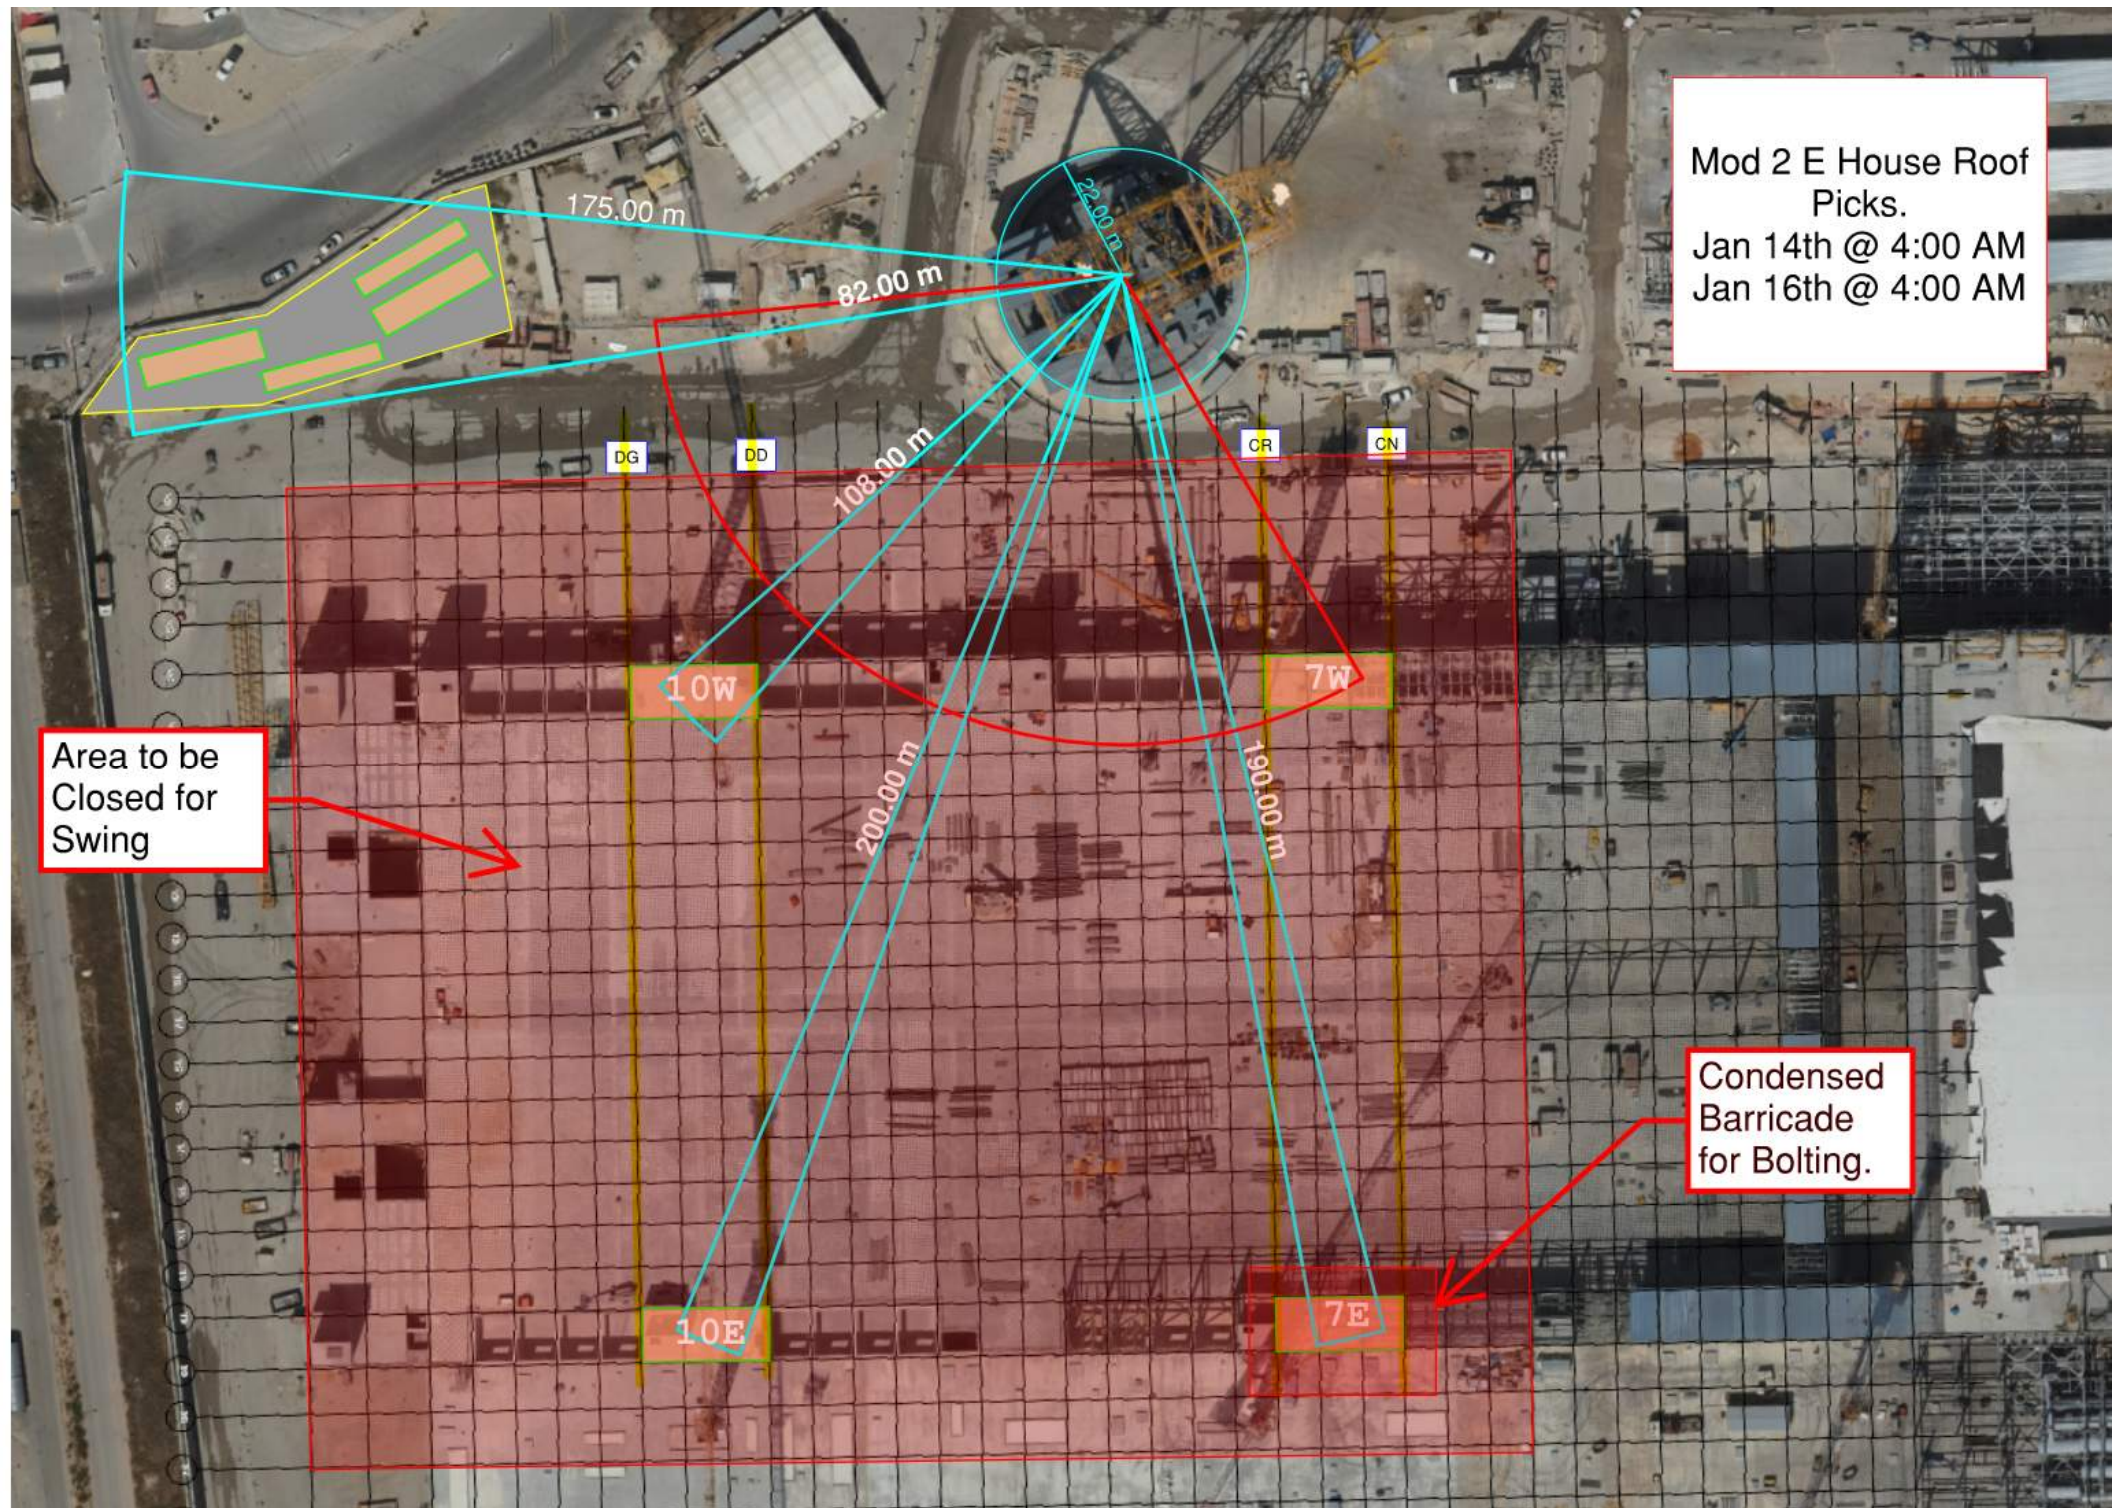

Siding - West FAB - JYG


BLOWDOWN 30%


Link


Siding - East FAB - PSSS

BLOWDOWN 30%

[illegible]

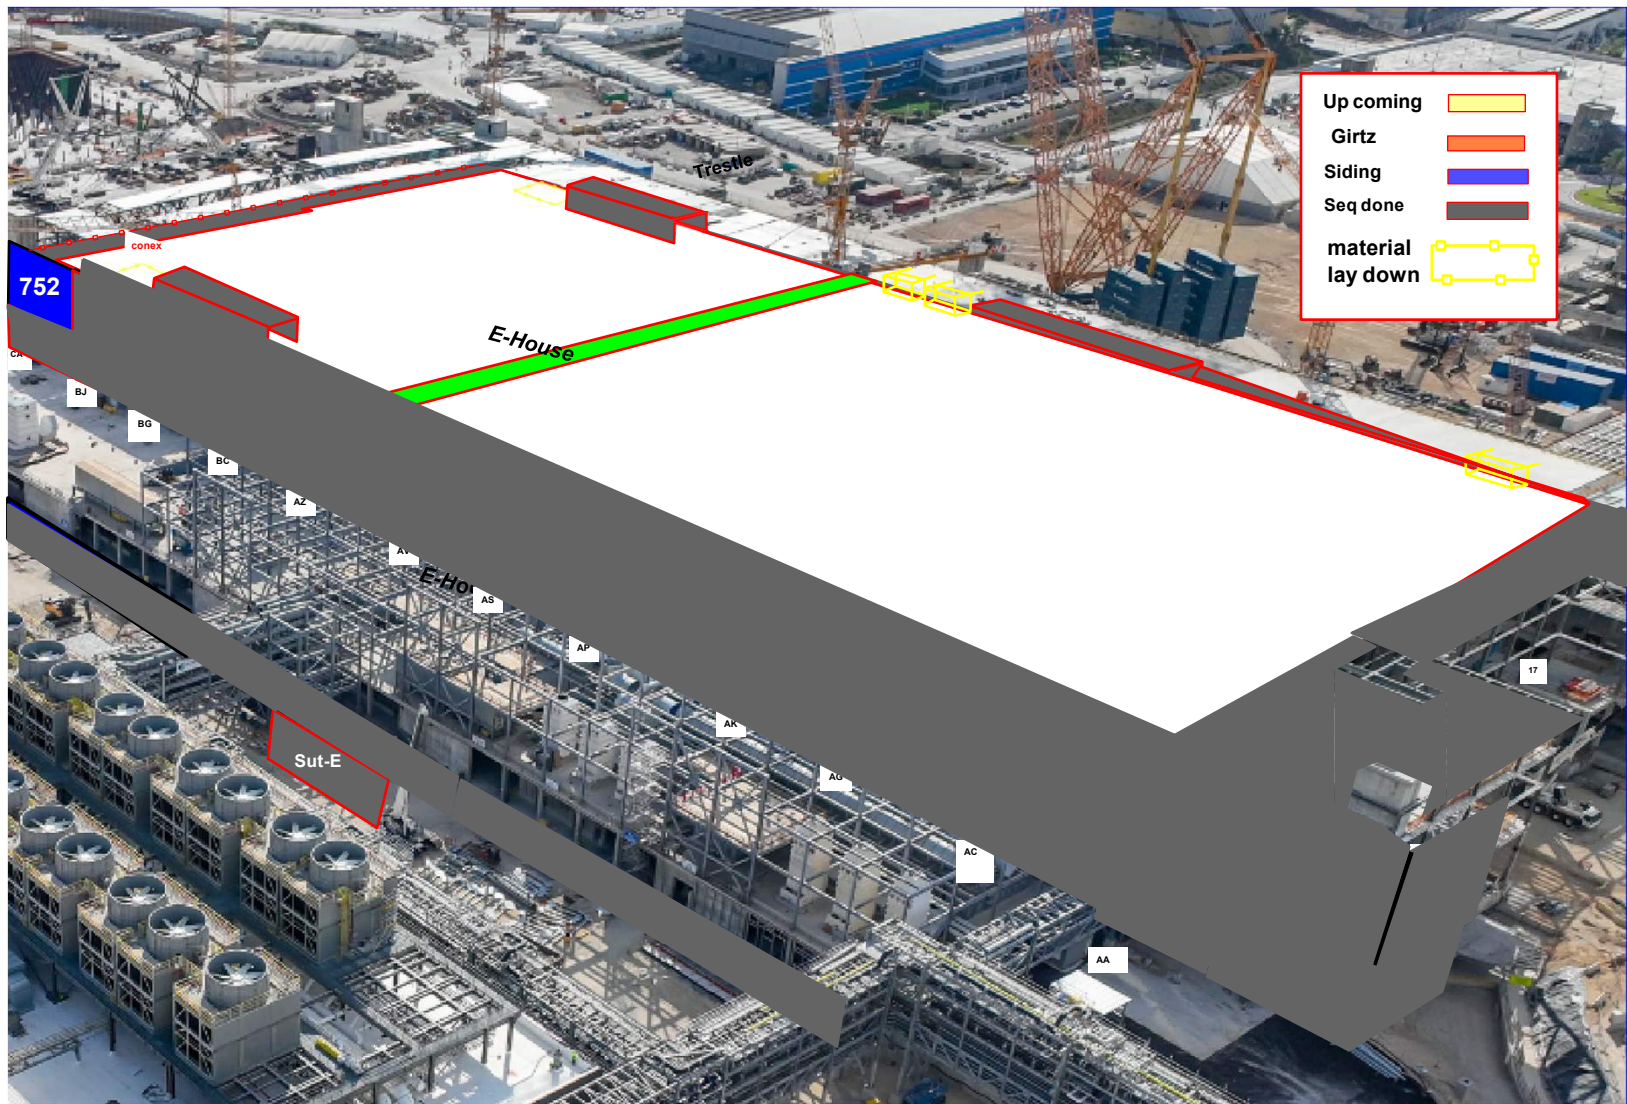

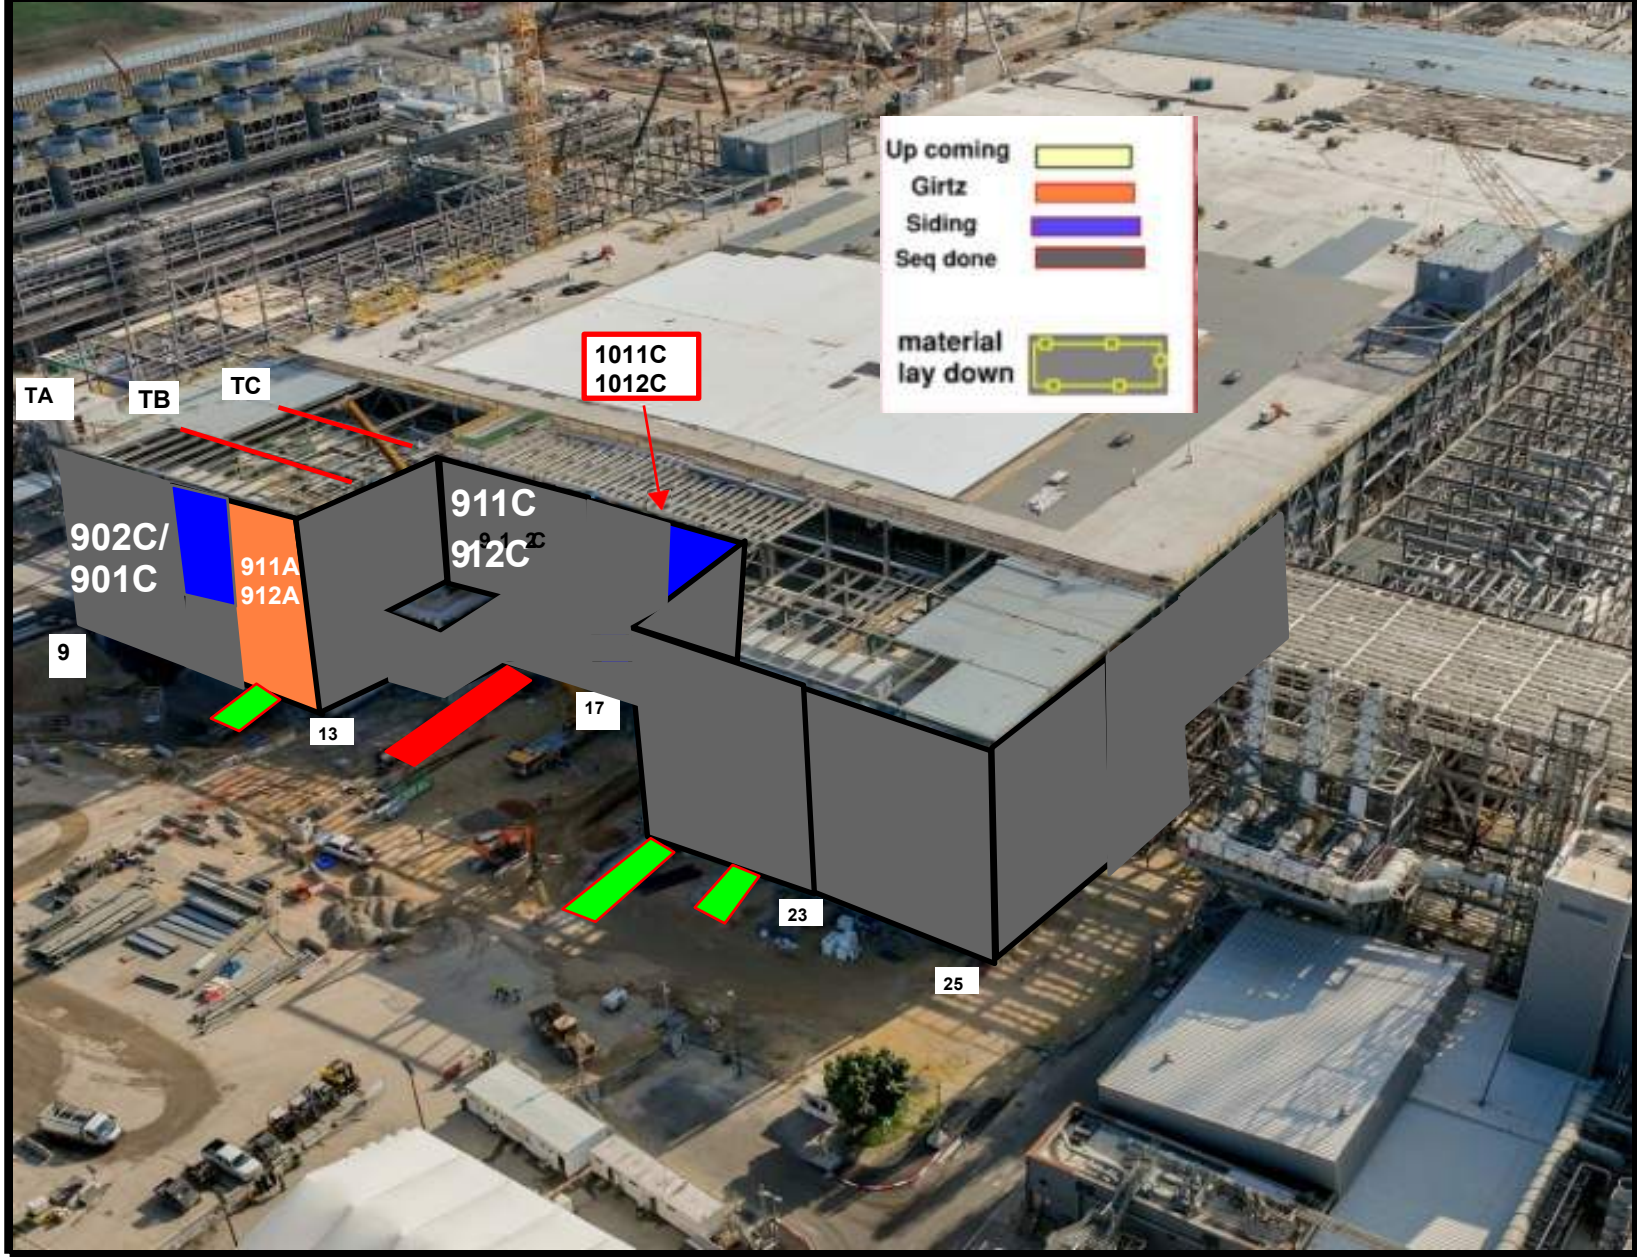

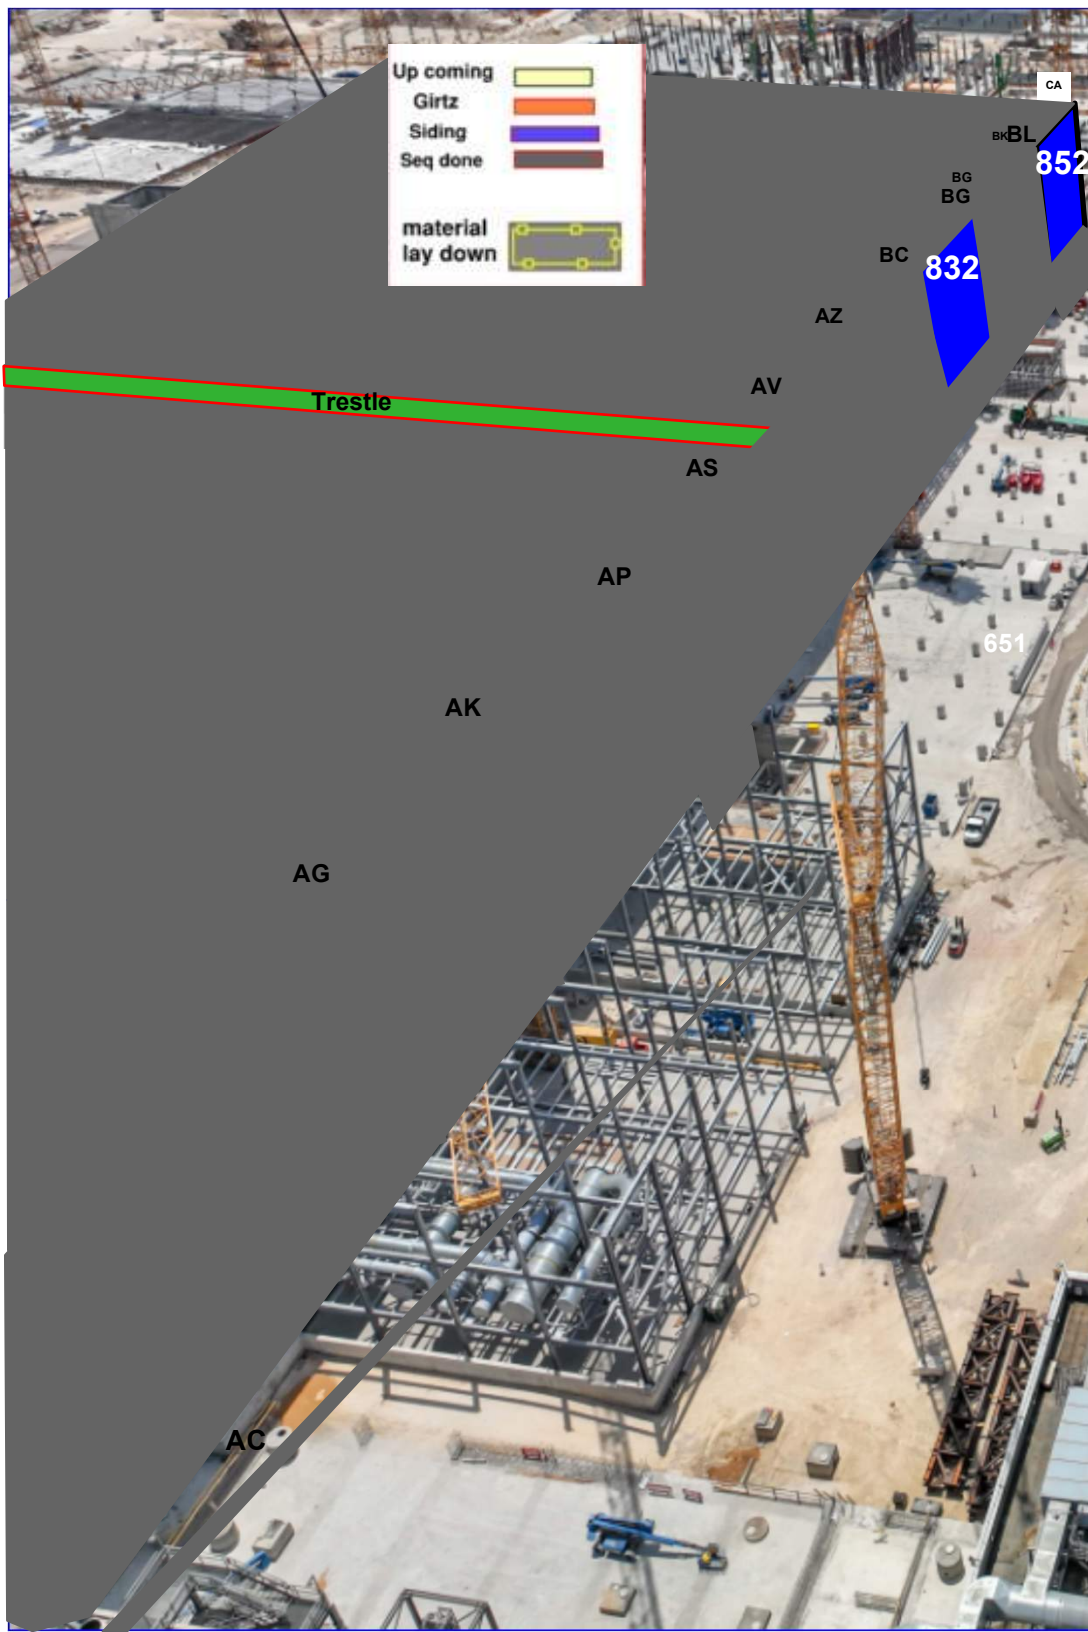


Up coming	
Girtz	
Siding	
Seq done	
material lay down	

PSSS.1

Utility Level
1YA


PSSS Roof
2SA

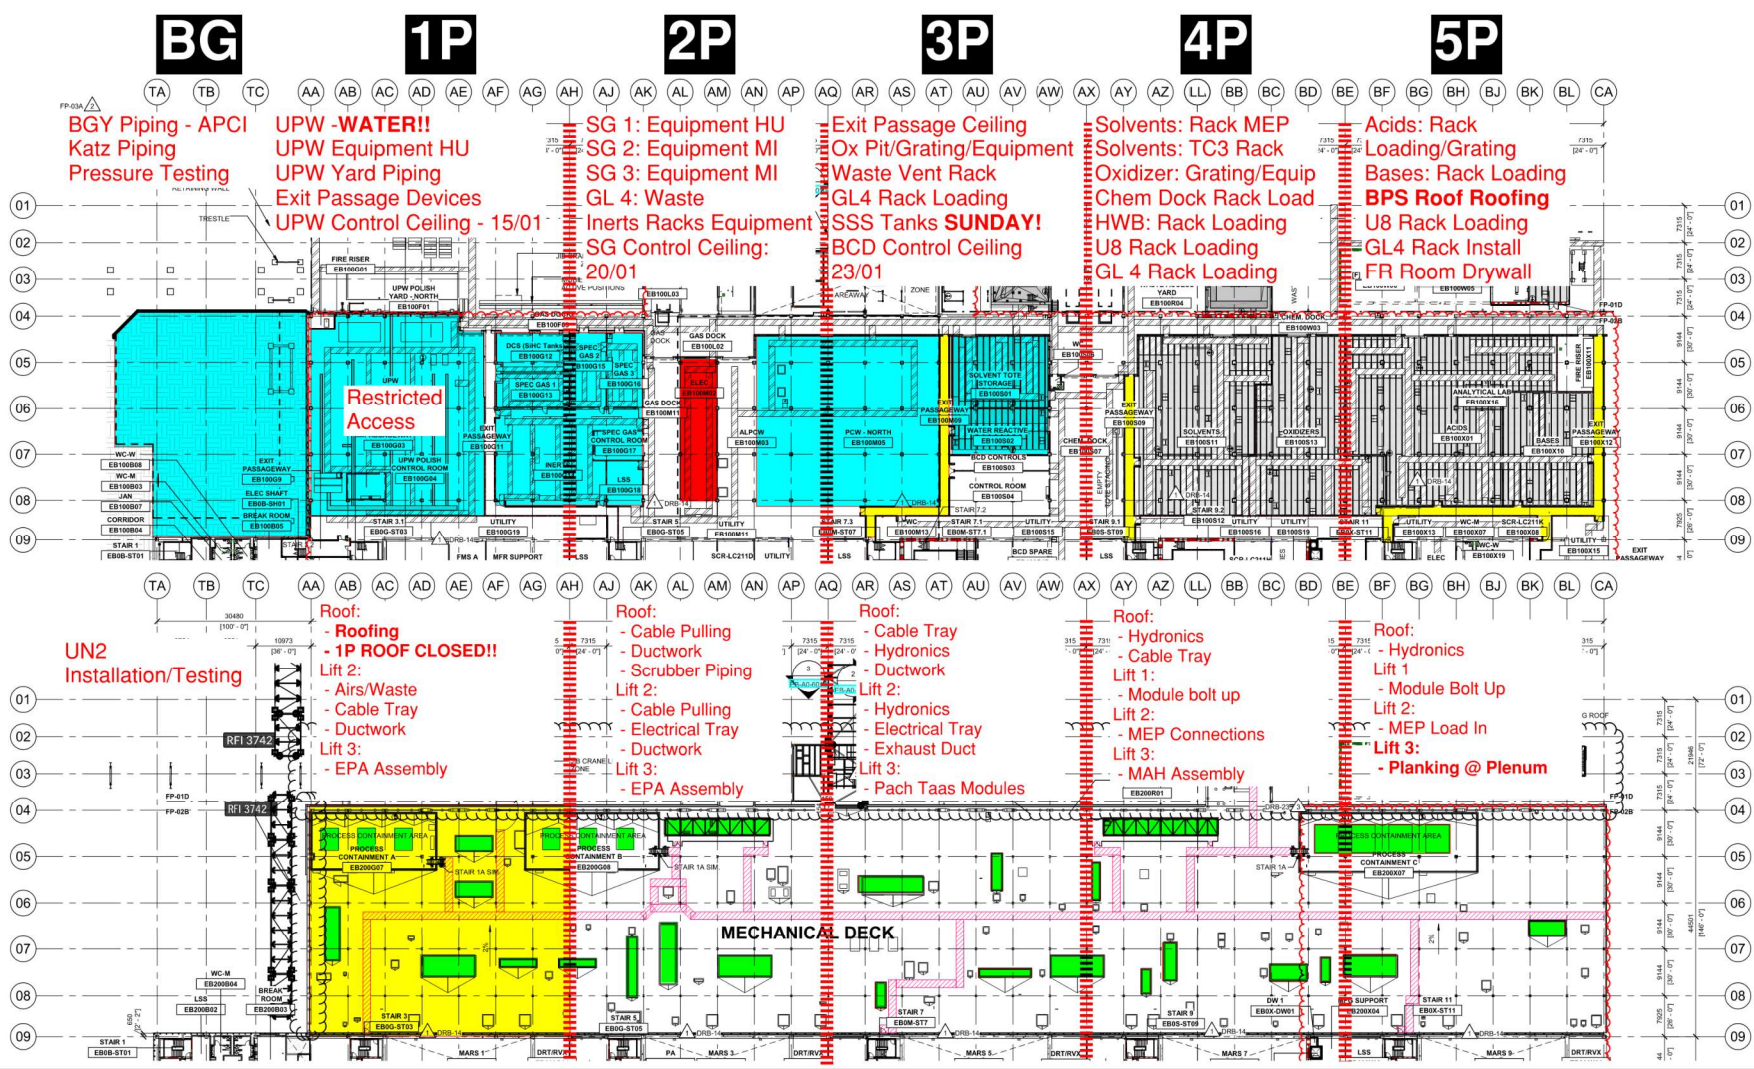


PSSS.2

Utility Level


1YA

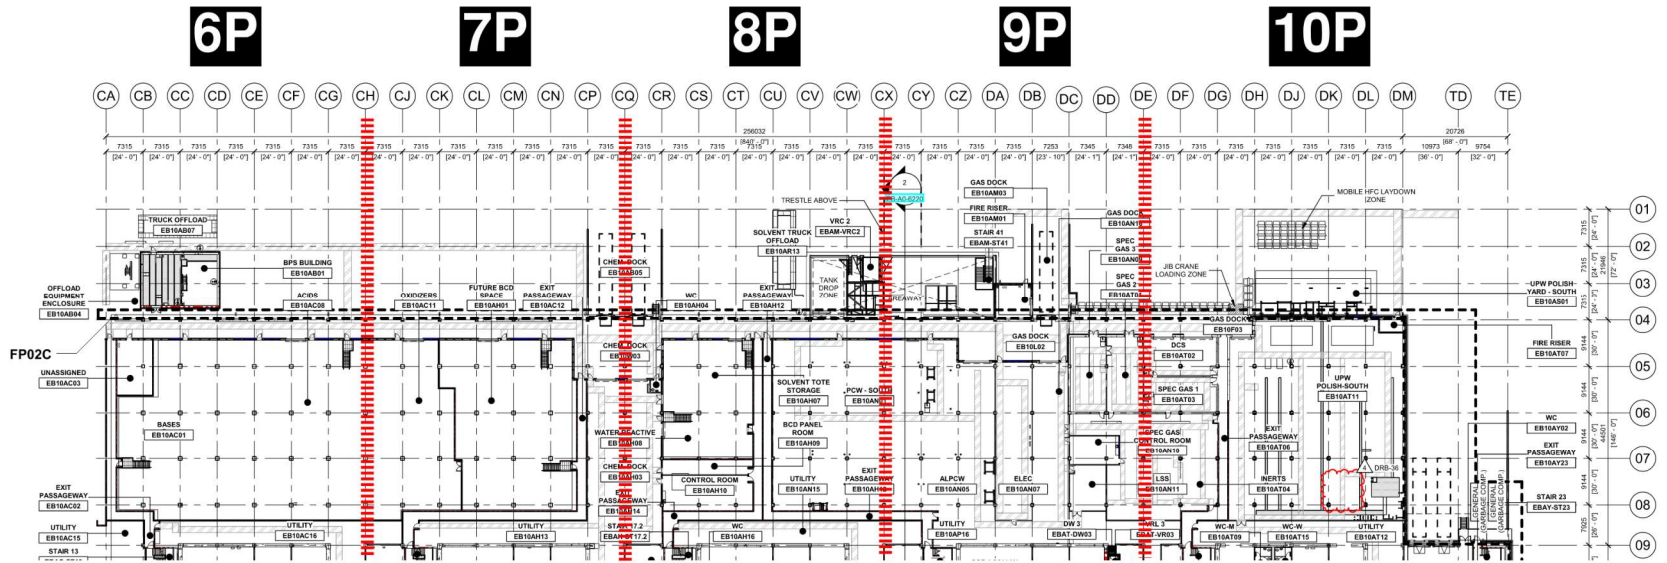


PSSS Roof 2SA

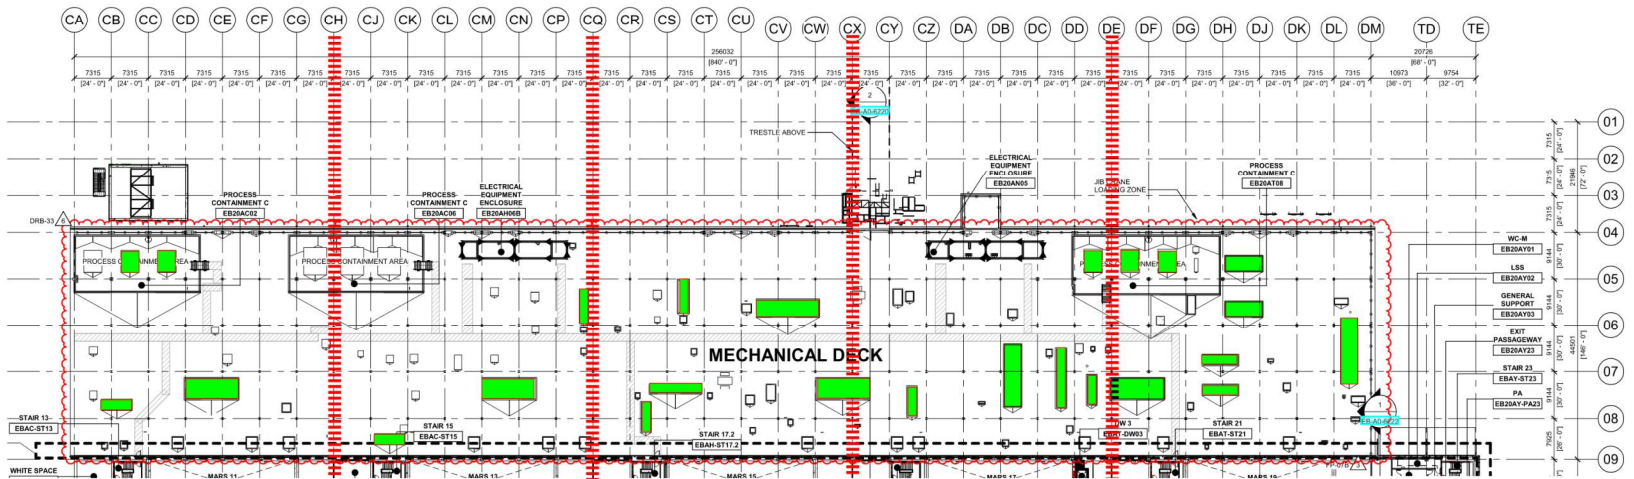


H2 Vent
Radiographic
Test
16/01
17:00-01:00

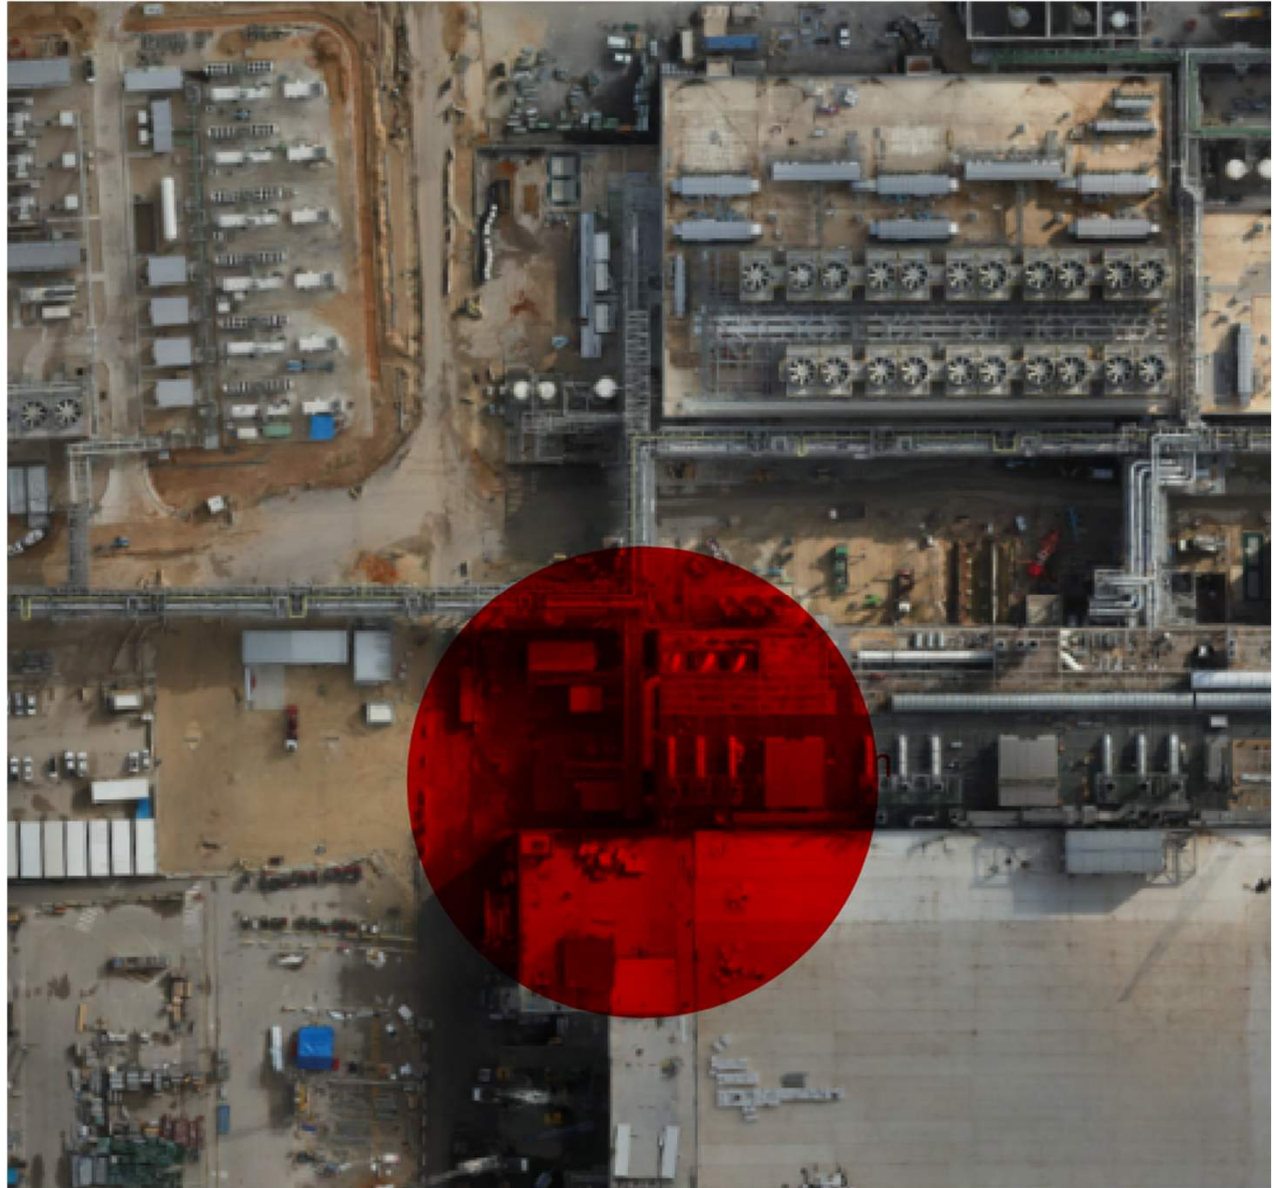

WJG 01J, 02J LIFT 2 & 3

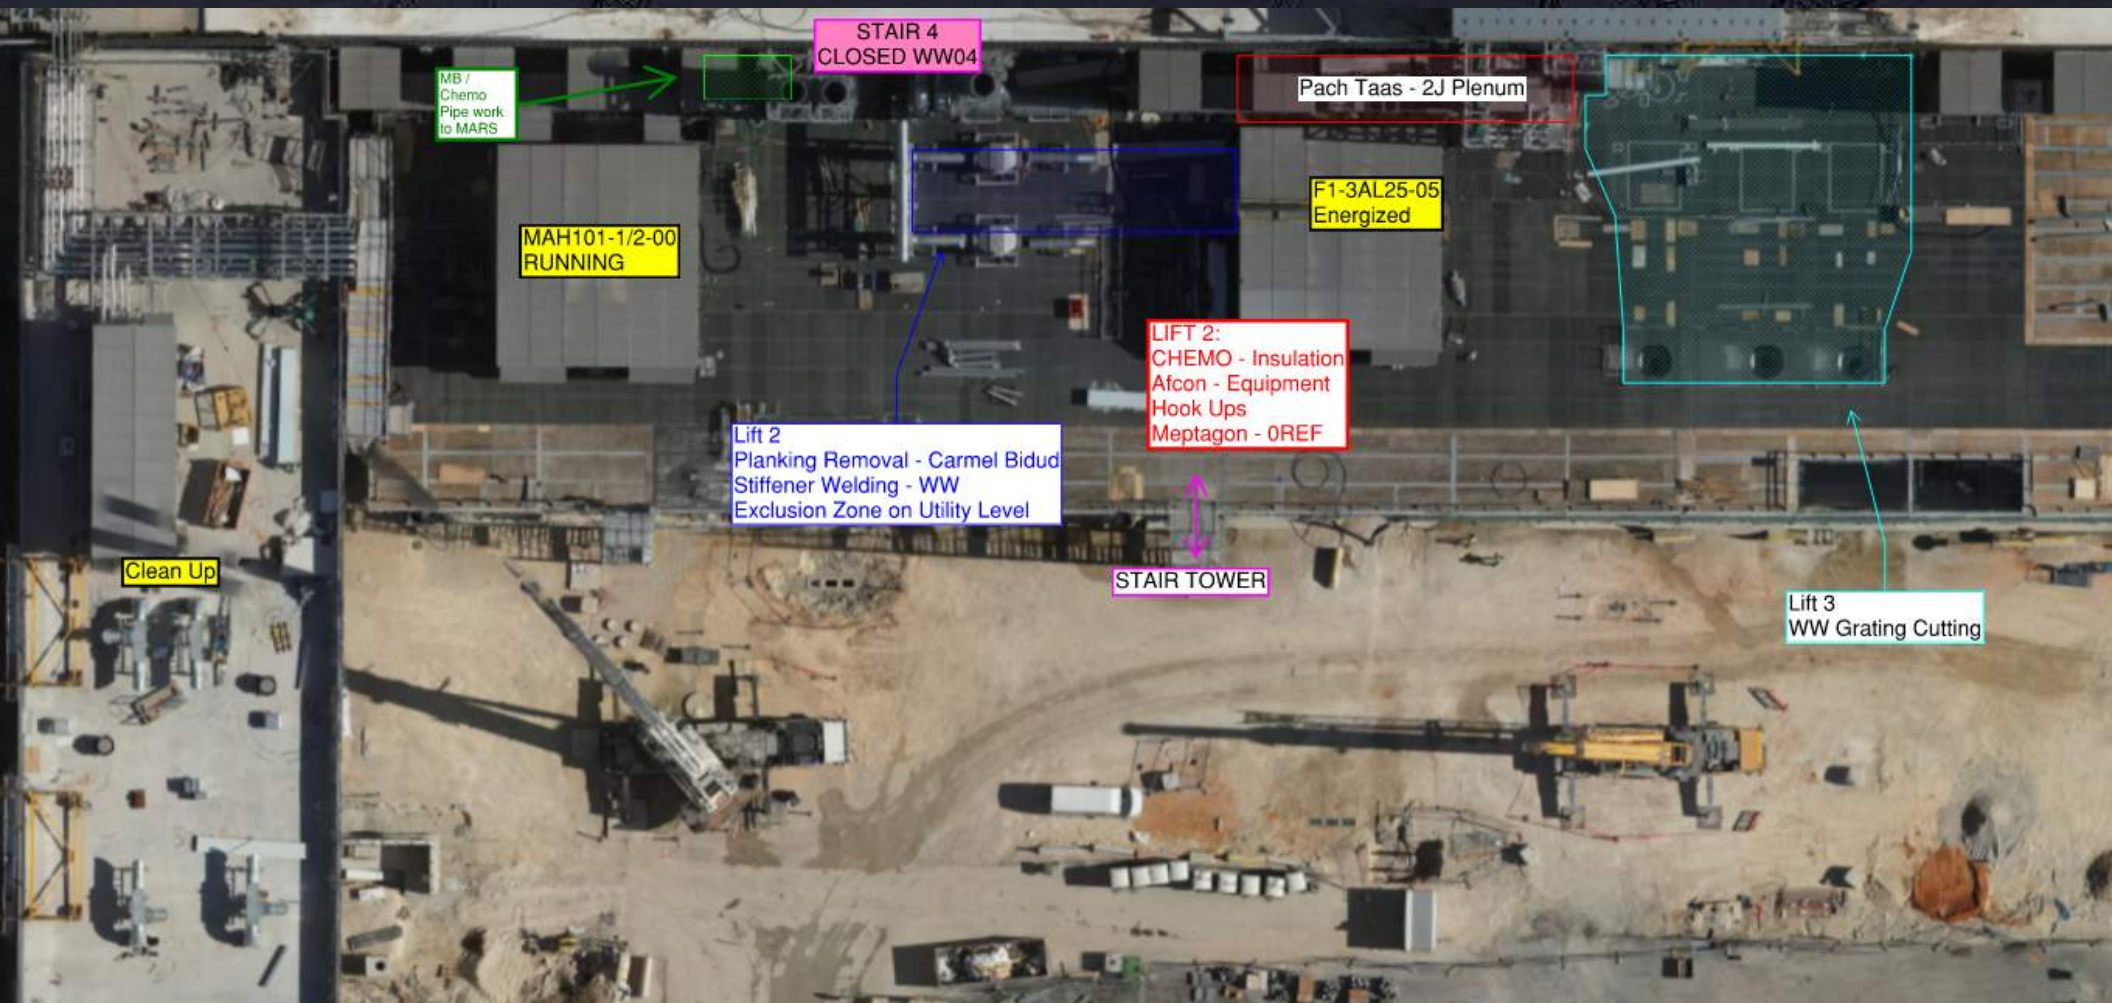


WJG 03J, 04J, 05J LIFT 2 & 3

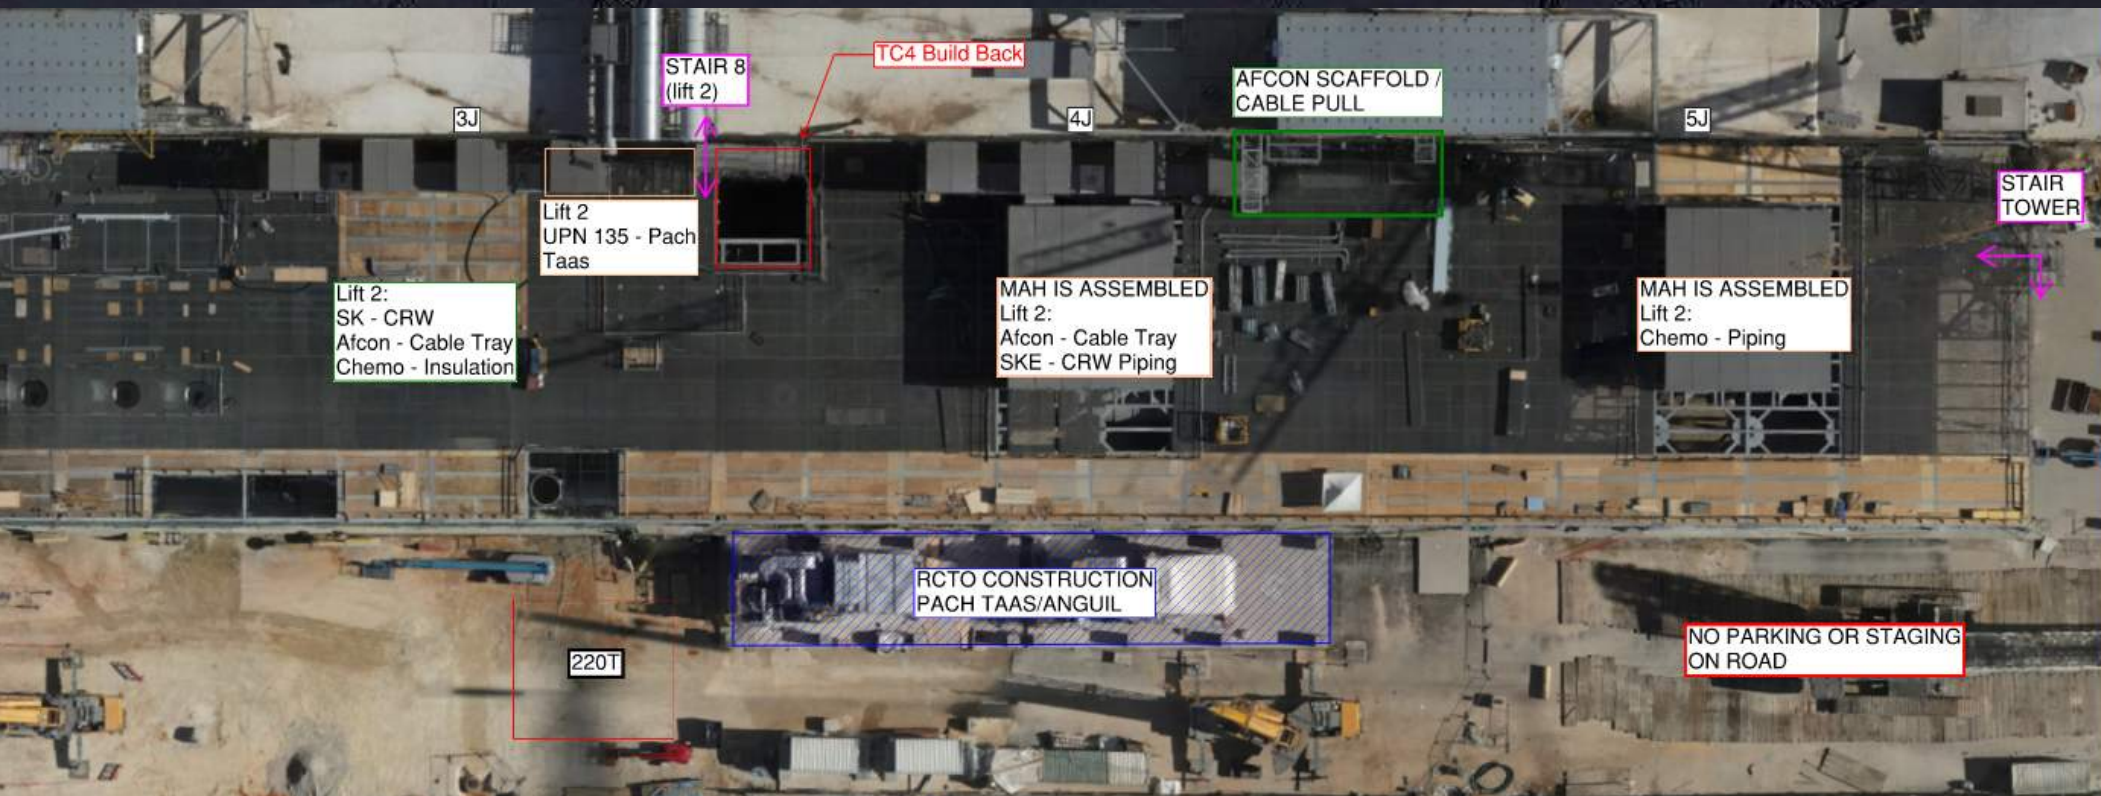





WJG UTILITY LEVEL BUILD OUT

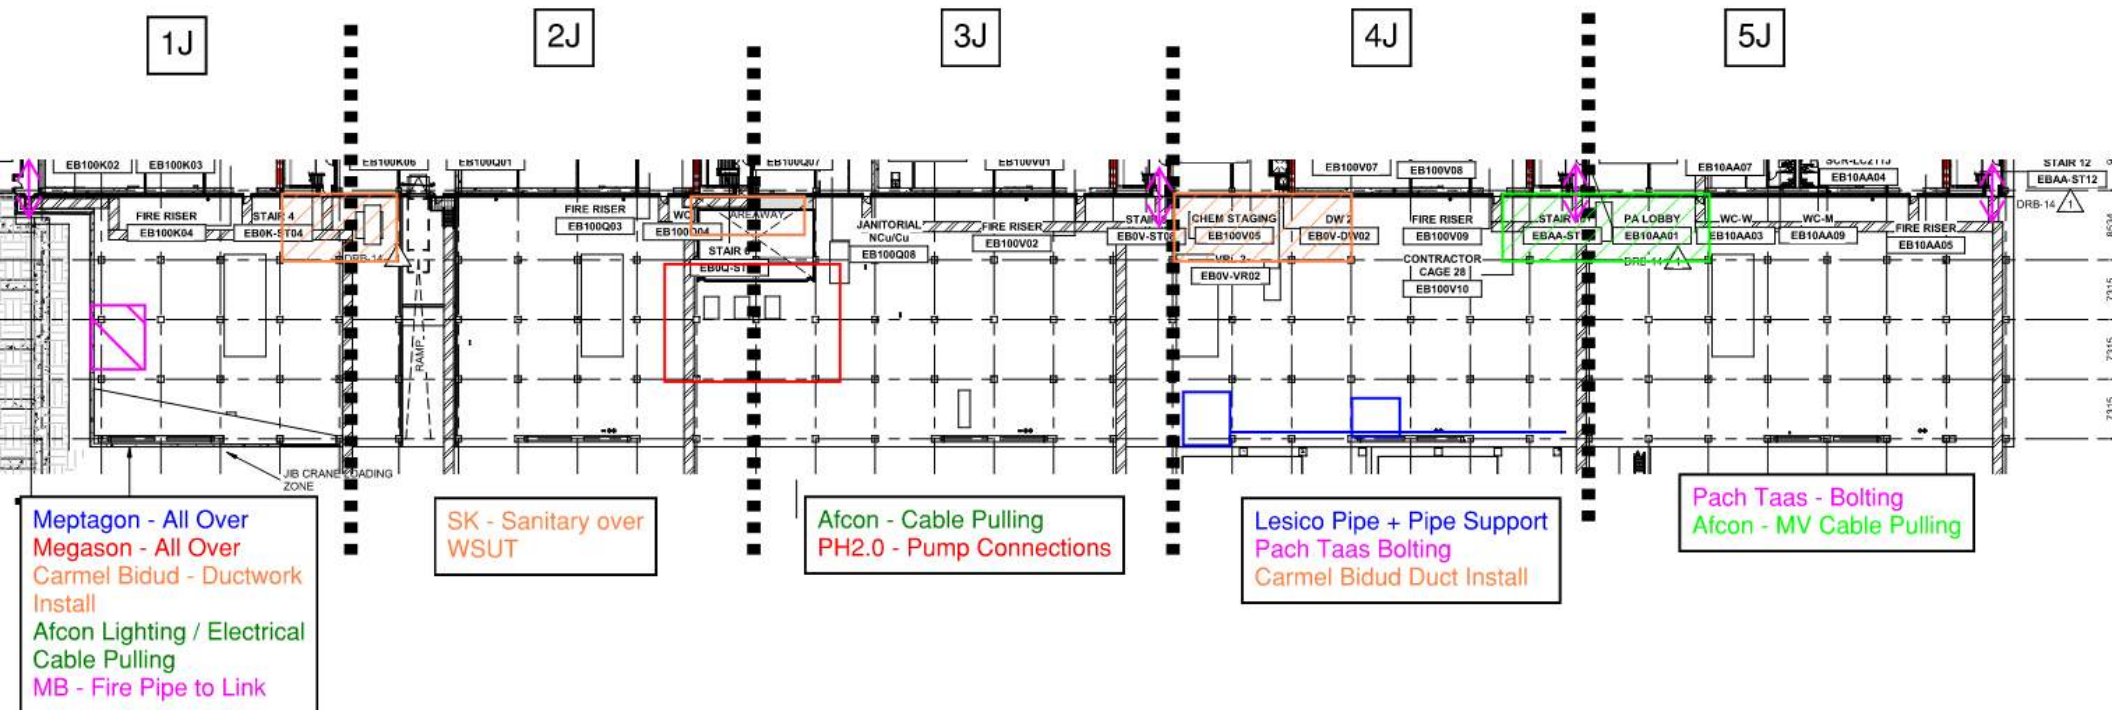

CUB COORDINATION MAP

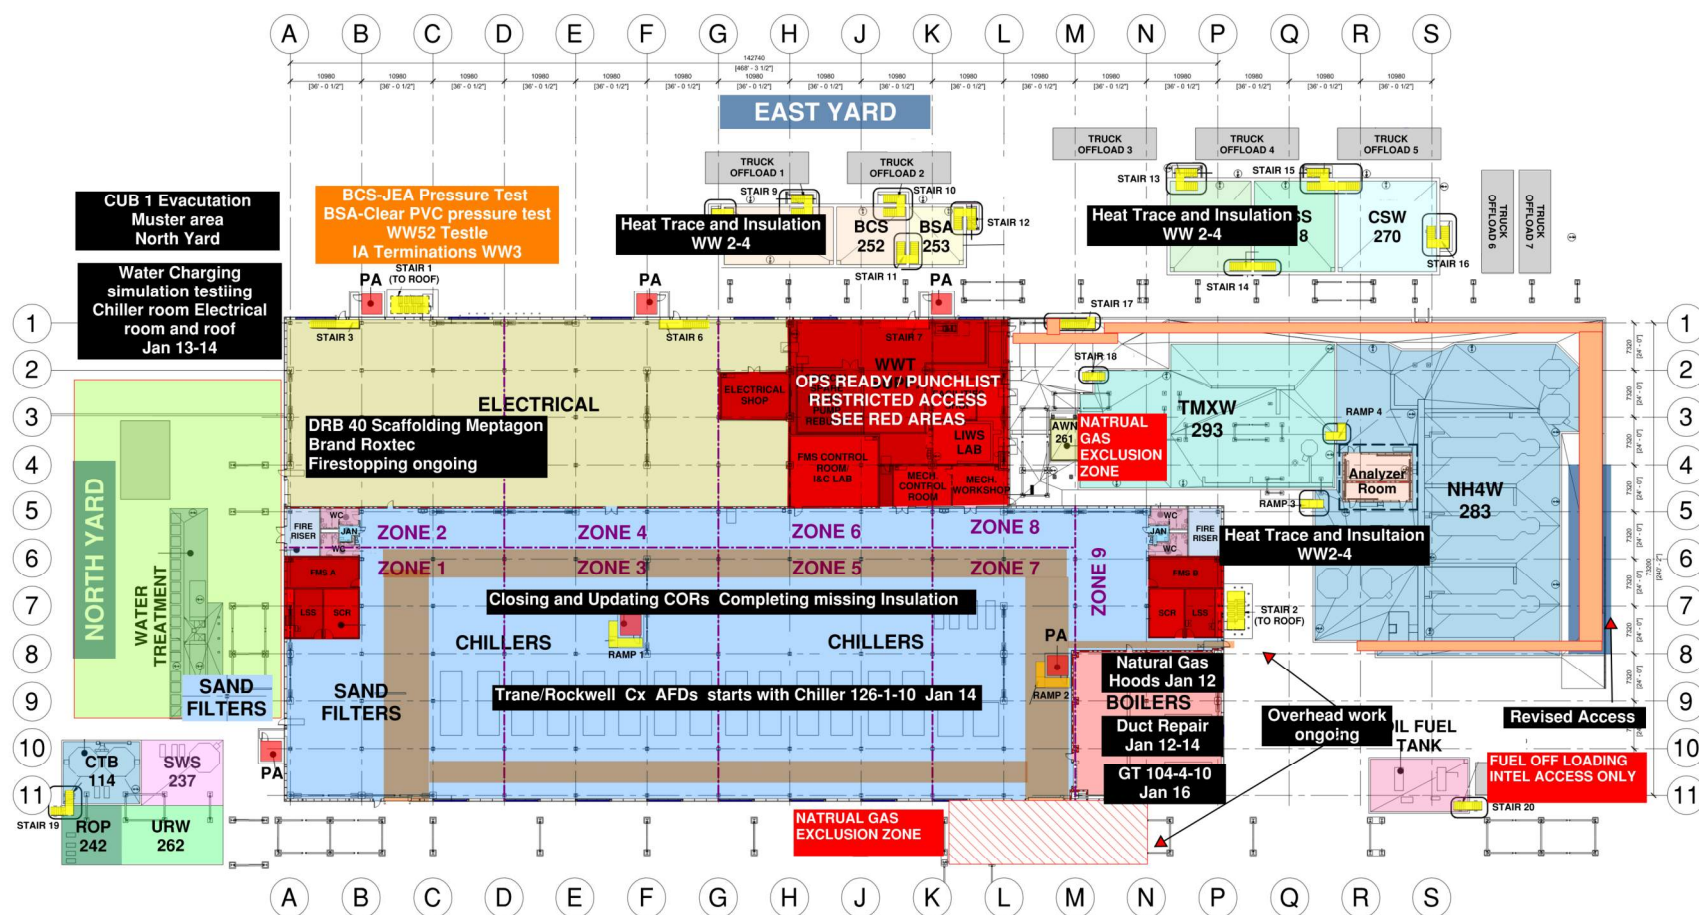


CUB 1 – EXTERIOR/ROOF

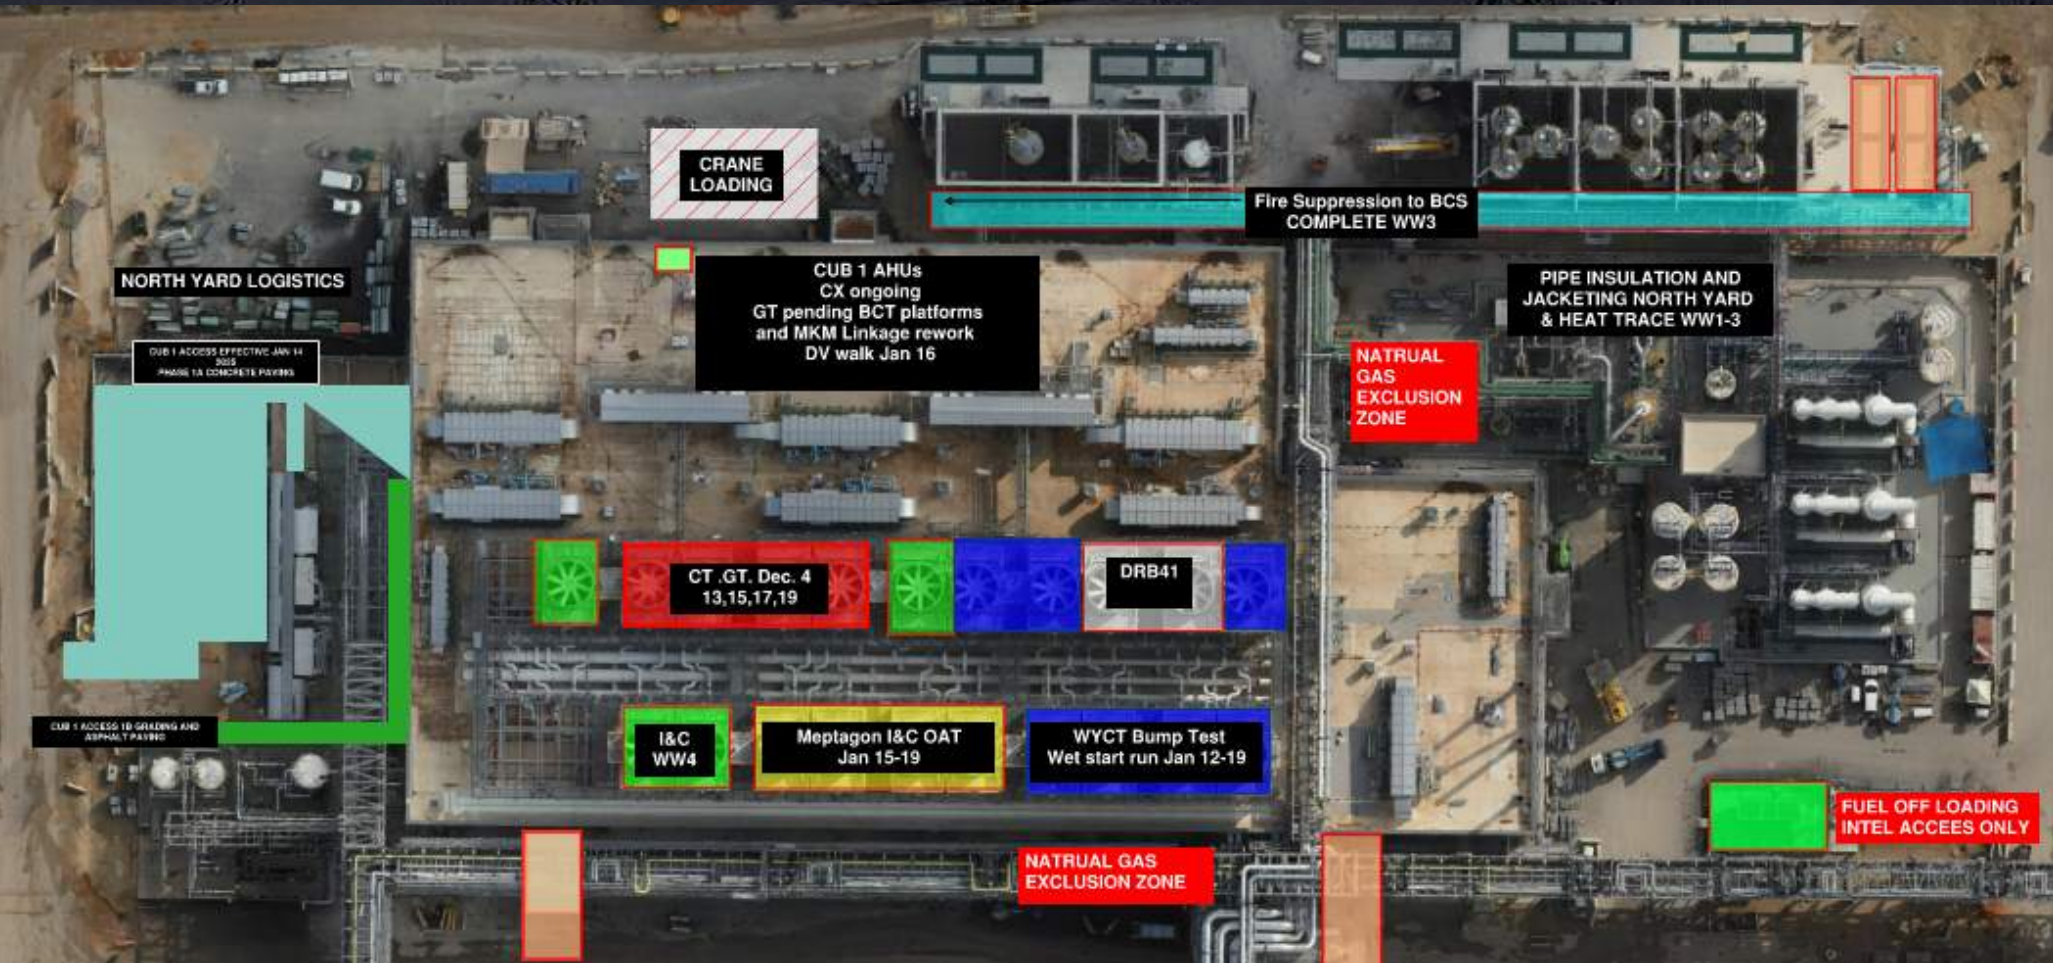


CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

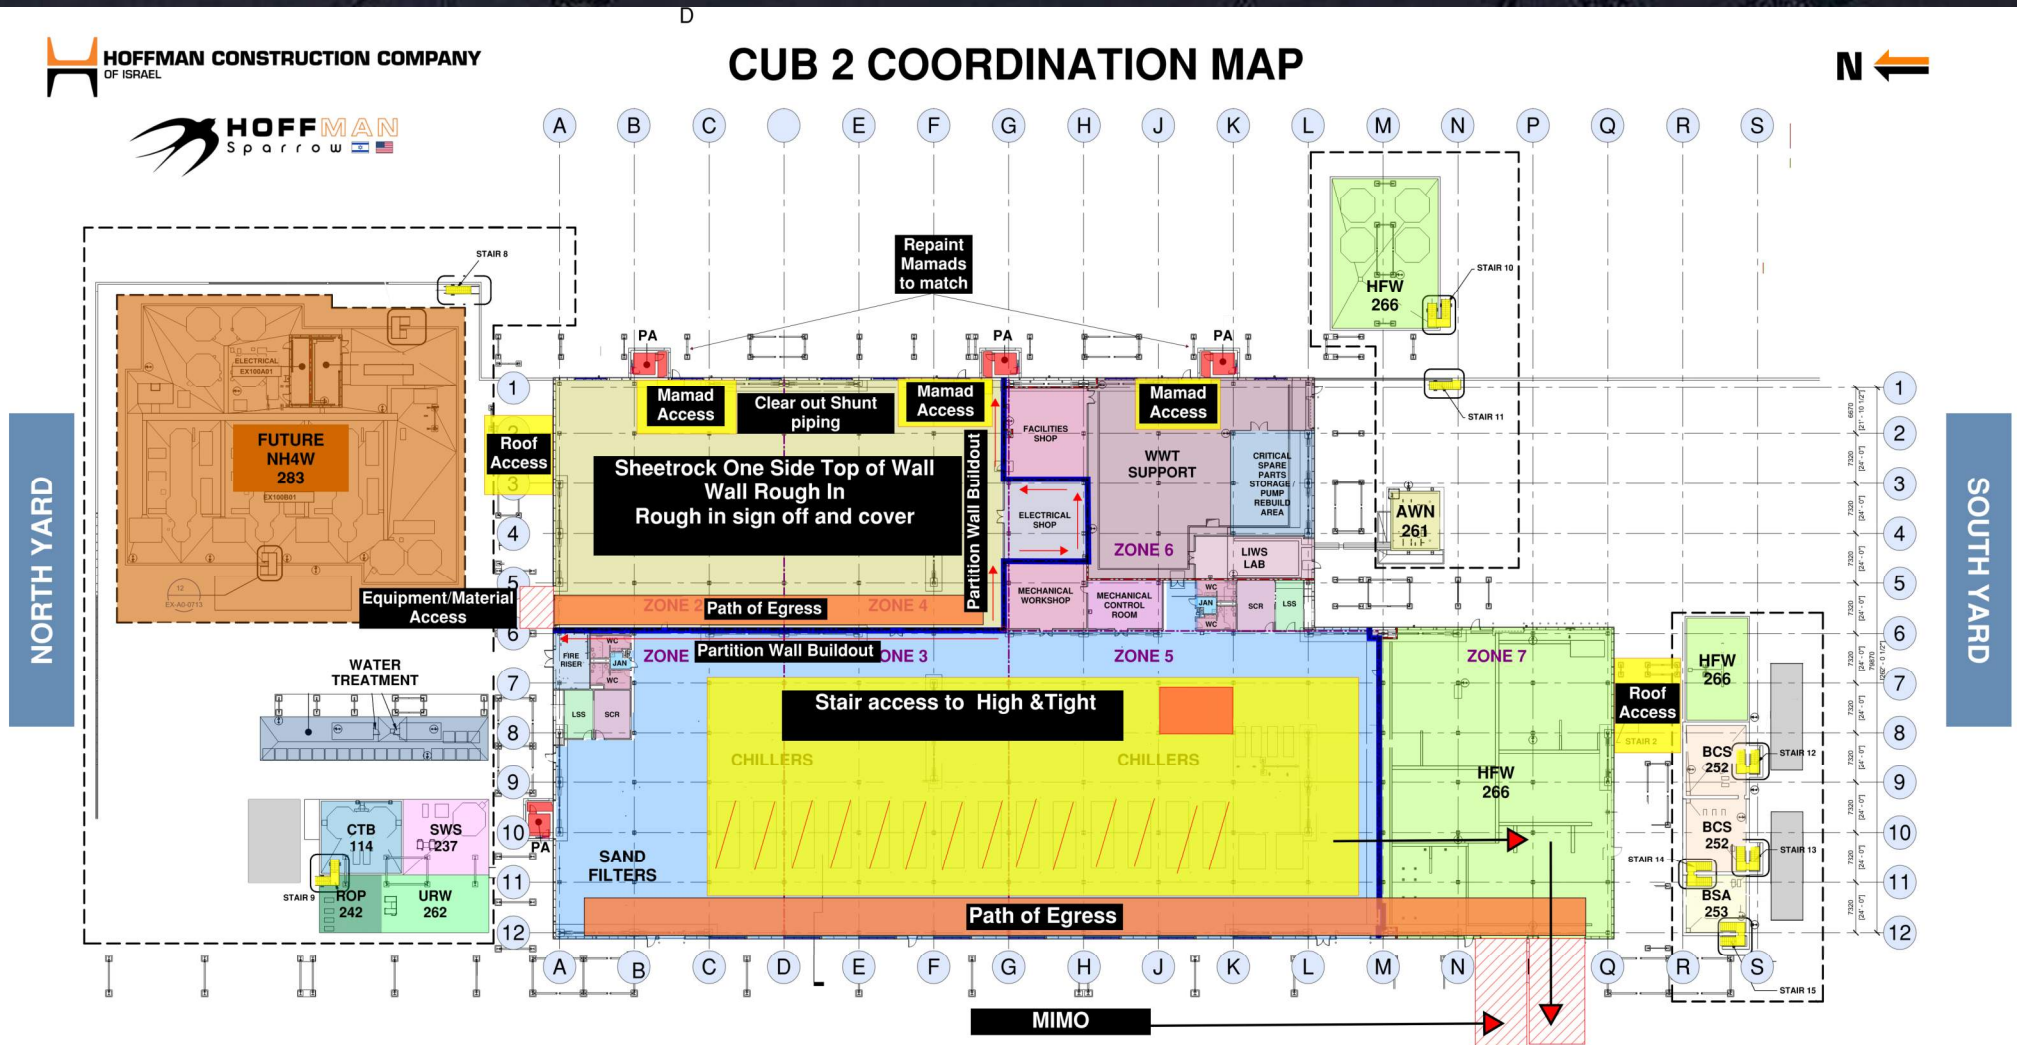



CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY

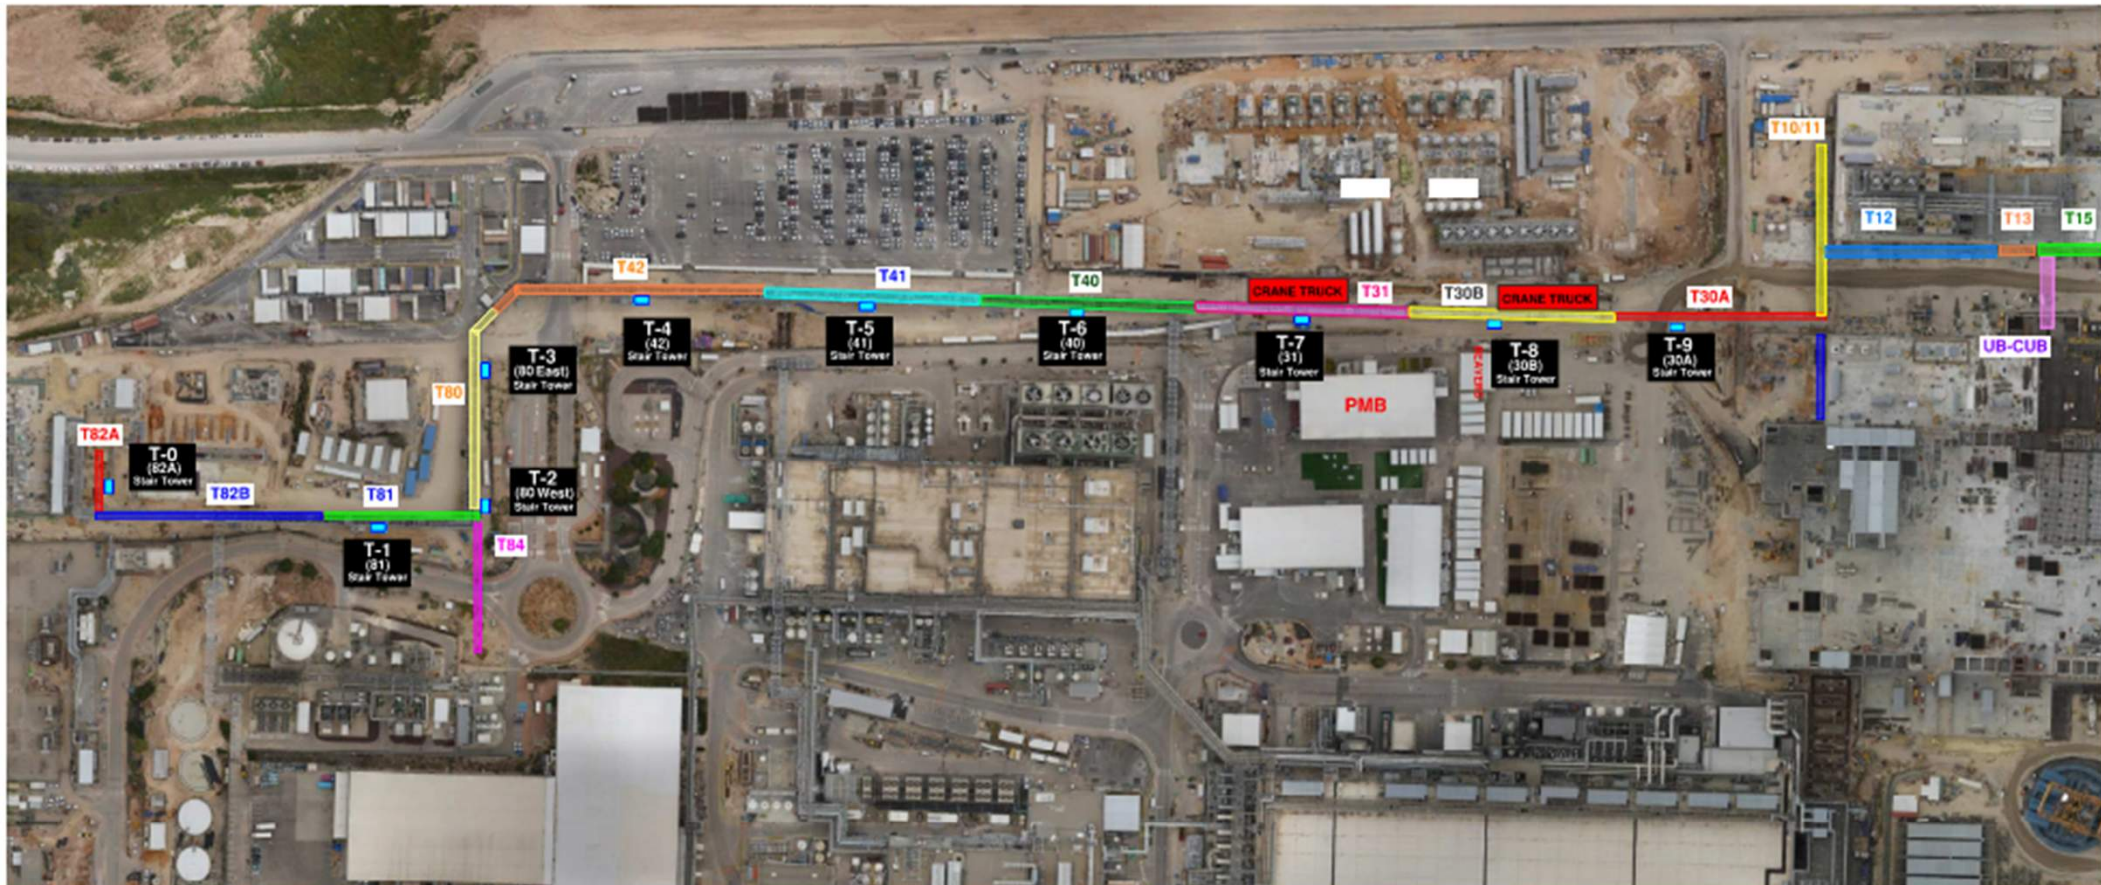



HOFFMAN CONSTRUCTION COMPANY




HOFFMAN
Sparrow  

SAMI NAJAMI – NDT RADIOGRAPHY OFA SYSTEM

AREA PLAN – TRESTLE: T-13 \ UB-CUB

WED 15/1/2025 22:00 - THU 16/1/2025 05:00

SNJ – NDT – OFA – 16" \ 20"

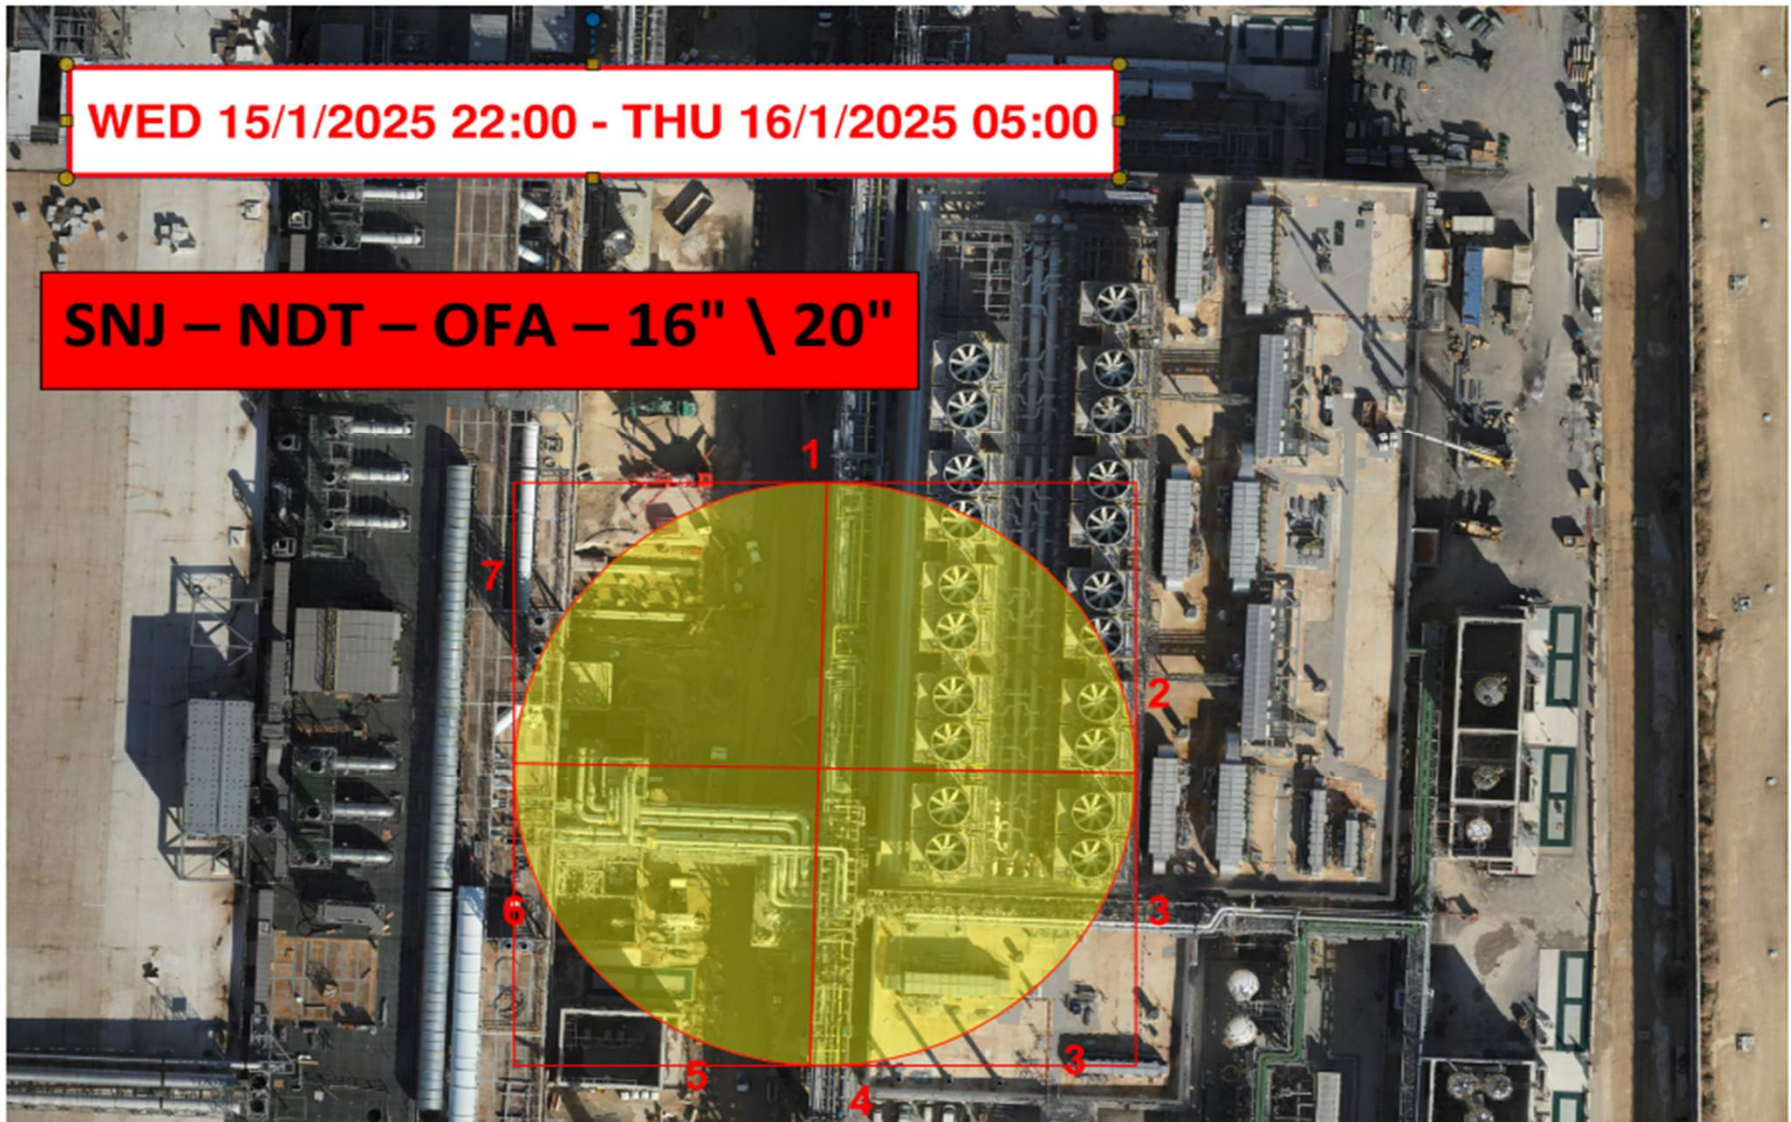




HOFFMAN CONSTRUCTION COMPANY



HOFFMAN
Sparrow  

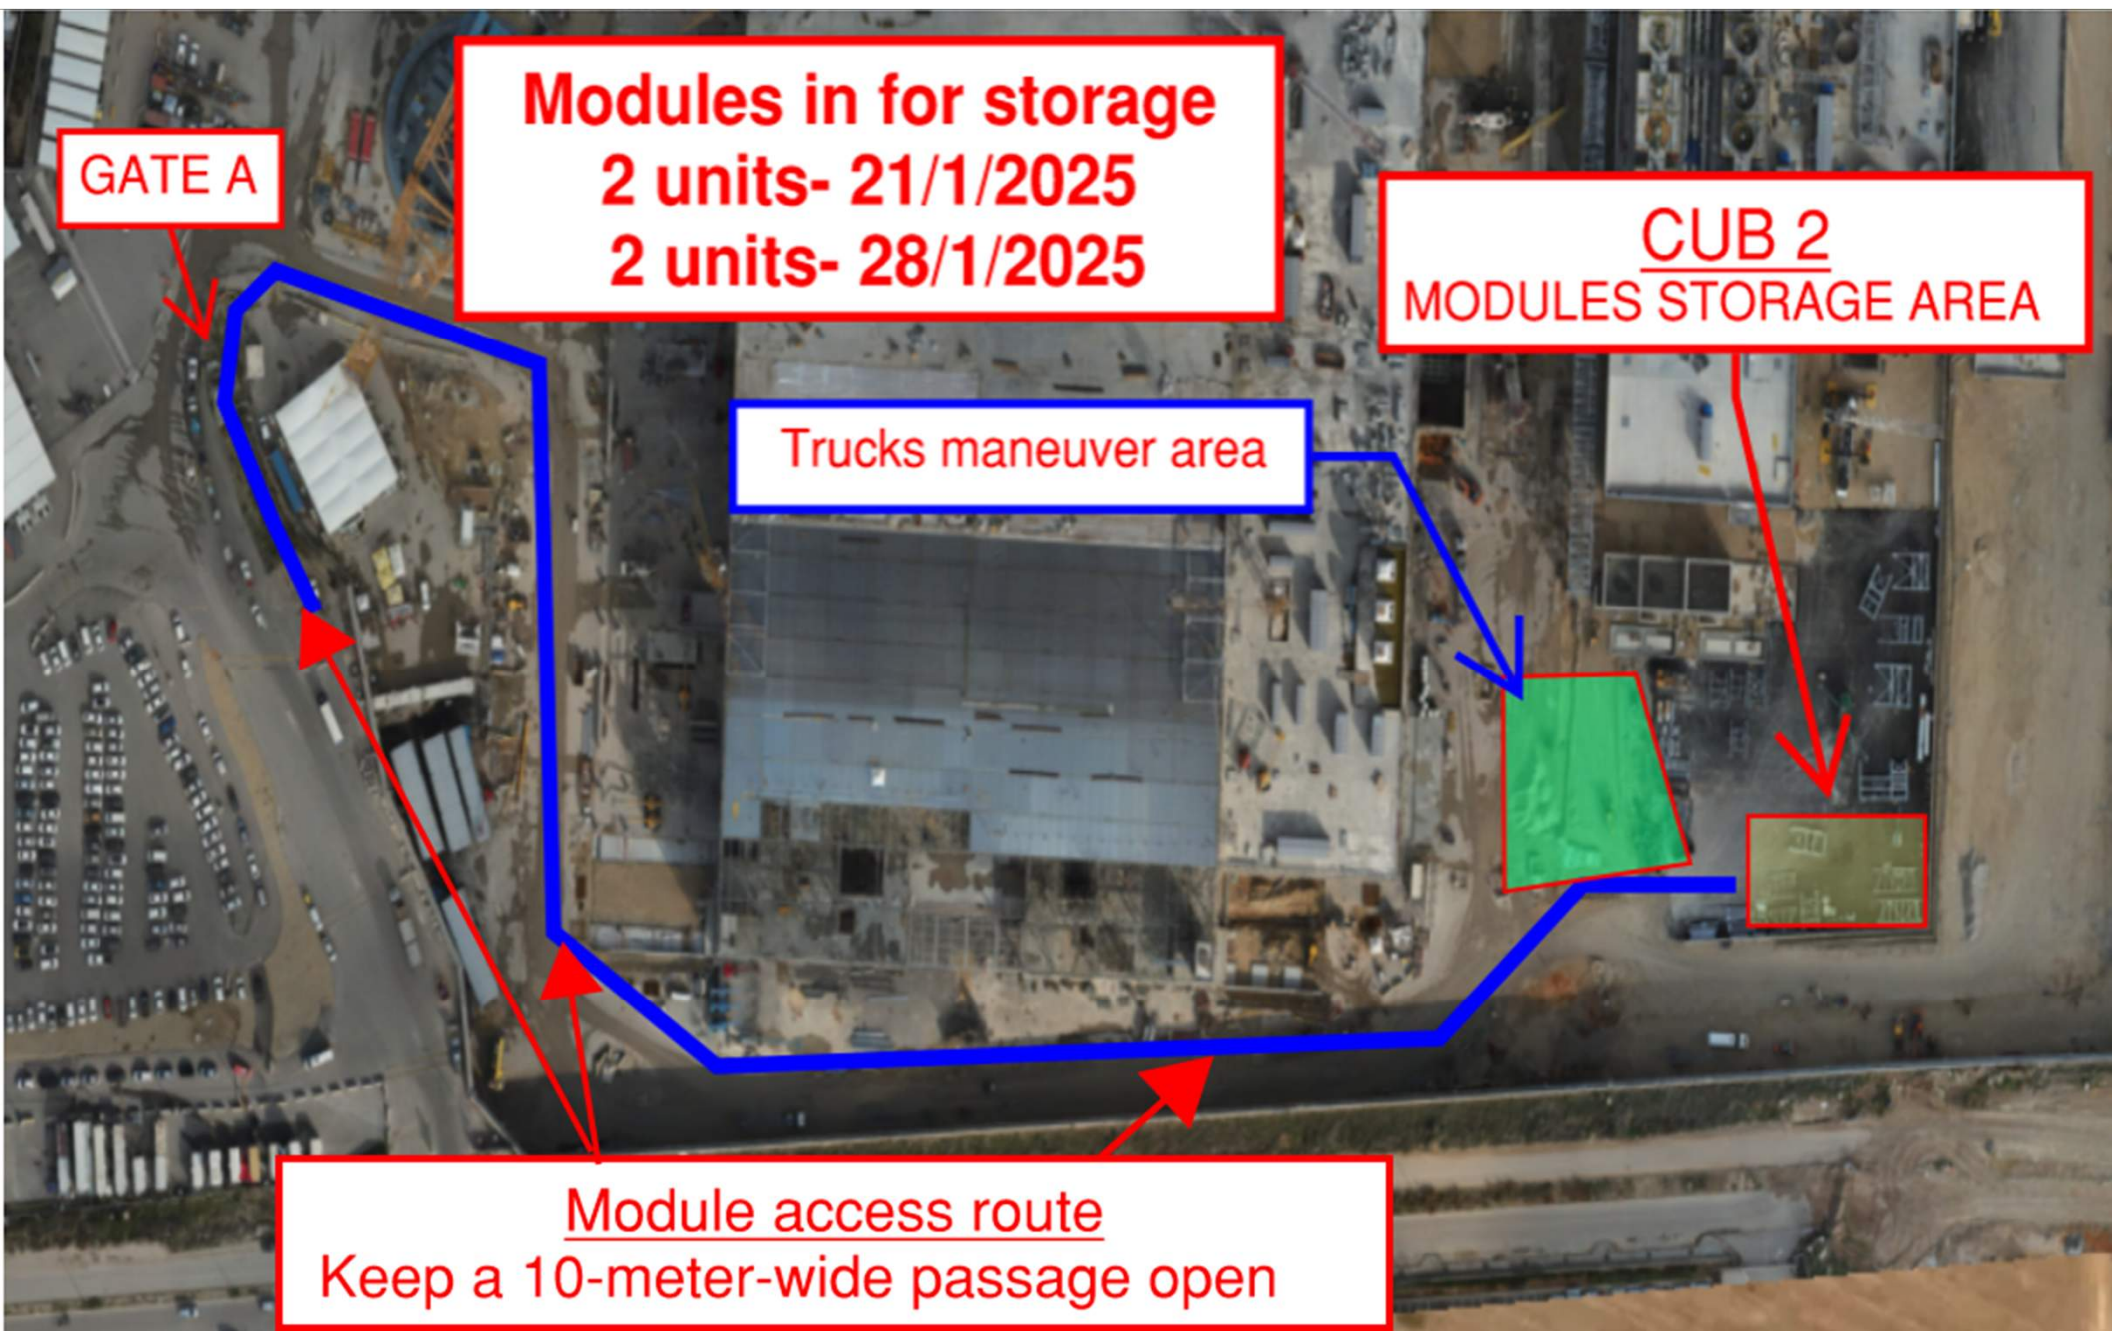

Modules in for storage
2 units- 21/1/2025
2 units- 28/1/2025

GATE A

CUB 2
MODULES STORAGE AREA

Trucks maneuver area

Module access route
Keep a 10-meter-wide passage open




HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics North

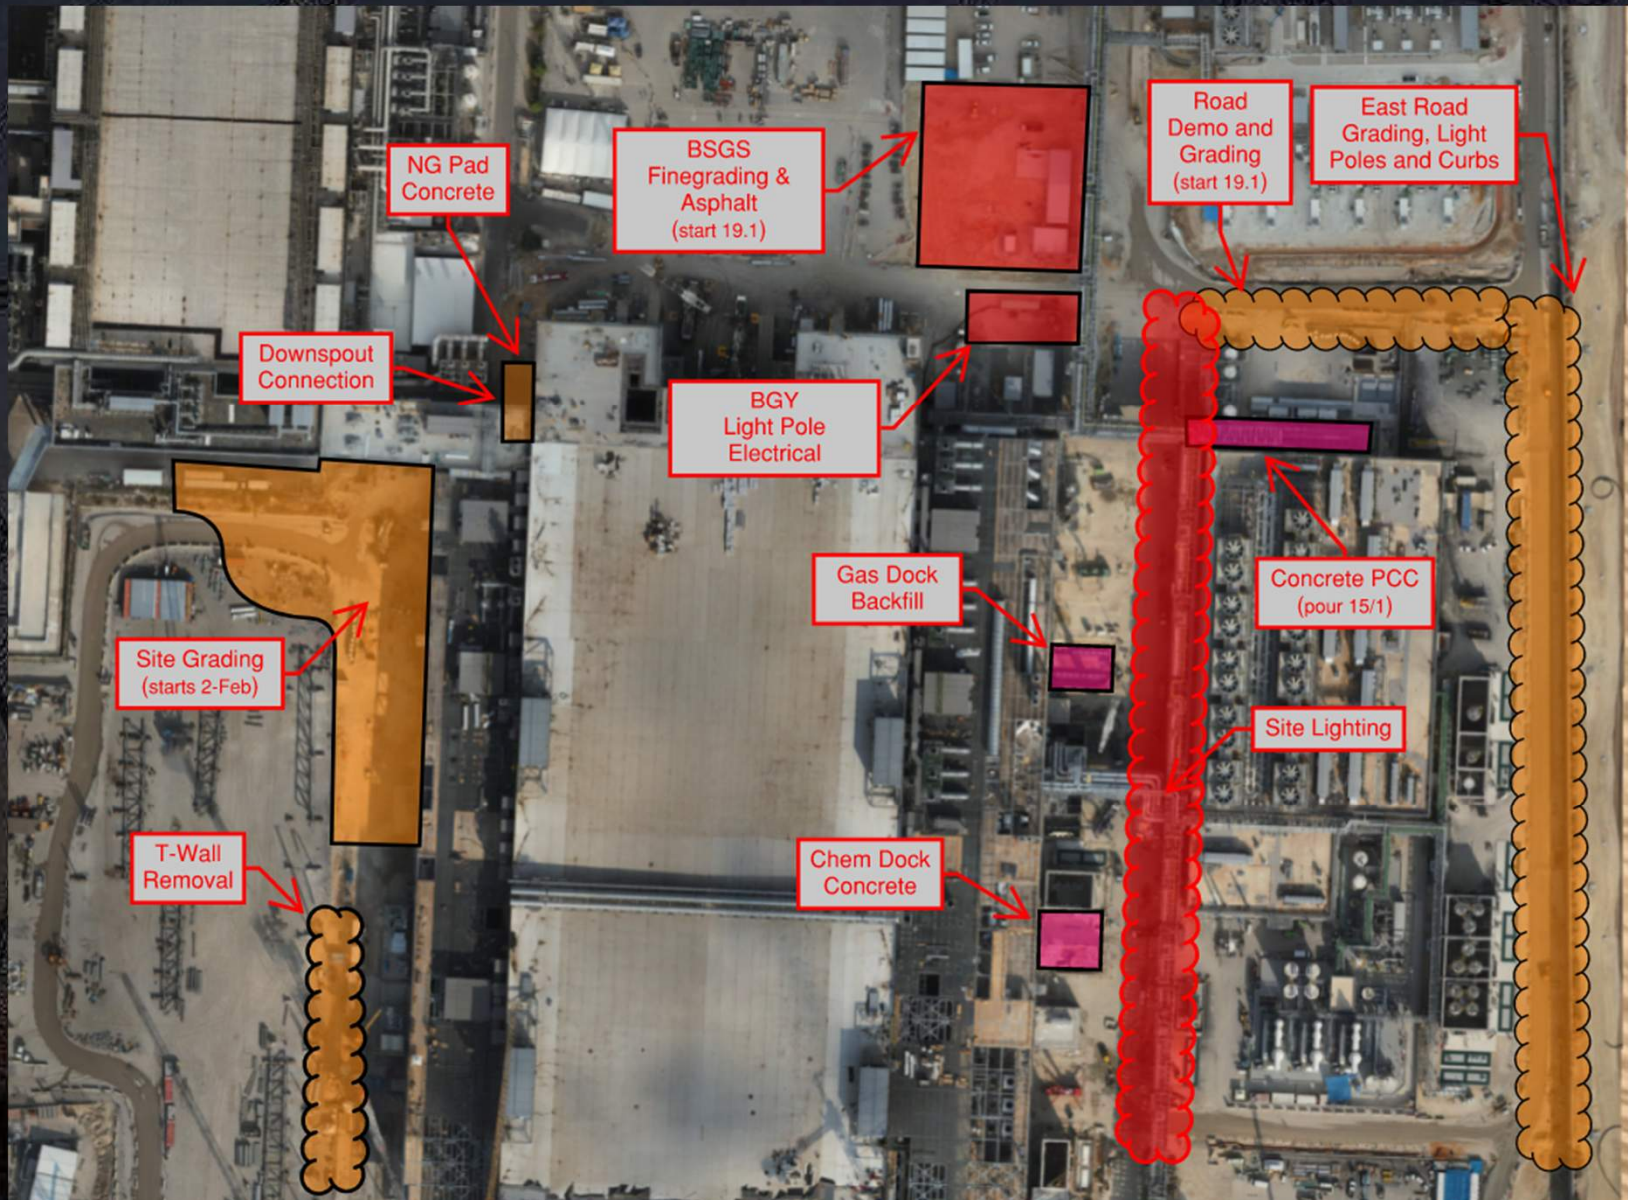



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
South



LOTO- Not Optional

- If a person is working on a system that COULD be energized, the sources must be locked out and tagged out by each person that is working on that system.
- Each person must have their own lock, that only has 1 key to it, and that lock must be red.
- Each lock must have a tag with the contact information for the person that placed the lock.
- Red locks must be removed by the end of the shift.
- If a system needs to be locked out for control, or for longer than 1 shift a yellow control lock must be used instead.
- This is a life saving program and is not optional.

HCC/EHS Weekend Work- 17.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

Zac Ross - 052-7582746

Tamir Hamo - 052-6230917

Yehuda Cohen - 052-3614292

Jimmy S

CSA CM

Girum Abay - 052-2237784

Nick Gividen - 052-3434754

Pauric O'Reilly - 052-3571665

Andrew Thomas - 052-3453815

Patrick Blunt - 052-3155787

Dave B

MEP

David sooter - 052-4121028

Cx

Cranes

Safety

- Safety Foreman - Rami Al Jaar 052-6169466 Rami-AlJaar@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 10.01.2025

FAB

Utility Level / Roof / Stair Shaft

Subfab

- Pach Taas
 - W-E Perimeter
 - Andrey 0502998167
- Afcon E
 - All over SF
 - Avi Eli: 0526008487
- Chemo
 - TTNE/TTNW
 - Tomi: 0523759408
- MEGASON
 - 7E
 - Israel 0526869393
- SELA
 - 5E,5W
 - David 0524382997

Clean Room

- Talad – 10 guys CR 2 W-Lids removal, 1W- Ceiling install, 3E-PVC cover (EHS Marcelo 0523540242, Super Igor 0544509386)
- Sig – 14 GUYS Mod1 – Scaffold removal, MOD2- 17 line (EHS Beni 0506232032, Super Shmulik 0549205966)
- Afcon – 20 guys CR – 2E boxes 2W module, , 3E lighting, 1W -1E cable pUlling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- Rolling Plains – 20 guys INT NWTT 5RA, Marshaft 4W, 5RA, MOD2 CA CH 17,24,10 (Super oleg +353873794553 , 0542689370 , EHS MARCOV 0546596857)
- Chemo –16 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Sela – 8 2E CRC (Supervisor David 0524382997, EHS Samuel 0506306031)
- D&p - 40 guys Freddie Hazan 0503827885
- Pach Taas 3 guys, BF-CA 17 Line
- Talent 1E-1W – Maintenance , 2E- Superclean (Super Yosi 0526557130, EHS Evgeniy 0543053595)

Subcontractor Weekend Work- 10.01.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- SK Engineering – GL4 UL Piping, 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112

WJG

- Afcon – Lift 2 and Utility Level Cable Tray
Foreman: Montu 055 911 6973
Safety: Pradeep 055 274 2935
- Chemo: 2J Utility Level, 4J/5J Lift 2 Piping (Hot Work)
Foreman: Maor 050 988 9071
Safety: Erez 054 971 6840
- Pach Taas: All over (HRA)
Foreman: Tomer 050 767 0585
Safety: Jad 050 5405016

Subcontractor Weekend Work- 10.01.2025

CUB

D&P:

Constantin - 0545501602
David - 0548894447

Sami Najami:

Husein - 0526917461
Barak - 0542262530

Chemo:

Dudu - 0509808846
Leonid - 0548883878

HSAI:

Sergey - 0552728807

Trestle

SNJ:

PIPES –T40 - UB CUB - 13 workers (3 teams)
STEEL –Galvanized paint + T30 A+B - 8 workers (2 teams)
Steel adjustment - 15 workers (3 teams)
FORMAN
Adiv asaly- 0526017477
SAFETY TRESTLE
Barak mesica tel. 0542262530

Stage Design

Scaffolding – T40-T30 UB CUB – 8 WORKERS
FORMAN
Doron kadan – 0502682680
SAFETY TRESTLE
Osama - 0522851458

Siding

Site

Derech Afar – Shotcrete wall
Supervision = Raed: 054-244203
EHS = Alex: 054-5403849

Olizki – Offload 18 & CUB1 trench drains, Southeast CUB1 grading
Supervision = Or: 052-4917313
EHS = Ben: 052-4033565

Afcon – BGY Electrical
Supervision = Tomer:
EHS =

Daily Coordination Meeting



14:00 Sign In
