

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:

- Buildings becoming cleaner = less materials, no piles of trash, smoke eaters required, etc.

NWTT Roof @ 11:00 pm

Mod1 roof pourbacks to follow


NWTT roof
@ 11:00 pm

אינטל קרית גת

FAB-28


UTILITY LEVEL P.Test

SK
Press. Test
9/19
From 17:00

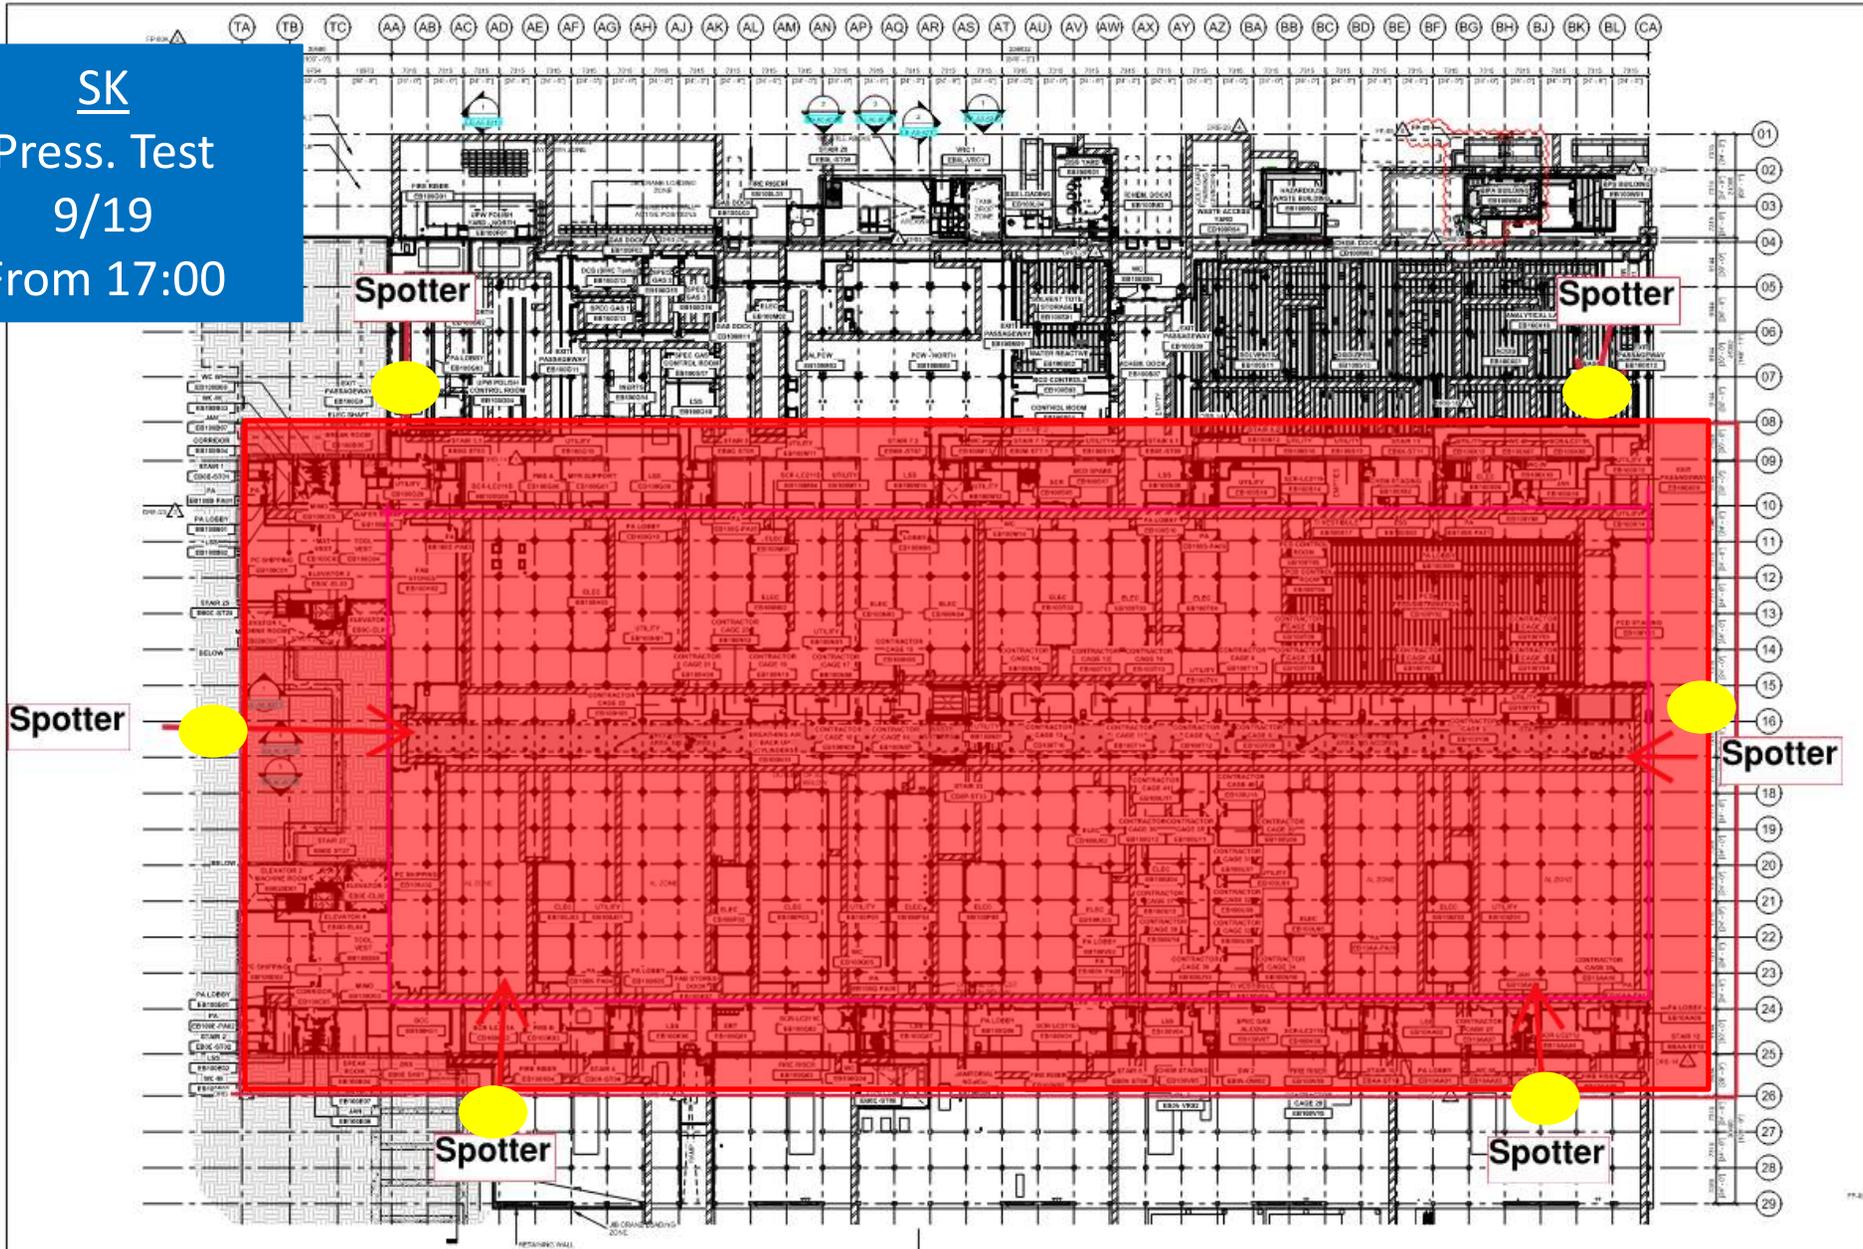



UTILITY LEVEL MOD1

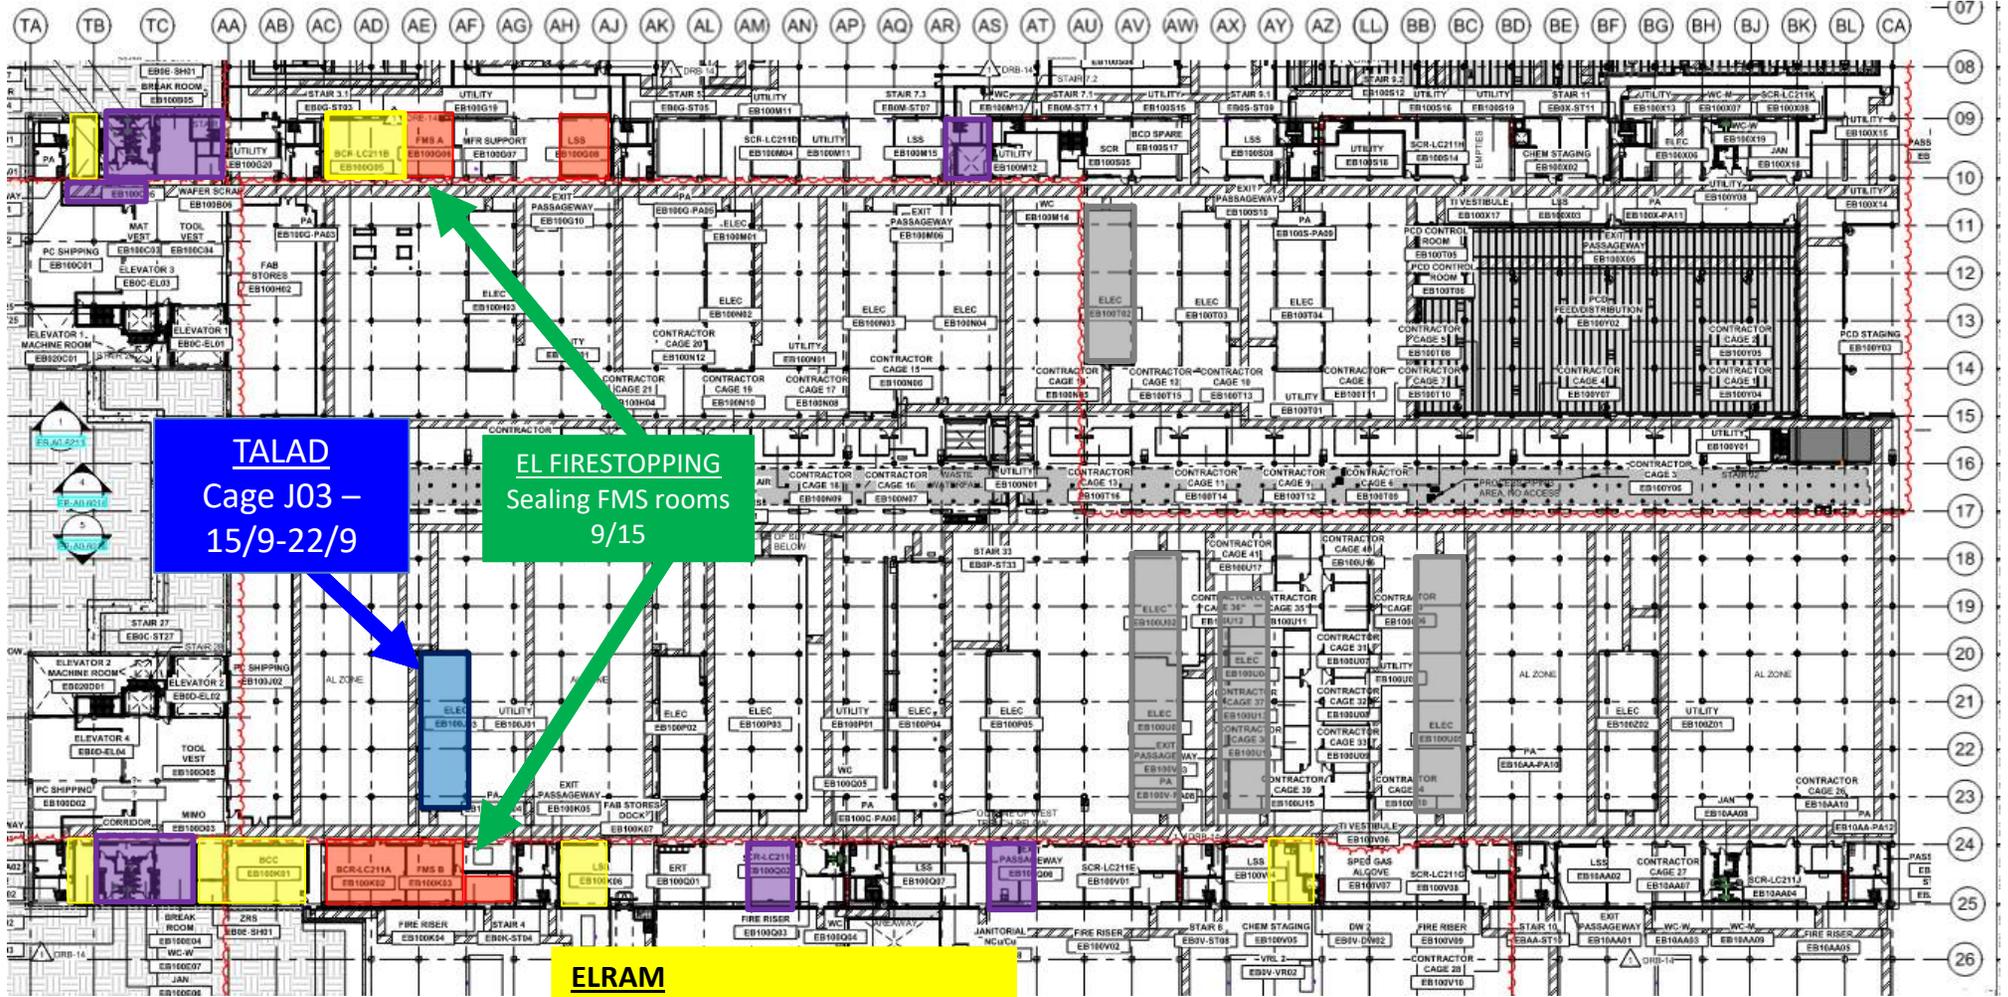

TALAD
Cage J03 –
15/9-22/9


EL FIRESTOPPING
Sealing FMS rooms
9/15

BELFOR
TTNE - Corridor + Toilets + Break R
Stairs 7.3
Wafer scrap
TTNW - Toilets + Break R
SCR 2W
Exit pass 3W

ELRAM
Ongoing
LSS TTNW + TTNE
BCR 1E
CHEN STAGING
LSS 2W
Chem staging
BACKING
BCR 1E+1W – Pending funding
LSS's

MEP+Elctrical
Ready for re-install
FMS A 1E
FMS B 1W
Fire Risers 1W
BCC


UTILITY LEVEL MOD2

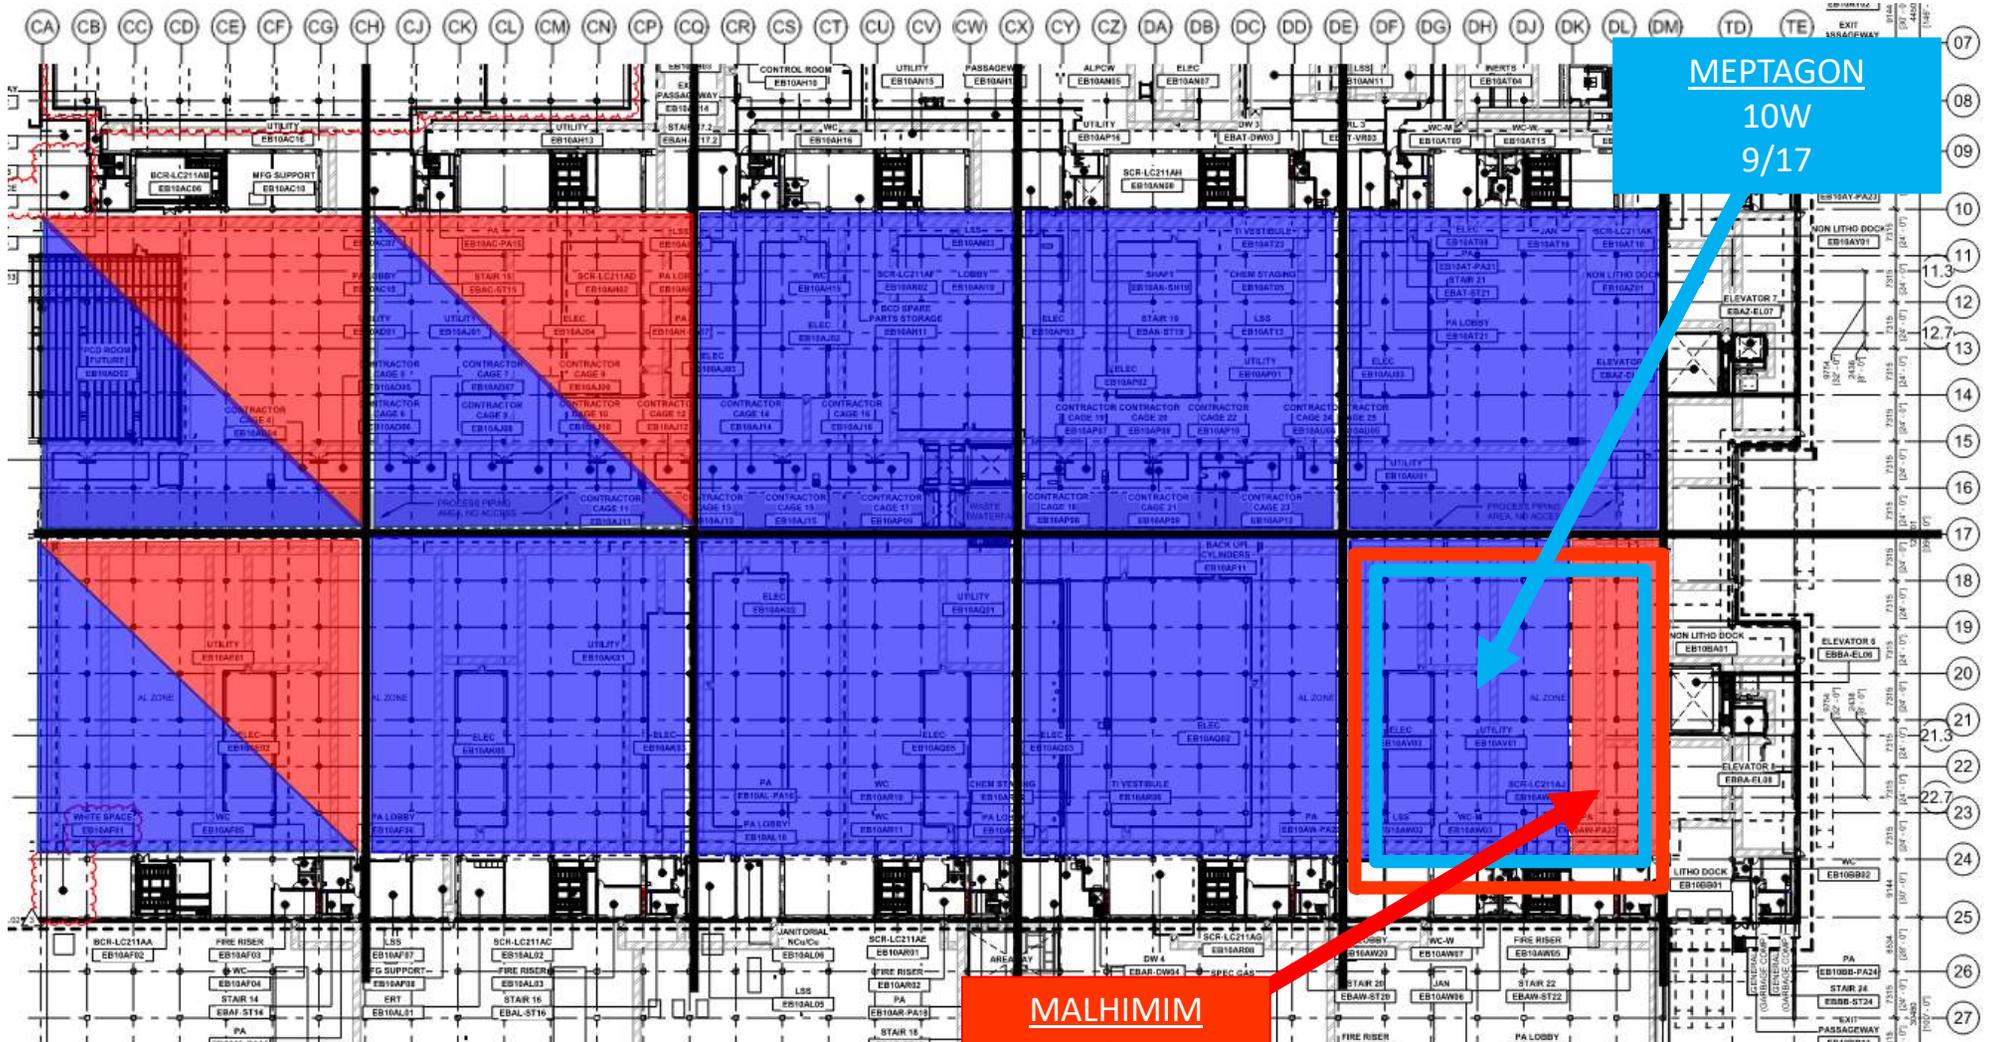

MEPTAGON
10W
9/17

MALHIMIM
10W
Sprinklers install
9/17

SUT 38.1 LEVEL

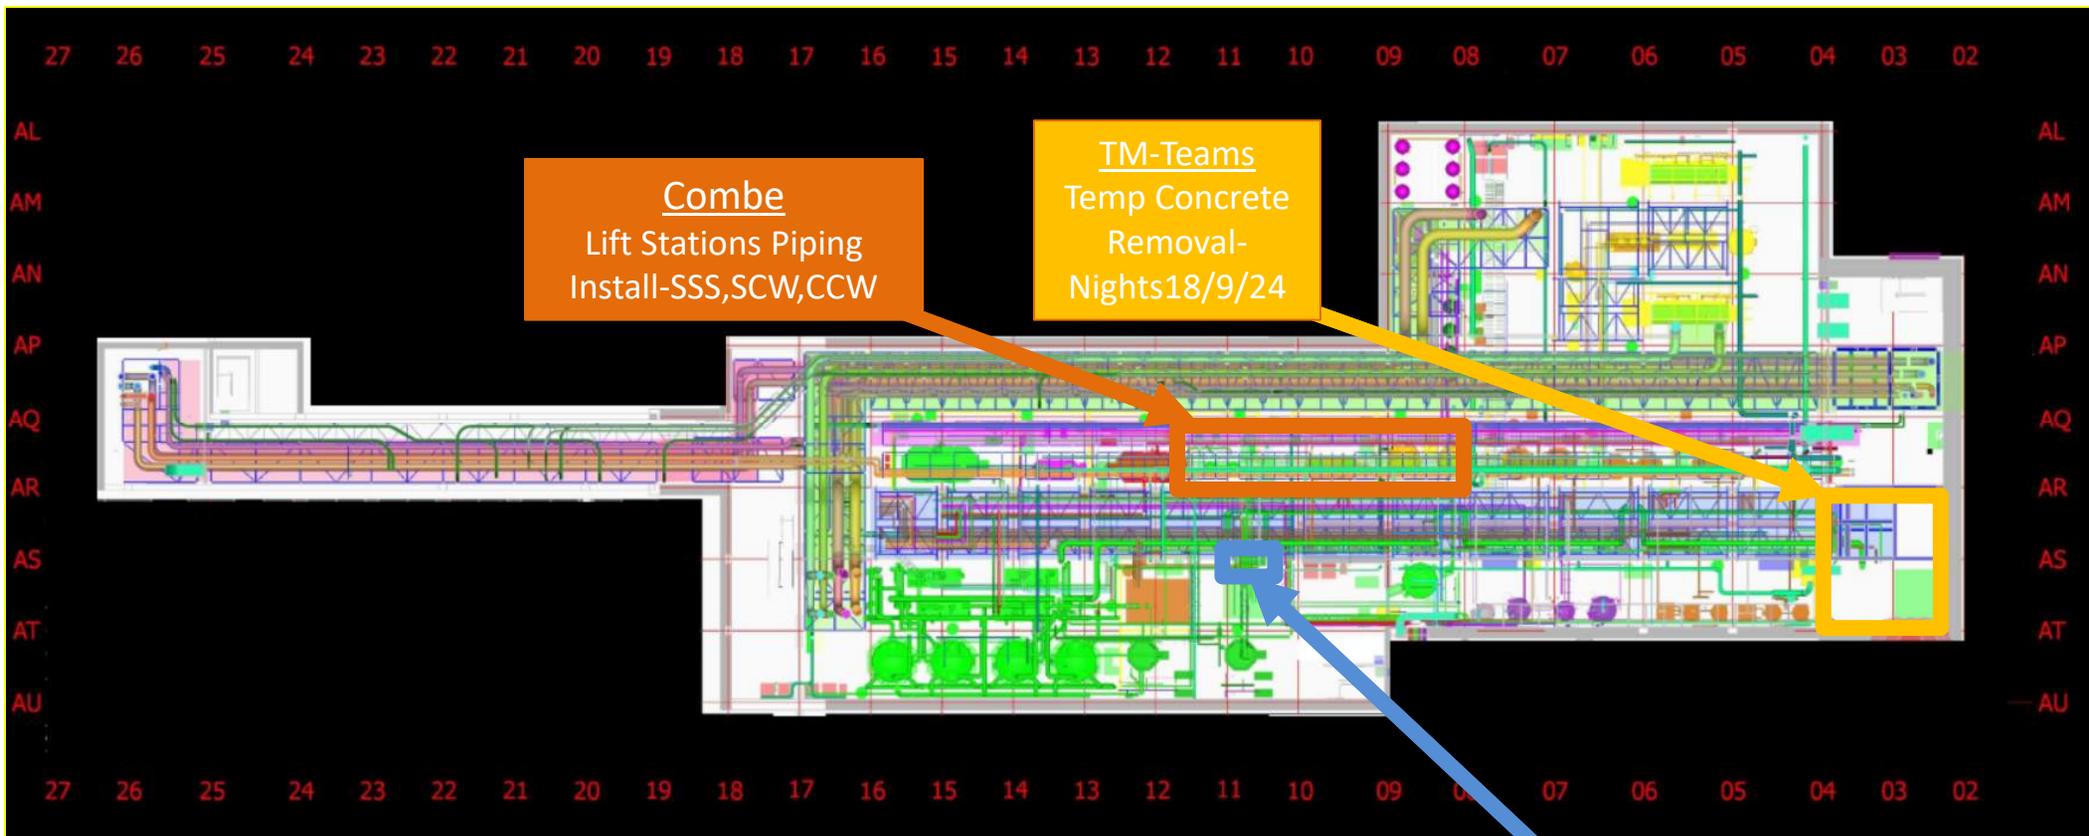


Combe
Lift Stations Piping
Install-SSS,SCW,CCW

TM-Teams
Temp Concrete
Removal-
Nights18/9/24

Sela
Biocide curb - CRC
15/9/24- 19/9/24

SUT 38.2 LEVEL

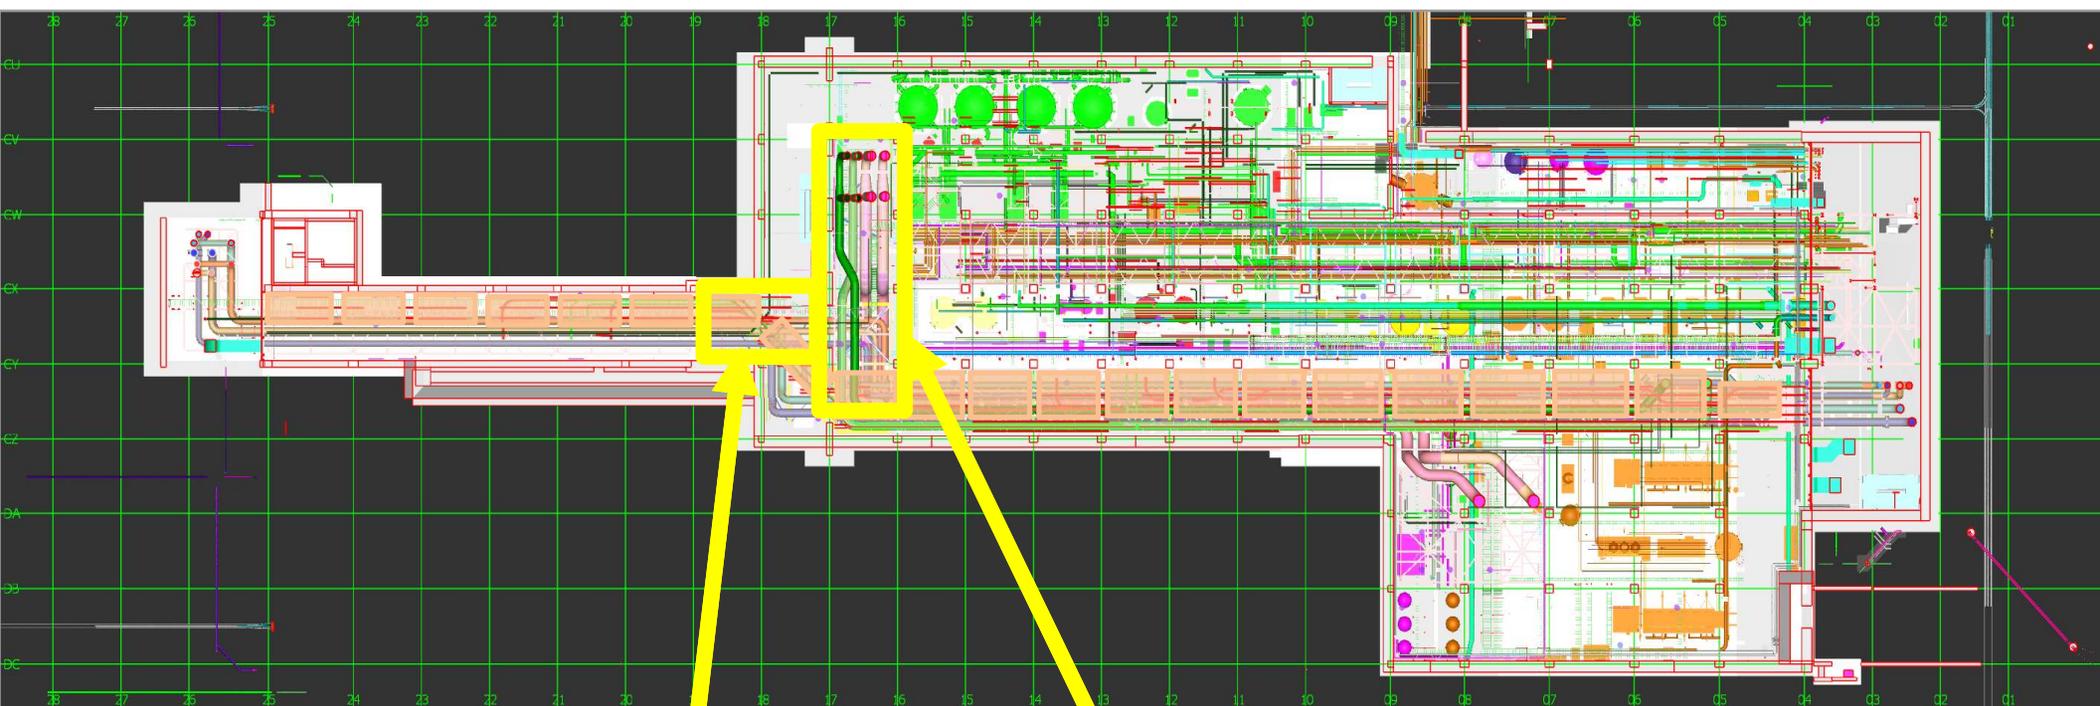


CRW
H&T
NEED PIPING

17-18 line
Bore Loading


16-17 line
lvl2+3
bed lift: Need a
Date

Vesda
H&T
Not actively installing


SUBFAB CRC TOPCOAT

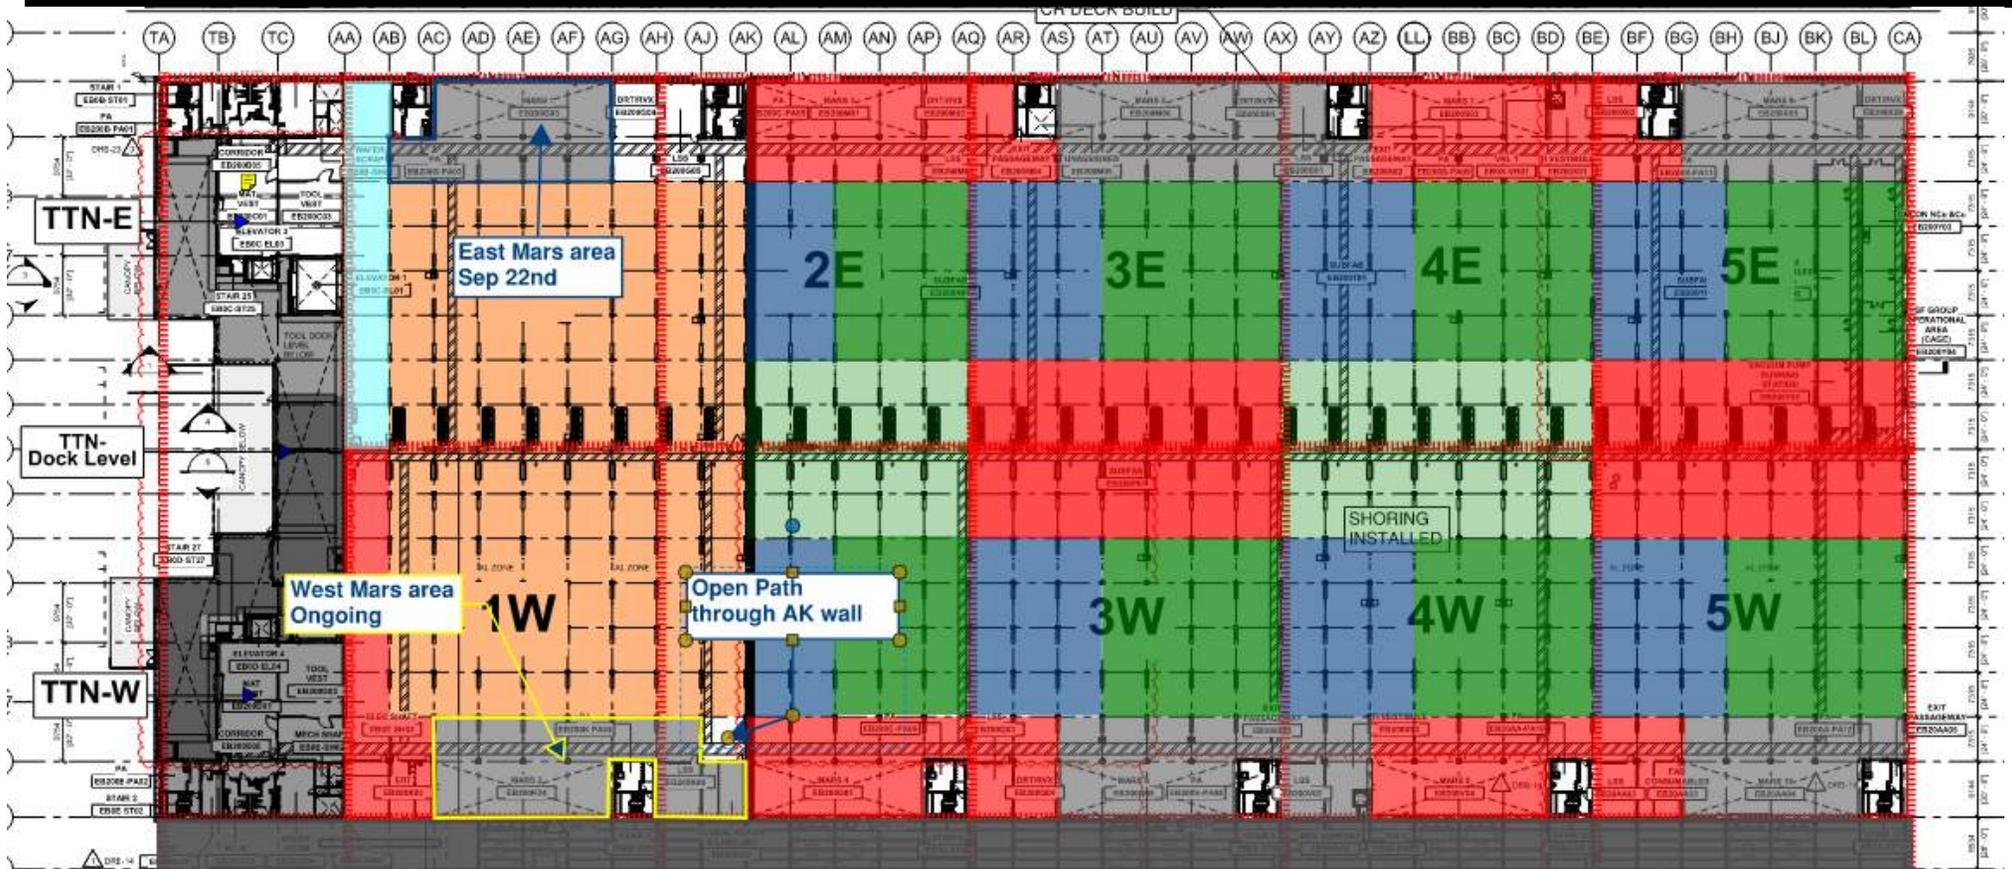


SUBFUB PRESSURE TEST EXCLUSION ZONES

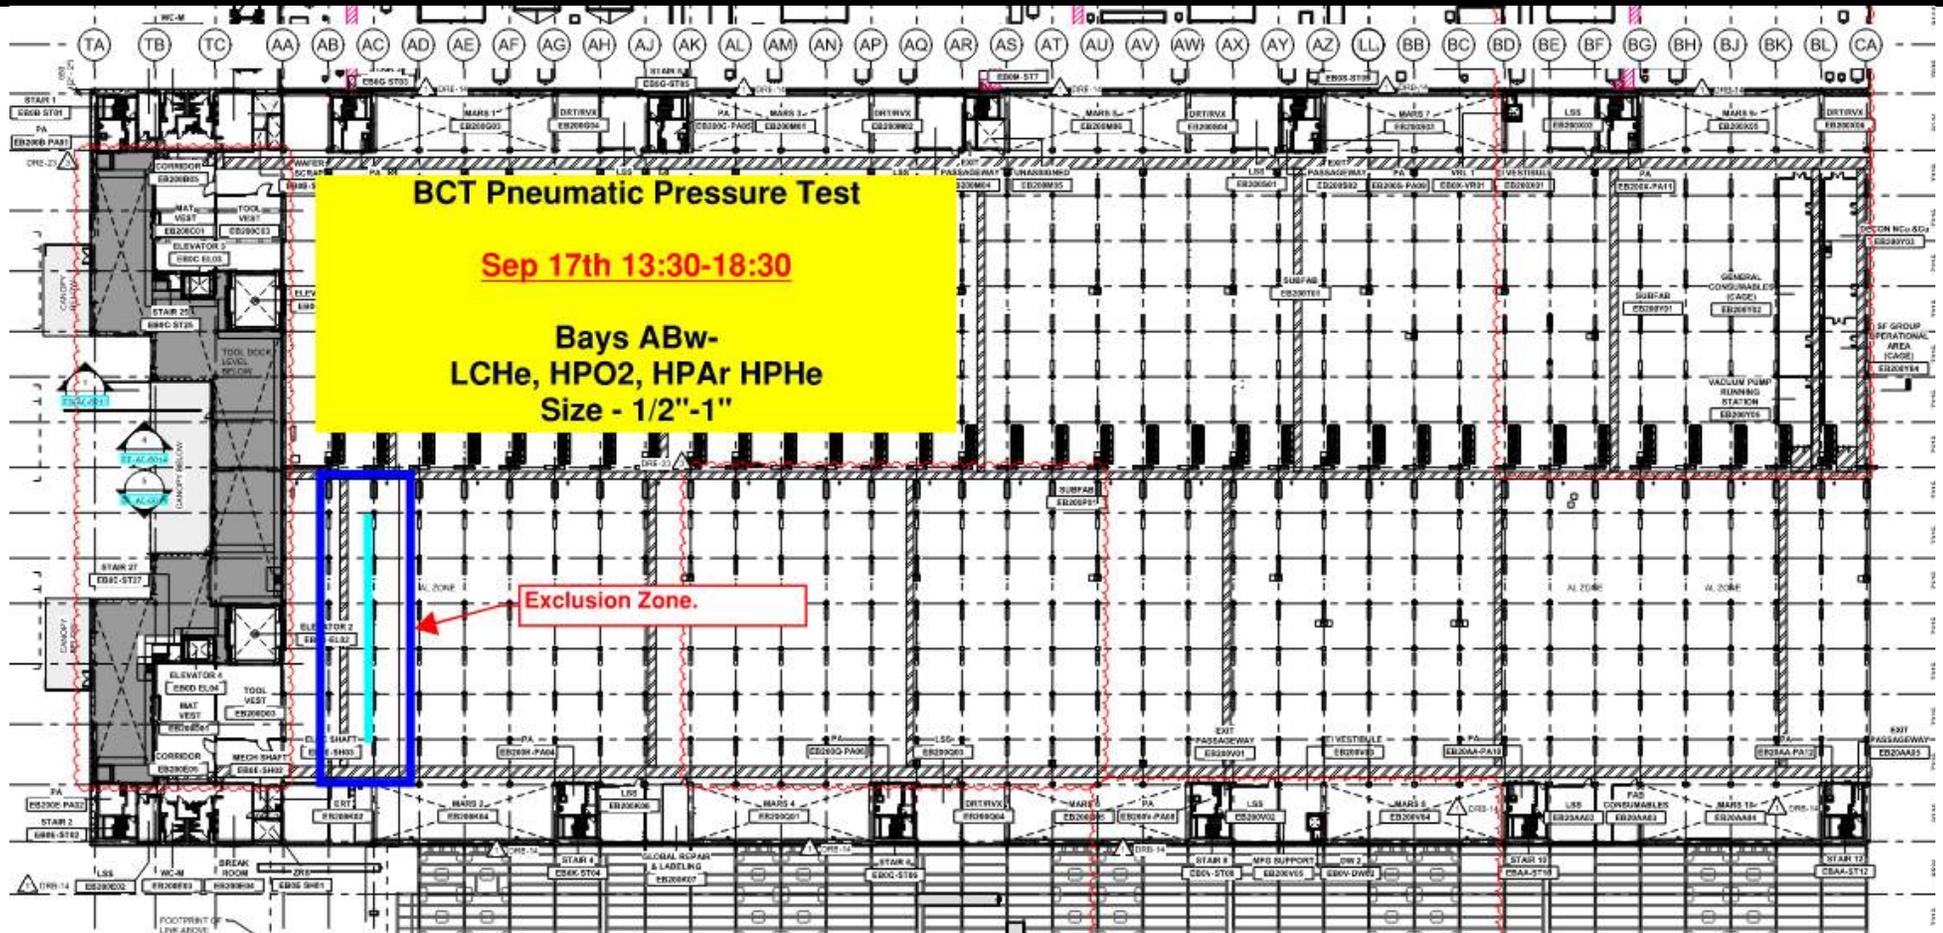


SUBFAB PRESSURE TEST EXCLUSION ZONES

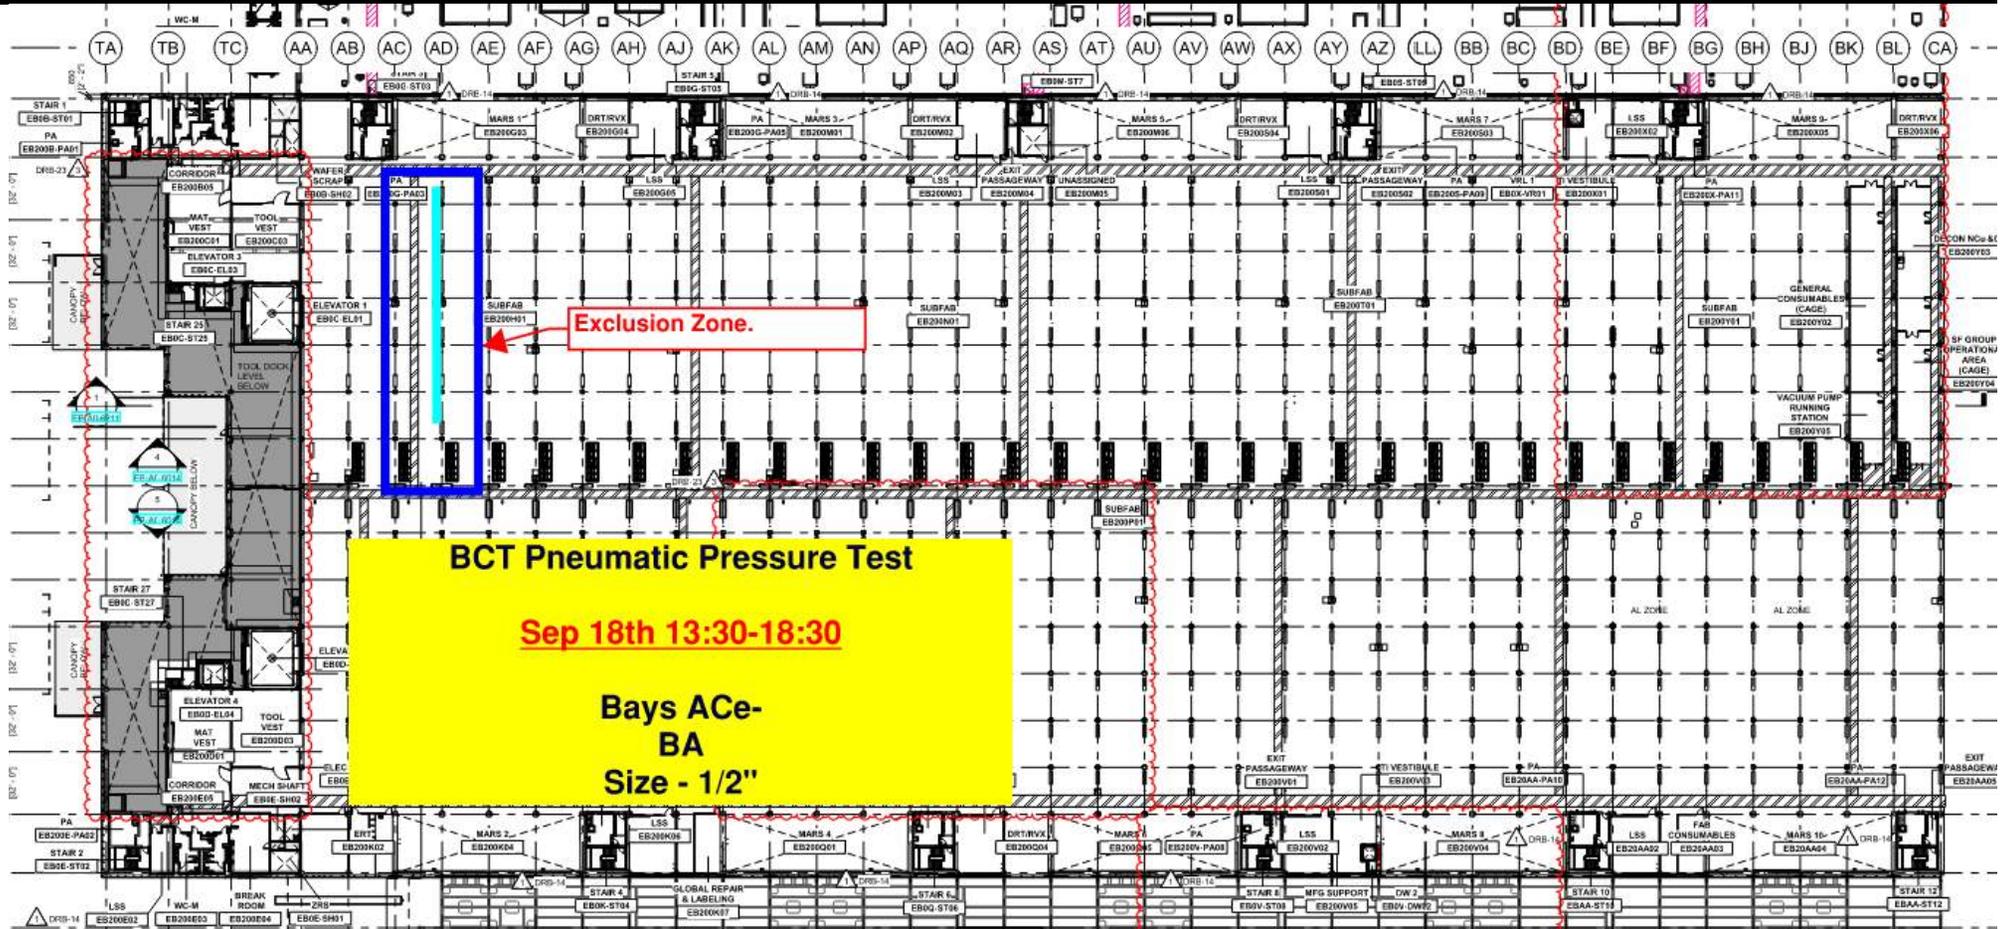


SUBFAB BUILDOUT MOD 2

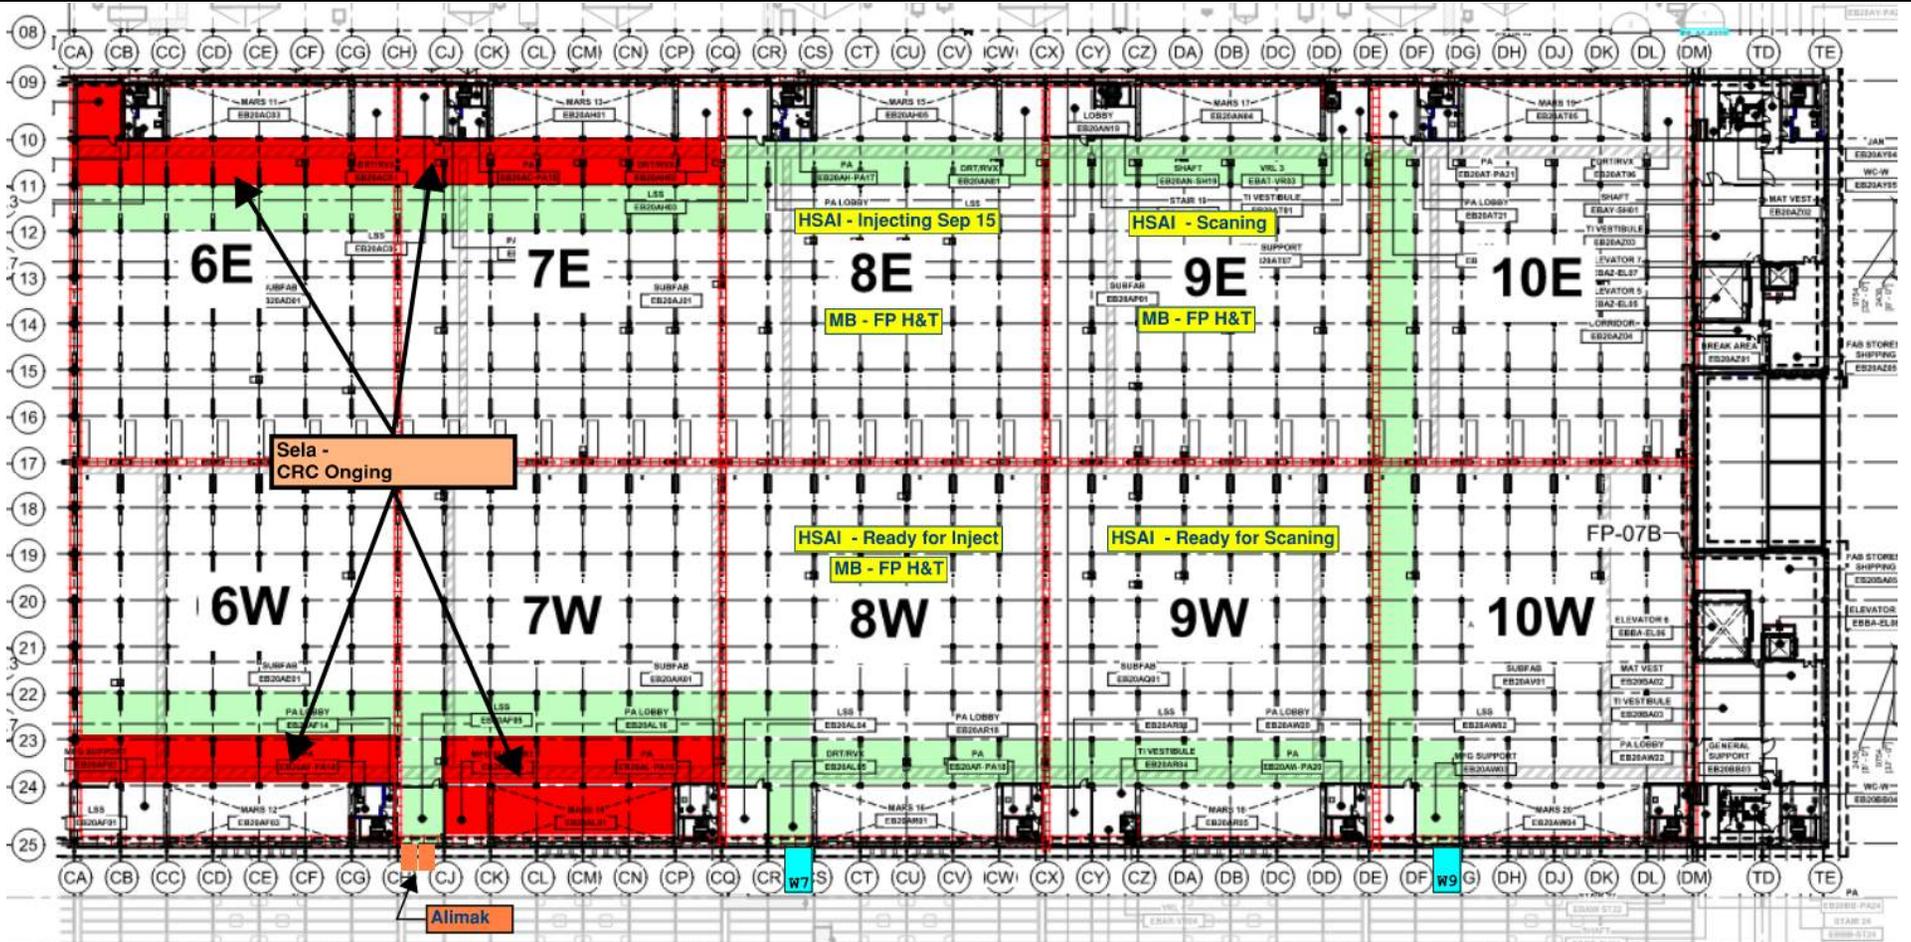

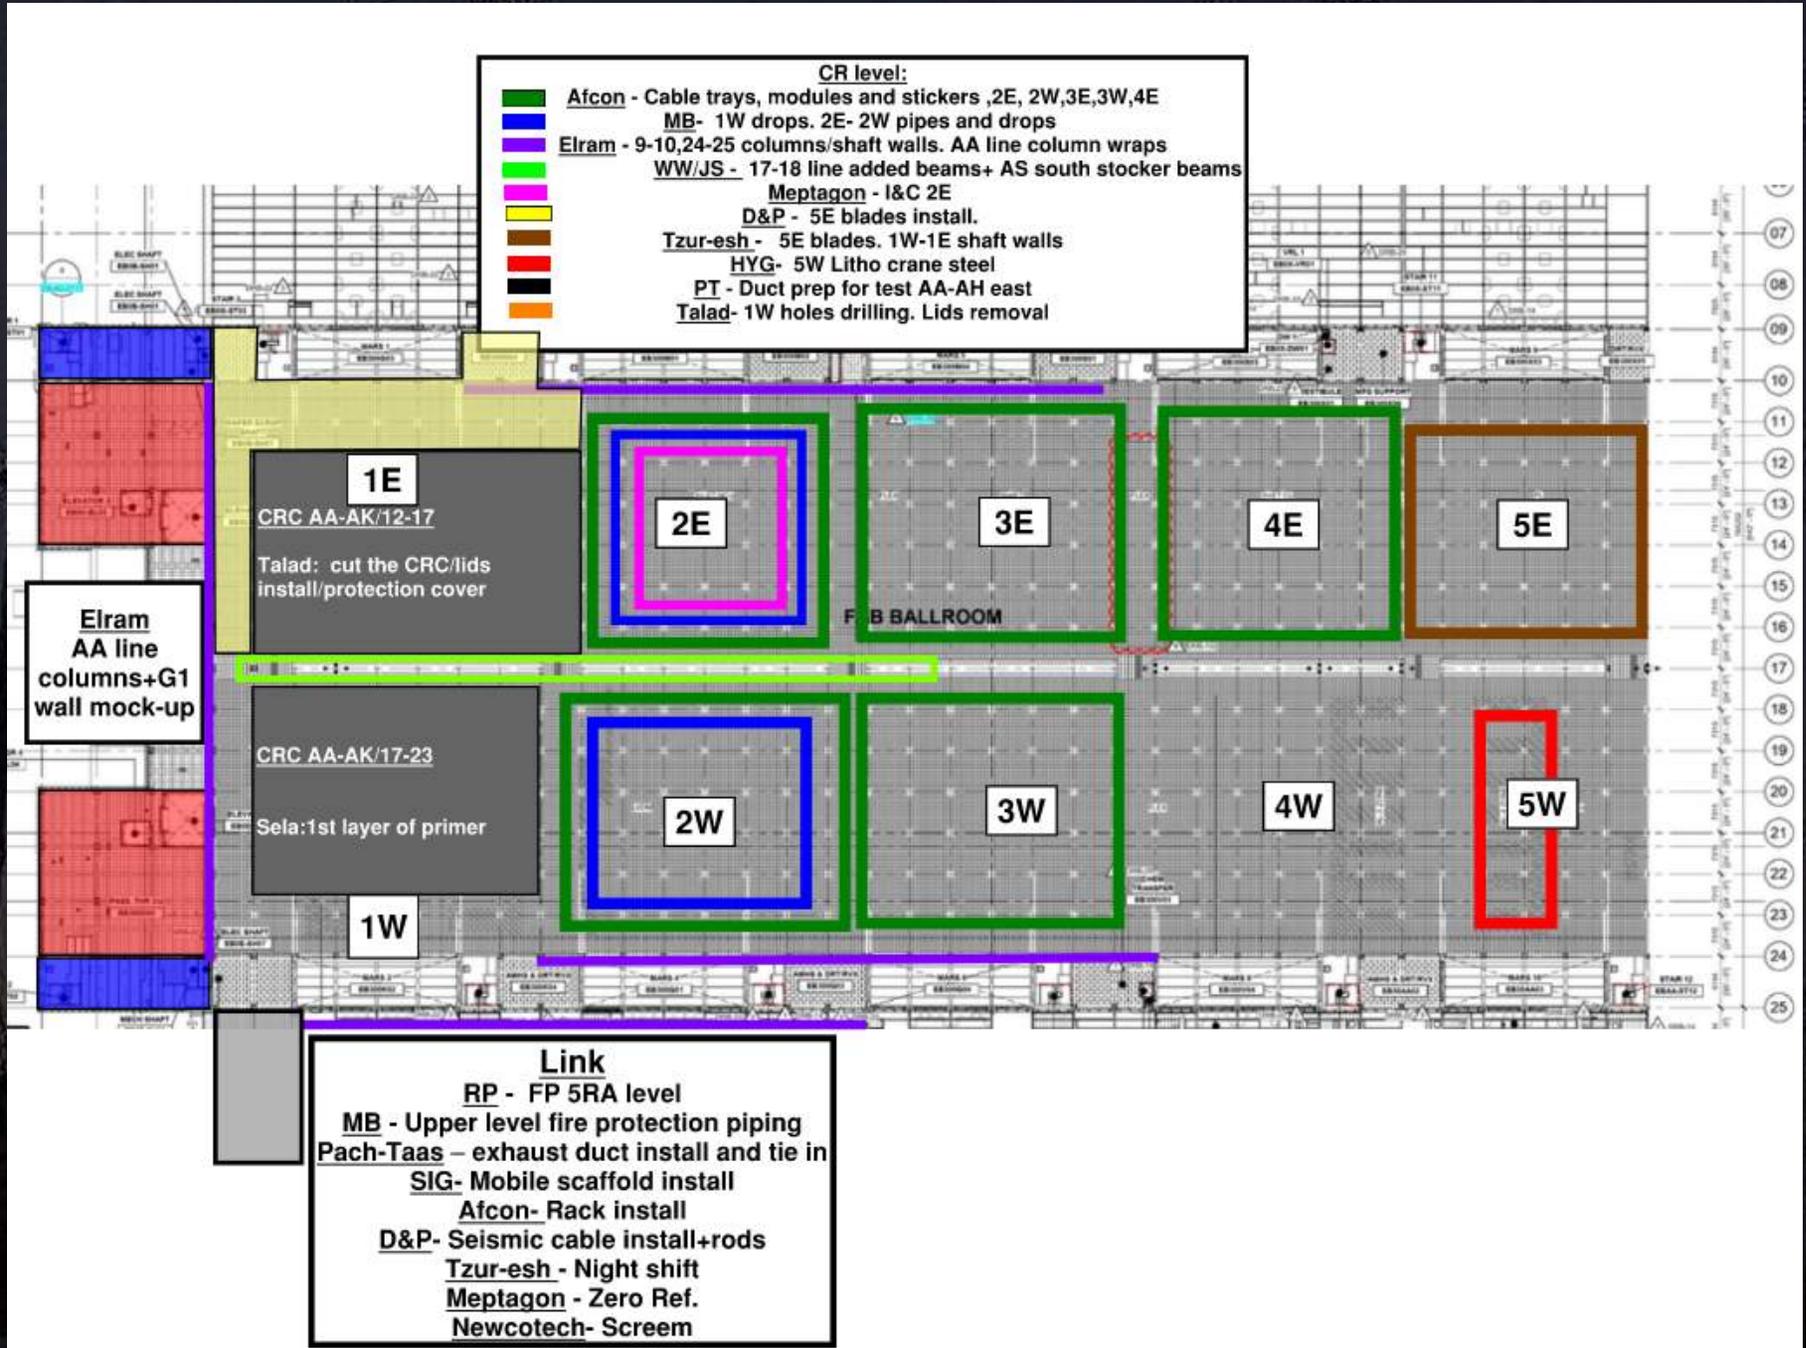

Int. level


- WW/SN - 2W penetrations
- Chemo- 10" pipe racks 4E-5E . Skids set 1E-1W
- Afcon - Cable trays, modules, cable pulling ,1W,2E,2W,3W
- HYG - 5RA added beams 3E
- MB- 3E,3W pipes
- SK- IA pipes 10/24 line
- Elram - Column wraps 9,10,24,25 lines
- RP- FP 4DA 3E-3W,2W racks
- Tzur-Esh - Steel paint 5E
- Megasone - Small wires+ speakers 2W+AA line
- SIG- Platforms 4W-5W

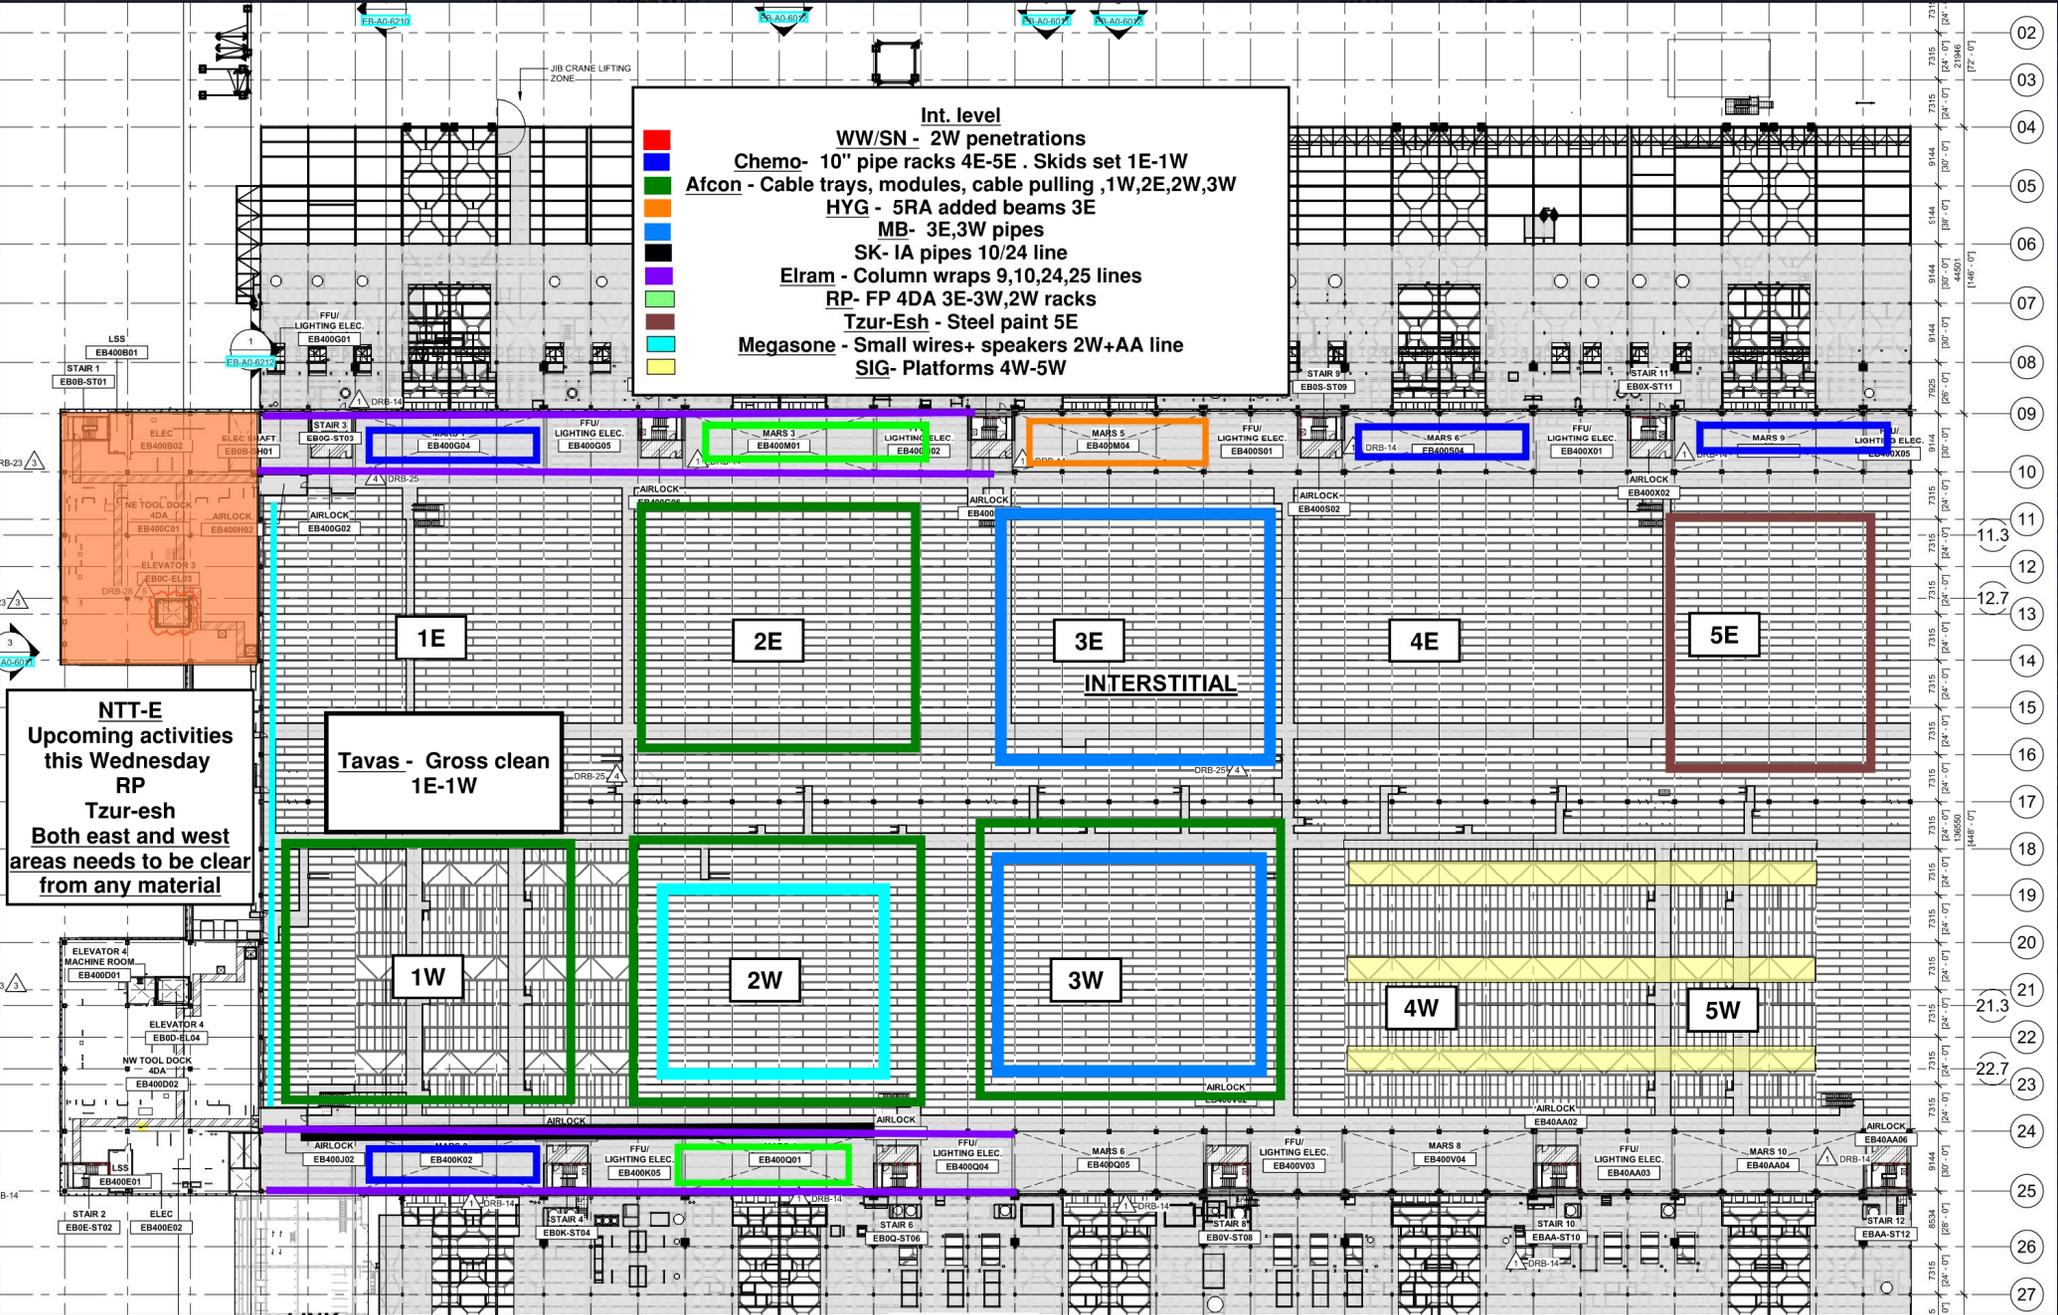


NTT-E
Upcoming activities
this Wednesday
RP
Tzur-esh
Both east and west
areas needs to be clear
from any material

Tavas - Gross clean
1E-1W

- 02
- 03
- 04
- 05
- 06
- 07
- 08
- 09
- 10
- 11
- 11.3
- 12
- 12.7
- 13
- 14
- 15
- 16
- 17
- 18
- 19
- 20
- 21
- 21.3
- 22
- 22.7
- 23
- 24
- 25
- 26
- 27

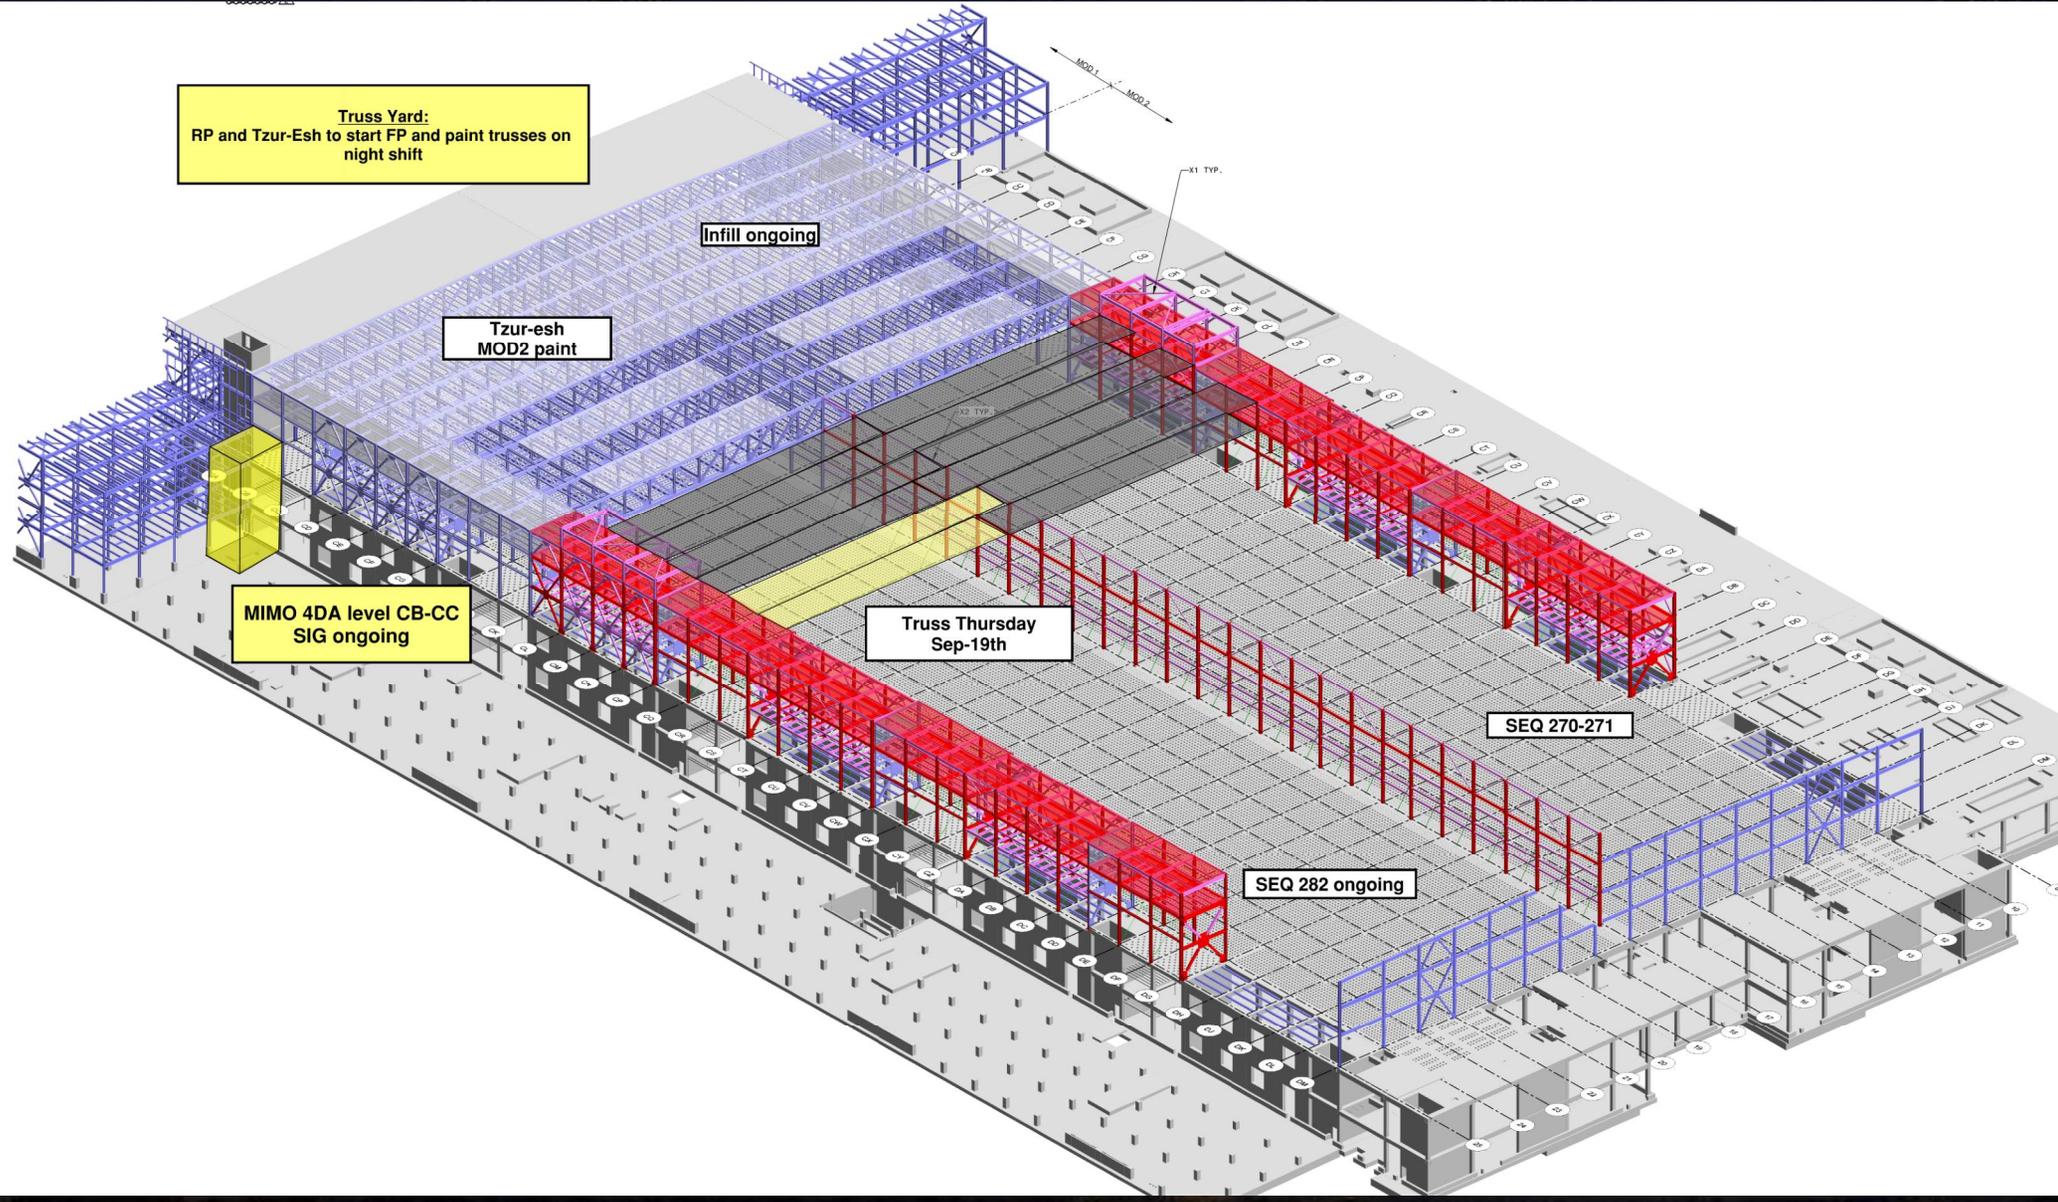

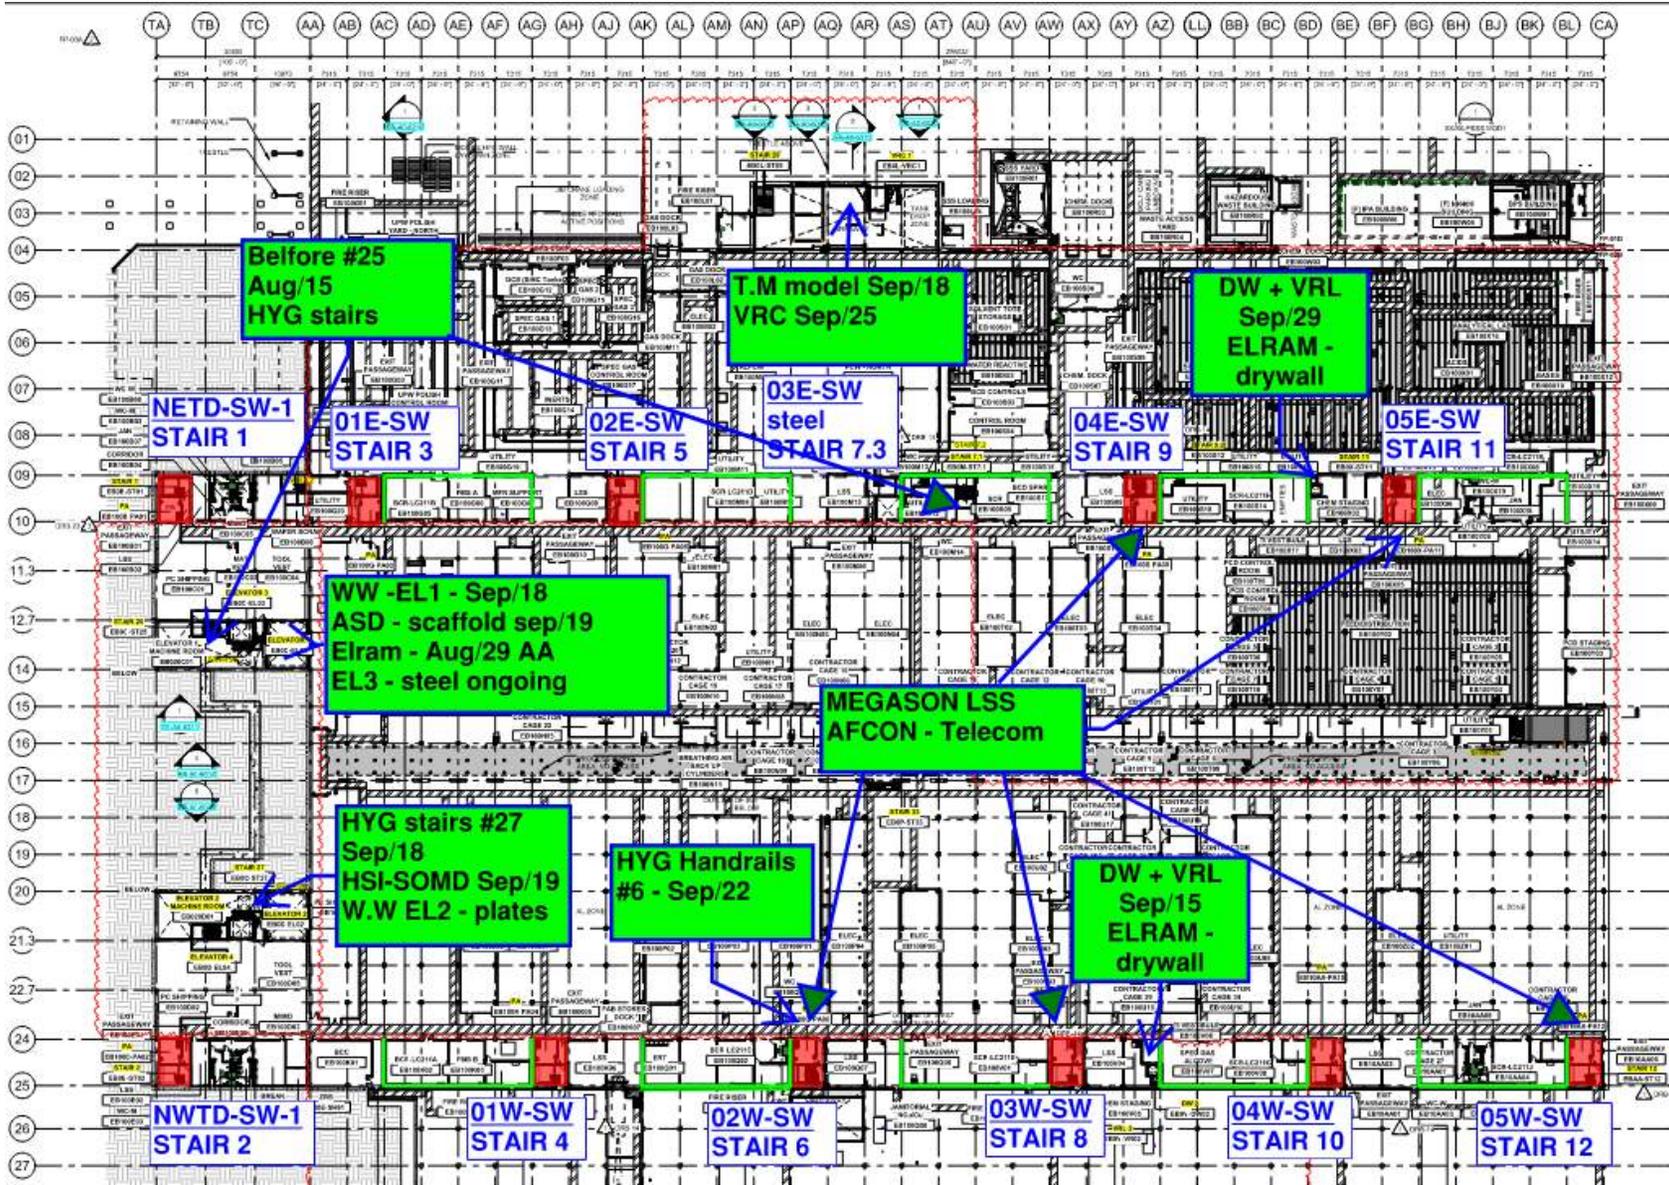

**Before #25
Aug/15
HYG stairs**

**T.M model Sep/18
VRC Sep/25**

**DW + VRL
Sep/29
ELRAM -
drywall**

**NETD-SW-1
STAIR 1**

**01E-SW
STAIR 3**

**02E-SW
STAIR 5**

**03E-SW
steel
STAIR 7.3**

**04E-SW
STAIR 9**

**05E-SW
STAIR 11**

**WW - EL1 - Sep/18
ASD - scaffold sep/19
Elram - Aug/29 AA
EL3 - steel ongoing**

**MEGASON LSS
AFCON - Telecom**

**HYG stairs #27
Sep/18
HSI-SOMD Sep/19
W.W EL2 - plates**

**HYG Handrails
#6 - Sep/22**

**DW + VRL
Sep/15
ELRAM -
drywall**

**NWT-D-SW-1
STAIR 2**


**01W-SW
STAIR 4**

**02W-SW
STAIR 6**

**03W-SW
STAIR 8**

**04W-SW
STAIR 10**

**05W-SW
STAIR 12**

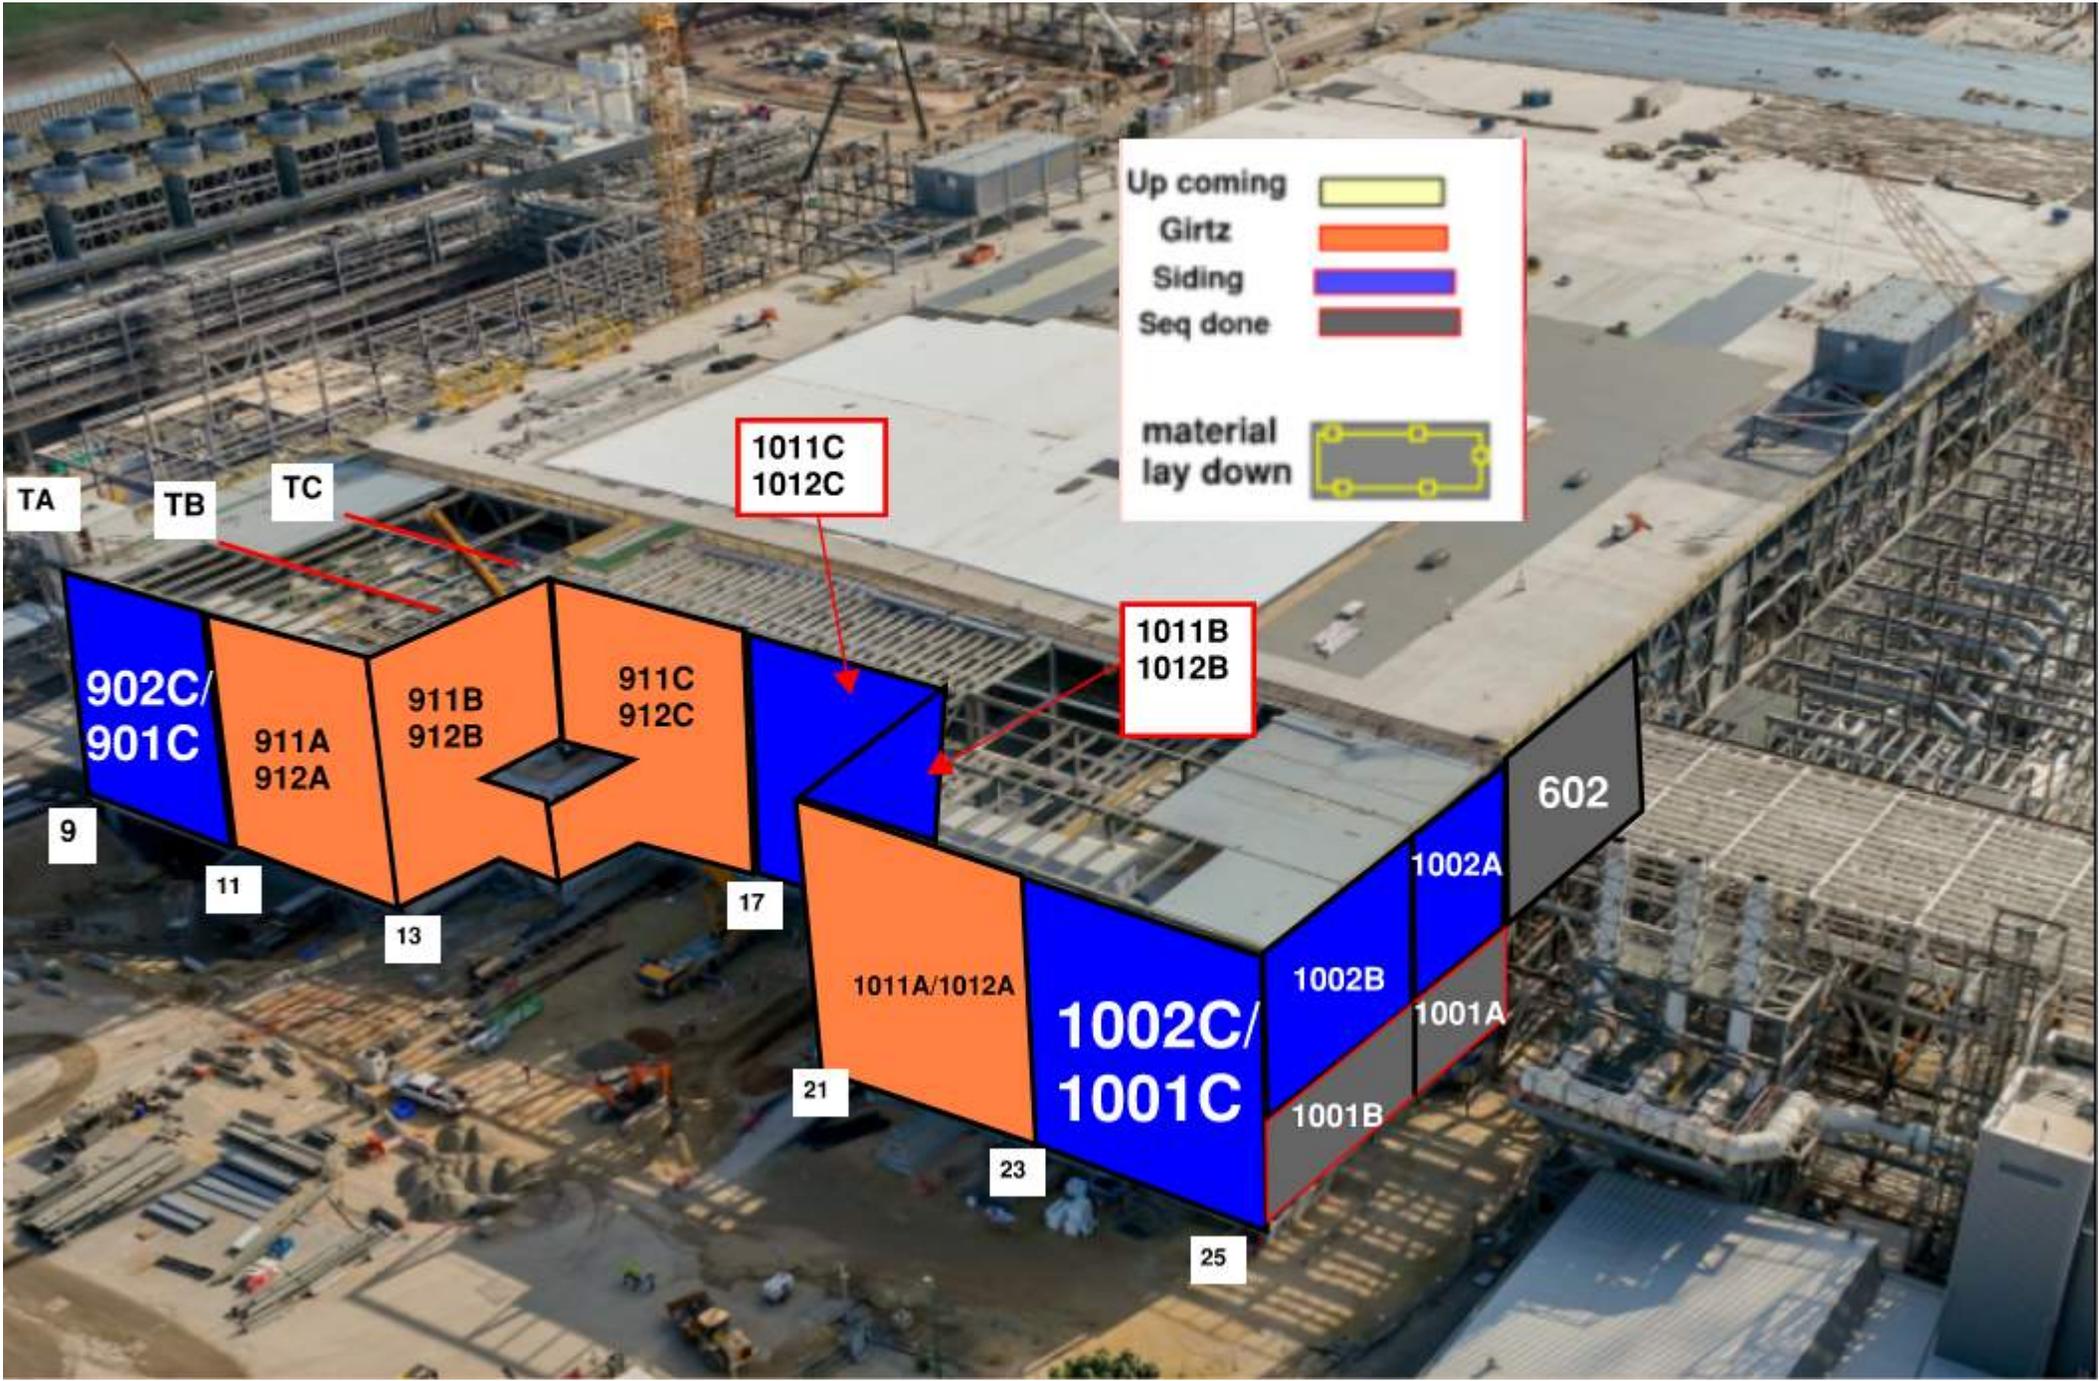

Up coming 

Girtz 

Siding 

Seq done 

material lay down 

1011C
1012C

1011B
1012B

902C/
901C

911A
912A

911B
912B

911C
912C

1011A/1012A

1002C/
1001C

1002A

1002B

1001A

1001B

602

TA

TB

TC

9

11


13

17

21

23


25

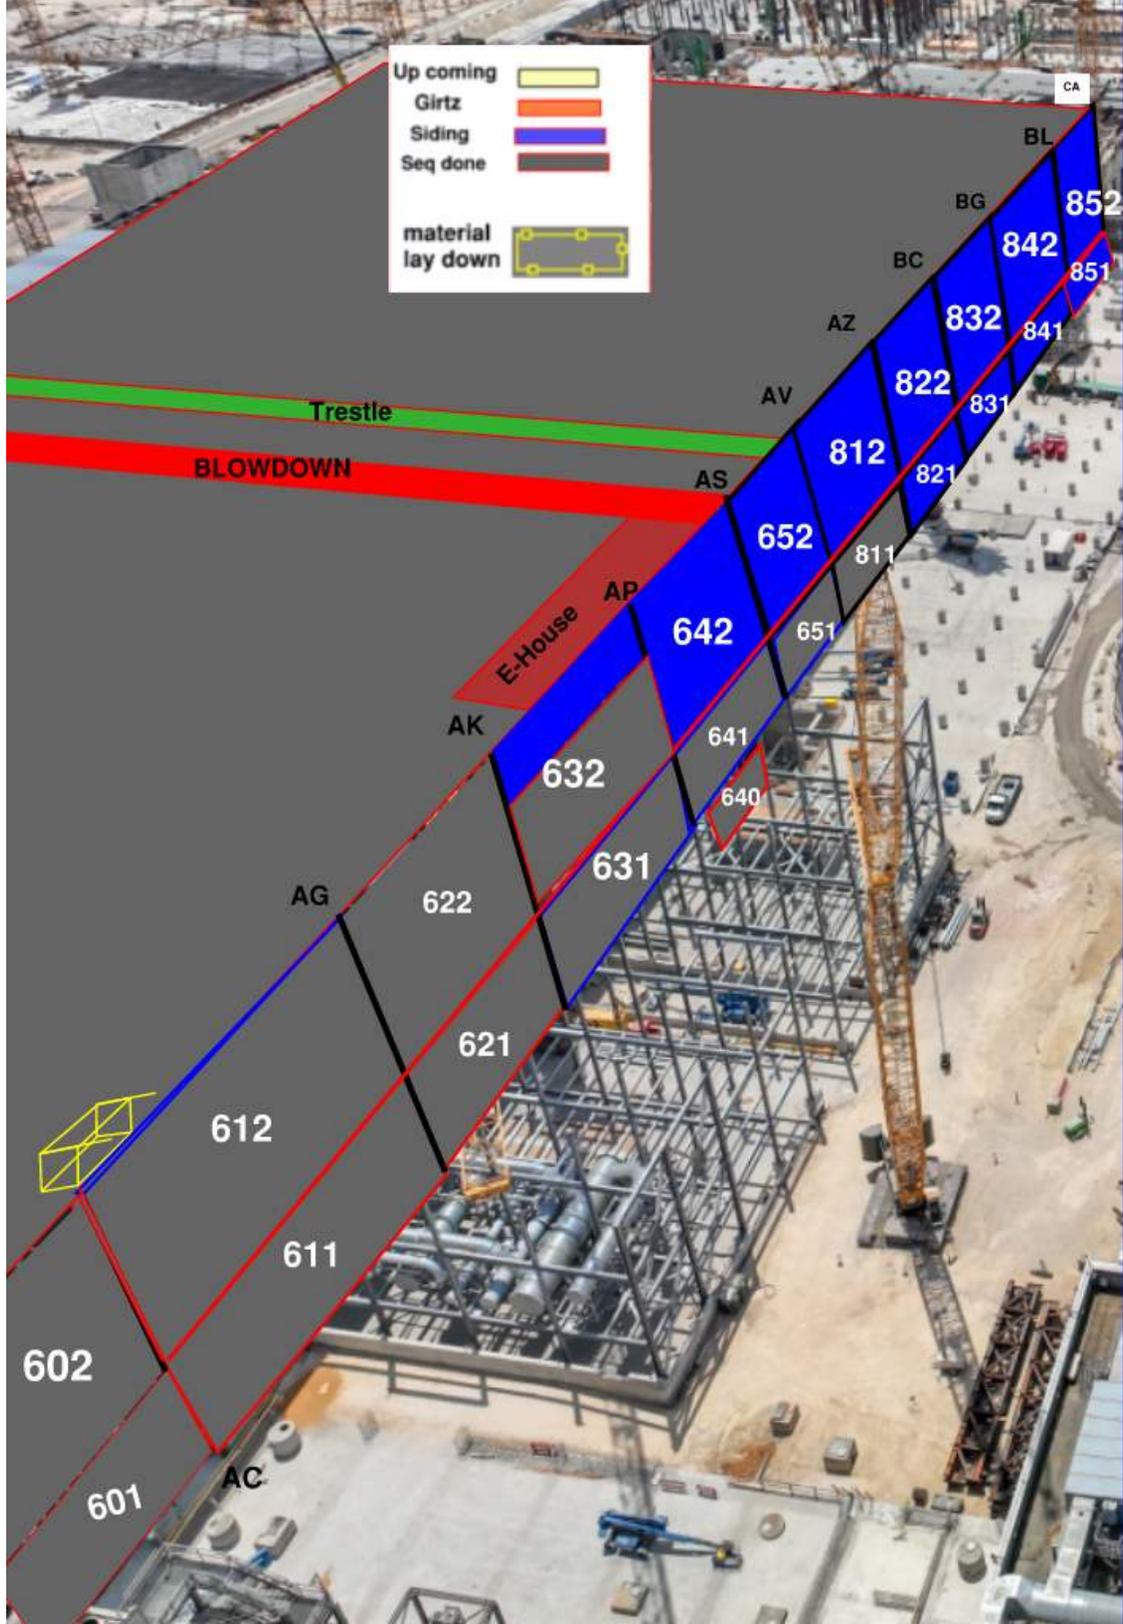

PSSS.1

Utility Level 1YA

PSSS Roof 2SA

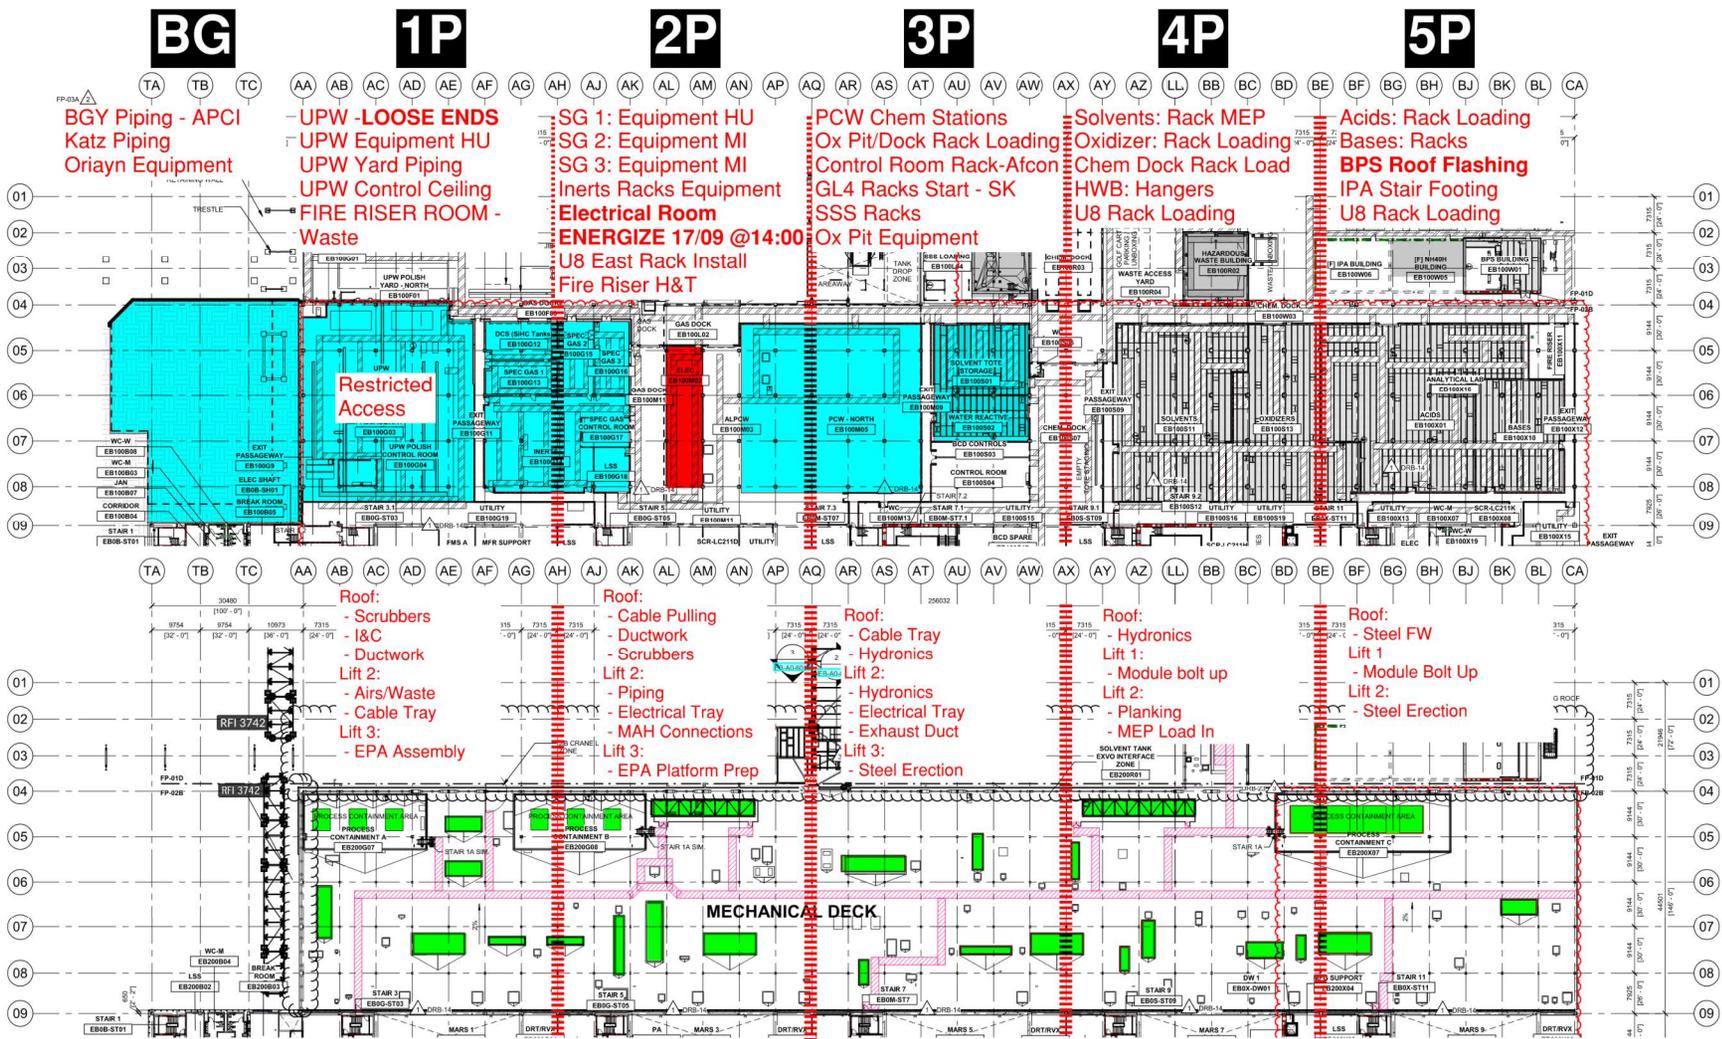


PSSS

4P VFD Set


Crane Mats – 19/09
DMAG Move – 22/09
Hoist VFD – 24/09




PSSS DMAG ROAD CLOSURES

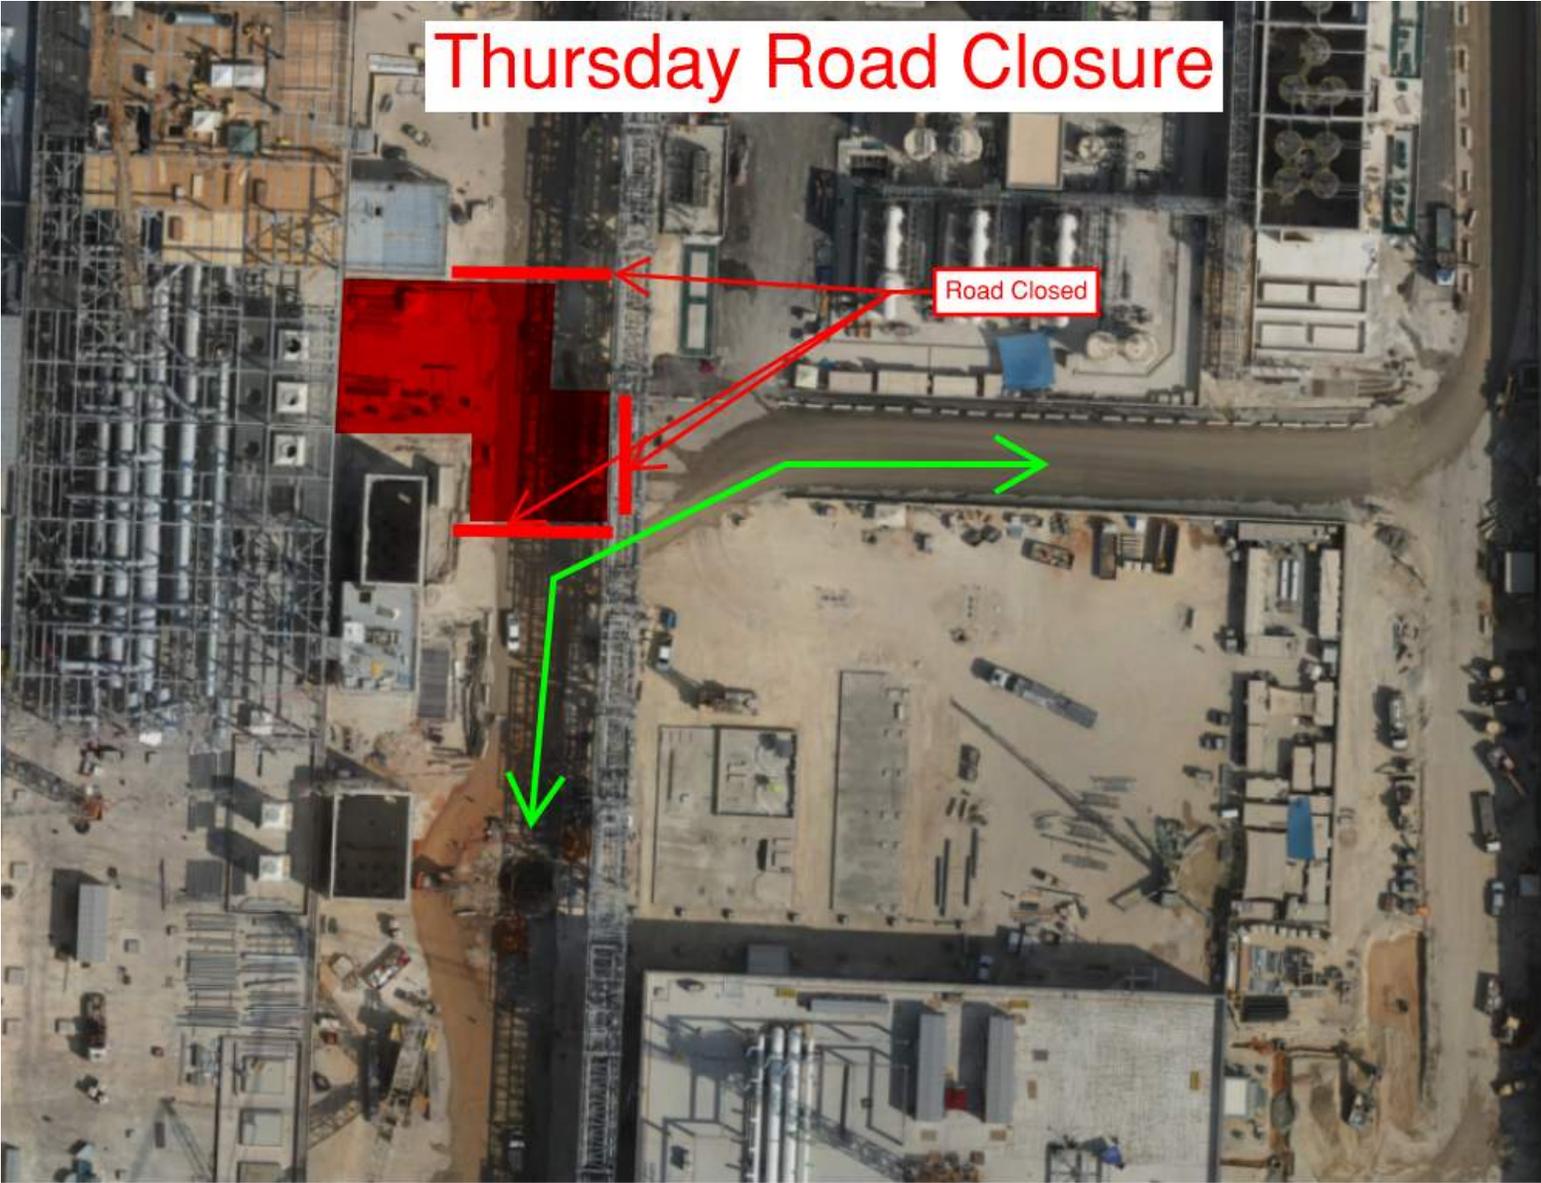

PSSS DMAG
ROAD
CLOSURES

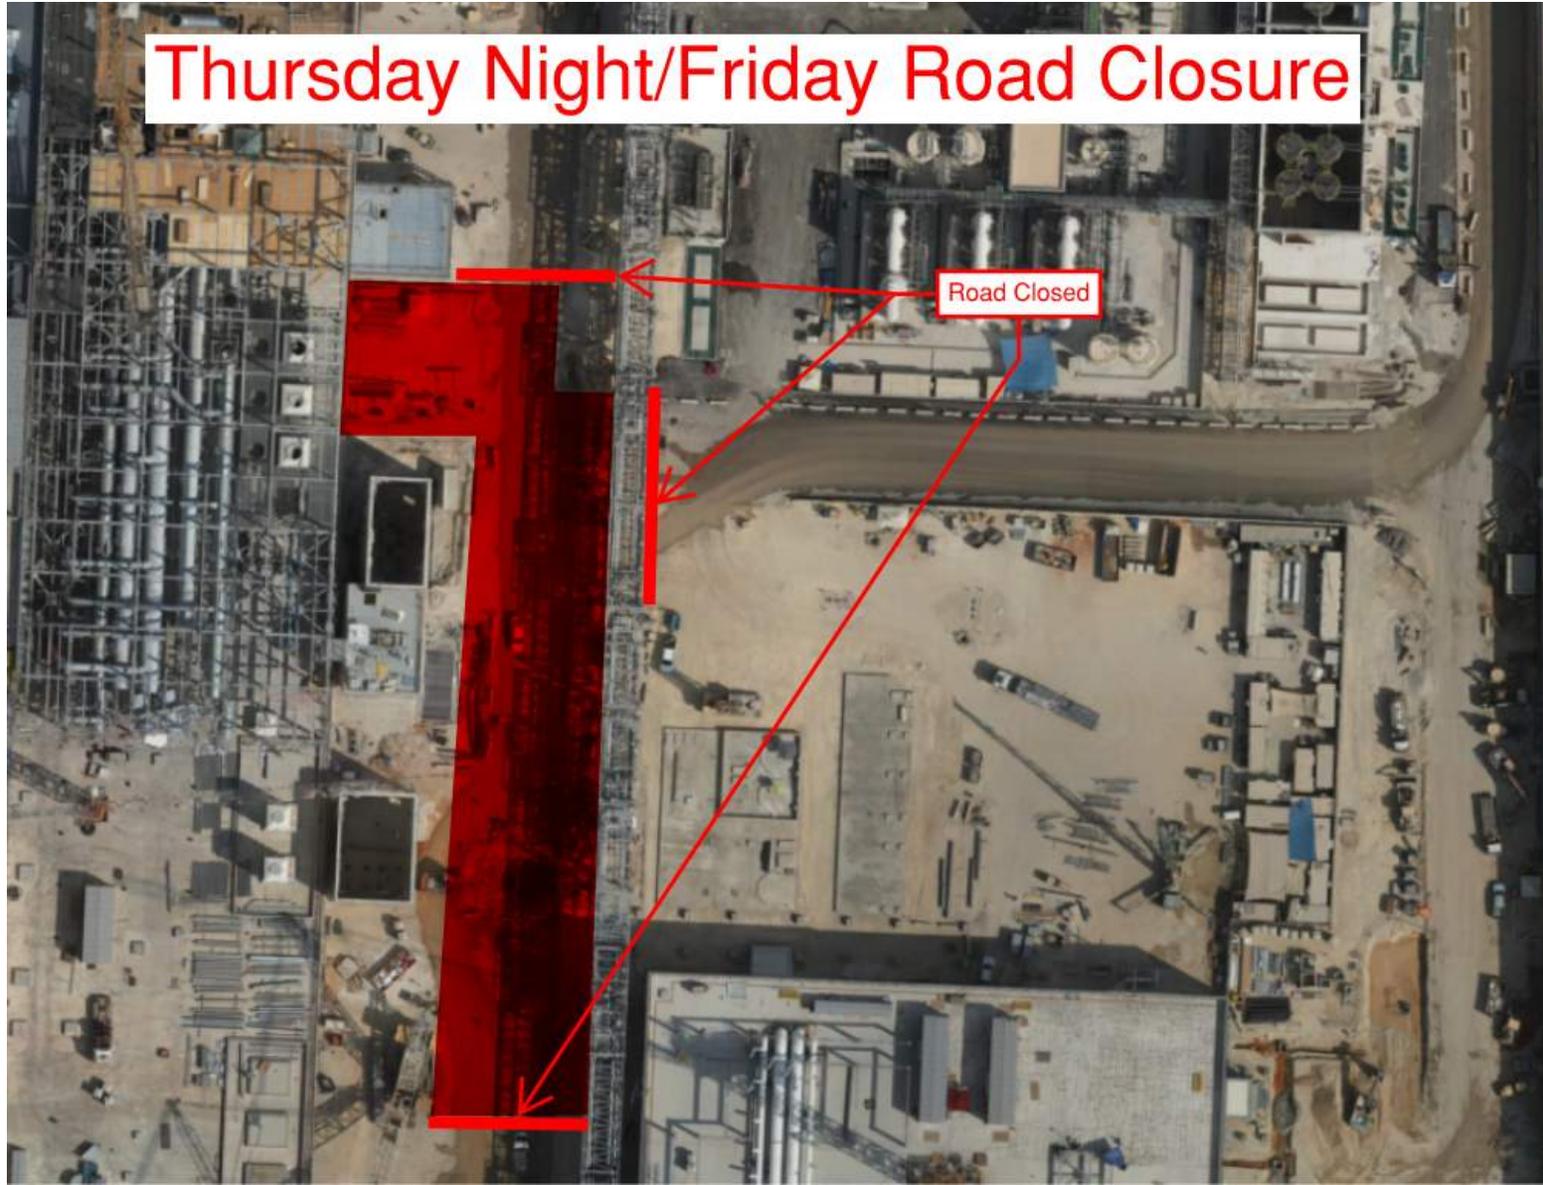

PSSS DMAG ROAD CLOSURES

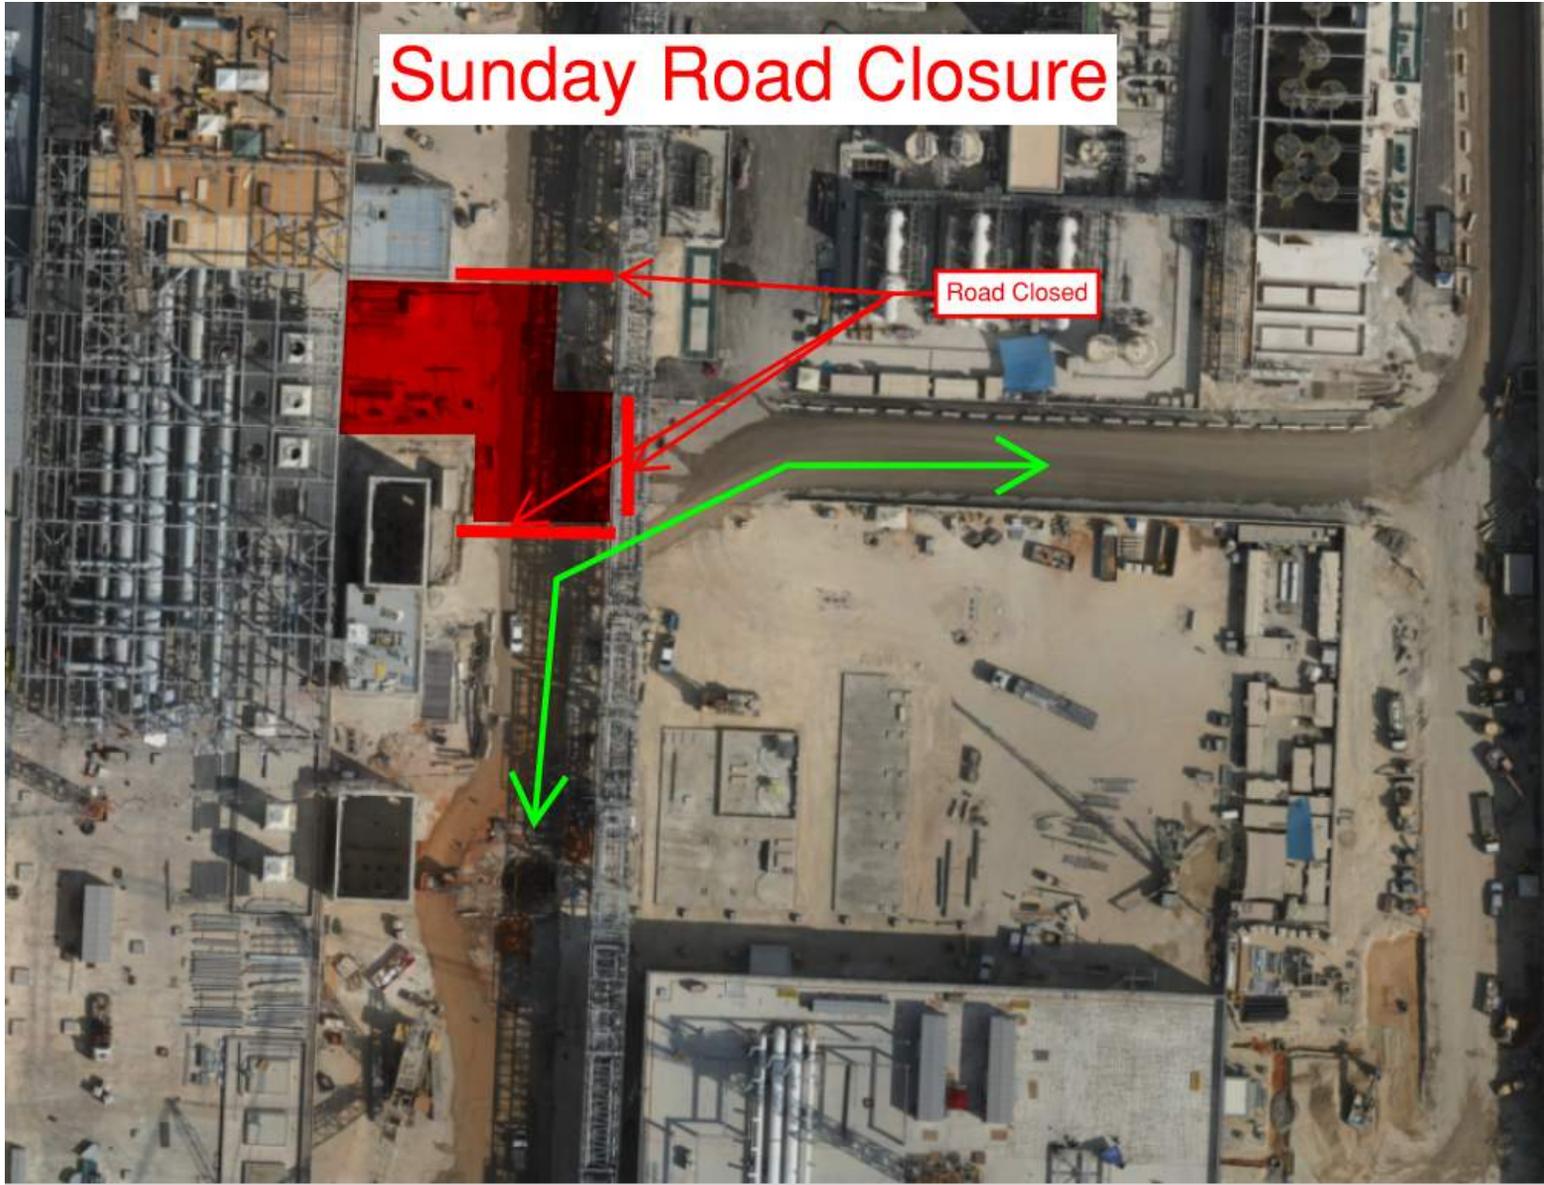


WJG 01J, 02J LIFT 2 & 3



WJG 03J, 04J, 05J LIFT 2 & 3



WJG UTILITY LEVEL BUILD OUT

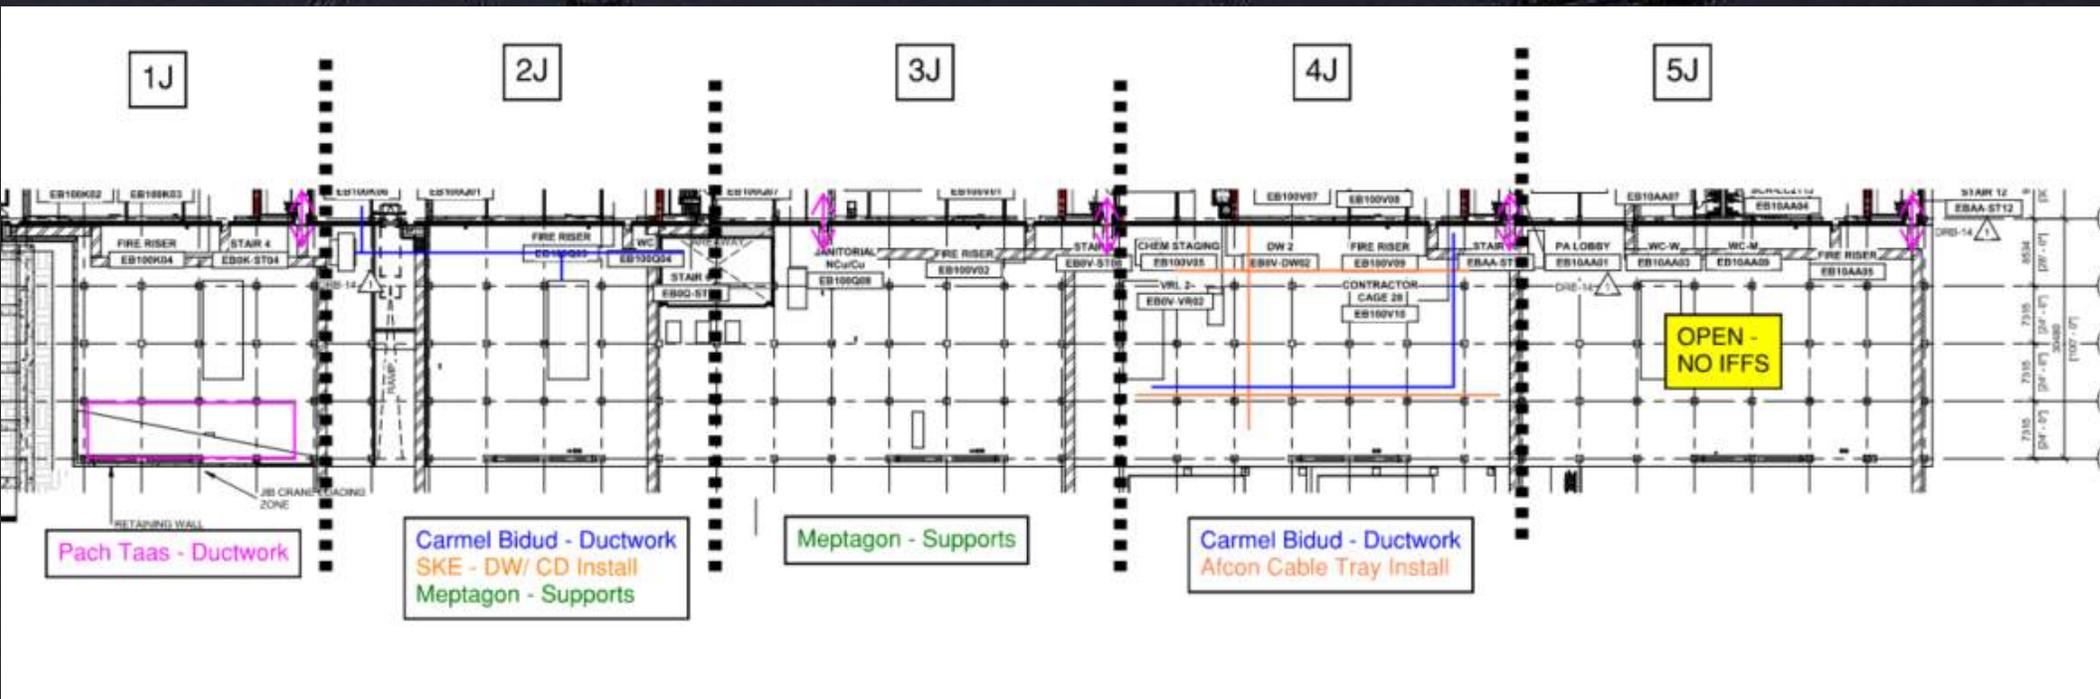

WJG Closed Night Shift 17/09/2024

SKE IA/PA PNEUMATIC TEST
138 PSI - 8 Hour
30m EXCLUSION ZONE
MAIN GL 28 @ UTILITY LEVEL
Date: 17/09/2024
2100 - 0600

21


BE

CD


Stair 12 open SF to Roof


Link Clean Rooms Closed

WALK PATH

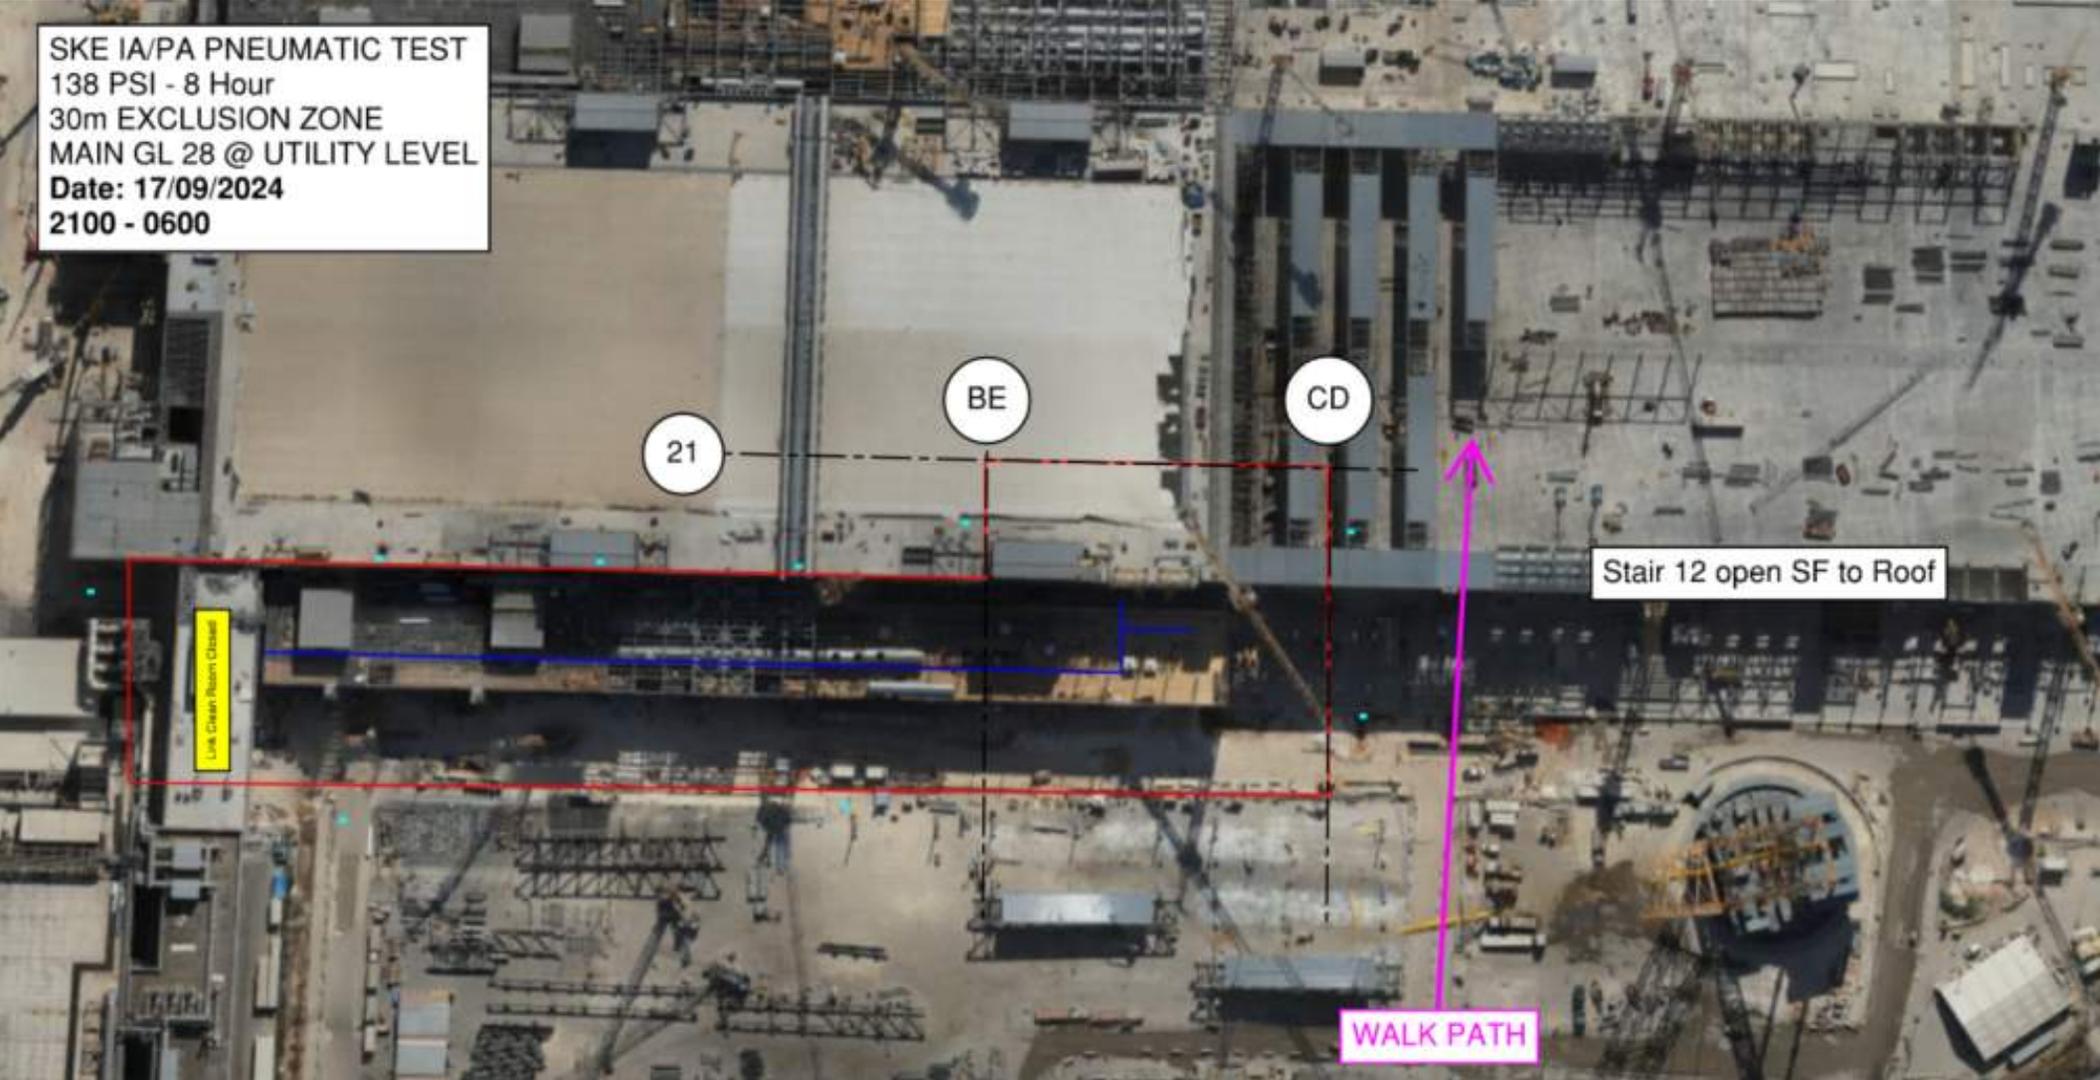

VFD SET 16/09/2024 & 18/09/2024

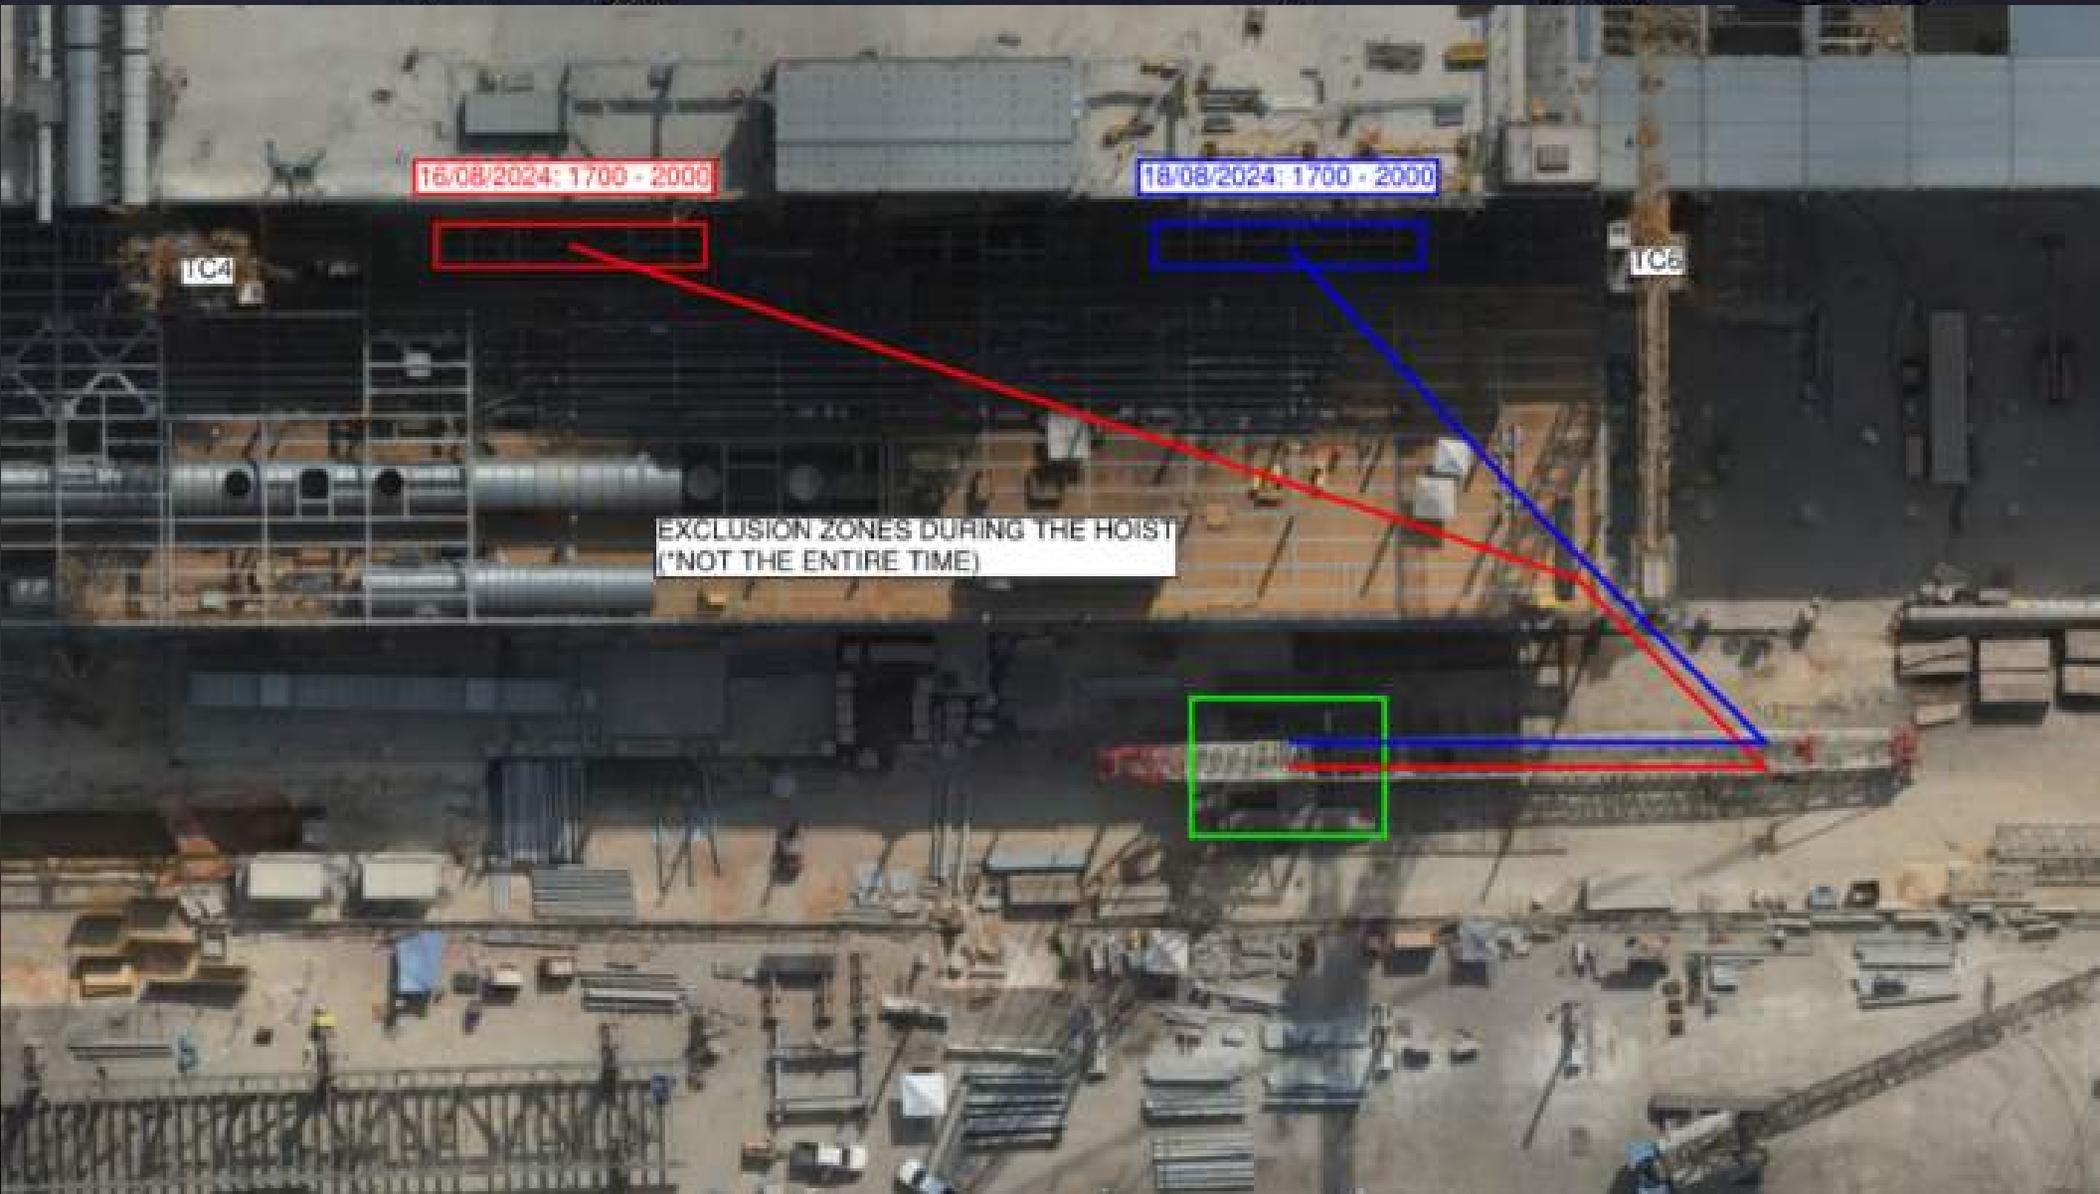

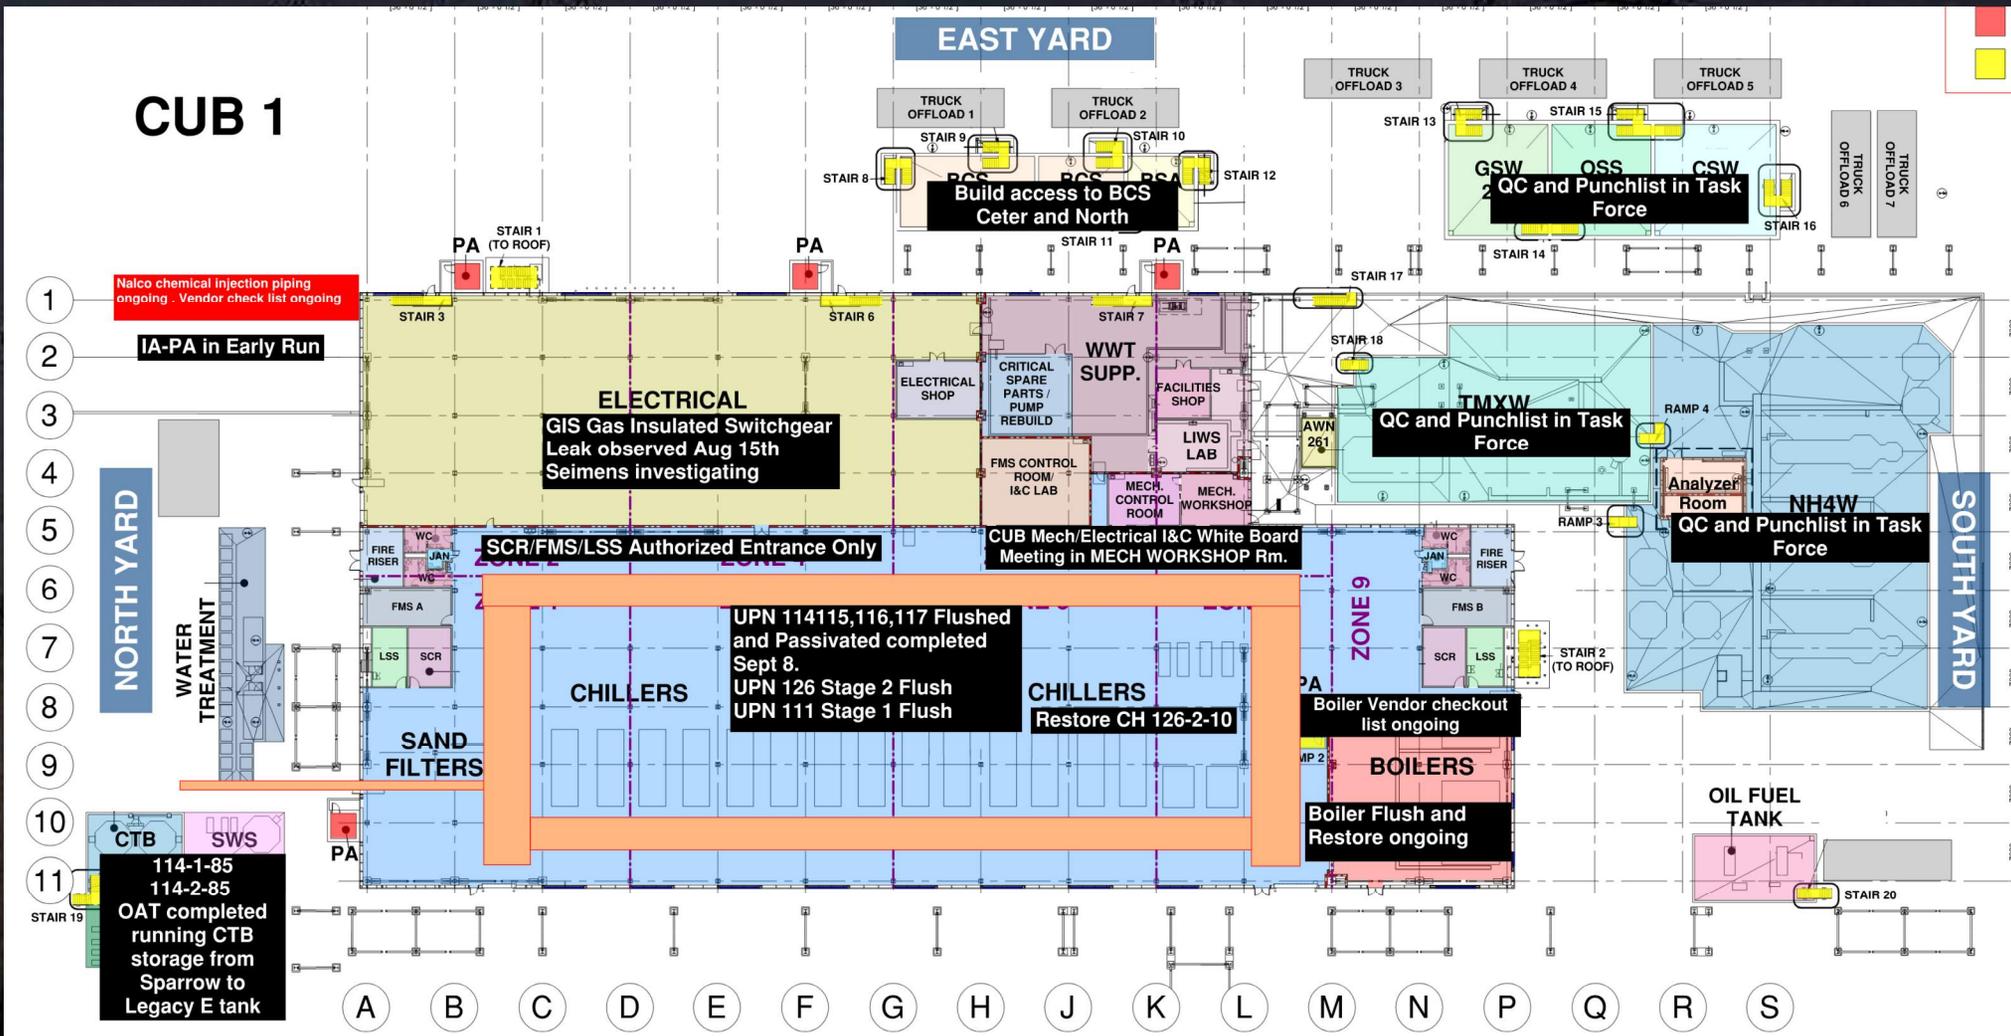



Site cleared for paving
Sept 8th Temp safety shower

North Yard Concrete paving needed Trench drain and Waste Mech. systems

Mobile Crane roof access and steel shake out area

E-House platform and stairs
Sept 1-25

Rigo Tec AHU platforms
Sept 1- Sept 25

Area needs to be backfilled and graded

Cable Tray install ongoing. Cable pulling to South Yard ongoing

hand graded paving


CT 13 ,15 ,17 ,19 Green Tag and Equipment Cx pending YWTC and CHEMO COR


Clear Roof and perform flood tests
Sept. 19th
Sept 26th

Concrete Grading After MIMO restored


Restricted Access Boiler Fuel tank

CUB 1

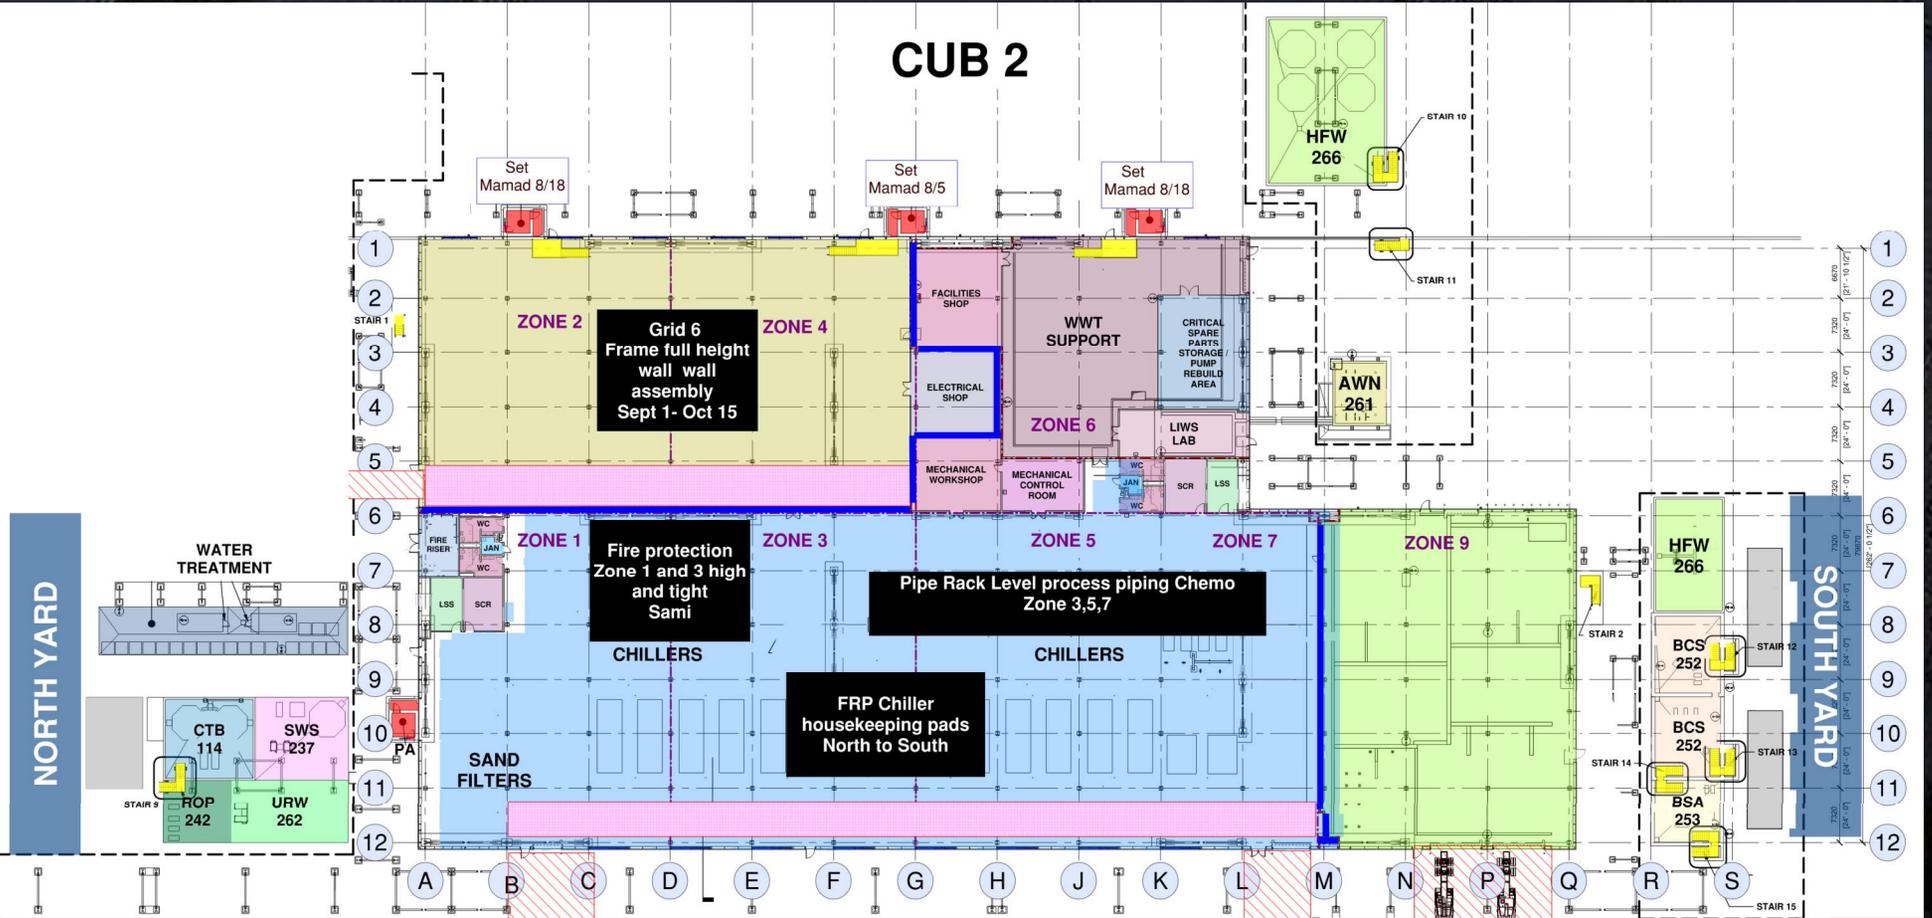

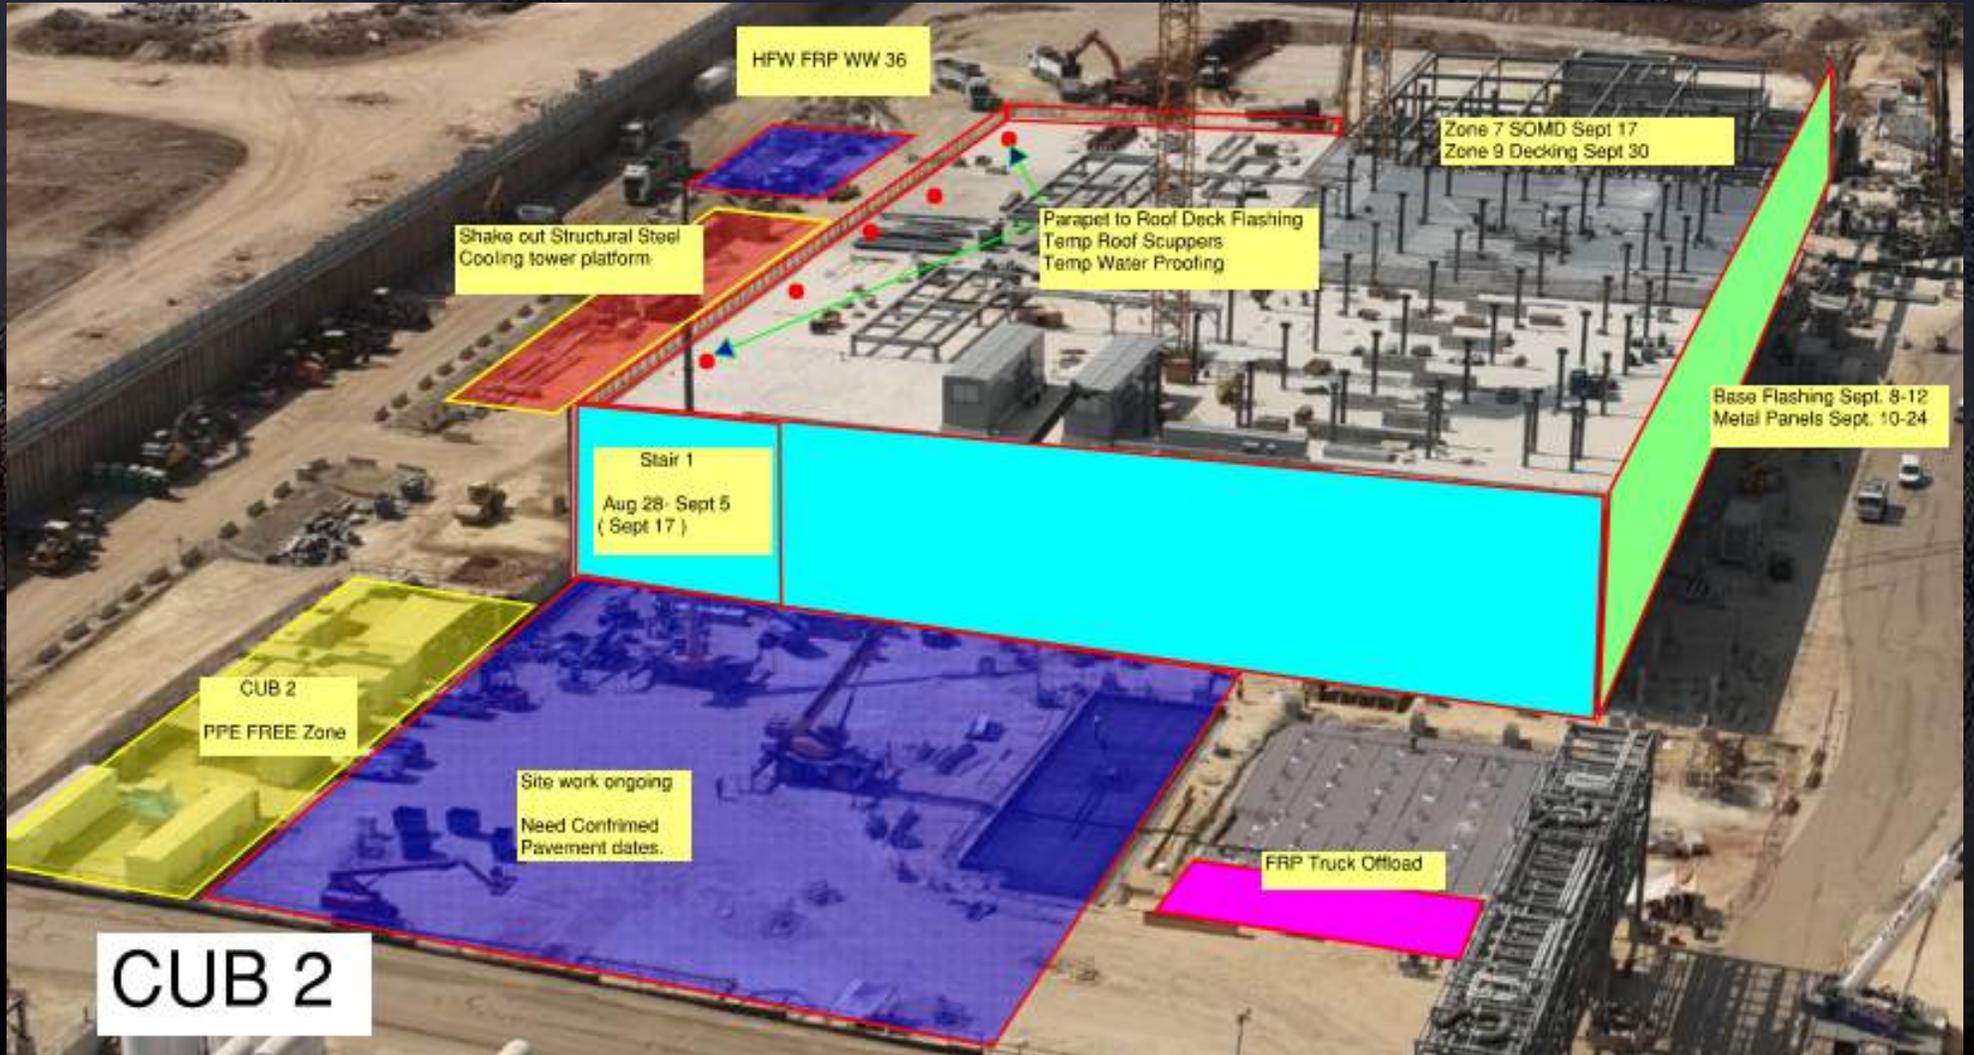

CC2800
60 meter radius
29 ton capacity
22 ton AHU = 75% capacity

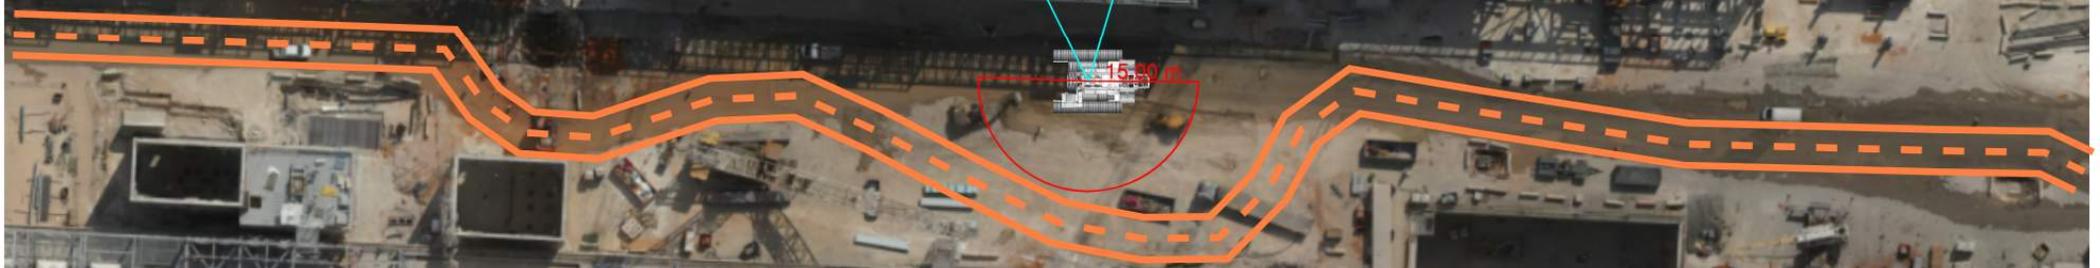


Elmoe
Z 2-,4,7- Red Valve- cable test- Megger
Ais- prep for term control cable


F.K. Electra-
testing & run
generators

NO ENTRY
HV ENERGIZED AREA

TMT -
CCTV UG SAN

TMT-
-clean & seal sewage & Drainage manholes
-Z 8- prep for asphalt next week- backfilling
,compacting & curb stones

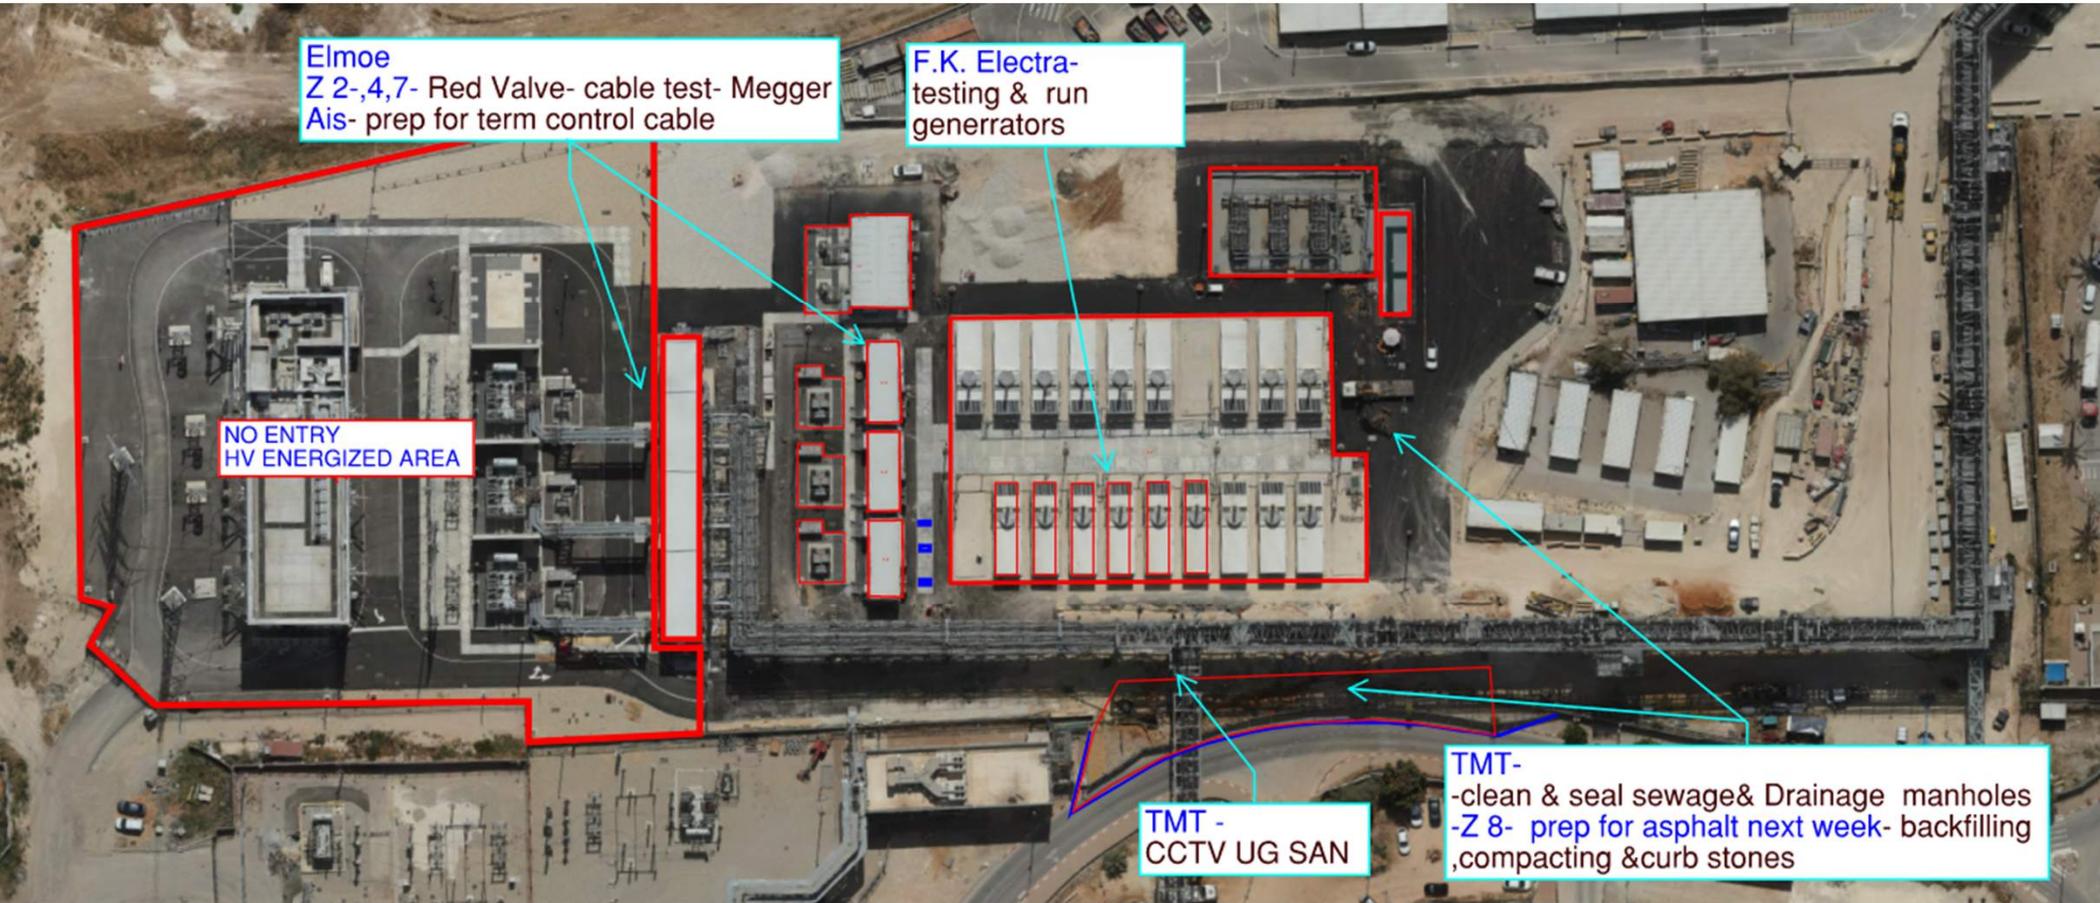

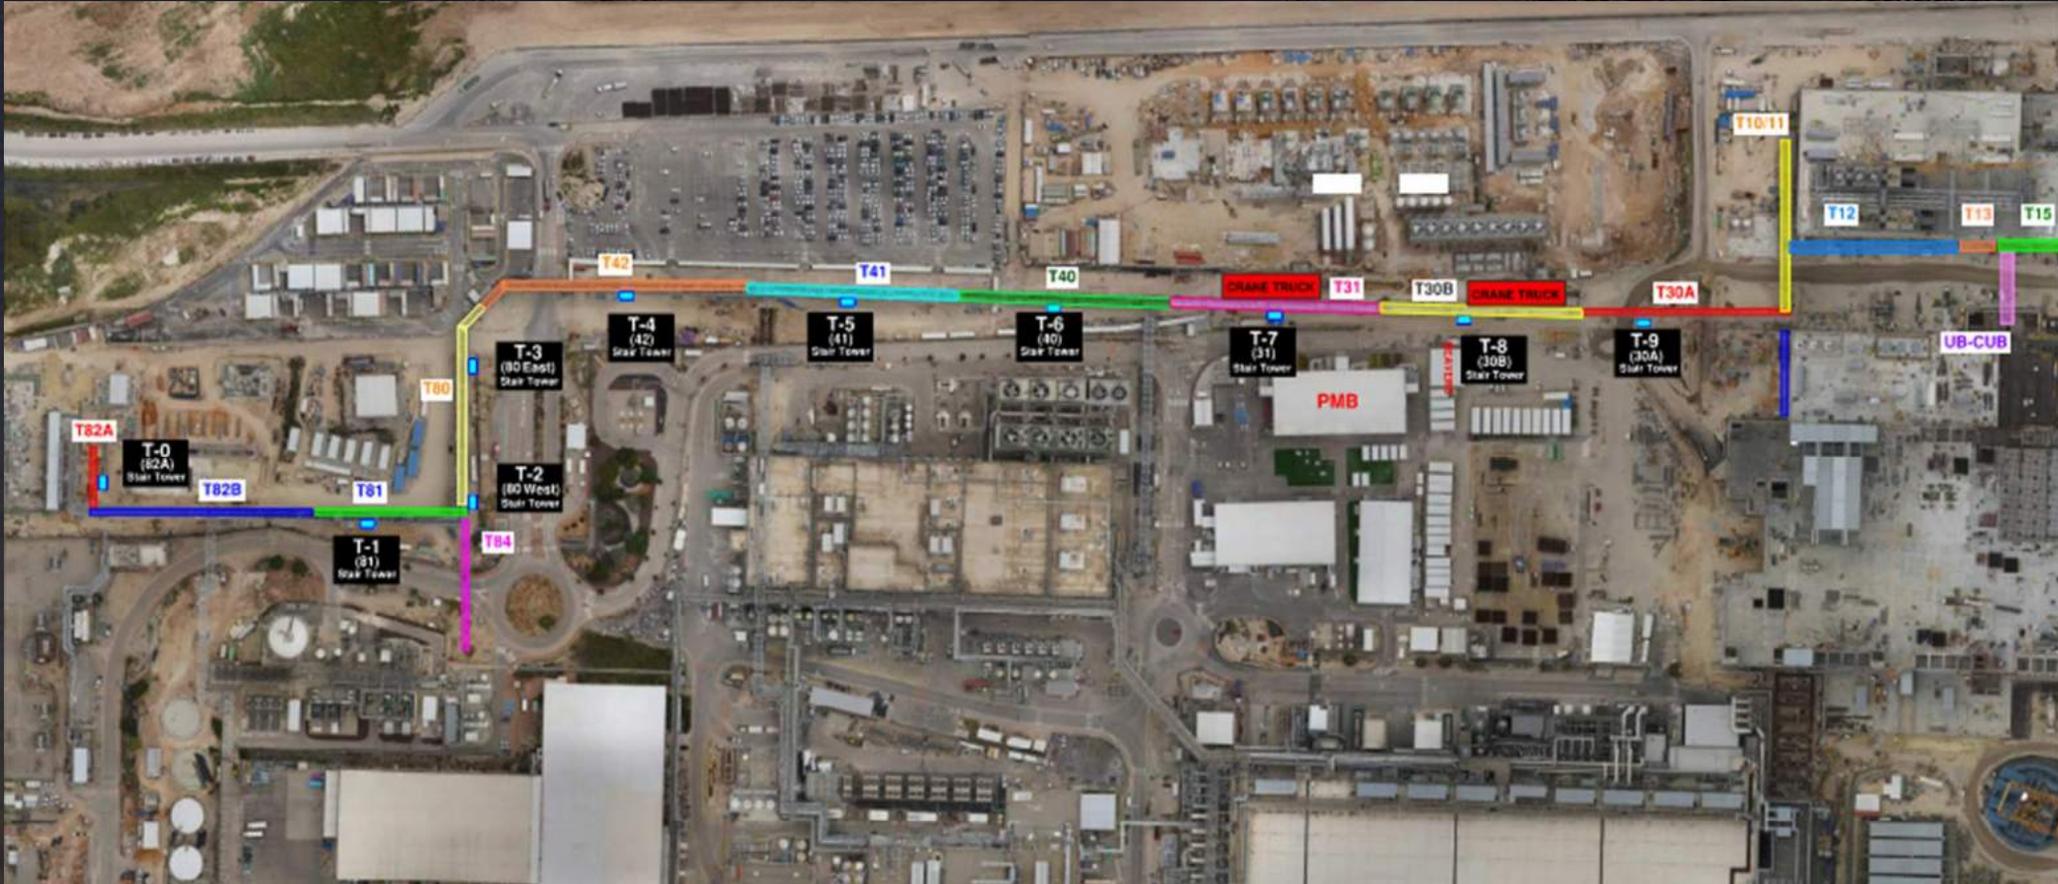

Thurs. 19/9 09:00 -11:00
Sun. 22/9 09:00 -11:00

CRANE



MODULE

Daily Coordination Meeting

Site Logistics
North Gate B






Daily Coordination Meeting

Site Logistics


North

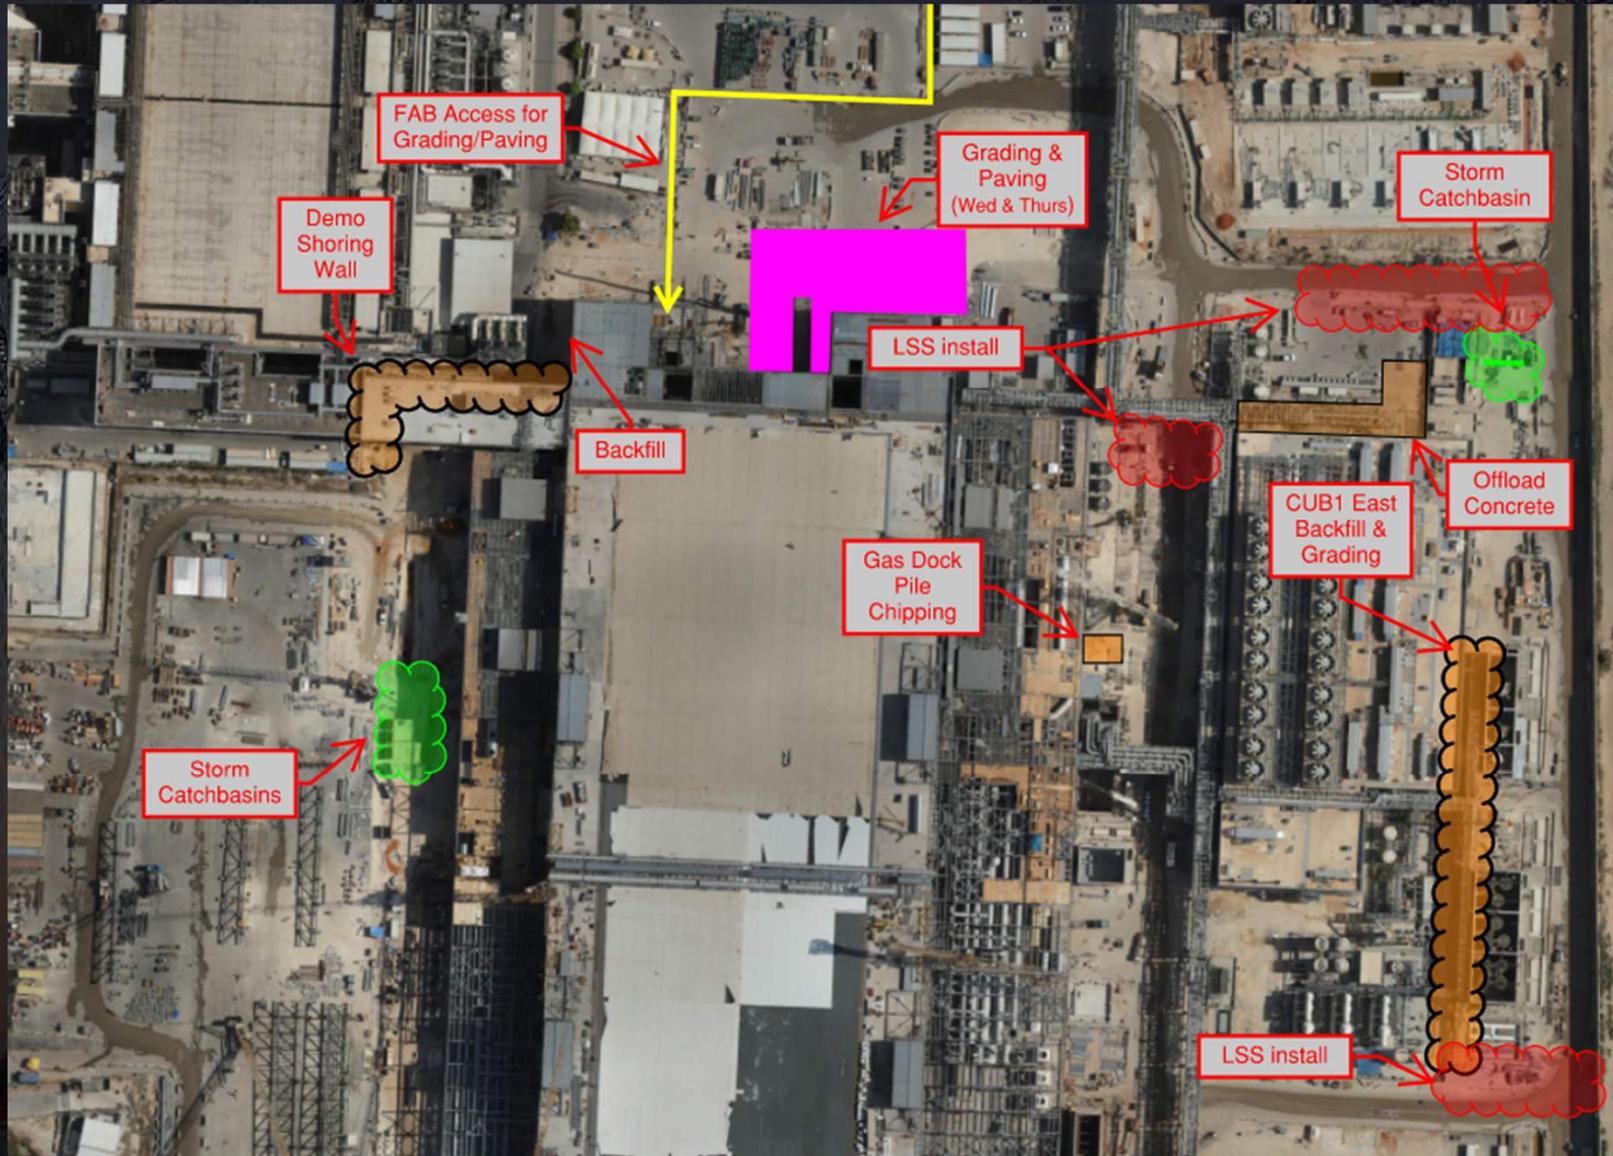

Daily Coordination Meeting

Site Logistics

South

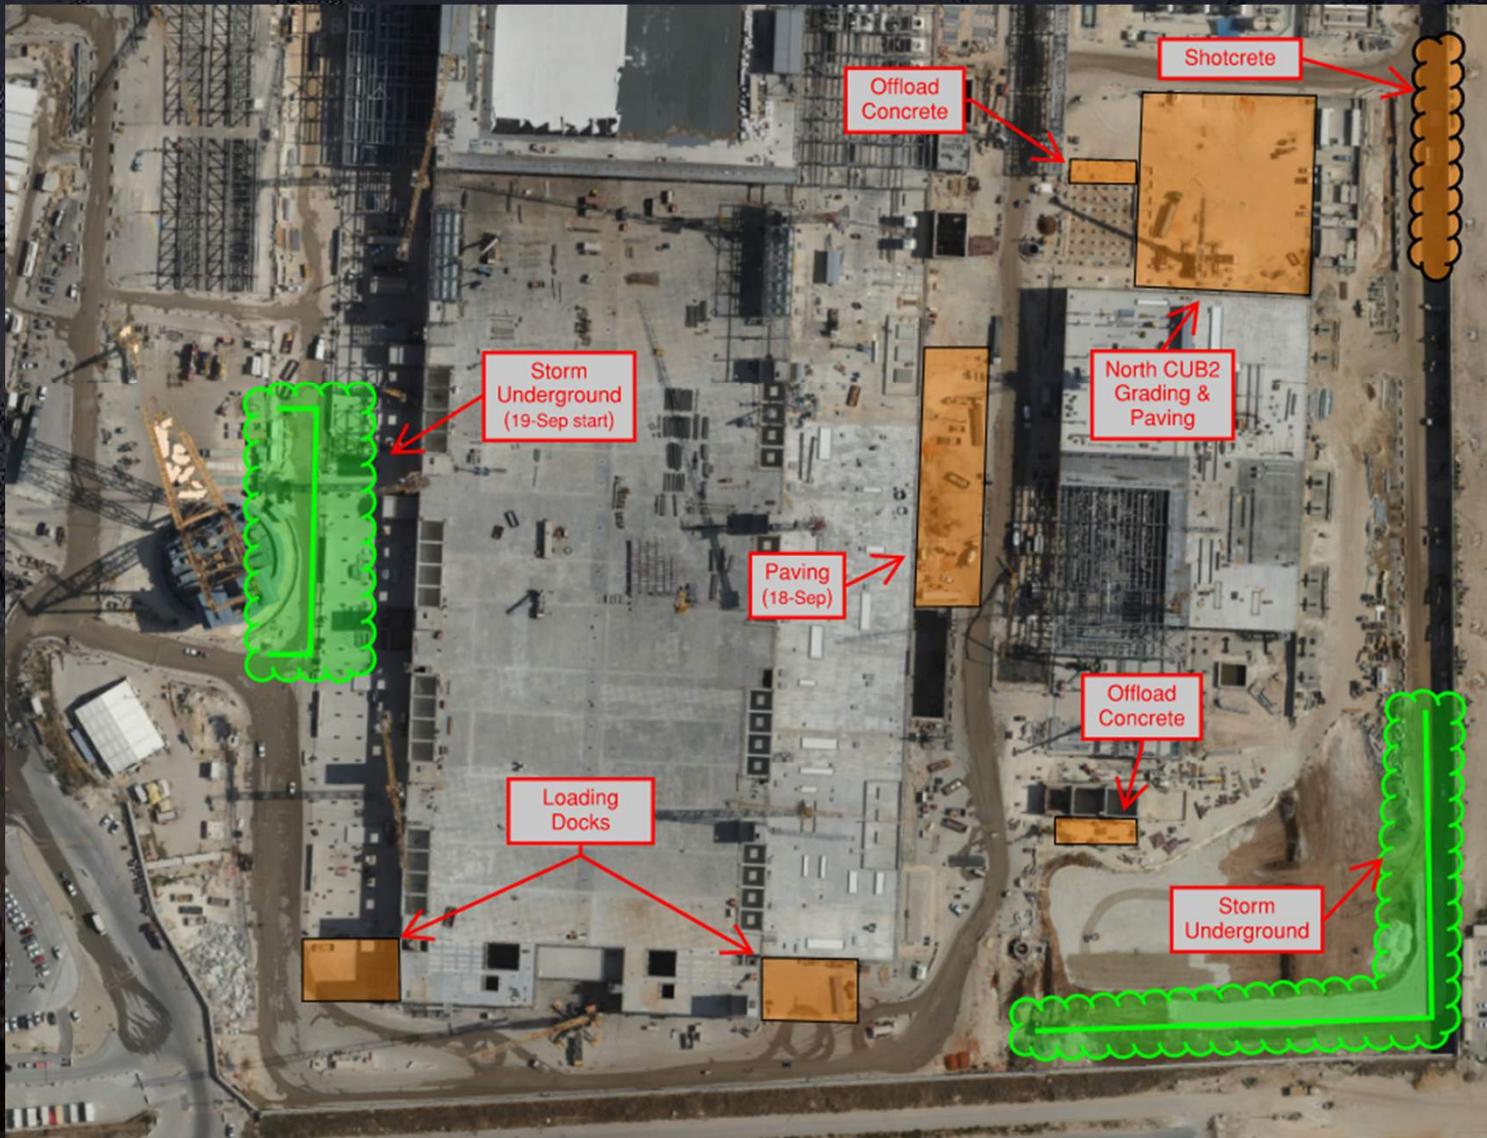

Job Services

Work Week 38

- ▶ Deep cleaning tent C2
- ▶ Flyable bathrooms


Deep cleaning on Friday 20th September – tent C2



C1

C2

Deep cleaning on Friday 20th September – tent C2


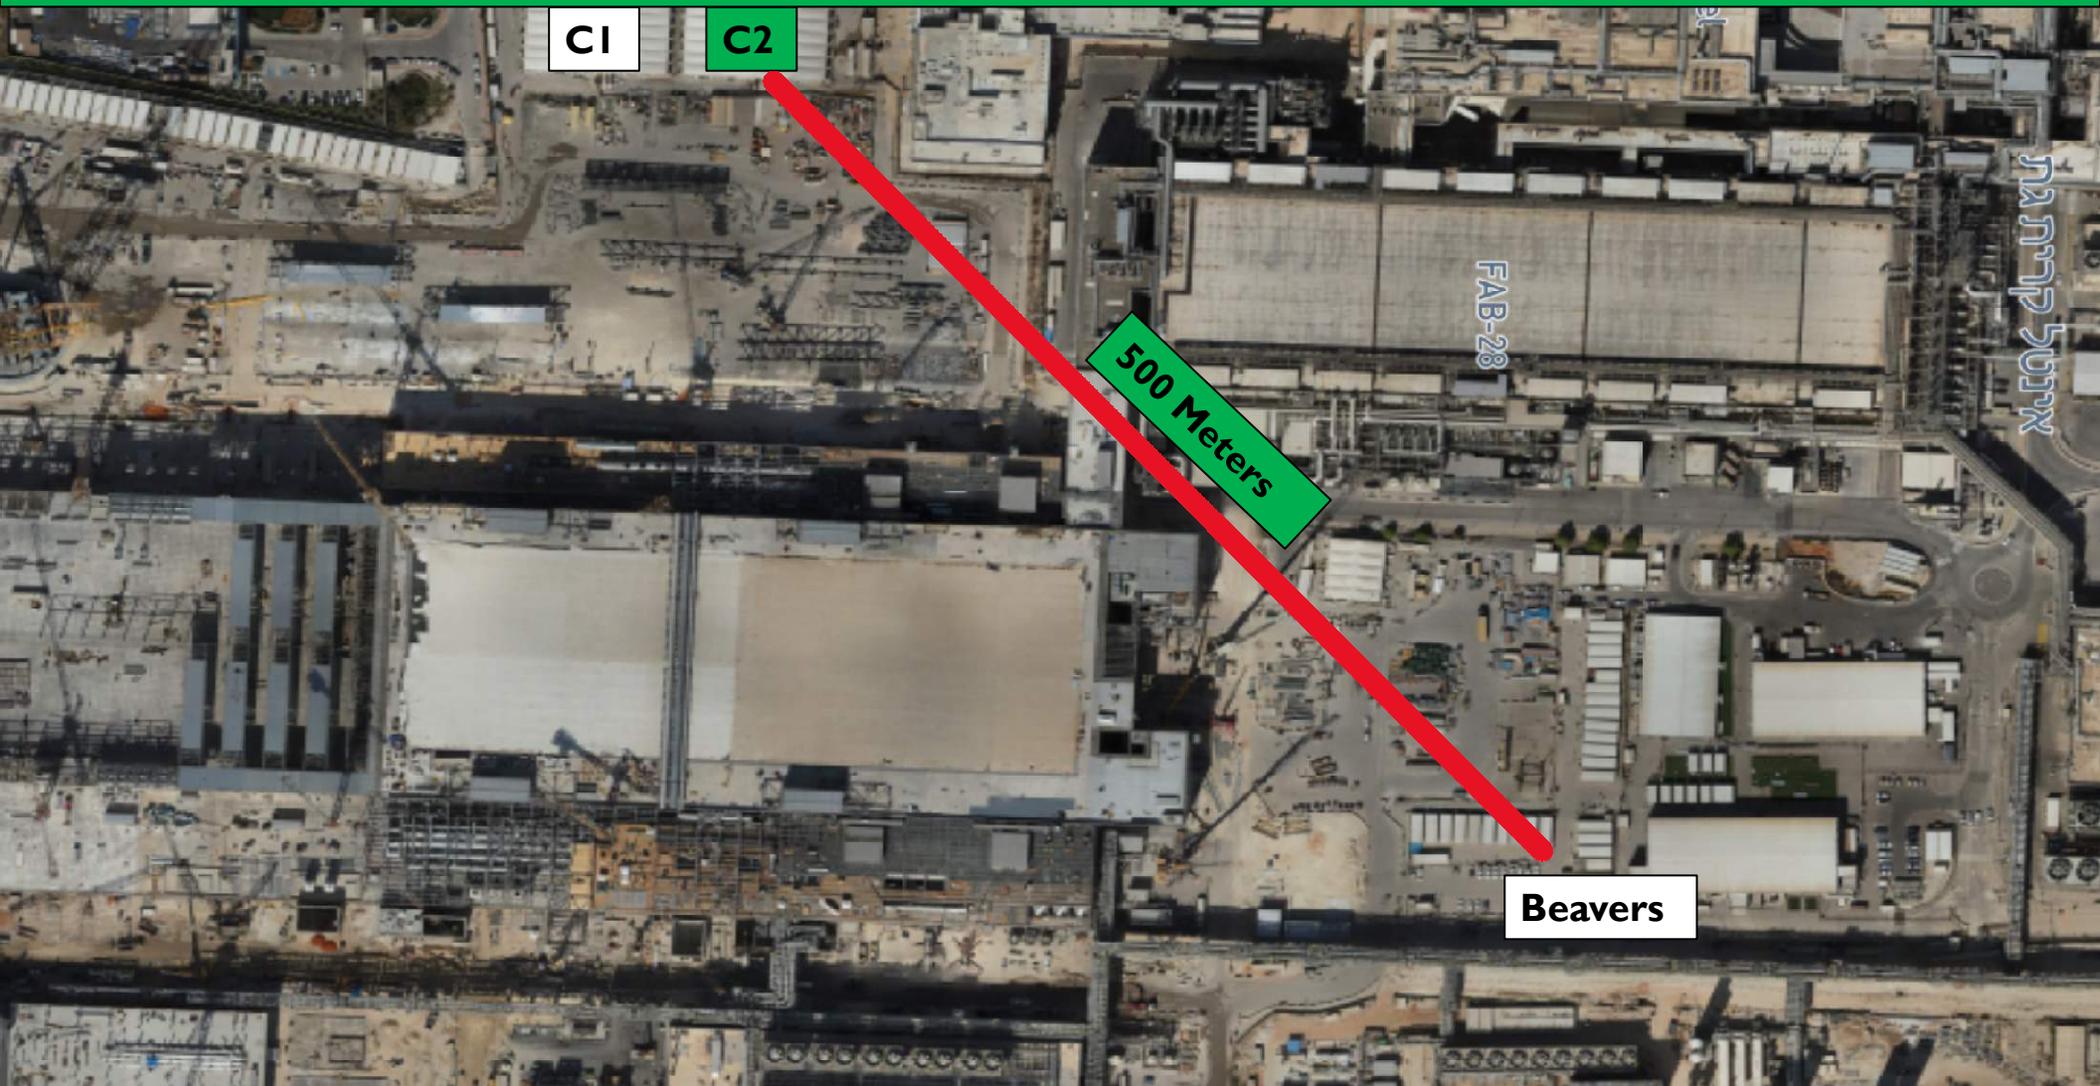


Flyable bathrooms



Fall protection equipment

All fall protection equipment must be accompanied by the manufacturer's instructions, or at least be able to present one in the field in real time.

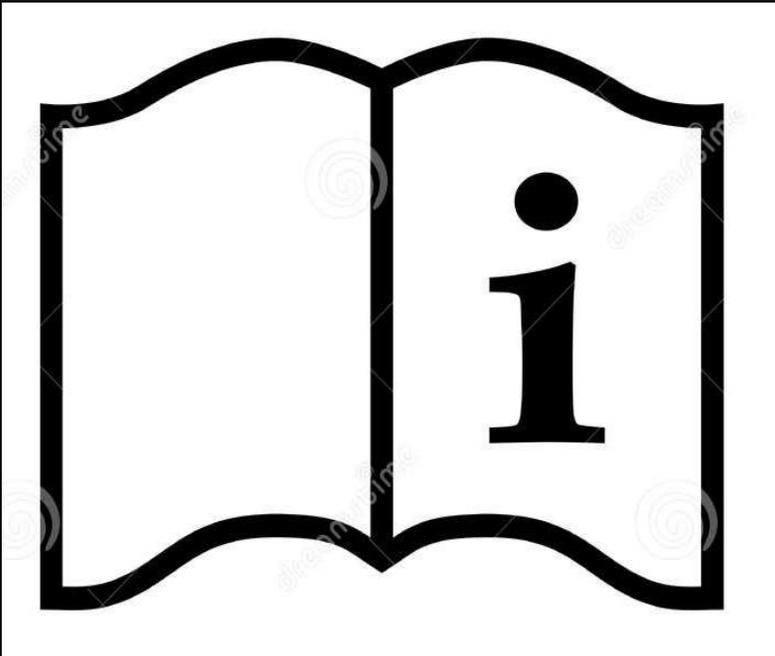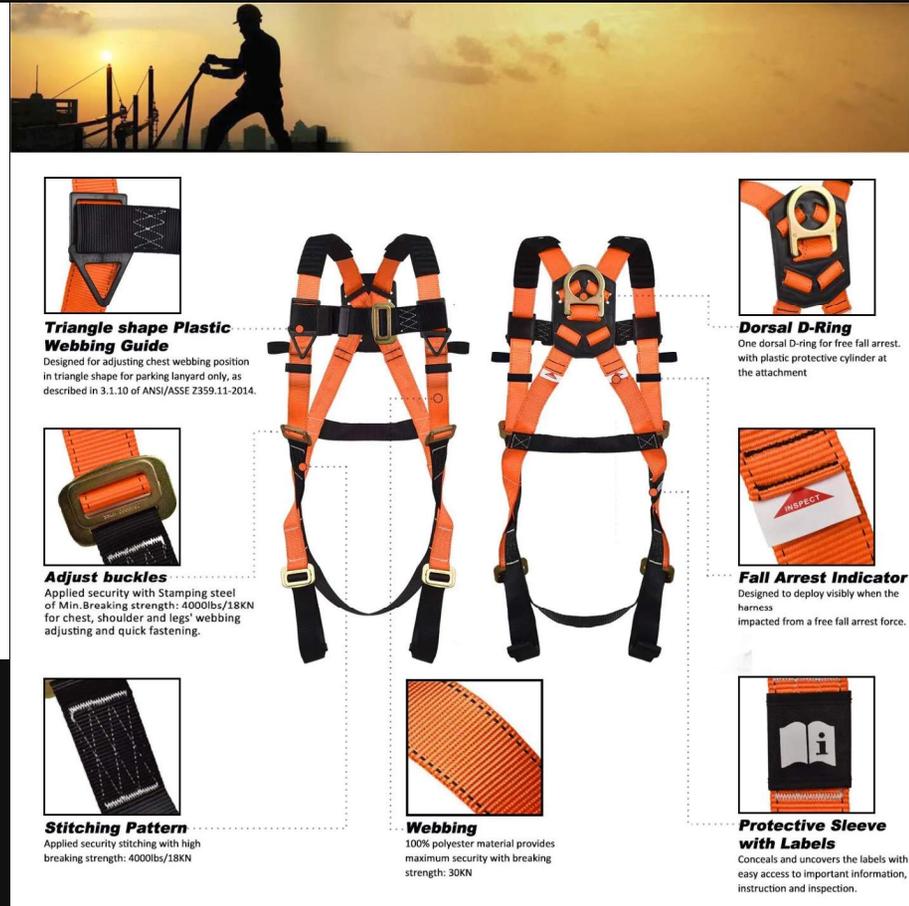Triangle shape Plastic Webbing Guide
Designed for adjusting chest webbing position in triangle shape for parking lanyard only, as described in 3.1.10 of ANSI/ASSE Z359.11-2014.

Adjust buckles
Applied security with Stamping steel of Min. Breaking strength: 4000lbs/18KN for chest, shoulder and legs' webbing adjusting and quick fastening.

Stitching Pattern
Applied security stitching with high breaking strength: 4000lbs/18KN

Webbing
100% polyester material provides maximum security with breaking strength: 30KN

Dorsal D-Ring
One dorsal D-ring for free fall arrest, with plastic protective cylinder at the attachment

Fall Arrest Indicator
Designed to deploy visibly when the harness impacted from a free fall arrest force.

Protective Sleeve with Labels
Conceals and uncovers the labels with easy access to important information, instruction and inspection.

Heat Index- September 18th

		temperature (°F)															
		80	82	84	86	88	90	92	94	96	98	100	102	104	106	108	110
Relative Humidity (%)	40	80	81	83	85	88	91	94	97	101	105	109	114	119	124	130	136
	45	80	82	84	87	89	93	96	100	104	109	114	119	124	130	137	
	50	81	83	85	88	91	95	99	103	108	113	118	124	131	137		
	55	81	84	86	89	93	97	101	106	112	117	124	130	137			
	60	82	84	88	91	95	100	105	110	116	123	129	137				
	65	82	86	89	93	98	103	108	114	121	128	136					
	70	83	86	90	95	100	105	112	119	126	134						
	75	84	88	92	97	103	109	116	124	132							
	80	84	89	94	100	106	113	121	129								
	85	85	90	96	102	110	117	126	135								
	90	86	91	98	105	113	122	131									
	95	86	93	100	108	117	127										
100	87	95	103	112	121	132											

Caution
 Extreme Caution
 Danger
 Extreme Danger

Caution

- Ensuring water and shaded areas available
- Acclimating workers
- Emergency planning and response
- Training workers and supervisors on the signs of heat stress and preventative measures
- Modified work schedules and/or rotating out workers
- Monitoring of workers for signs of heat stress

Daily Coordination Meeting



14:00 Sign In
