

Daily Coordination Meeting



14:00 Sign In

Daily Coordination Meeting

General Topics:


- **BGY Shut Down Until Sunday**
- **Weekend Work**



SE Loading dock
ramp
2:00am




UTILITY LEVEL PRESS TEST

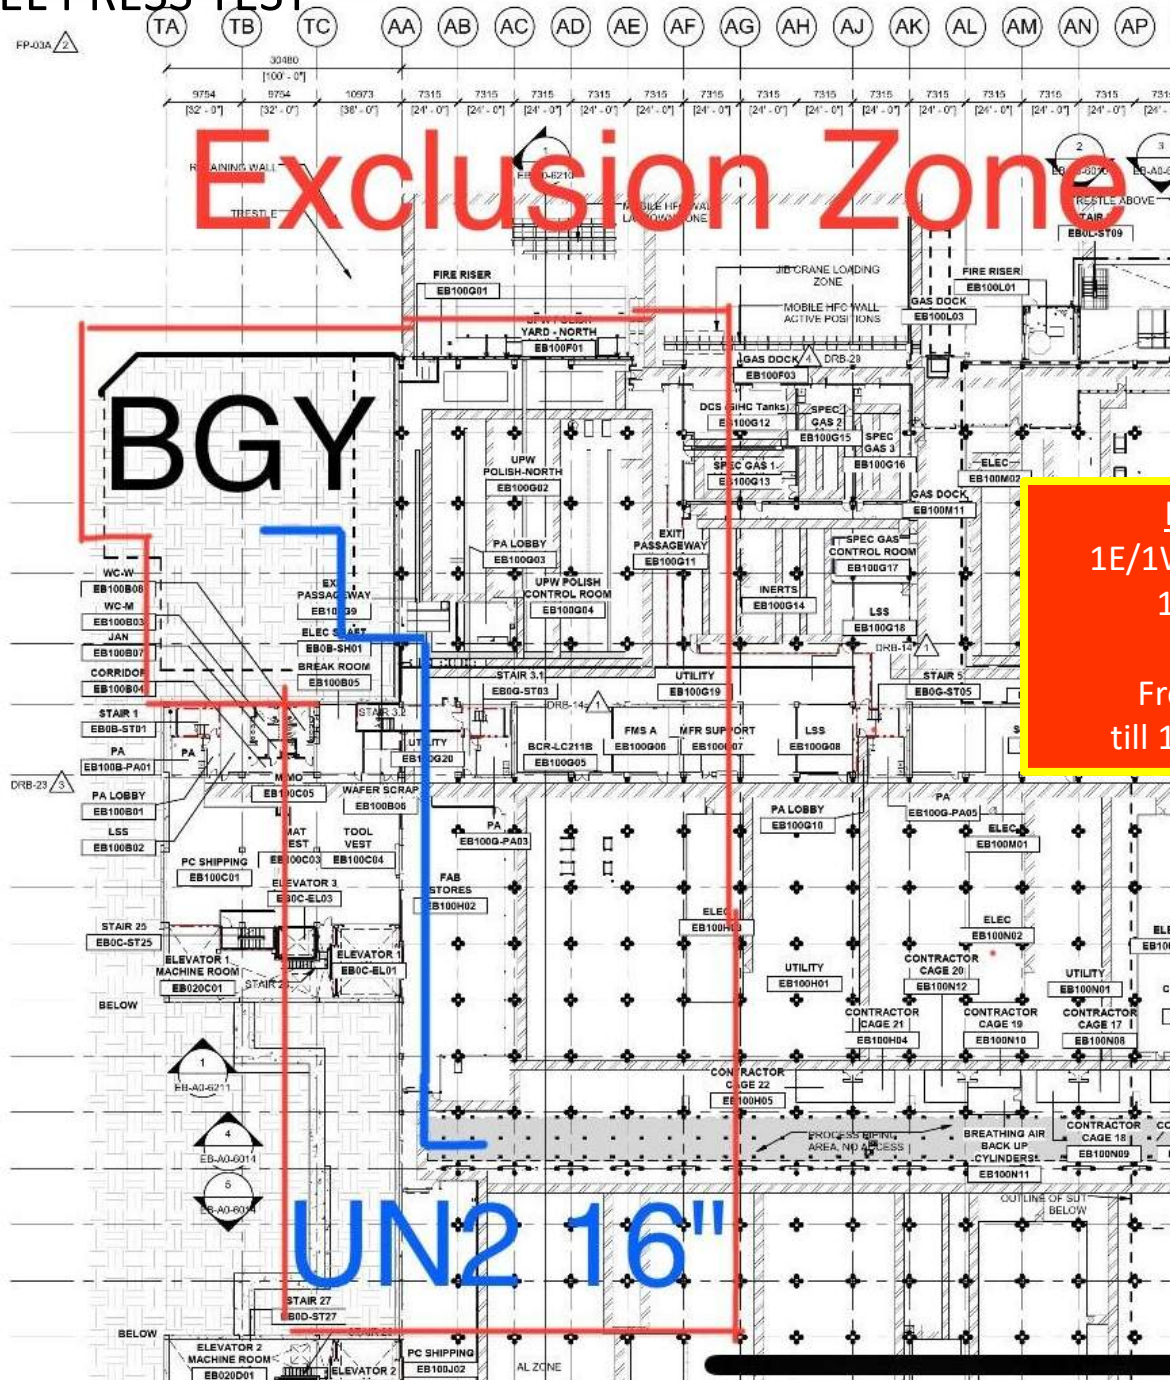

LESICO
1E/1W Pres. Test
1/30-31


From 1/30
till 1/31 13:00

UTILITY LEVEL MOD1

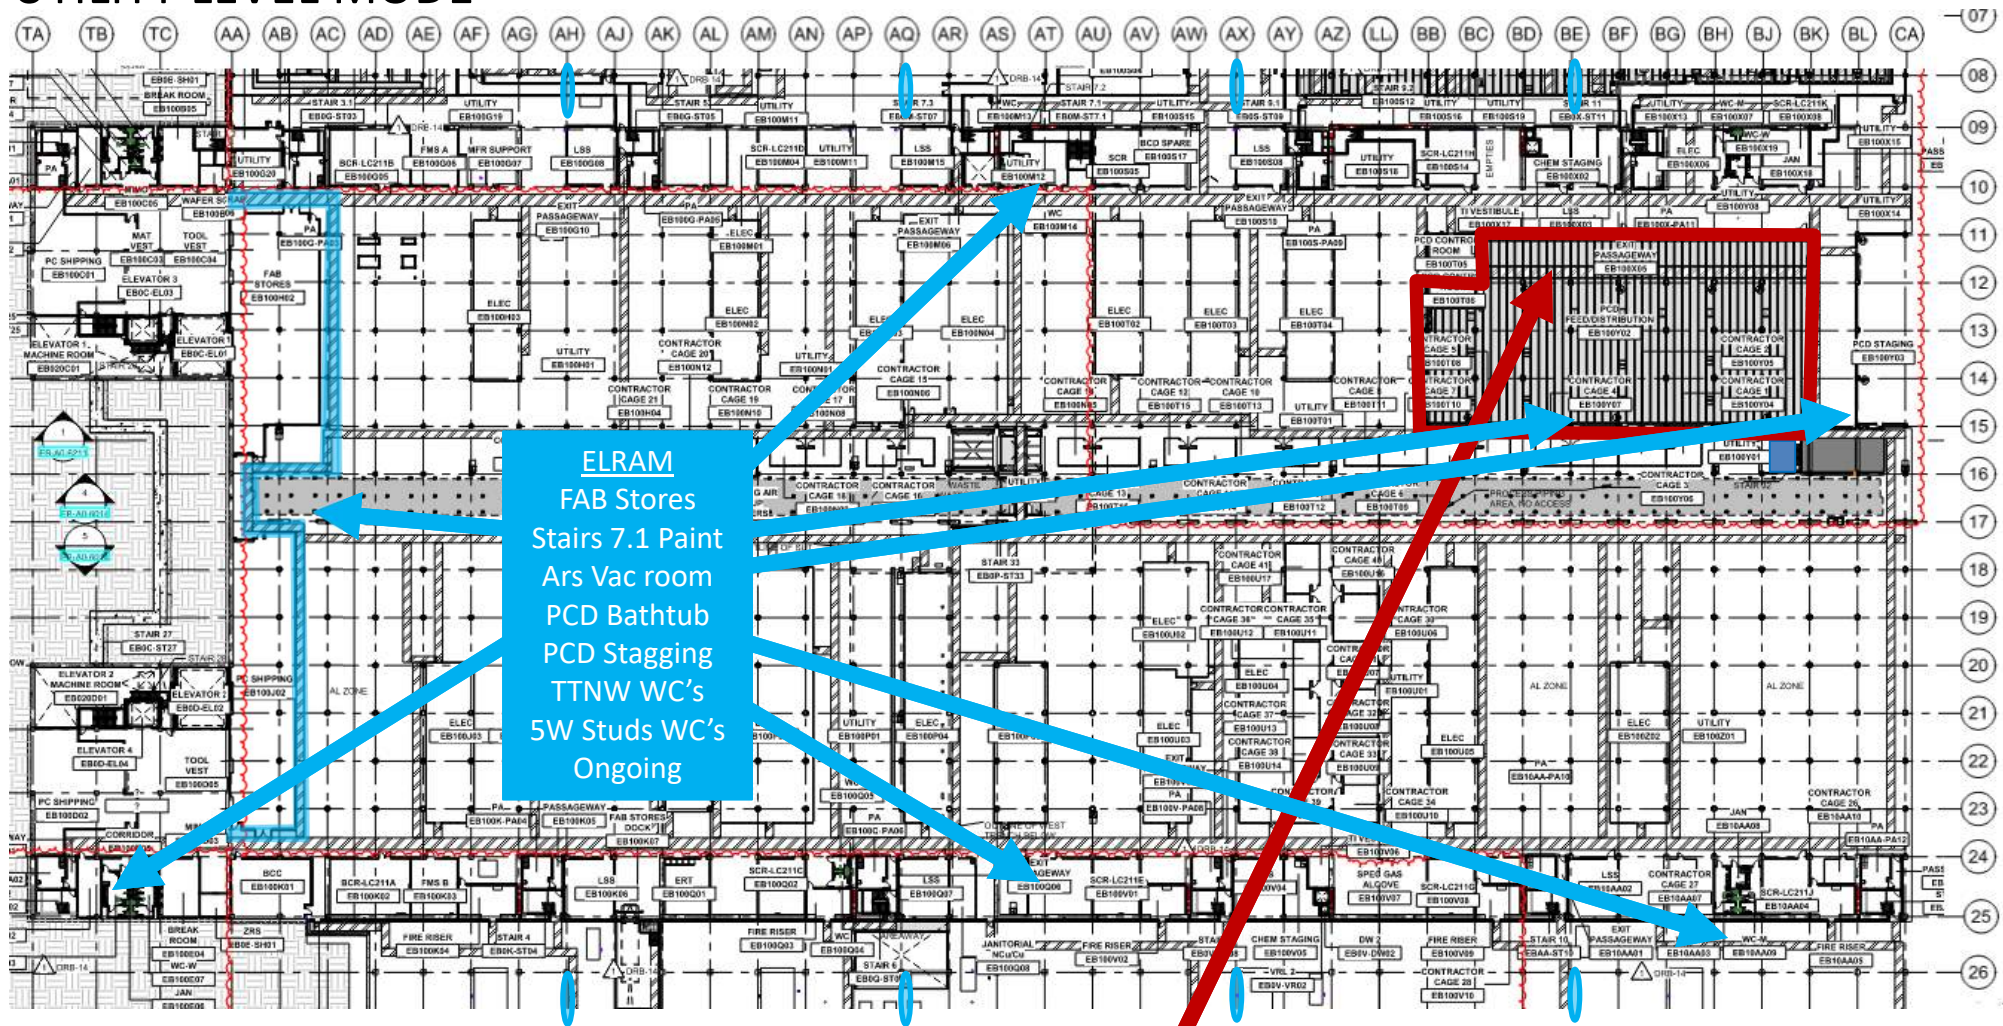




UTILITY LEVEL MOD2

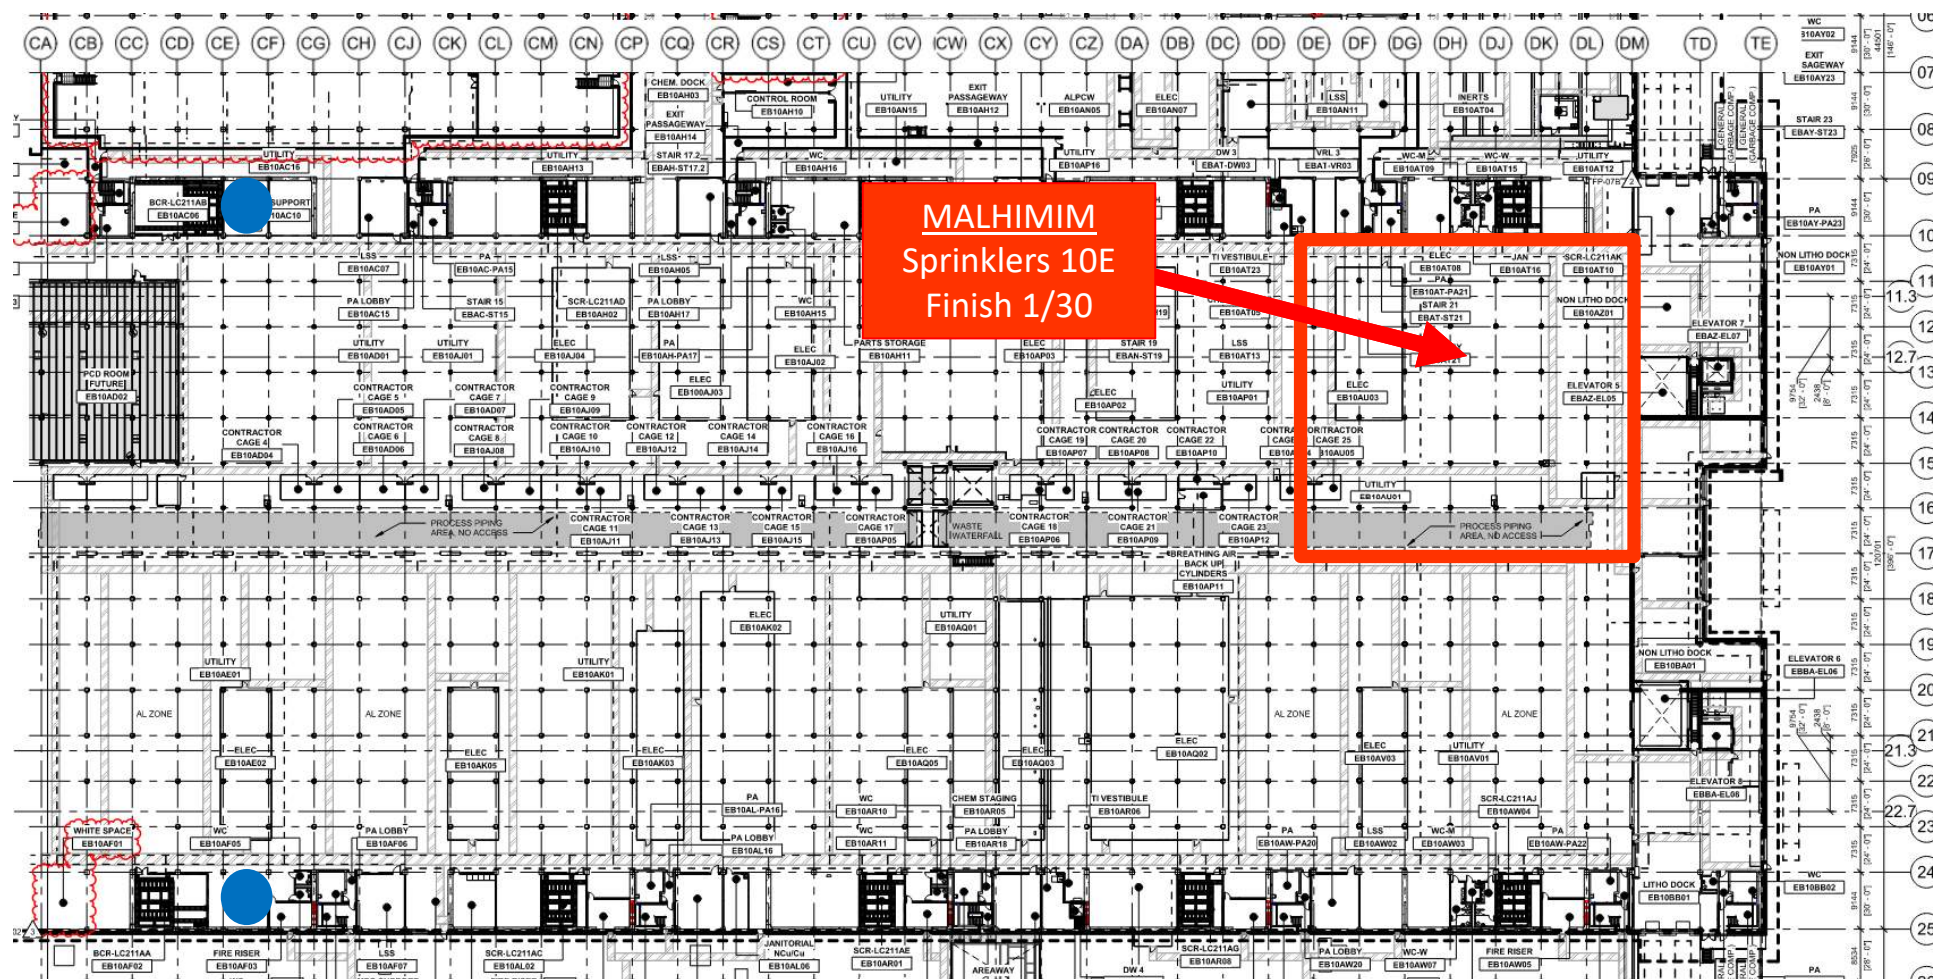

SUT 38.1 LEVEL

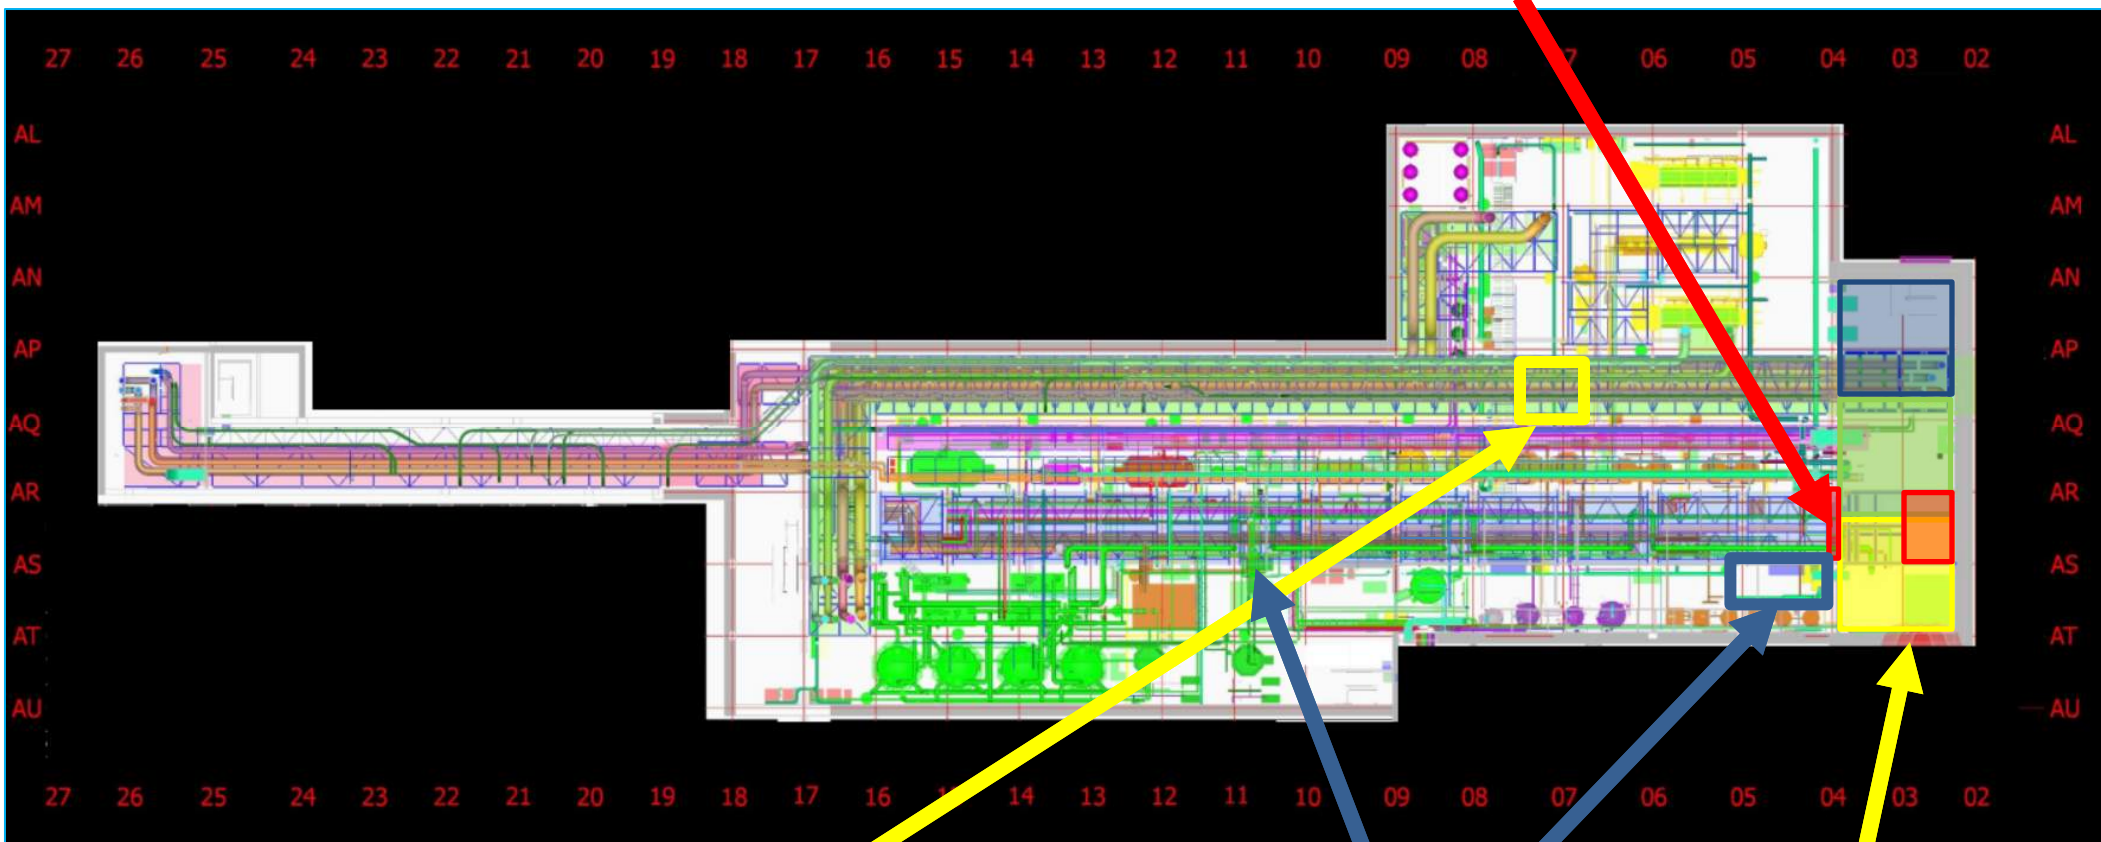

OH roll-up door
Install 30/1

CRC

HYG
Need to install SOG platform +
Bodice Grating ASAP

Topping slab Schedule


Pour 1 – 1/9 – 1/15 V
Pour 2 – 1/15 – 1/22 V
Pour 3 -1/22-1/27 V
Pour 4 – 1/28-2/4



HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL

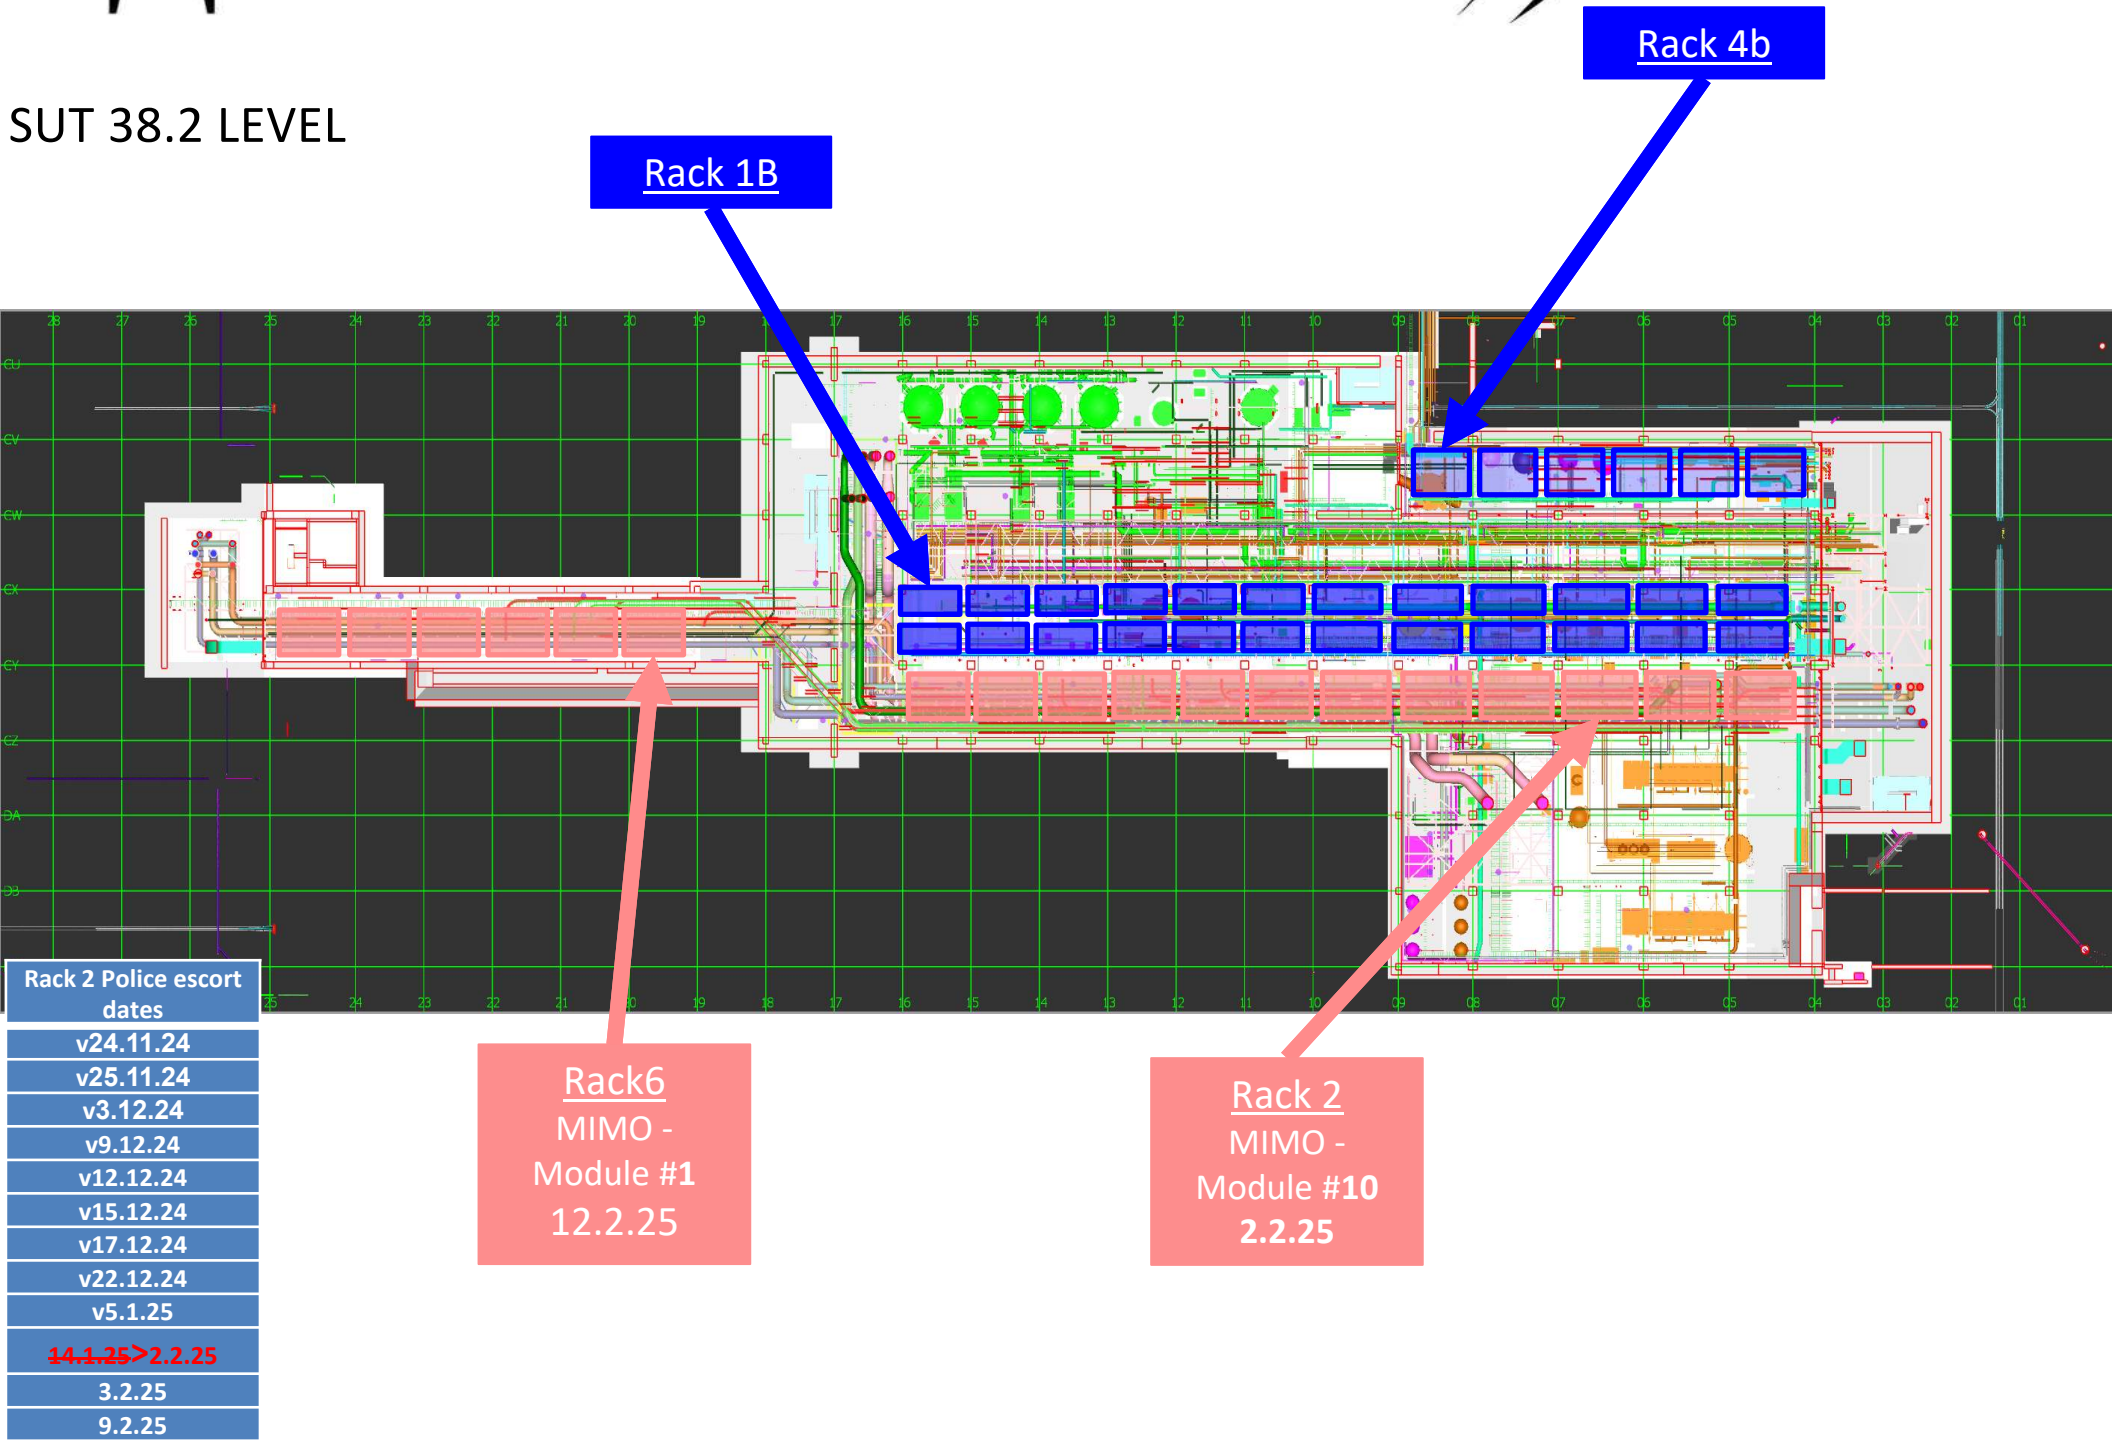

Rack 1B

Rack 4b

Rack 6
MIMO -
Module #1
12.2.25

Rack 2
MIMO -
Module #10
2.2.25

**Rack 2 Police escort
dates**

v24.11.24

v25.11.24

v3.12.24

v9.12.24

v12.12.24

v15.12.24

v17.12.24

v22.12.24


v5.1.25

14.1.25 > 2.2.25


3.2.25

9.2.25


SUBFAB BUILDOUT MOD 1

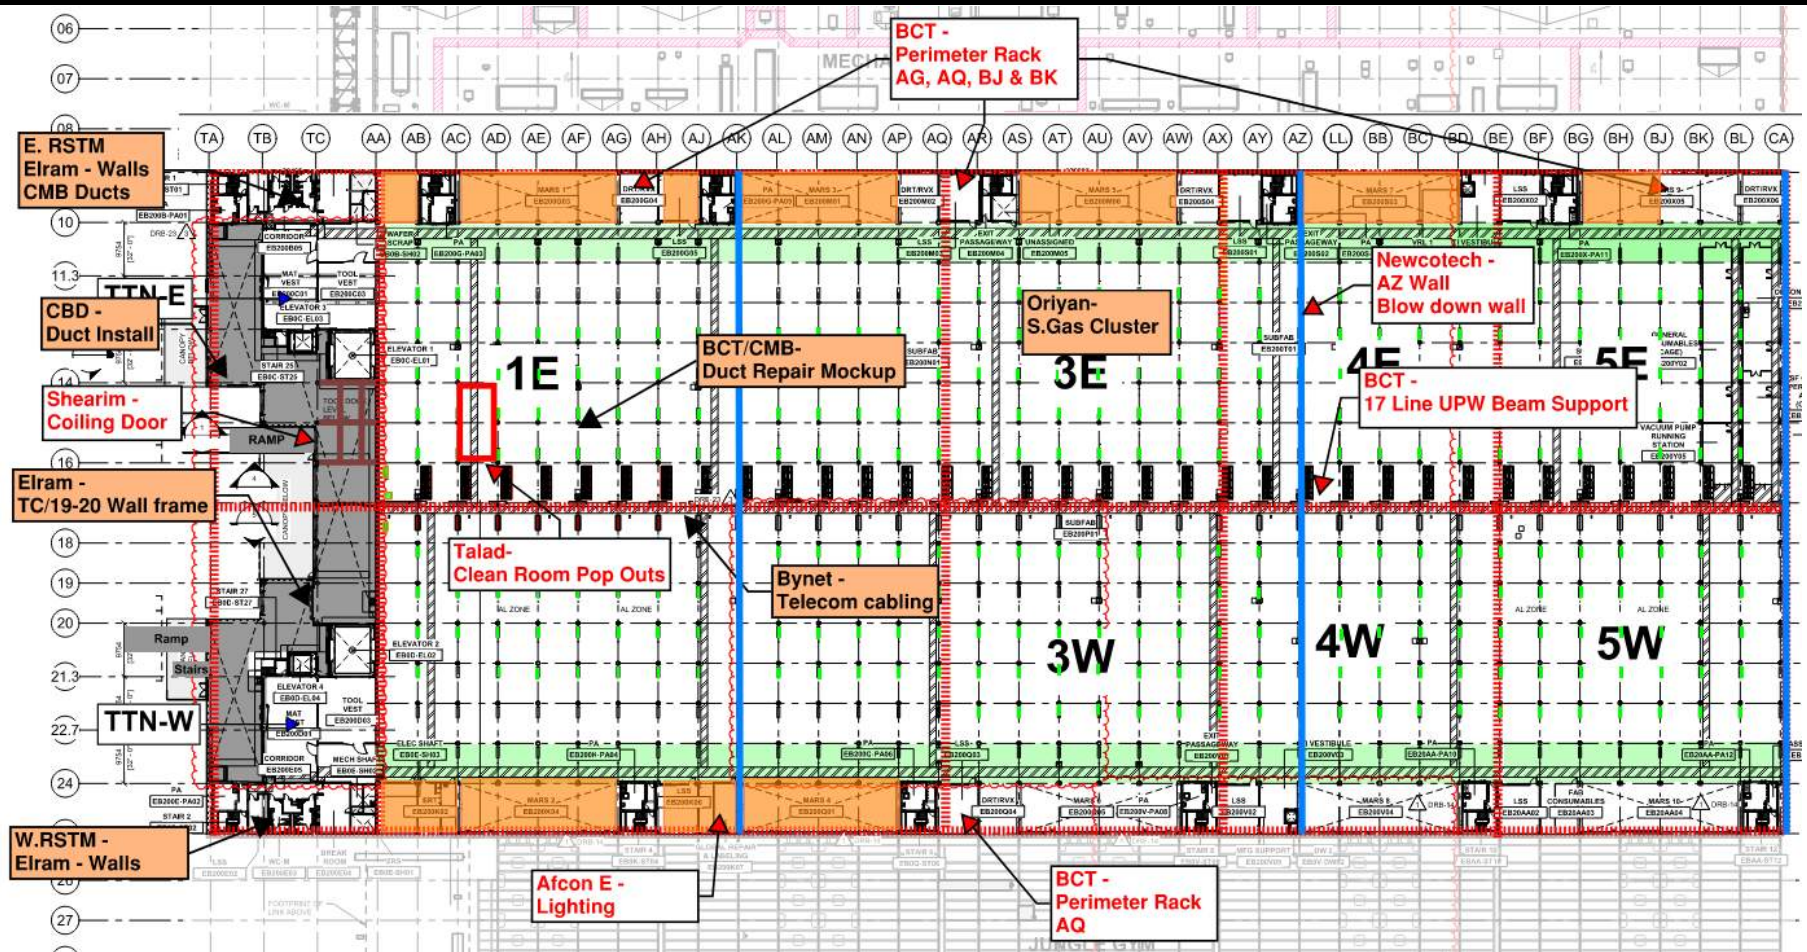

SUBFAB CRC TOPCOAT

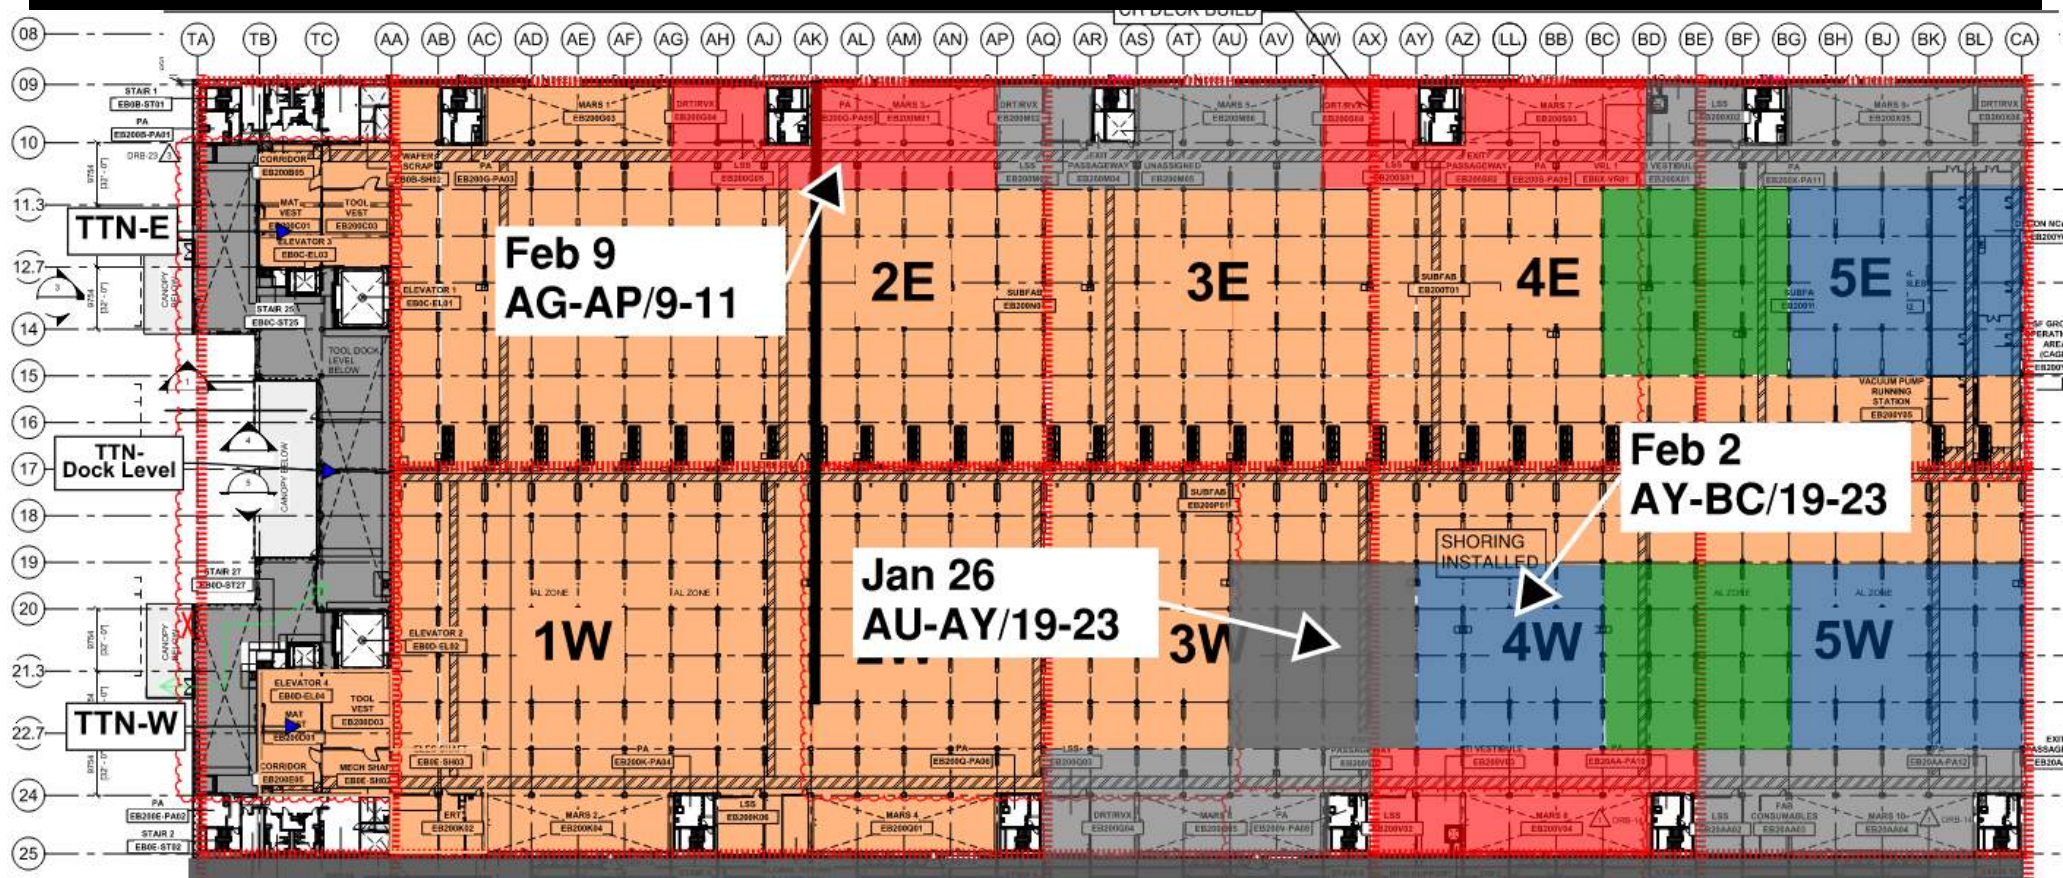



BCT Pressure Test Today

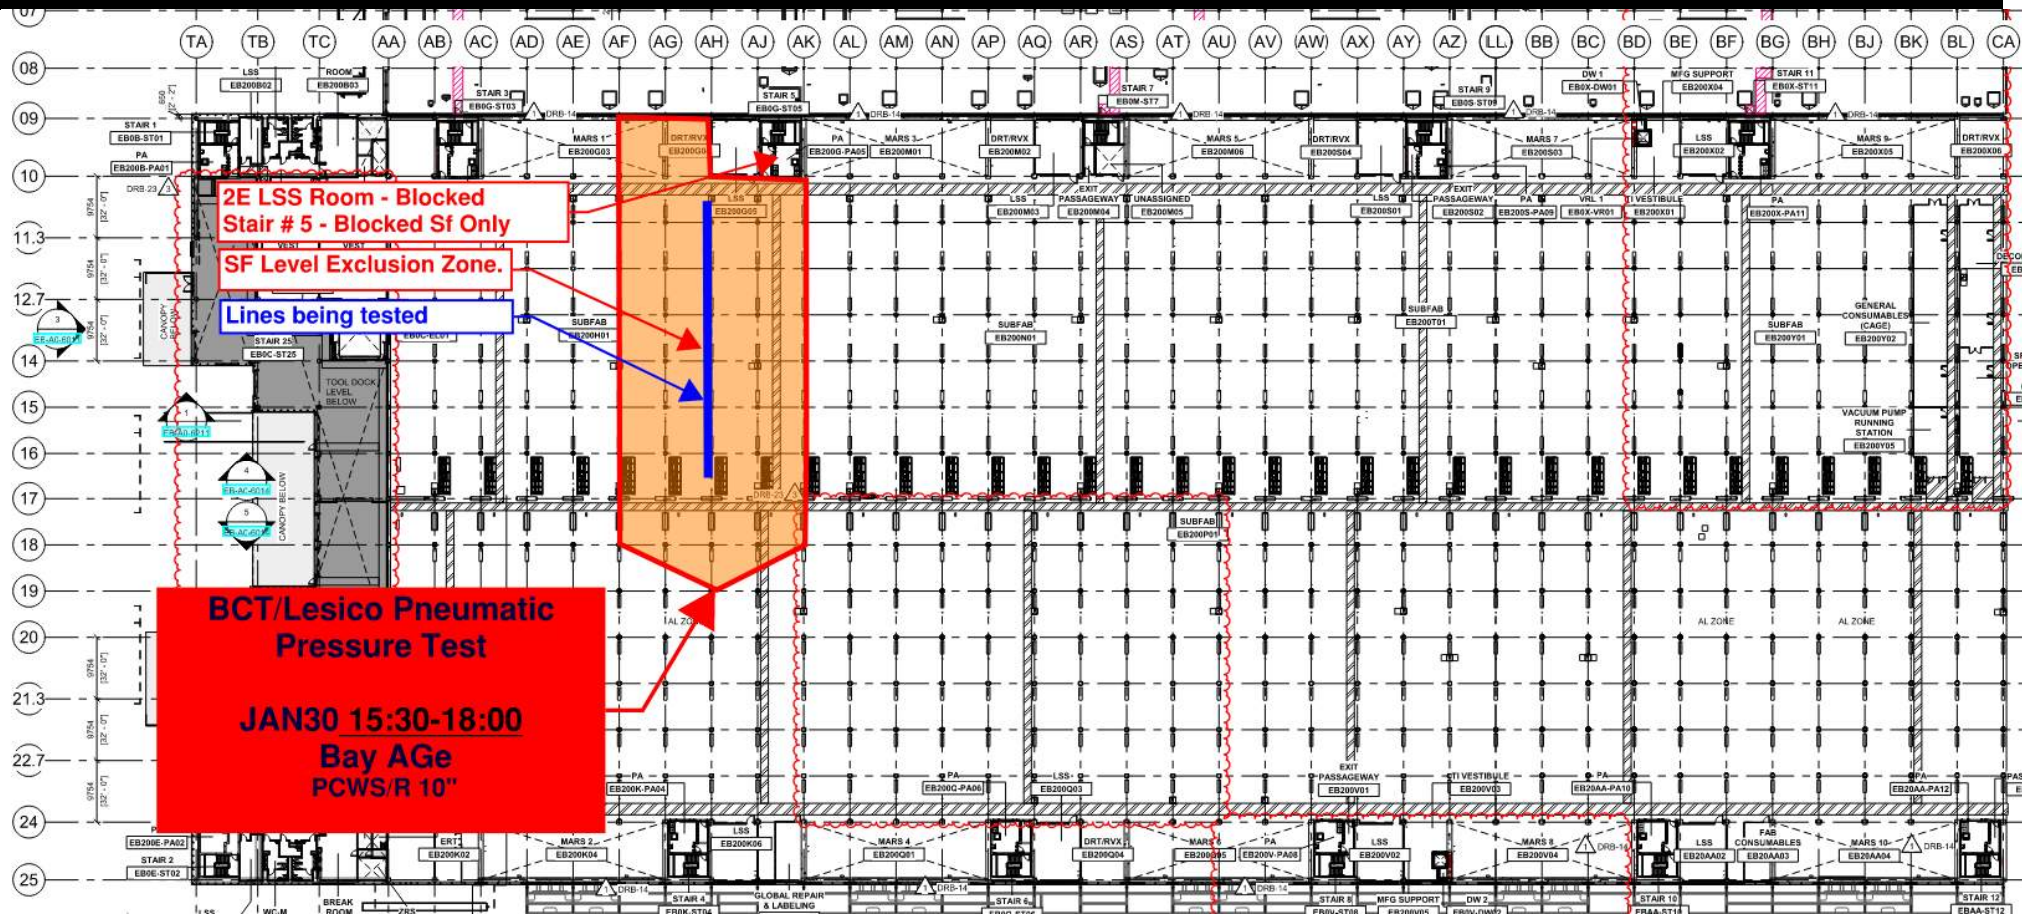



BCT Pressure Test Tomorrow

SUBFAB BUILDOUT MOD 2

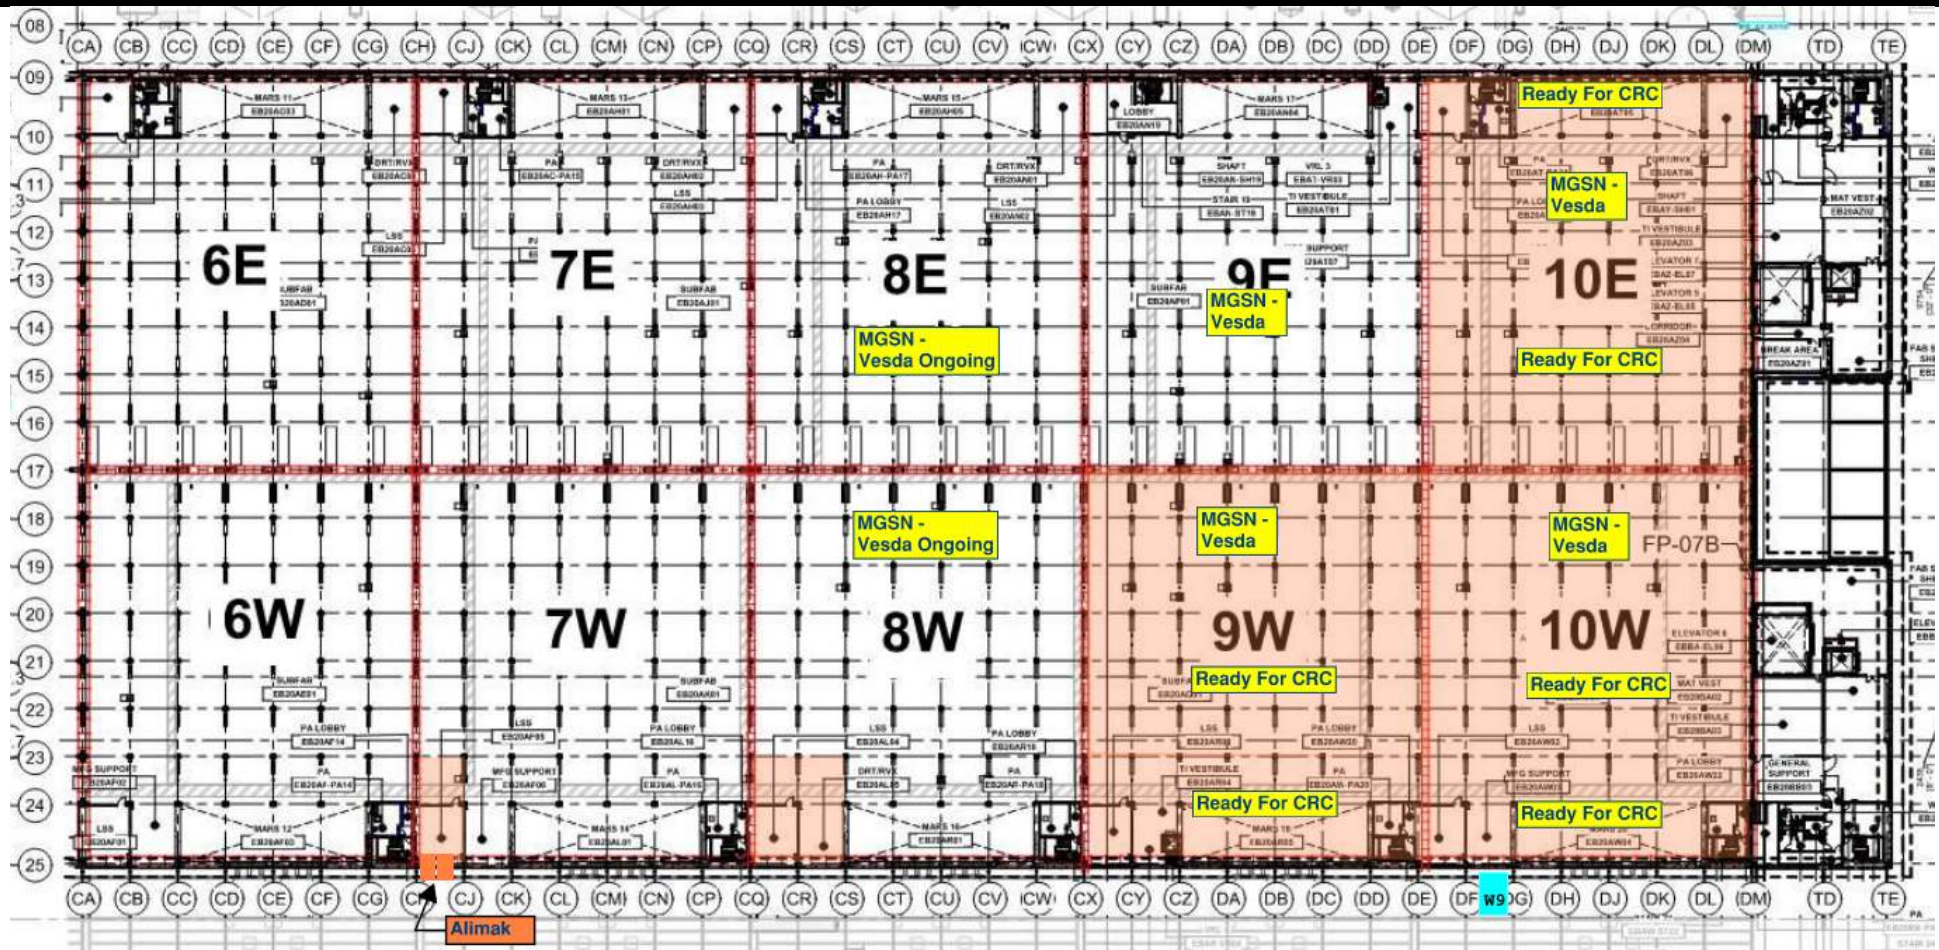

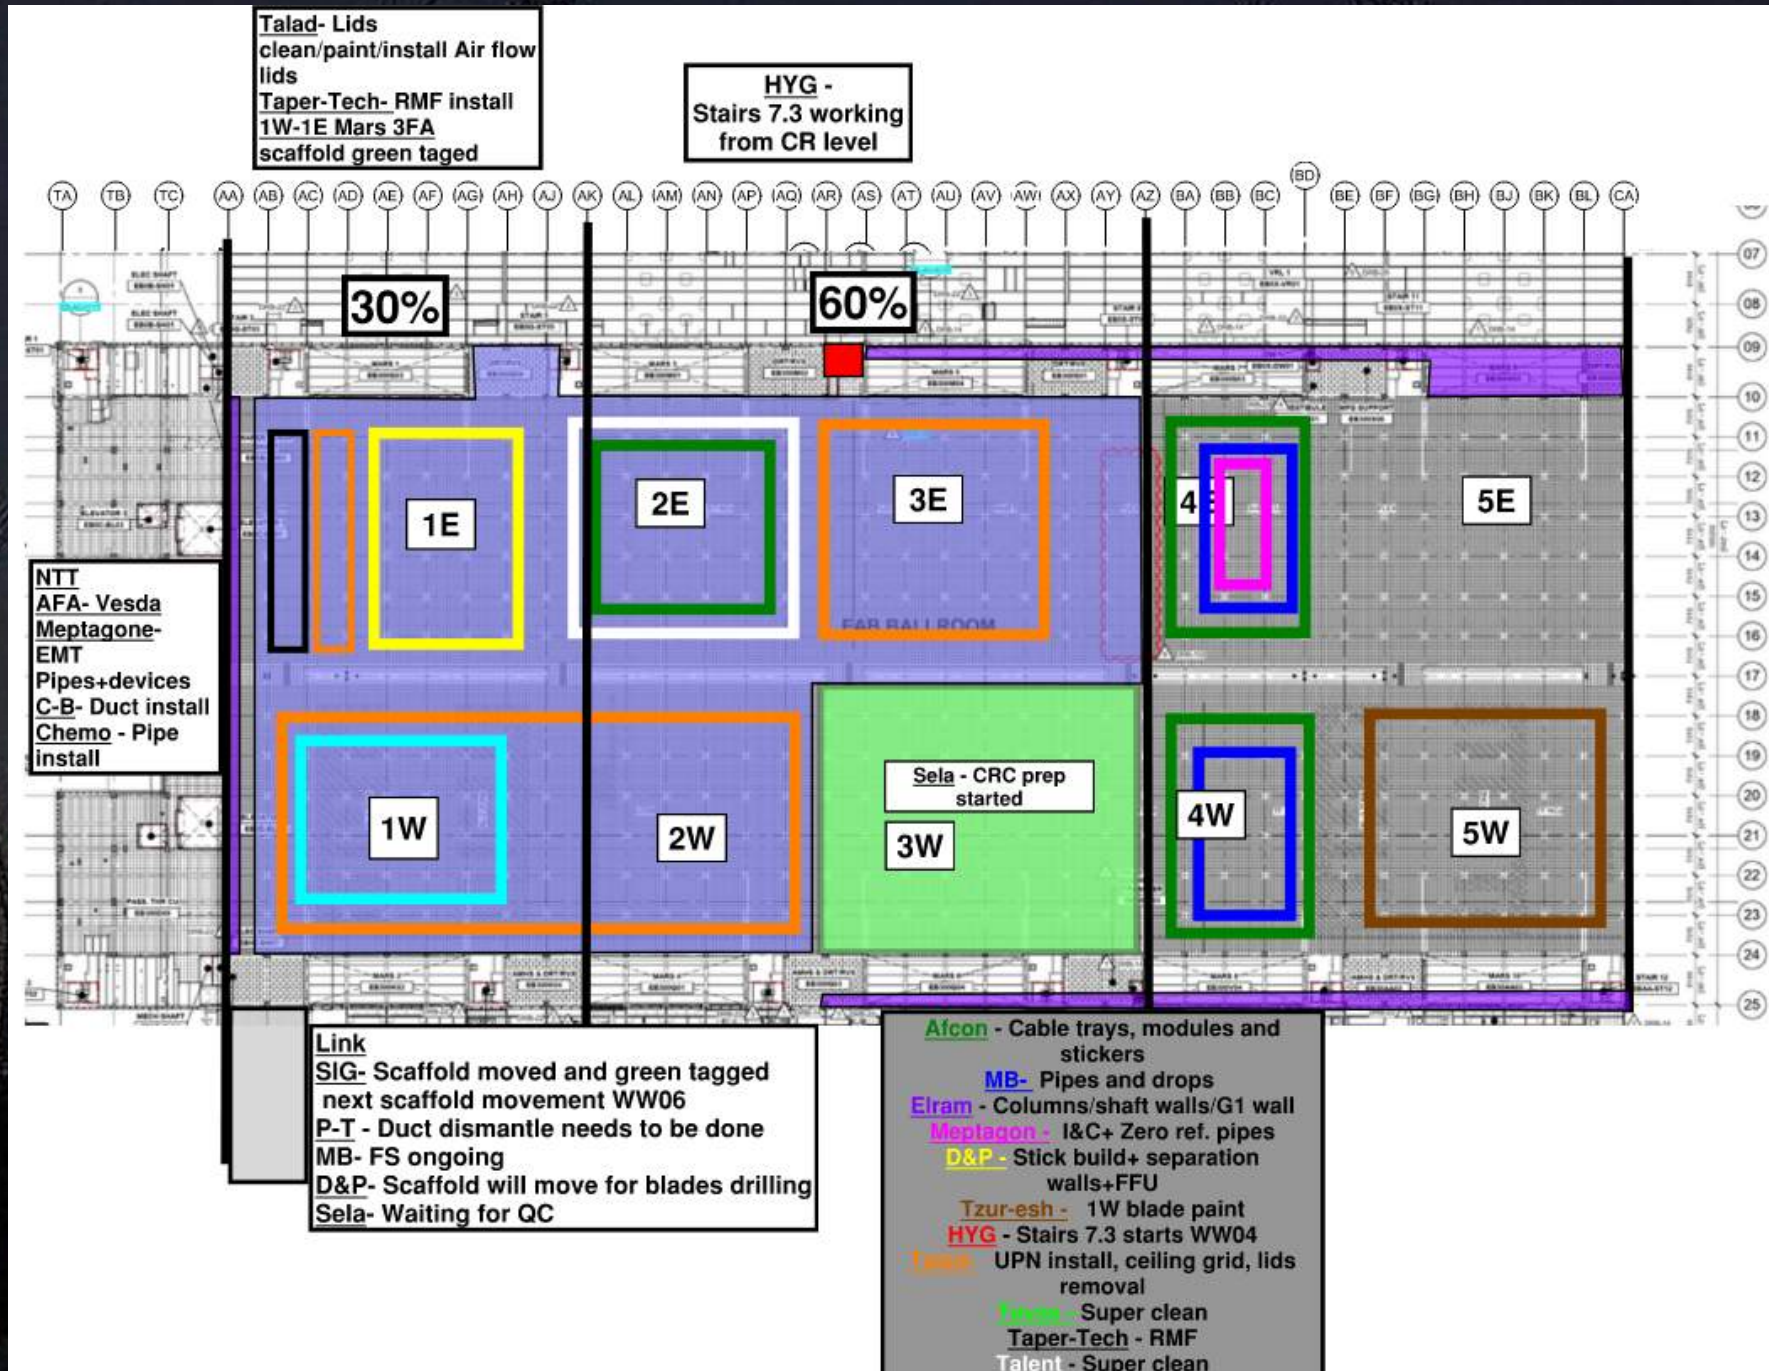

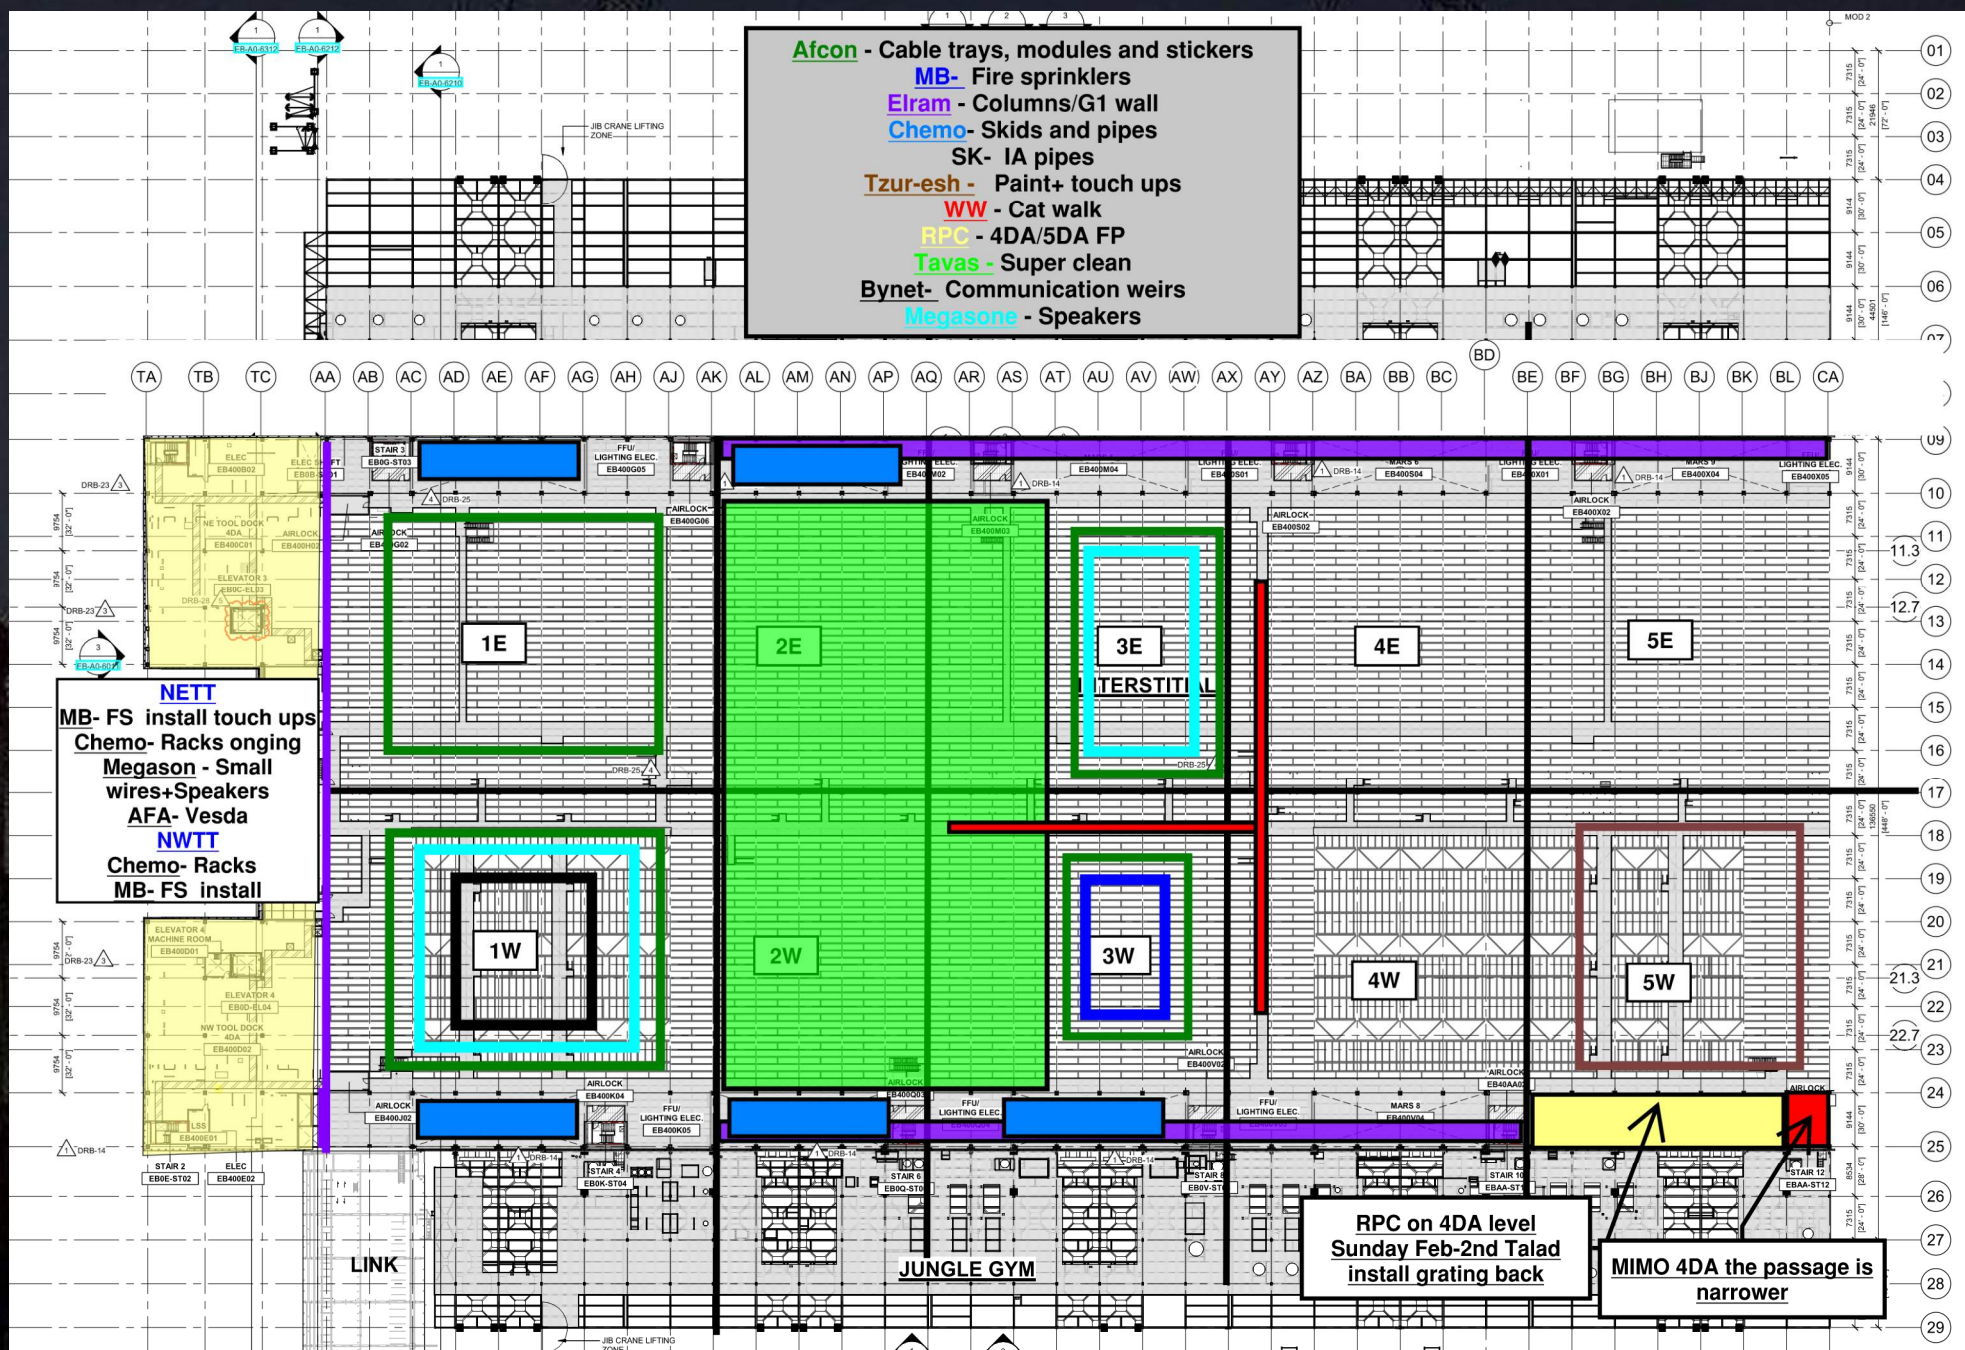



Chemo Aharon will perform two test on UPN 113, tomorrow at 5 PM

**MARS (3) at zone 2E at the CR, will will also
effect on small portion from zone 1P lift 2**





Main boom 44 m

Radius (m)	Jib length in (m)							
	20	29	41	53	62	71	83	95
14.2	64.2	1	1	1	1	1	1	1
17	52.3	50.4						
22	38.0	37.7	34.1					
24	34.1	33.9	33.1	24.5				
26	30.9	30.7	30.3	24.3				
28		28.1	27.7	23.8	18.5			
30		25.8	25.4	23.3	18.2	14.3		
34		22.1	21.8	21.3	17.5	13.8	9.8	
36		12.1	20.3	19.9	17.2	13.7	9.6	
38			19.0	18.5	17.0	13.4	9.4	6.2
46			14.9	14.5	14.2	12.6	8.6	5.6
55				11.4	11.2	10.8	7.9	5.0
65					8.8	8.4	7.3	4.5
75						6.7	6.3	3.9
85							4.9	n.c.
100								

South Tool Tower AHU's - Tapertech - Set Date 2/2/2025

AHU's = 10 Tons Maximum

LR1250

83 degree main Boom at 36 meter Radius = 20.3 Ton Capacity
49% of Capacity



Personal protocol violations

Personal protocol violations are documented and addressed in the following order:

*Employees name and number will be taken.

- **First violation:** team leader\champion will be informed.
- **Second violation:** team leader\champion will be informed + requires additional protocol training
- **Third violation:** Escalated to the HCC project manager.

Please note that violations will be based on the protocol spec as instructed during the trainings:

PL3 Dress code:



Put on Hair-net



Put on Beard cover



Put on shoe cover



Wear Latex Gloves



Siding - West FAB - JYG

BLOWDOWN 30%

	TA	TB	TC	TD	TE	TF	TG	TH	TI	TJ	TK	TL	TM	TN	TO	TP	TQ	TR	TS	TT	TU	TV	TW	TX	TY	TZ	BA	BB	BC	BD	BE	BF	BG	BH	BI	BJ	BK	BL	CA
	1001 / 1002			601 / 602			611 / 612			621 / 622			631 / 632			641 / 642			651 / 652			611 / 612			621 / 622			631 / 632			641 / 642			651 / 652					
Total	20	20	20	15	10	21	31	31	31	31	31	31	30	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	
Installed	20	20	27	15	10	21	31	31	31	31	31	31	30	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	
IC	100%	100%	96%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	
SRA																																						0	
MDA																																						0	
2FK																																						0	
2FA																																						0	
22A 2F																																						0	
UL																																						0	

Link

LM BL BT BO BV BW BX BY BZ CA CB CC CD CE CF CG CH CI CJ CK CL CM CN CO CP CQ CR CS CT CU CV CW CX CY CZ DA DB DC DD DE DF DG DH DI DJ DK DL DM DN DO DP DQ DR DS DT DU DV DW DX DY DZ EA EB EC ED EE EF EG EH EI EJ EK EL EM EN EO EP EQ ER ES ET EU EV EW EX EY EZ FA FB FC FD FE FF FG FH FI FJ FK FL FM FN FO FP FQ FR FS FT FU FV FW FX FY FZ GA GB GC GD GE GF GH GI GJ GK GL GM GN GO GP GQ GR GS GT GU GV GW GX GY GZ HA HB HC HD HE HF HG HI HJ HK HL HM HN HO HP HQ HR HS HT HU HV HW HX HY HZ IA IB IC ID IE IF IG IH II IJ IK IL IM IN IO IP IQ IR IS IT IU IV IW IX IY IZ JA JB JC JD JE JF JG JH JI JJ JK JL JM JN JO JP JQ JR JS JT JU JV JW JX JY JZ KA KB KC KD KE KF KG KH KI KJ KL KM KN KO KP KQ KR KS KT KU KV KW KX KY KZ LA LB LC LD LE LF LG LH LI LJ LK LL LM LN LO LP LQ LR LS LT LU LV LW LX LY LZ MA MB MC MD ME MF MG MH MI MJ MK ML MN MO MP MQ MR MS MT MU MV MW MX MY MZ NA NB NC ND NE NF NG NH NI NJ NK NL NO NP NQ NR NS NT NU NV NW NX NY NZ OA OB OC OD OE OF OG OH OI OJ OK OL OM ON OP OQ OR OS OT OU OV OW OX OY OZ PA PB PC PD PE PF PG PH PI PJ PK PL PM PN PO PP PQ PR PS PT PU PV PW PX PY PZ QA QB QC QD QE QF QG QH QI QJ QK QL QM QN QO QQ QR QS QT QU QV QW QX QY QZ RA RB RC RD RE RF RG RH RI RJ RK RL RM RN RO RP RQ RR RS RT RU RV RW RX RY RZ SA SB SC SD SE SF SG SH SI SJ SK SL SM SN SO SP SQ SR SS ST SU SV SW SX SY SZ TA TB TC TD TE TF TG TH TI TJ TK TL TM TN TO TP TQ TR TS TT TU TV TW TX TY TZ UA UB UC UD UE UF UG UH UI UJ UK UL UM UN UO UP UQ UR US UT UU UV UW UX UY UZ VA VB VC VD VE VF VG VH VI VJ VK VL VM VN VO VP VQ VR VS VT VU VW VX VY VZ WA WB WC WD WE WF WG WH WI WJ WK WL WM WN WO WP WQ WR WS WT WU WV WW WX WY WZ XA XB XC XD XE XF XG XH XI XJ XK XL XM XN XO XP XQ XR XS XT XU XV XW XX XY XZ YA YB YC YD YE YF YG YH YI YJ YK YL YM YN YO YP YQ YR YS YT YU YV YW YX YY YZ ZA ZB ZC ZD ZE ZF ZG ZH ZI ZJ ZK ZL ZM ZN ZO ZP ZQ ZR ZS ZT ZU ZV ZW ZX ZY ZZ

Siding - East FAB - PSSS

BLOWDOWN 30%

OF - 172166.0

CK - 167798.0

Q 16'-1" - 162,037.0

1 - 156,825.2


150,349.064

143,433.6

CK - 147,700.0

1 - 145,647.2

DEMO

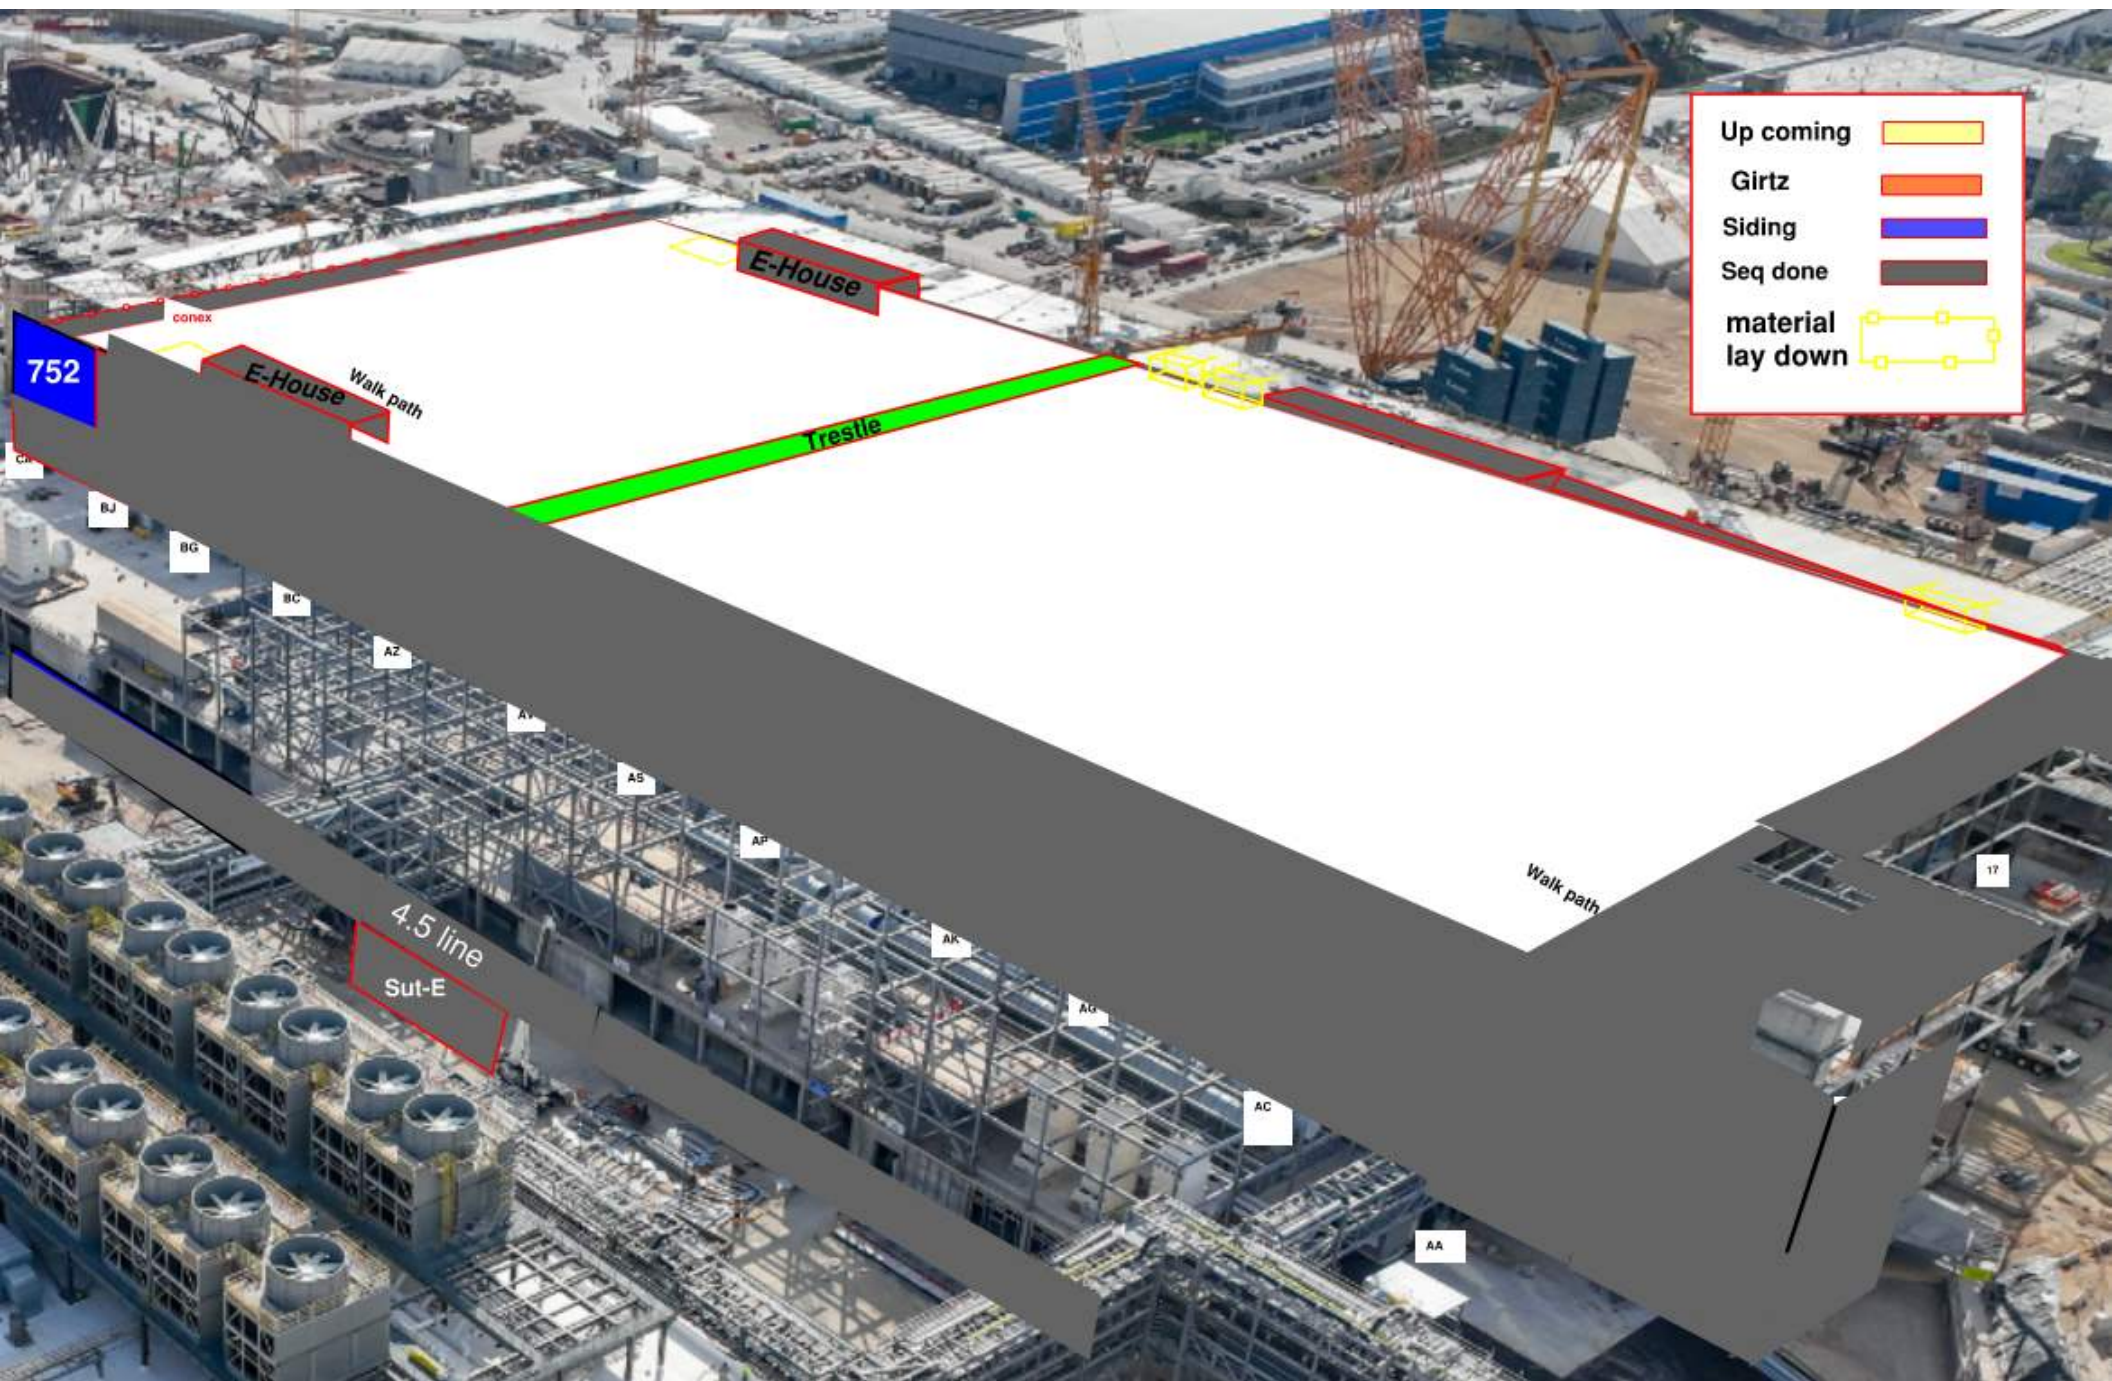

Up coming	
Girtz	
Siding	
Seq done	
material lay down	

752

E-House

E-House

Walk path

Trestle

Walk path

4.5 line
Sut-E

17

BJ

BG

BC

AZ

AV

AS


AP

AK

AG

AC

AA

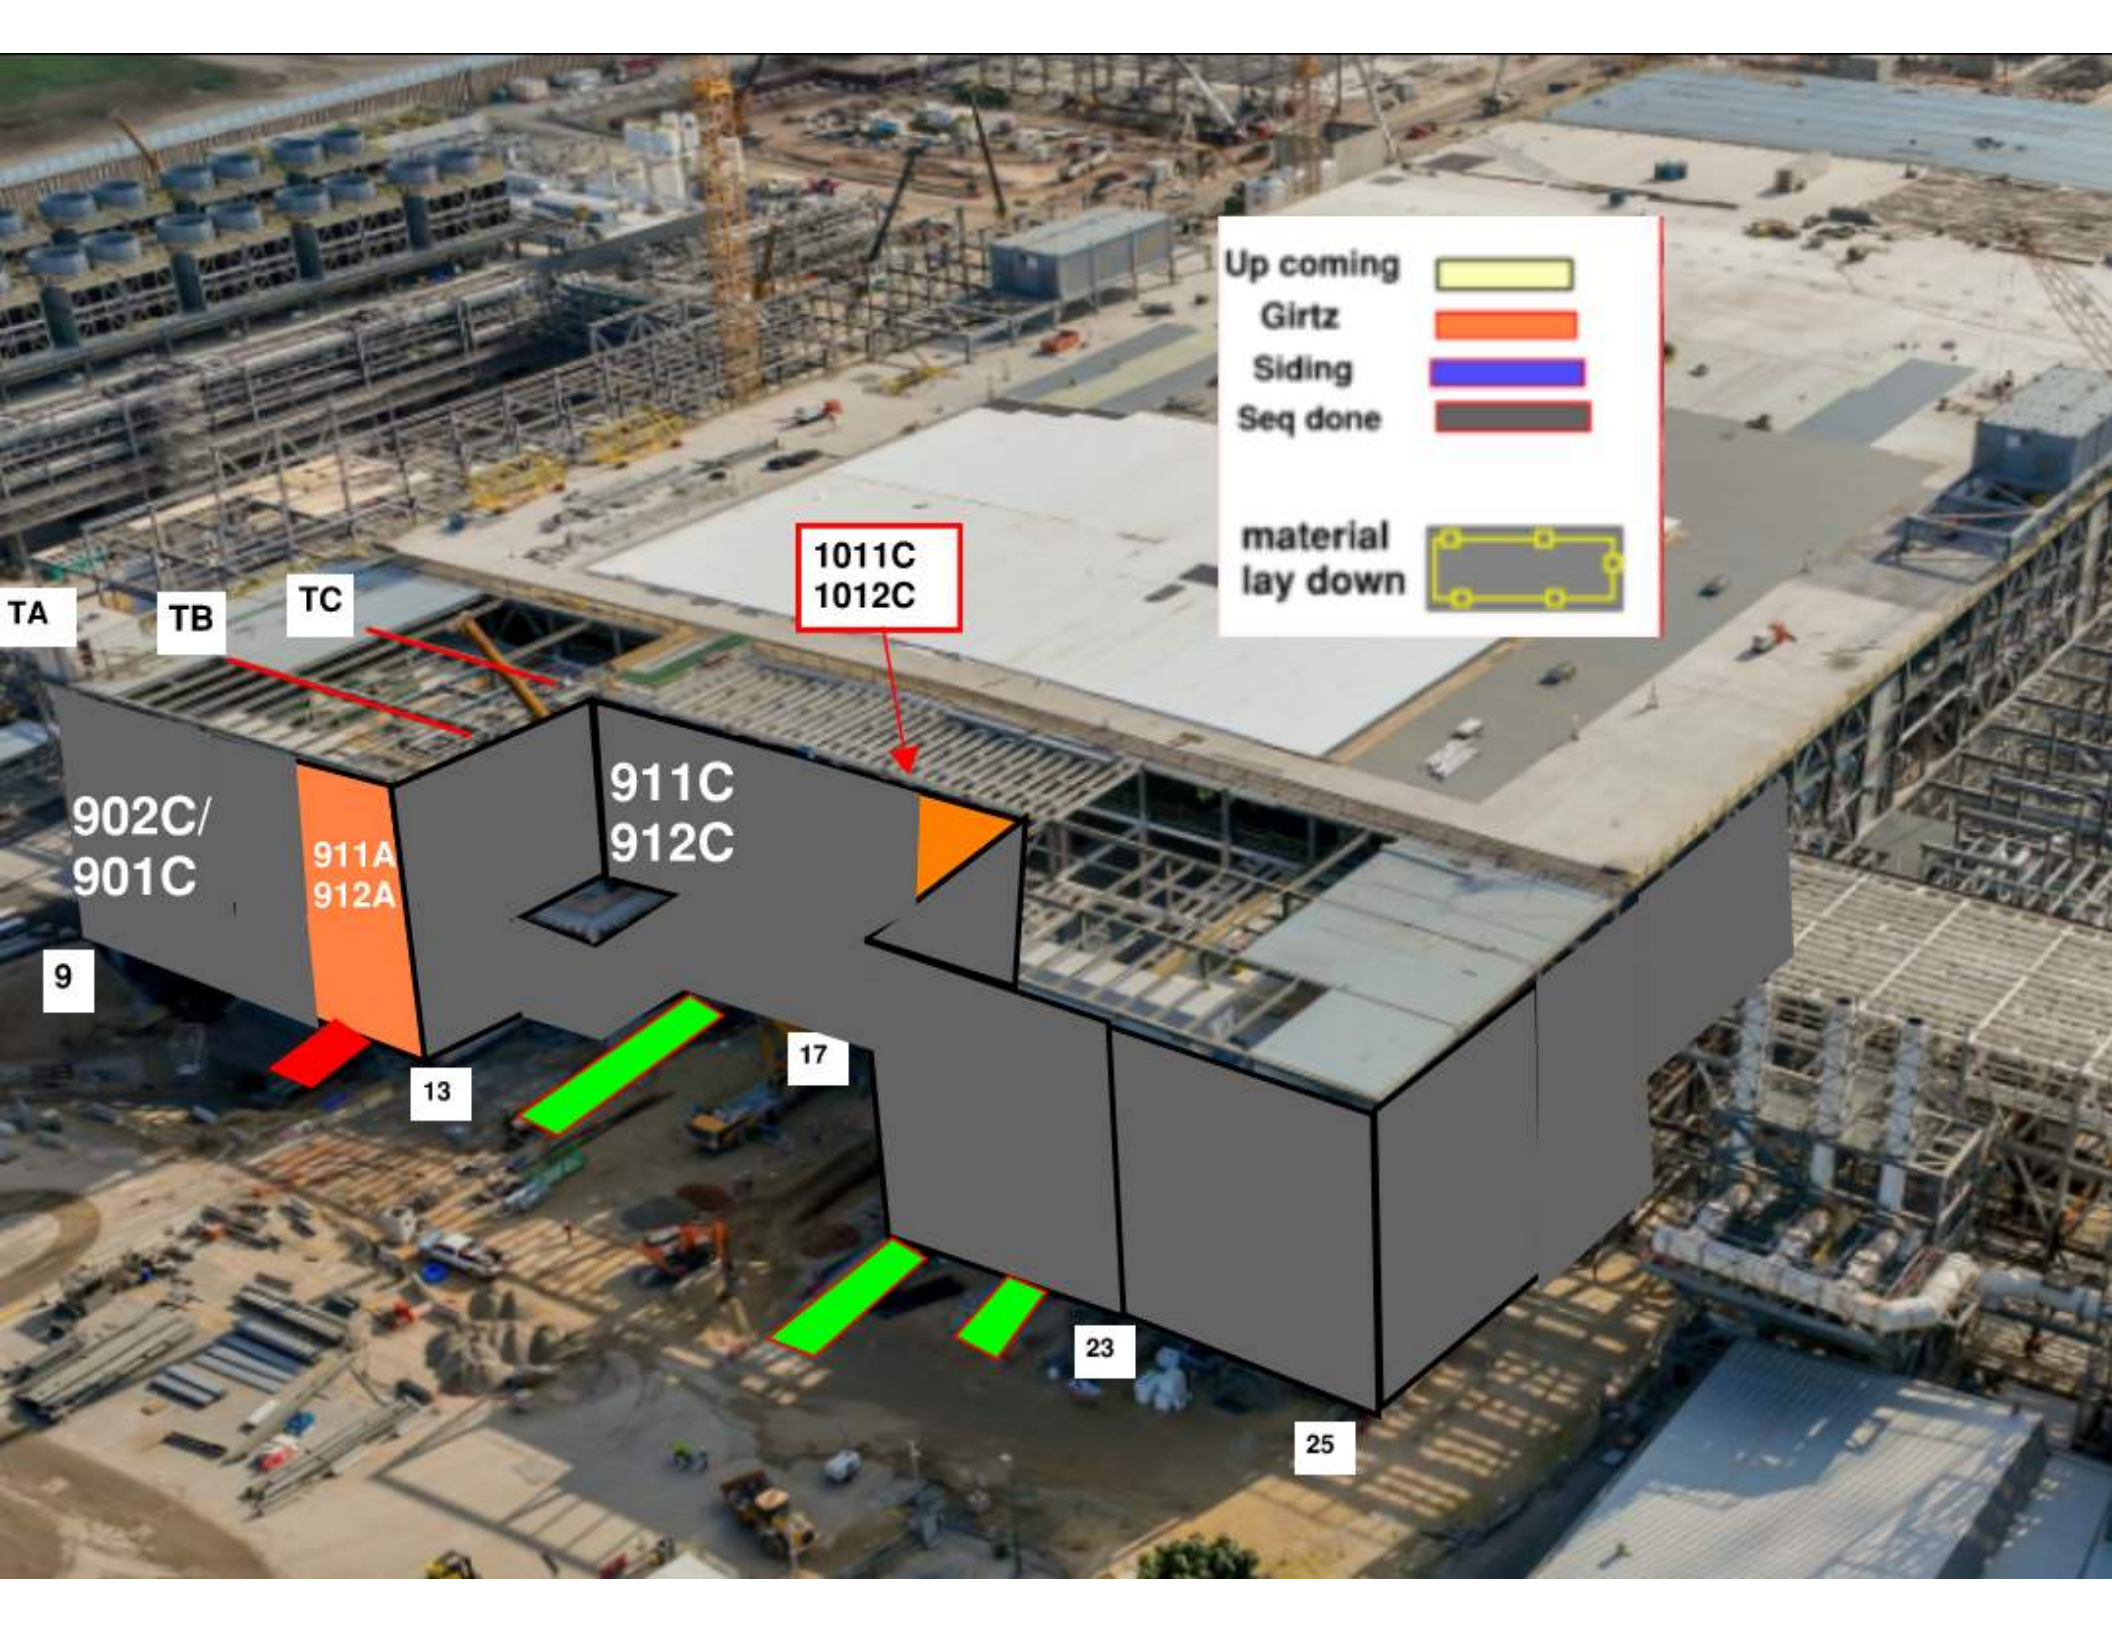

Up coming



Girtz



Siding



Seq done



material
lay down



TA

TB

TC

1011C
1012C

902C/
901C

911A
912A

911C
912C


9

13

17

23


25

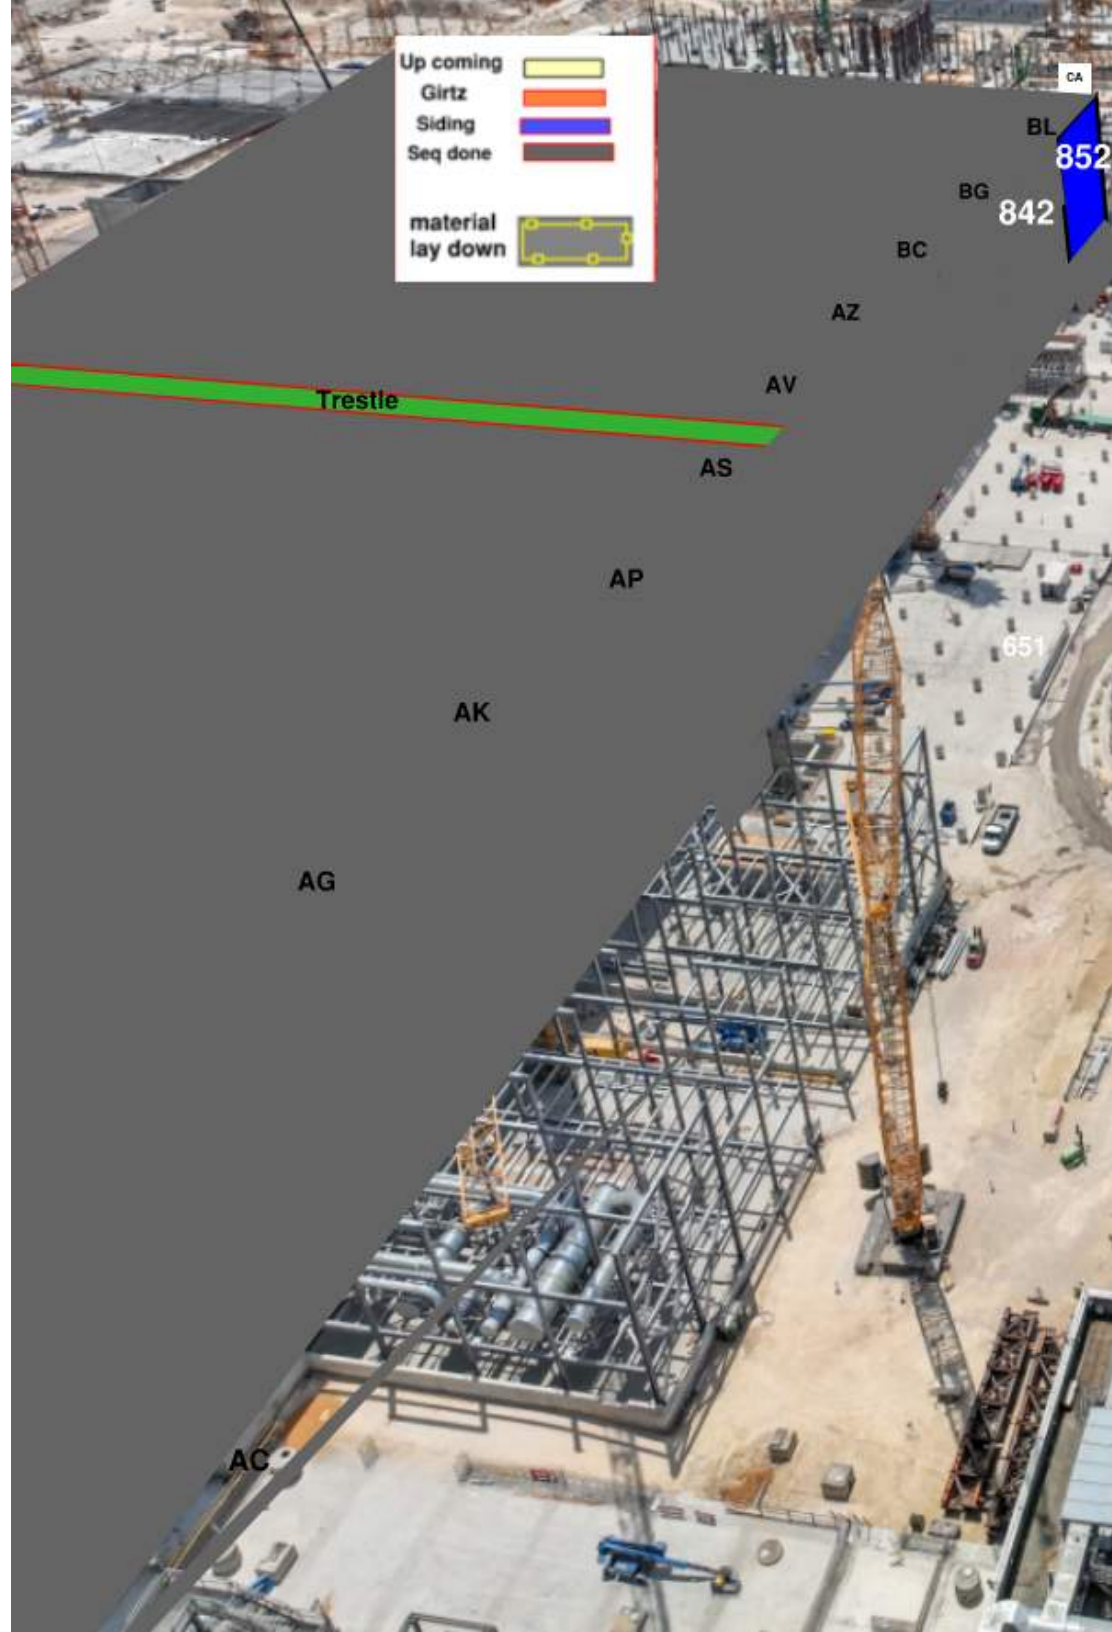

PSSS.1

Utility Level 1YA

PSSS Roof 2SA

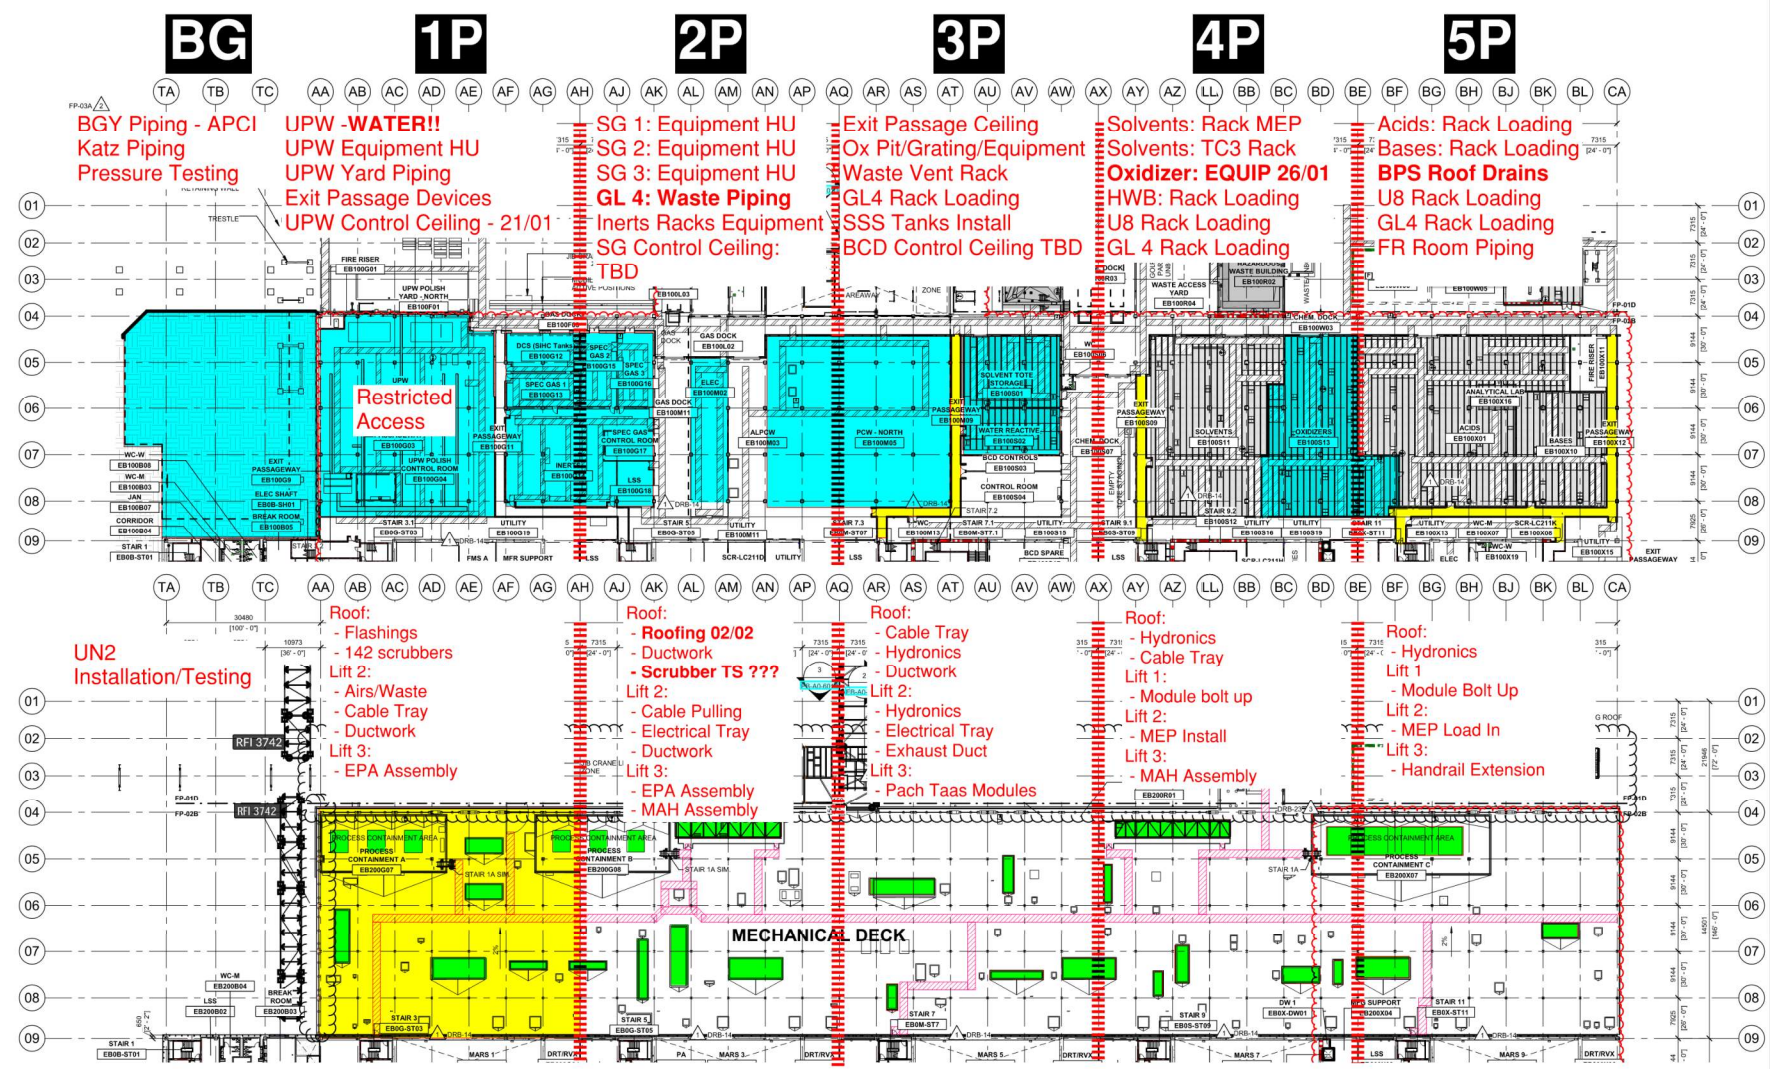

PSSS.2

6P


7P

8P


9P

10P

Utility Level
1YA


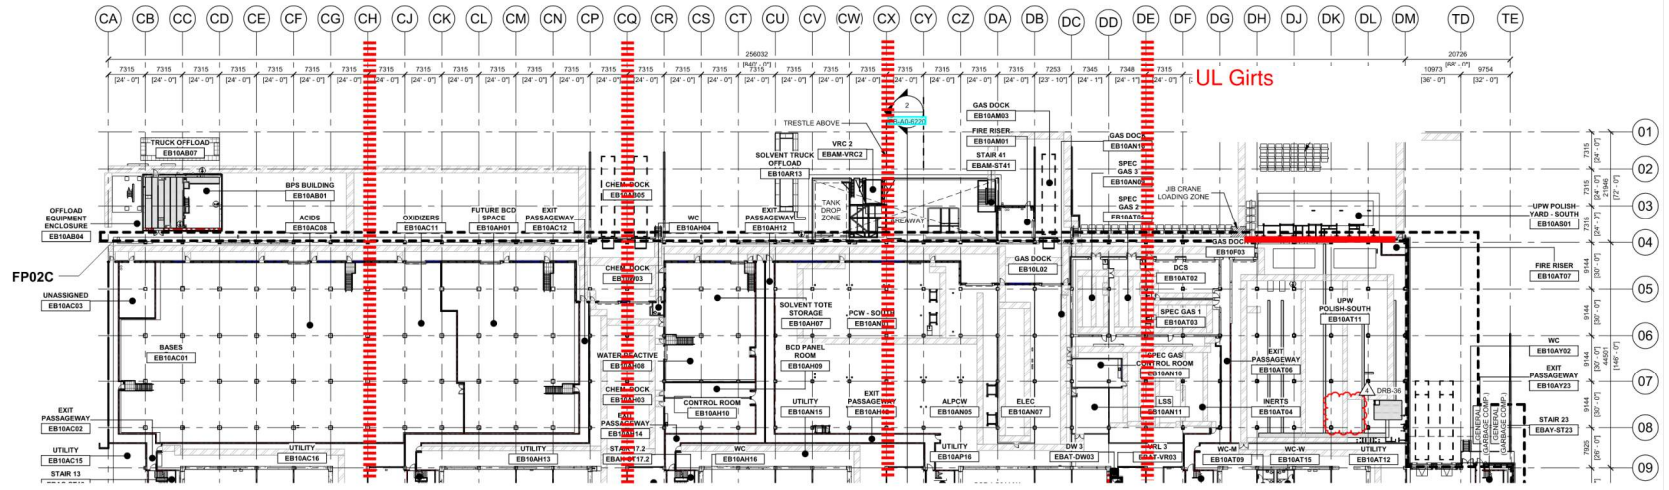


PSSS Roof
2SA

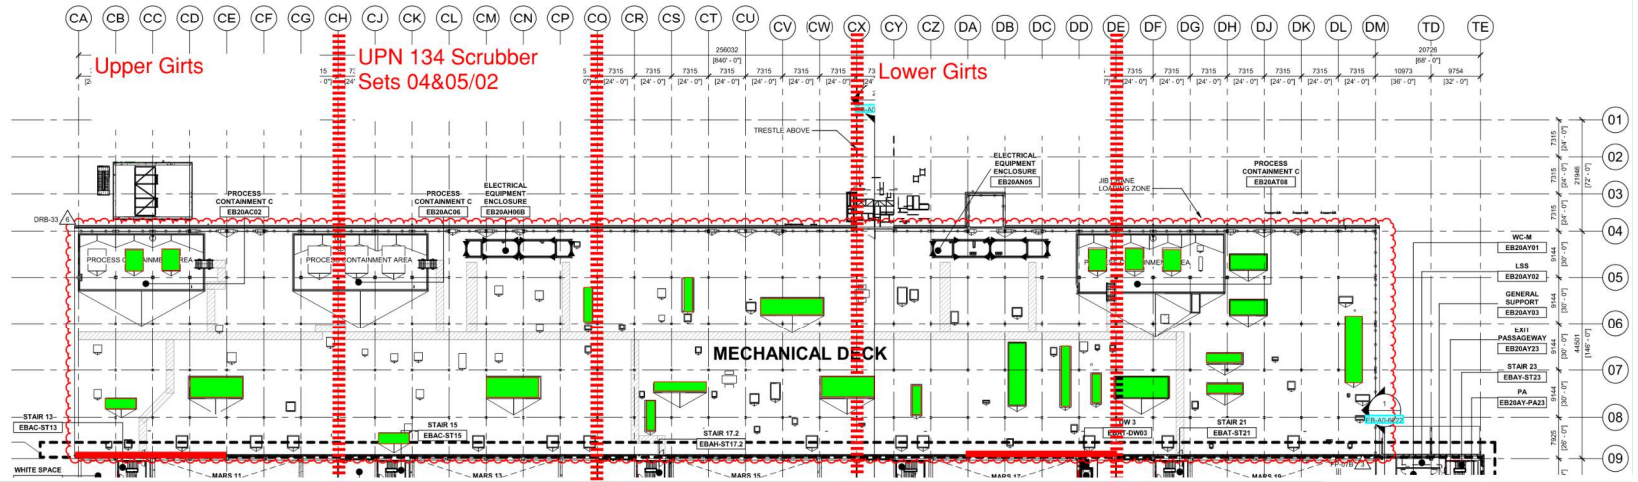

H2 Vent Radiographic Test

30/01 17:00-01:00

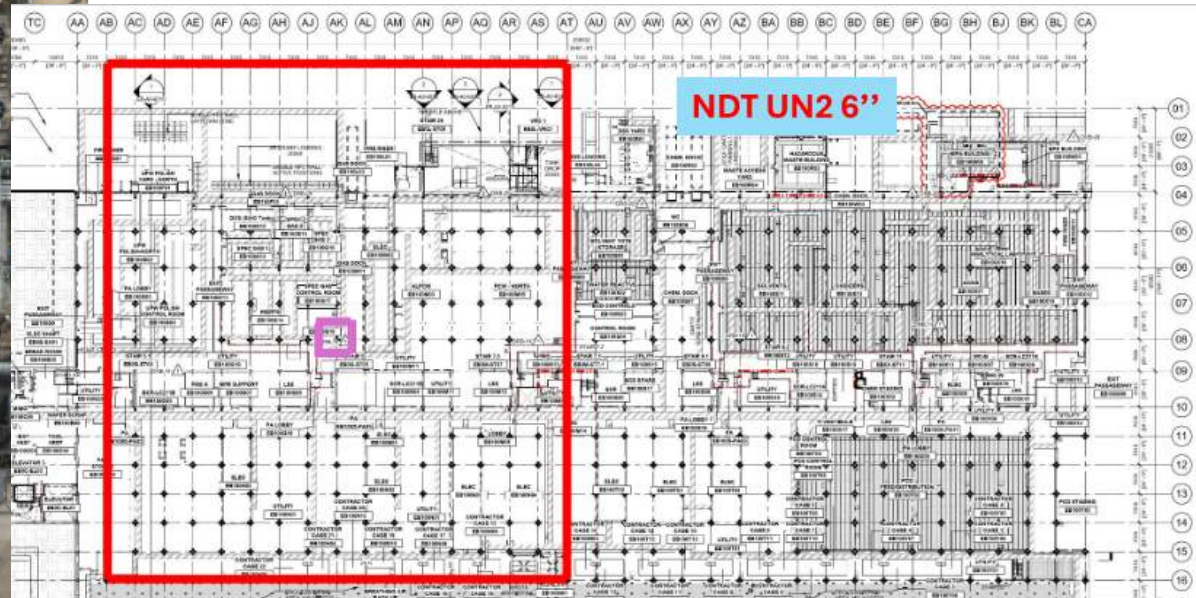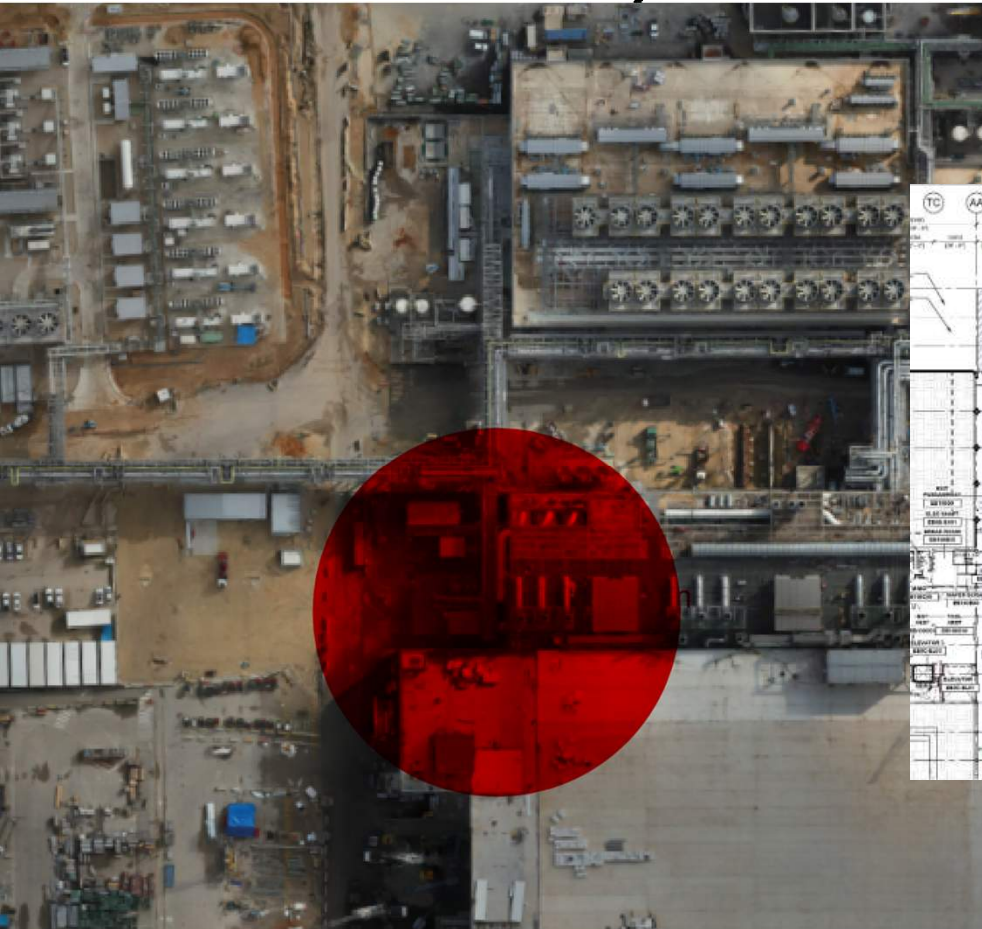

GN2


Analytical

BGY Closed


30/01 @12:00

to 02/02 @

23:59

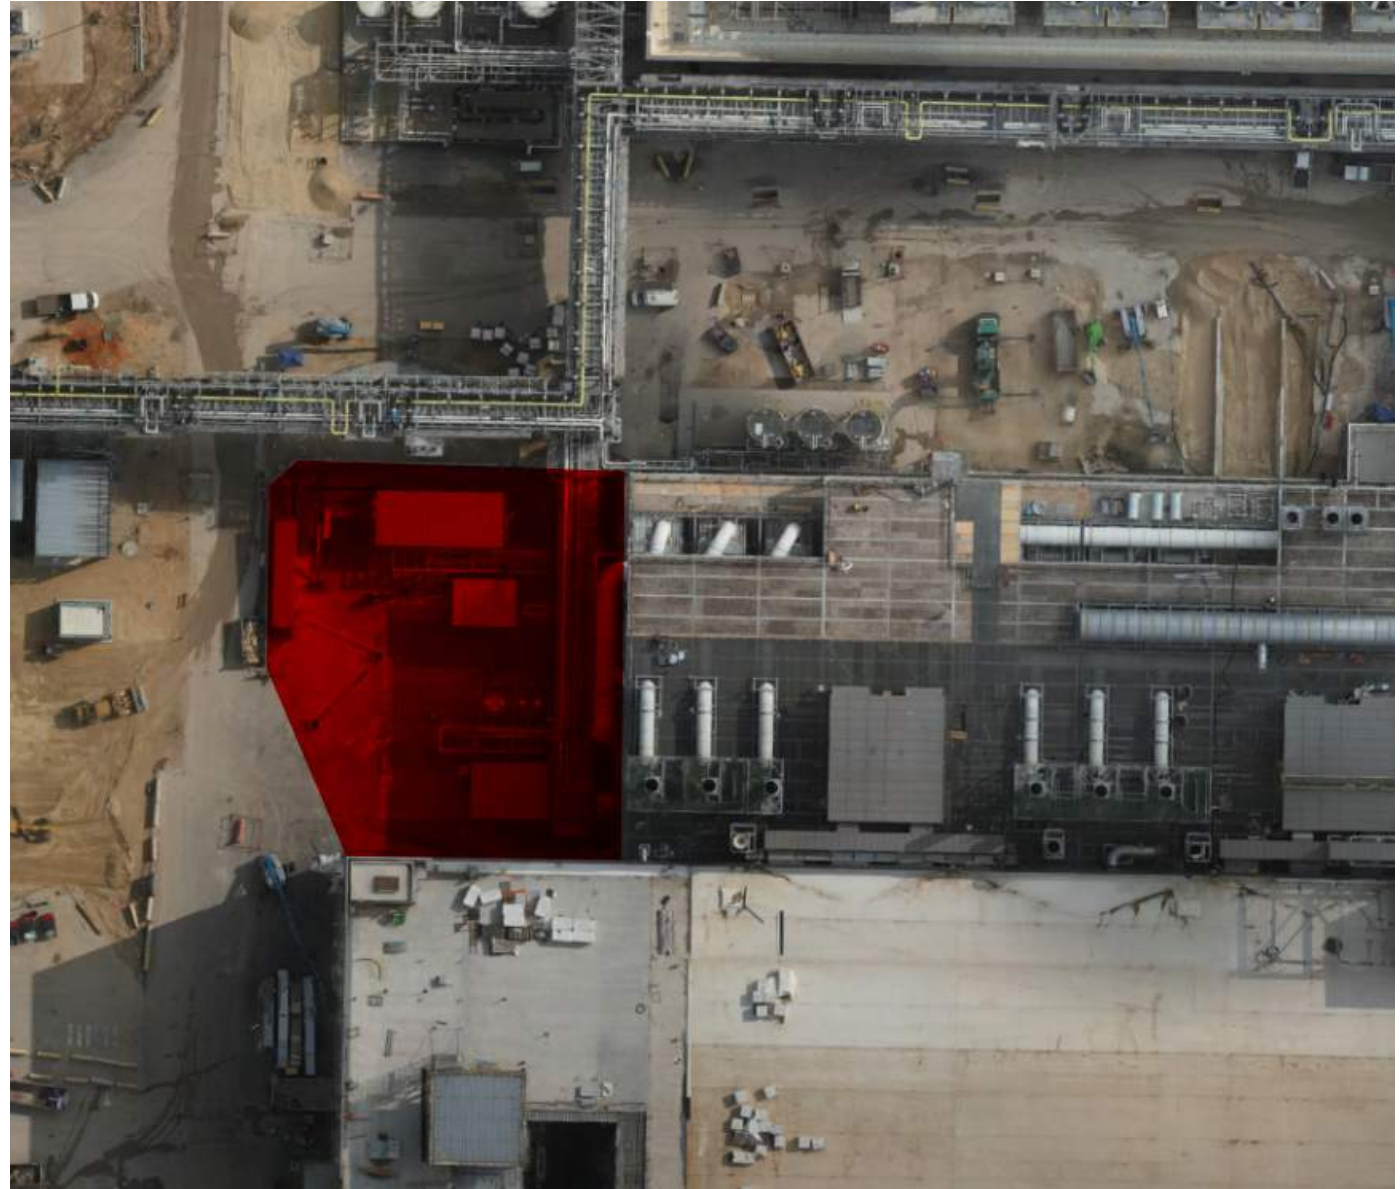


PSSS 02/02 Pressure Tests

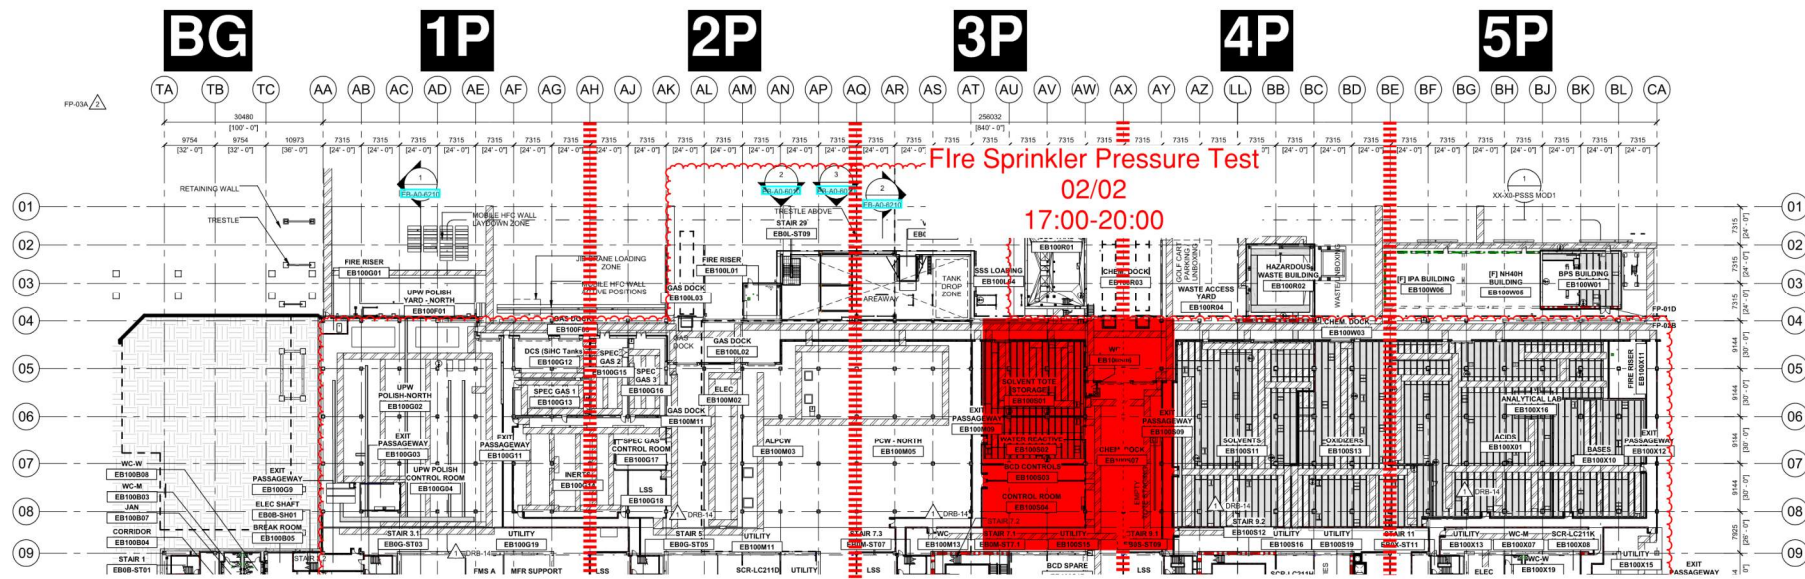


Utility Level 1YA

WJG 01J, 02J LIFT 2 & 3

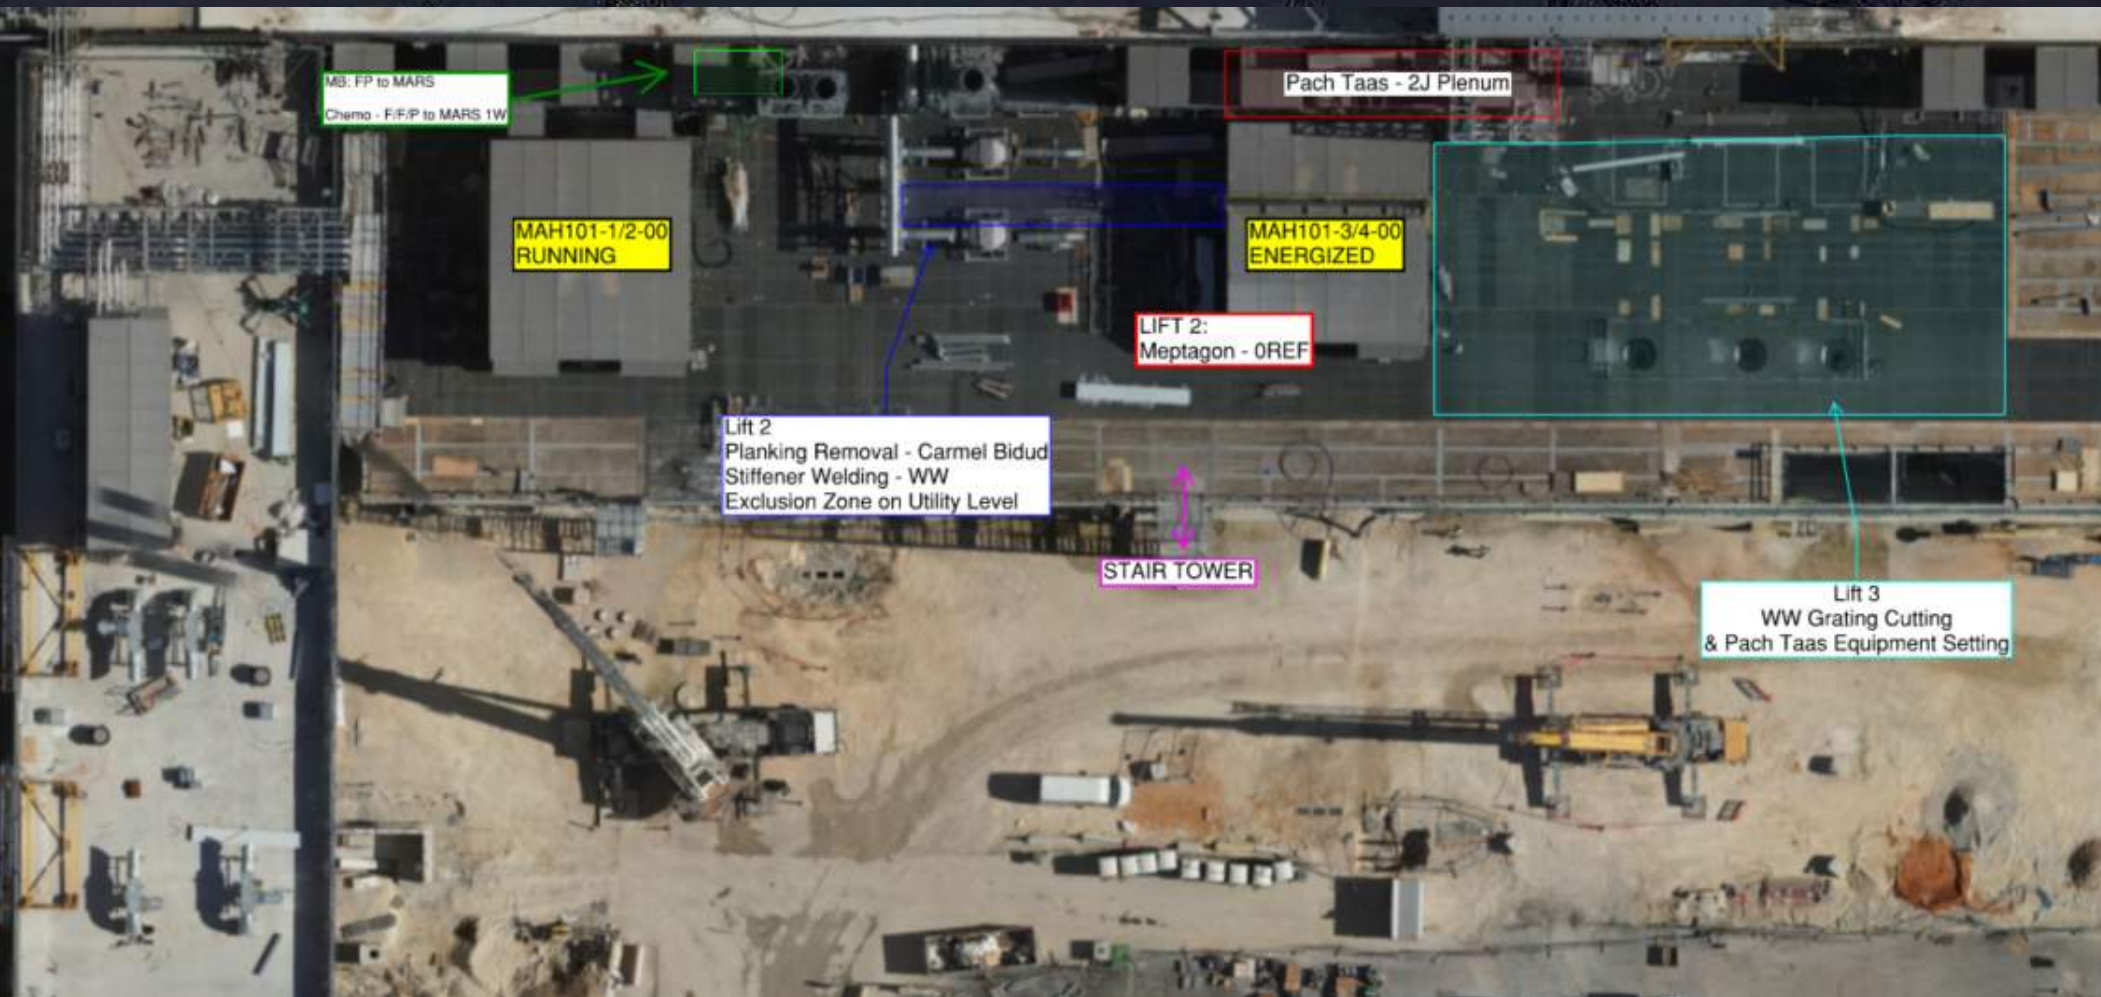


WJG 03J, 04J, 05J LIFT 2 & 3



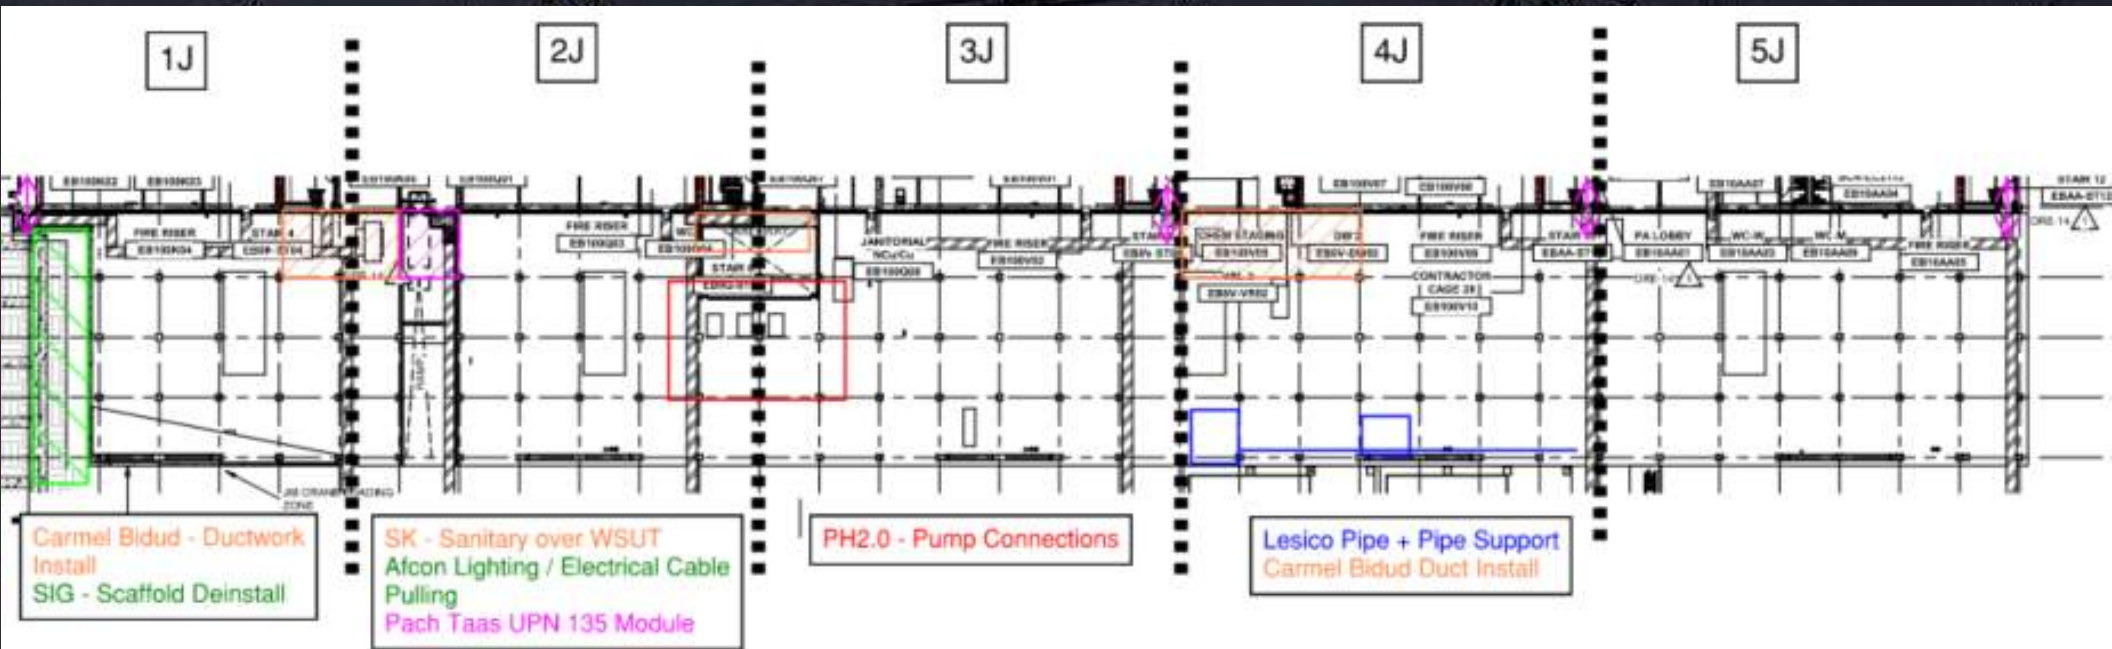




CUB 1

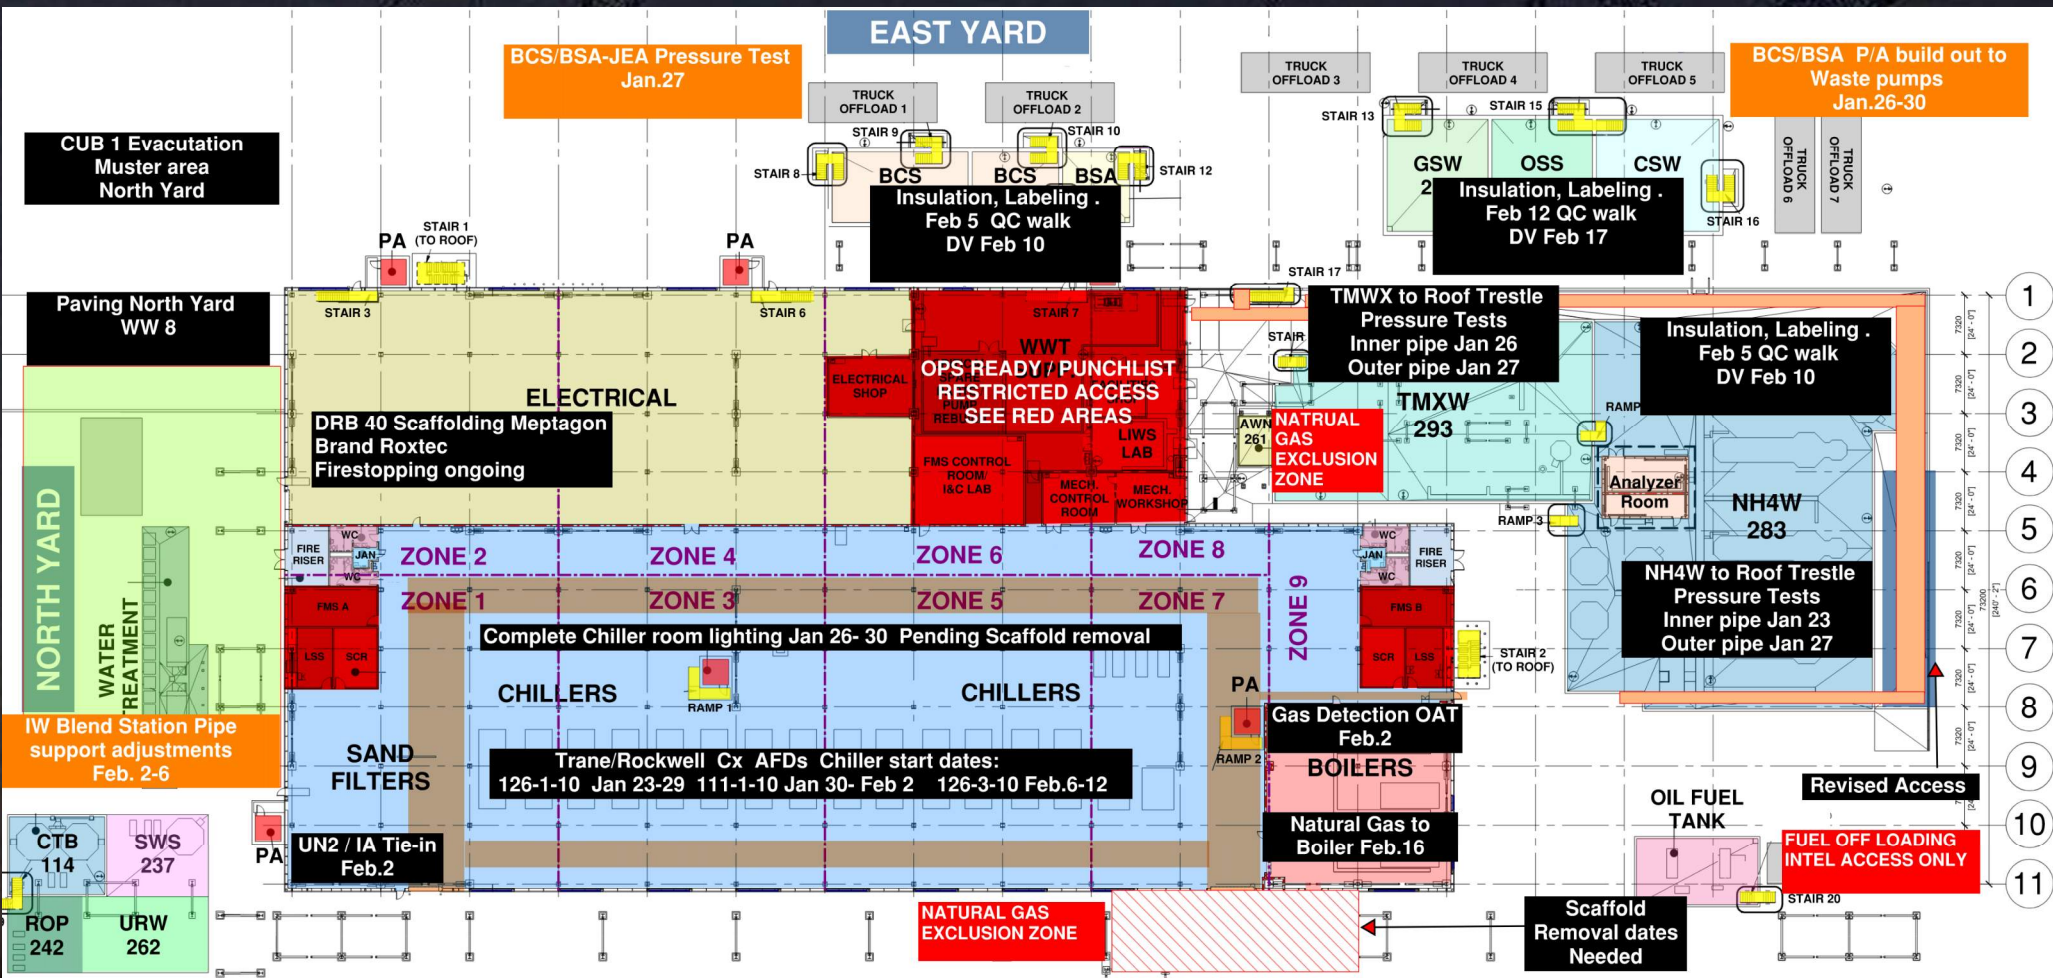


CUB 1 – EXTERIOR/ROOF

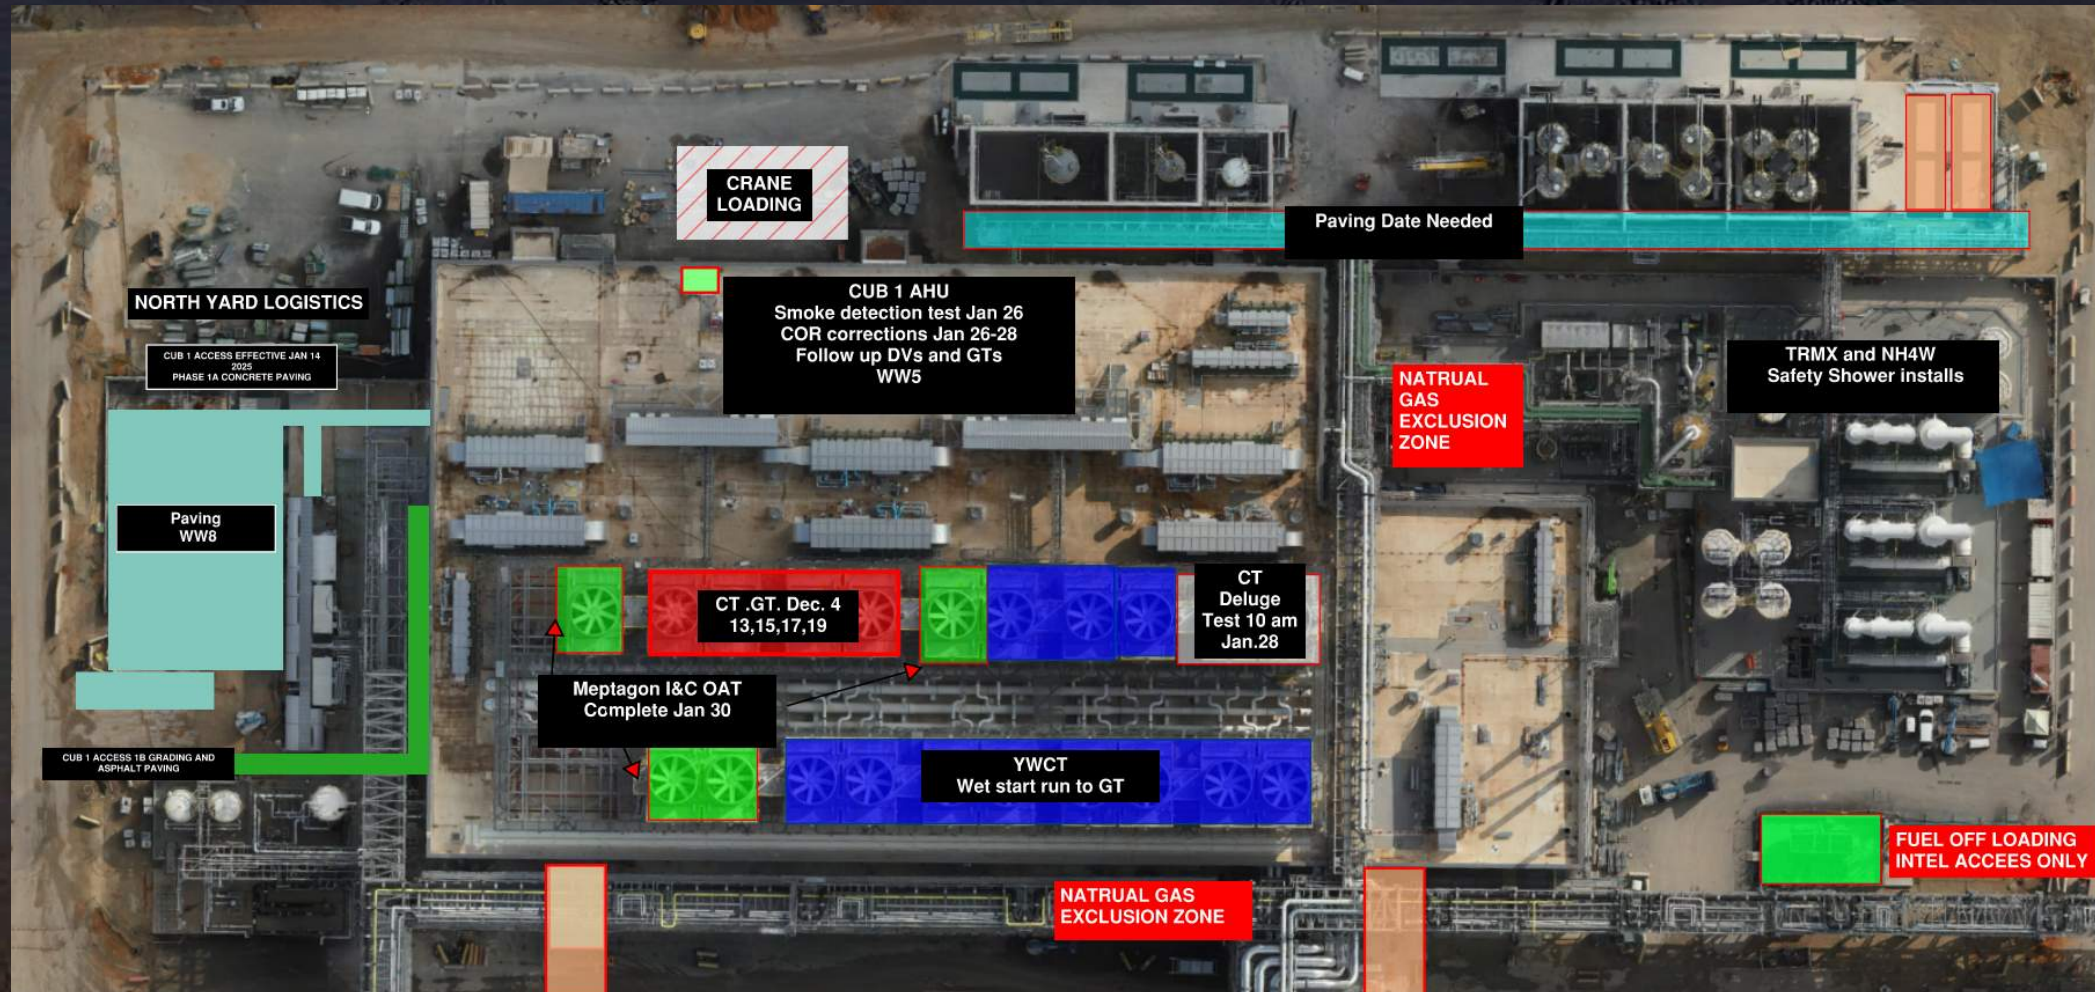



CUB 2- Load in ,H&T, Framing and Sheetrock

CUB 2 COORDINATION MAP

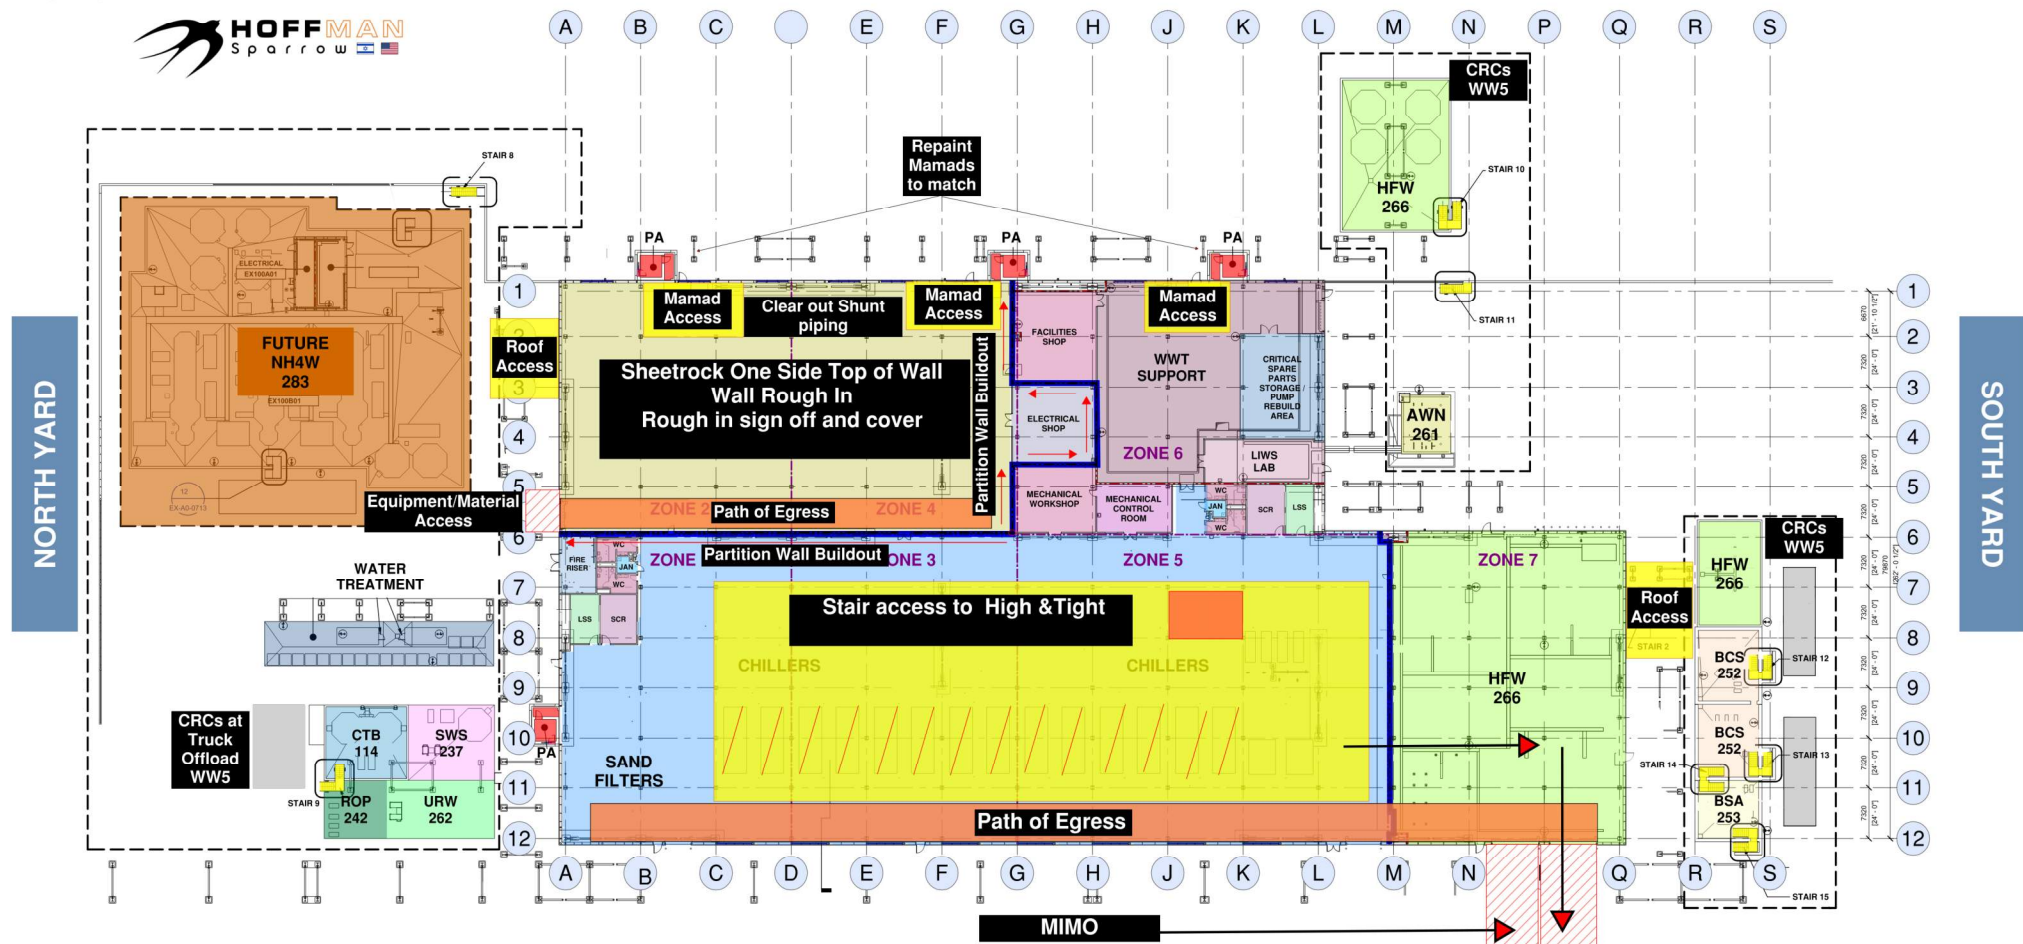


CUB 2 – EXTERIOR/ROOF

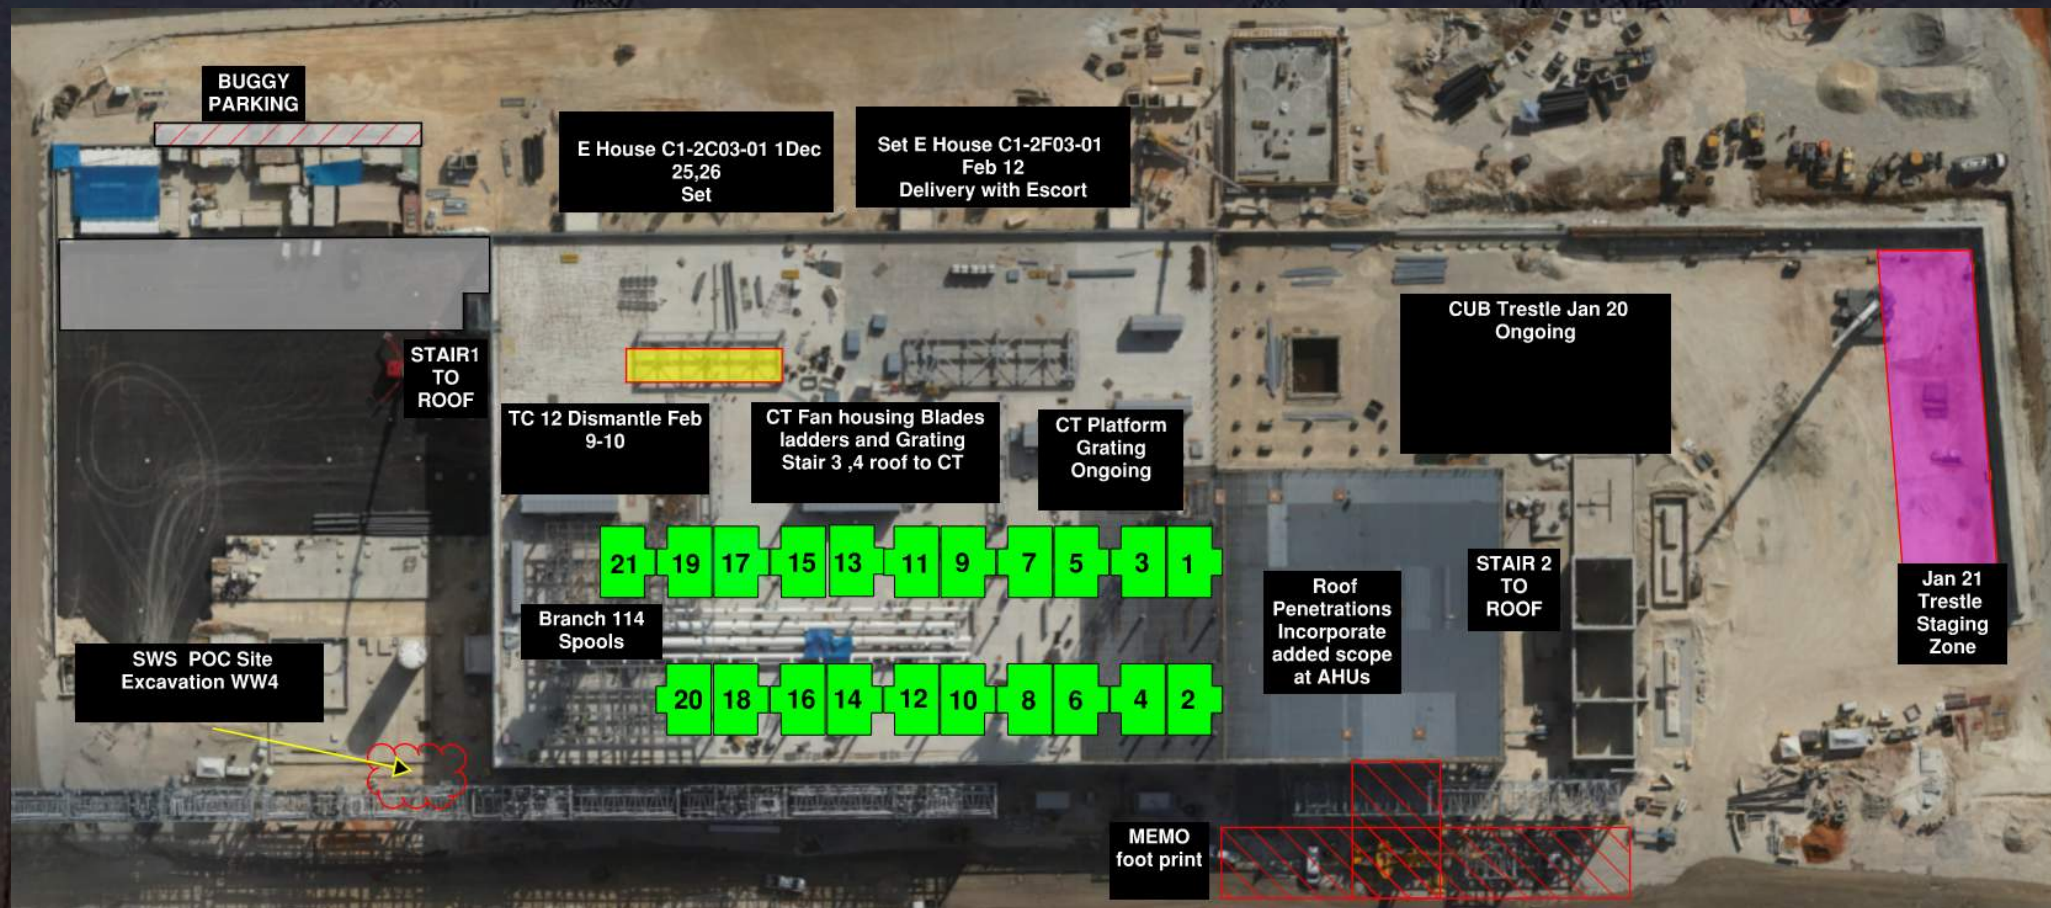



HOFFMAN CONSTRUCTION COMPANY

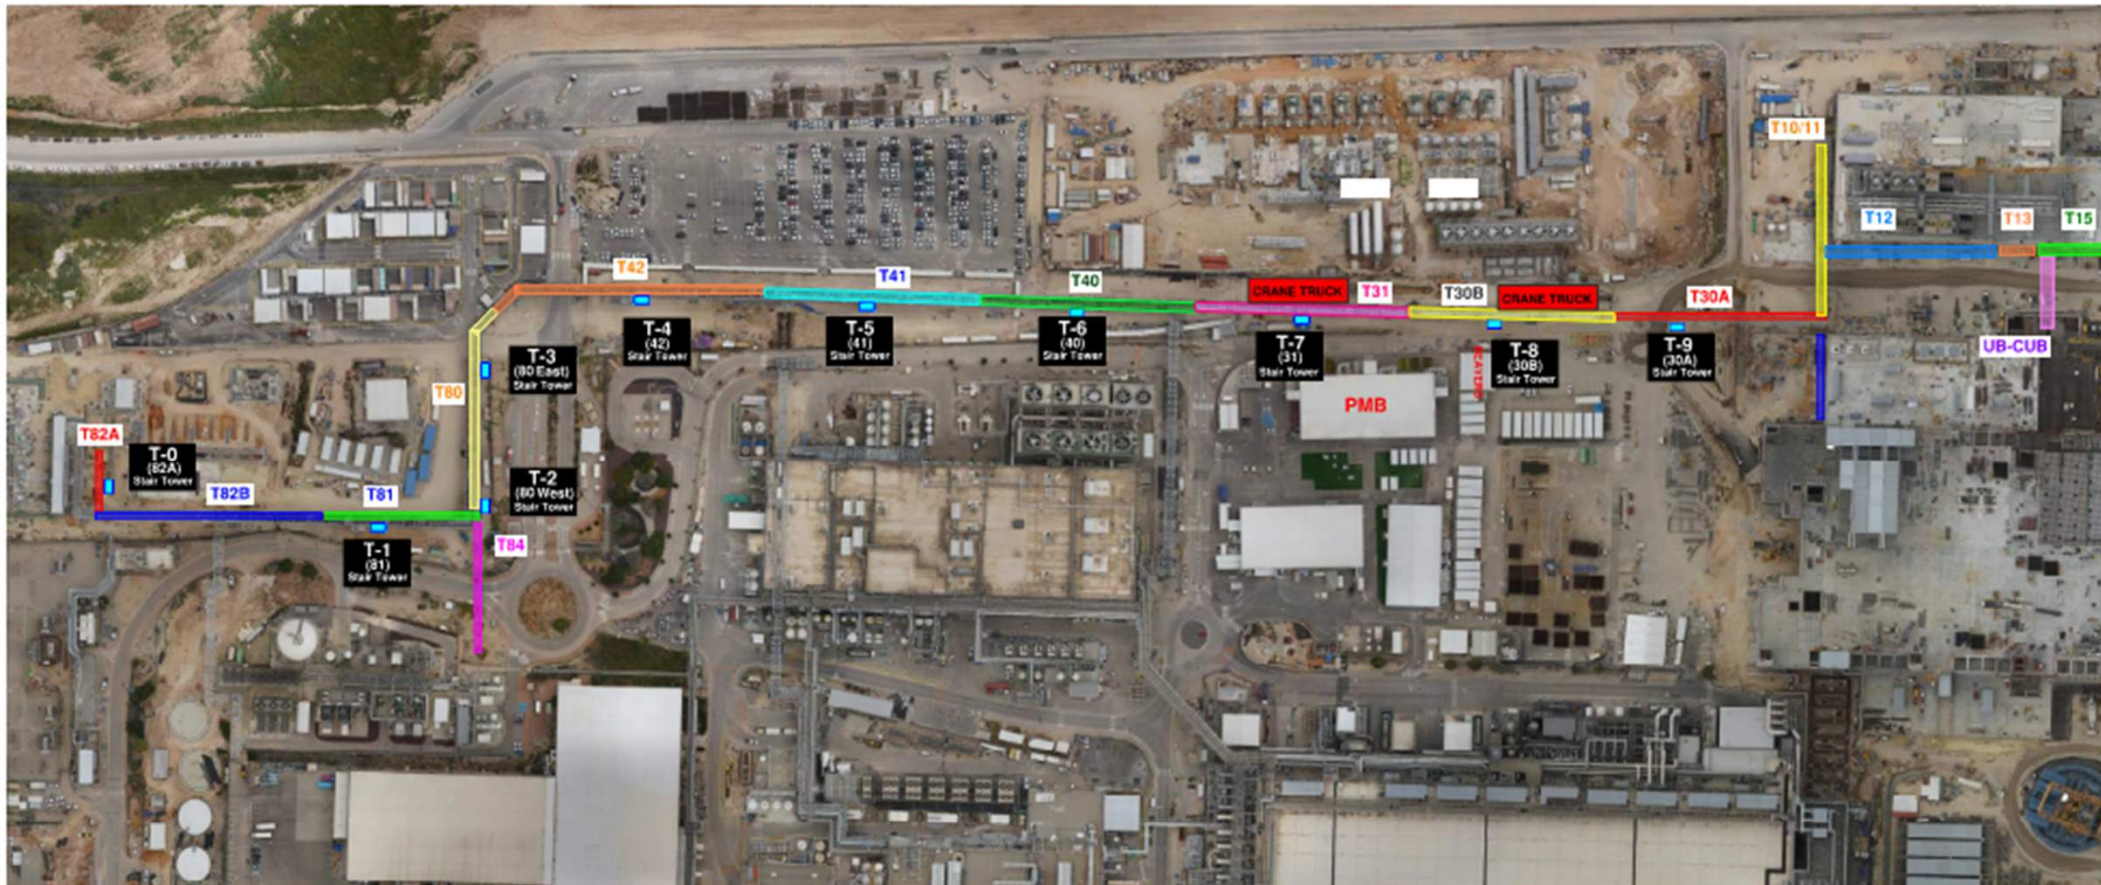



HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

North Entry





HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics
North






Daily Coordination Meeting

Site Logistics

South

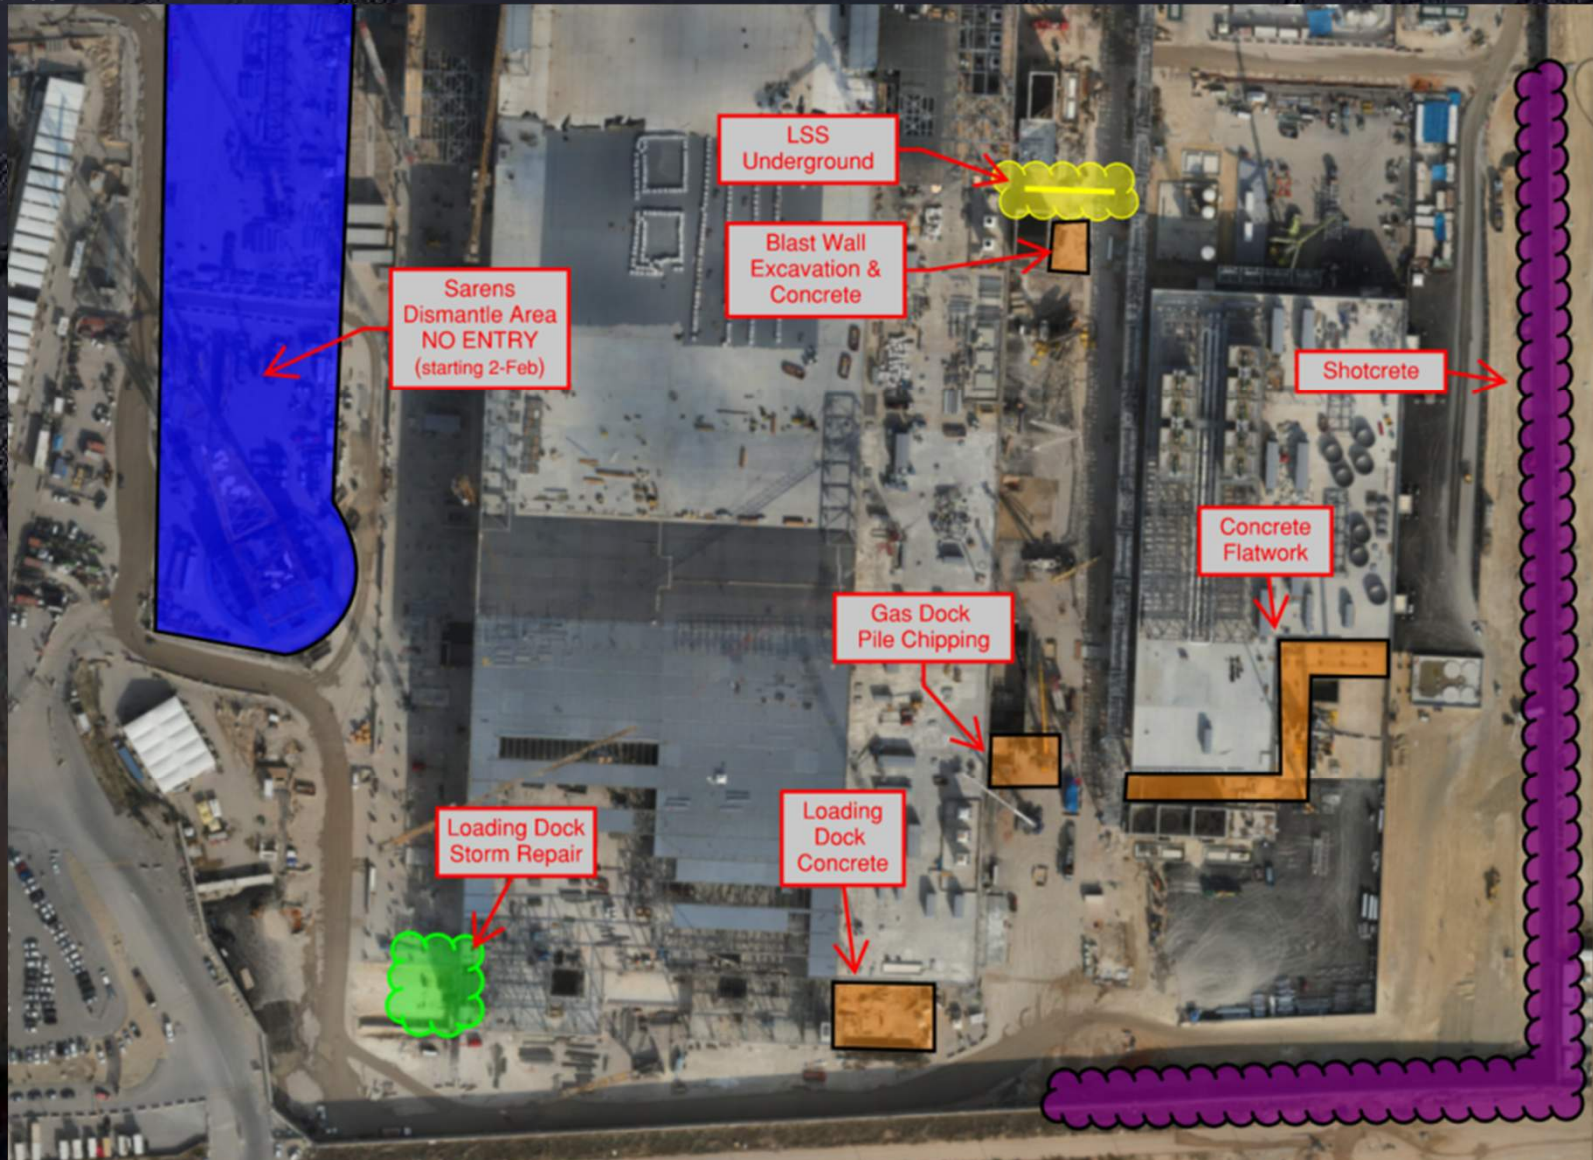


Set Up Should be the Focus

- How we prepare for our work is when we have the greatest potential to ensure a safe, efficient, and high quality operation.
- Too much focus is on trying to fix problems after the fact. If we gave more of our time and attention to ensuring that everything is set up correctly, we would have fewer issues.
- How people are trained, how crews are configured, how detailed/complete plans are, how instruction is given, how work areas are prepared, etc. is vital to our operations.
- In the end, less work/stress/problems are created if we take the time and care to set ourselves up for success. Take the steps to make failure something that someone would have to aim for in order for it to be the outcome.

Contractor Spotlight

- Meptagon I&C team on the clean room has taken this mentality and is seeing success with it. We were able to recognize their crew for their great work area set up. Which included:
- Organized storage
- Work stations with clamps for holding material
- Lighting
- Plan drawings
- Trash can
- Drinking water
- Broom

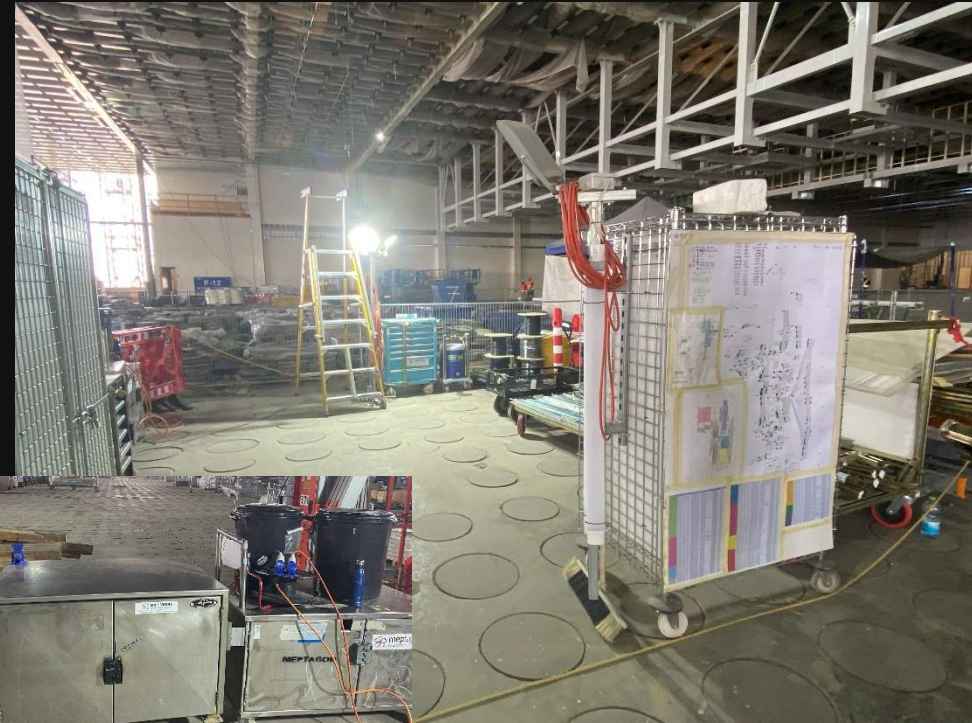

HCC/EHS Weekend Work- 31.01.2025

White Board Meeting in Beavers at 06:30

Superintendents

John Scott - 052-3291705

Ziv Srur - 053-2712258

Tsurriel Evgi - 052-3718851

Ken Power - 052-2531428

Kevin O'Hanlon - 052-3239625

CSA CM

Brandon Britton - 052-6042828

Nitzan Mulay - 052-3257365

Andy Jollands - 052-9659290

Dan Stanley - 052-6215642

Tareq Nairoukh - 052-6636782

Kevin O'Hanlon - 052-3239625

MEP

Cx

Cranes

Maksym Panov - 055-9181086

Safety

- Safety Foreman- Hay Halfon- 052-8049342 Hay-Halfon@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 31.01.2025

FAB

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Elram

Foreman: Shlomo 0545551702

Ehs: shy 0523632132

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Clean Room

- **Talad** – 20 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Mati 0504887477, Super Igor 0544509386)
- **Afcon** – 5 guys CR – cable trays, INT Level cable pulling (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)
- **Chemo** – 35 GUYS INT -TNTNE/W Supports, 1E Mars prep for PT , 1W Mars (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- **Sela** – 10 1E, 3W CRC (Supervisor Yoav 0548076339, EHS Sergey 0526650046)
- Protocol 2 guys (Roni 0542496363, Lidia 05072148)
- **Talent solution** 11 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Yosi 0526557130)
- **W&W** 10 guys MOD1 – catwalks, MOD2-TTSE docking (EHS – Wisam 0509828381, Supervisor Rakesh - 0552837963)
- **Megason** 6 guys 4DA 4W-4E FOREMAN ISRAEL BITON 0526869393 EHS GUY ISHBIT

Subfab

- **Pach Taas**
 - Perimeter Racks AQe, BJe
 - Safety: Offek Ben Harush - 0507838486
 - Team leader: Itamar - 0509301917
- **Afcon E**
 - All over the SF
 - Team leader: Raz - 0546838626
- **Combe UPW**
 - TTNE/W
 - Team leader: Dani - 0526527883

Subcontractor Weekend Work- 31.01.2025

PSSS

- **Pach Taas** – Module bolting PSSS Roof, Lift 2 3-5P
 - Foreman – Vadim – 053-5552472
 - Safety – Offek – 050-2161429
- **Afcon Electrical** – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
 - Foreman – Charles – 055-2740190
 - Safety – Stevan – 055-9129333
- **Chemo A.** – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
 - Foreman – Maor – 050-955-9071
 - Safety – Rotem – 054-447-7112
- **SK Engineering** – GL4 UL Piping, 3P roof/Lift 2 Piping
 - Foreman – Marcela – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe Waste** – 2P Waste Piping at GL4/SSS Building
 - Foreman – Chaim – 054-5210133
 - Safety – Marzuke – 054-447-7112
- **Combe UPW** – BCD/UPW Rooms
 - Foreman – Boris – 054-8346412
 - Safety – Shimon – 054-5348843
- **Lesico** – UN2 Pressure Test
 - Foreman – Suju Pally – 052-7755967
 - Safety – Tal Madar – 052-8229109

WJG

WW – 2J/3J Lift 3 Grating Install (with 500T & 220T)
Foreman: Chris 052 588 3215

Afcon – Lift 2 Cable Tray and Utility Level Lighting
Foreman: Montu 055 911 6973
Safety: Pradeep 055 274 2935

Chemo 1J/4J/5J Lift 2 Piping / Insulation
Foreman: Maor 050 988 9071
Safety: Erez 054 971 6840

Pach Taas: All over (HRA)
Foreman: Ilya 050 577 1907
Safety: Eran 054 770 6233

Lesico: Natural Gas Piping Utility Level
Foreman: Anoop 058 691 1748

Subcontractor Weekend Work- 31.01.2025

CUB

D&P:

Constantin - 0545501602

David - 0548894447

Chemo:

Dudu - 0509808846

Alberto - 0508573970

SK:

Reynato - 0548991623

Marzuk - 0548830263

Sami Najami:

Hussein - 0526917461

Average - 0509059920

Pach Taas:

Itamar - 0509301917

Ofek - 0507838486

Megason:

Israel - 0526869393

Guy - 0544915407

HSI:

Sergey - 0552728807

Haim - 0548038554

Trestle

SNJ:

PIPES –T40 - UB CUB - 20 workers (4 teams)

STEEL –Galvanized paint + T30 A+B -T41 8 workers (2 teams)

Steel adjustment - 12 workers (3 teams).

FORMAN-

Mucles- 0526017477

SAFETY TRESTLE-

Aviram shrike - 0509059920

Siding

Site

- Derech Afar – Shotcrete wall
 - Supervision = Raed: 054-244203
 - EHS = Alex: 054-5403849

Daily Coordination Meeting



14:00 Sign In
