

Daily Coordination Meeting



Daily Coordination Meeting

General Topics:

- Weather - ensure material is secure before leaving
- Weekend work




TC12 pour back
UL lvl
4:00 am


BPS.2 Blast wall
5:00 am

Pan stairs @
elevators 1&2
5:00 am

UTILITY LEVEL MOD1

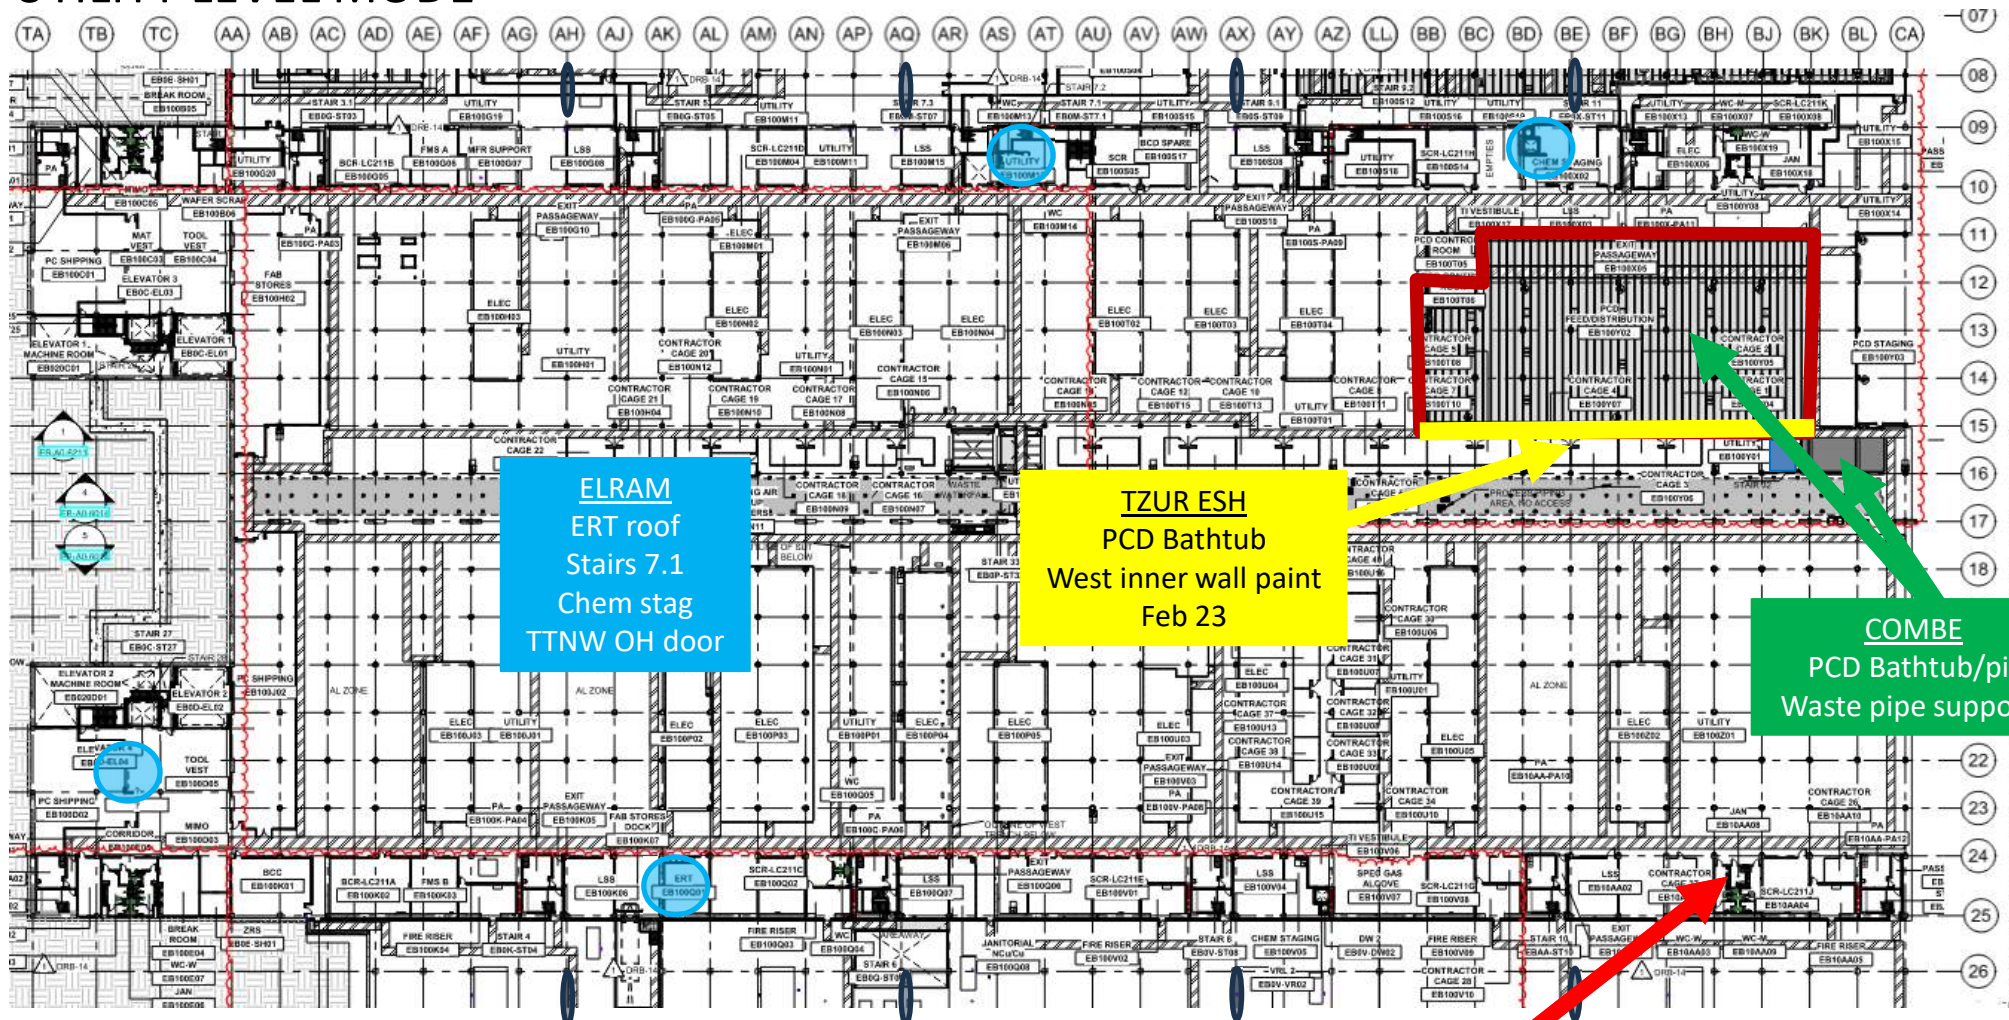

SUT 38.1 LEVEL

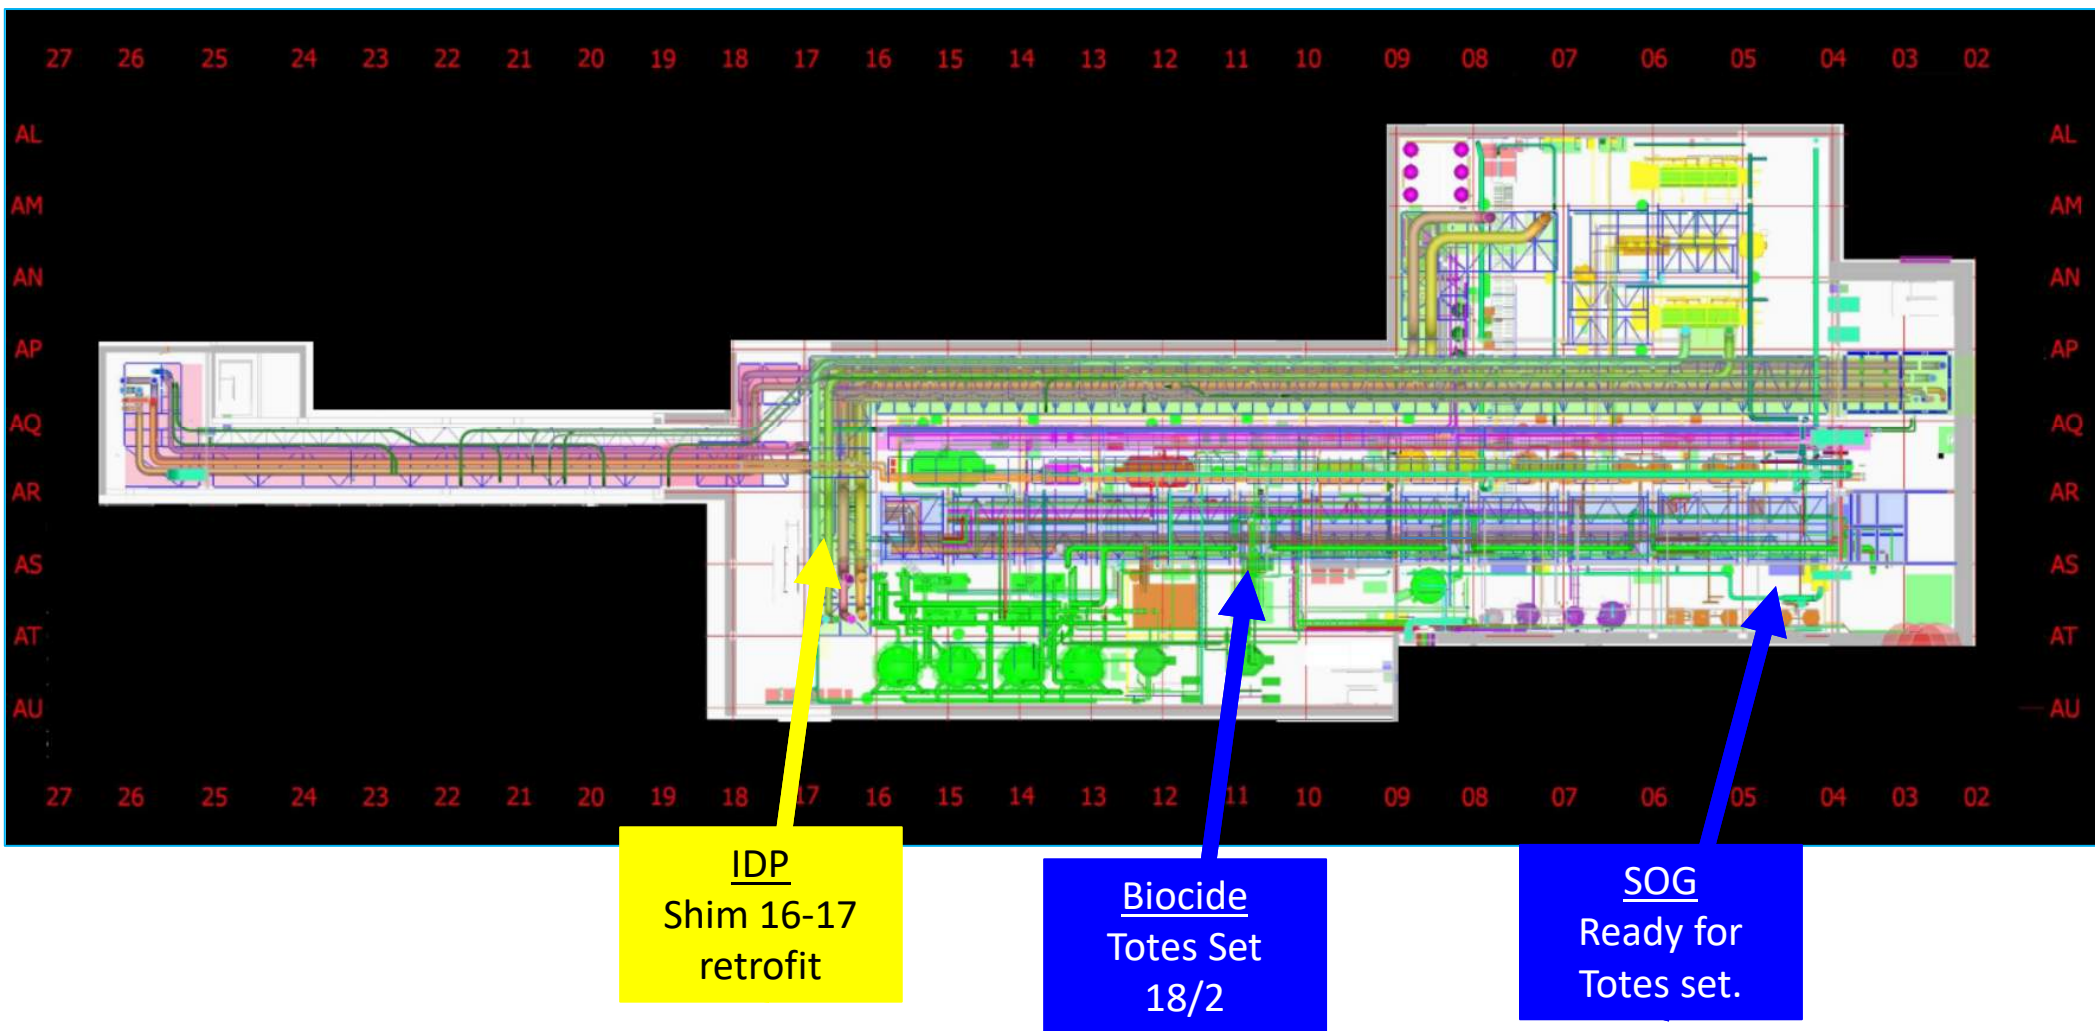



HOFFMAN CONSTRUCTION COMPANY



SUT 38.2 LEVEL


Rack 4b
Inter
Connection's



Temp stairs
relocation

16.2.2025	Module 1
17.02.2025	Module 2
24.02.2025	Module 3
25.02.2025	Module 4
03.03.2025	Module 5
04.03.2025	Module 6

SUBFAB BUILDOUT MOD 1

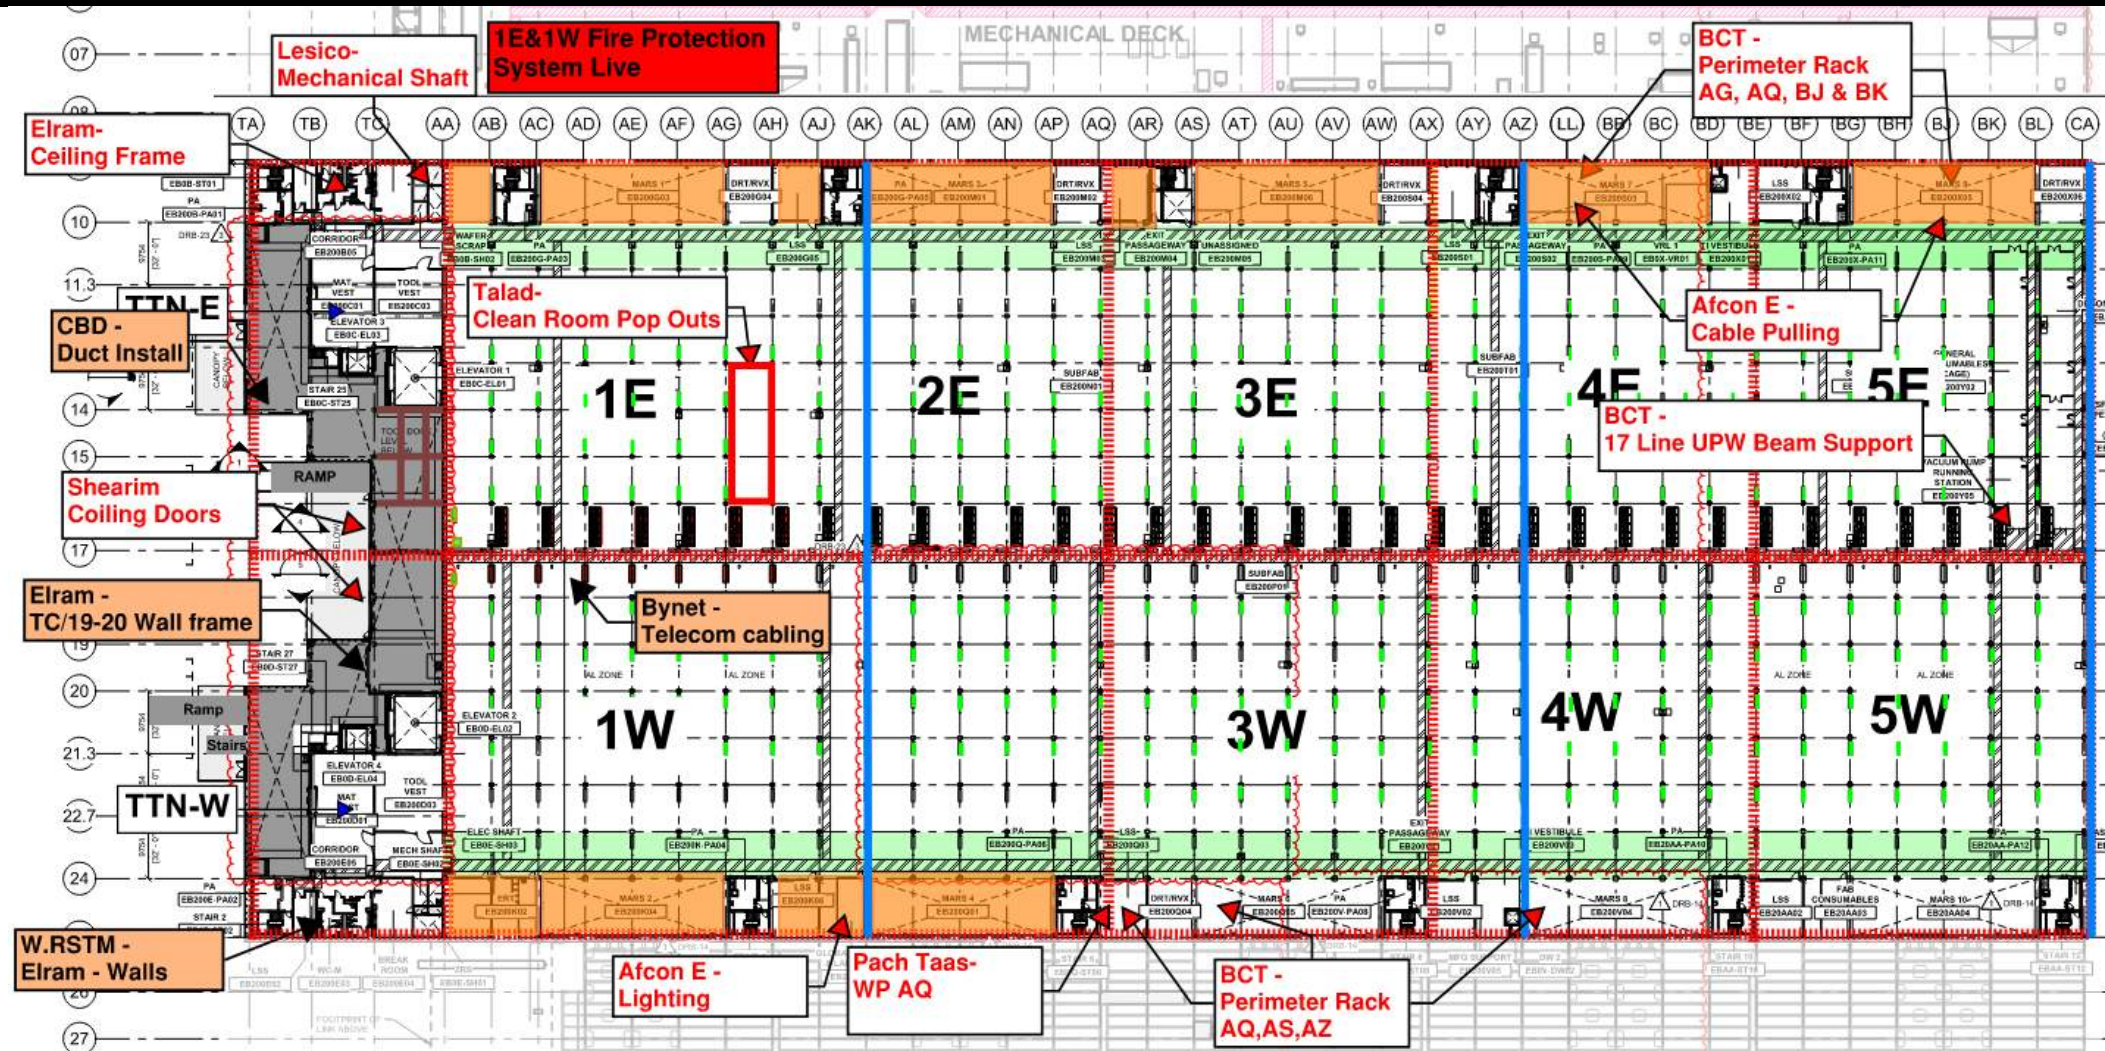


Lines being tested

FEB 20th 15:30-18:00
Bay ANw
ALCPCWR/S 6"


SF Level Exclusion Zone.


Stairs #6 Blocked SF Only
3W LSS Room Stays Open


BCT Pressure Tests Sunday


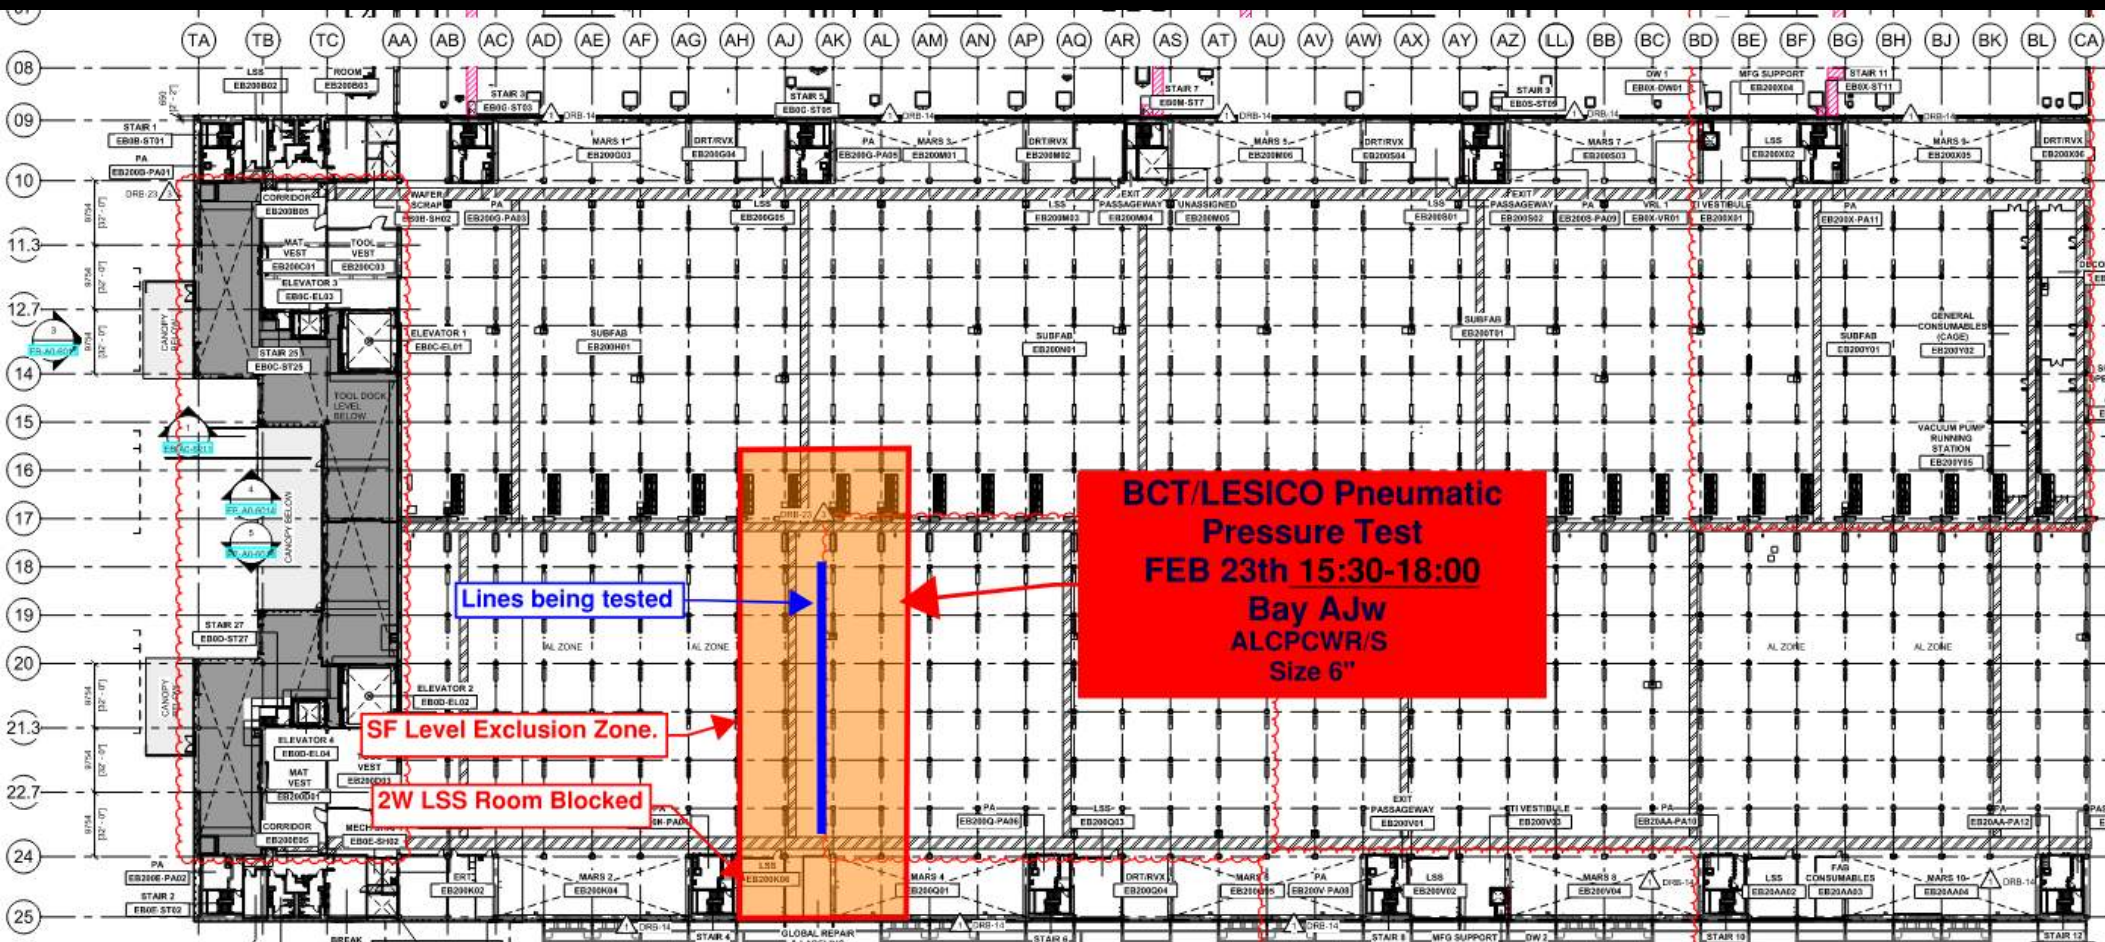



SUBFAB BUILDOUT MOD 2

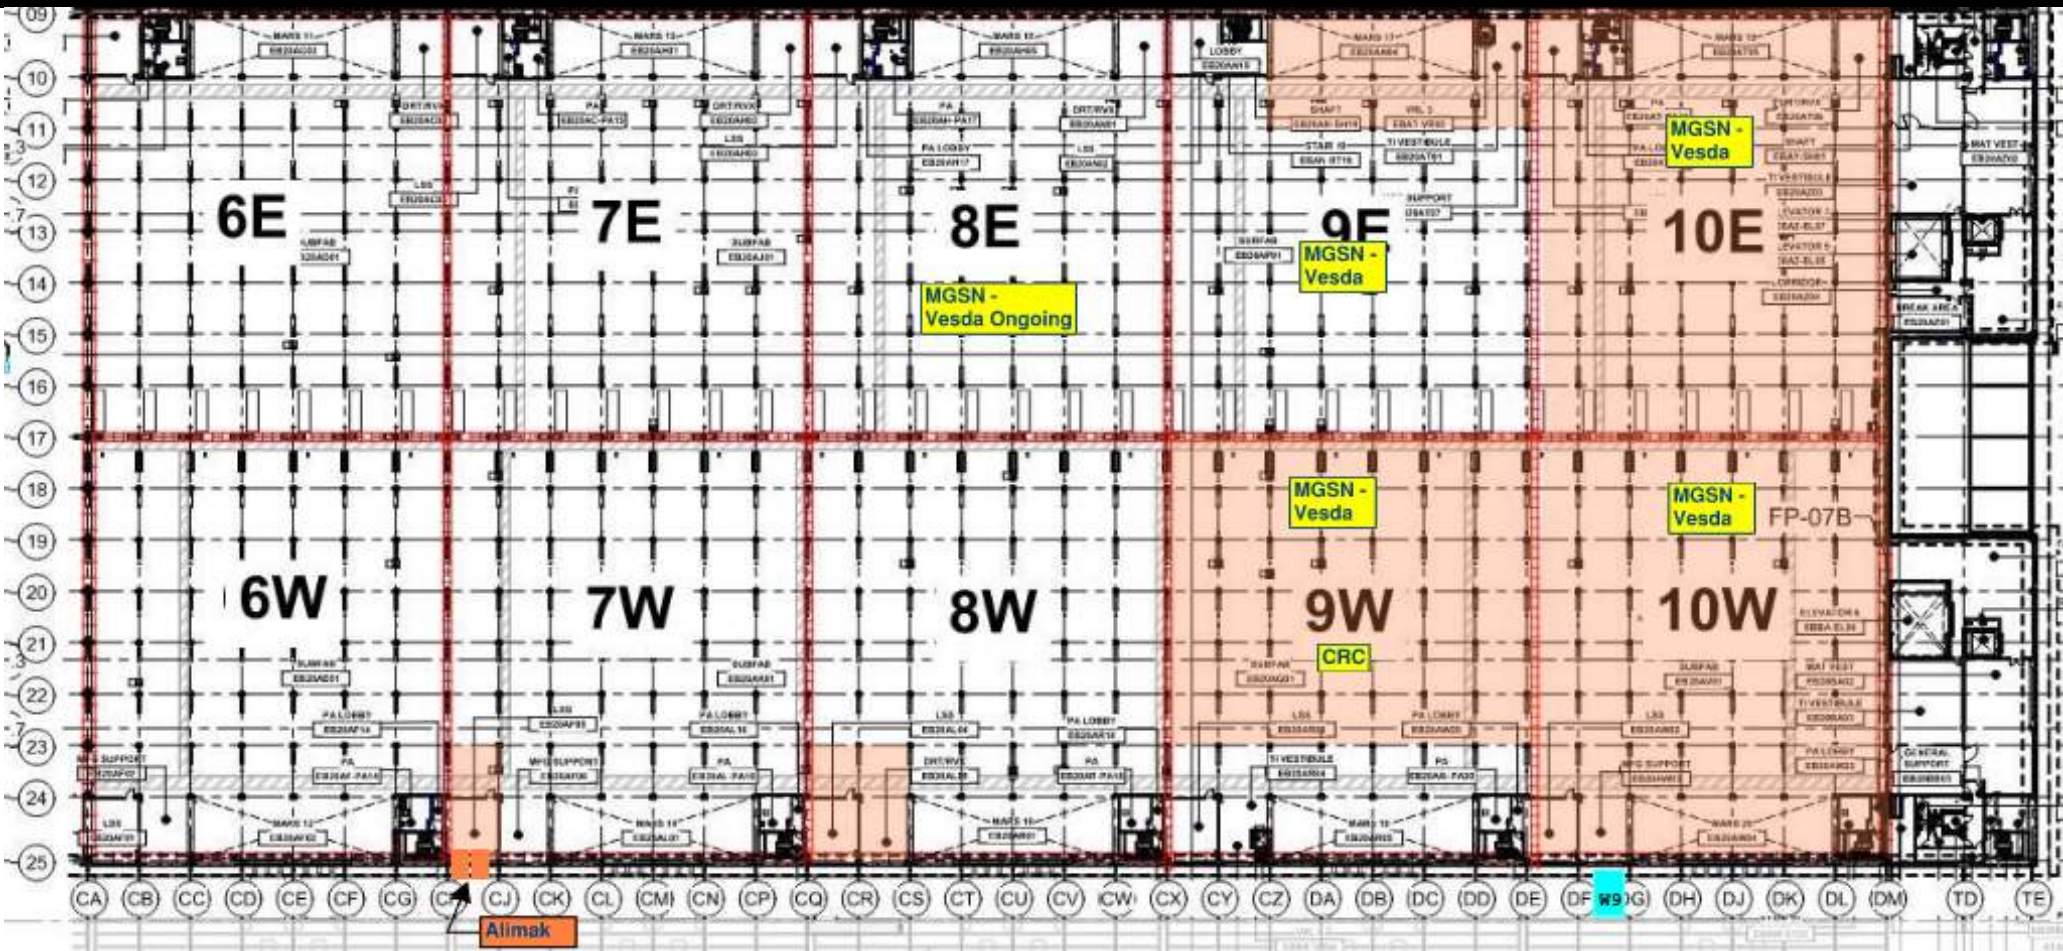

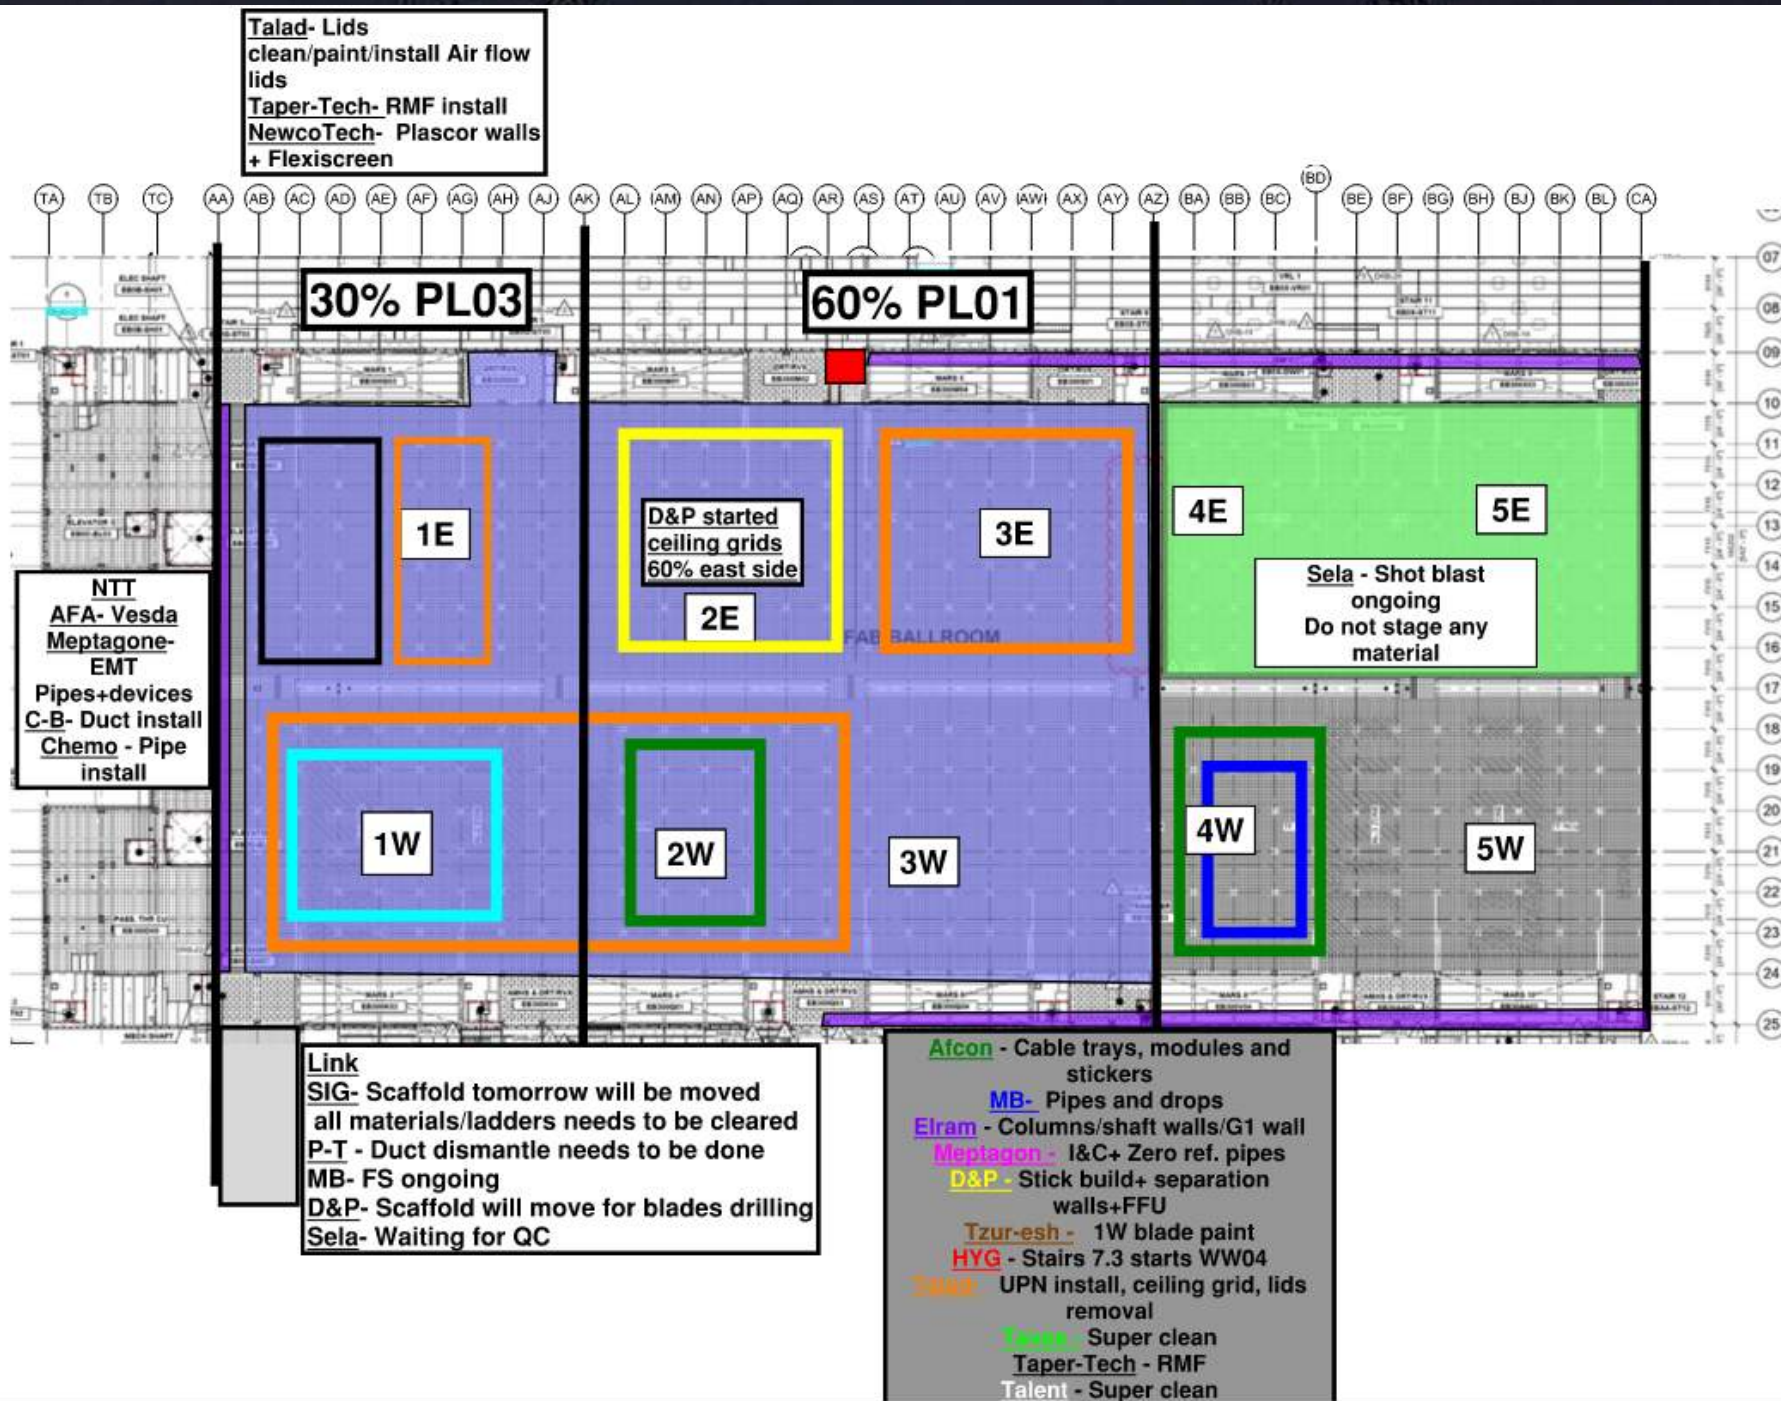

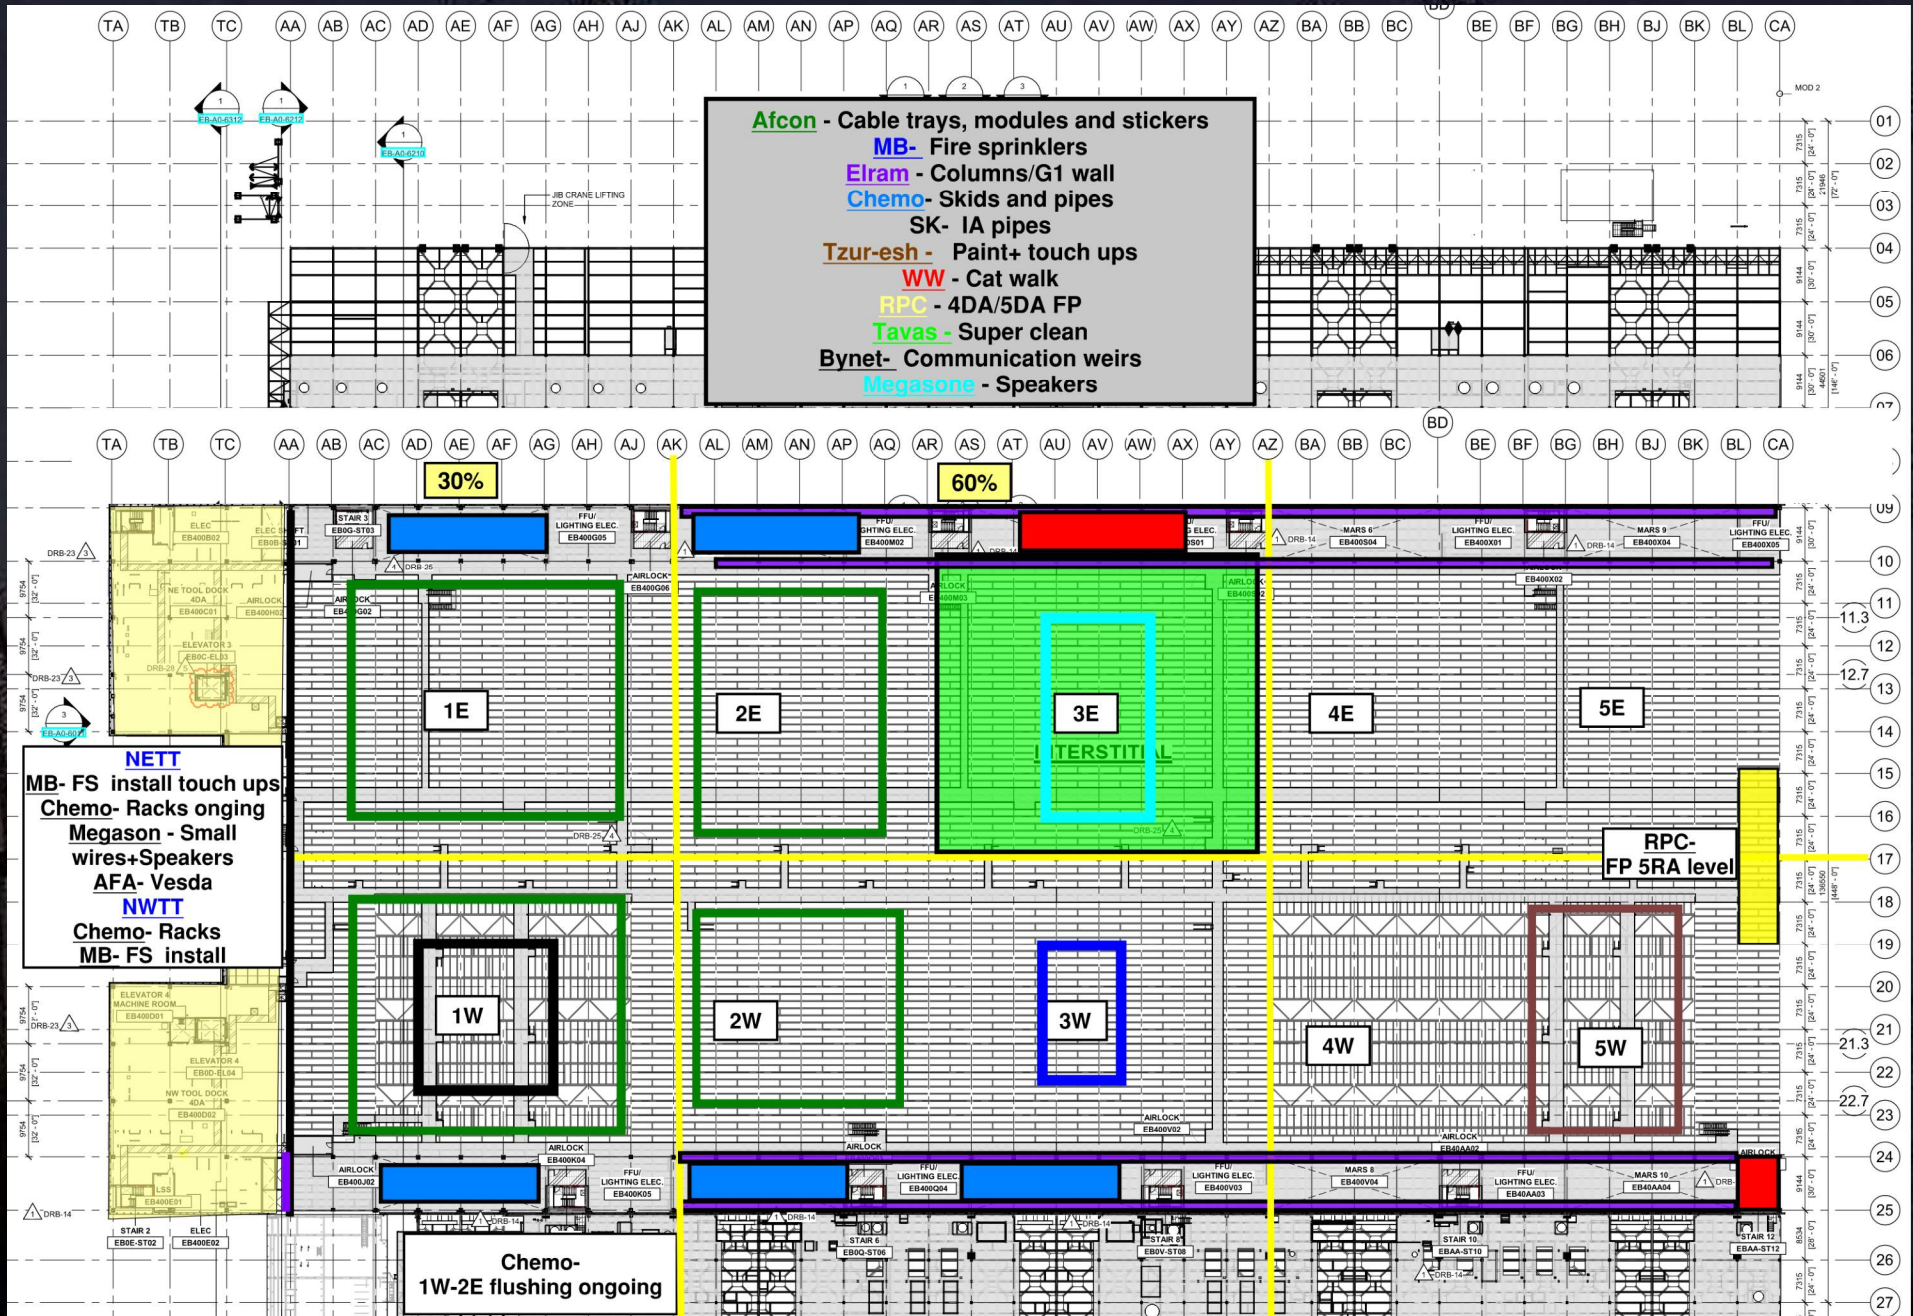

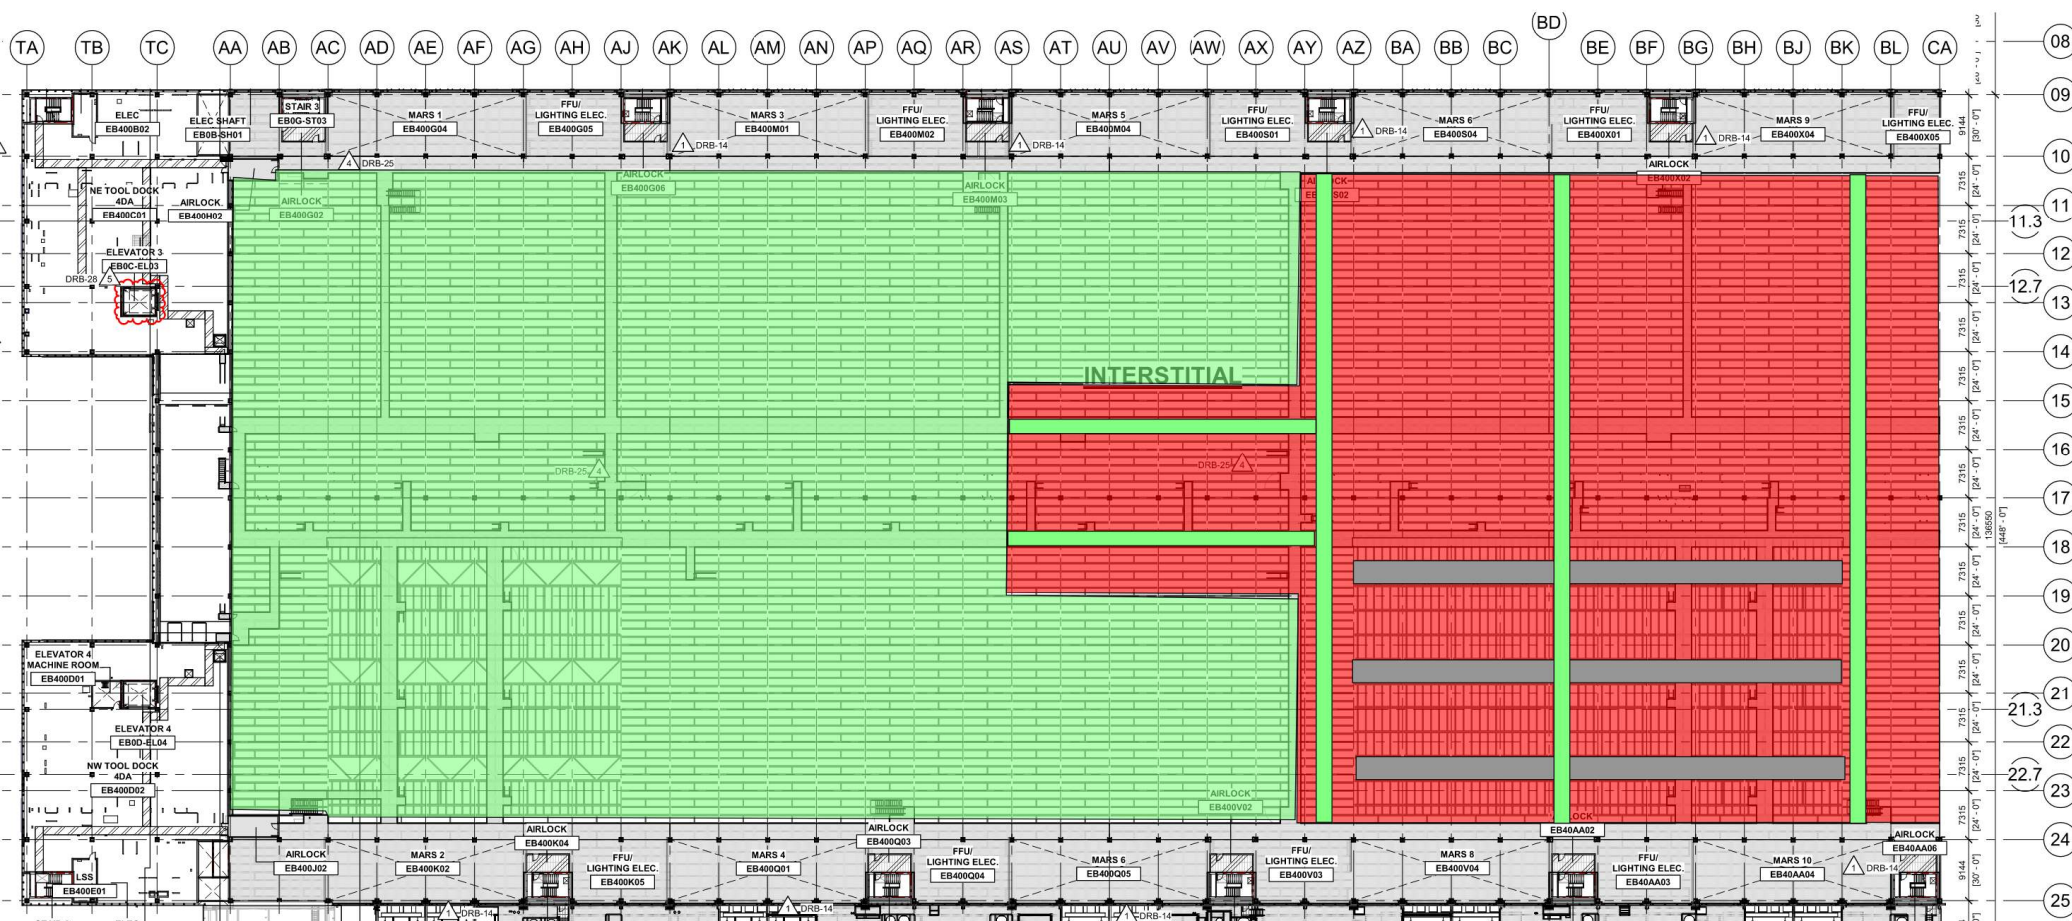

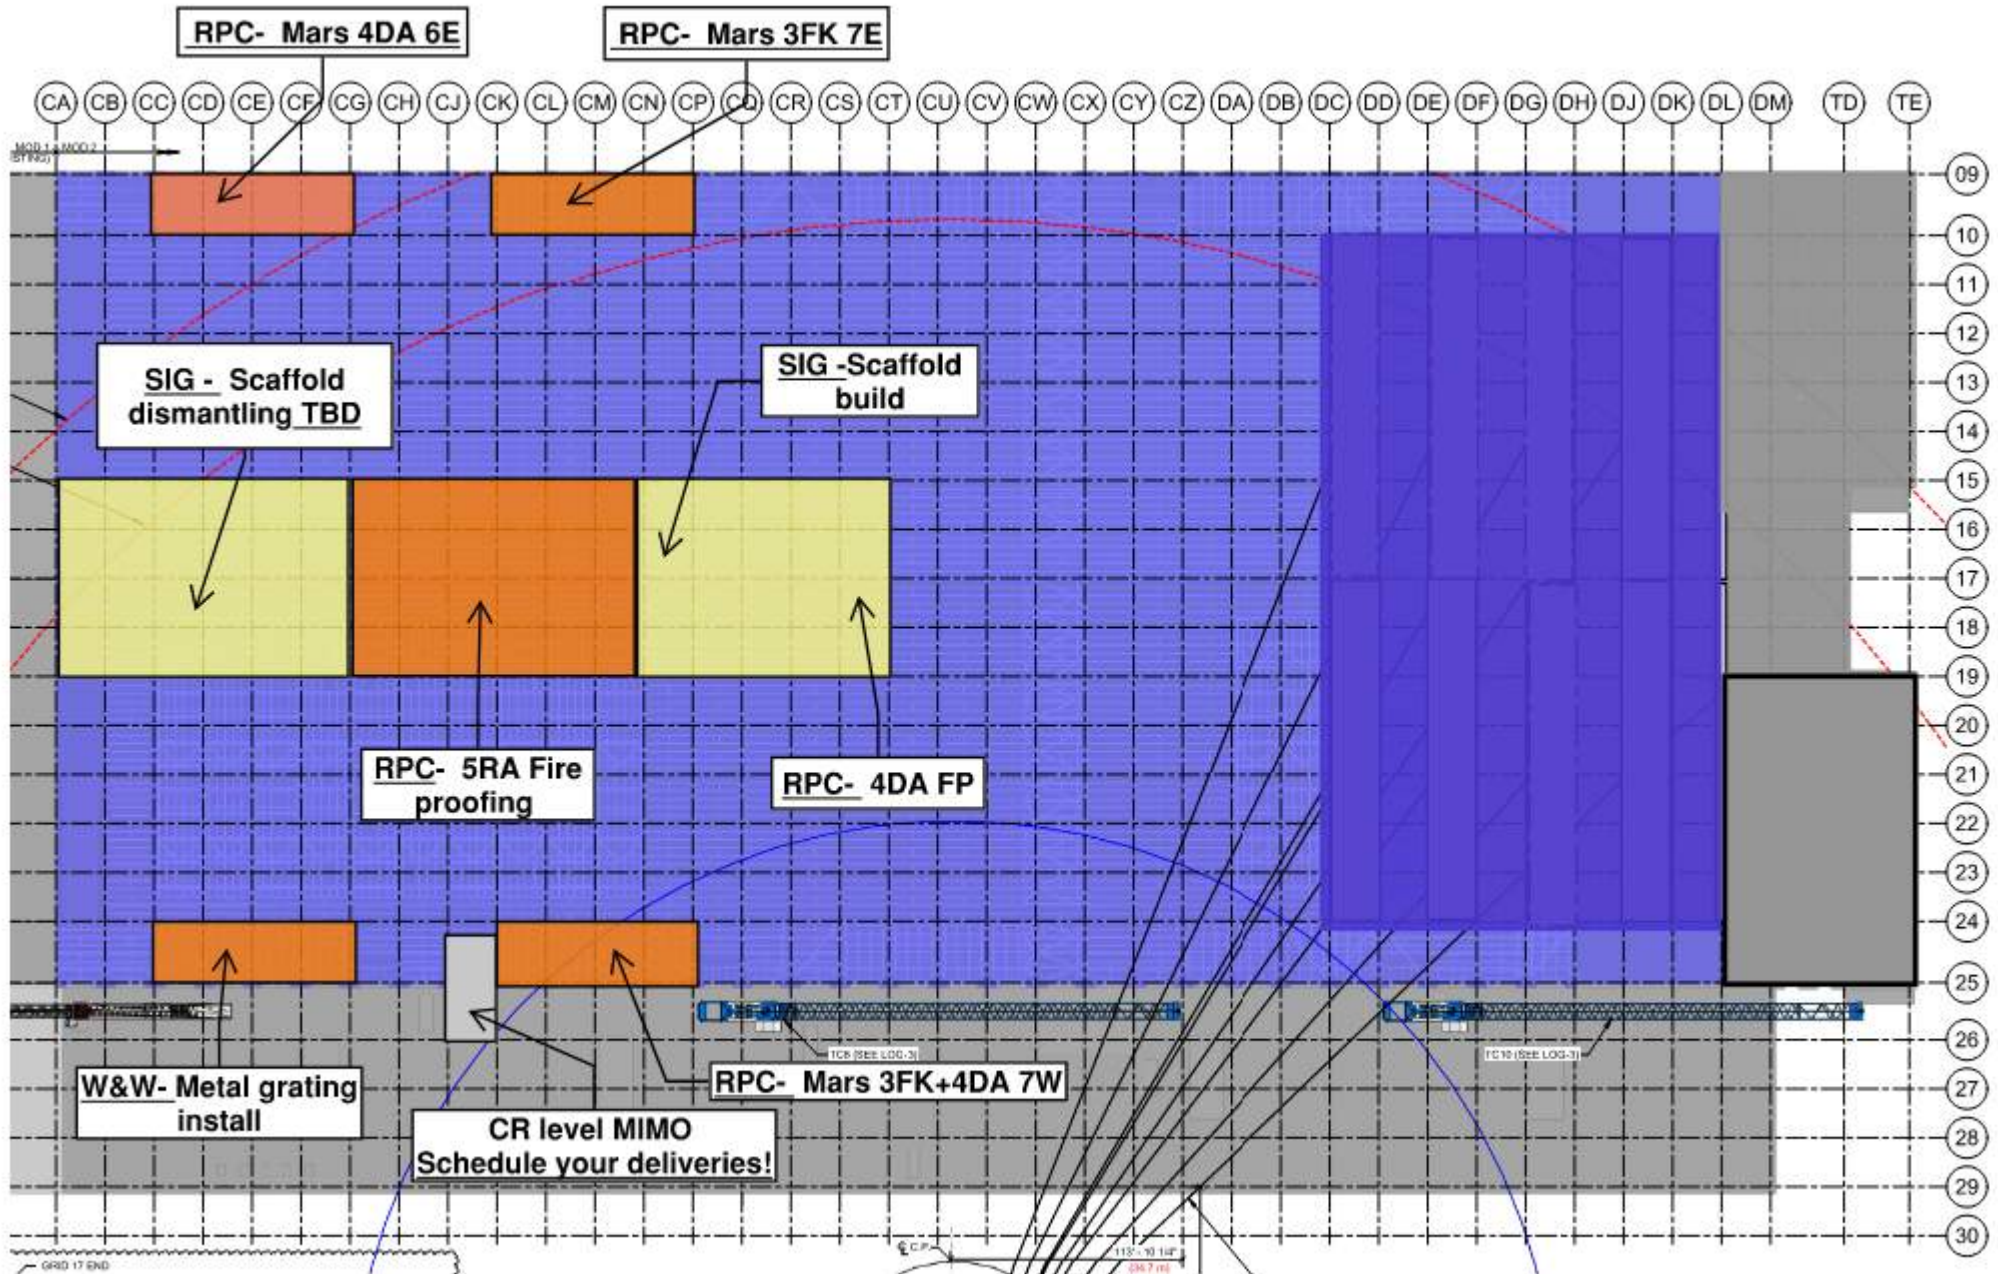




HOFFMAN CONSTRUCTION COMPANY




RPC
**Keep up with
good work**




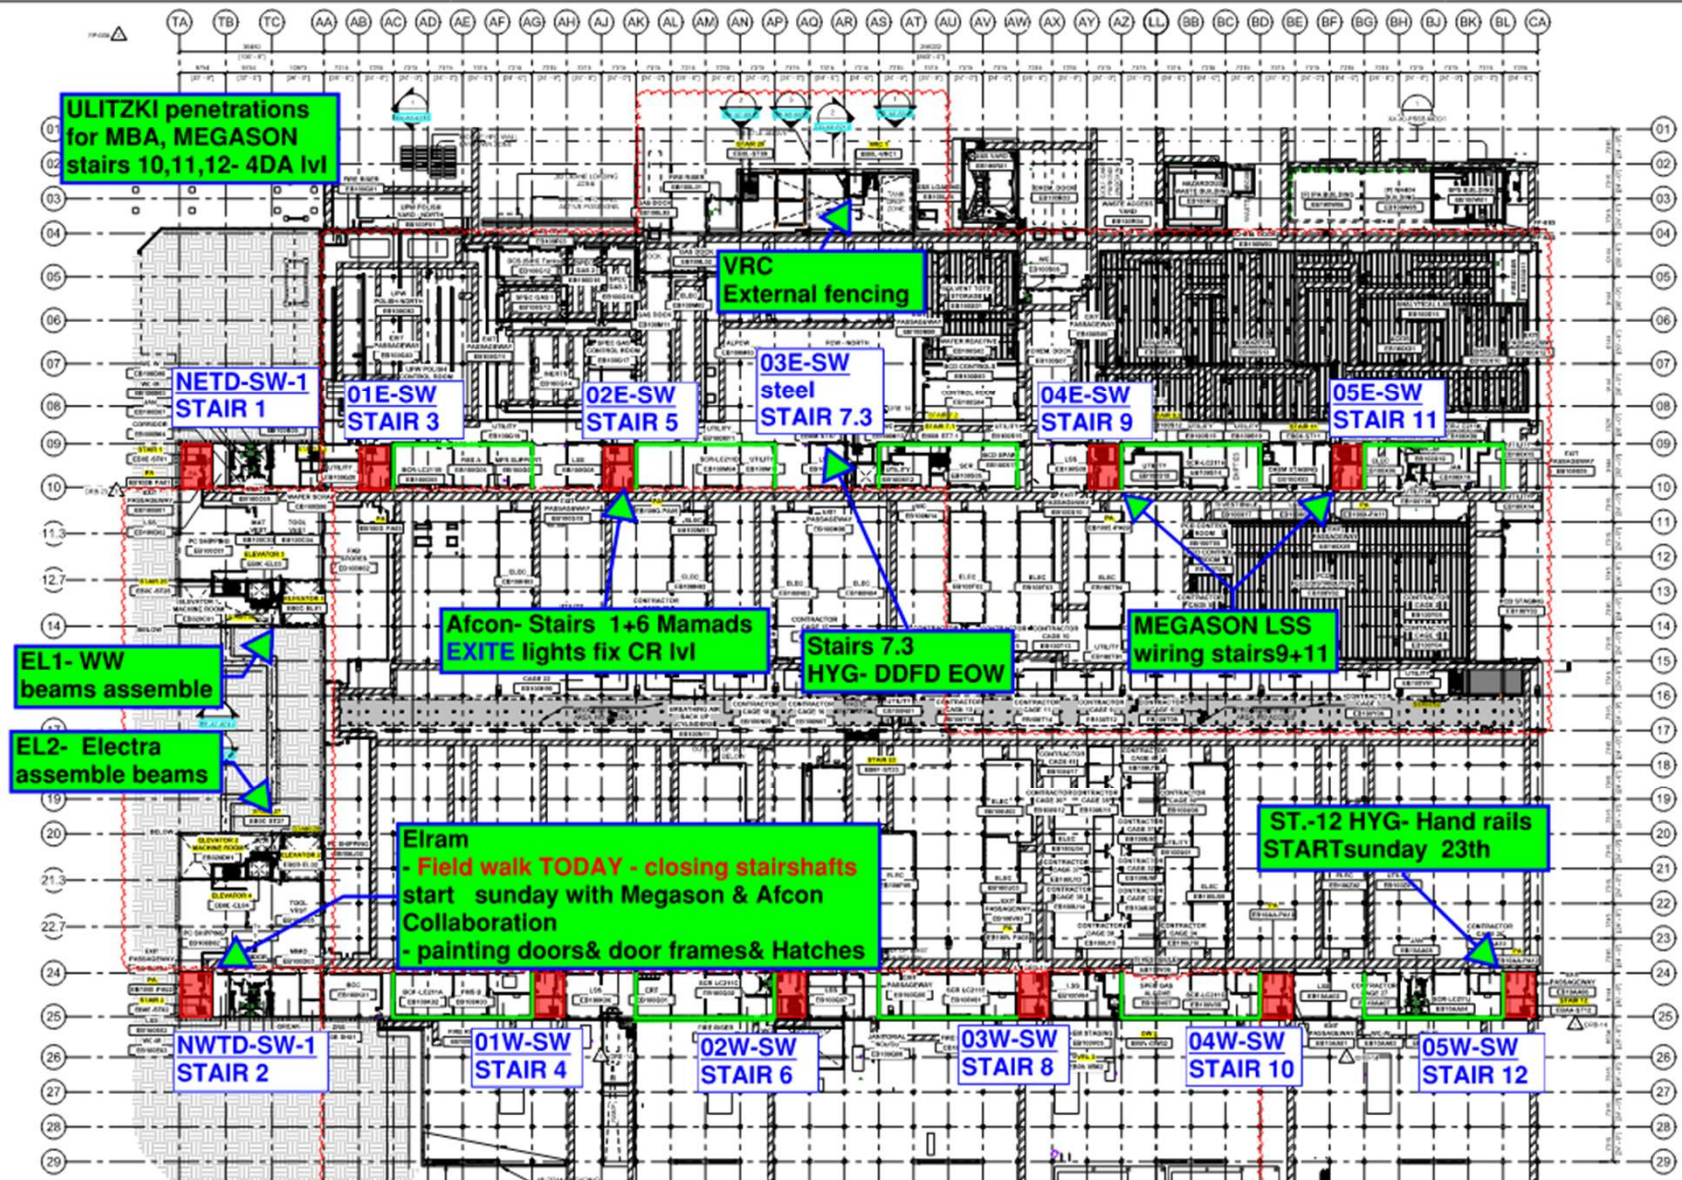


Siding Penetration Request Form



Subcontractor must fill out and submit all required cells in order to get a penetration cut through the siding.

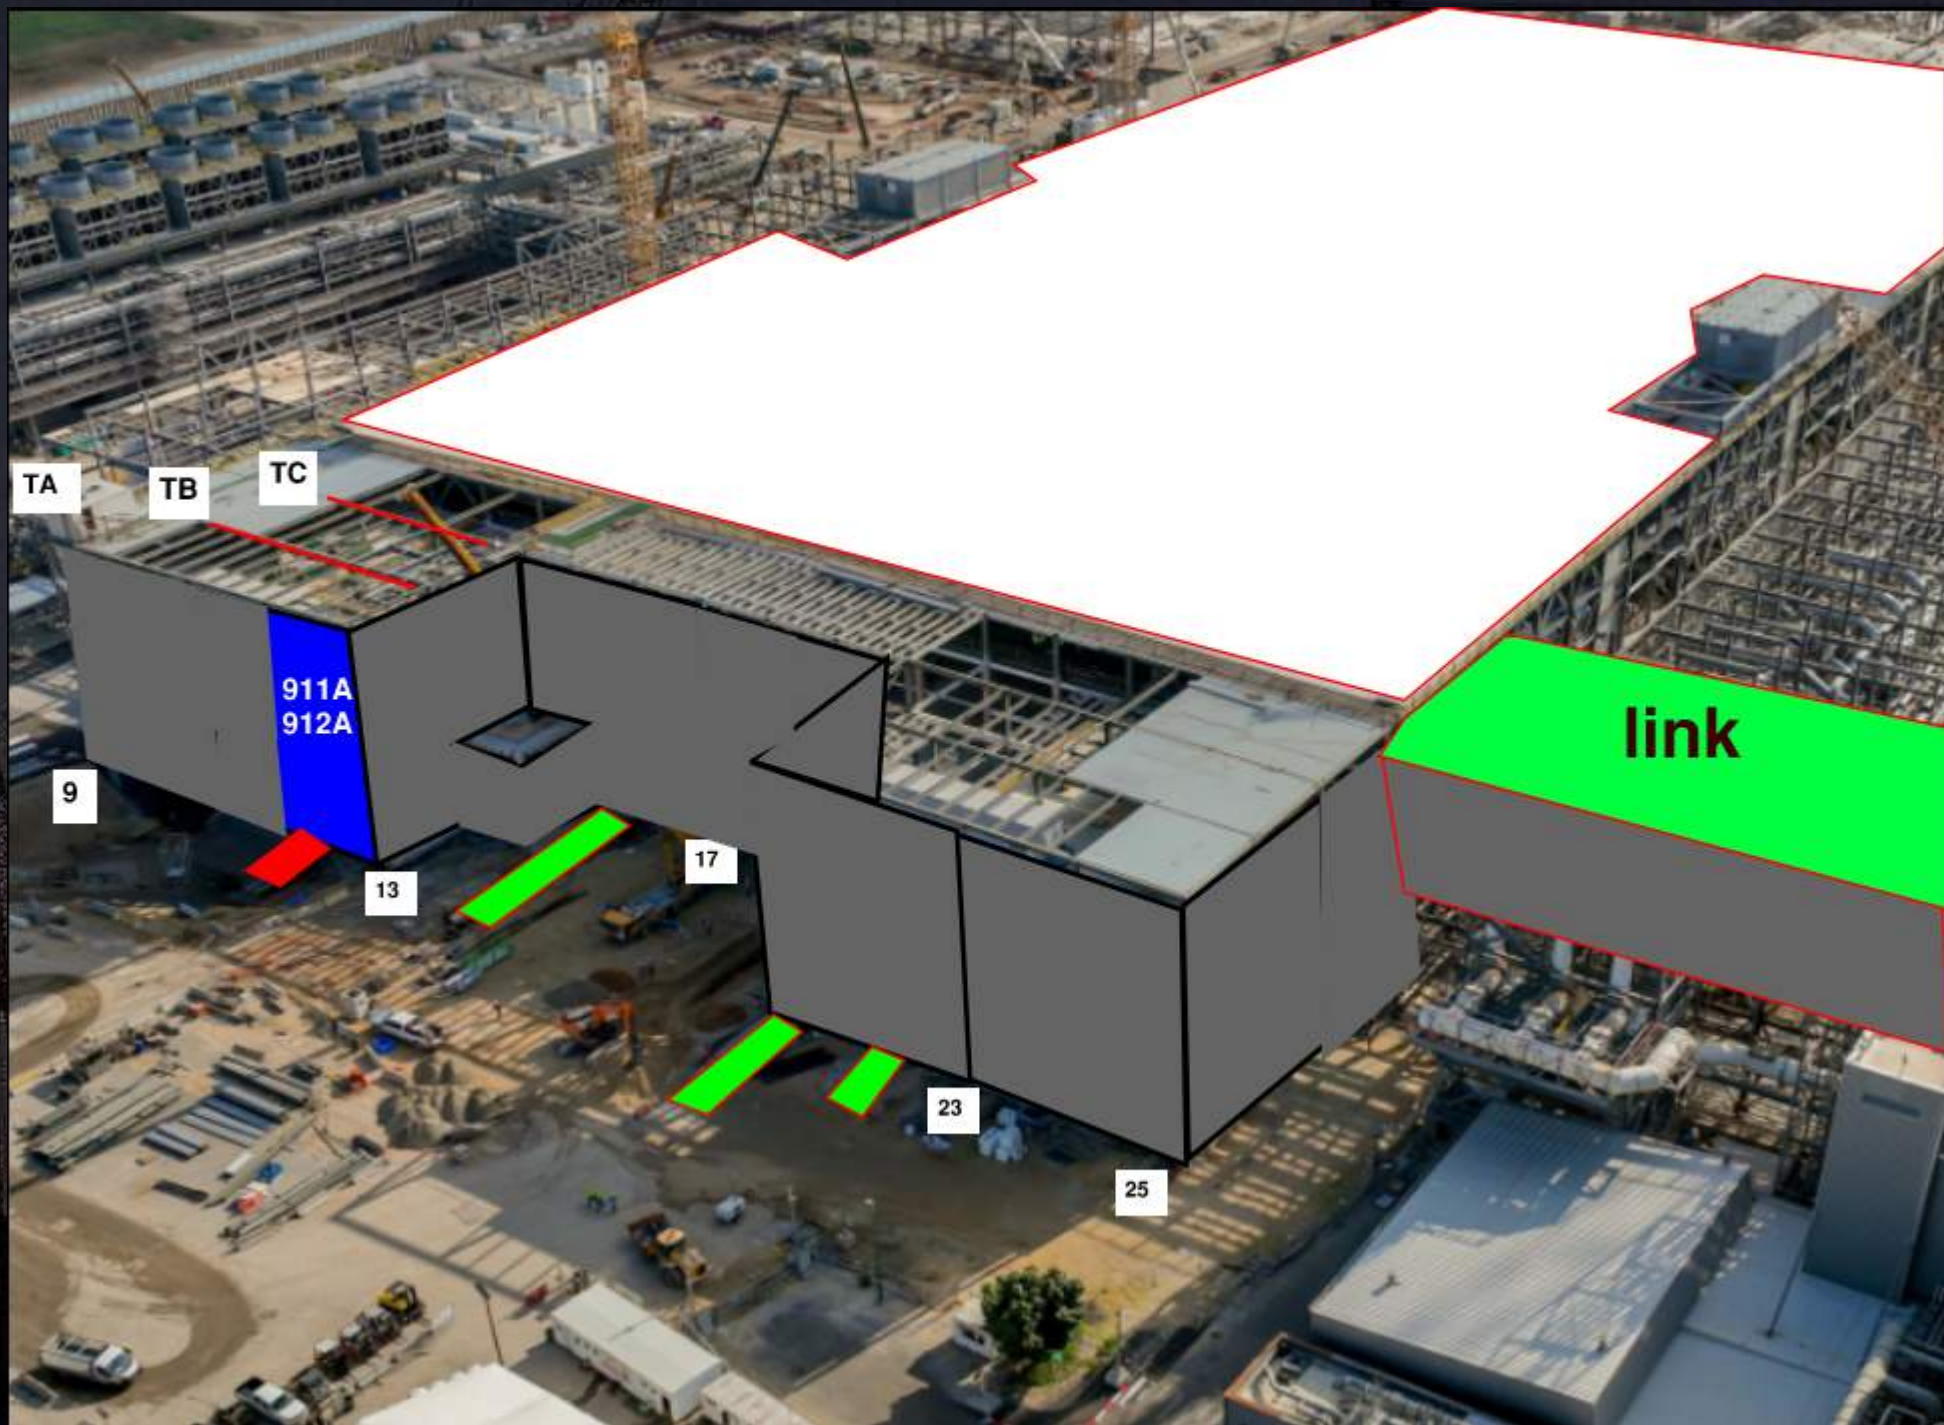

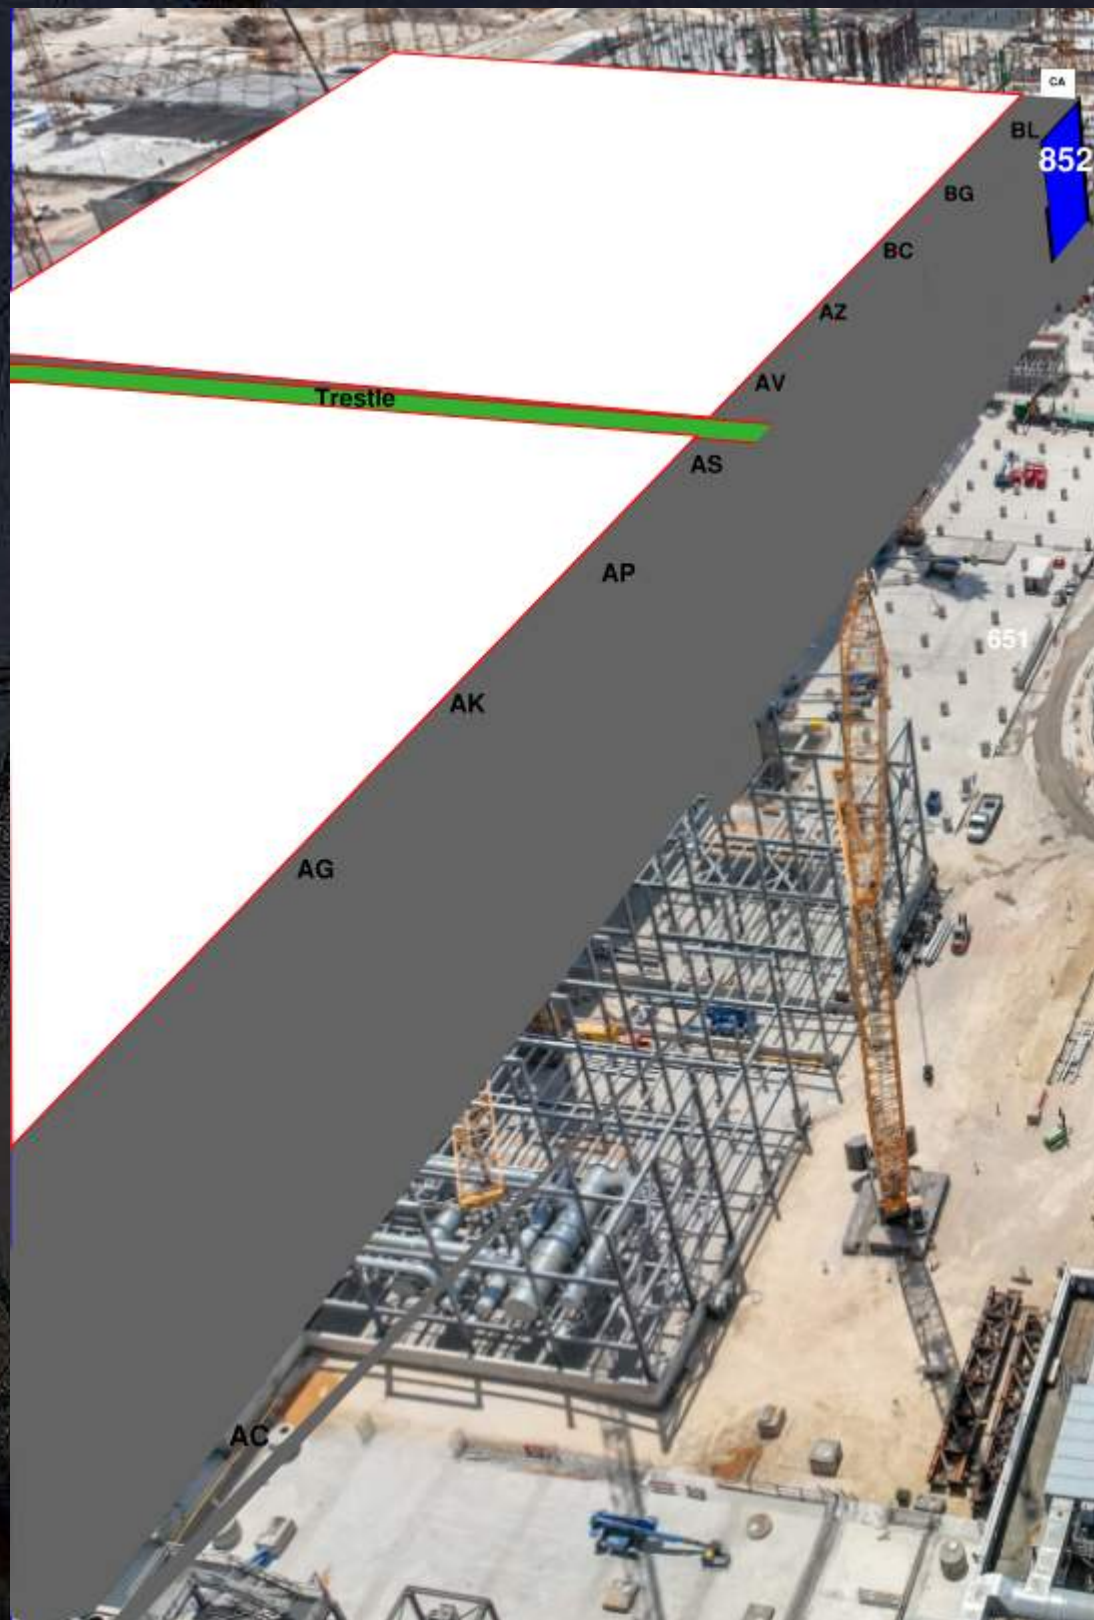

MOD 2 EASTSIDE GIRTS/SIDING

2752/ 2751	2742/ 2741	2732/ 2731	2722/ 2721	2712/ 2711	2552/ 2551	2542/ 2541	2532/ 2531	2522/ 2521	2512/ 2511	2502/ 2501
---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------	---------------

READY FOR GIRTS	
INSTALLING GIRTS	
READY FOR PANELS	
PANELS INSTALLED	

MOD 2 WESTSIDE GIRTS/SIDING

READY FOR GIRTS 

INSTALLING GIRTS 

READY FOR PANELS 

PANELS INSTALLED 

2602/
2601

2612/
2611

2622/
2621

2632/
2631

2642/
2641

2652/
2651

2812/
2811


2822/
2821

2832/
2831

2842/
2841


2852/
2851

PSSS.1

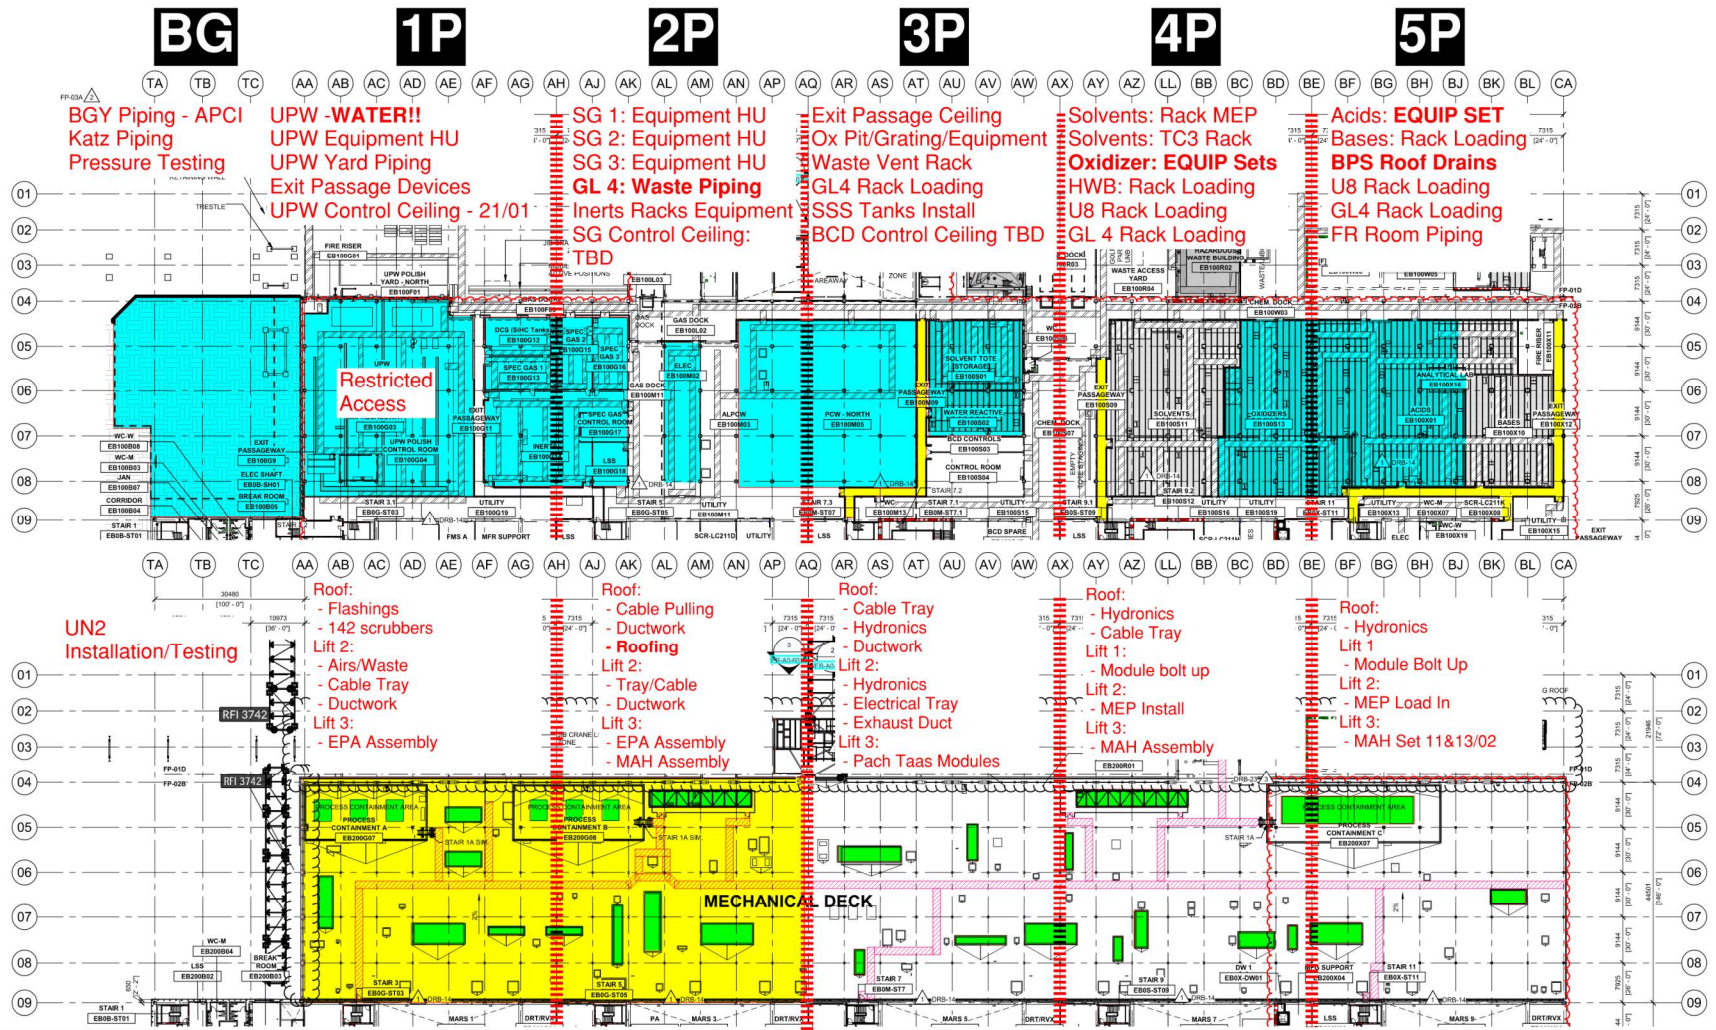


PSSS.2

Utility Level
1YA

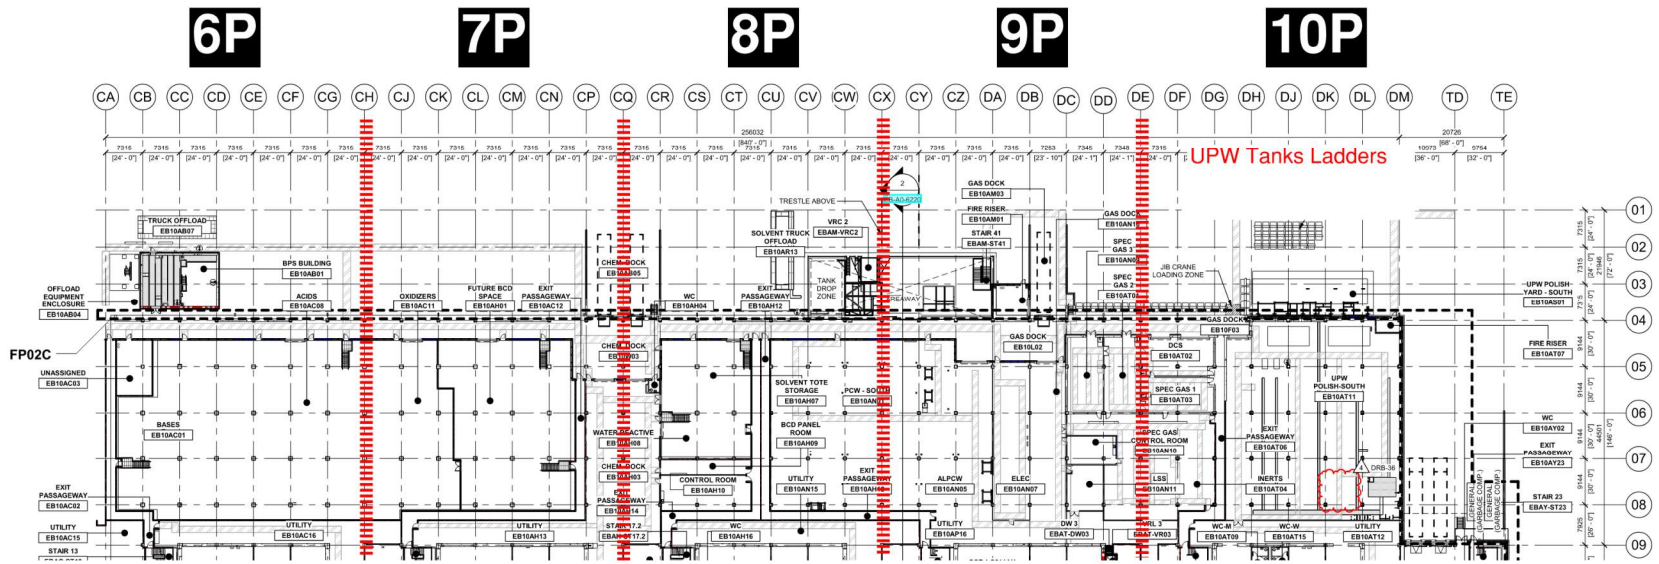


PSSS Roof
2SA

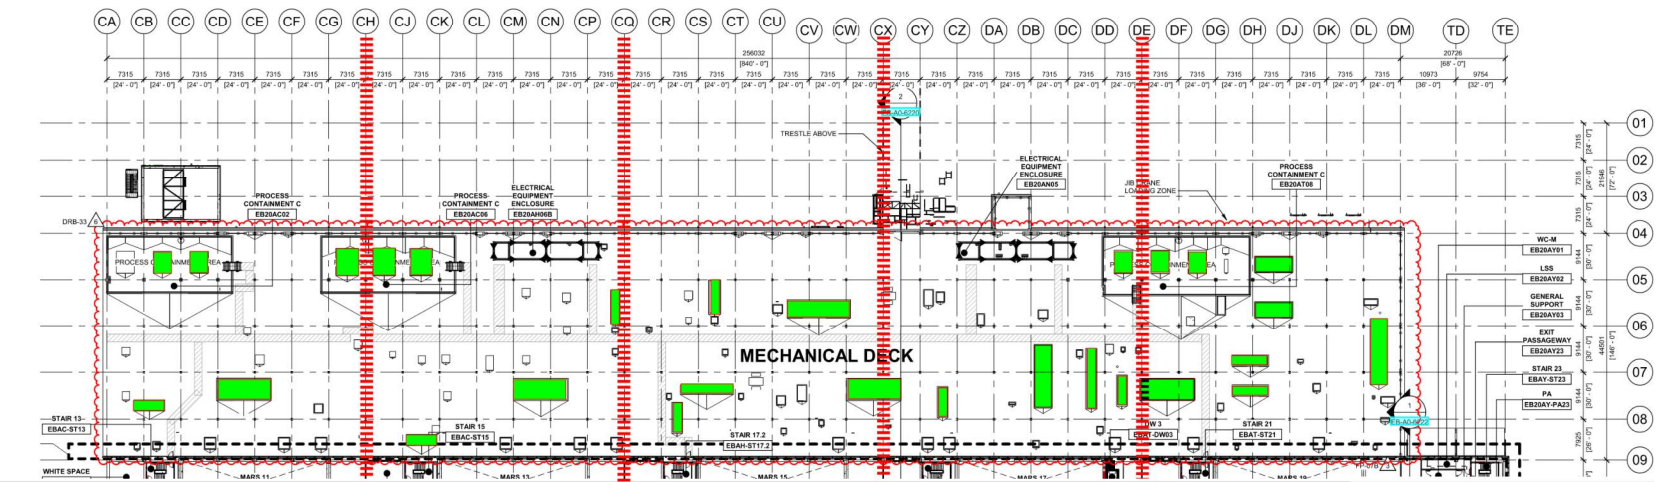

PSSS Pressure Tests

Utility Level
1YA

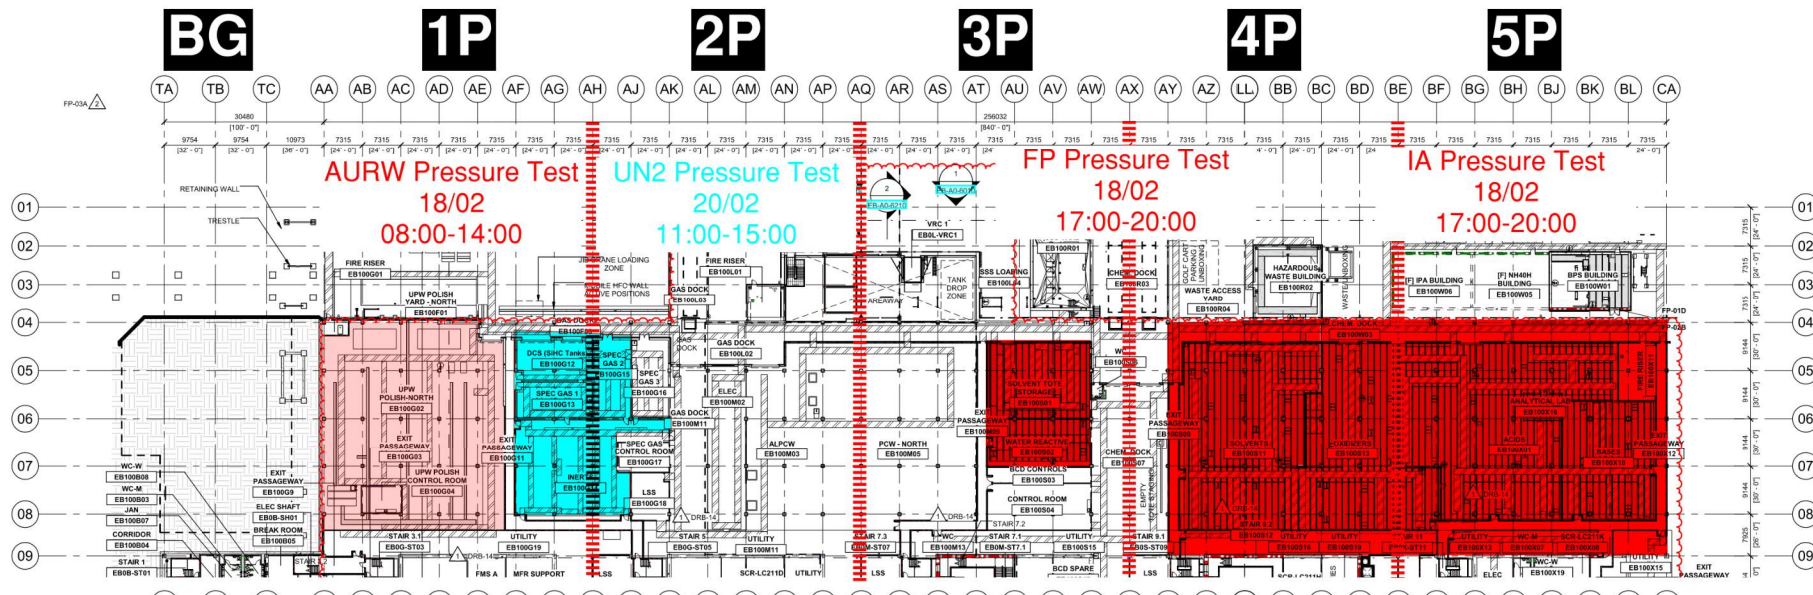

500T Dismantle 18th-20th




WJG – UL

* Megason - working on fire detection and alarm


* Afcon - installation of permanent lighting and cable pulling.
* Pach Taas - installation of modules in west SUT.

* Afcon - installation of permanent lighting and cable pulling to the fixtures.
* Pach Taas - installation of wall penetrations

* SK - installation of 3" cooper pipe
* W&W - welding of shims for outriggers

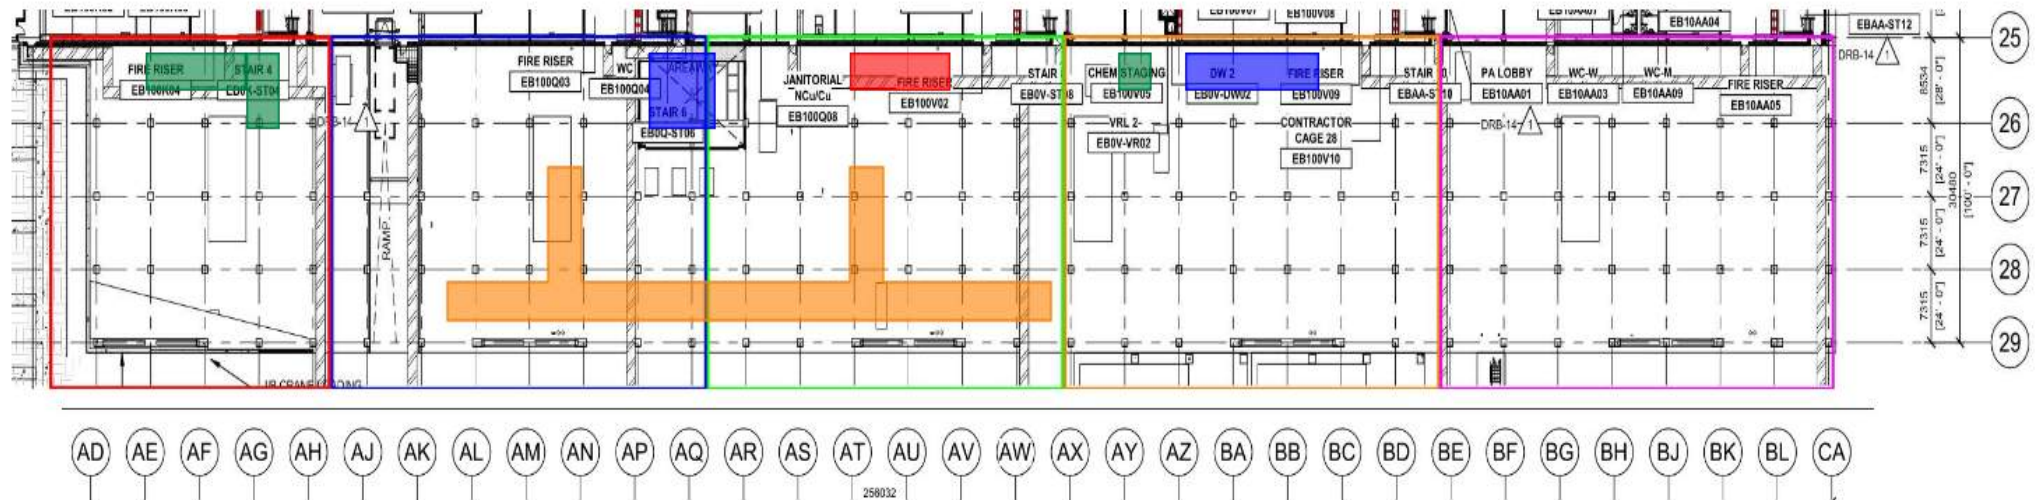

* W&W - working on Jib crane supports.		* Pach Taas - installation of 1800 mm module and WP.	* SK - installation of CRW pipes to MAH. *Afcon - installation of cable trays and connections to MAH. *4J MAH scaffold will be dismantled on 27/02/25	* Chemo Aharon - Insulation of UPN 117.
--	--	--	---	---

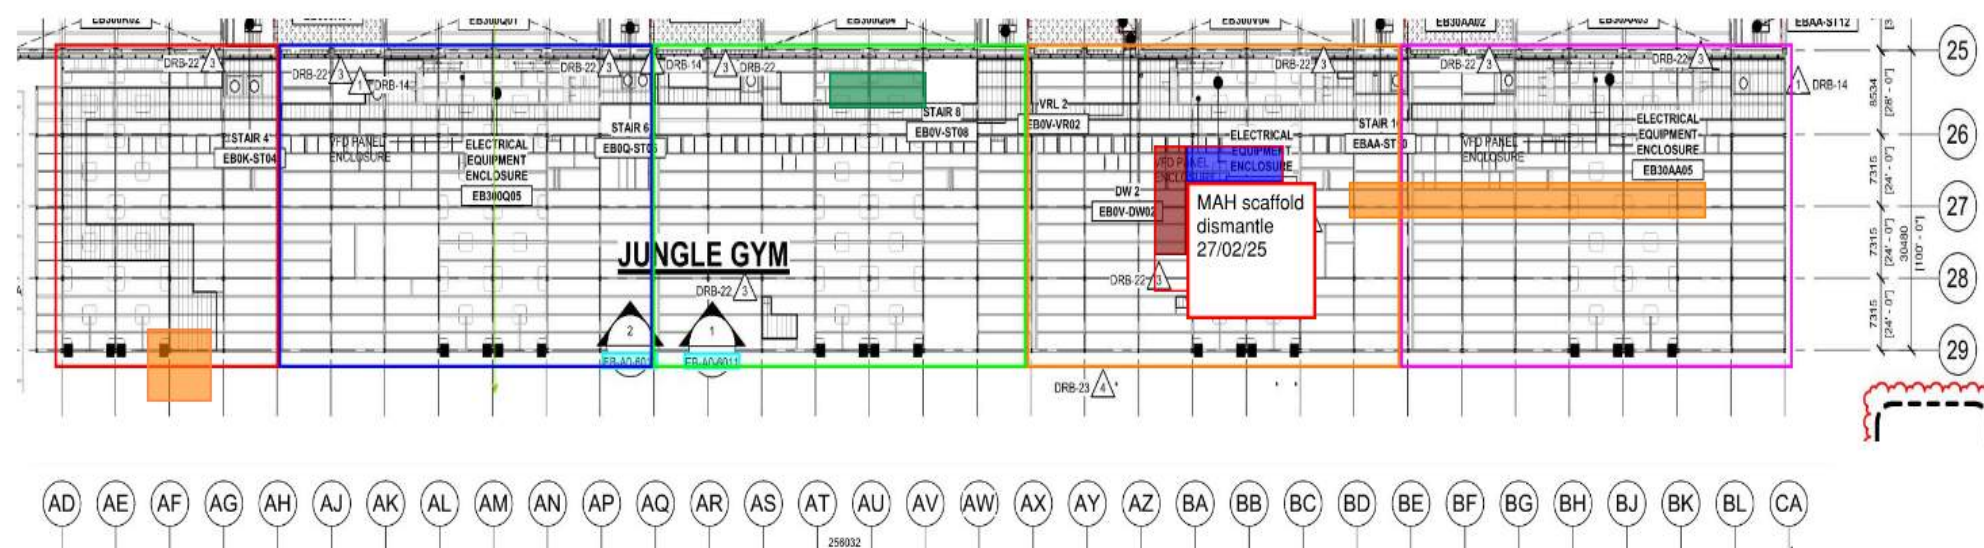

WJG – Lift 3

		* Pach Taas - working on connections of horizontal ductwork and EPA * Sami Najami - cutting grating penetrations.	* Sami Najami - cutting grating penetrations. * W&W -welding supports for Jib crane.	Sami Najami - cutting grating penetrations.
--	--	---	--	--



Crane logistics

Crane: 220 ton crane
location: AF on west
road
leaves the WJG on
27/02/25

Crane: 500 ton crane
location: AQ on west
road


Crane: 650 ton crane
location: BE-BK on west
road




[illegible]




CUB 1 Exterior Pre-Punch Status

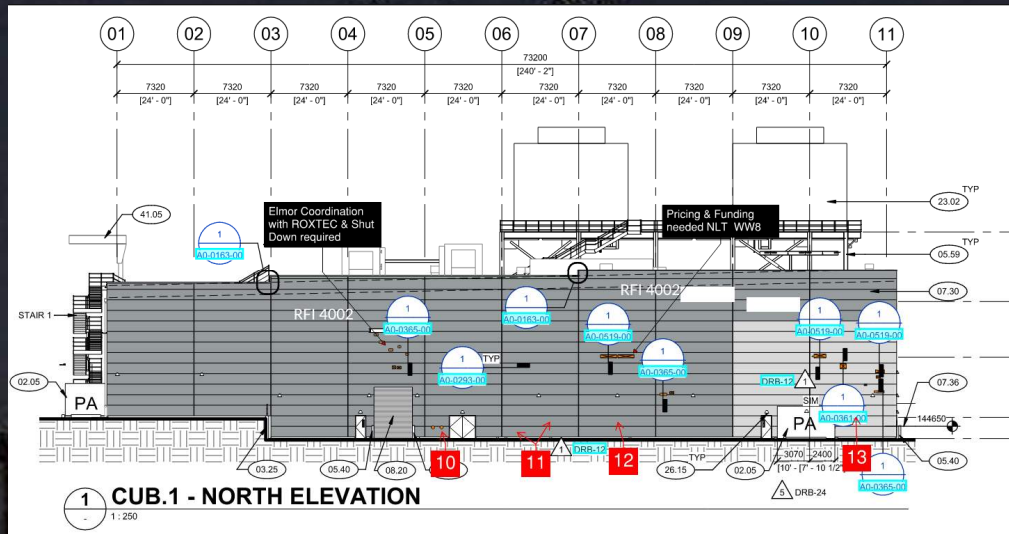


1. North Elevation ROXTEC Electrical in Coordination with Elmor WW 9
2. West Elevation pending UN2 tie in, Blank out Conditioned water to CUB 2
3. Set Final Man door complete Access Controls March 6- 20
4. Light Fixtures ongoing West El.

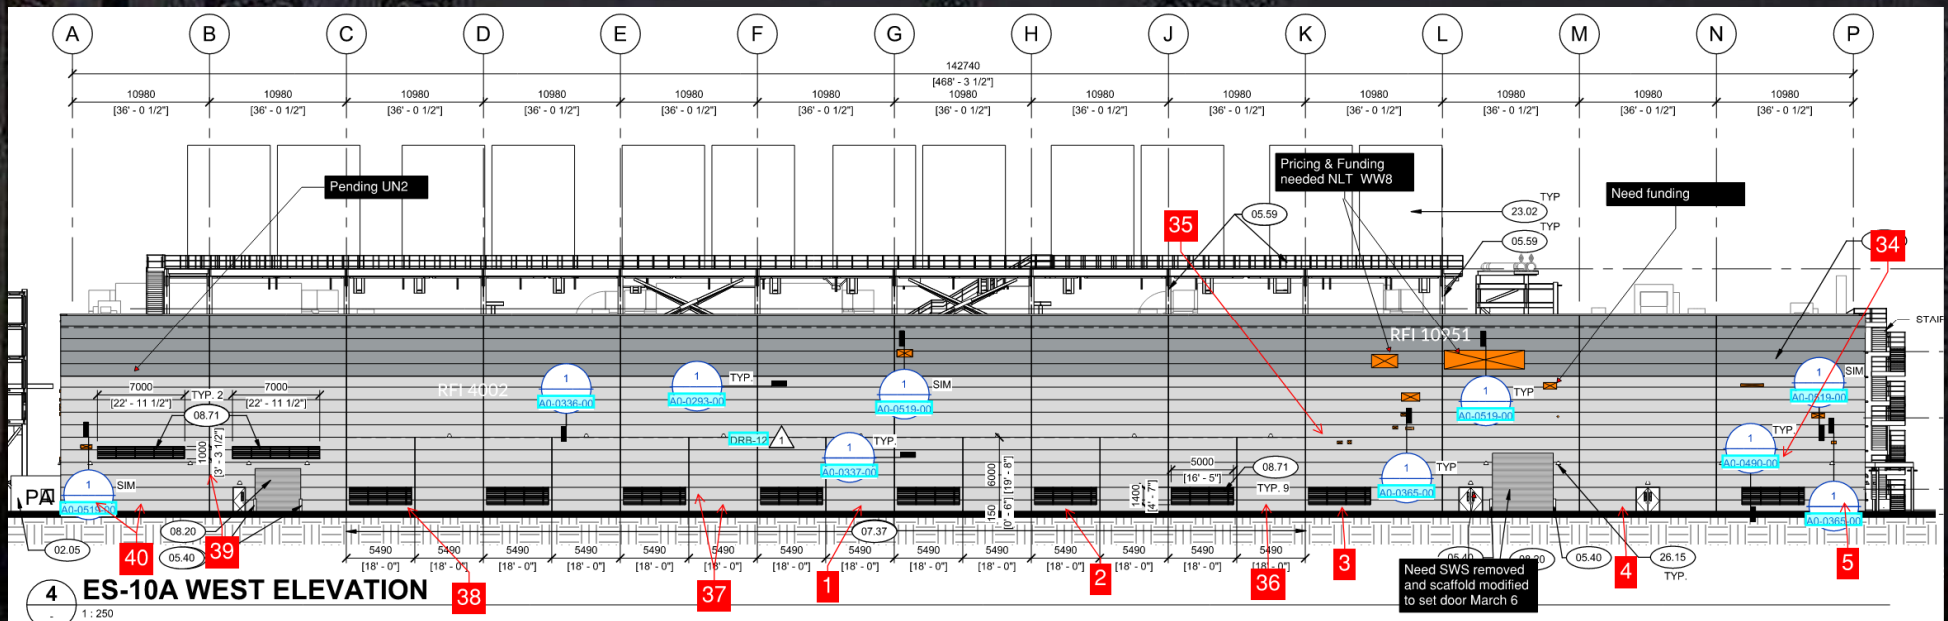

CUB 1 – EXTERIOR/ROOF

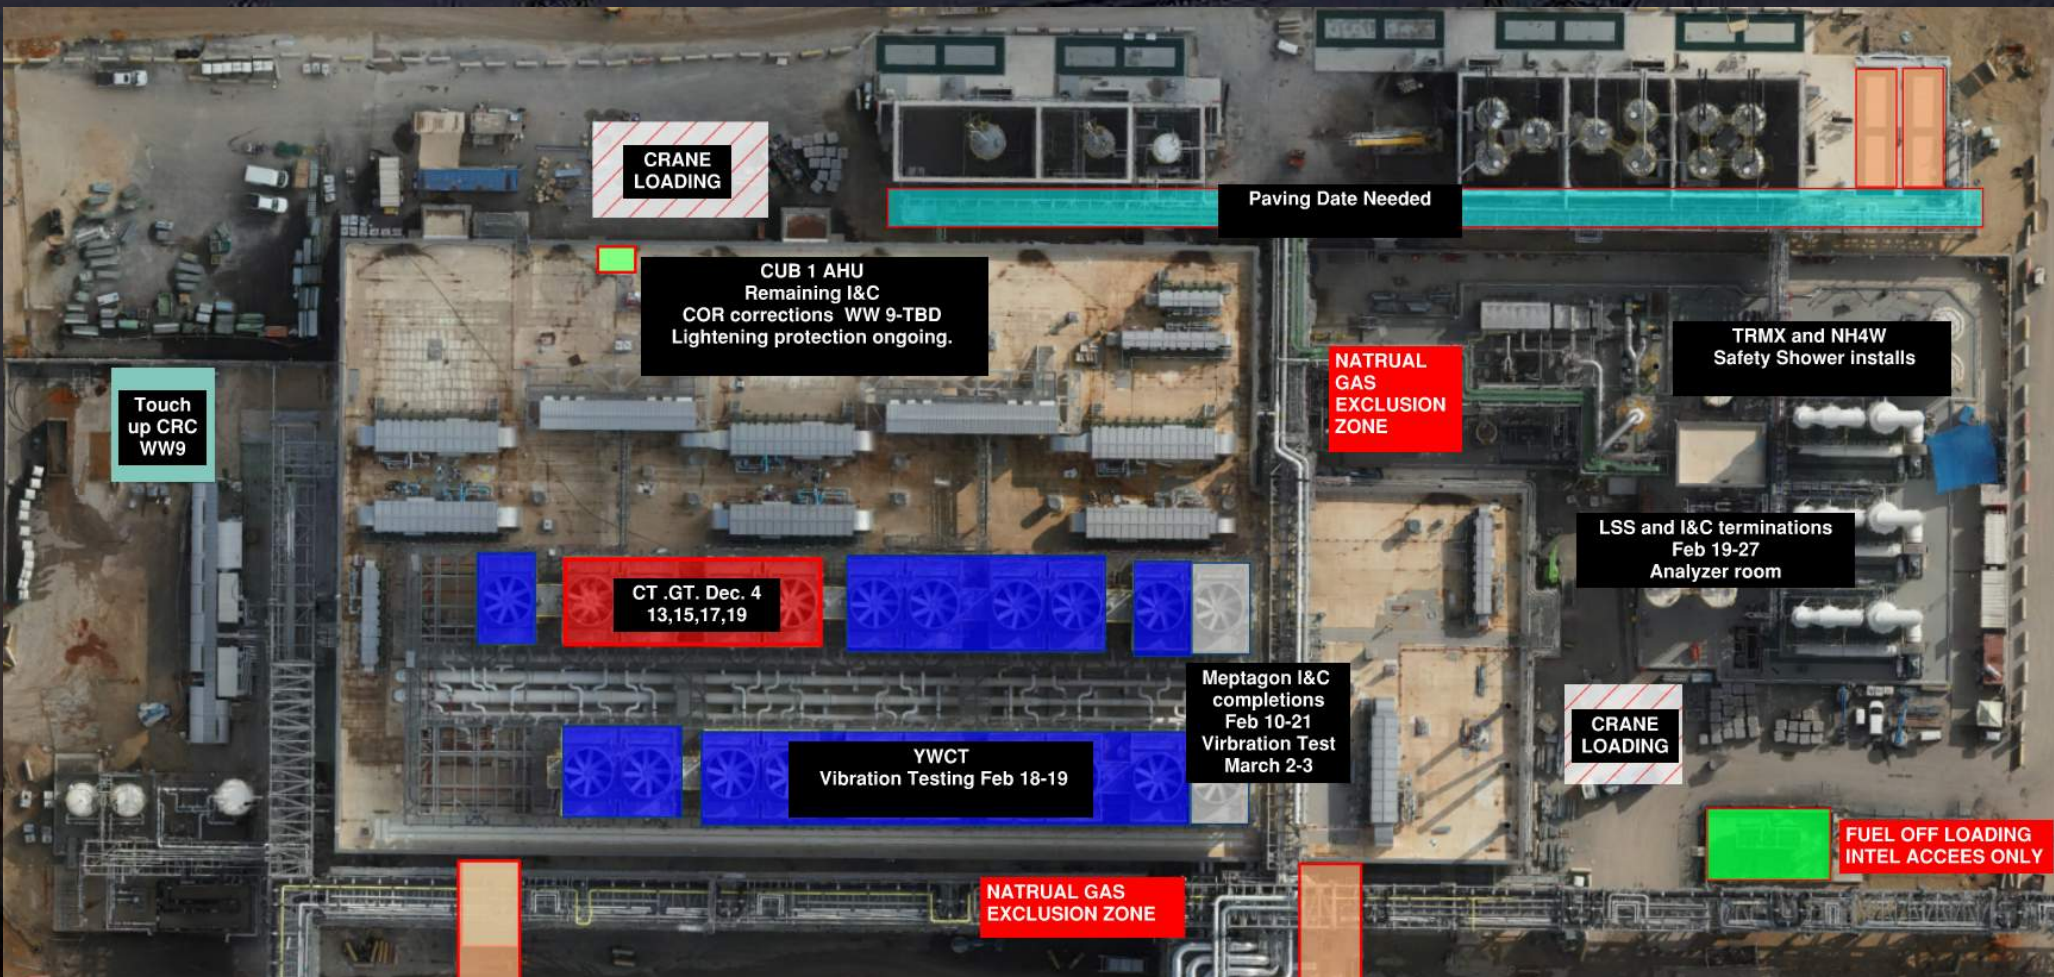


CUB 2- Load in ,H&T, Framing and Sheetrock

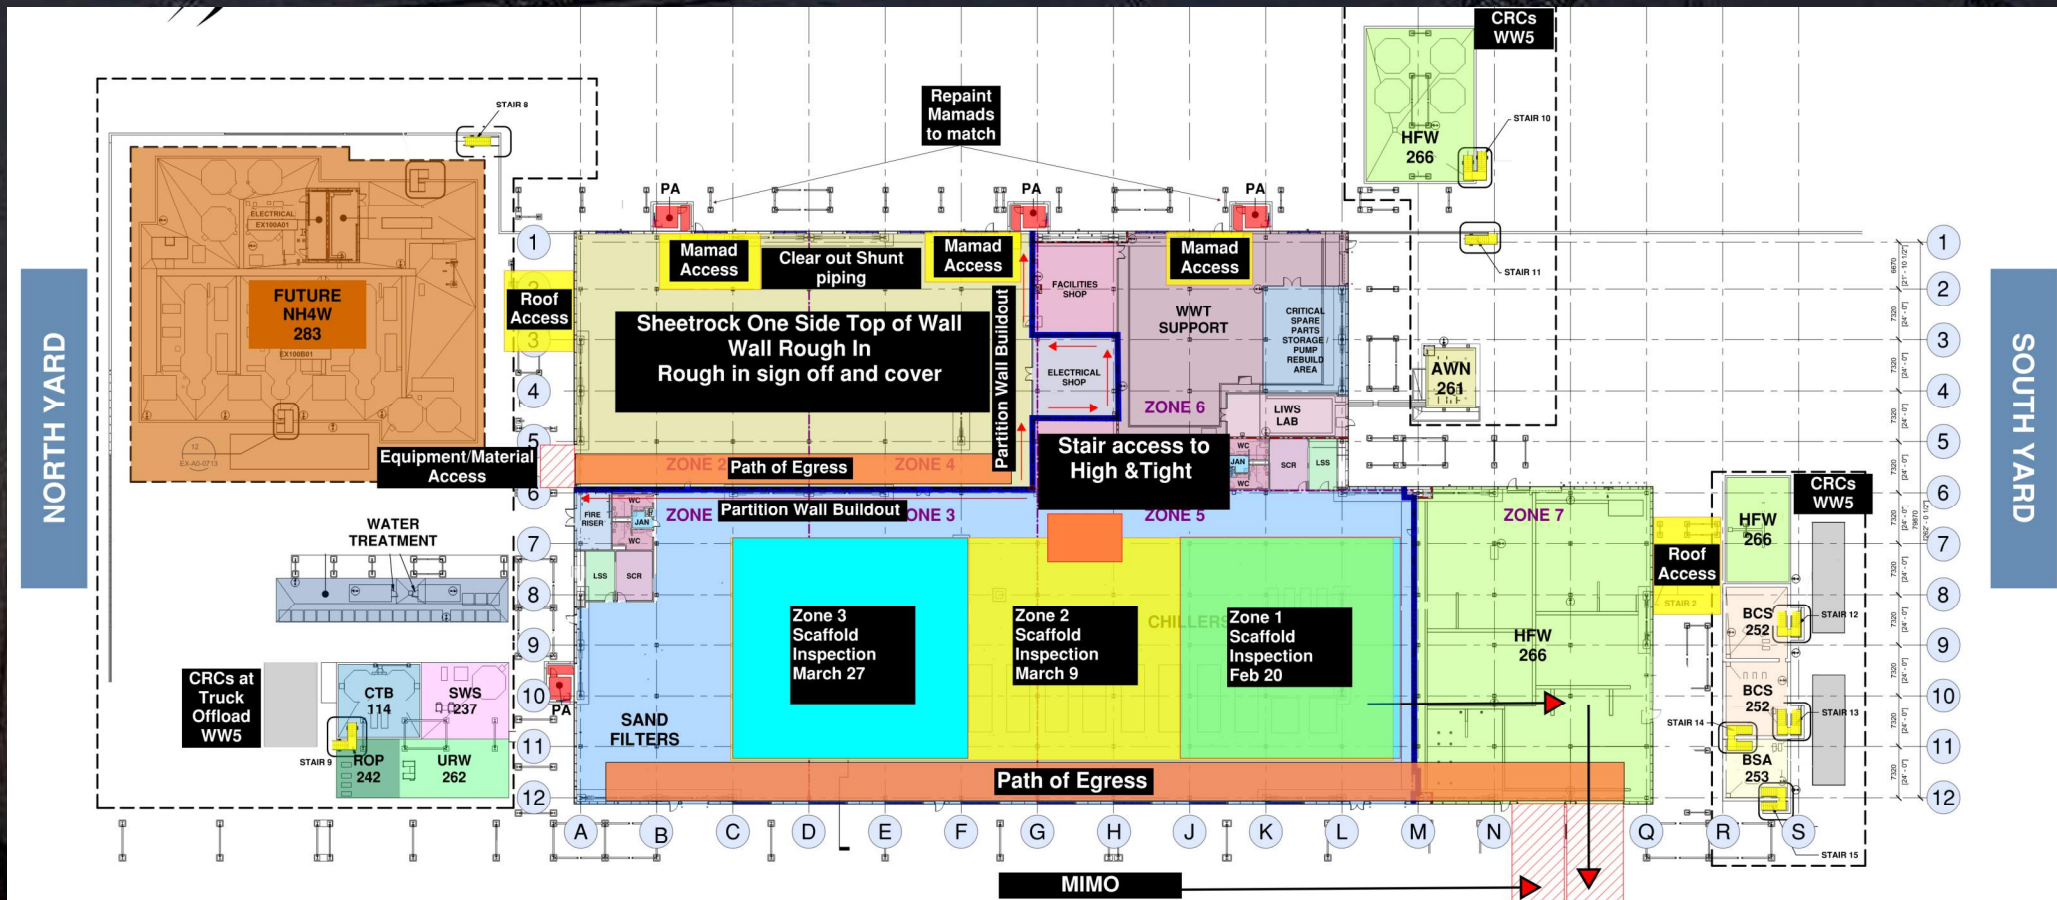


CUB 2 – EXTERIOR/ROOF





HOFFMAN CONSTRUCTION COMPANY

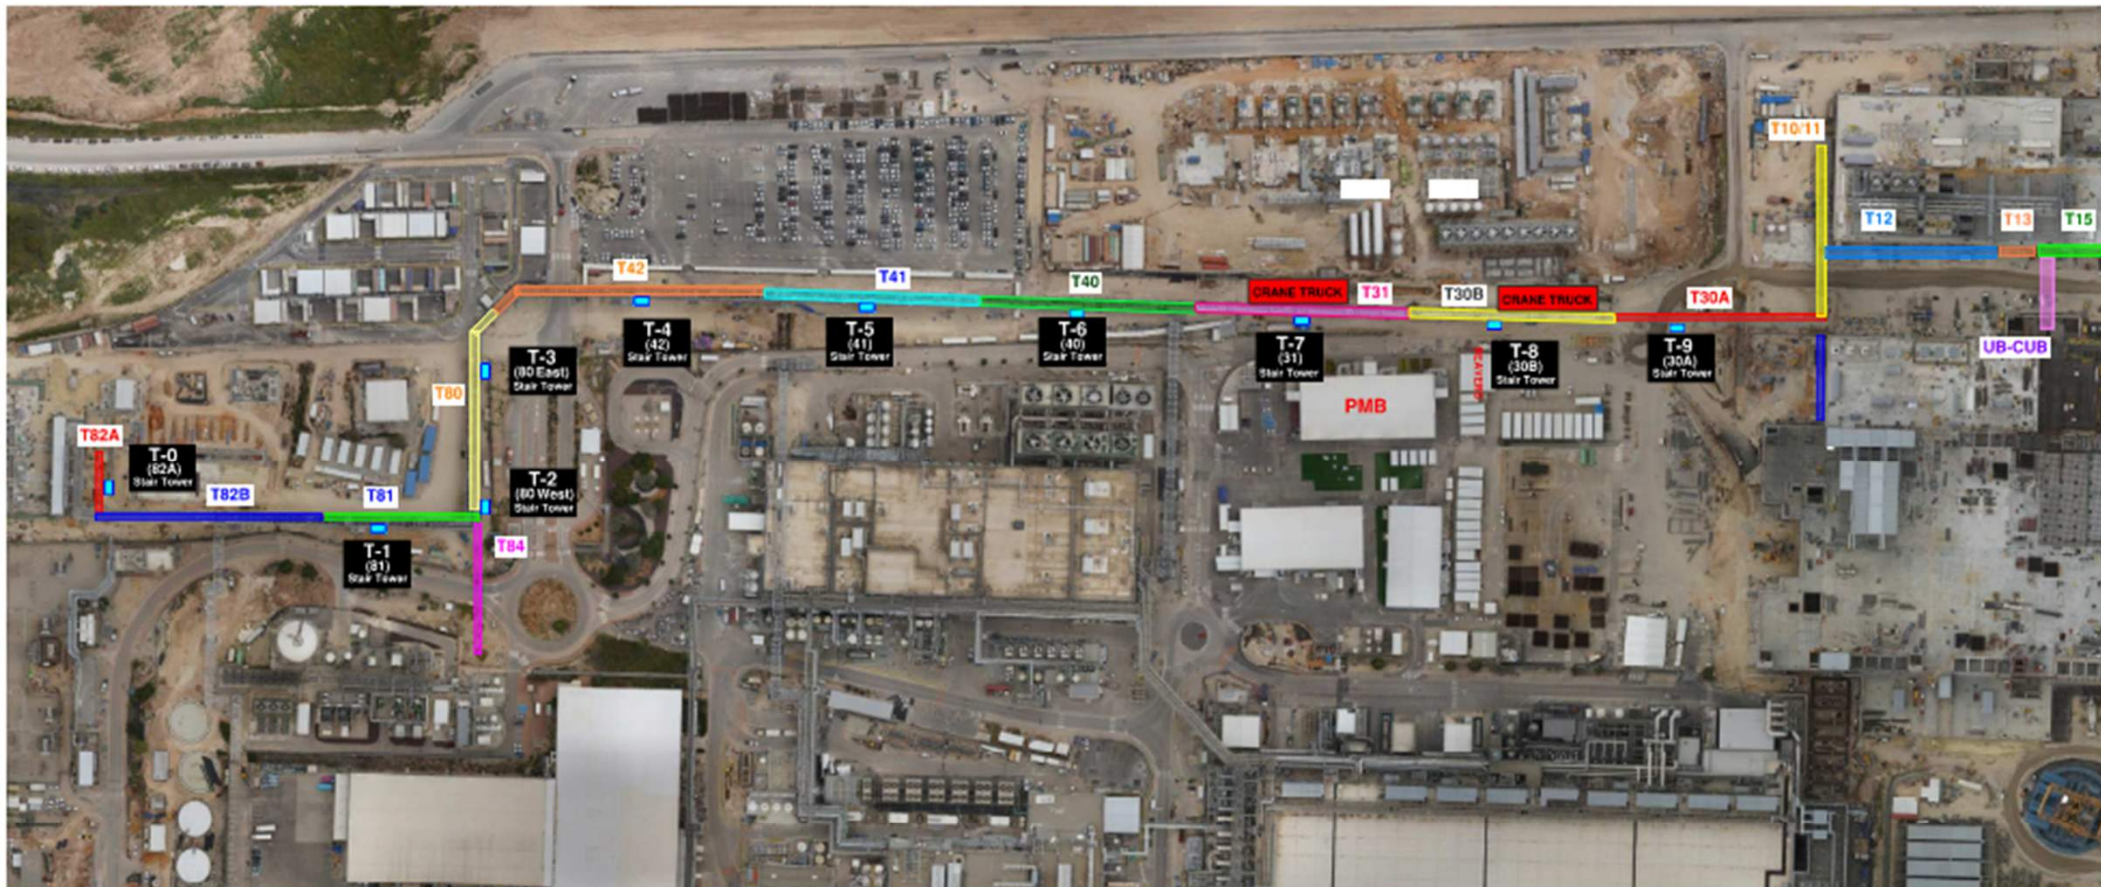




Daily Coordination Meeting

Site Logistics

North

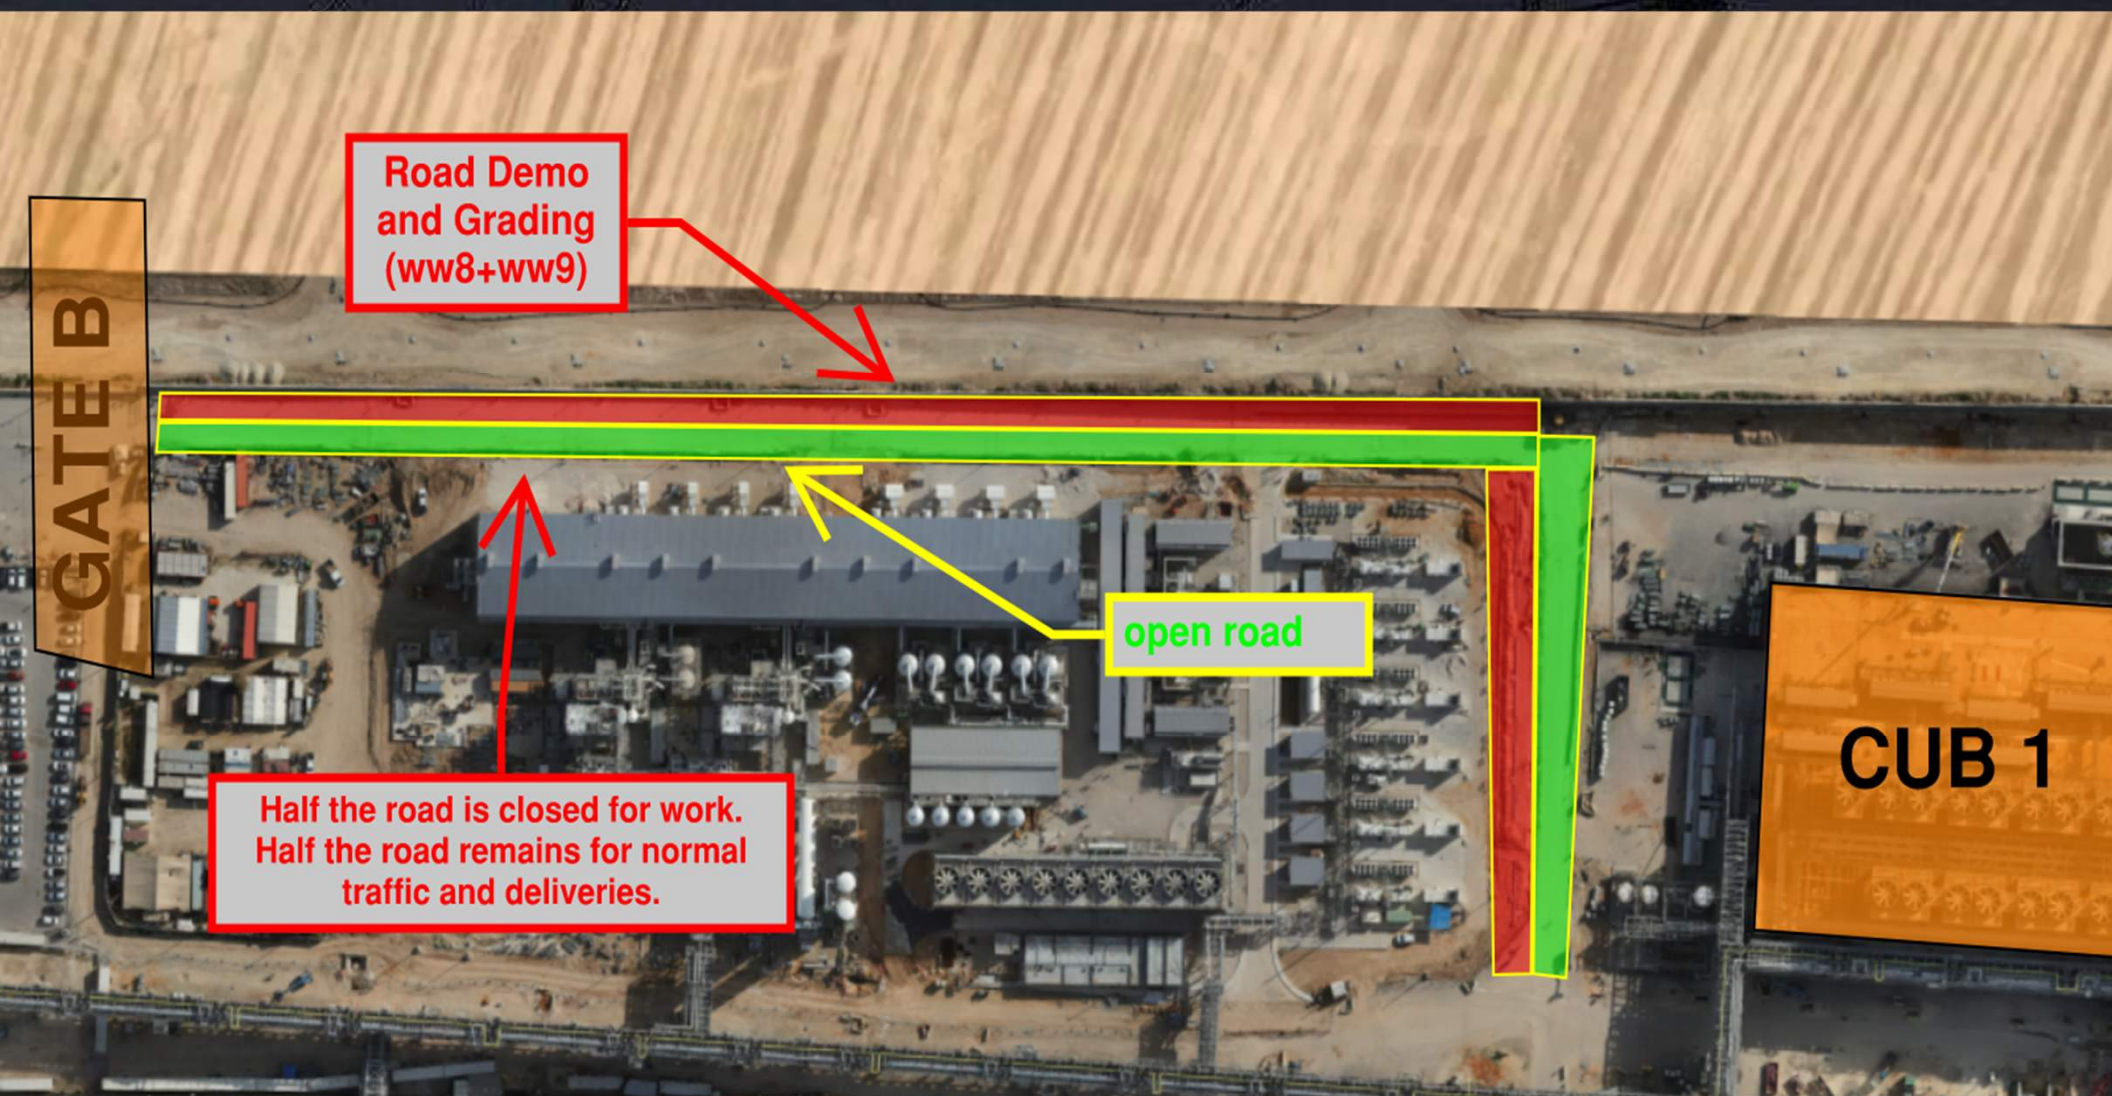



Daily Coordination Meeting

Site Logistics North






HOFFMAN CONSTRUCTION COMPANY



Daily Coordination Meeting

Site Logistics

South

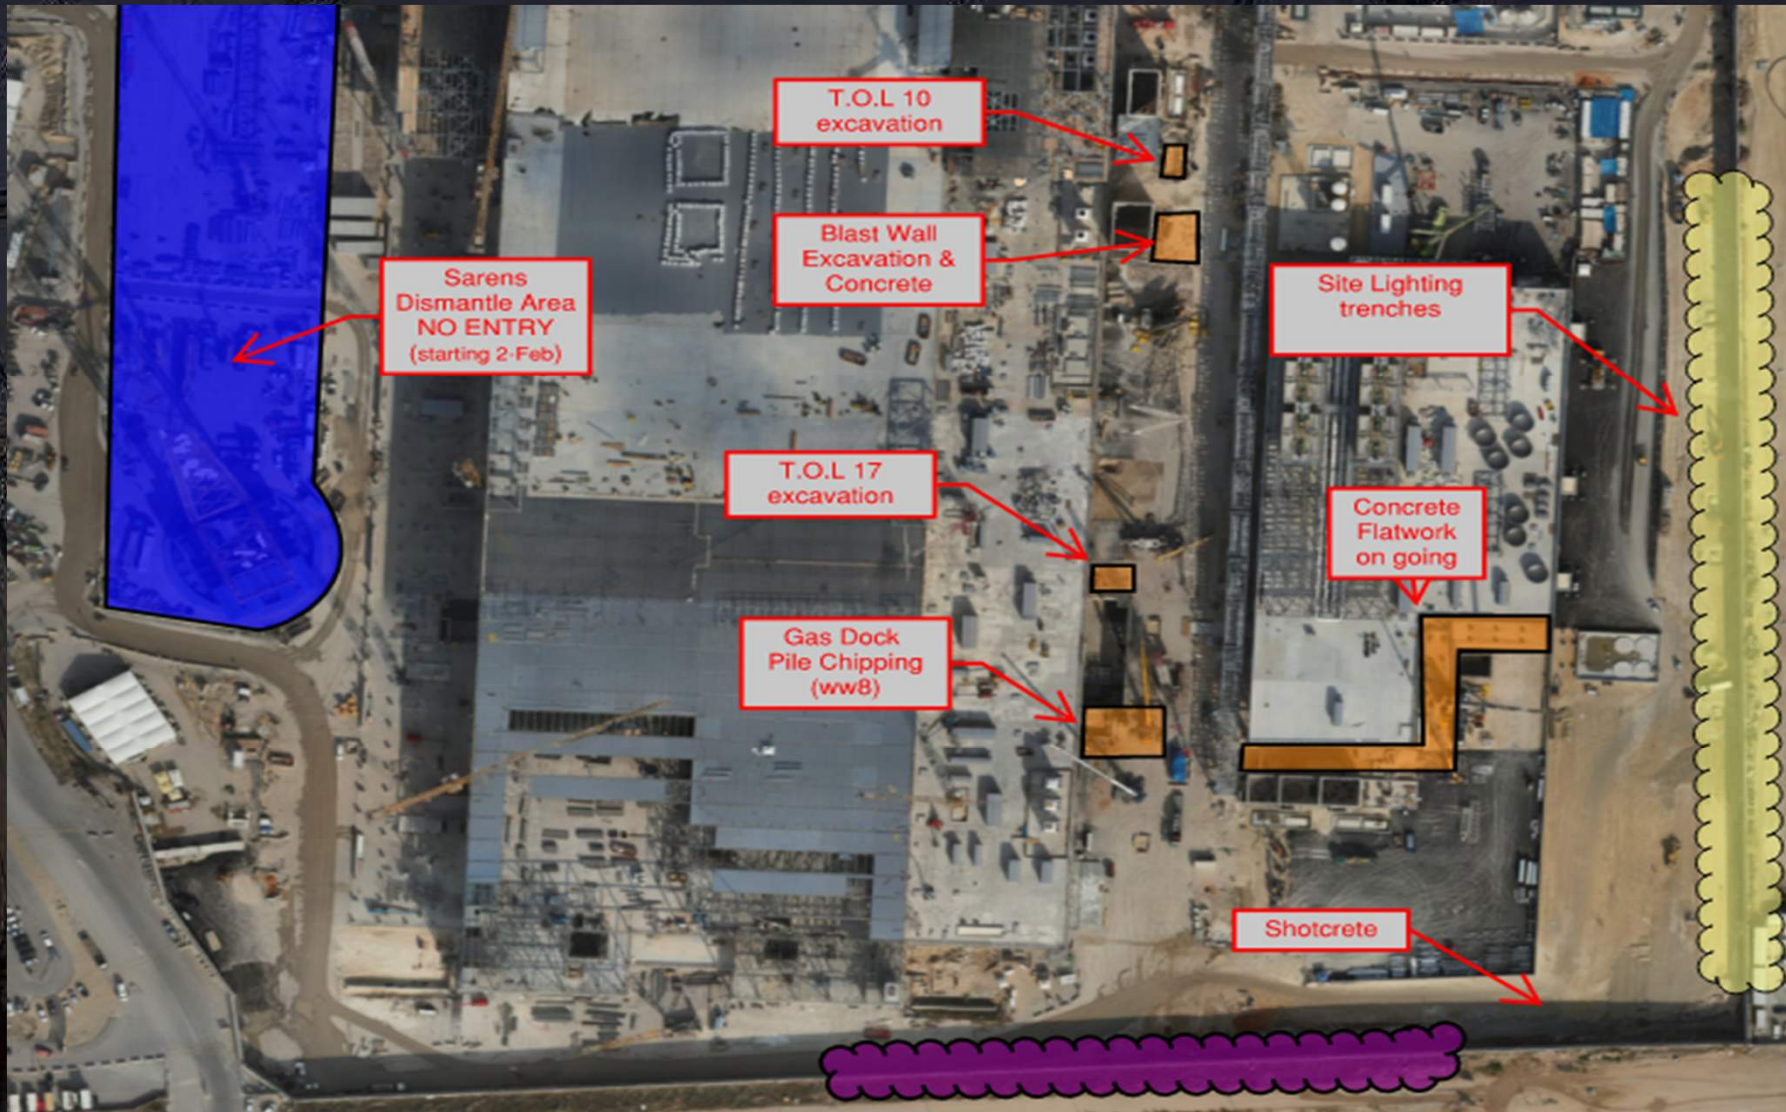



Housekeeping

A reminder to ensure the work areas are tidied up before leaving for the weekend. Additionally, please make sure that all equipment on-site is locked and secured. A storm with strong winds is expected over the weekend, so ensure that all wheels and equipment are stable, and will not move, damage, or collide with other equipment or objects during the storm.

Also, don't forget to empty any full trash bins in the work area before leaving. Please make sure all bins are cleared. If anyone needs assistance, feel free to reach out to HCC.



Extreme Cold

The weather next week is expected to be unusually cold. Workers should be prepared to come with warm clothing for work.

24/02 | שני

4^{UV}_{MAX}  0°-2°

23/02 | ראשון

3^{UV}_{MAX}  1°-6°

HCC/EHS Weekend Work- 21.02.2025

White Board Meeting in Beavers at 06:30

Superintendents

Shelby Standefer - 052-3440752

Soly Nir - 052-3126049

Asher Amar - 052-8801316

CSA CM

Nick Dailey - 052-3308928

Nissim A

Leonid Khomich - 053-2722138

Andy Jollands - 052-9659290

Hillel Mashiah - 052-6175084

Kenny C

David S

MEP

Cx

Cranes

Safety

- Safety Foreman -Waseem Alhozil- 052-358-4978 Waseem-Alhozil@Hoffmancorp.com
- Safety Assistant- Hudifa Alshieck- 054-9408858 Hudifa-Elscheich@Hoffmancorp.com
- Safety Professional- Nassim Yones- 052-2208434 Nassim-Yones@Hoffmancorp.com

Subcontractor Weekend Work- 21.02.2025

FAB

Utility level/ SUT

Lesico

Ehs Michel 0526060223

Foreman Manoj 0522450258

Chemo

Ehs lilach 0547886704

Foreman sergey 0544659688

Combe waste

Foreman: Denis 0525238504

Ehs: Michael 0525506596

Afcon electrical

Ehs Steven 0559129333

Foreman Perdit 0552742935

Subfab

- Pach Taas
 - Wall Penetration
 - Valiry: 0528762468
- Afcon E
 - E,W MARSES
 - Avi Eli: 0526008487
- Lesico
 - SF East Mechanical Shaft
 - Elia 0543369795

Clean Room

- Talad – 30 guys CR 3E- lids cutting, 1W- Ceiling install, Int -3E grating (EHS Marcelo 0523540242, Super Elad 0546654473)
- Chemo – 35 GUYS INT -TNTNE/W Supports, 5RA Racks, 3W Skids (EHS lotem 0544477112, Supervisor Winai – 0528090588)
- Protocol 2 guys (Roni 0542496363, Eden 0585335445)
- Talent solution 14 guys CR 2E 1E/W maintenance cleaning (EHS Yosiel 0508777611, Super Super Musat 0505135022)
- Sig – 19 GUYS MOD2- 17 Line, MOD1 2E-2W scaffold (EHS Beni 0506232032, Super Shmulik 0549205966)
- Rolling Plains – 23 guys 7W, CA to CG17 MOD2- Grid 17 4DA (Super Codrin 0546594273, EHS Ovidiu 0546993648)
- Afcon – 10 guys CR – Cable tags, INT Cable puling , cable tags (EHS Lokanath – 0559652398, Supervisor Pradeep - 0552742935)

Subcontractor Weekend Work- 21.02.2025

PSSS

- Pach Taas – Module bolting PSSS Roof, Lift 2 3-5P
- Foreman – Vadim – 053-5552472
- Safety – Offek – 050-2161429
- Afcon Electrical – Cable Tray and Cable Pulling UPW/BCD UL and 2-3P Roof & Lift 2
- Foreman – Charles – 055-2740190
- Safety – Stevan – 055-9129333
- Chemo A. – PSSS Roof and Lift 2 2-5P and PCW Room Insulation
- Foreman – Maor – 050-955-9071
- Safety – Rotem – 054-447-7112
- Combe Waste – 2P Waste Piping at GL4/SSS Building
- Foreman – Chaim – 054-5210133
- Safety – Marzuke – 054-447-7112
- Lesico – H2 Vent/SUT East Area Way Rack
- Foreman – Suju Pally – 052-7755967
- Safety – Tal Madar – 052-8229109
- Combe UPW – BCD/UPW Rooms
- Foreman – Boris – 054-8346412
- Safety – Shimon – 054-5348843
- SK Engineering – 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- SK Engineering – 3P roof/Lift 2 Piping
- Foreman – Marcela – 054-5210133
- Safety – Marzuke – 054-447-7112
- Carmel Bidud Duct – Spec Gas, BCD, and 2P Roof
- Foreman –
- Safety –
- SNJ –
- Foreman –
- Safety –

WJG

Afcon:

Team leader – Montu: 0559116973

Safety – Steven: 0559129333

Pach Taas:

Team leader – Valery: 0528762468

Safety – Ofek: 0507838486

Chemo:

Team leader – Maor: 0509889071

Safety – Rotem: 0544477112

Subcontractor Weekend Work- 21.02.2025

CUB

Meptagon CUB 1:

Sergey - 0537981592

Itzik - 0587441140

Chemo Aharon CUB 1:

Dudu - 050-9808846

Leonid - 0548883878

HSAI CUBs:

Sergey - 0552728807

Haim - 054-8038554

SKE CUB 2:

Mario - 0548991051

Marzuk - 0548830263

D&P CUBs:

Constantino - 0545501602

David - 0548894447

Trestle

Site

Daily Coordination Meeting



14:00 Sign In
