Daily Coordination Meeting

HOFFMAN CONSTRUCTION COMPANY

14:00 Sign In

Daily Coordination Meeting

General Topics:

- Change in weather - don't touch pumps/call JS, stay on walkpaths
- PTP area assessment, over all awareness, know your surroundings, all systems are live

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

UTILITY LEVEL TRUSS

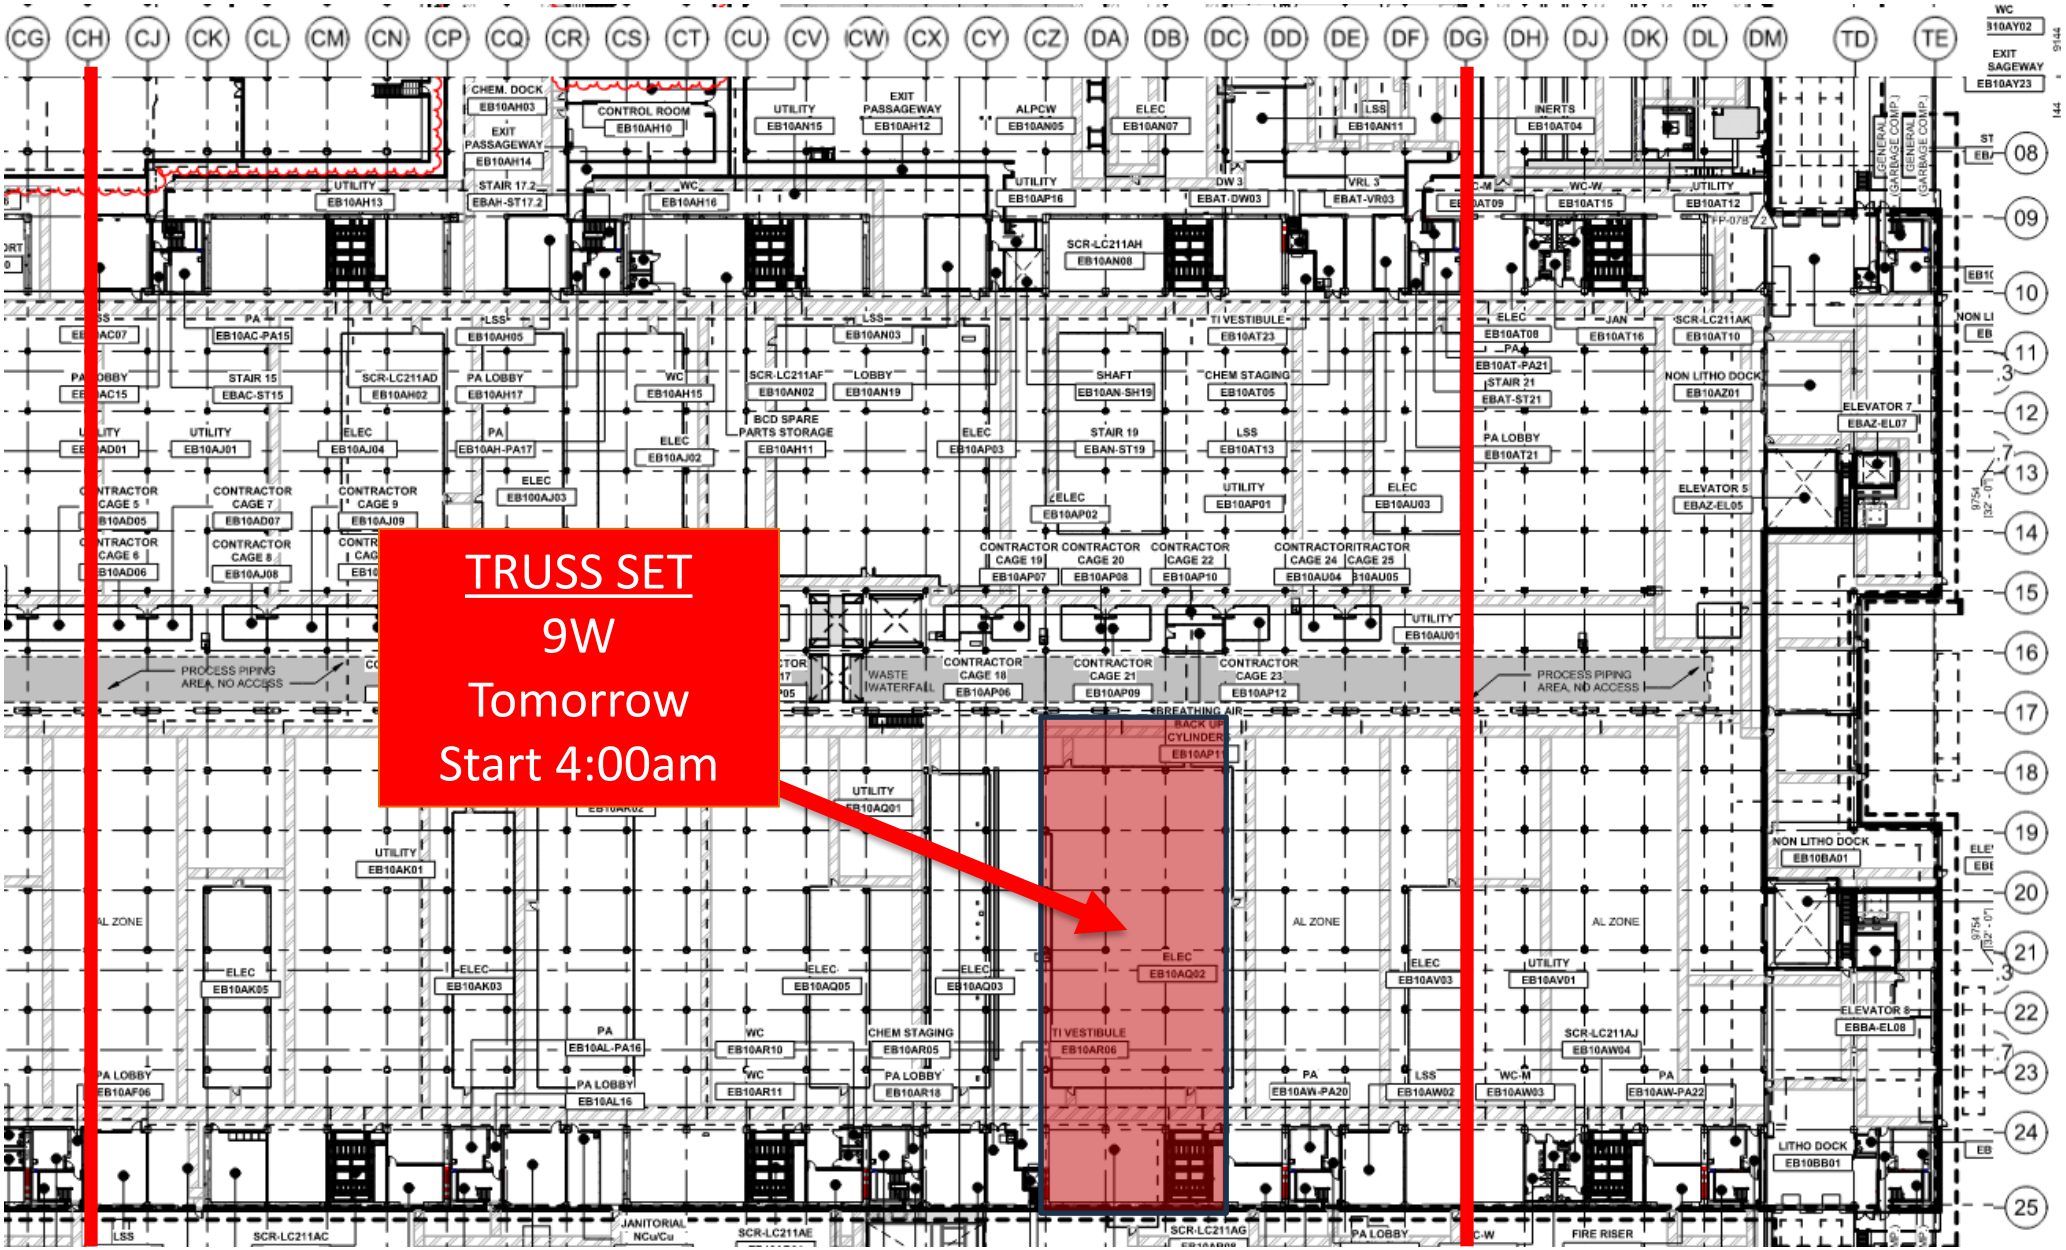

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

UTILITY LEVEL MOD1

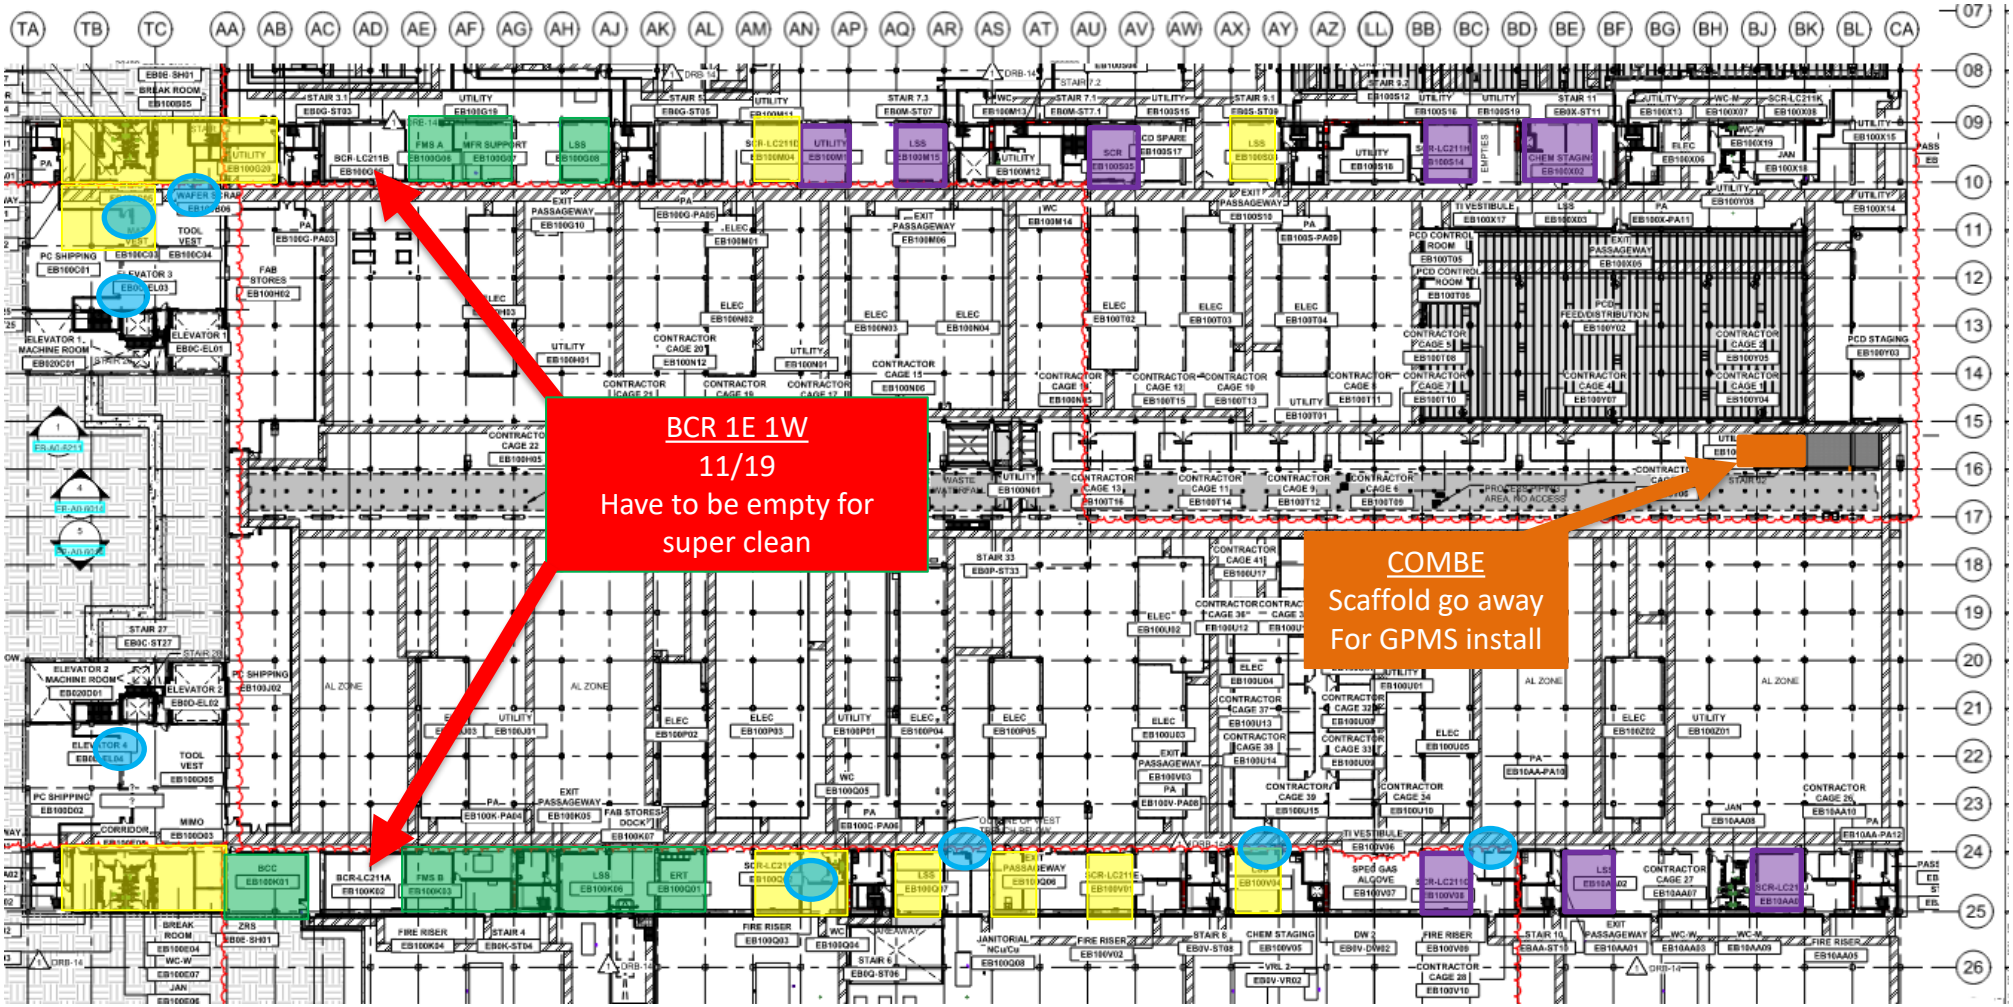

BELFOR
Mold remediation

ELRAM
Drywall install

MEP+Elctrical
Ready for re-install

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

UTILITY LEVEL MOD2

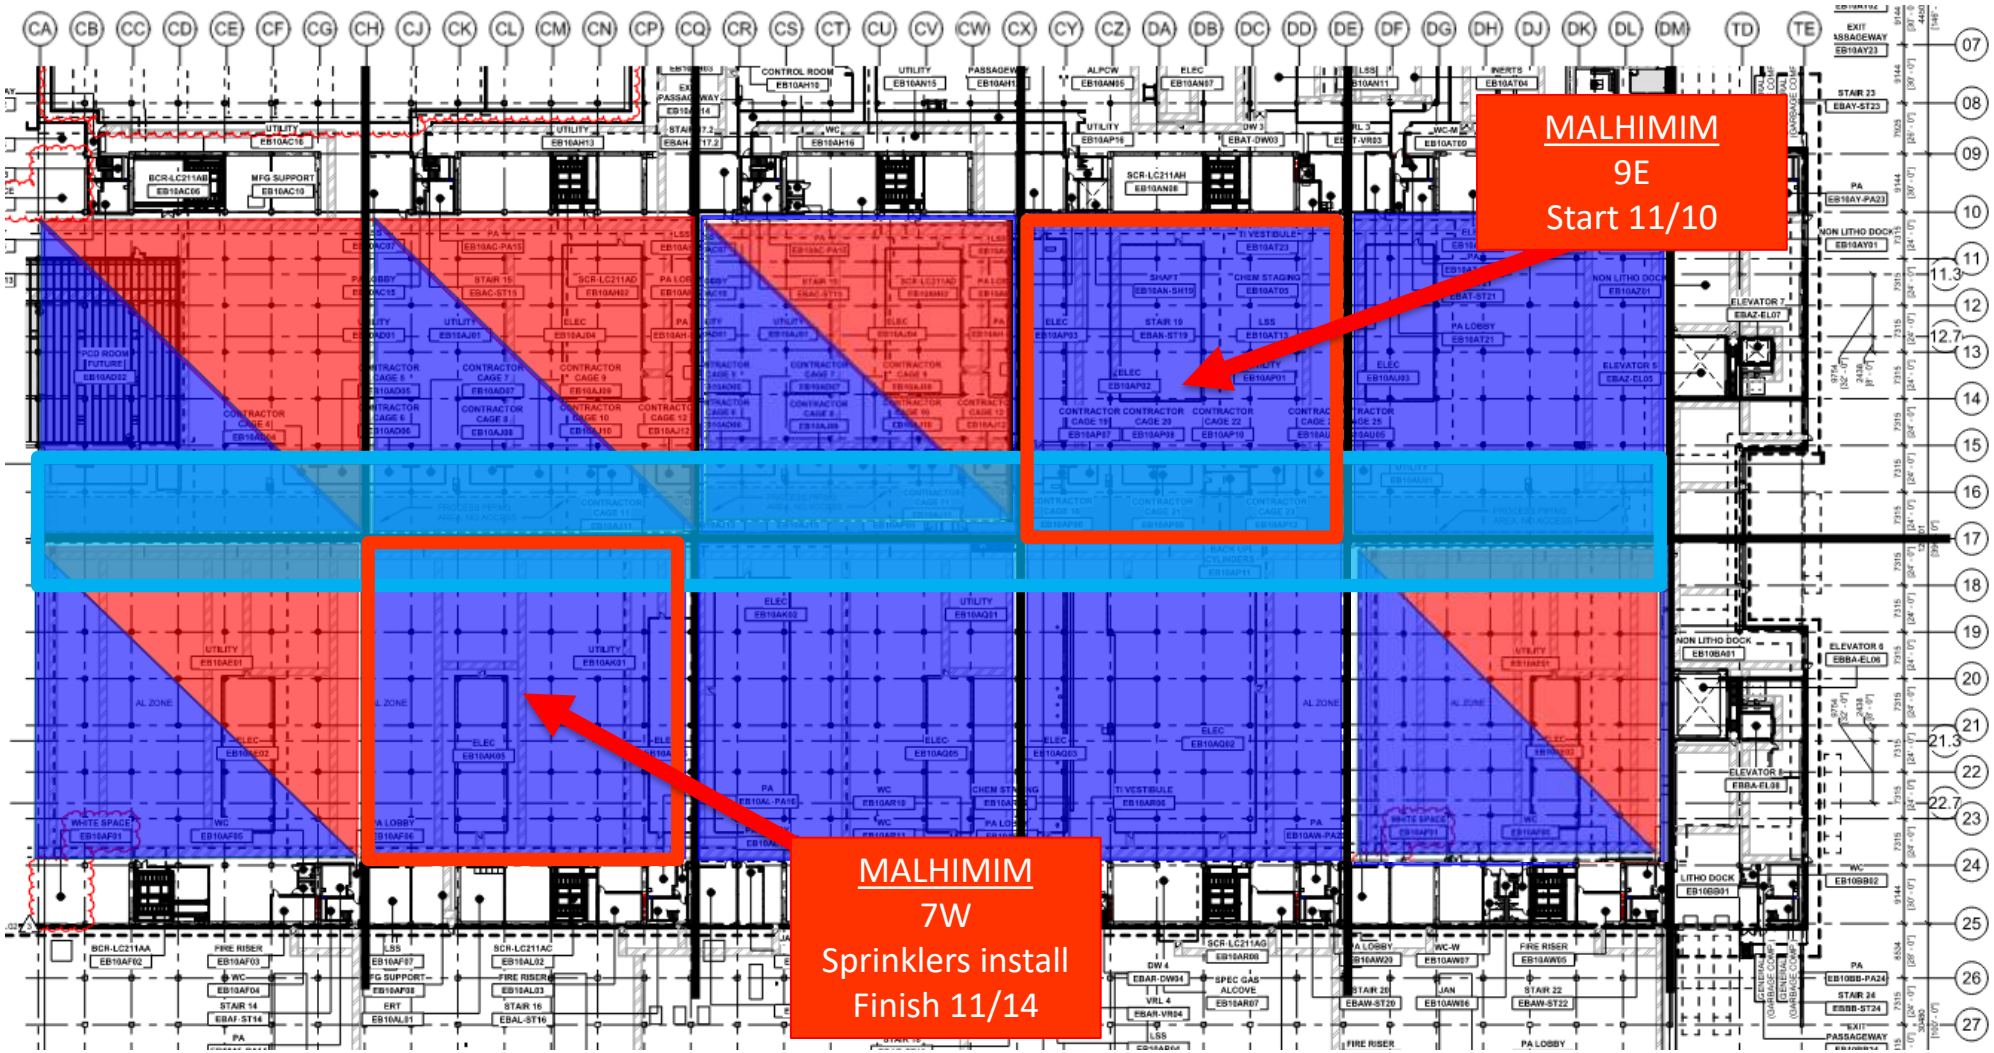

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

SUT 38.1 LEVEL

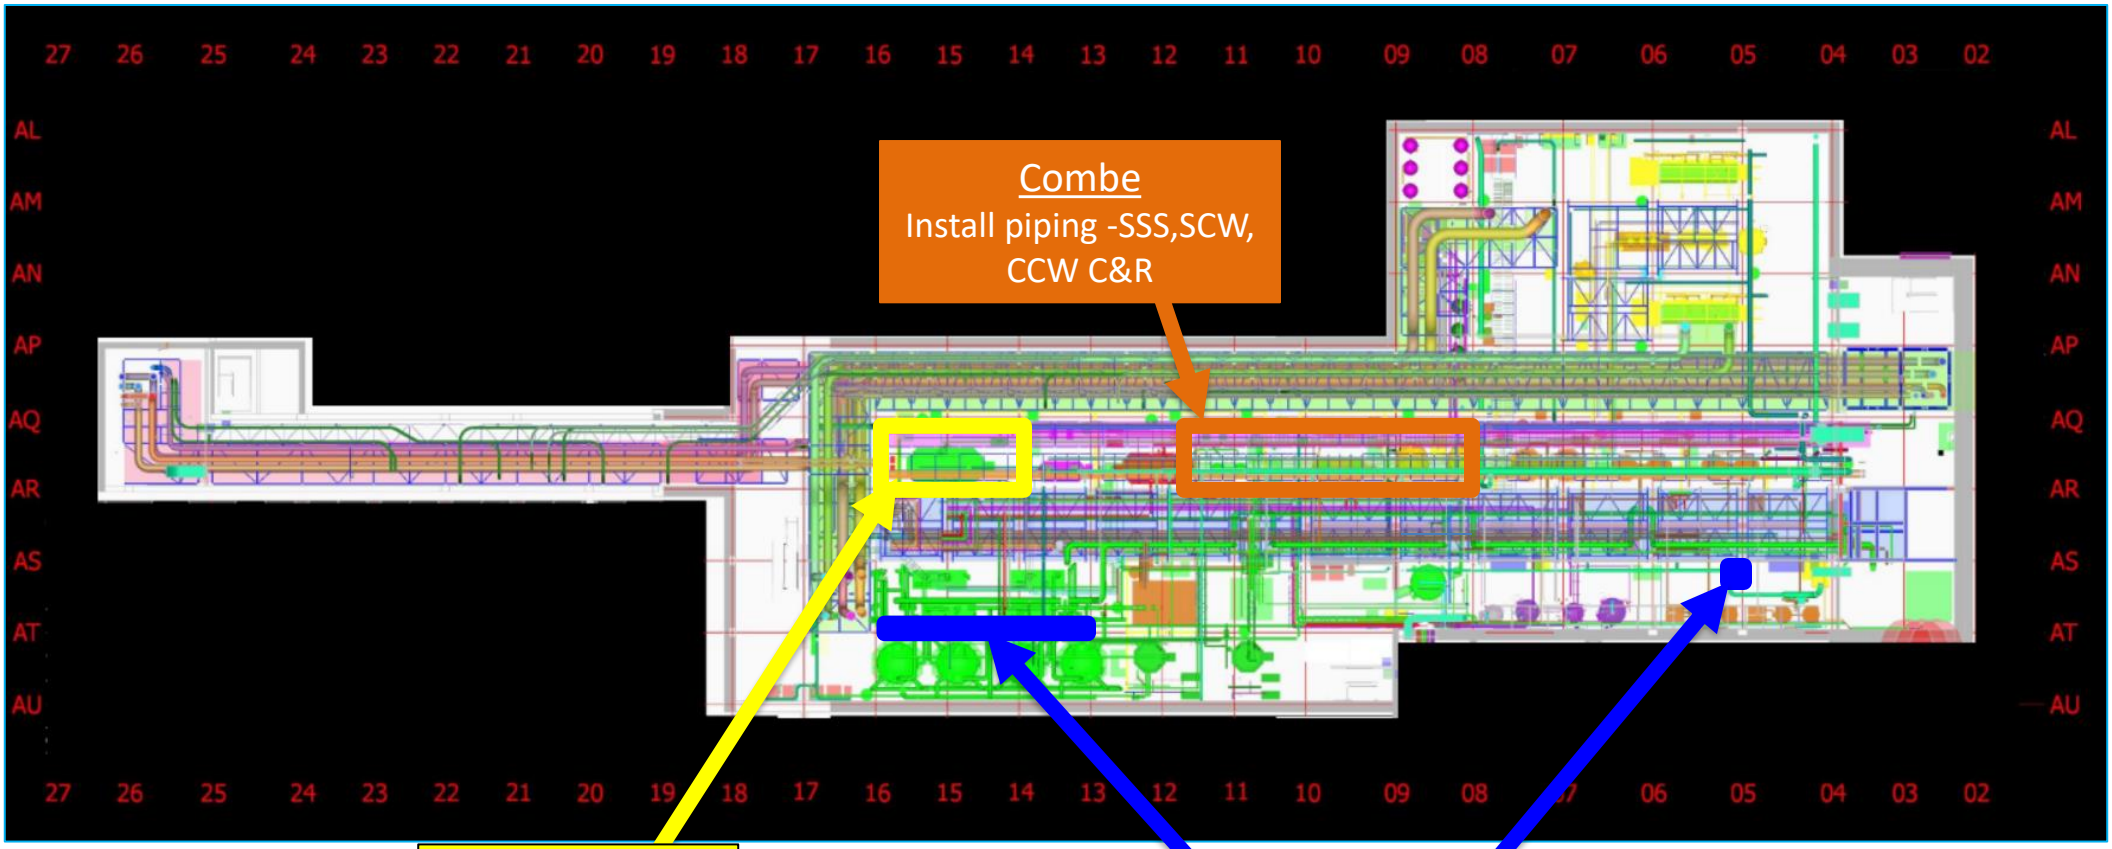

Combe
Install piping -SSS,SCW, CCW C&R

HFW lift station
2. CRC.
3. Pipe support's.

Concrete HSAI
4 AWN strings pads
1 PMP pad solvent

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

SUT 38.2 LEVEL

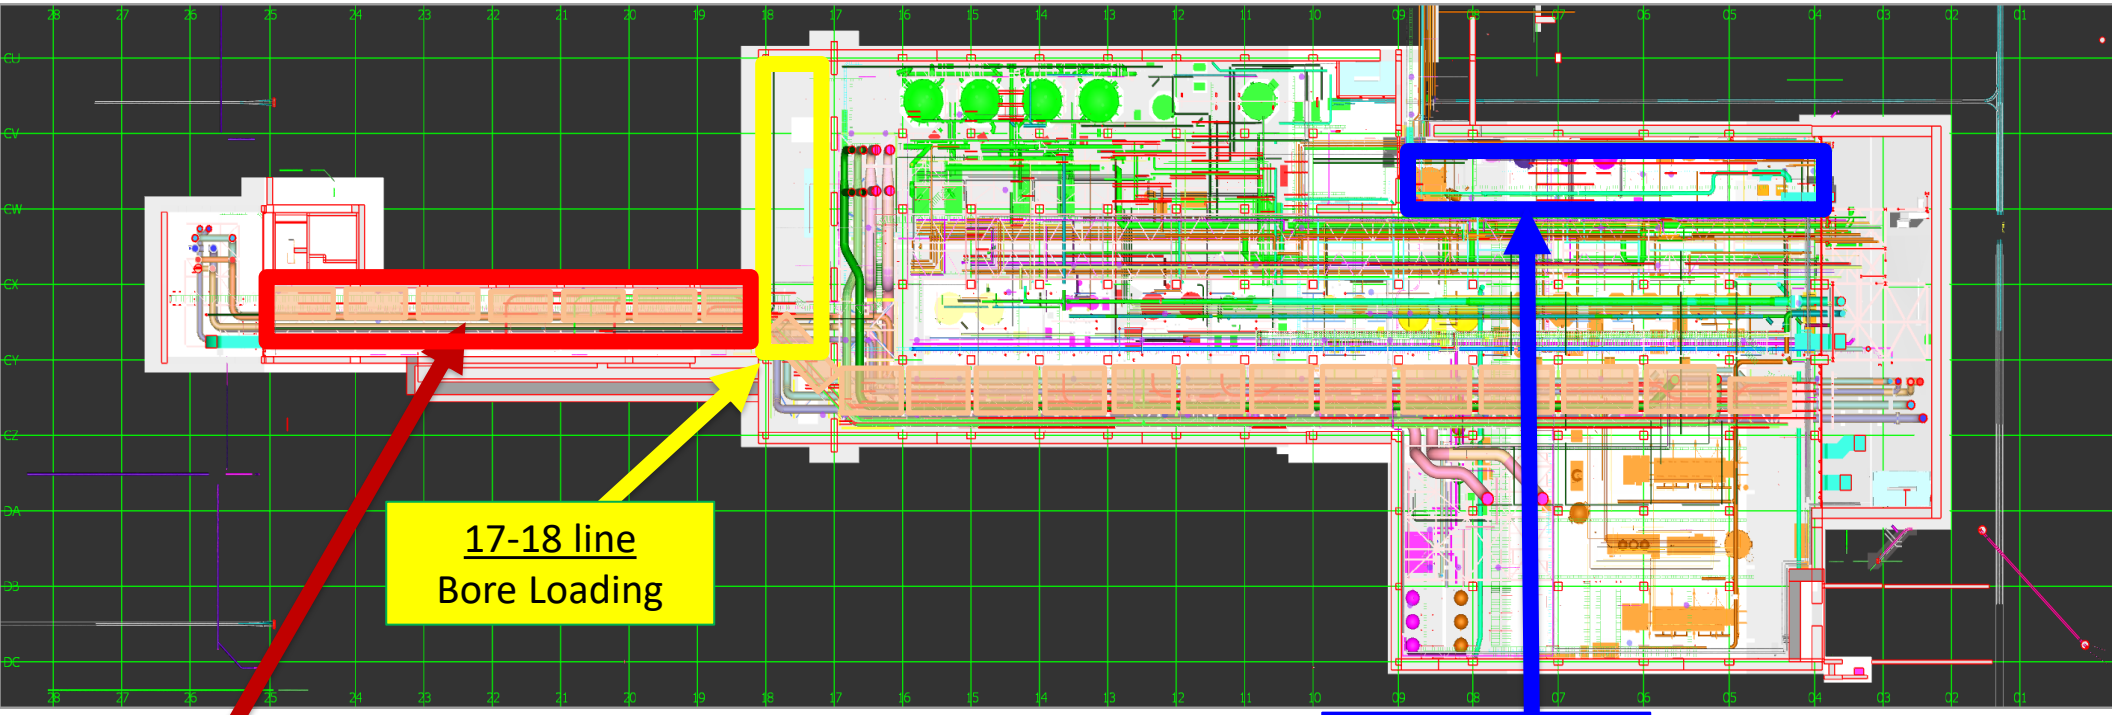

17-18 line
Bore Loading

Vesda
Need to install
on the West.

Rack 4b
First delivery
18/11

SUBFAB BUILDOUT MOD 1

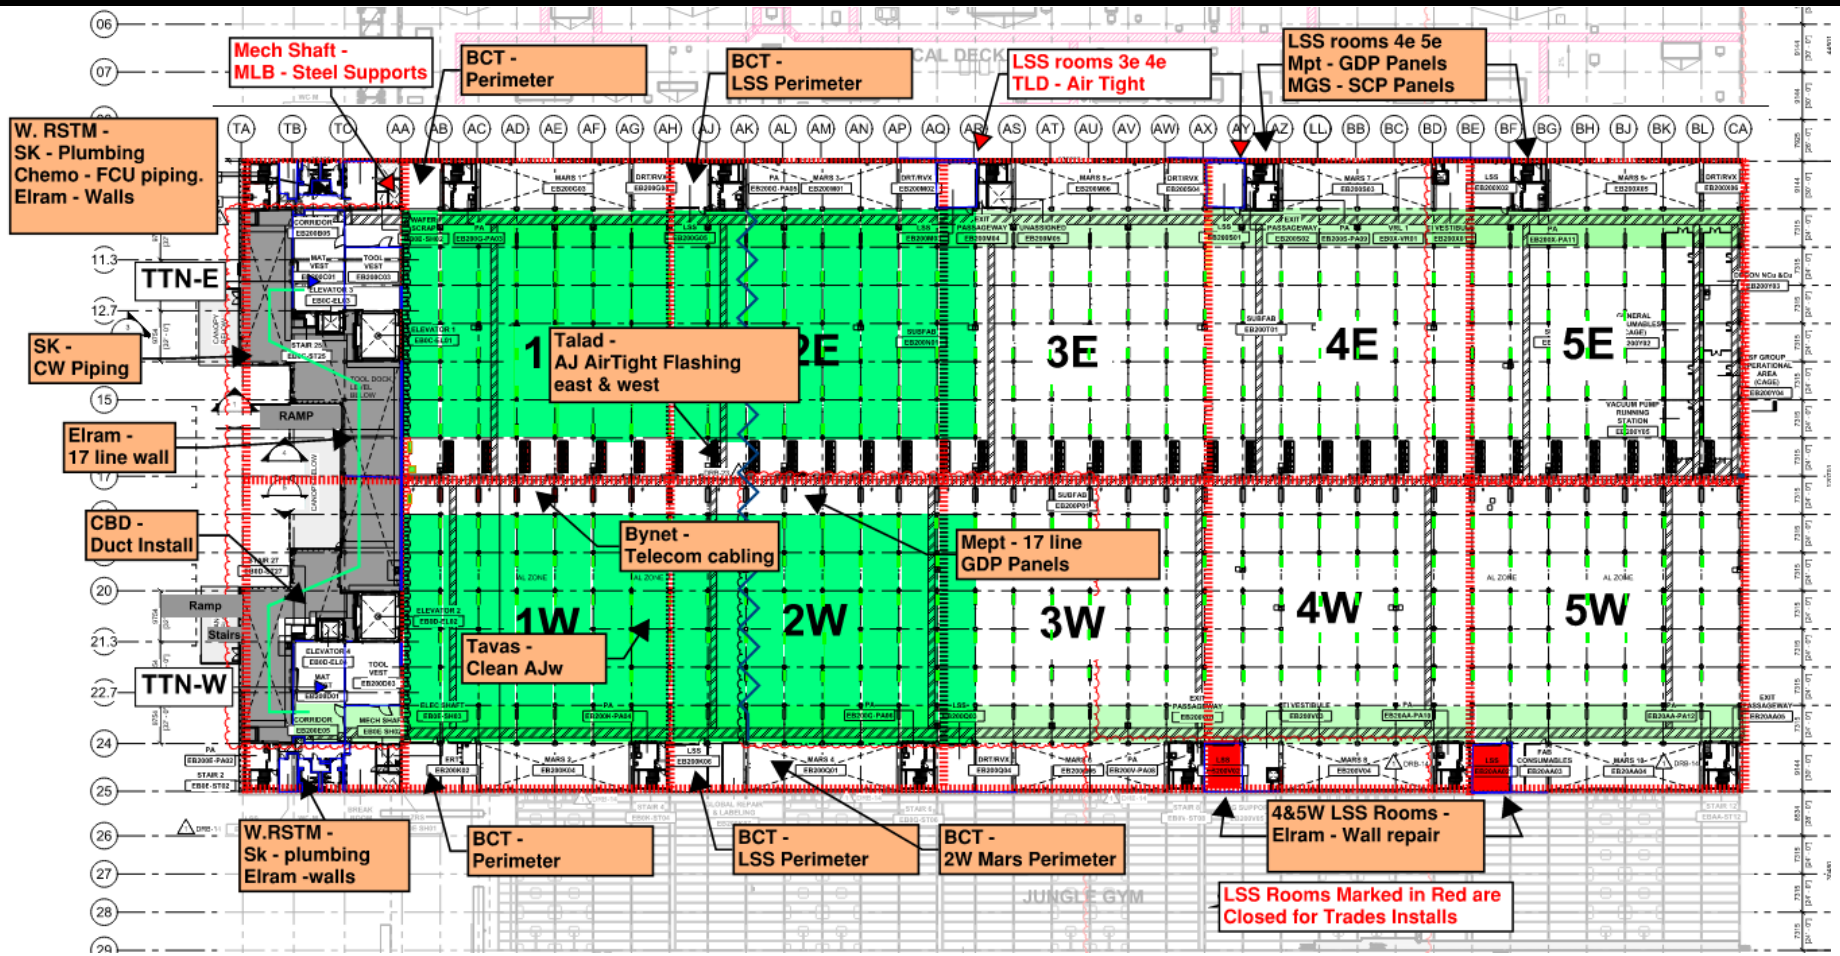

SUBFAB CRC TOPCOAT

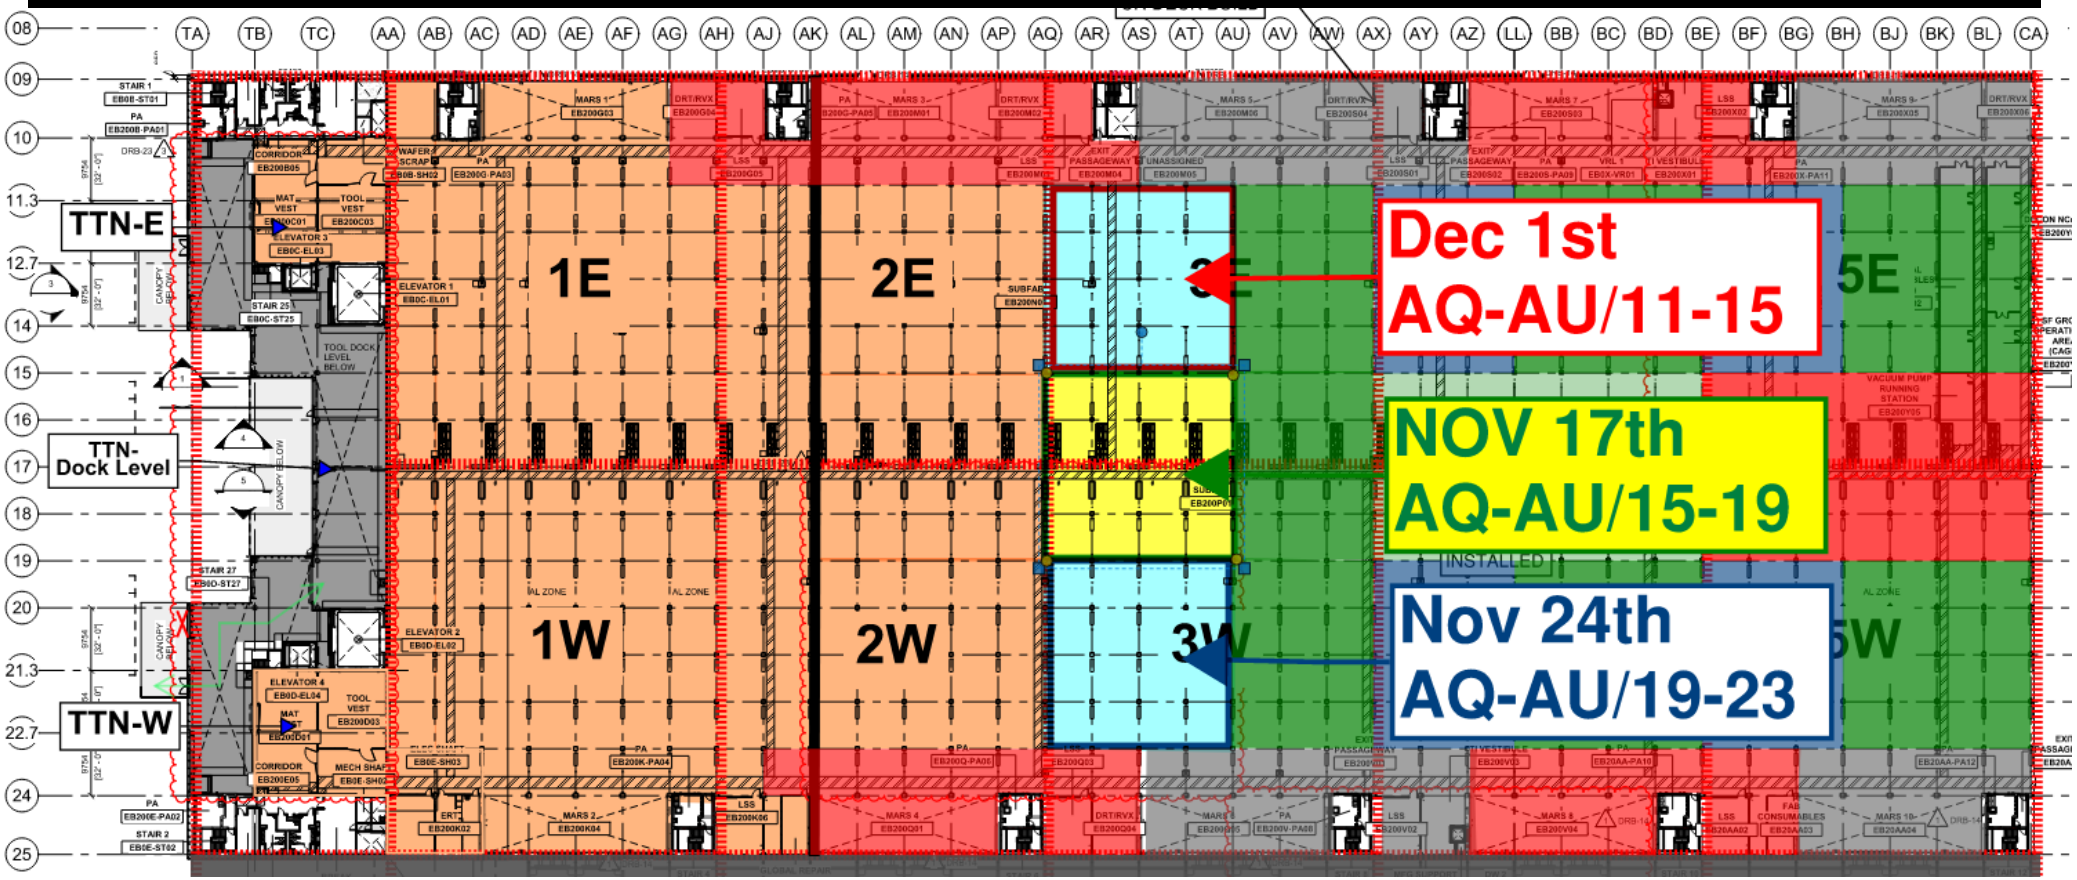

BCT Pressure Test Today

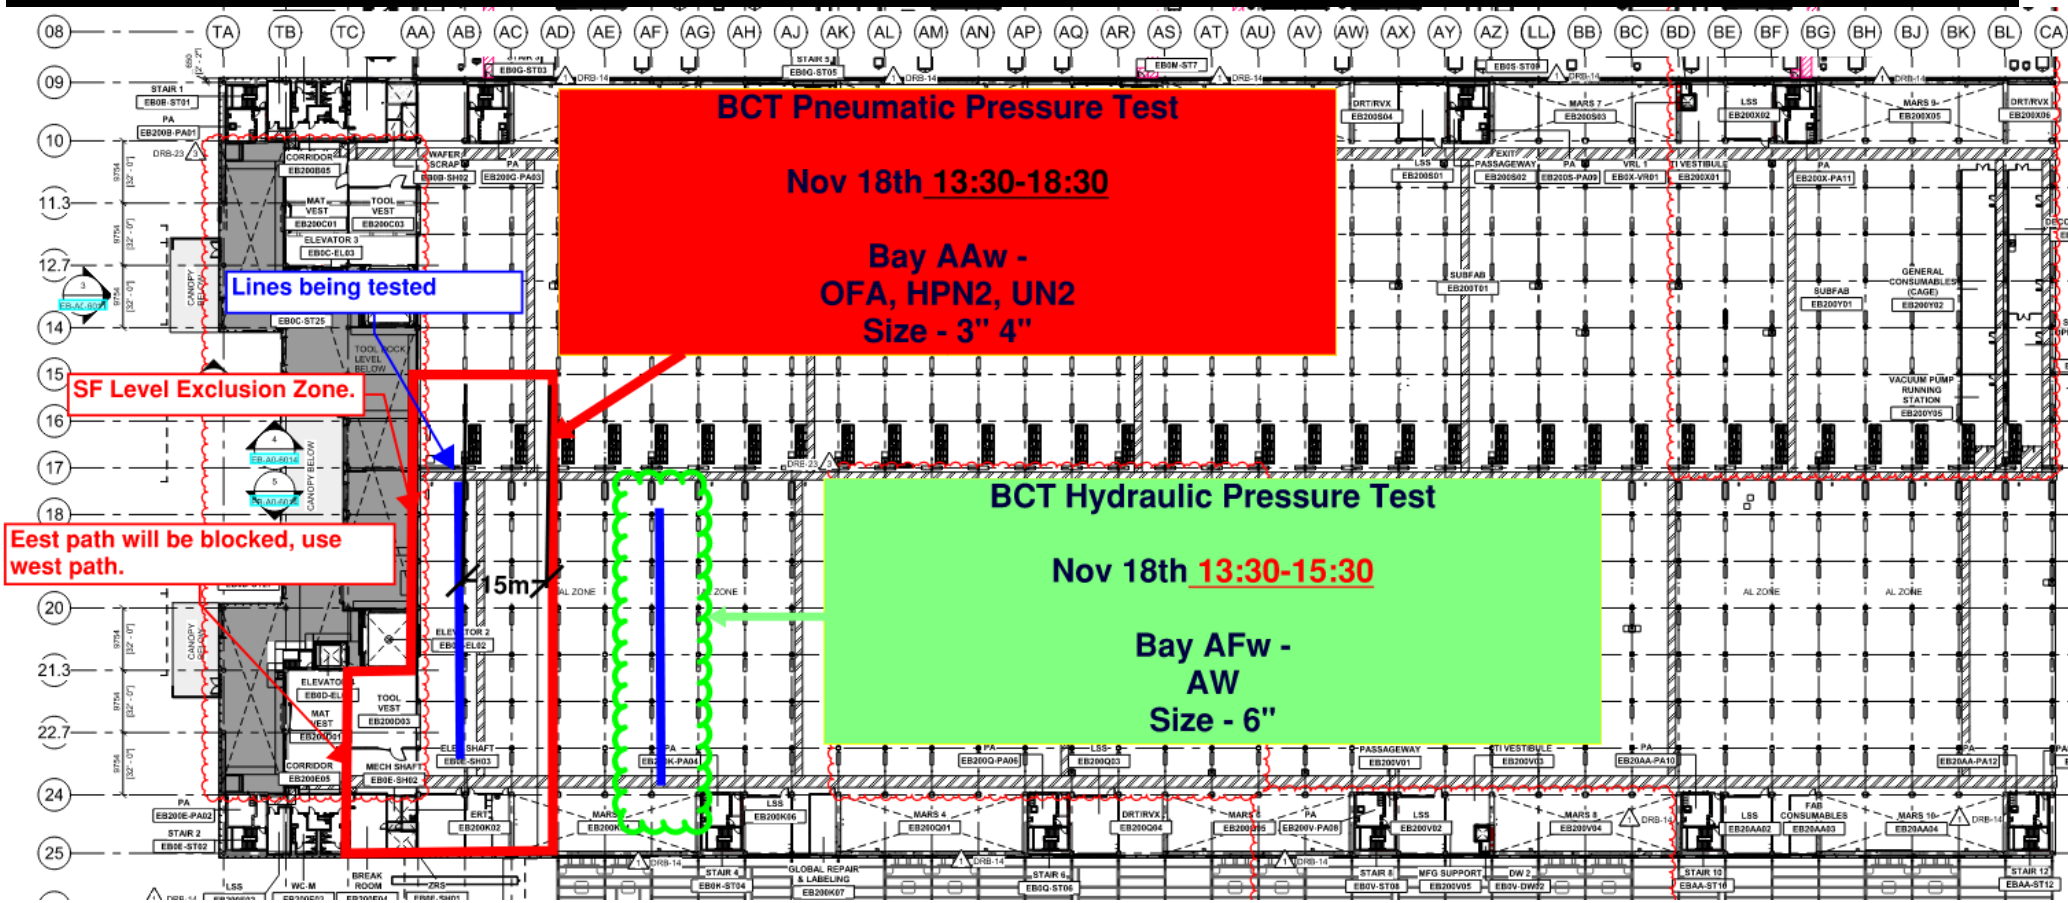

BCT Pressure Test Tomorrow

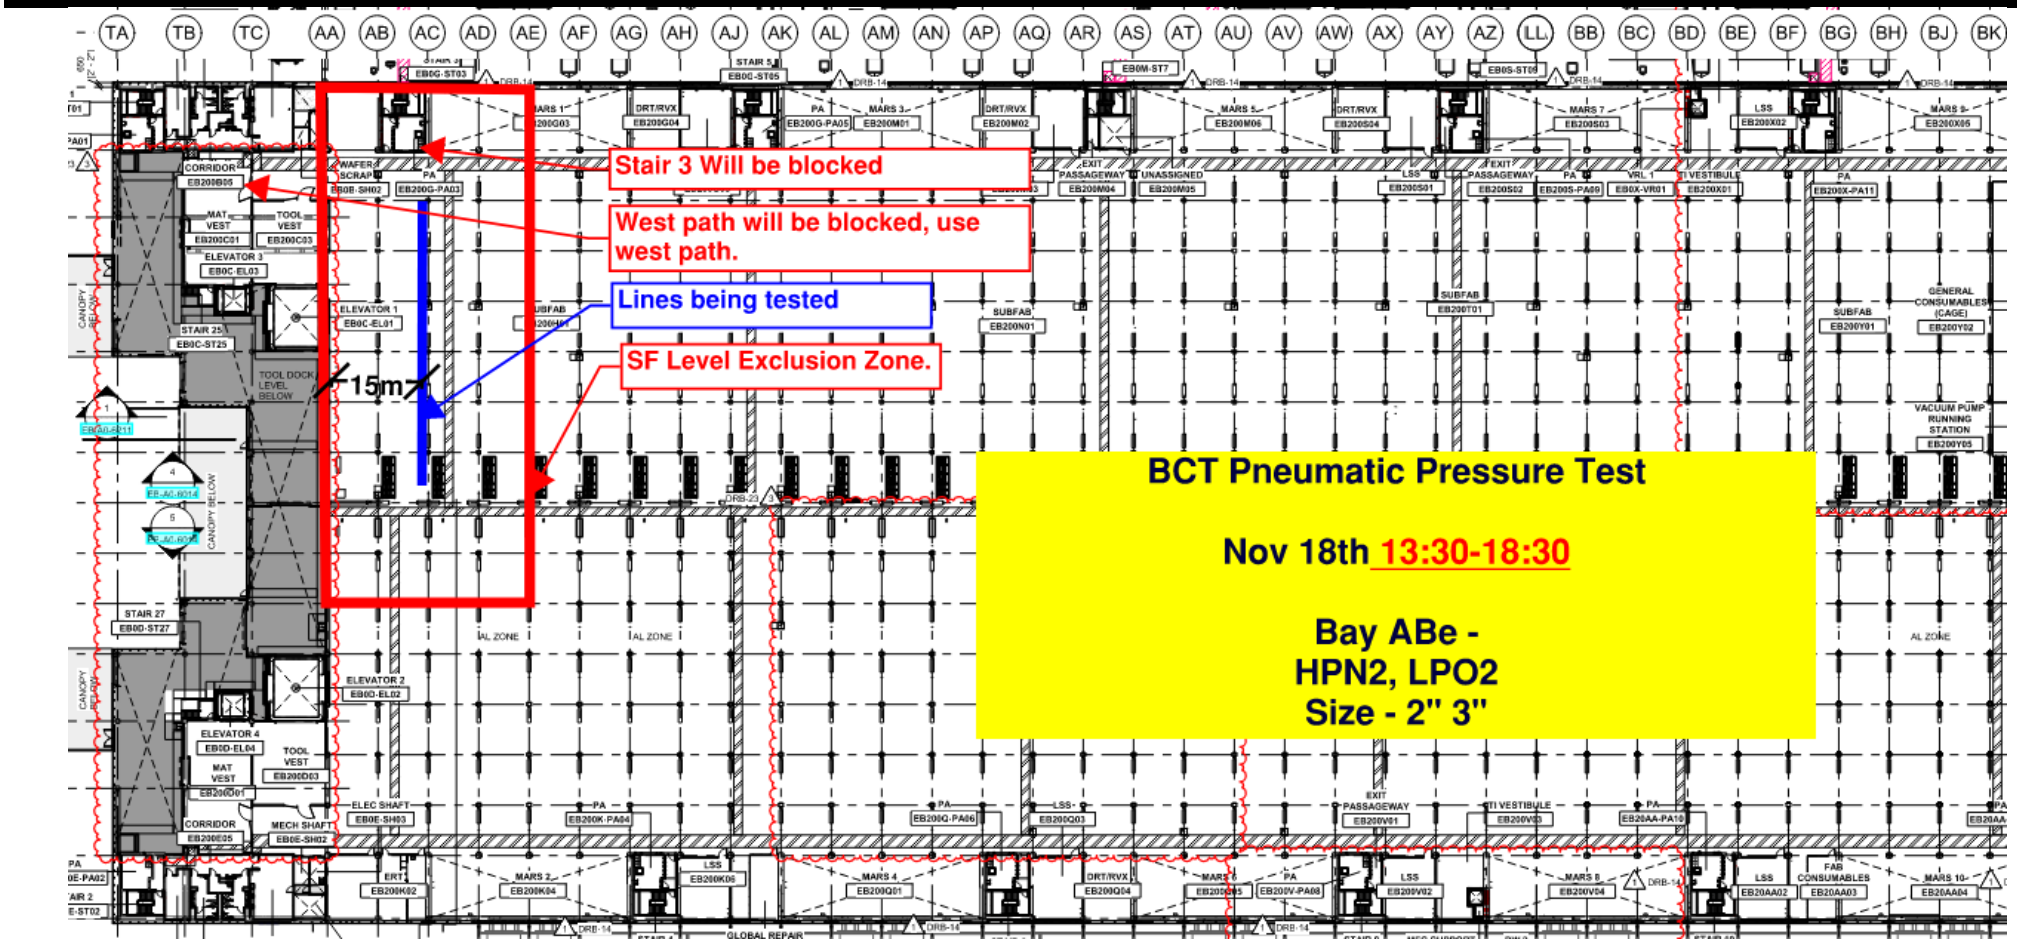

SUBFAB BUILDOUT MOD 2

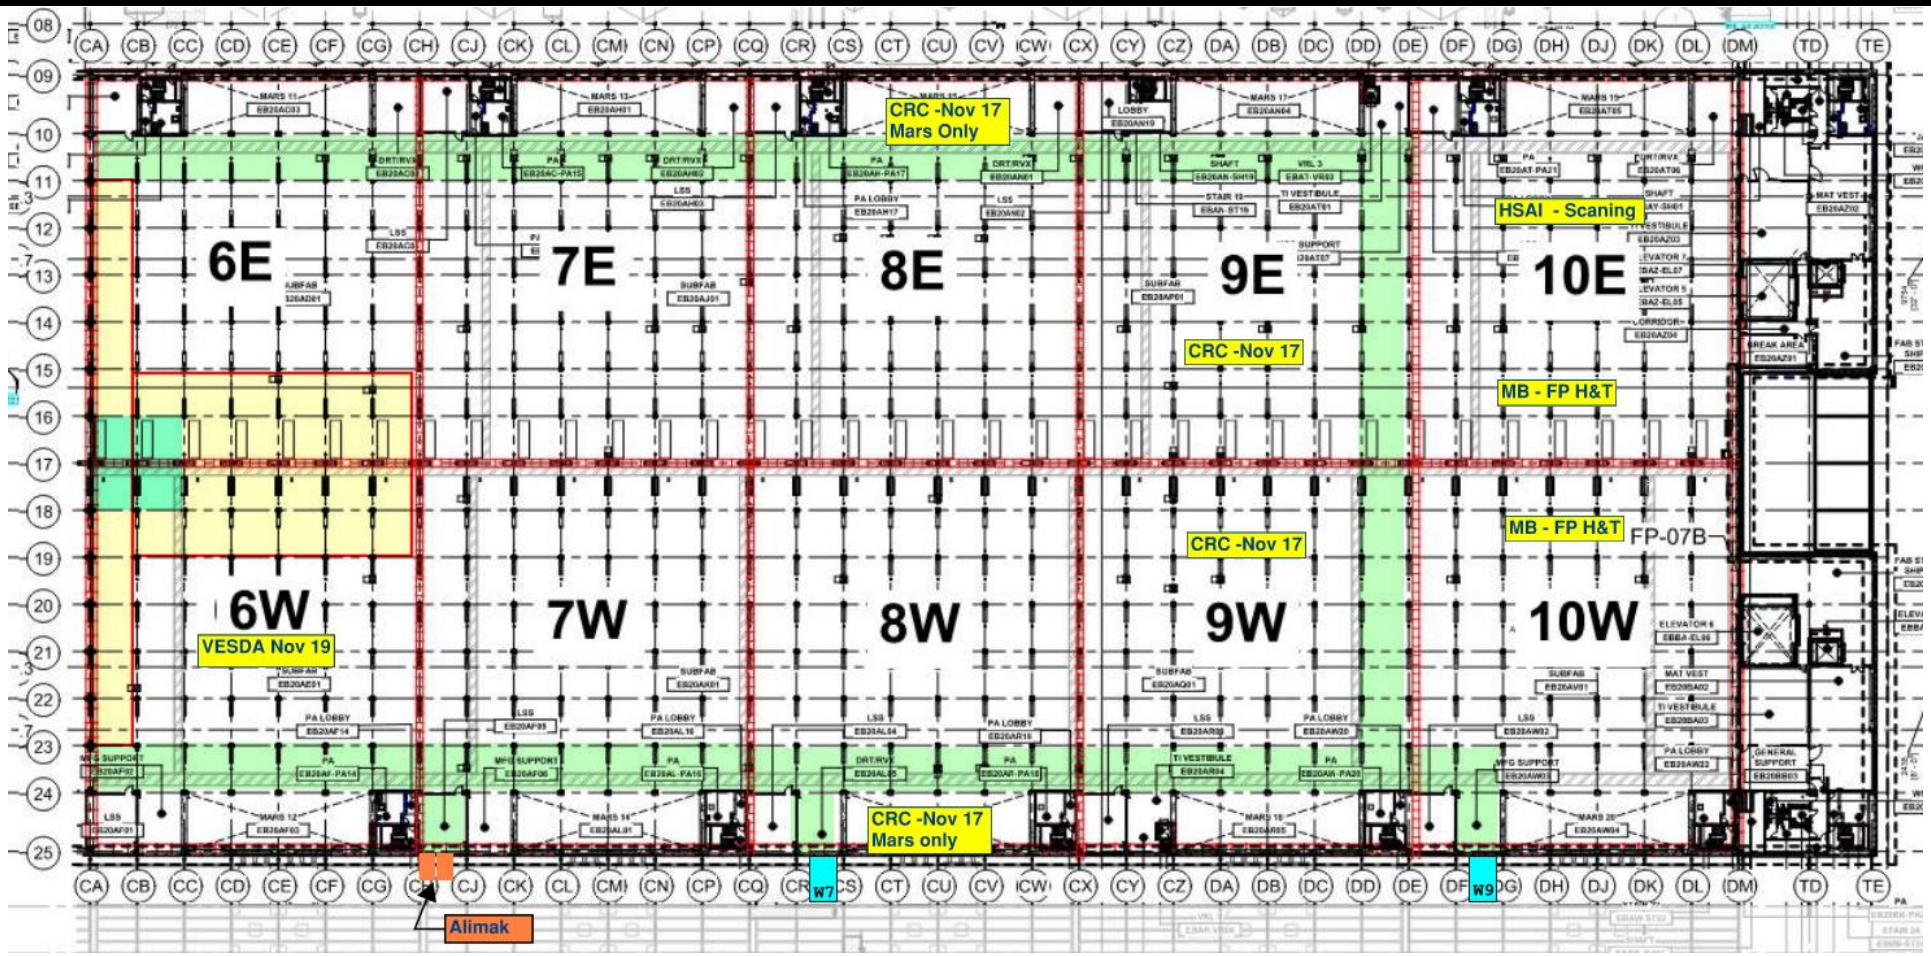

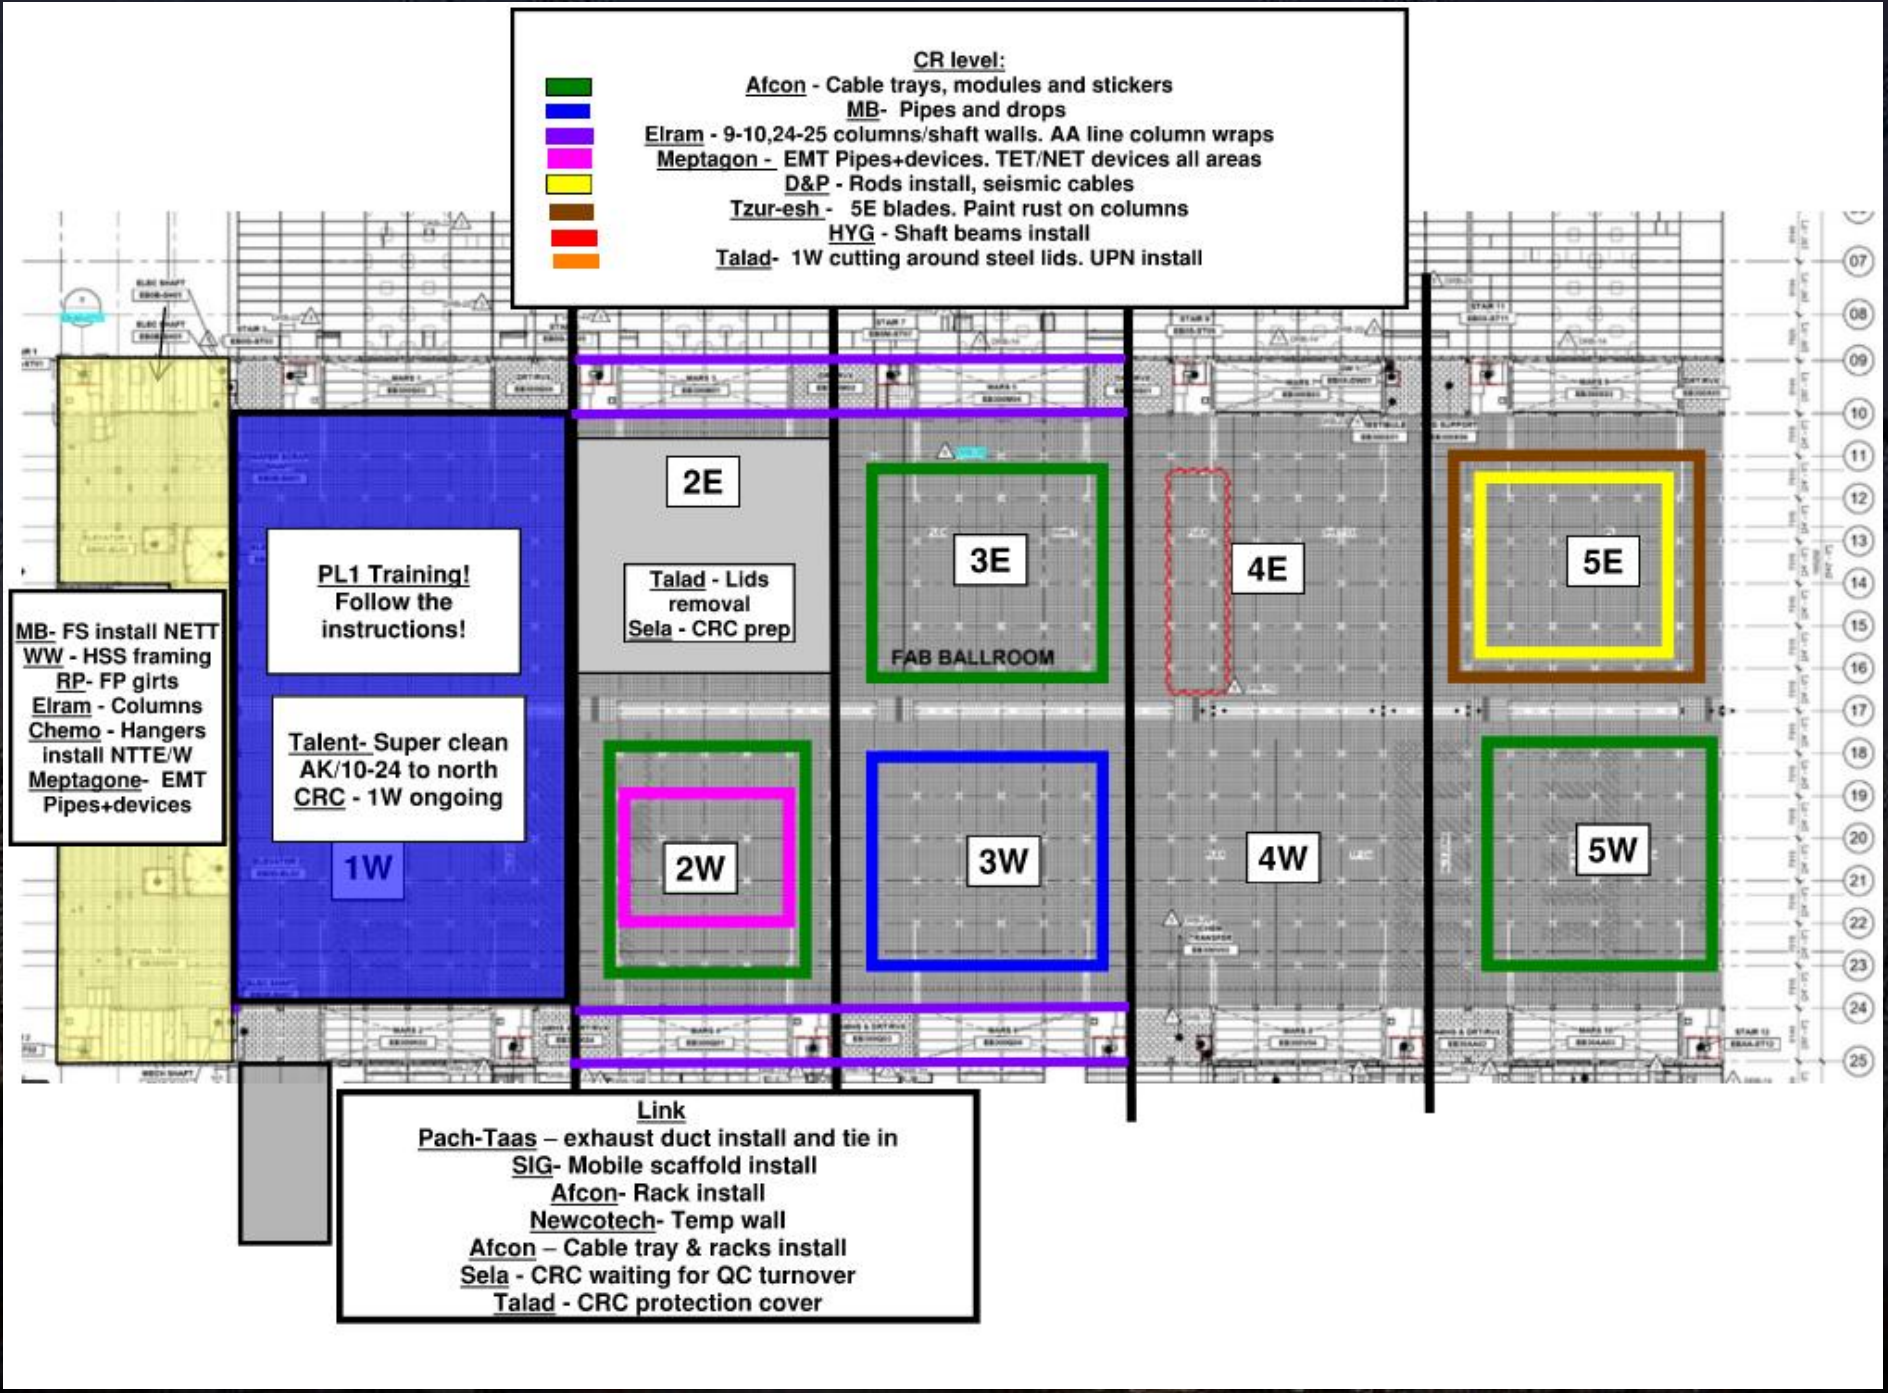
CR level:
Afcon - Cable trays, modules and stickers
MB- Pipes and drops
Elram - 9-10,24-25 columns/shaft walls. AA line column wraps
Meptagon - EMT Pipes+devices. TET/NET devices all areas
D&P - Rods install, seismic cables
Tzur-esh - 5E blades. Paint rust on columns
HYG - Shaft beams install
Talad- 1W cutting around steel lids. UPN install
MB- FS install NETT
WW - HSS framing
RP- FP girts
Elram - Columns
Chemo - Hangers install NTTE/W
Meptagone- EMT Pipes+devices
PL1 Training! Follow the instructions!
Talent- Super clean AK/10-24 to north
CRC - 1W ongoing
1W
2E
Talad - Lids removal
Sela - CRC prep
2W
3E
FAB BALLROOM
3W
4E
4W
5E
5W
Link
Pach-Taas – exhaust duct install and tie in
SIG- Mobile scaffold install
Afcon- Rack install
Newcotech- Temp wall
Afcon – Cable tray & racks install
Sela - CRC waiting for QC turnover
Talad - CRC protection cover

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

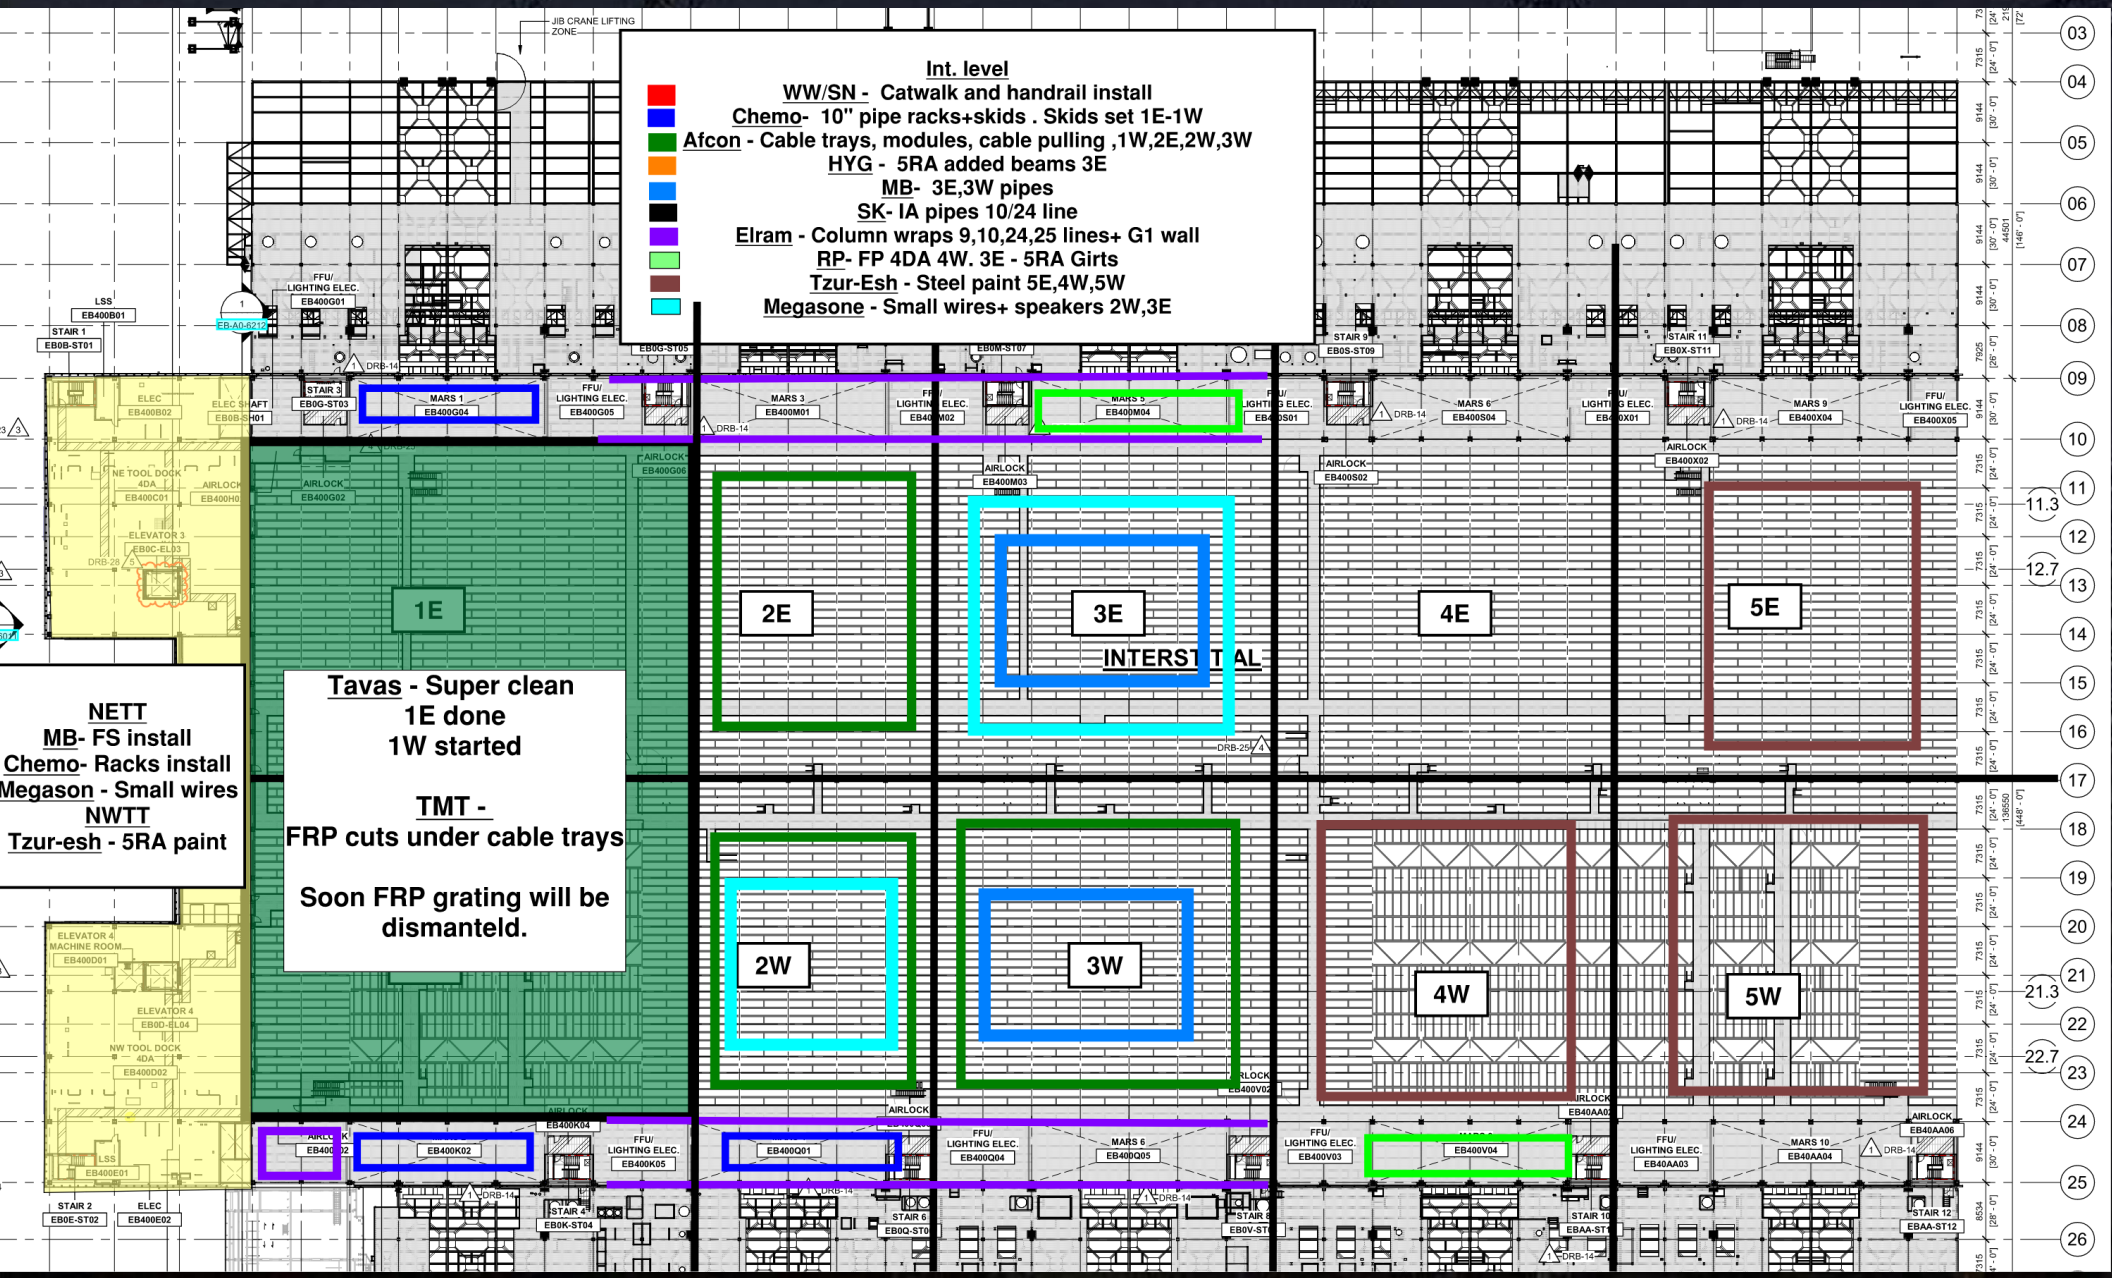

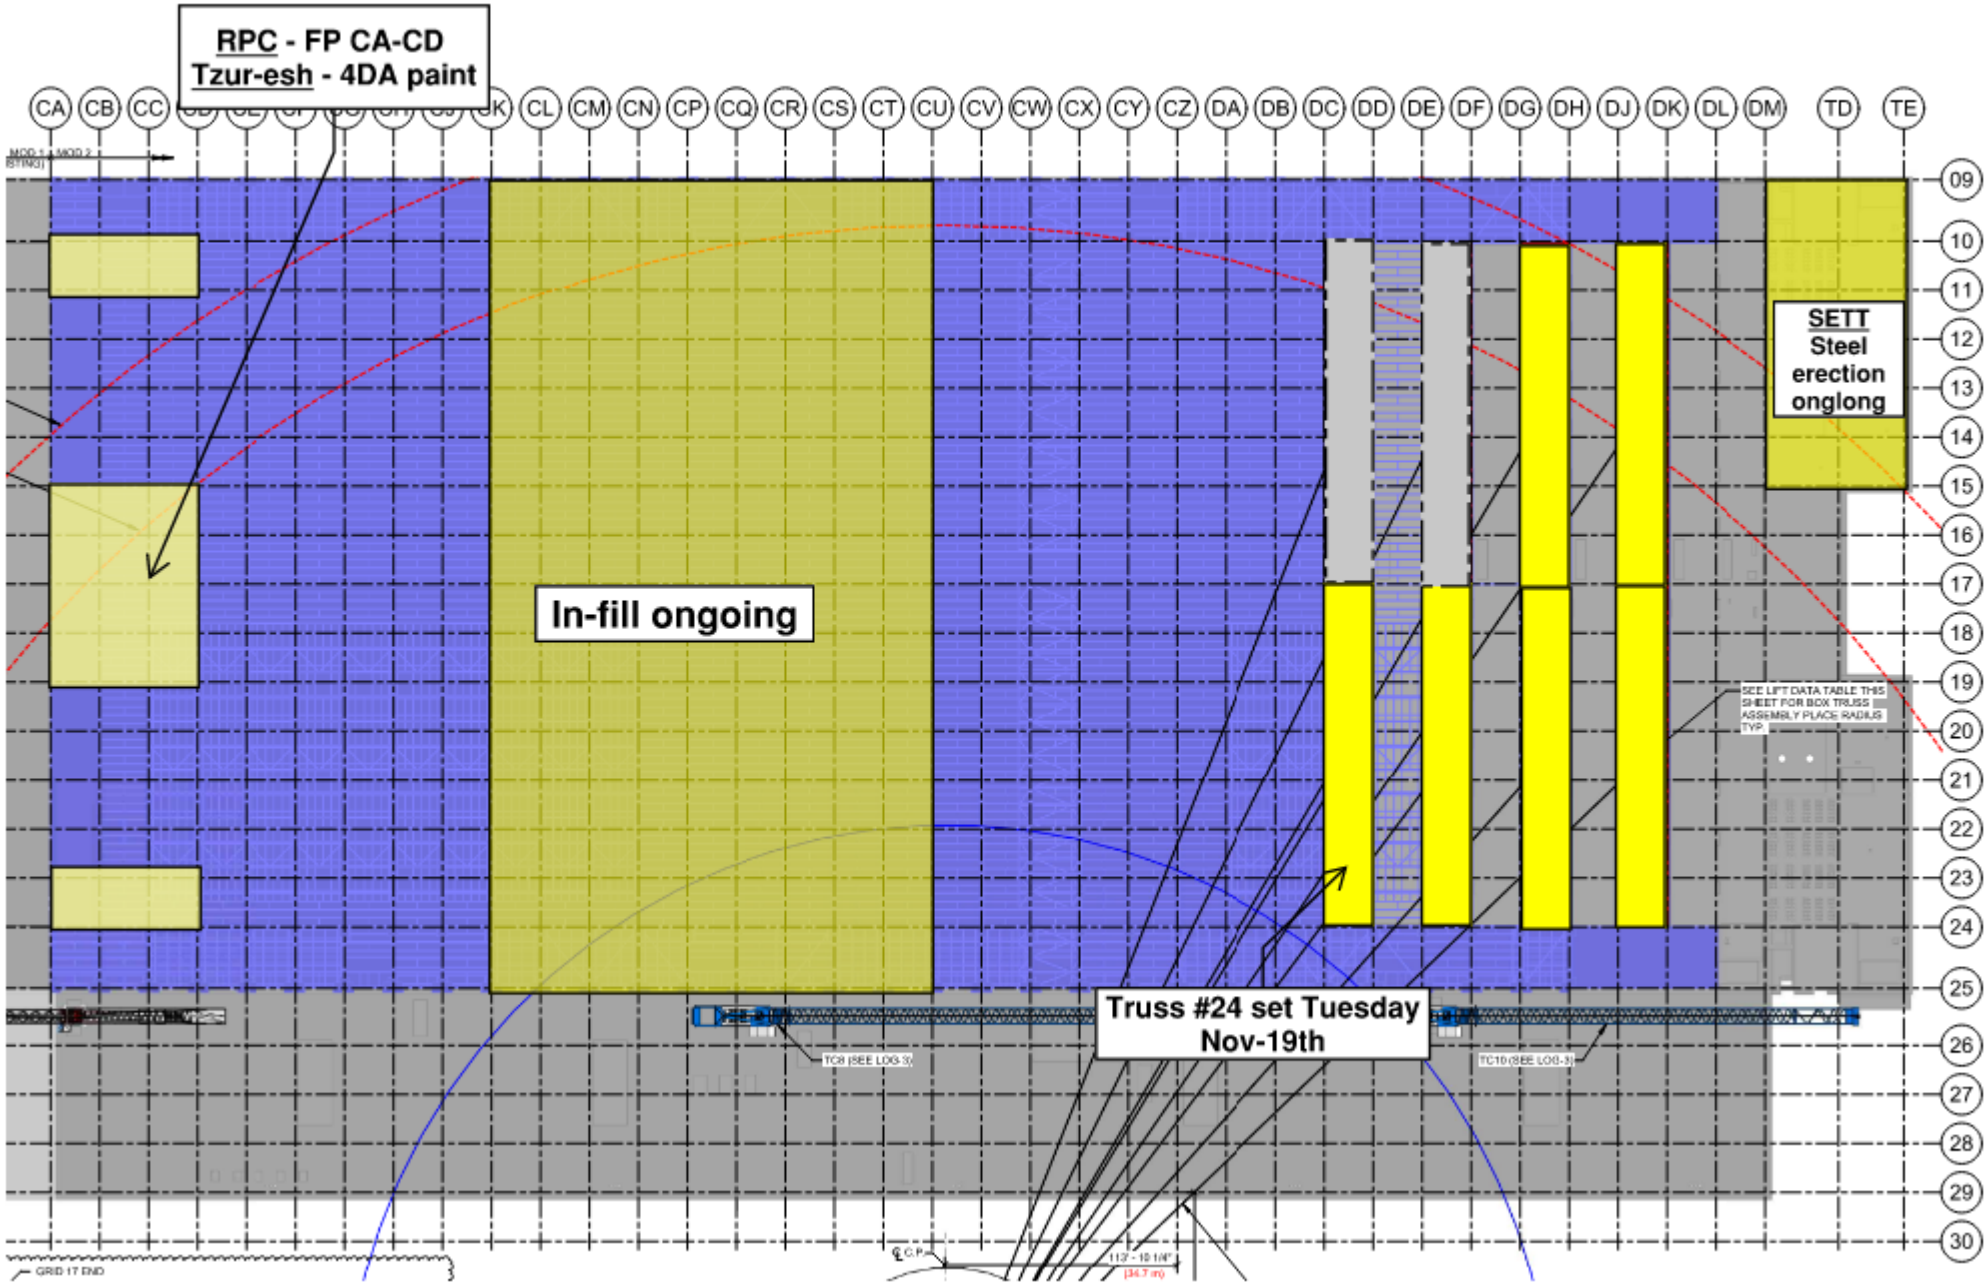
RPC - FP CA-CD
Tzur-esh - 4DA paint
In-fill ongoing
SETT
Steel
erection
onglong
Truss #24 set Tuesday
Nov-19th
CA CB CC CL CM CN CP CQ CR CS CT CU CV CW CX CY CZ DA DB DC DD DE DF DG DH DJ DK DL DM TD TE
09 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30

Clean Room Wall Of Shame
Trade Damage

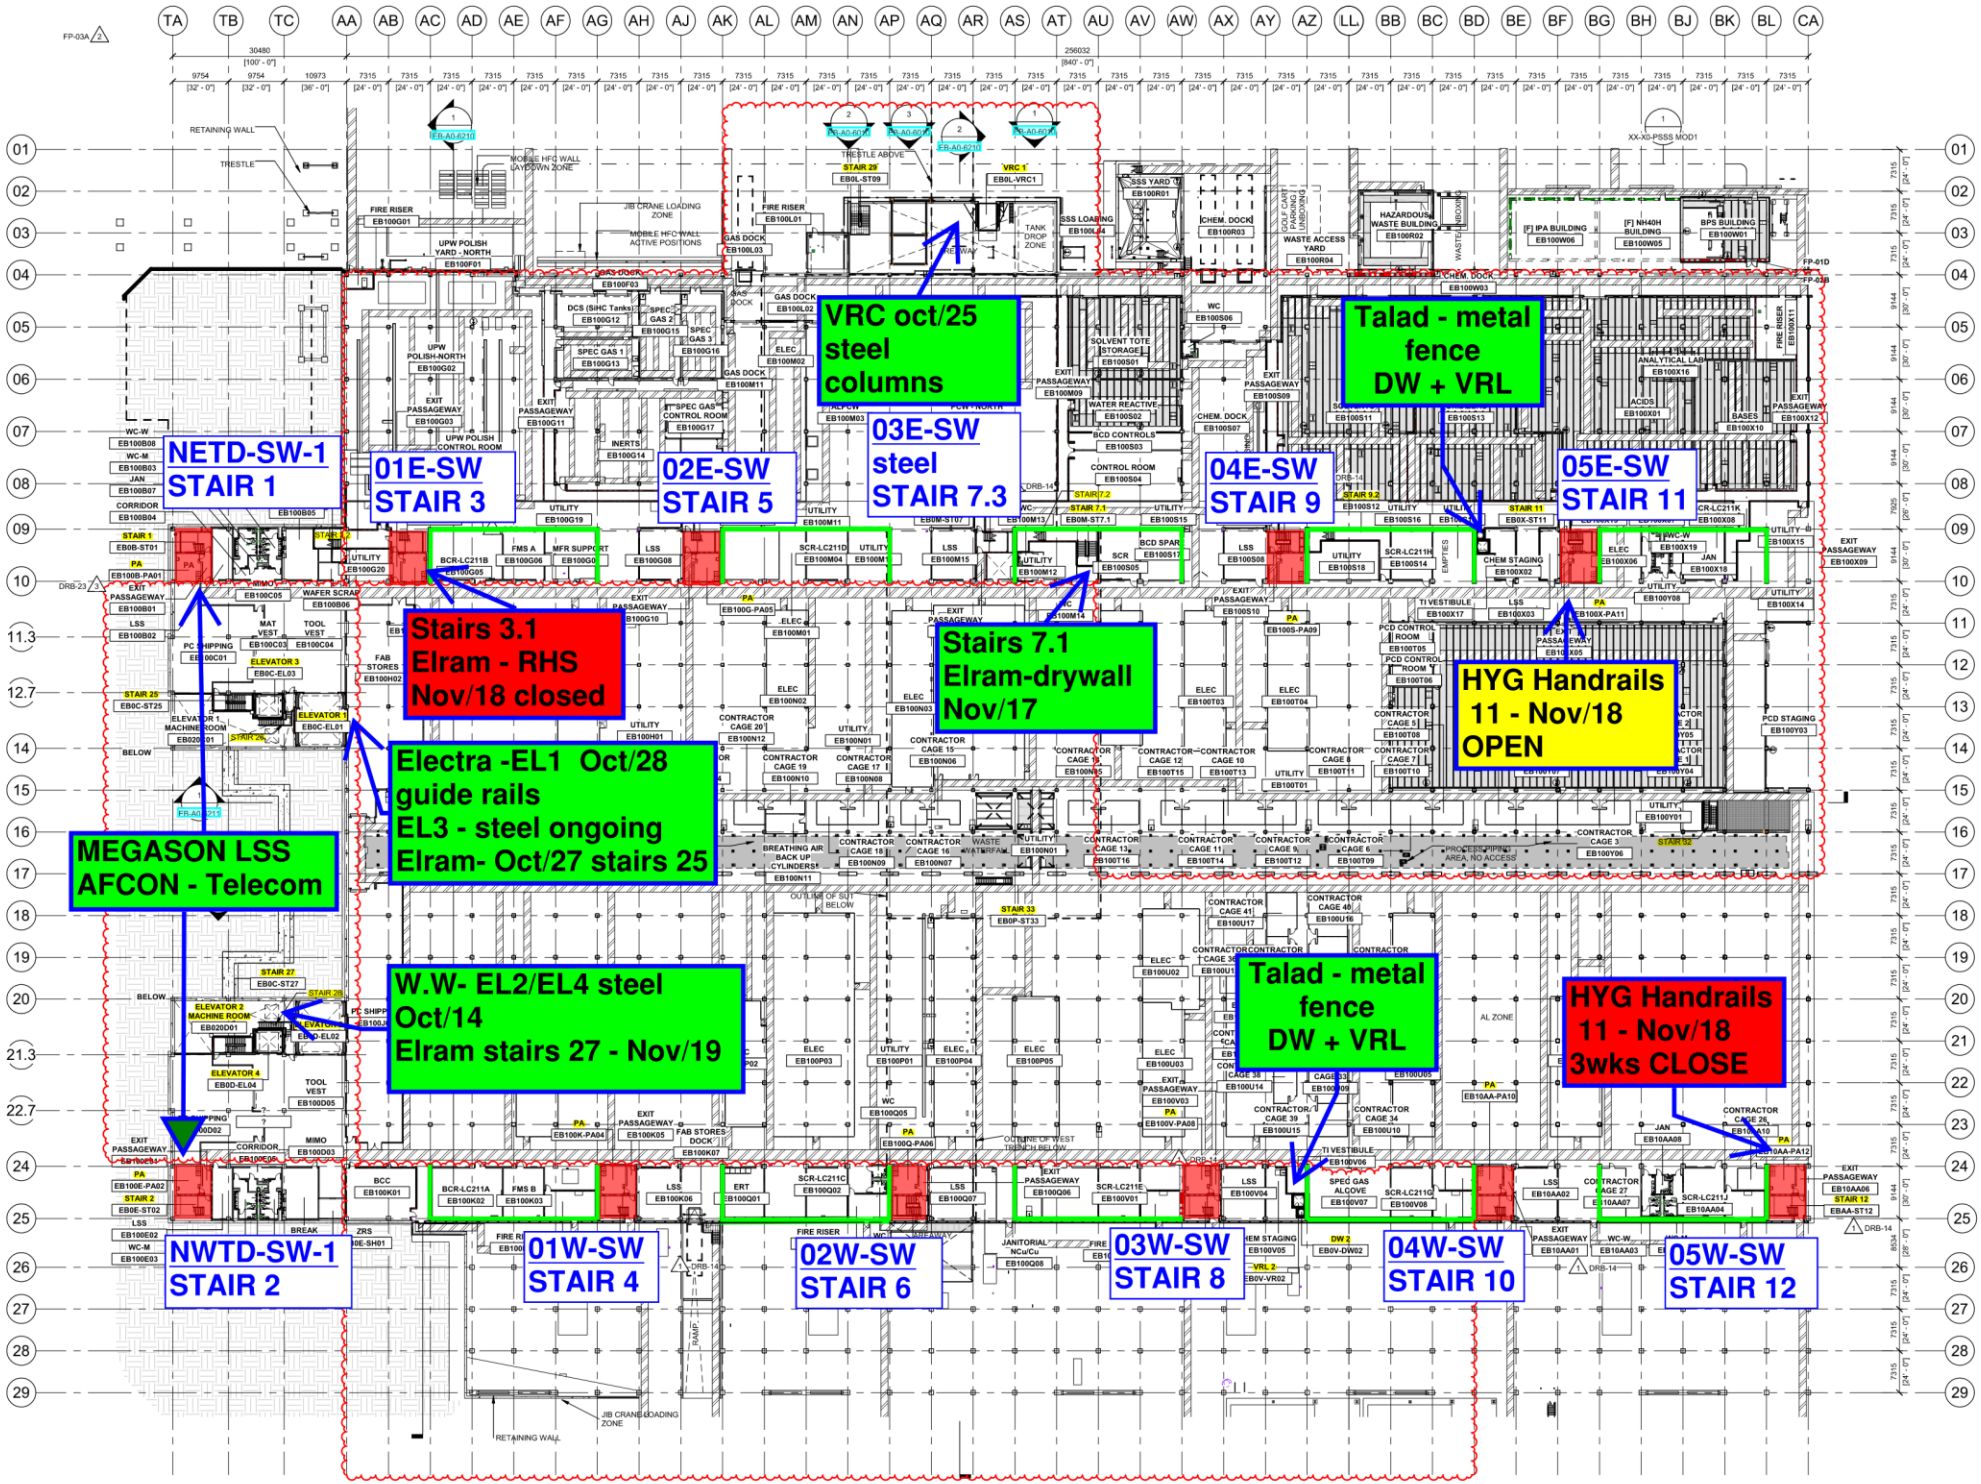
VRC oct/25
steel
columns
Talad - metal
fence
DW + VRL
NETD-SW-1
STAIR 1
01E-SW
STAIR 3
02E-SW
STAIR 5
03E-SW
steel
STAIR 7.3
04E-SW
STAIR 9
05E-SW
STAIR 11
Stairs 3.1
Elram - RHS
Nov/18 closed
Stairs 7.1
Elram-drywall
Nov/17
HYG Handrails
11 - Nov/18
OPEN
Electra -EL1 Oct/28
guide rails
EL3 - steel ongoing
Elram- Oct/27 stairs 25
MEGASON LSS
AFCON - Telecom
W.W- EL2/EL4 steel
Oct/14
Elram stairs 27 - Nov/19
Talad - metal
fence
DW + VRL
HYG Handrails
11 - Nov/18
3wks CLOSE
NWTD-SW-1
STAIR 2
01W-SW
STAIR 4
02W-SW
STAIR 6
03W-SW
STAIR 8
04W-SW
STAIR 10
05W-SW
STAIR 12

Siding - West FAB - JYG

BLOWDOWN 30%

Link

	TA	TB	TC	AA	AB	AC	AD	AE	AF	AG	AH	AJ	AK	AL	AM	AN	AP	AQ	AR	AS	AT	AU	AV	AW	AX	AY	AZ	BA	BB	BC	BD	BE	BF	BG	BH	BJ	BK	BL	CA
	1001 / 1002			601 / 602		611 / 612					621 / 622			631 / 632			641 / 642			651 / 652			811 / 812				821 / 822			831 / 832				841 / 842				851 / 852
Total	28	28	28	15	18	31	31	31	31	31	31	31	31	31	30	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31	31
Installed	21	28	10	15	18	31	31	31	31	31	31	31	31	31	30	23	22	22	31	29	27	24	24	25	19	17	17	17	14	14	14	14	14	14	14	14	14	14	14
%	75%	100%	36%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	74%	71%	71%	100%	94%	87%	77%	77%	81%	61%	55%	55%	55%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%	45%
5RA	0	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	0	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	0	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	0	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	0	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
4DA	0	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
3FK	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
3FA	1	1	0	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	0	0	0	0	0	0	0	0	0	0	0
	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
2SA SF	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
					1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
UL					1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1

Siding - East FAB - PSSS

BLOWDOWN 30%

	CA	BL	BK	BJ	BH	BG	BF	BE	BD	BC	BB	BA	AZ	AY	AX	AW	AV	AU	AT	AS	AR	AQ	AP	AN	AM	AL	AK	AJ	AH	AG	AF	AE	AD	AC	AB	AA	TC	TB	TA	
	751 / 752			741 / 742		731 / 732				721 / 722				711 / 712				551 / 552			541 / 542			531 / 532				521 / 522				511 / 512				501 / 502		901 / 902			
Total	24	24	24	24	24	24	24	24	24	24	24	24		24	24	24	24	24	24	24	24	24	24	24	24	24		17	17	17		24	24	24	24		24	24	28	28	28	
Installed	12	12	12	12	12	12	12	12	12	17	17	16		17	16	20	16	7	7	17	24	24	24	16	16	16	16	17	17	17		24	24	24	24		24	24	26	26	26	
%	50%	50%	50%	50%	50%	50%	50%	50%	50%	71%	71%	75%		71%	75%	83%	75%	29%	29%	71%	100%	100%	100%	75%	75%	75%	75%	100%	100%	100%		100%	100%	100%	100%		##	100%	100%	100%	93%	
5RA	0	0	0	0	0	0	0	0	0	0	0	0		0	0	0	0	0	0	0	1	1	1	0	0	0	0	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	0	0	0		0	0	0	0	0	0	0	1	1	1	0	0	0	0	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	0	0	0		0	0	0	0	0	0	0	1	1	1	0	0	0	0	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	0	0	0		0	0	0	0	0	0	0	1	1	1	0	0	0	0	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	0	0	0		0	0	1	0	0	0	0	1	1	1	0	0	0	0	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	0	0	0		0	0	0	0	0	0	0	1	1	1	0	0	0	0	1	1	1		1	1	1	1		1	1	1	1	1	
4DA	0	0	0	0	0	0	0	0	0	0	0	0		0	1	1	1	0	0	0	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	1	1	1		1	1	1	1	0	0	0	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	1	1	1		1	1	1	1	0	0	0	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	1	1	1		1	1	1	1	0	0	0	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	0	0	0	0	0	0	0	0	0	1	1	1		1	1	1	1	0	0	0	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
3FK	0	0	0	0	0	0	0	0	0	1	1	1		1	1	1	1	0	0	0	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	0	0	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	0	0	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	0	0	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
3FA	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	0	0	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
DEMO	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1	1	1	1	1	1	1					1	1	1	1		1	1	1	1	1	
Sub Fab																																				1		1	1	1	
																																				1		1	1	0	
																																				1		1	1	0	

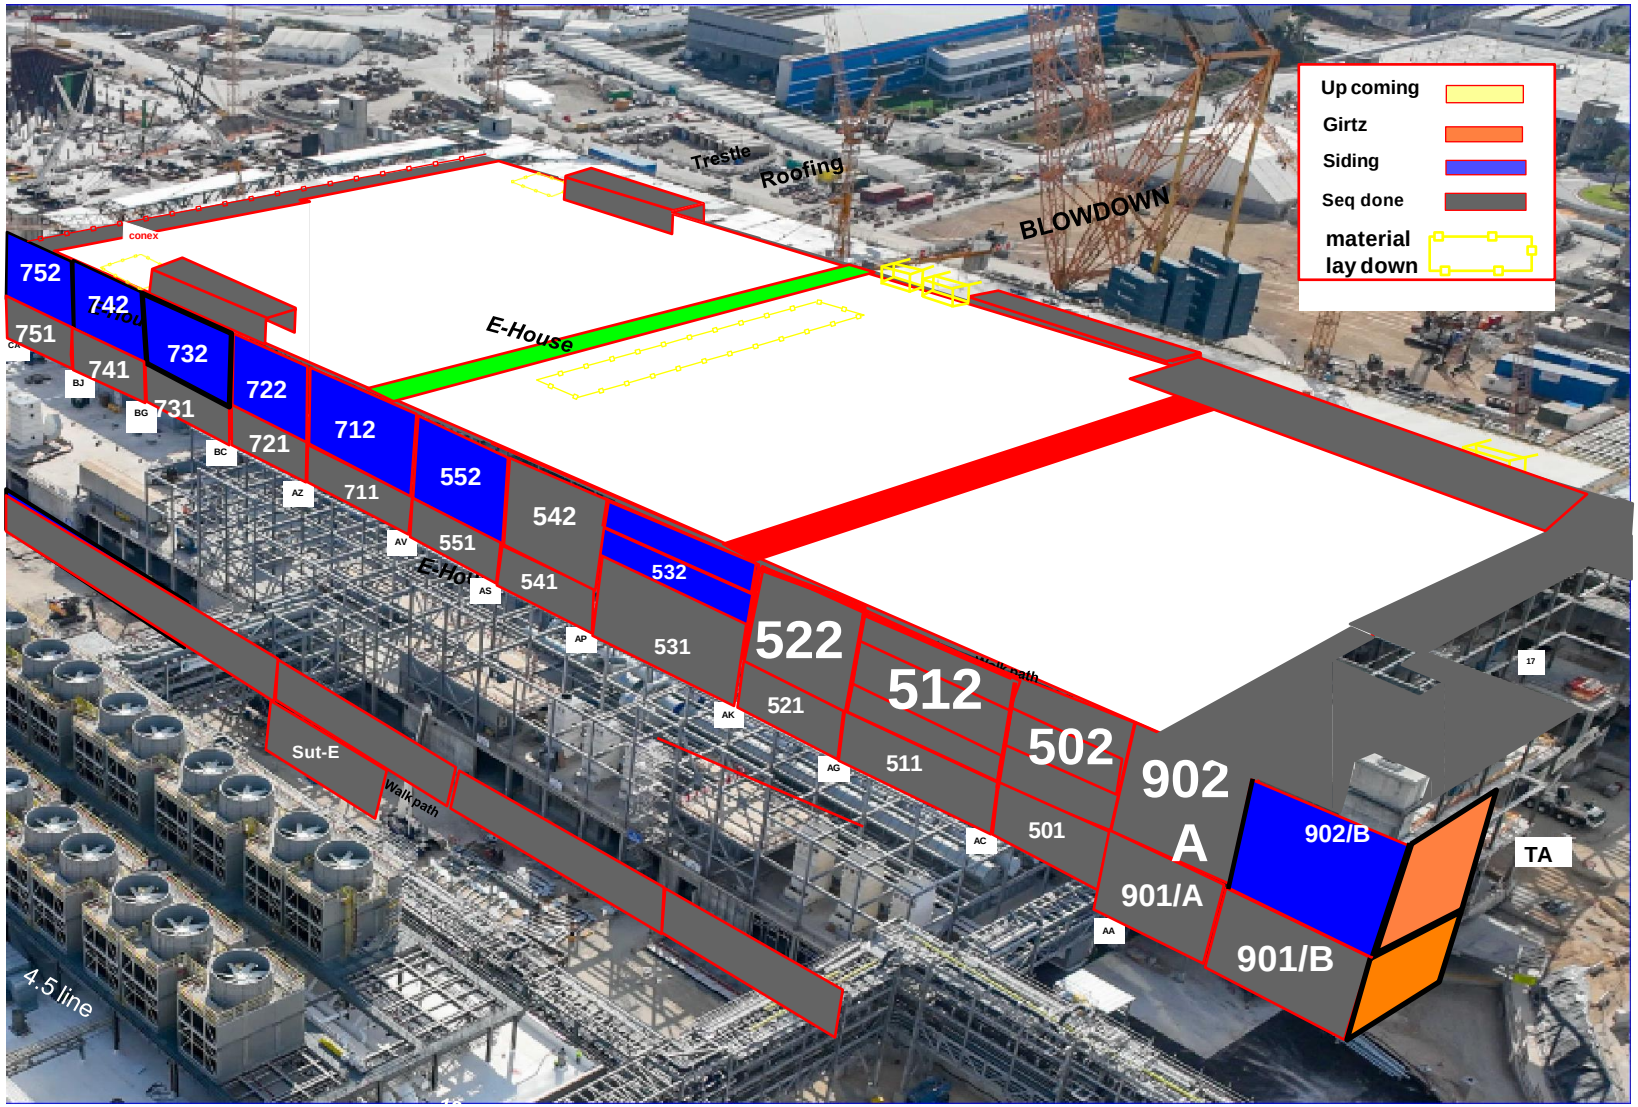
Up coming
Girtz
Siding
Seq done
material lay down
Trestle
Roofing
BLOWDOWN
E-House
conex
752
742
751
741
732
731
722
721
712
711
552
551
542
541
532
531
522
521
512
511
502
501
902 A
901/A
902/B
901/B
TA
BJ
BG
BC
AZ
AV
AS
AP
AK
AG
AC
AA
17
Sut-E
Walk path
4.5 line

Walk path

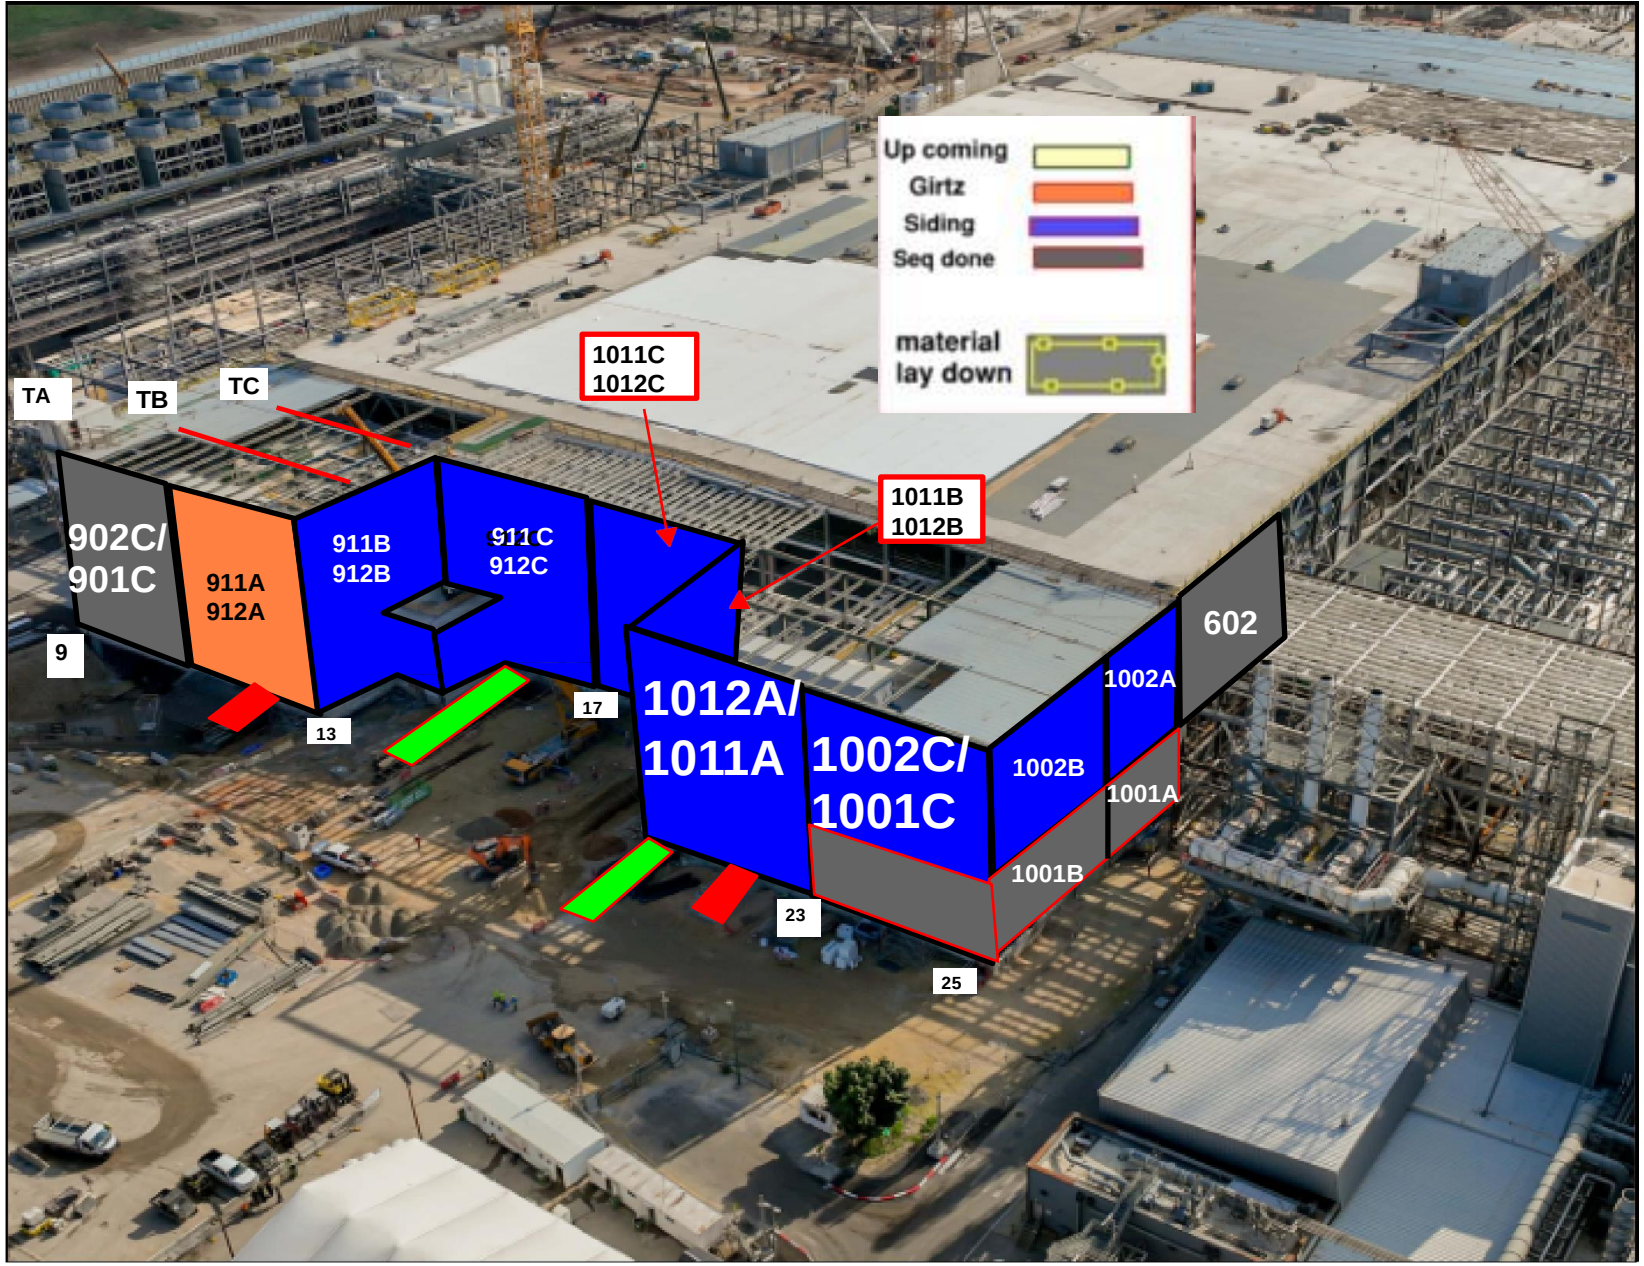
Up coming
Girtz
Siding
Seq done
material lay down
TA
TB
TC
1011C
1012C
1011B
1012B
902C/
901C
911A
912A
911B
912B
911C
912C
9
13
17
1012A/
1011A
1002C/
1001C
1002B
1002A
1001A
1001B
602
23
25

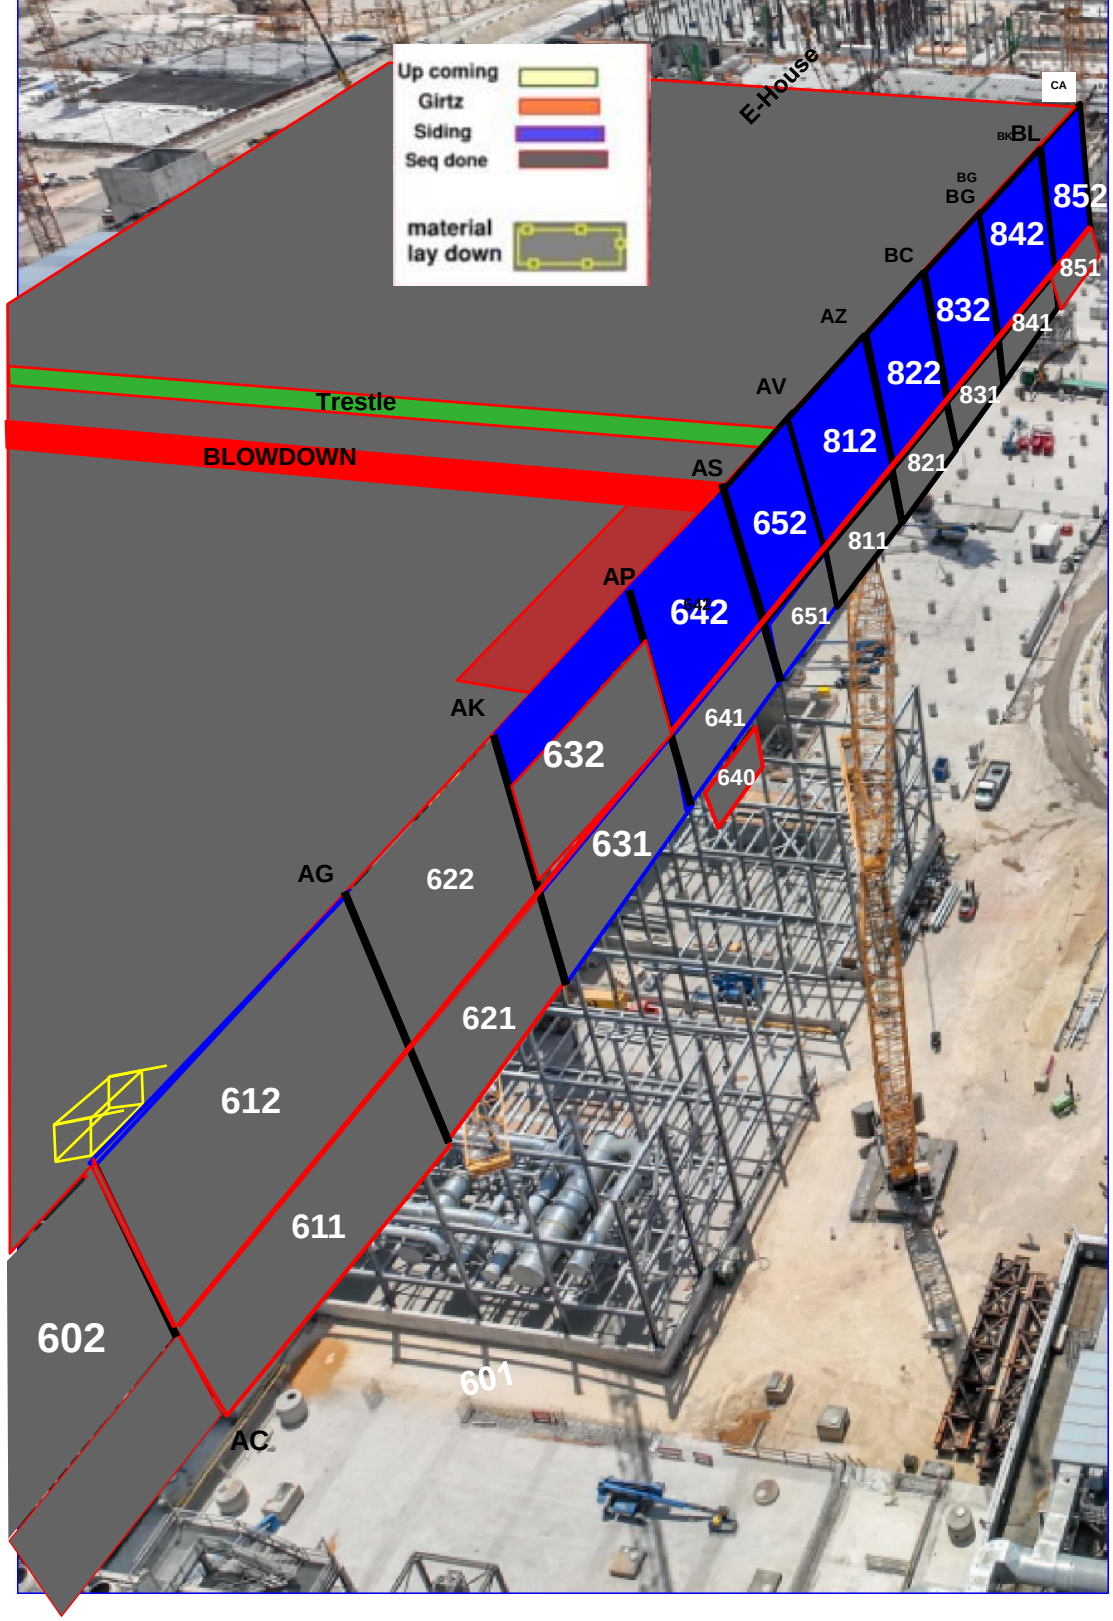
Up coming
Girtz
Siding
Seq done
material lay down
E-House
CA
BK BL
BG BG
BC
AZ
AV
AS
AP
AK
AG
AC
Trestle
BLOWDOWN
852
842
851
832
841
822
831
812
821
652
811
642
651
641
640
632
631
622
621
612
611
602
601

PSSS.1

Utility Level 1YA

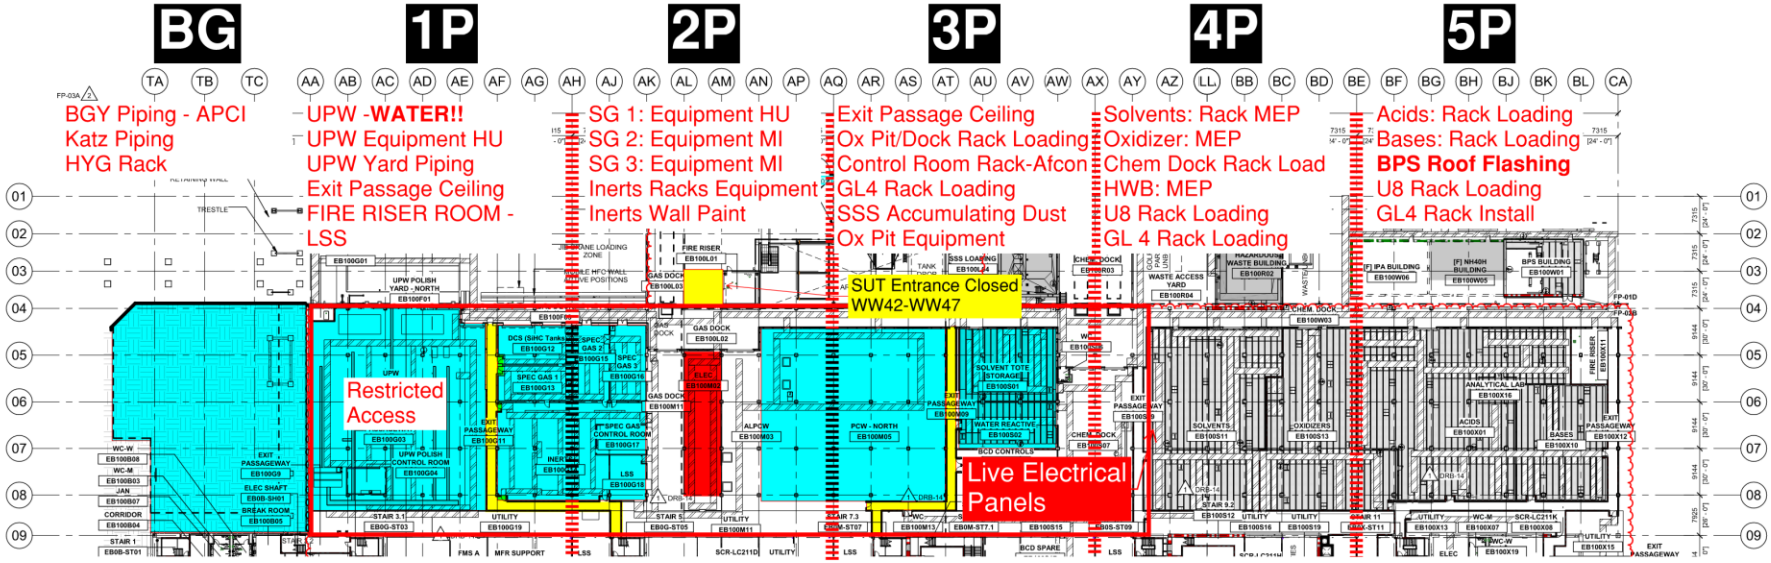

PSSS Roof 2SA

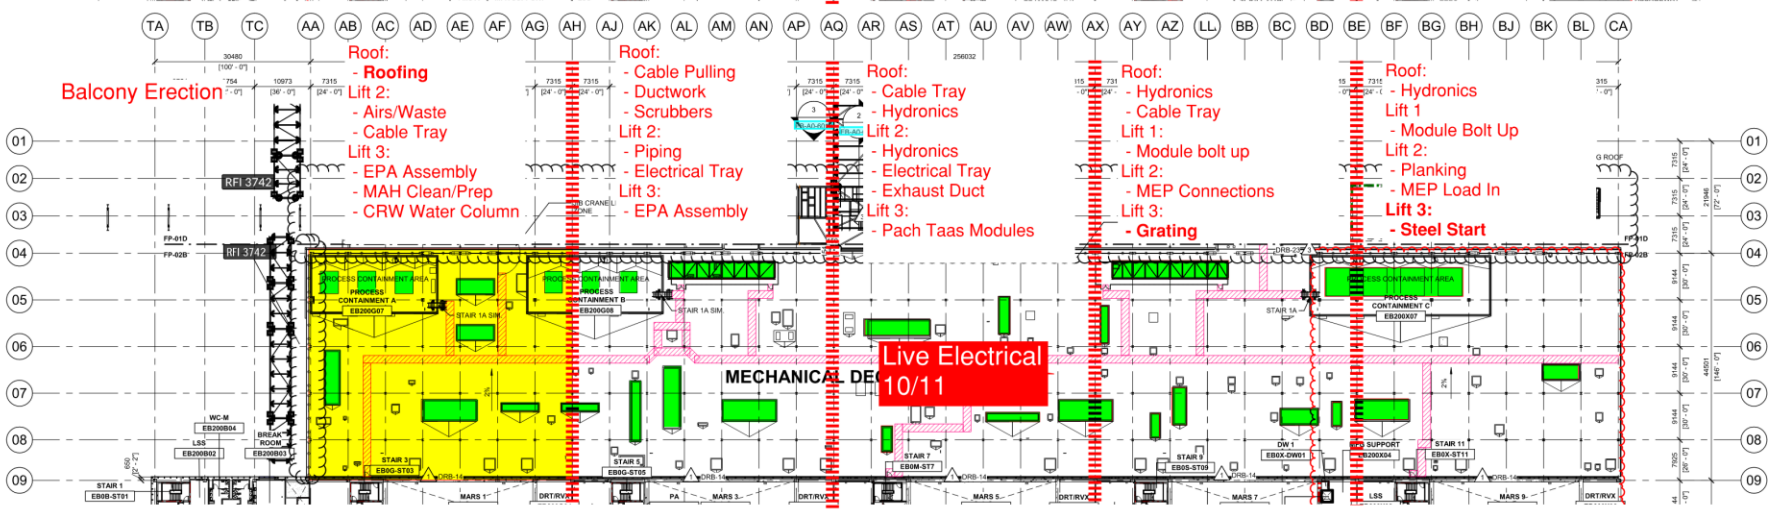

PSSS.2

Utility Level
1YA

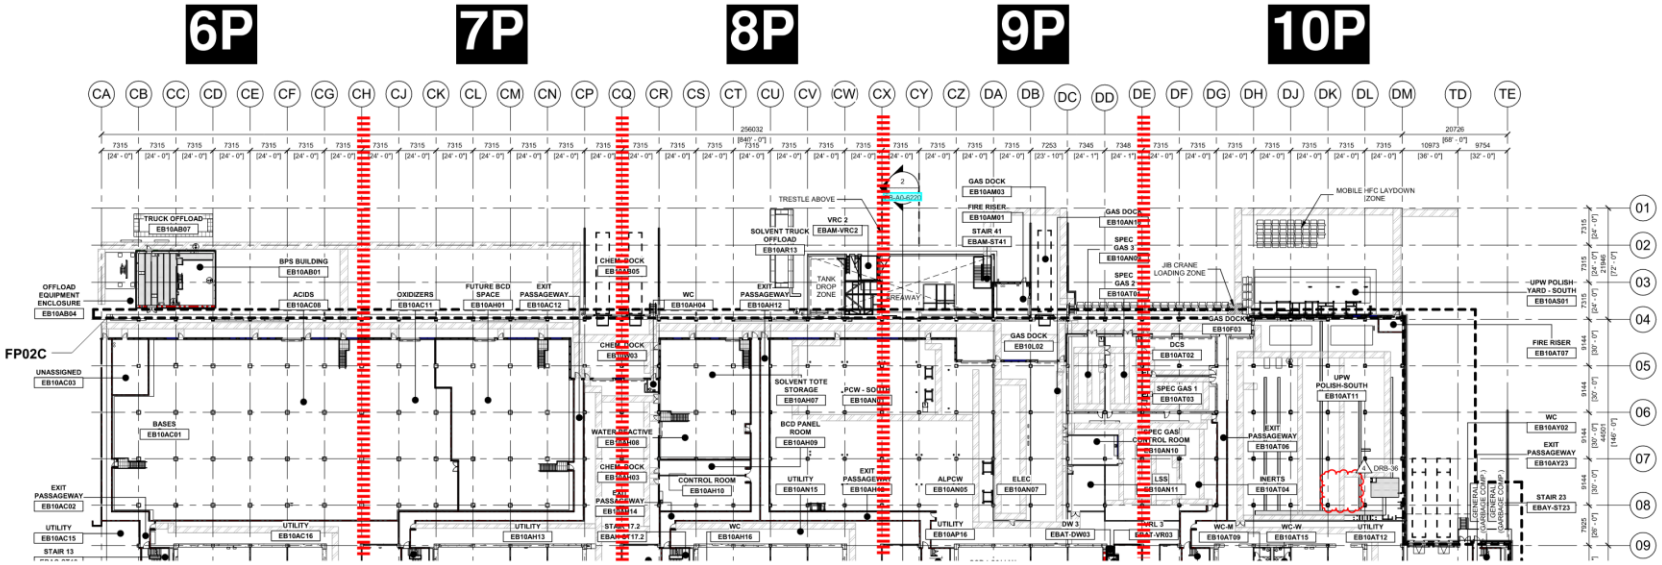

PSSS Roof
2SA

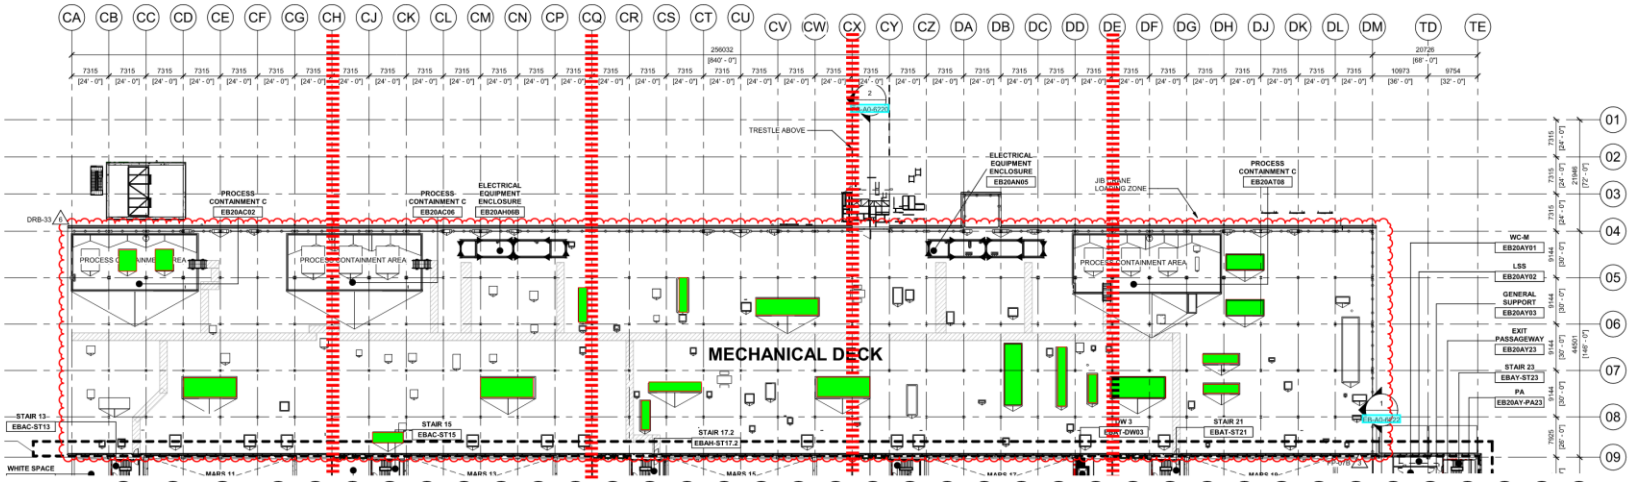

TC3 Dismantle 14/11 (Nights)

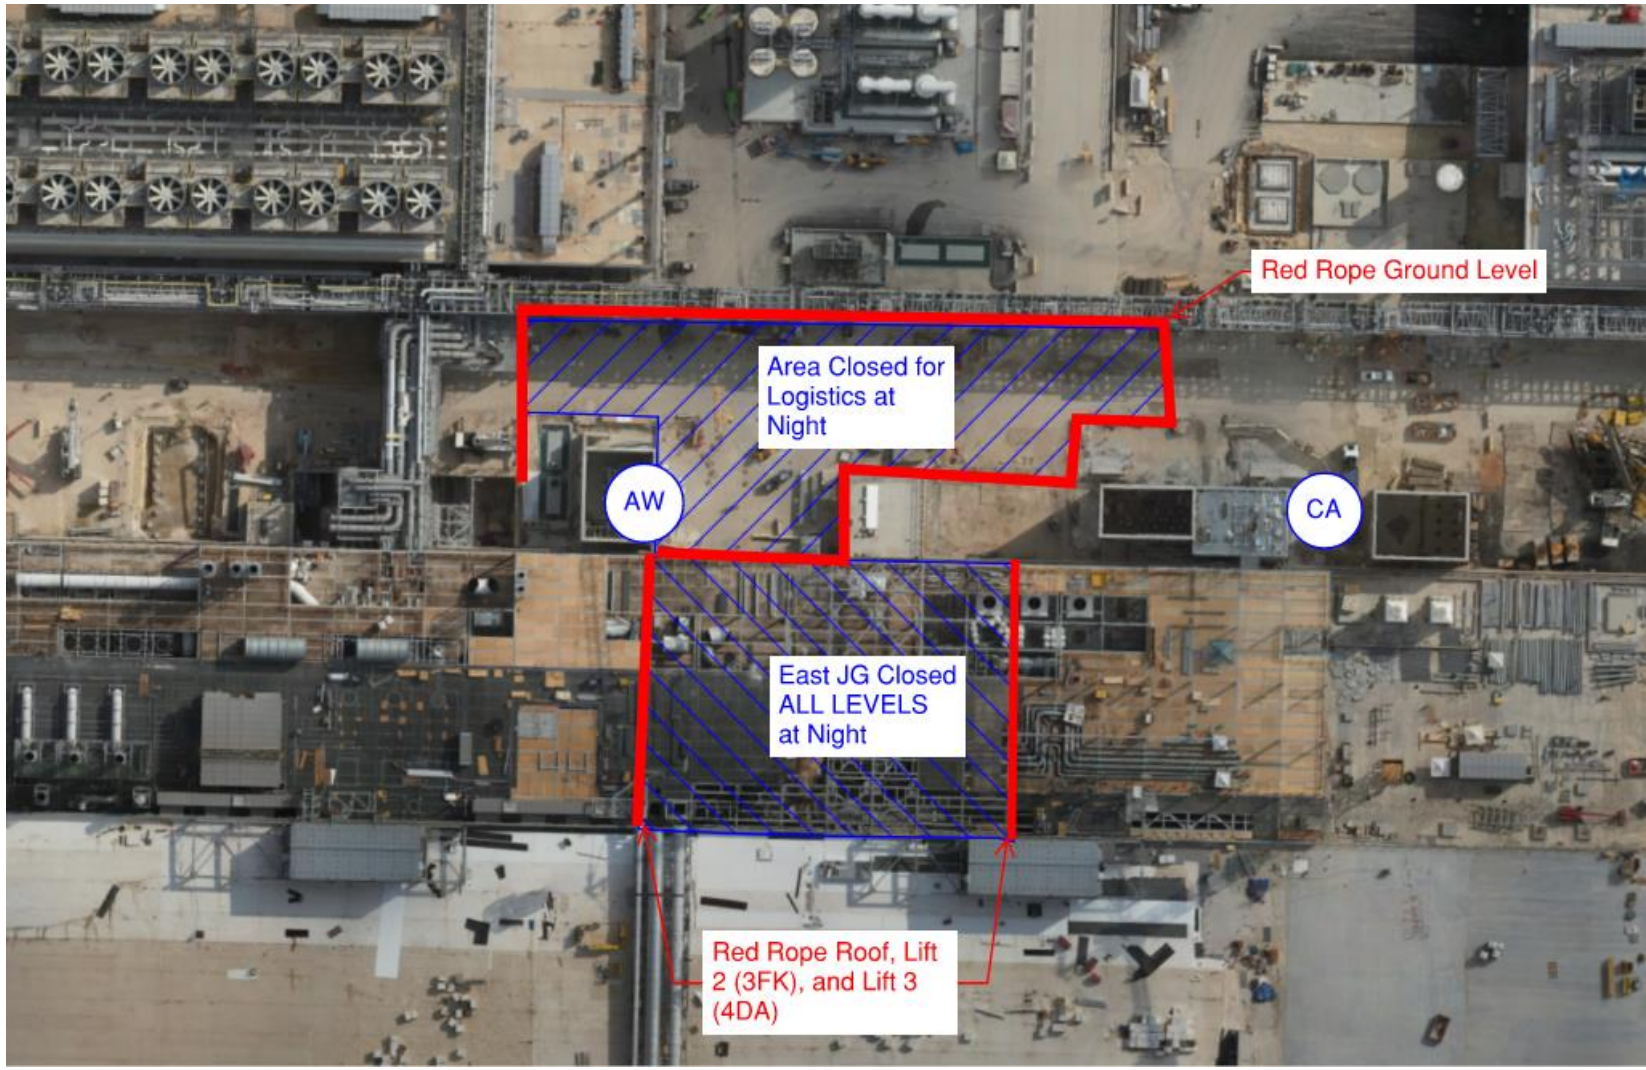

PSSS Vehicular Access

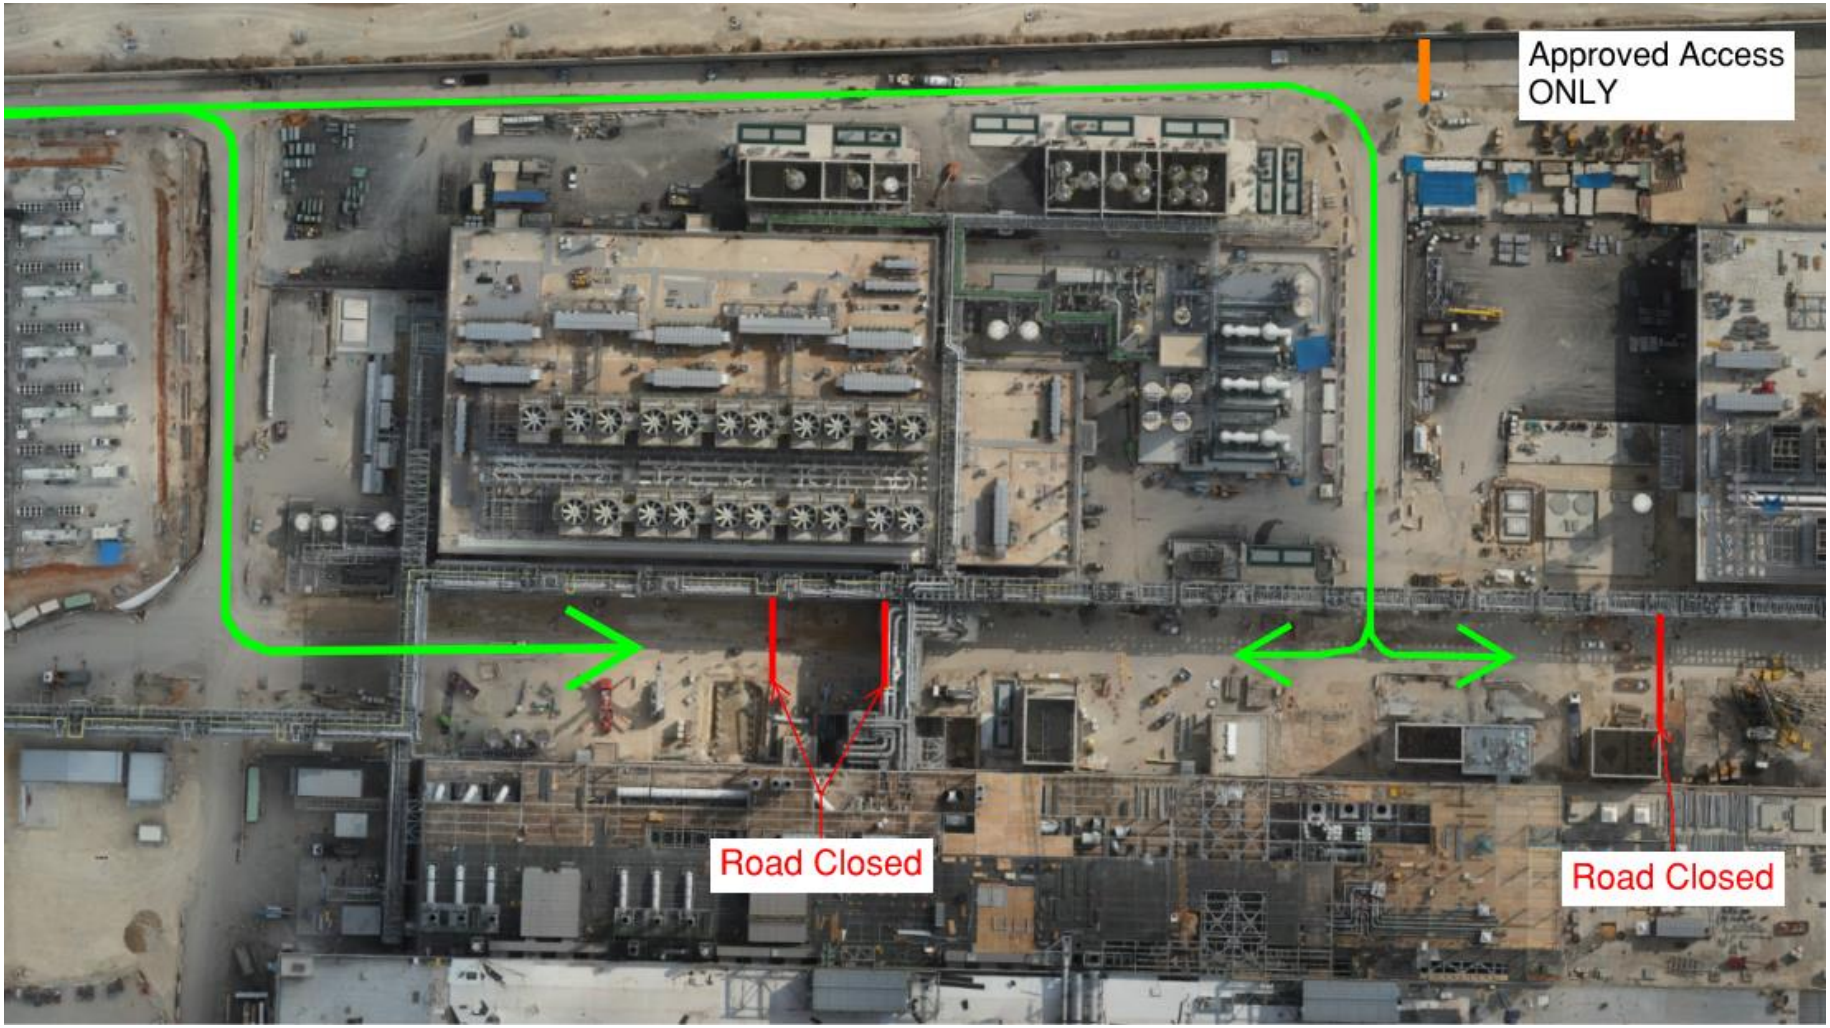

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

WJG 01J, 02J LIFT 2 & 3

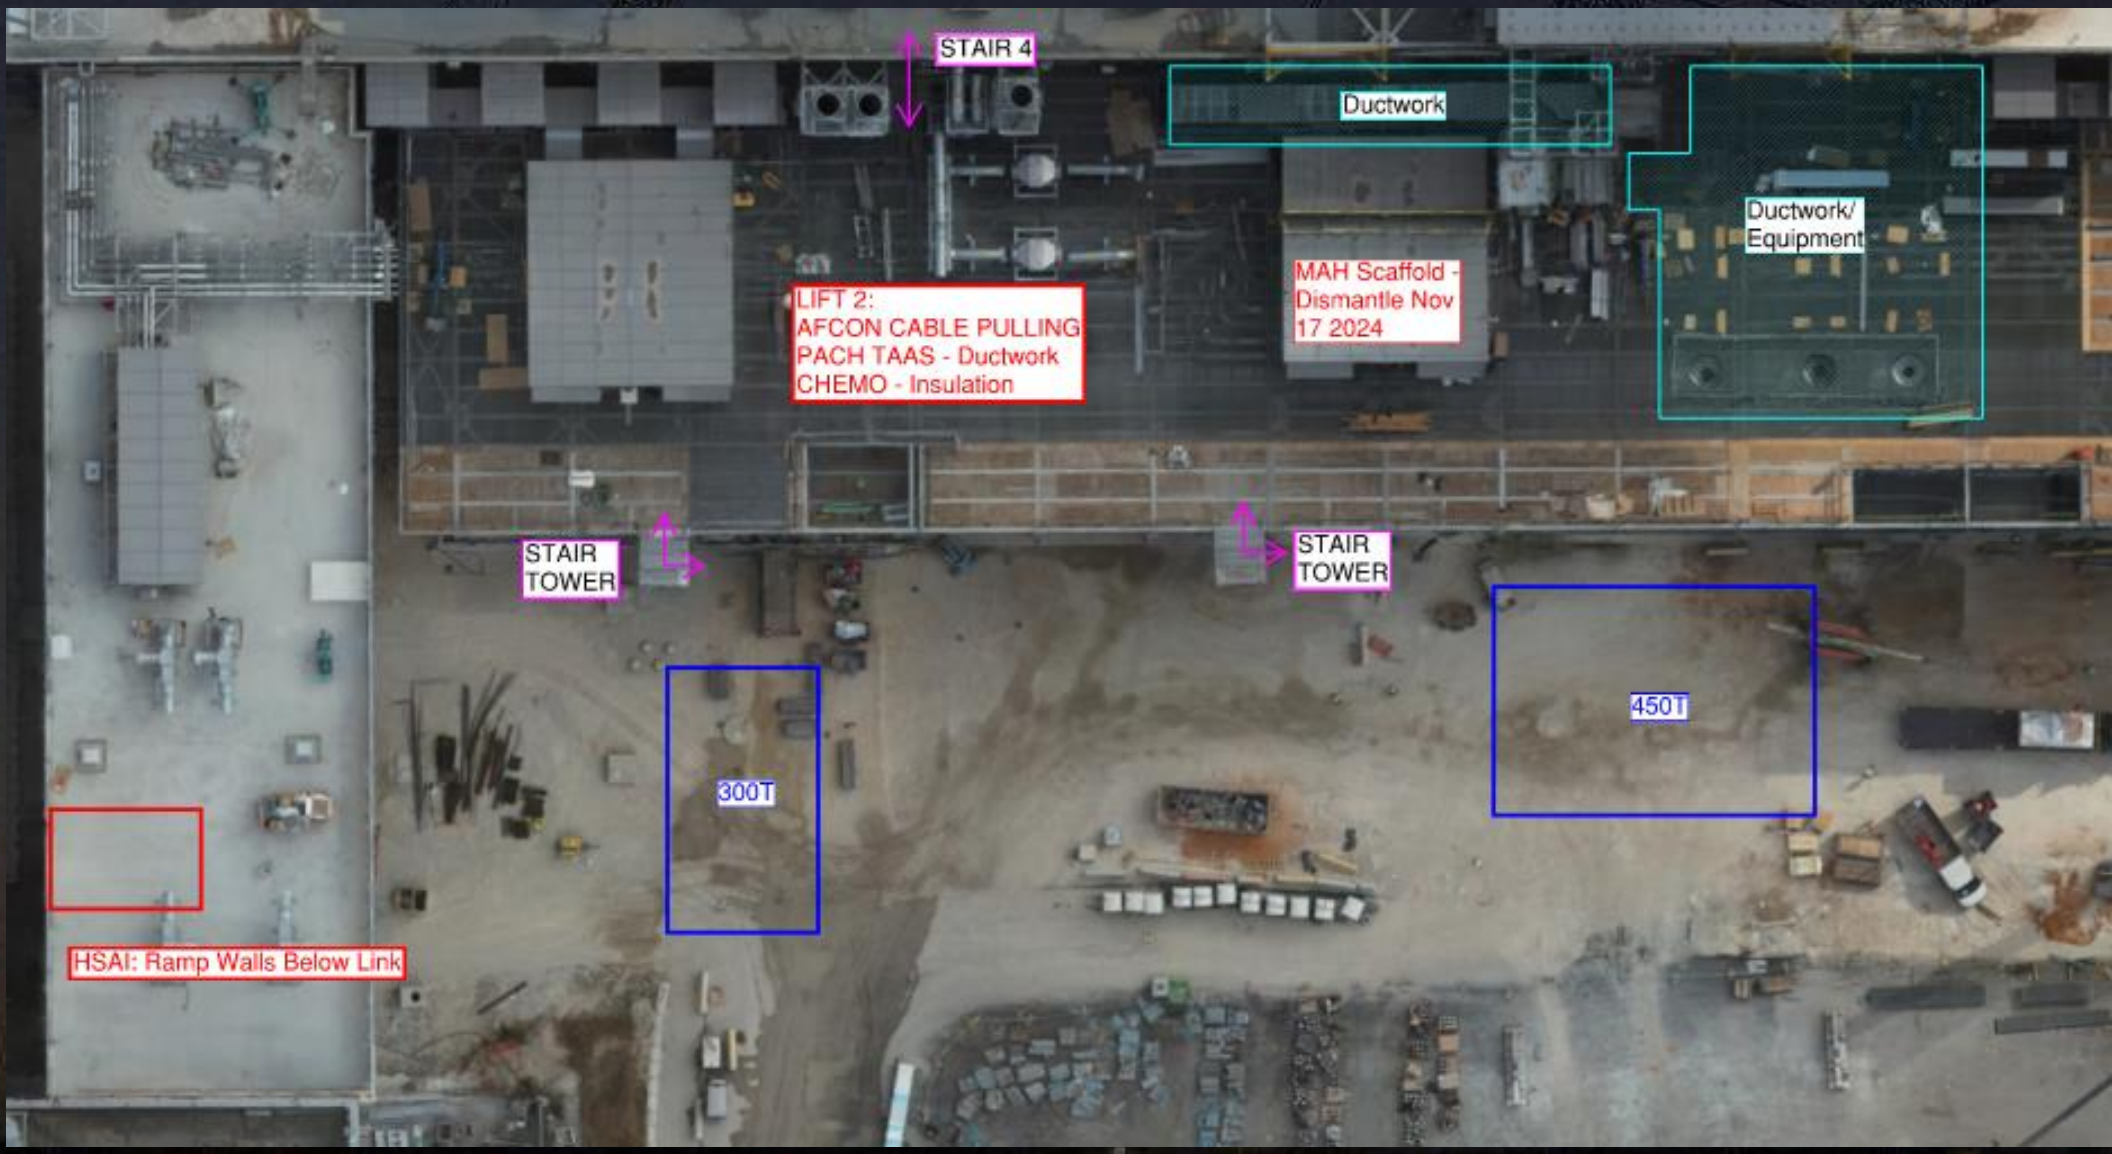

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

WJG 03J, 04J, 05J LIFT 2 & 3

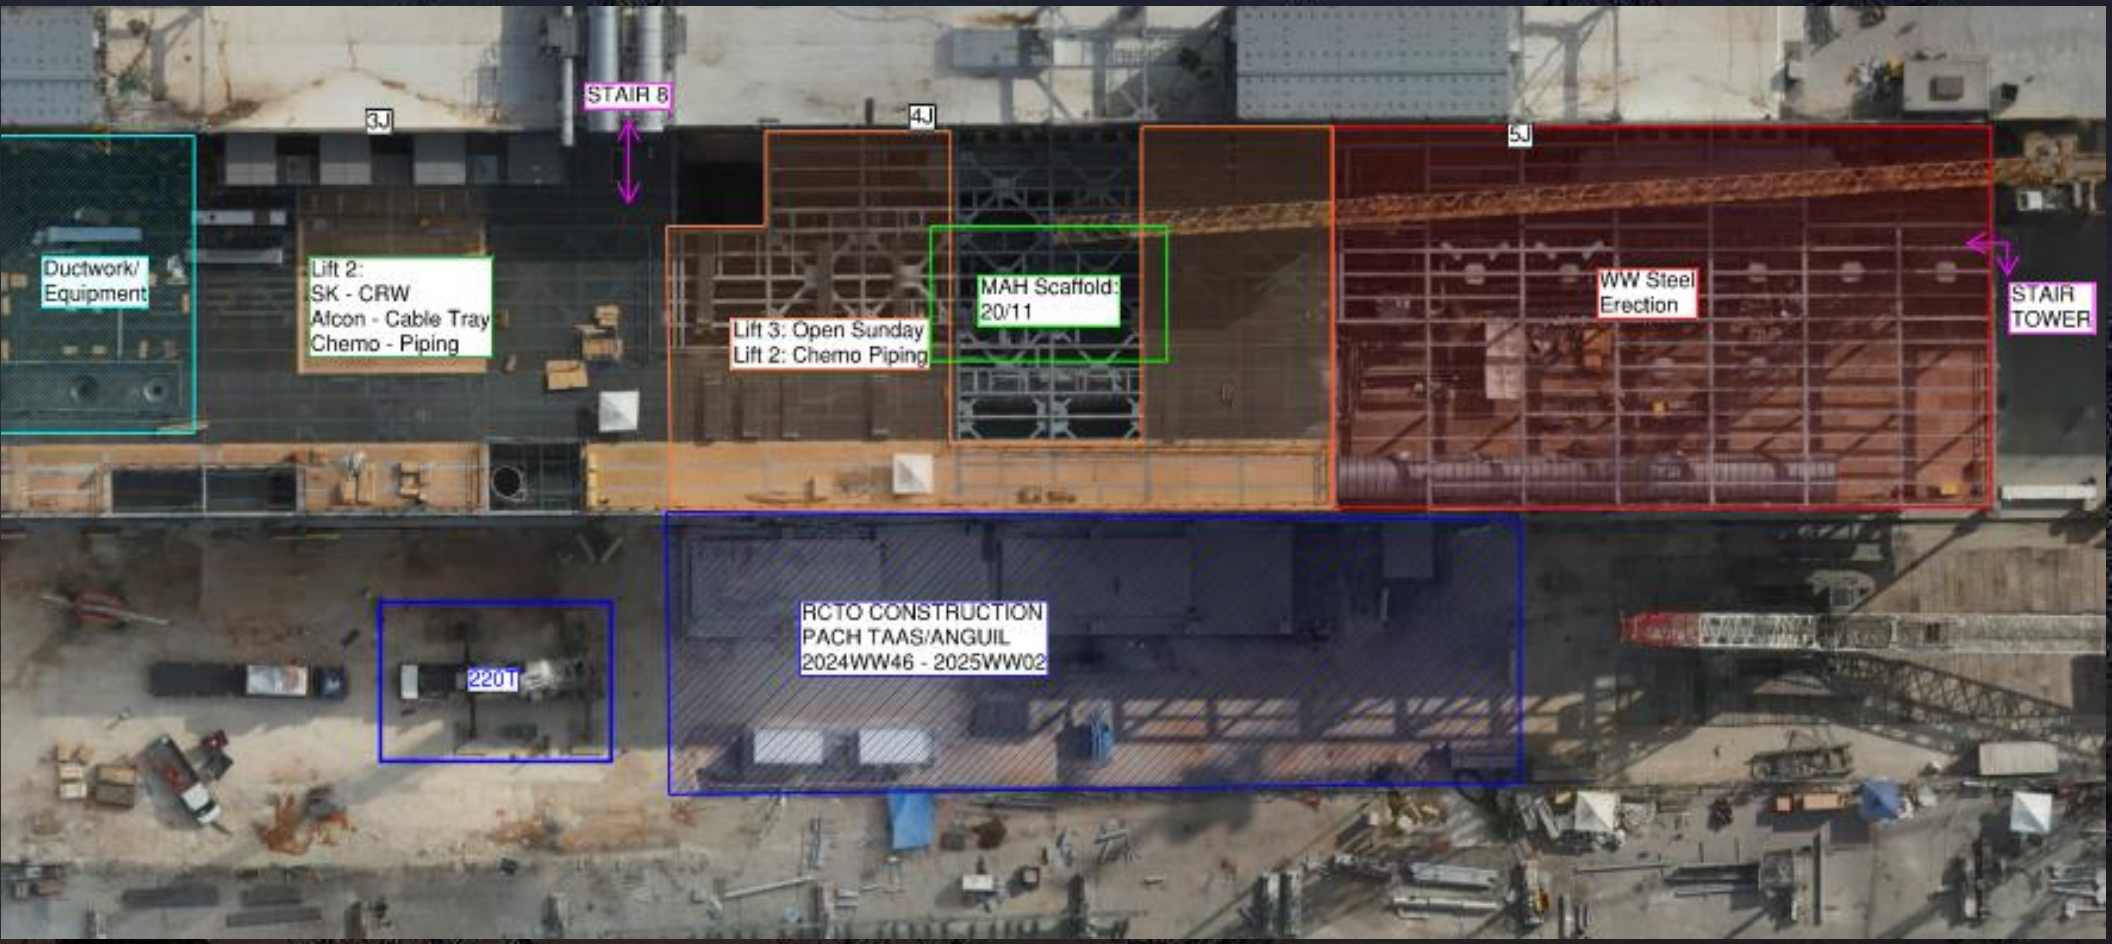

MAH101-7/8-00 Set WW47

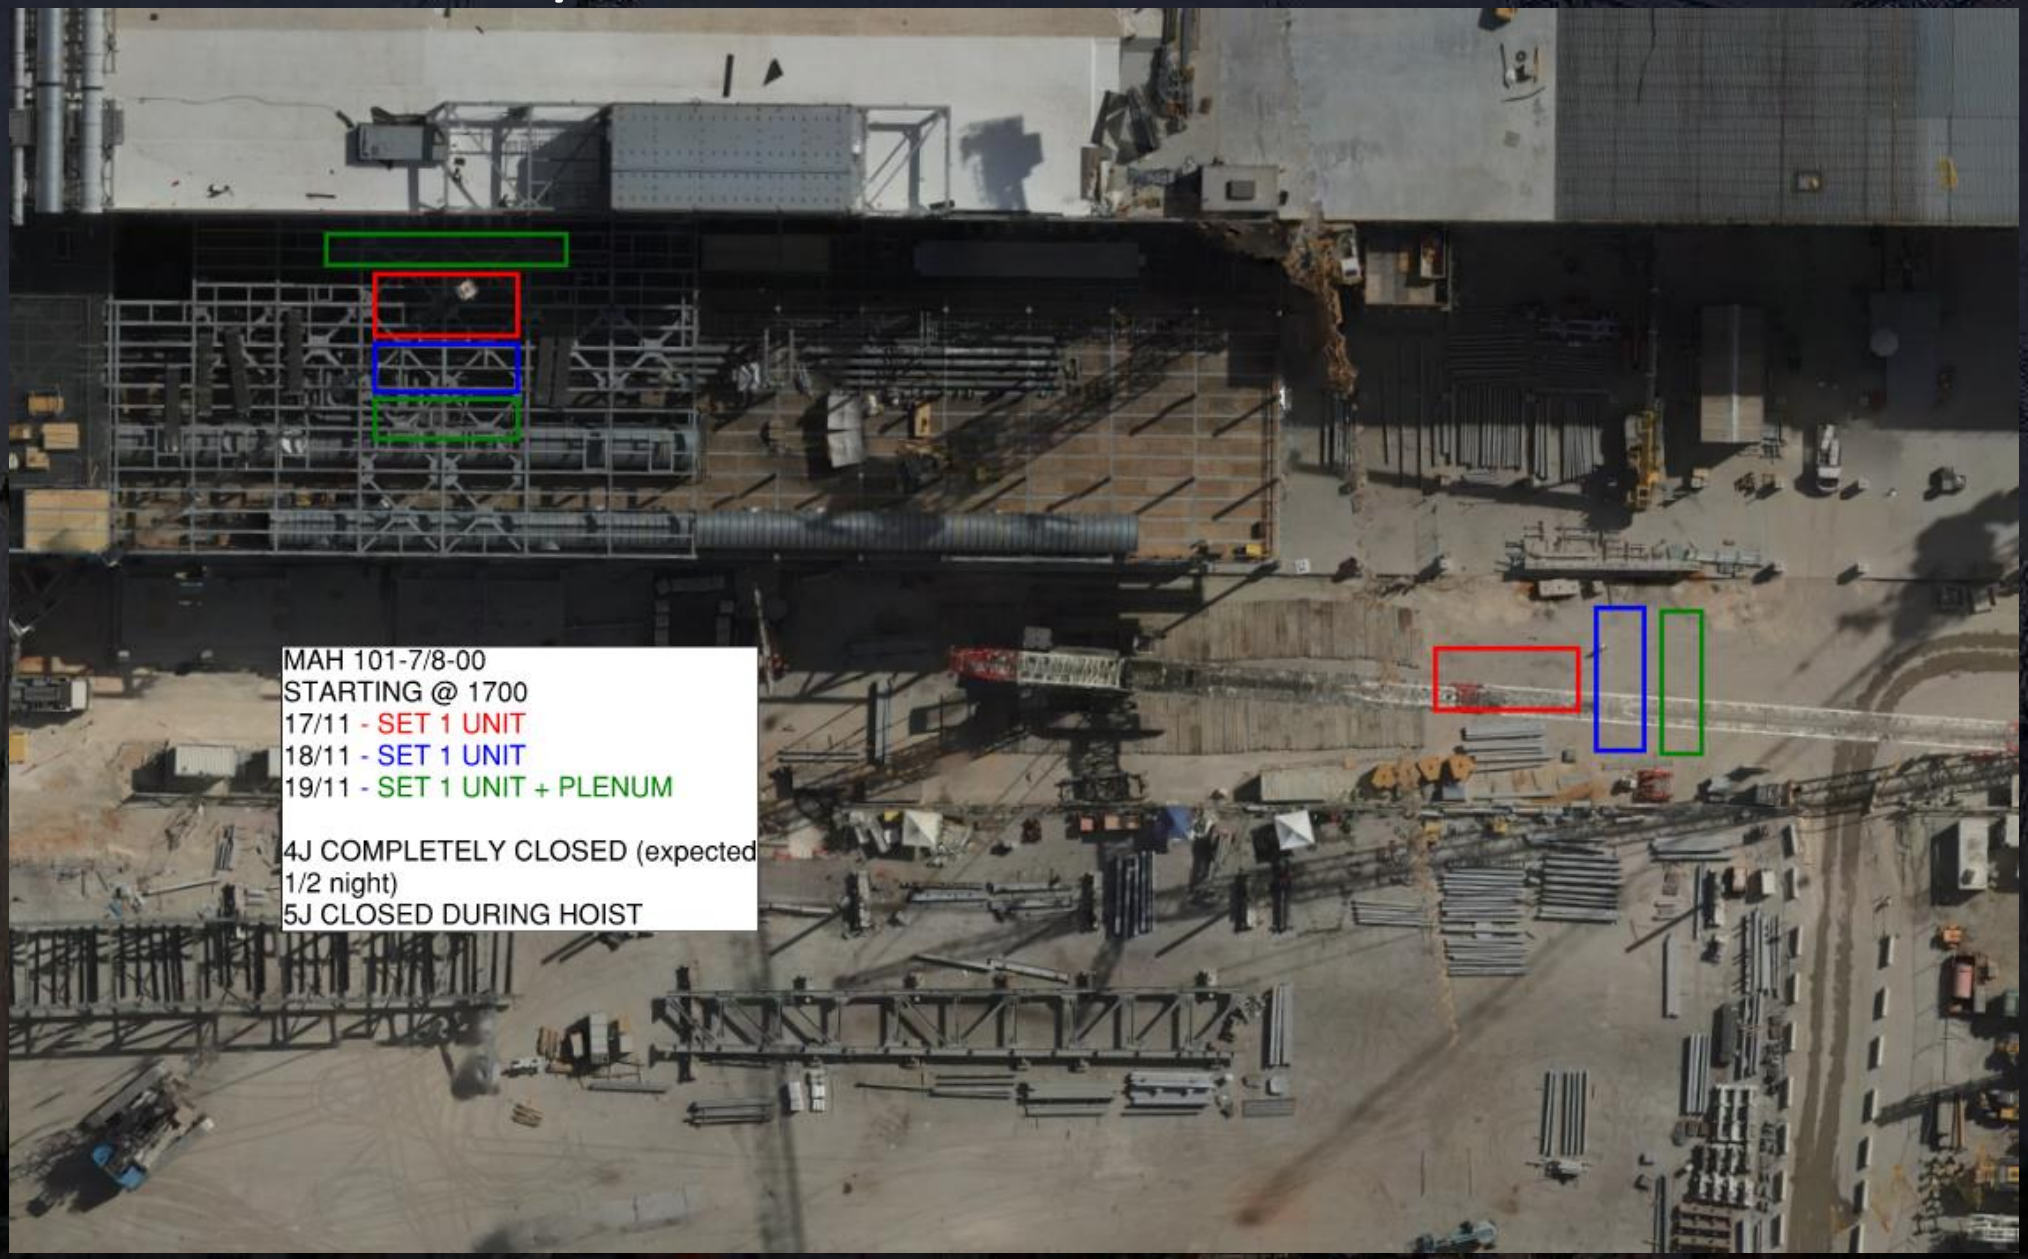

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

WJG UTILITY LEVEL BUILD OUT

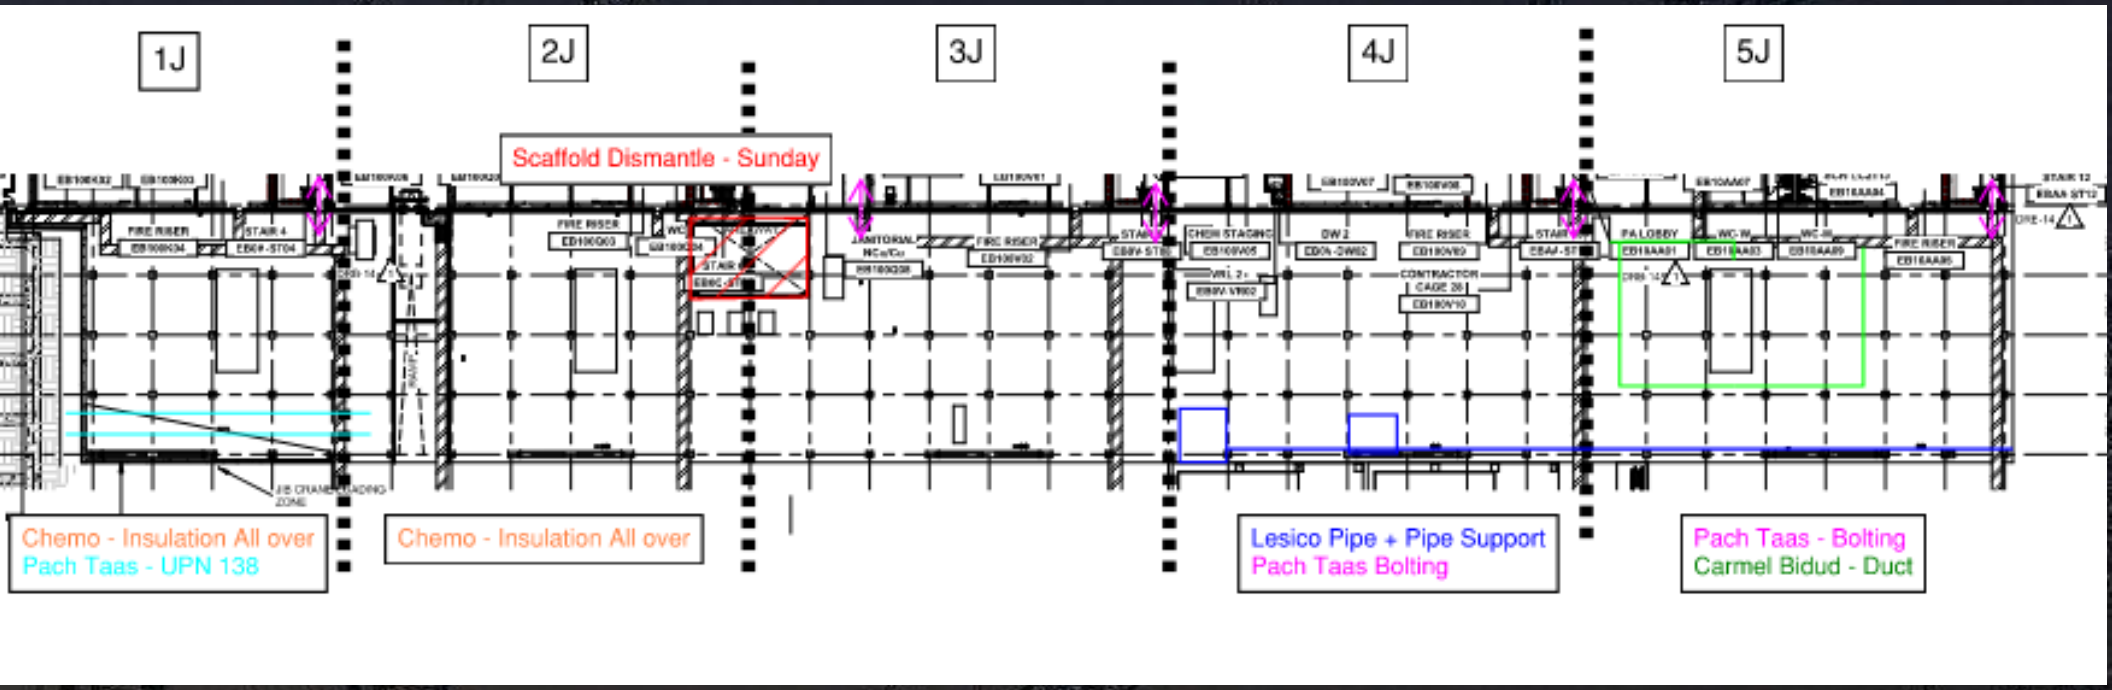

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

CUB 1- Start up logisitics

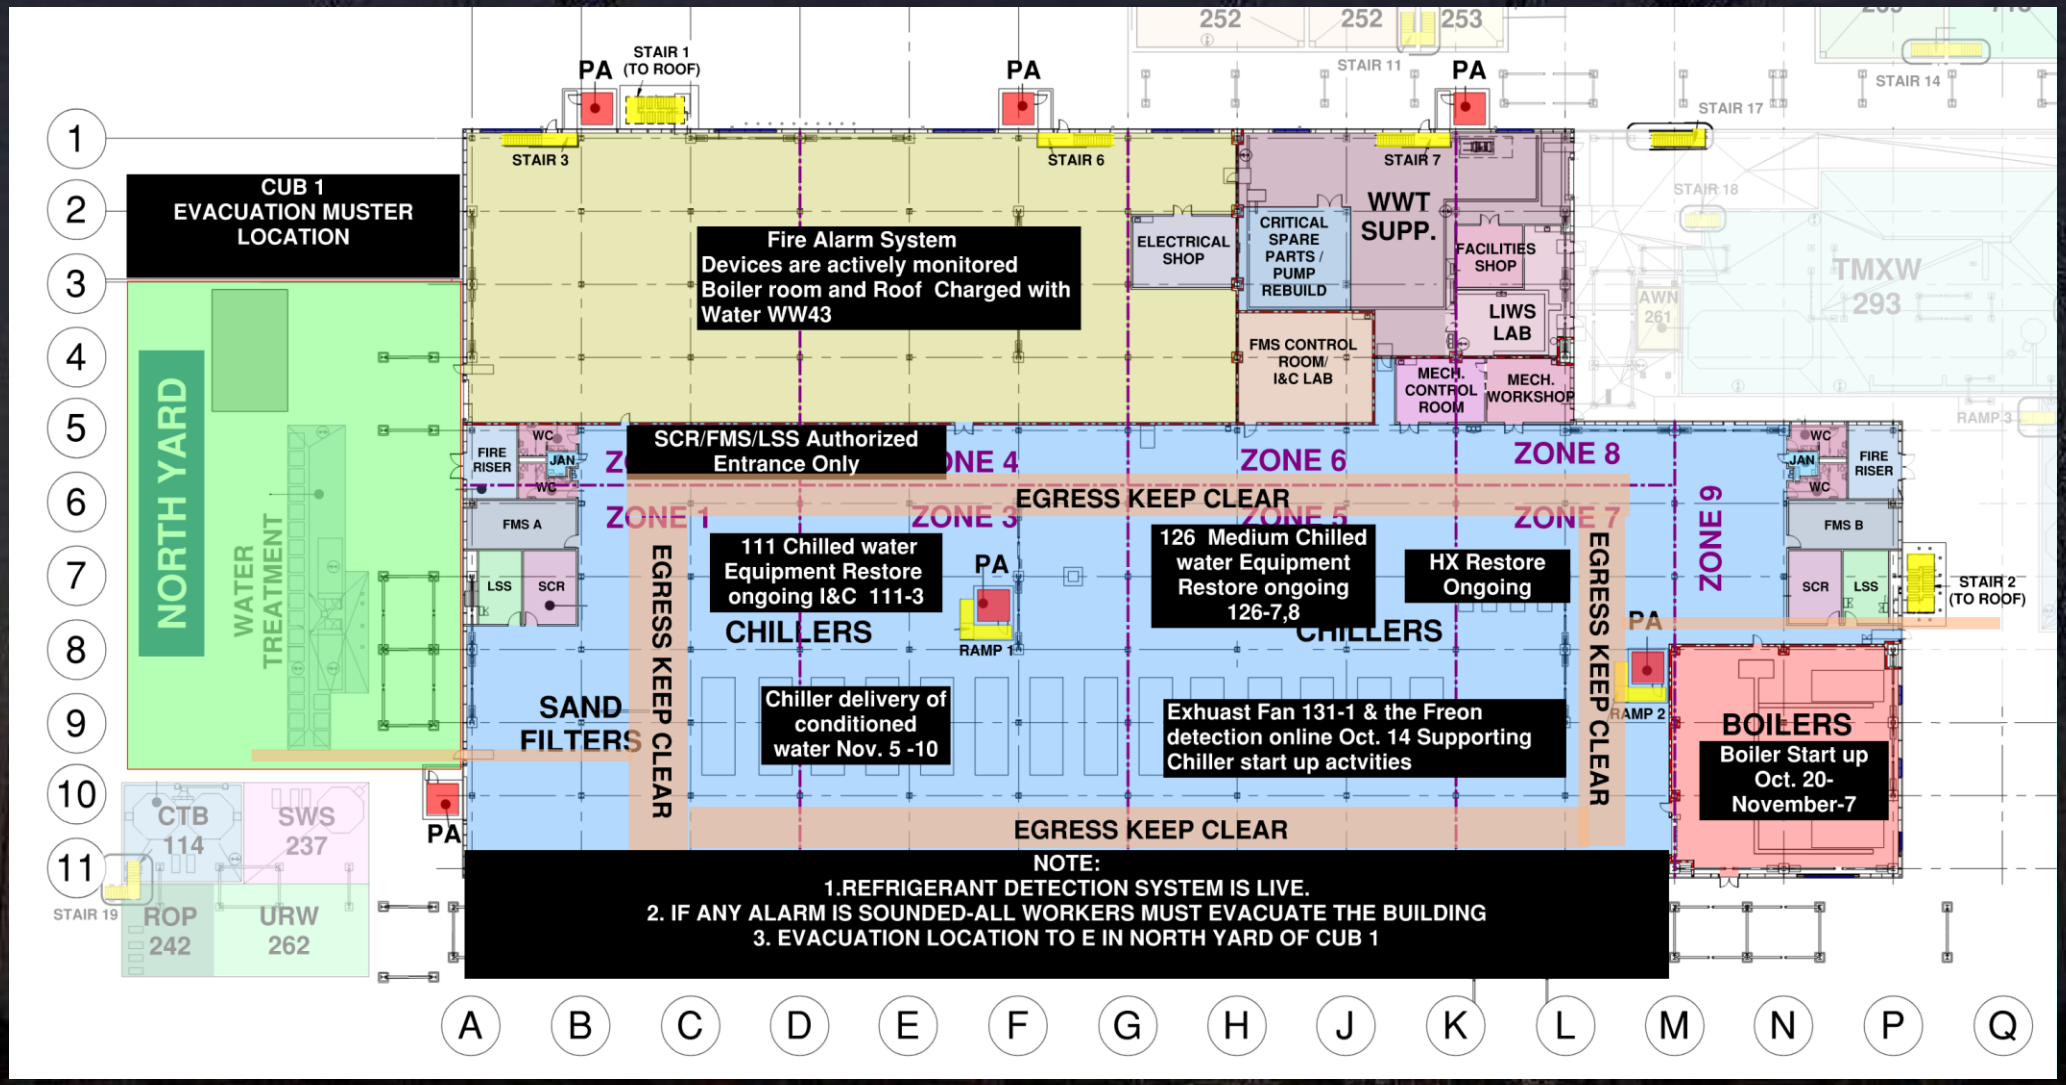

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

CUB 1 – EXTERIOR/ROOF

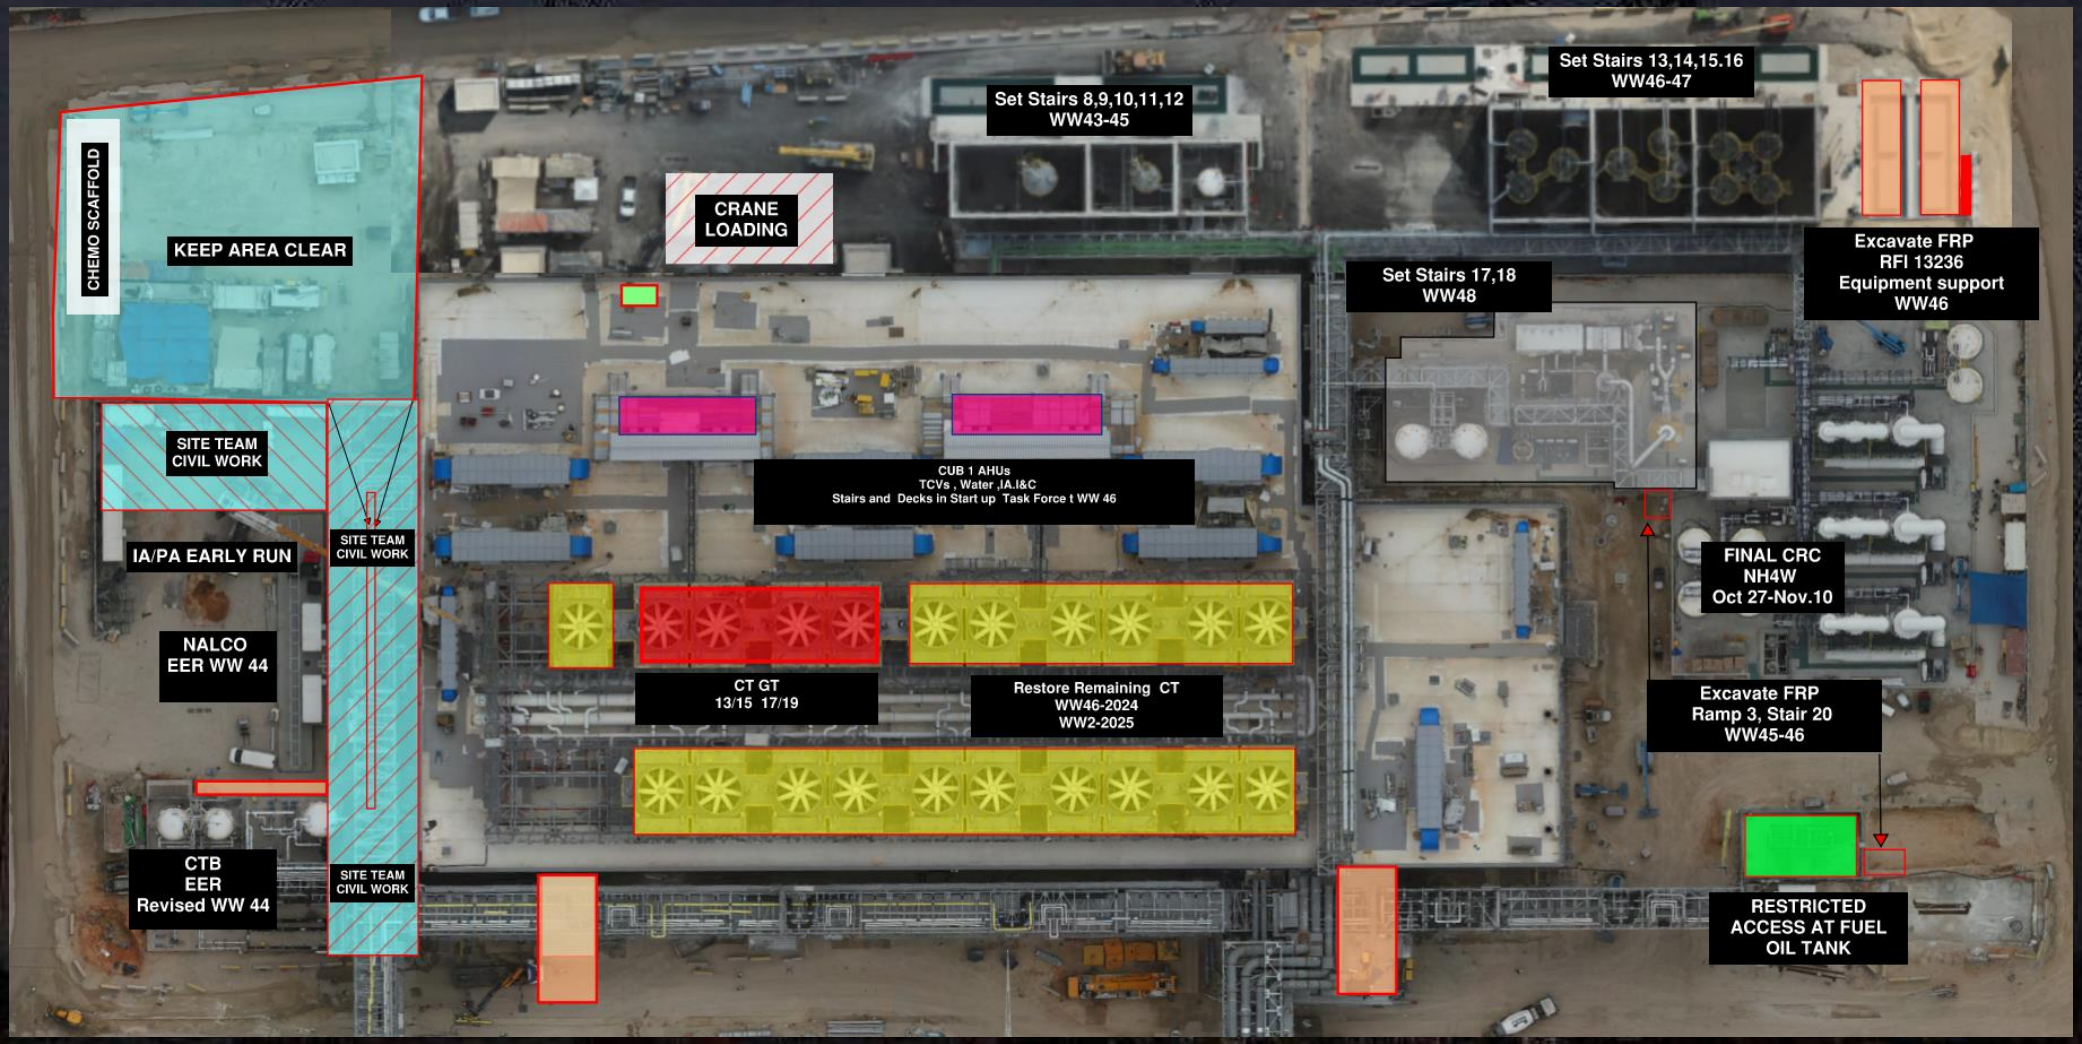

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

CUB 2- Load in and H&T

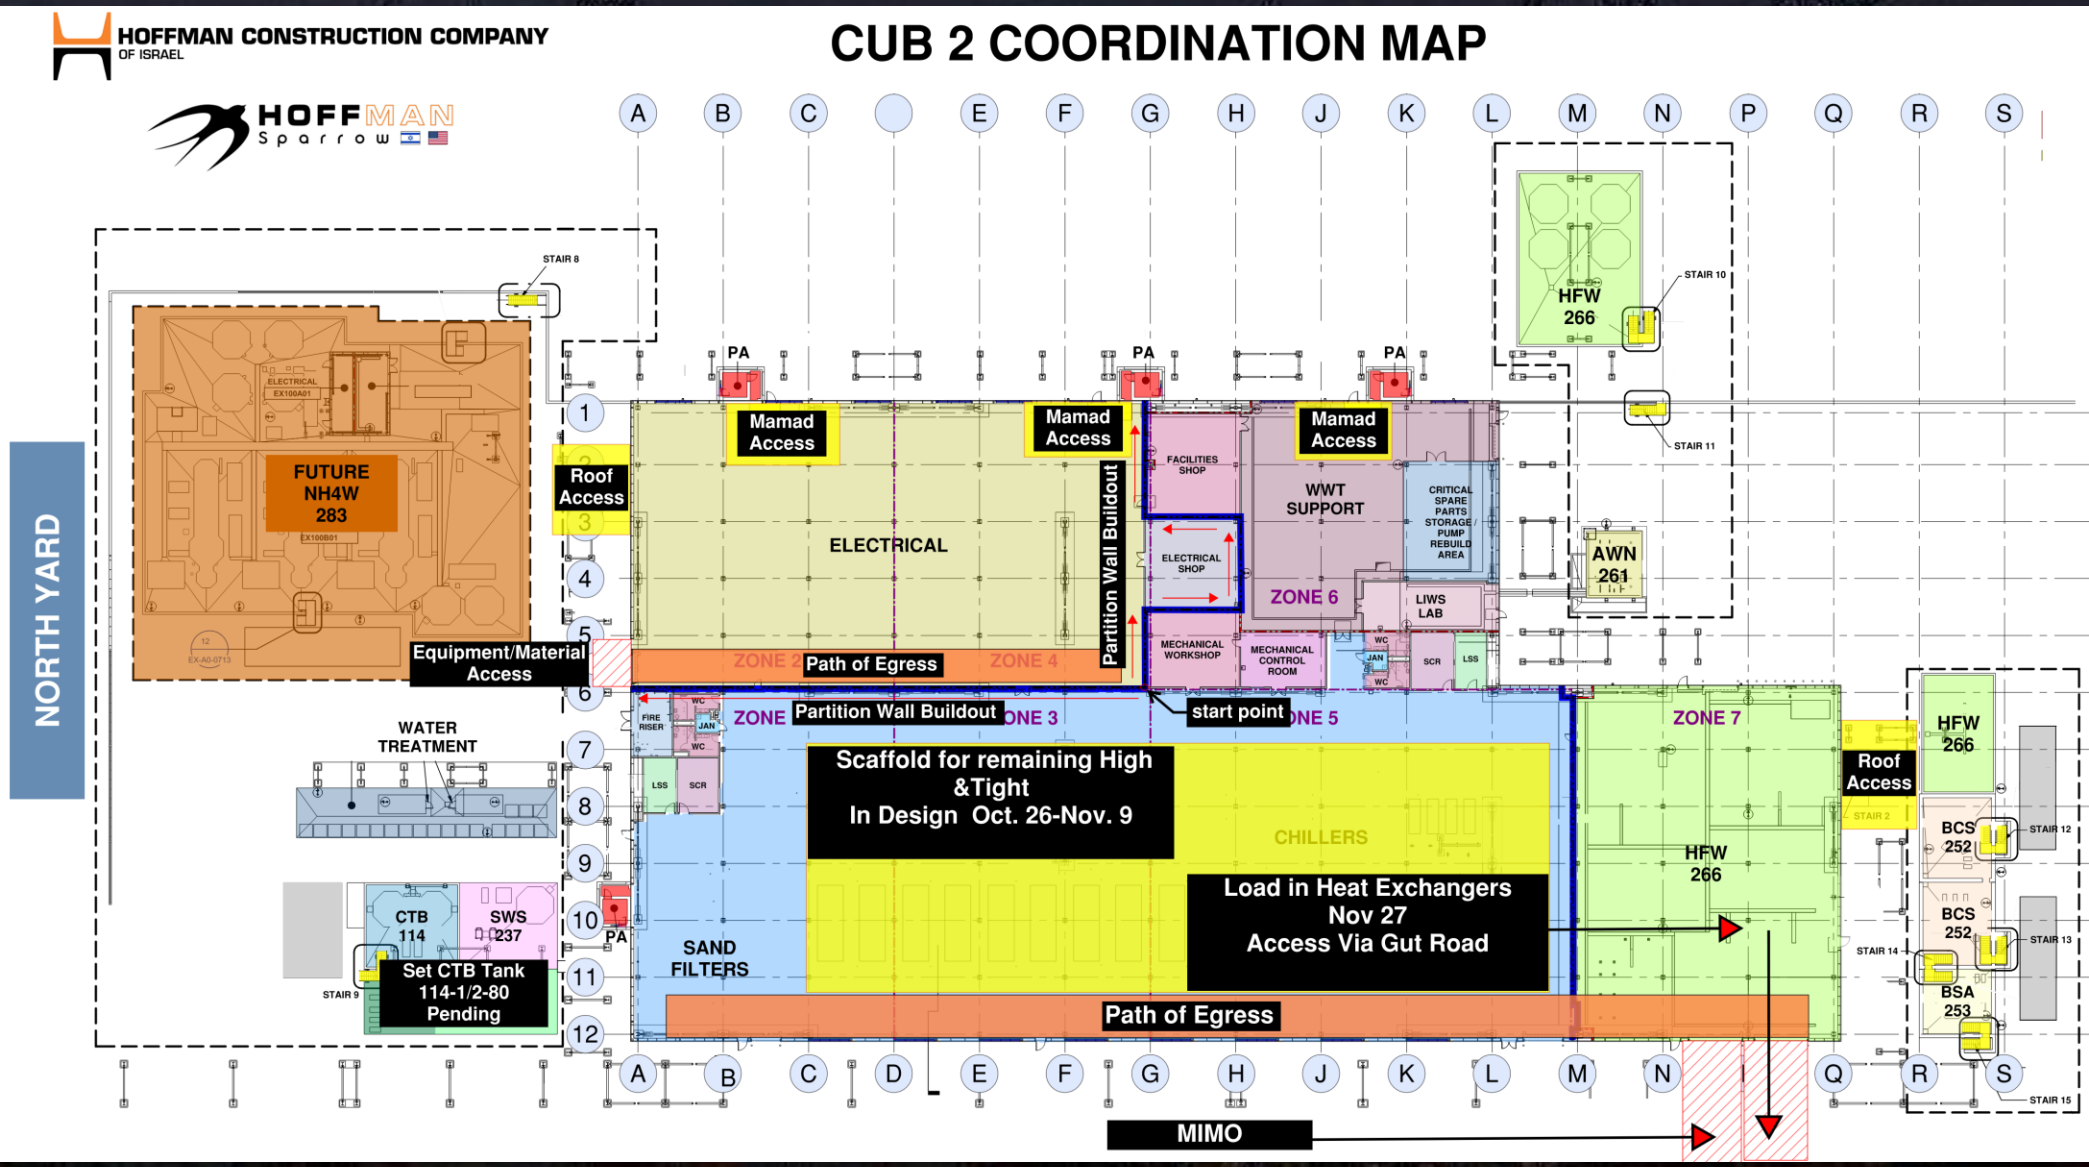

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

CUB 2 – EXTERIOR/ROOF

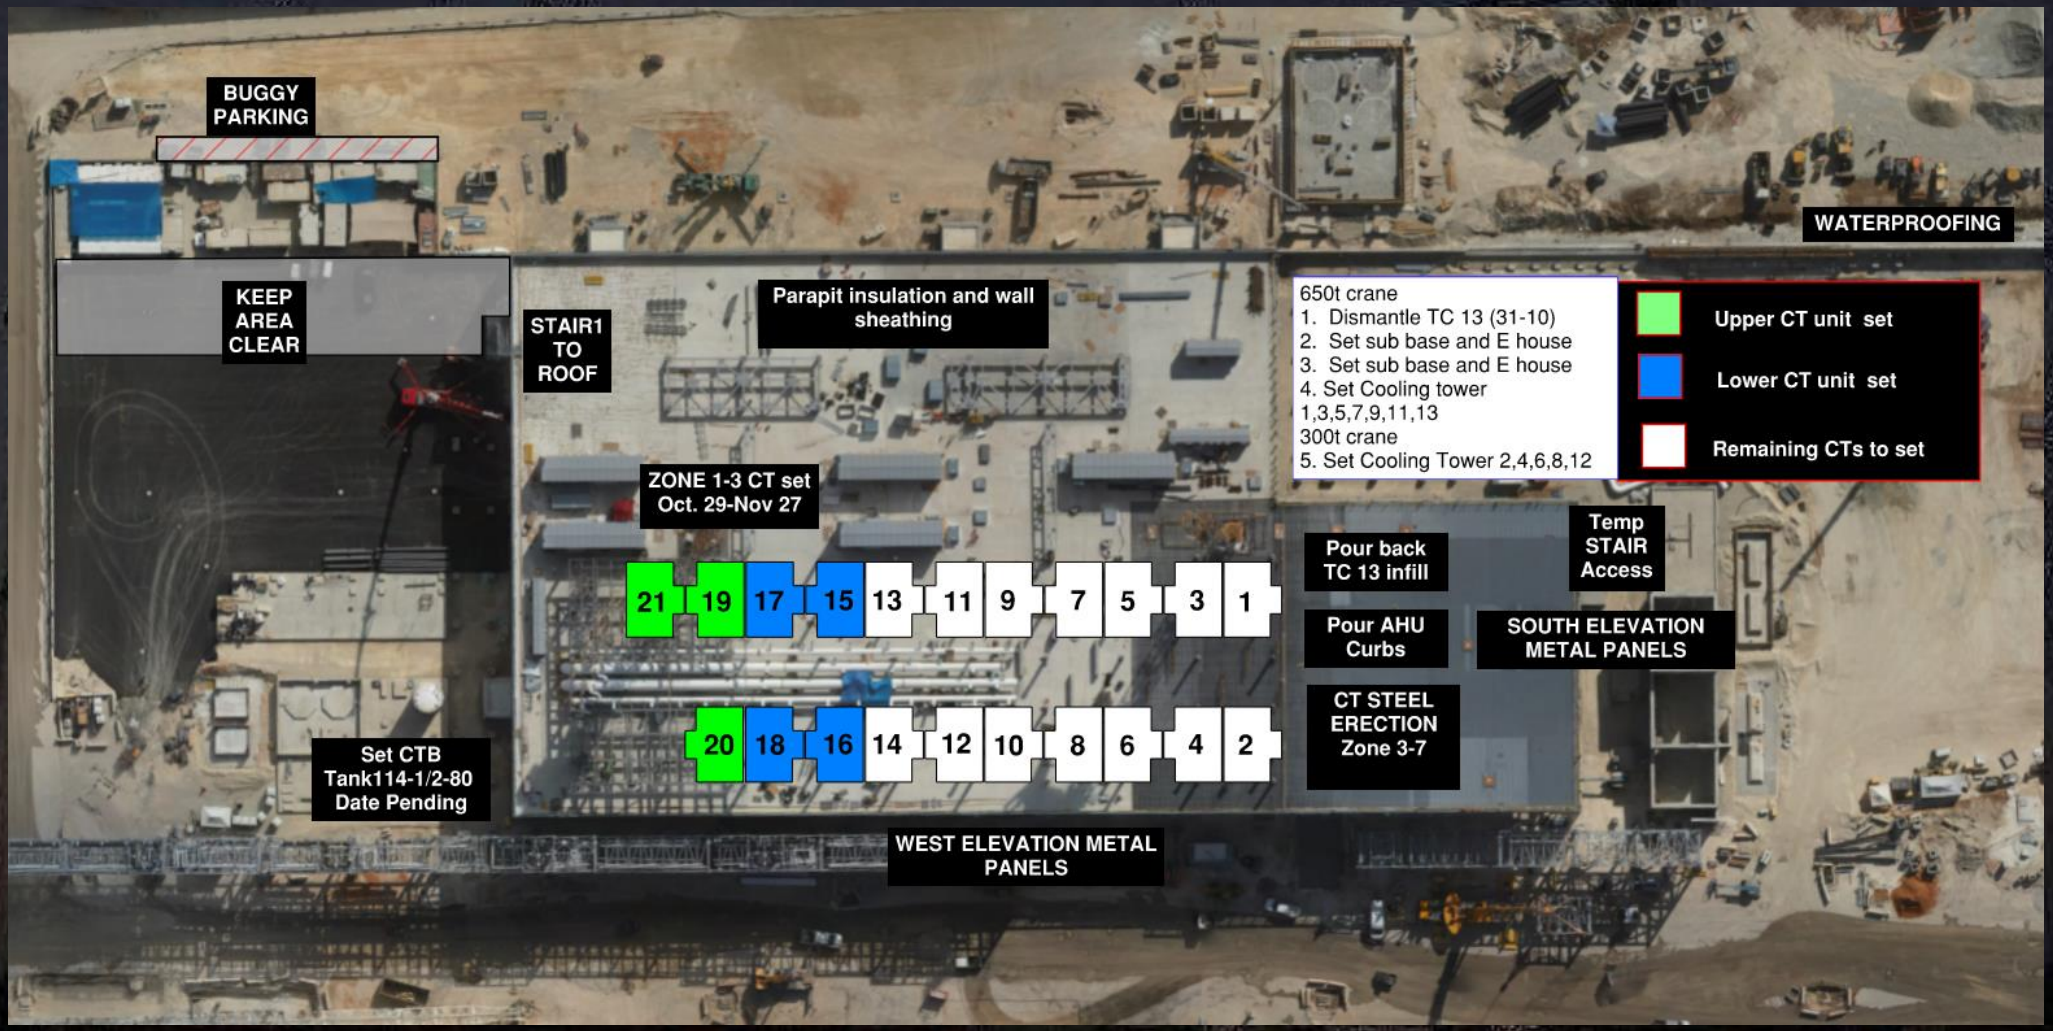

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

CUB 2 – Crane Logistics

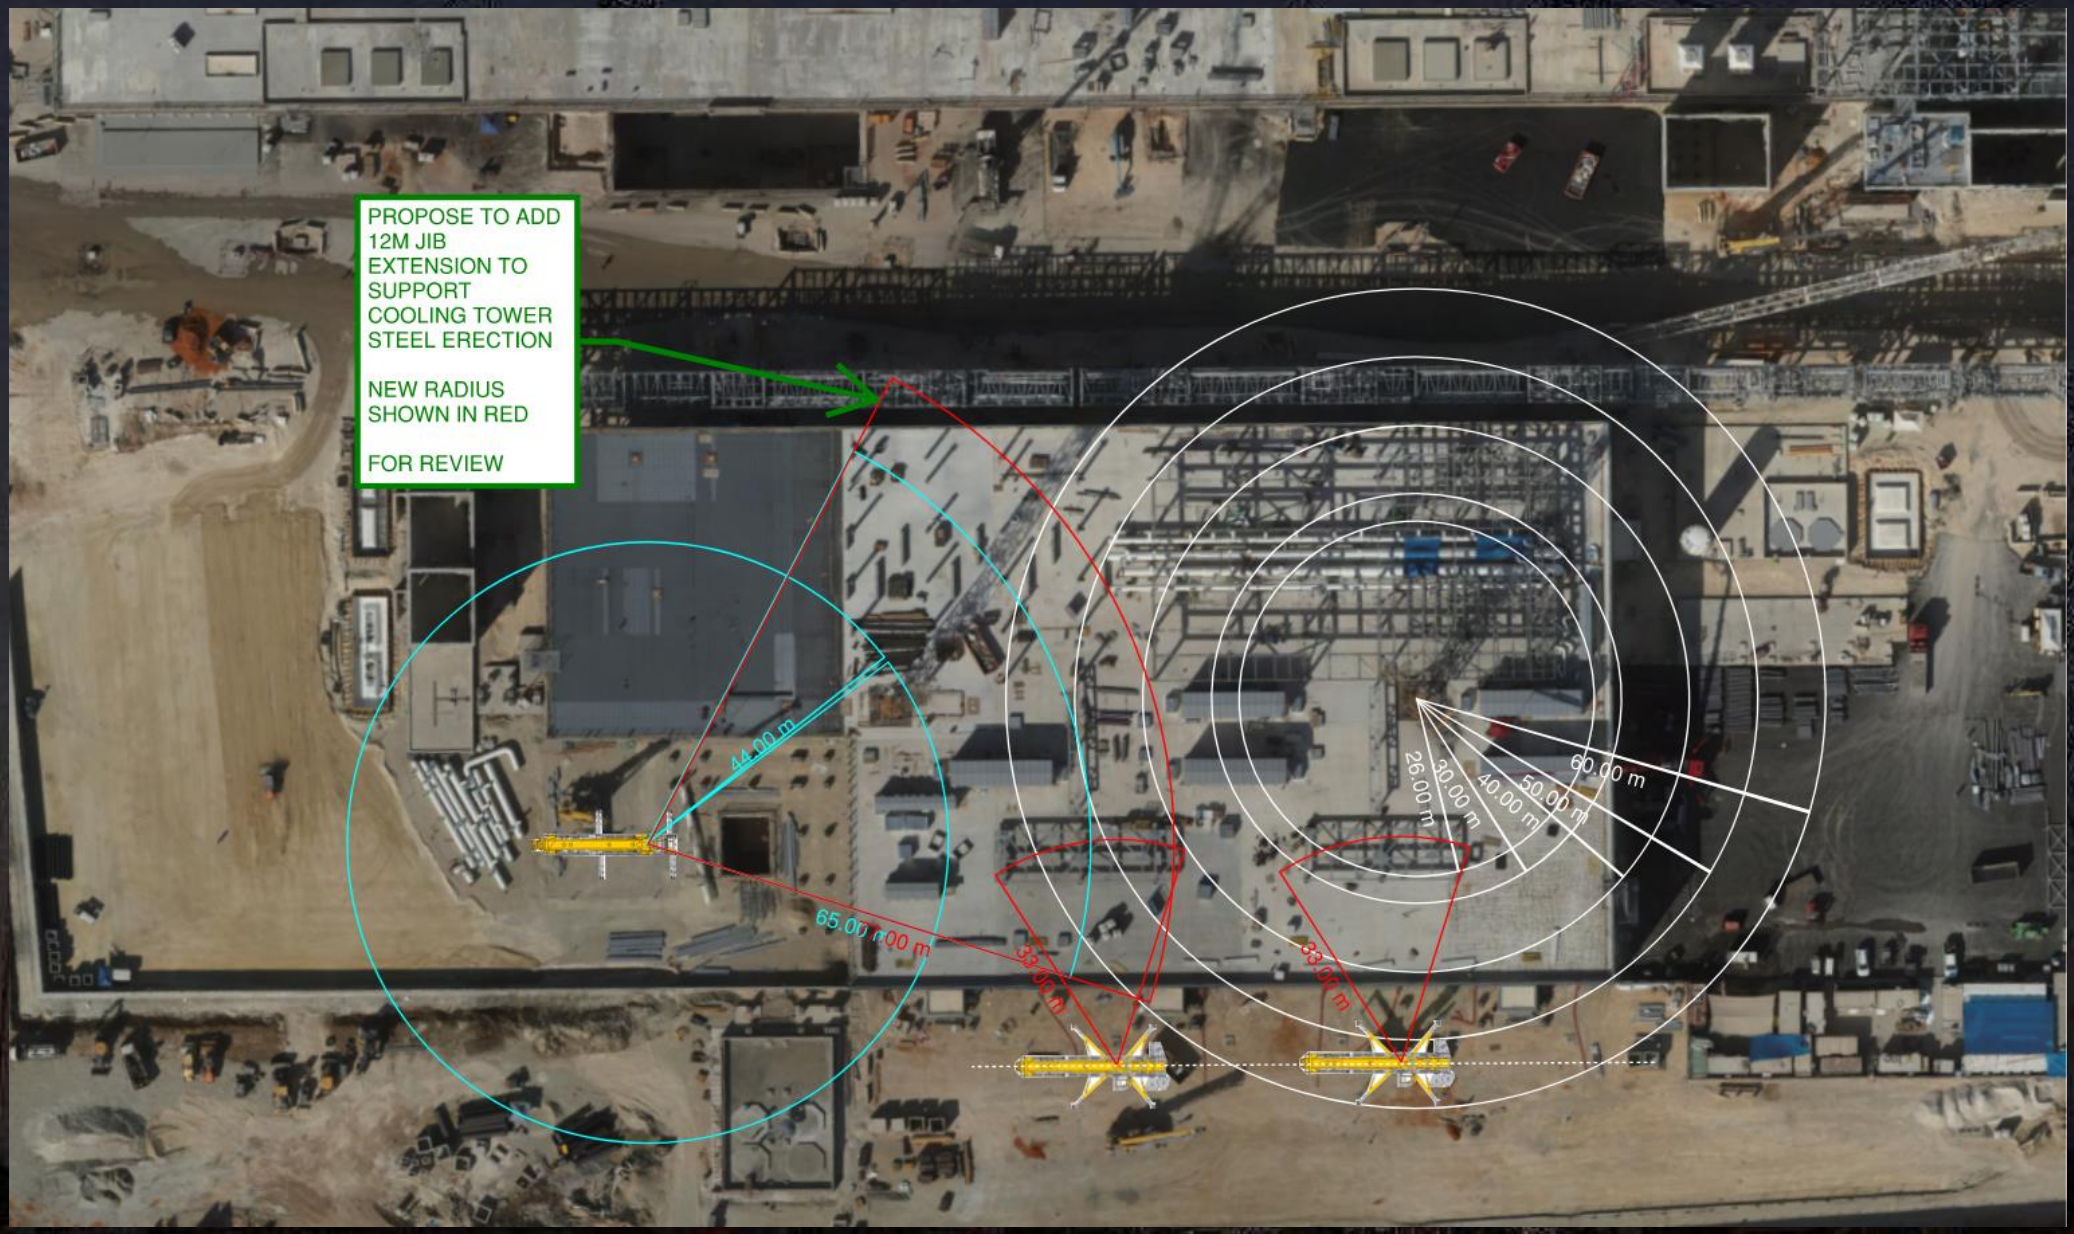

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

Daily Coordination Meeting

Site Logistics

North

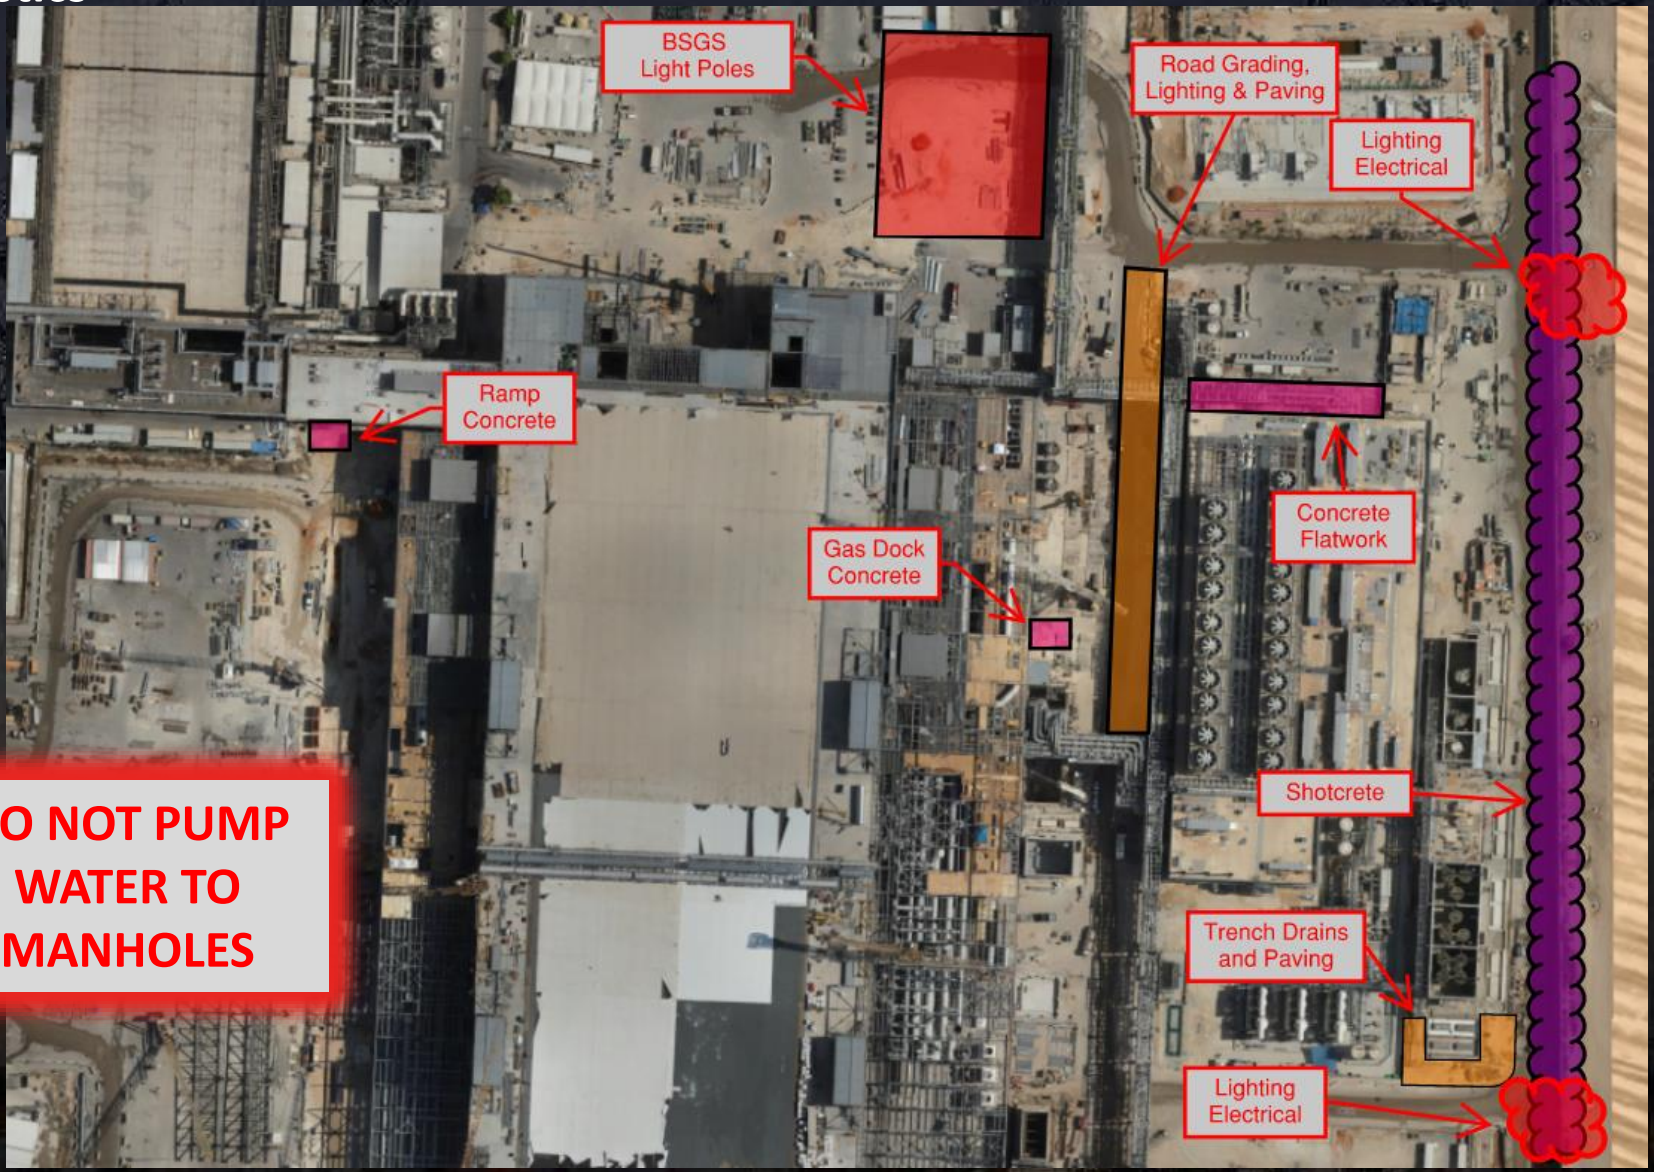

DO NOT PUMP WATER TO MANHOLES

HOFFMAN CONSTRUCTION COMPANY

HOFFMAN Sparrow

Daily Coordination Meeting

Site Logistics

South

Stop the Drop

We are continuing to see a high number of dropped objects on this project.

Remember, tools and material must be secured at heights. This can be with containers, tethers, netting, etc. But cannot be ignored.

Tools must be inspected before use, if something is loose, it shouldn't be used.

Barricades are our last line of defense, not first. Just because a barricade is in place does not mean it is okay or acceptable to have something unsecured at heights.

All of you need to be checking on your work areas and ensuring that your crews are doing everything that they can to STOP THE DROP of tools, material, equipment, etc.

Daily Coordination Meeting

HOFFMAN CONSTRUCTION COMPANY

14:00 Sign In
